

**406th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
August, 2019**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for August 2019 contains information on the status of the 1634 Central Sector Infrastructure Projects costing ₹150 crore and above. During August 2019, 9 projects (2 projects of Coal and 7 projects of Road Transport & Highways Sector) have reported completion.

2. During the reference month, out of 1634 projects, 552 projects are delayed with respect to their original schedules and 42 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 42 projects, 8 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	855	222	21	2
2	RAILWAYS	315	142	7	2
3	PETROLEUM	152	48	6	2
4	COAL	106	37	4	0
5	POWER	75	45	2	2
6	URBAN DEVELOPMENT	63	25	2	0
7	HEALTH AND FAMILY WELFARE	21	11	0	0
8	CIVIL AVIATION	13	5	0	0
9	STEEL	9	8	0	0
10	FERTILISERS	5	1	0	0
11	MINES	5	0	0	0
12	ATOMIC ENERGY	4	4	0	0
13	TELECOMMUNICATIONS	4	2	0	0
14	INFORMATION AND BROADCASTING	3	1	0	0
15	WATER RESOURCES	2	1	0	0
16	HEAVY INDUSTRY	1	0	0	0
17	SHIPPING AND PORTS	1	0	0	0
Total		1634	552	42	8

3. Total original cost of implementation of the 1634 projects was ₹19,40,699.03 crore and their anticipated completion cost is likely to be ₹23,29,746.02 crore, which reflects overall cost overruns of ₹3,89,046.99 crore (20.05% of original cost). The expenditure incurred on these projects till August 2019 is ₹9,75,180.06 crore, which is 41.85% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-09-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.02
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.02
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	19.86
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	24.10
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.06
PETROLEUM					
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	95.30
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	345.92	70.45
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
POWER					
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
3	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	5024.35	203.22
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	155.05

5	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
RAILWAYS					
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
2	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	1800.00	1391.30
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
4	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
5	ATTIPPATTU PUTTUR	04/2008	151.84	1105.00	627.74
ROAD TRANSPORT AND HIGHWAYS					
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	880.06
2	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
3	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
4	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	408.77	143.84
5	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	195.04	377.99	93.80
SHIPPING AND PORTS					
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	27.84
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	49.05
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	3.58
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
3	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
4	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	488.28	25.85
WATER RESOURCES					
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-09-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00

2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.14
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.07
	COAL				
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	1173.30
2	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
3	BHANEGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	99.78
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.09
	PETROLEUM				
1	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
2	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
3	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
4	MUMBAI REFINERY EXPANSION PROJECT	09/2015	4199.00	5060.00	861.00
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	821.27
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	6077.52
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	9996.59	4643.59
	RAILWAYS				
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12524.00	8069.83
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
	ROAD TRANSPORT AND HIGHWAYS				
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	6786.82

2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
3	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
4	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2525.80	1137.46
5	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
SHIPPING AND PORTS					
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1169.18
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	7615.00
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	8.30
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
3	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5687.79	506.00
4	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23
WATER RESOURCES					
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1634 projects, 372 are on schedule, 552 are delayed, 373 projects reported cost overrun and 185 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 489 if delay is calculated on the basis of latest schedule of completion. Further, for 687 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 552 delayed projects, 181 (32.79%) projects have overall delay in the range of 1 to 12 months, 128 (23.19%) projects have delay in the range of 13 to 24 months, 127 (23%) projects have delay in the range of 25 to 60 months and 116 (21.01%) projects have delay of 61 months and above. **The average time overrun in these 552 delayed projects is 38.89 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-09-2019)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700	10/2009	12/2016	12/2020	48

	MW)				
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
2	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB I AIRPORT KOLKATA	01/2016	03/2020	12/2020	9
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	12/2020	8
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	12/2019	6
5	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	08/2022	6
COAL					
1	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2022	144
2	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
4	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2020	120
5	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2021	120
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	09/2019	34
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	10/2020	83
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	09/2019	28
3	AIIMS - OPD(NEW)	08/2014	05/2017	08/2019	27
4	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	09/2019	19
5	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	09/2019	16
INFORMATION AND BROADCASTING					
1	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	02/2019	11/2019	9
PETROLEUM					
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
2	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	12/2019	81
3	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2019	79
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
5	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014	08/2019	58
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	10/2019	118
3	BARH STPP(3X660MW) NTPC	02/2005	10/2011	08/2021	118
4	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2022	114
5	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	03/2022	103
RAILWAYS					
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
2	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
3	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2021	252
4	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	06/2022	235
ROAD TRANSPORT AND HIGHWAYS					
1	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	08/2020	149
2	NALBARI T BIJNI (AS-7)	12/2003	04/2008	03/2020	143
3	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	10/2019	136
4	GWALIOR-JHANSI, NH-75	12/2003	12/2009	08/2020	128

5	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	04/2009	08/2019	124
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2020	62
2	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
3	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	11/2019	23
4	COKE OVEN BATTERY-5	12/2011	12/2017	10/2019	22
5	INSTALLATION OF NEW HOT STRIP MILL AT RSP	04/2015	04/2018	11/2019	19
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	09/2019	11
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2020	89
2	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
3	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70
4	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2020	67
5	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	05/2020	64
WATER RESOURCES					
5	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	06/2021	15

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-09-2019)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	213.50	06/2019	12/2019

3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	219.91	219.91	61.61	03/2020	12/2020
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	233.38	233.38	84.73	04/2020	12/2020
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	232.44	03/2021	03/2021
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	09/2019
3	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	20.30	03/2022	03/2022
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	7203.71	11/2021	11/2021
5	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	319.93	03/2020	03/2020
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	147.00	11/2013	10/2020
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	184.93	06/2020	08/2020
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	244.66	04/2020	06/2020
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	241.39	09/2018	N.A.
HEAVY INDUSTRY							
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	335.03	09/2019	09/2019
INFORMATION AND BROADCASTING							
1	NATIONAL FILM HERITAGE MISSION	11/2014	597.41	597.41	29.80	N.A.	N.A.
2	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	204.32	204.32	0.00	02/2019	11/2019
3	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	167.70	167.70	0.00	03/2020	03/2020
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.57	02/2017	10/2021
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
5	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	07/2014	247.00	247.00	0.00	03/2021	03/2021
POWER							
1	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10945.40	09/2010	N.A.
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3268.00	10/2017	N.A.
4	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	210.72	04/2016	12/2019
5	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9072.36	1211.92	12/2018	12/2019
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2010.00	654.07	07/2012	03/2024

3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	274.97	03/2019	03/2020
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	148.43	03/2006	03/2025
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	541.07	07/2014	N.A.
ROAD TRANSPORT AND HIGHWAYS							
1	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	131.71	N.A.	10/2020
2	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	113.67	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	278.45	08/2016	N.A.
SHIPPING AND PORTS							
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1394.52	03/2023	03/2023
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.03	06/2017	N.A.
3	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	117.63	10/2018	09/2019
URBAN DEVELOPMENT							
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.
WATER RESOURCES							
1	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	233.57	233.57	32.20	12/2019	12/2019

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost

Estimates (as on 01-09-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5784.74
	COAL				
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	0.00	286.19
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	347.15
3	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.10	0.00	501.82
4	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	539.59
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	228.90
	HEALTH AND FAMILY WELFARE				
1	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	508.29
	PETROLEUM				
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	0.00	1314.42
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7551.56
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10945.40
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	0.00	2237.45
4	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	0.00	3003.16
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	7861.51
	RAILWAYS				
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	654.07
2	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF,	04/1991	329.39	803.11	845.59
3	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	669.21
4	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	927.86
5	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	164.36	0.00	999.64
	ROAD TRANSPORT AND HIGHWAYS				
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	456.92	488.37
2	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	223.68
3	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	0.00	451.15
4	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	337.76
5	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	328.47
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	0.00	15938.88
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65

3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.87
4	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	5188.00
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	0.00	424.11
WATER RESOURCES					
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	0.00	16417.99

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-09-2019)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
3	MURAIH UG TURN-KEY PROJECT	02/2011	04/2014	N.A.	N.A.
4	MOONIDH XV SEAM UG	08/2011	04/2015	N.A.	N.A.
5	KAPURIA UG(PSLW)	08/2011	04/2017	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
3	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	N.A.
INFORMATION AND BROADCASTING					
1	NATIONAL FILM HERITAGE MISSION	11/2014	N.A.	N.A.	N.A.
MINES					
1	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
3	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	03/2015	N.A.	N.A.
4	RESID UPGRADATION PROJECT	03/2013	11/2015	N.A.	N.A.
5	POLYPROPYLENE PLANT AT PARADIP REFINERY	03/2014	09/2017	06/2019	07/2019
POWER					
1	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
4	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
5	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.

3	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	N.A.
4	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	02/2009	N.A.	N.A.
5	ETAWAH-MAINPURI (NL),NCR	04/1997	12/2008	N.A.	03/2015
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
4	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 30.08.2019 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	855	21
2	RAILWAYS	315	7
3	PETROLEUM	152	6
4	COAL	106	4
5	POWER	75	2
6	URBAN DEVELOPMENT	63	2
7	HEALTH AND FAMILY WELFARE	21	0
8	CIVIL AVIATION	13	0
9	STEEL	9	0
10	FERTILISERS	5	0
11	MINES	5	0
12	ATOMIC ENERGY	4	0
13	TELECOMMUNICATIONS	4	0
14	INFORMATION AND BROADCASTING	3	0
15	WATER RESOURCES	2	0
16	HEAVY INDUSTRY	1	0
17	SHIPPING AND PORTS	1	0
	Total	1634	42

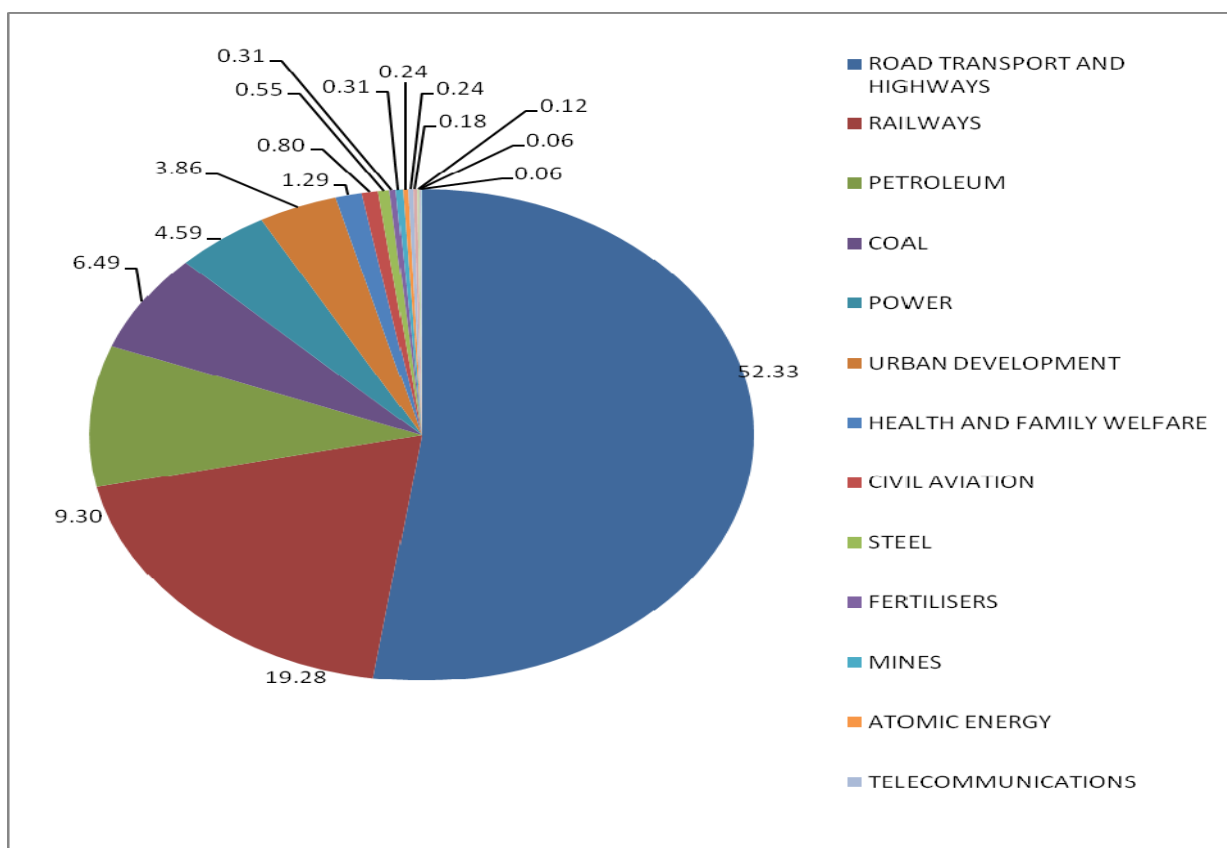


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2019			
	<u>COAL</u>			
1	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI (NORTHERN COAL FIELDS LIMITED) - [N06000033]	259.40	03/2012	266.38
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) (NORTHERN COAL FIELDS LIMITED) - [N06000091]	1,131.28	03/2018	796.85
	<u>PETROLEUM</u>			
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000175]	3,076.00	09/2017	3,450.30
	<u>POWER</u>			
4	BONGAIGAON THERMAL POWER PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000041]	4,375.35	10/2011	7,000.00
5	TRIPURA GAS BASED POWER PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000071]	421.01	07/2013	963.23
	<u>RAILWAYS</u>			
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) RAILWAY) - [N22000113]	653.19	03/2014	862.17
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000357]	567.51	03/2018	421.60
	May,2019			
	<u>COAL</u>			
8	MAKARDHOKRA I OC (WESTERN COAL FIELDS LIMITED) - [N06000119]	266.23	03/2021	144.38
	<u>PETROLEUM</u>			
9	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000084]	736.65	09/2011	331.47
10	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000290]	474.15	05/2019	348.64
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	WESTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000035]	477.69	09/2010	691.96
12	KUDGI STPP STAGE 1 (NATIONAL THERMAL POWER CORPORATION) - [N18000131]	15,166.19	01/2017	15,364.00
13	SOLAPUR STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000133]	9,395.18	01/2017	8,617.00
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000158]	539.82	06/2016	434.33
15	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000174]	3,363.12	12/2016	2,244.00
16	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000222]	790.13	06/2019	575.24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000145]	1,585.00	05/2013	2,023.33
18	JORBAT - BARAPANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000180]	536.00	01/2014	845.41
19	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S EPC(PUBLIC WORKS DEPT OF STATE) - [N24000241]	177.18	03/2016	40.51
20	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000242]	158.65	03/2016	103.50
21	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW EPC(PUBLIC WORKS DEPT OF STATE) - [N24000243]	244.08	03/2016	38.32
22	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000244]	340.00	03/2016	2.00
23	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000246]	244.30	12/2016	2.00
24	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S (PUBLIC WORKS DEPT OF STATE) - [N24000249]	218.31	12/2015	208.28
25	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000250]	260.39	11/2016	188.00
26	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000255]	220.72	11/2016	155.30
27	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000261]	267.16	11/2017	308.33
28	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A EPC(DEPT OF ROAD TRANSPORT & HIGHWAYS) - [N24000262]	201.12	02/2015	150.19
29	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) (PUBLIC WORKS DEPT OF STATE) - [N24000263]	241.61	02/2017	178.94

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
30	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN EPC(PUBLIC WORKS DEPT OF STATE) - [N24000265]	297.78	02/2017	284.89
31	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC (PUBLIC WORKS DEPT OF STATE) - [N24000266]	361.30	07/2014	203.29
32	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) EPC(PUBLIC WORKS DEPT OF STATE) - [N24000267]	258.99	07/2014	200.44
33	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC EPC(PUBLIC WORKS DEPT OF STATE) - [N24000268]	251.55	02/2015	172.65
34	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000269]	175.03	-	152.53
35	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP EPC(PUBLIC WORKS DEPT OF STATE) - [N24000272]	266.00	-	182.13
36	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000273]	314.43	-	216.96
37	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000277]	185.82	-	142.23
38	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000278]	213.47	03/2015	182.91
39	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV EPC(PUBLIC WORKS DEPT OF STATE) - [N24000279]	298.34	03/2015	269.93
40	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I EPC(PUBLIC WORKS DEPT OF STATE) - [N24000280]	262.54	03/2015	215.11
41	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000283]	169.26	12/2012	280.72
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000284]	170.21	11/2014	140.09
43	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000286]	394.20	-	332.62
44	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000288]	422.34	-	406.40
45	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE EPC(PUBLIC WORKS DEPT OF STATE) - [N24000289]	435.90	-	380.41
46	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000290]	279.68	-	286.96
47	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000291]	463.65	-	536.84

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
48	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000292]	573.96	-	557.08
49	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000293]	480.21	-	372.37
50	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000299]	224.83	05/2015	189.85
51	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU EPC(PUBLIC WORKS DEPT OF STATE) - [N24000300]	309.01	09/2015	391.89
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION EPC(PUBLIC WORKS DEPT OF STATE) - [N24000303]	417.61	06/2014	261.29
53	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000310]	377.83	07/2017	318.66
54	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000329]	497.89	04/2017	735.92
55	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000330]	629.74	-	721.04
56	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000336]	227.74	10/2016	187.85
57	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000369]	269.26	10/2016	212.72
58	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI EPC(PUBLIC WORKS DEPT OF STATE) - [N24000370]	483.38	-	470.16
59	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000372]	616.36	-	554.68
60	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000374]	486.74	-	415.58
61	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000377]	397.04	10/2016	368.49
62	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000381]	257.80	02/2016	59.30
63	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000383]	312.79	-	258.86
64	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K EPC(PUBLIC WORKS DEPT OF STATE) - [N24000384]	319.80	-	289.40
65	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000387]	264.16	-	533.18

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
66	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000390]	1,494.48	02/2011	2,158.50
67	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000393]	774.57	03/2018	613.58
68	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000394]	532.49	05/2017	386.02
69	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000399]	317.76	03/2017	344.30
70	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000403]	283.45	10/2016	285.18
71	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000404]	578.38	-	481.30
72	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA EPC(PUBLIC WORKS DEPT OF STATE) - [N24000405]	789.83	-	608.55
73	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000406]	208.87	05/2016	206.78
74	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000409]	176.22	02/2018	0.10
75	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000410]	641.02	12/2017	449.66
76	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000416]	224.83	04/2015	189.85
77	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000418]	493.94	03/2017	503.25
78	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000419]	165.00	09/2010	174.57
79	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000420]	104.00	09/2010	218.29
80	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000421]	235.08	05/2018	235.08
81	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000447]	670.82	02/2015	590.00
82	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000474]	327.32	05/2017	301.41
83	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000476]	273.06	-	199.72

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
84	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000512]	207.88	-	179.58
85	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000526]	899.21	-	748.74
86	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000529]	207.88	-	179.58
87	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000536]	377.64	03/2014	755.28
88	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO (PUBLIC WORKS DEPT OF STATE) - [N24000538]	292.98	11/2014	160.96
89	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000561]	244.00	07/2018	231.90
90	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000573]	322.01	08/2014	267.00
91	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY - KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000615]	334.22	06/2016	334.22
92	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000647]	162.51	05/2016	136.31
93	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 (PUBLIC WORKS DEPT OF STATE) - [N24000856]	170.00	02/2015	115.57
94	REHABILITATION AND UPGRADATION OF PURANPUR - KHUTAR SECTION FROM KM 38.00 TO KM 82.00 OF NH-730 TO 2 (PUBLIC WORKS DEPT OF STATE) - [N24001142]	225.96	06/2018	174.63
	June,2019			
	<u>RAILWAYS</u>			
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) (NORTH CENTRAL RAILWAY) - [220100007]	158.77	03/1994	682.34
96	AMRAVATI-NARKHER NL(CR) (CENTRAL RAILWAYS) - [220100118]	663.01	06/1999	726.33
97	CALICUT-MANGALORE (DL) (SR) (SOUTHERN RAILWAY) - [220100151]	240.00	-	0.01
98	MANDARHILL-DUMKA-RAMPURHAT (NL),ER (EASTERN RAILWAYS) - [220100168]	1,125.89	03/2016	1,180.08
99	KARUR-SALEM(NL),SR (SOUTHERN RAILWAY) - [220100191]	155.55	-	863.54
100	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR (NORTH CENTRAL RAILWAY) - [220100243]	108.00	12/2009	455.39
101	KATI HAR - JOGBANI (GC)(NEFR) (NORTH EAST FRONTIER RAILWAY) - [220100247]	792.46	12/2010	944.80

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
102	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) (NORTH EASTERN RAILWAY) - [220100256]	744.71	-	917.49
103	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) (SOUTHERN RAILWAY) - [220100263]	280.00	-	942.28
104	JIND-SONEPAT (NL),NR (NORTHERN RAILWAY) - [220100280]	238.56	03/2012	785.75
105	KODERMA GIRIDH (NL), ECR (EAST CENTRAL RAILWAYS) - [220100306]	768.87	-	988.38
106	MAHARAJGANJ-MASRAKH (NL) - NER (NORTH EASTERN RAILWAY) - [220100316]	218.19	06/2018	380.50
107	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000049]	732.81	03/2008	2,191.46
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE (SOUTHERN RAILWAY) - [N22000080]	343.17	-	1,110.44
109	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) (NORTHERN RAILWAY) - [N22000088]	369.90	03/2010	891.24
110	AGARTALA SABROOM, NL, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000099]	1,142.00	03/2014	3,354.18
111	DAKSHIN-BARASAL-LAKSHMIKANTAPUR (EASTERN RAILWAYS) - [N22000116]	259.51	02/2012	148.37
112	GHUTIASHARIF-CANNING (ER) (EASTERN RAILWAYS) - [N22000117]	193.08	12/2011	154.30
113	PANDABESWAR-CHINPAI DOUBLING (ER) (EASTERN RAILWAYS) - [N22000118]	293.74	12/2010	128.78
114	BHOJIPUR TANAKPUR VIA PILIBHIT (NORTH EASTERN RAILWAY) - [N22000132]	195.64	-	450.62
115	AUNRIHAR MANDUADIH (NORTH EASTERN RAILWAY) - [N22000133]	199.75	08/2018	287.33
116	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000164]	309.44	12/2015	529.27
117	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC (SOUTHERN RAILWAY) - [N22000188]	271.24	-	468.58
118	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA (NORTH EAST FRONTIER RAILWAY) - [N22000194]	895.00	03/2007	1,566.57
119	CHENGANNUR-CHINGAVANAM (SOUTHERN RAILWAY) - [N22000203]	191.72	-	447.03
120	LUMDING-HOJAI PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000211]	246.07	03/2019	490.29
121	MEERUT-MUZAFARNAGAR PATCH DL (NORTHERN RAILWAY) - [N22000267]	377.44	-	430.12
122	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER- CHANDIGARH (NORTHERN RAILWAY) - [N22000290]	338.54	-	384.61
123	JAKHAL-MANSA DOUBLING ON SPR SECTION (NORTHERN RAILWAY) - [N22000291]	162.96	-	160.25
124	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI (SOUTHERN RAILWAY) - [N22000303]	460.94	01/1999	0.01
125	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000439]	458.63	03/2015	367.71
126	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000440]	200.84	03/2014	394.51
127	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000446]	600.00	03/2010	673.80

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
128	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000450]	199.55	03/2009	238.61
129	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. (SOUTHERN RAILWAY) - [N22000453]	208.00	03/2012	206.20
130	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. (SOUTHERN RAILWAY) - [N22000454]	241.00	03/2014	293.37
131	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR- LUCKNOW (NORTH EASTERN RAILWAY) - [N22000455]	233.00	04/1999	349.37
132	MANDHANA - BRAHMAWART NEW LINE PROJECT. (NORTH EASTERN RAILWAY) - [N22000458]	609.04	04/1999	1,806.84
133	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM (EAST CENTRAL RAILWAYS) - [N22000474]	624.47	02/2016	3,376.08
	July,2019			
	<u>COAL</u>			
134	NORTH URIMARI OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000084]	179.87	03/2012	163.23
	<u>STEEL</u>			
135	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) (RASTRIYA ISPAT NIGAM LIMITED) - [N12000120]	465.85	07/2018	390.25
	<u>PETROLEUM</u>			
136	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000072]	3,957.00	12/2018	2,707.26
137	PARADIP-RAIPUR- RANCHI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000088]	1,793.00	12/2016	1,788.86
138	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) (INDIAN OIL CORPORATION LIMITED) - [N16000187]	191.96	05/2015	76.28
139	REPLACEMENT OF KV SECTION OF KSPL Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000287]	279.00	08/2018	200.05
	<u>POWER</u>			
140	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) (SATLUJ JAL VIDYUT NIGAM LIMITED) - [N18000235]	330.00	11/2017	331.46
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
141	BHOPAL-BIORA (4L) OF NH-12 IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000380]	704.26	05/2015	5.21
	<u>TELECOMMUNICATIONS</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
142	MADHYA PRADESH ACCESS (LOT1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000110]	215.30	05/2018	33.46
	August,2019			
	<u>COAL</u>			
143	AMLAI OC EXPANSION SECTOR B (1.50 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000082]	198.59	03/2016	169.15
144	GOKUL (WESTERN COAL FIELDS LIMITED) - [N06000120]	267.67	03/2018	209.47
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
145	IMPROVEMENT FROM KM 0/0 TO 68/0 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000413]	319.80	10/2016	268.01
146	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000642]	226.31	10/2017	137.43
147	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000643]	319.80	05/2016	268.27
148	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000918]	251.92	10/2015	225.98
149	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000919]	265.35	10/2015	247.56
150	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000924]	229.29	11/2015	163.40
151	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000971]	574.19	07/2017	456.98

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2019			
	<u>RAILWAYS</u>			
1	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL (RAIL VIKAS NIGAM LTD.) - [220100149]	631.78	12/2012	762.72
2	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR (NORTHERN RAILWAY) - [220100258]	625.30	06/2007	848.84
3	TAMLUK DIGHA,LINE DOUBLING (SER) (SOUTH EASTERN RAILWAY) - [N22000097]	293.97	06/2005	0.00
4	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) (NORTH WESTERN RAILWAY) - [N22000112]	829.74	03/2015	823.85
5	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE (EASTERN RAILWAYS) - [N22000248]	268.52	-	0.00
6	MUNIRABAD (GINGERA) -RAICHUR NL (SOUTH WESTERN RAILWAY) - [N22000257]	179.65	-	940.47
7	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL (NORTHERN RAILWAY) - [N22000268]	396.04	-	225.18
8	CHANDIGARH-BADDI NL (NORTHERN RAILWAY) - [N22000296]	328.14	-	233.84
9	MM FROM BURAMARA-CHAKULIA (SOUTH EASTERN RAILWAY) - [N22000305]	466.48	-	0.83
10	MIRAJ-LONDA (SOUTH WESTERN RAILWAY) - [N22000327]	1,830.00	-	254.57
11	CHHINDWARA-MANDLA FORT GC (SOUTH EAST CENTRAL RAILWAY) - [N22000481]	556.54	03/2012	0.00
12	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM (SOUTH EAST CENTRAL RAILWAY) - [N22000482]	1,471.93	03/2022	0.00
	<u>WATER RESOURCES</u>			
13	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [300100001]	542.90	12/2007	0.00
	July,2019			
	<u>STEEL</u>			
14	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000085]	188.93	04/2015	138.83
15	REVAMPING OF SINTER MACHINES - 1 AND 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000091]	343.00	10/2016	254.65
16	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000097]	4,749.00	09/2017	110.95

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
17	2 MTPA PELLET PLANT AT NAGARNAR (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000115]	818.00	06/2020	31.60
	<u>RAILWAYS</u>			
18	BHADUTOLA-JHARGRAM VIA LALGARH (NL) (SOUTH EASTERN RAILWAY) - [N22000161]	289.64	-	0.13
19	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI (NORTHERN RAILWAY) - [N22000270]	654.00	-	0.00
20	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR (NORTHERN RAILWAY) - [N22000271]	1,239.00	-	0.00
21	HISSAR-SIRSA VIA AGROHA AND FATEHABAD (NORTHERN RAILWAY) - [N22000292]	400.00	-	0.00
22	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH (NORTHERN RAILWAY) - [N22000293]	876.00	-	0.00
23	MM FROM PANSKURA-GHATAL NL (SOUTH EASTERN RAILWAY) - [N22000309]	276.69	-	0.00
24	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI(SOUTH EASTERN RAILWAY) - [N22000397]	1,013.45	12/2021	0.01
25	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO(SOUTH EASTERN RAILWAY) - [N22000398]	524.43	12/2021	184.33
	<u>August,2019</u>			
	<u>SHIPPING AND PORTS</u>			
26	SETHUSAMUDRAM SHIP CHANNEL PROJECT (PORT TRUST) - [250100175]	2,427.40	10/2008	0.00
27	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) (PORT TRUST) - [N25000035]	150.00	03/2006	0.00
28	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB(MUMBAI PORT TRUST) - [N25000063]	366.39	12/2010	0.00
29	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000066]	244.50	12/2017	0.00
30	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT (KAMARAJAR PORT LIMITED) - [N25000070]	600.00	12/2017	0.00
31	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA (COCHIN SHIPYARD LTD) - [N25000073]	1,799.00	05/2021	347.03
32	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES (COCHIN SHIPYARD LTD) - [N25000074]	970.00	05/2020	322.54
	<u>DEFENCE PRODUCTION</u>			
33	CONSTRUCTION WORKS PHASE 4 (GOA SHIPYARD LIMITED) - [N39000001]	167.69	05/2018	141.83
34	CONSTRUCTION WORKS PHASE 3B (GOA SHIPYARD LIMITED) - [N39000002]	285.95	08/2020	84.40

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1623
No of Projects Completed/Dropped/Frozen in Current Month	18
No of Projects Fell down in current Month	6
No of Projects added in Current Month	35
No of Projects in Current Month	1634

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	552 (33.78%)	23 (1.41%)	372(22.77%)	175 (0.71%)	512(1.33%)	1634
Latest Approved (Date)	489 (29.93%)	29 (1.77%)	455(27.85%)	142 (8.69%)	519(1.76%)	1634

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1317	16,09,313.59	18,32,969.84	7,08,677.39	38.70	2,23,656.25	13.90
Project with Revision in Cost	317	5,01,484.05	4,97,024.73	2,66,525.22	53.60	-4,707.87	-90
Total	1,634	21,10,797.64	23,29,746.02	9,75,180.06	41.85	2,18,948.38	10.37
Original Cost of All Projects							
Original Cost	1,634	19,40,699.03	23,29,746.02	9,75,180.06	41.85	3,89,046.99	20.05

Delayed Project cost Rs.150 Crore and above							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	552	8,23,289.61	10,55,842.45	5,45,346.15	51.70	2,32,552.84	28.25
Latest Approved (RCE)	489	7,04,497.54	8,24,989.48	3,81,115.75	46.20	1,20,491.94	17.10

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	42	44,112.21	52,627.67	34,867.32	66.30	8,515.46	19.30
Total	42	44,112.21	52,627.67	34,867.32	66.25	8,515.46	19.30


Summary of projects in the Flash Report for the month of August, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1623
Number of Projects completed/dropped/frozen in Current Month	18
	0
Number of Projects not Reported in Current Month	6
Number of Projects Added in Current Month	35
Number of Projects in Current Month	1634

Brief Analysis

Project Status with respect to Original Schedule: Out of 1634 projects, 23 projects are ahead of schedule, 372 projects are on schedule 552 projects are delayed. 512 projects do not have fixed dates of commissioning. 175 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

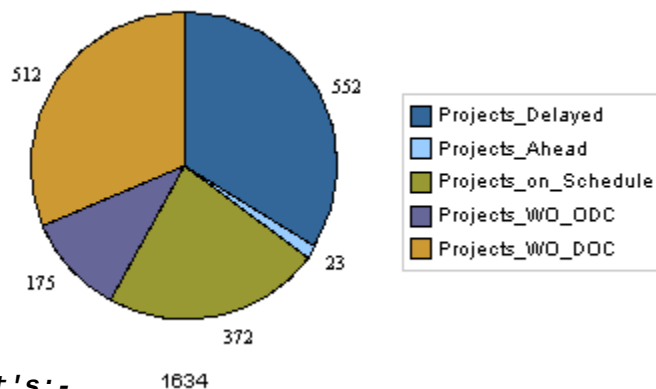

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1634 projects when sanctioned, was of the order of Rs. 1940947.58 crore but this was subsequently revised to Rs. 2329994.57 crore implying a cost overrun of 20%. The expenditure incurred on these projects till August, 2019 is Rs. 975202.61 crore, which is 41.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

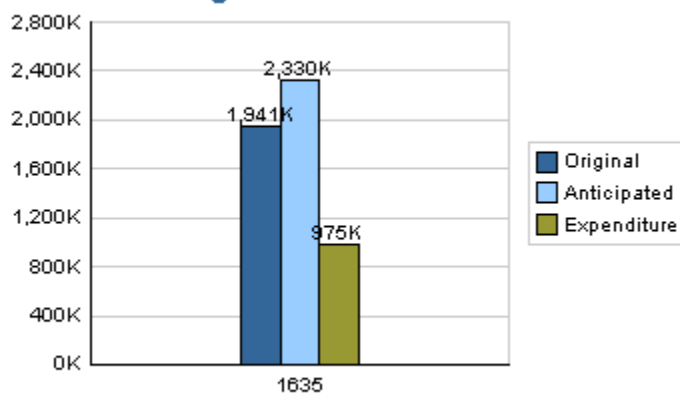


TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) RS.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	106	1,02,335.60	1,02,788.94	0.44	11	25,725.94	28,037.55	8.99
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
8	PETROLEUM	152	2,46,655.89	2,55,016.79	3.39	28	44,172.45	54,739.81	23.92
9	POWER	75	2,81,499.09	3,55,386.08	26.25	30	1,54,828.95	2,29,232.99	48.06
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	3	1,076.25	1,193.54	10.90
12	RAILWAYS	315	4,61,117.38	6,60,824.02	43.31	187	1,78,466.58	3,89,829.96	118.43
13	ROAD TRANSPORT AND HIGHWAYS	855	5,09,411.08	5,30,872.20	4.21	88	62,106.81	86,941.38	39.99
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	83.58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,93,294.88	3.55	14	29,058.09	35,689.91	22.82
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
Total		1634	19,40,699.03	23,29,746.02	20.05	373	5,67,859.10	9,76,976.06	72.05

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6
Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above

(All Cost/ Expenditure in Rs. Crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	75	1,19,490.46	1,69,432.76	41.80	11	21,235.36	71,694.19	237.62
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	5	9,284.82	28,244.13	204.20
3	ASSAM	48	26,216.03	31,003.54	18.26	18	6,570.68	11,631.28	77.02
4	BIHAR	94	90,608.62	1,27,647.16	40.88	30	38,346.70	75,460.87	96.79
5	GOA	10	5,325.87	5,336.30	0.20	1	280.16	290.59	3.72
6	GUJARAT	56	64,665.47	71,517.57	10.60	10	18,114.14	25,526.79	40.92
7	HARYANA	40	30,880.96	33,245.93	7.66	5	3,330.78	5,915.01	77.59
8	HIMACHAL PRADESH	13	18,053.17	28,163.70	56.00	2	6,886.58	16,997.11	146.82
9	JAMMU AND KASHMIR	12	16,534.64	42,210.89	155.29	2	4,659.00	30,468.00	553.96
10	KARNATAKA	63	73,084.28	76,598.88	4.81	15	13,979.23	18,026.26	28.95
11	KERALA	20	36,309.60	39,755.52	9.49	9	16,705.01	20,346.47	21.80
12	MADHYA PRADESH	78	86,555.71	93,301.25	7.79	9	28,541.25	37,229.83	30.44
13	MAHARASHTRA	257	2,35,637.97	2,45,422.34	4.15	32	40,628.79	55,699.73	37.09
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	181.17
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	1	906.46	6,000.00	561.92
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	95.51
17	NAGALAND	26	14,842.43	15,515.91	4.54	1	2,326.52	3,000.00	28.95
18	ODISHA	92	1,06,784.06	1,09,230.71	2.29	17	27,343.52	33,369.70	22.04
19	PUNJAB	27	13,539.35	15,038.78	11.07	5	3,867.41	5,421.60	40.19
20	RAJASTHAN	63	47,345.31	54,833.78	15.82	13	17,425.66	24,914.13	42.97
21	SIKKIM	9	3,476.73	6,368.17	83.17	3	1,909.76	4,801.20	151.40
22	TAMIL NADU	65	1,16,109.47	1,34,527.19	15.86	23	39,899.68	59,915.02	50.16
23	TRIPURA	7	1,977.29	2,139.55	8.21	5	1,436.39	1,598.65	11.30
24	UTTAR PRADESH	118	1,44,722.96	1,49,516.00	3.31	19	39,319.51	46,140.00	17.35
25	WEST BENGAL	63	56,442.22	68,725.50	21.76	21	21,256.89	33,876.47	59.37
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	2	552.41	679.33	22.98
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	25	55,985.34	63,868.57	14.08	6	6,981.71	14,864.94	112.91
29	CHHATISGARH	34	73,625.10	85,279.62	15.83	8	34,846.39	46,931.47	34.68
30	JHARKHAND	47	62,036.07	67,344.06	8.56	9	23,217.46	28,529.23	22.88
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	9	10,197.17	19,115.09	87.45
32	TELANGANA	56	39,959.69	42,435.36	6.20	11	5,987.17	9,116.11	52.26
33	MULTI STATE	131	3,17,640.98	4,24,187.55	33.54	65	1,13,774.75	2,21,623.22	94.79
Total		1634	19,40,699.03	23,29,746.02	20.05	373	5,67,859.10	9,76,976.06	72.05

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	106	1,02,335.60	1,02,788.94	0.44	37	19,631.90	20,845.52	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34 - 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
7	STEEL	9	26,228.23	33,485.23	27.67	8	25,964.87	33,221.87	12 - 62
8	PETROLEUM	152	2,46,655.89	2,55,016.79	3.39	48	1,06,346.22	1,11,106.84	1 - 110
9	POWER	75	2,81,499.09	3,55,386.08	26.25	45	1,70,427.67	2,29,653.46	2 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	11	4,693.67	4,793.45	2 - 83
12	RAILWAYS	315	4,61,117.38	6,60,824.02	43.31	142	1,75,002.73	2,56,024.18	1 - 324
13	ROAD TRANSPORT AND HIGHWAYS	855	5,09,411.08	5,30,872.20	4.21	222	1,34,093.27	1,41,413.50	1 - 149
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	11 - 58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,93,294.88	3.55	25	92,316.50	93,868.28	2 - 89
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
Total		1634	19,40,699.03	23,29,746.02	20.05	552	8,23,289.61	10,55,842.45	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	75	1,19,490.46	1,69,432.76	41.80	31	67,052.64	1,14,266.48	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	11	5,692.01	11,138.52	15 - 118
3	ASSAM	48	26,216.03	31,003.54	18.26	18	8,536.32	10,384.47	1 - 149
4	BIHAR	94	90,608.62	1,27,647.16	40.88	19	37,443.97	62,697.40	6 - 118
5	GOA	10	5,325.87	5,336.30	0.20	0	0.00	0.00	-
6	GUJARAT	56	64,665.47	71,517.57	10.60	15	30,118.07	36,362.47	2 - 120
7	HARYANA	40	30,880.96	33,245.93	7.66	10	7,716.19	9,850.32	1 - 118
8	HIMACHAL PRADESH	13	18,053.17	28,163.70	56.00	3	6,676.35	12,753.87	15 - 147
9	JAMMU AND KASHMIR	12	16,534.64	42,210.89	155.29	4	8,792.63	34,241.63	18 - 235
10	KARNATAKA	63	73,084.28	76,598.88	4.81	25	47,871.66	48,822.24	3 - 264
11	KERALA	20	36,309.60	39,755.52	9.49	9	17,162.14	18,898.34	8 - 89
12	MADHYA PRADESH	78	86,555.71	93,301.25	7.79	35	31,809.42	37,546.60	2 - 54
13	MAHARASHTRA	257	2,35,637.97	2,45,422.34	4.15	79	1,16,023.29	1,18,447.11	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	3	5,188.43	13,198.46	36 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	2	843.19	843.19	16 - 19
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	15,515.91	4.54	4	3,525.63	4,199.11	36 - 79
18	ODISHA	92	1,06,784.06	1,09,230.71	2.29	37	46,885.19	49,322.48	3 - 180
19	PUNJAB	27	13,539.35	15,038.78	11.07	7	3,169.78	3,570.93	1 - 28
20	RAJASTHAN	63	47,345.31	54,833.78	15.82	16	19,889.85	25,553.86	1 - 70
21	SIKKIM	9	3,476.73	6,368.17	83.17	2	333.87	420.73	76 - 82
22	TAMIL NADU	65	1,16,109.47	1,34,527.19	15.86	26	72,235.51	80,434.28	2 - 133
23	TRIPURA	7	1,977.29	2,139.55	8.21	2	908.56	989.00	6 - 21
24	UTTAR PRADESH	118	1,44,722.96	1,49,516.00	3.31	34	47,102.02	51,272.75	2 - 68
25	WEST BENGAL	63	56,442.22	68,725.50	21.76	27	29,591.66	36,827.05	9 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	25	55,985.34	63,868.57	14.08	8	4,226.33	5,106.90	3 - 83
29	CHHATISGARH	34	73,625.10	85,279.62	15.83	14	39,819.26	50,888.18	3 - 84
30	JHARKHAND	47	62,036.07	67,344.06	8.56	16	21,811.56	23,206.78	9 - 120
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	10	25,218.73	33,623.06	6 - 114
32	TELANGANA	56	39,959.69	42,435.36	6.20	24	20,904.77	21,241.26	3 - 156
33	MULTI STATE	131	3,17,640.98	4,24,187.55	33.54	54	86,746.32	1,26,425.70	4 - 252
Total		1634	19,40,699.03	23,29,746.02	20.05	552	8,23,289.61	10,55,842.45	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	4	77,000.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	106	1,03,508.90	1,02,788.94	-0.70	38	21,077.93	21,118.25	0 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34 - 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
7	STEEL	9	26,228.23	33,485.23	27.67	0	0.00	0.00	-
8	PETROLEUM	152	2,53,837.66	2,55,016.79	0.46	29	63,559.74	63,831.70	1 - 110
9	POWER	75	3,06,777.01	3,55,386.08	15.85	35	88,889.48	1,18,080.31	2 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	11	4,693.67	4,793.45	2 - 83
12	RAILWAYS	315	5,69,290.78	6,60,824.02	16.08	126	1,96,108.57	2,31,710.25	1 - 264
13	ROAD TRANSPORT AND HIGHWAYS	855	5,26,111.43	5,30,872.20	0.90	213	1,44,480.32	1,38,163.36	0 - 149
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	1	13,334.00	24,664.00	58 - 58
16	URBAN DEVELOPMENT	63	1,87,205.75	1,93,294.88	3.25	24	81,226.85	82,616.91	0 - 89
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
Total		1634	21,10,797.64	23,29,746.02	10.37	489	7,04,497.54	8,24,989.48	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns[^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	106	1,03,508.90	1,02,788.94	-0.70	10	19,818.83	20,957.14	5.74
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
8	PETROLEUM	152	2,53,837.66	2,55,016.79	0.46	13	16,950.80	20,051.58	18.29
9	POWER	75	3,06,777.01	3,55,386.08	15.85	26	1,27,696.04	1,76,822.16	38.47
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	3	1,076.25	1,193.54	10.90
12	RAILWAYS	315	5,69,290.78	6,60,824.02	16.08	155	1,37,078.75	2,38,856.43	74.25
13	ROAD TRANSPORT AND HIGHWAYS	855	5,26,111.43	5,30,872.20	0.90	102	58,769.29	77,379.59	31.67
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	83.58
16	URBAN DEVELOPMENT	63	1,87,205.75	1,93,294.88	3.25	10	28,341.60	34,430.73	21.48
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
Total		1634	21,10,797.64	23,29,746.02	10.37	328	4,34,176.59	6,81,973.91	57.07

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	133- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	106	1,03,508.90	1,02,788.94	-0.70	8	2,393.89	3,309.66	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34- 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
7	STEEL	9	26,228.23	33,485.23	27.67	0	0.00	0.00	0- 0
8	PETROLEUM	152	2,53,837.66	2,55,016.79	0.46	4	4,392.47	4,792.21	4- 110
9	POWER	75	3,06,777.01	3,55,386.08	15.85	16	70,692.54	99,883.37	12- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	1	414.11	513.89	83- 83
12	RAILWAYS	315	5,69,290.78	6,60,824.02	16.08	61	58,139.66	99,280.99	6- 252
13	ROAD TRANSPORT AND HIGHWAYS	855	5,26,111.43	5,30,872.20	0.90	32	18,818.40	23,856.85	1- 143
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	1	13,334.00	24,664.00	58- 58
16	URBAN DEVELOPMENT	63	1,87,205.75	1,93,294.88	3.25	4	7,285.00	8,675.06	17- 40
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
Total		1634	21,10,797.64	23,29,746.02	10.37	132	1,89,964.44	3,28,354.67	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	106	1,02,335.60	1,02,788.94	0.44	9	8,301.00	10,390.07	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34- 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	62- 62
8	PETROLEUM	152	2,46,655.89	2,55,016.79	3.39	17	30,257.31	36,284.99	1- 110
9	POWER	75	2,81,499.09	3,55,386.08	26.25	24	1,32,442.77	1,91,668.56	12- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	1	414.11	513.89	83- 83
12	RAILWAYS	315	4,61,117.38	6,60,824.02	43.31	83	80,932.28	1,70,910.21	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	855	5,09,411.08	5,30,872.20	4.21	35	23,498.27	32,093.91	1- 143
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	11- 58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,93,294.88	3.55	6	7,948.75	9,500.53	7- 70
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
Total		1634	19,40,699.03	23,29,746.02	20.05	185	3,51,158.66	5,96,443.90	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	75	1,19,490.46	1,69,432.76	41.80	5	14,004.98	61,590.13	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	2	2,635.83	8,082.34	36 - 118
3	ASSAM	48	26,216.03	31,003.54	18.26	6	1,853.86	3,858.96	4 - 143
4	BIHAR	94	90,608.62	1,27,647.16	40.88	10	30,865.91	56,127.05	12 - 118
5	GOA	10	5,325.87	5,336.30	0.20	0	0.00	0.00	-
6	GUJARAT	56	64,665.47	71,517.57	10.60	5	13,479.15	19,879.88	12 - 120
7	HARYANA	40	30,880.96	33,245.93	7.66	2	1,395.00	3,661.50	100 - 111
8	HIMACHAL PRADESH	13	18,053.17	28,163.70	56.00	1	3,919.59	9,997.11	147 - 147
9	JAMMU AND KASHMIR	12	16,534.64	42,210.89	155.29	1	2,500.00	27,949.00	235 - 235
10	KARNATAKA	63	73,084.28	76,598.88	4.81	6	4,136.21	5,400.22	3 - 36
11	KERALA	20	36,309.60	39,755.52	9.49	5	12,261.94	14,022.18	15 - 33
12	MADHYA PRADESH	78	86,555.71	93,301.25	7.79	6	17,231.95	23,065.44	6 - 36
13	MAHARASHTRA	257	2,35,637.97	2,45,422.34	4.15	19	23,471.40	31,050.07	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	108 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	0	0.00	0.00	-
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	15,515.91	4.54	1	2,326.52	3,000.00	79 - 79
18	ODISHA	92	1,06,784.06	1,09,230.71	2.29	14	24,067.16	30,004.02	3 - 180
19	PUNJAB	27	13,539.35	15,038.78	11.07	3	1,589.83	1,990.98	1 - 28
20	RAJASTHAN	63	47,345.31	54,833.78	15.82	7	14,217.88	19,881.89	6 - 48
21	SIKKIM	9	3,476.73	6,368.17	83.17	1	182.28	269.14	82 - 82
22	TAMIL NADU	65	1,16,109.47	1,34,527.19	15.86	8	17,651.33	26,599.21	12 - 133
23	TRIPURA	7	1,977.29	2,139.55	8.21	2	908.56	989.00	6 - 21
24	UTTAR PRADESH	118	1,44,722.96	1,49,516.00	3.31	8	14,750.30	19,482.81	5 - 68
25	WEST BENGAL	63	56,442.22	68,725.50	21.76	11	16,382.67	23,633.10	12 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	25	55,985.34	63,868.57	14.08	2	1,633.32	2,513.89	17 - 83
29	CHHATISGARH	34	73,625.10	85,279.62	15.83	6	32,944.43	44,443.91	9 - 62
30	JHARKHAND	47	62,036.07	67,344.06	8.56	4	16,497.75	17,892.97	9 - 36
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	5	7,847.16	16,277.99	19 - 114
32	TELANGANA	56	39,959.69	42,435.36	6.20	7	3,574.19	4,563.95	12 - 144
33	MULTI STATE	131	3,17,640.98	4,24,187.55	33.54	31	60,467.11	1,00,226.19	8 - 240
Total		1634	19,40,699.03	23,29,746.02	20.05	185	3,51,158.66	5,96,443.90	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	155	2
2	ROAD TRANSPORT AND HIGHWAYS	150	2
3	PETROLEUM	56	2
4	POWER	42	2
5	URBAN DEVELOPMENT	16	0
6	COAL	15	0
7	STEEL	6	0
8	ATOMIC ENERGY	4	0
9	CIVIL AVIATION	2	0
10	TELECOMMUNICATIONS	2	0
11	MINES	1	0
12	HEAVY INDUSTRY	1	0
13	HEALTH AND FAMILY WELFARE	1	0
14	SHIPPING AND PORTS	1	0
15	WATER RESOURCES	1	0
	Total	453	8

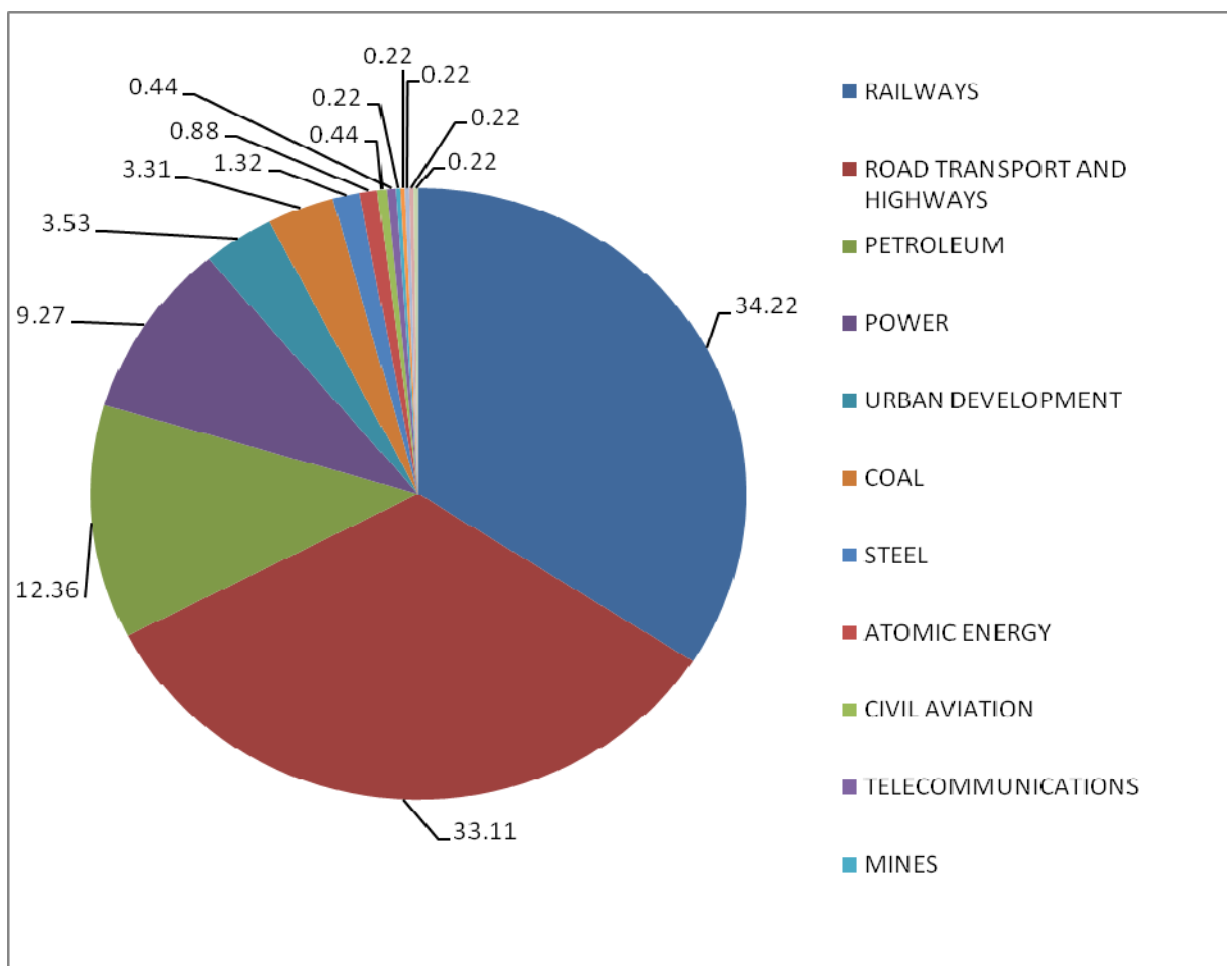


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	448
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	13
No of Projects in Current Month	453

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	187 (41.28%)	6 (1.32%)	96 (21.19%)	52 (11.48%)	112(4.72%)	453
Latest Approved (Date)	151 (33.33%)	6 (1.32%)	139(30.68%)	43 (9.49%)	114(5.17%)	453

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	363	12,15,928.86	14,28,555.36	5,52,715.18	38.70	2,12,626.50	17.50
Project with Revision in Cost	90	4,03,503.91	4,03,584.46	2,21,963.00	55.00	80.55	.00
Total	453	16,19,432.77	18,32,139.82	7,74,678.18	42.28	2,12,707.05	13.13
Original Cost of All Projects							
Original Cost	453	14,58,776.49	18,32,139.82	7,74,678.18	42.28	3,73,363.33	25.59

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	187	6,70,323.71	8,97,200.35	4,65,044.79	51.80	2,26,876.64	33.85
Latest Approved (RCE)	151	5,58,441.71	6,78,736.73	3,08,343.83	45.40	1,20,295.02	21.54

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	8	28,009.99	35,921.25	24,518.61	68.30	7,911.26	28.20
Total	8	28,009.99	35,921.25	24,518.61	68.26	7,911.26	28.24

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	15	63,354.75	64,528.85	1.85	2	23,144.11	24,318.21	5.07
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	56	2,06,905.35	2,14,210.01	3.53	16	38,761.90	48,089.93	24.06
7	POWER	42	2,68,238.12	3,41,692.36	27.38	24	1,52,955.09	2,26,926.38	48.36
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0.00
10	RAILWAYS	155	3,92,364.27	5,80,915.59	48.06	97	1,47,036.65	3,41,119.98	132.00
11	ROAD TRANSPORT AND HIGHWAYS	150	2,20,454.23	2,38,786.75	8.32	30	40,634.62	59,269.07	45.86
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	16	1,72,867.22	1,79,131.70	3.62	5	26,033.88	32,298.36	24.06
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		453	14,58,776.49	18,32,139.82	25.59	181	4,99,047.29	8,81,242.98	76.59

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	21	98,791.39	1,48,859.72	50.68	8	20,509.81	70,936.14	245.86
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	2	8,782.23	27,423.68	212.26
3	ASSAM	8	11,678.49	14,282.38	22.30	3	2,127.51	4,868.01	128.81
4	BIHAR	23	58,263.22	91,887.56	57.71	12	31,165.06	64,789.40	107.89
5	GUJARAT	18	46,707.74	53,208.72	13.92	5	16,441.81	22,942.79	39.54
6	HARYANA	12	17,495.51	19,355.01	10.63	1	1,108.00	2,967.50	167.82
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	2	6,886.58	16,997.11	146.82
8	JAMMU AND KASHMIR	8	15,337.84	41,014.09	167.40	2	4,659.00	30,468.00	553.96
9	KARNATAKA	19	55,423.75	58,665.63	5.85	8	10,837.45	14,275.34	31.72
10	KERALA	9	30,871.86	34,193.65	10.76	6	14,996.96	18,342.79	22.31
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	8	28,044.20	36,348.78	29.61
12	MAHARASHTRA	52	1,54,949.73	1,67,635.94	8.19	19	36,356.65	49,814.73	37.02
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	181.17
14	MEGHALAYA	1	906.46	6,000.00	561.92	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	109.80
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	28.95
17	ODISHA	34	82,737.16	84,721.70	2.40	10	25,048.54	30,532.65	21.89
18	PUNJAB	3	3,627.54	4,765.00	31.36	1	1,388.34	2,525.80	81.93
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	3	14,015.71	20,158.75	43.83
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	13	36,705.21	53,730.54	46.38
22	UTTAR PRADESH	42	1,11,806.06	1,16,702.16	4.38	9	35,631.09	41,468.32	16.38
23	WEST BENGAL	23	40,606.18	51,886.85	27.78	10	17,240.88	28,552.59	65.61
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
25	DELHI	7	50,481.91	58,224.75	15.34	3	6,254.39	13,997.23	123.80
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	7	34,693.96	46,471.98	33.95
27	JHARKHAND	13	49,100.48	53,989.92	9.96	5	21,821.72	26,711.16	22.41
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	8,654.06	17,090.60	97.49
29	TELANGANA	5	18,567.06	20,644.30	11.19	2	2,378.60	4,455.84	87.33
30	MULTI STATE	59	2,87,449.36	3,89,331.54	35.44	33	1,01,879.43	2,04,743.11	100.97
Total		453	14,58,776.49	18,32,139.82	25.59	181	4,99,047.29	8,81,242.98	76.59

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	15	63,354.75	64,528.85	1.85	2	6,962.16	8,135.46	24 - 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	25,381.34	32,638.34	28.59	6	25,381.34	32,638.34	12 - 62
6	PETROLEUM	56	2,06,905.35	2,14,210.01	3.53	20	94,803.47	98,828.64	1 - 110
7	POWER	42	2,68,238.12	3,41,692.36	27.38	26	1,62,772.86	2,21,666.68	4 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	-
10	RAILWAYS	155	3,92,364.27	5,80,915.59	48.06	79	1,42,918.41	2,21,110.54	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	150	2,20,454.23	2,38,786.75	8.32	40	57,598.29	63,690.89	1 - 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	16	1,72,867.22	1,79,131.70	3.62	7	86,815.14	88,101.93	2 - 64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		453	14,58,776.49	18,32,139.82	25.59	187	6,70,323.71	8,97,200.35	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,48,859.72	50.68	10	59,598.89	1,06,825.54	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	2	3,750.00	9,180.44	60 - 118
3	ASSAM	8	11,678.49	14,282.38	22.30	2	2,850.35	3,910.86	12 - 81
4	BIHAR	23	58,263.22	91,887.56	57.71	8	31,710.79	55,850.64	12 - 118
5	GUJARAT	18	46,707.74	53,208.72	13.92	5	26,057.77	31,659.26	2 - 54
6	HARYANA	12	17,495.51	19,355.01	10.63	2	4,637.00	6,496.50	5 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	2	6,405.52	12,483.04	15 - 147
8	JAMMU AND KASHMIR	8	15,337.84	41,014.09	167.40	4	8,792.63	34,241.63	18 - 235
9	KARNATAKA	19	55,423.75	58,665.63	5.85	10	39,415.14	40,342.70	3 - 264
10	KERALA	9	30,871.86	34,193.65	10.76	5	15,319.19	16,962.71	8 - 33
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	7	20,977.06	26,426.55	6 - 26
12	MAHARASHTRA	52	1,54,949.73	1,67,635.94	8.19	25	89,458.58	95,393.35	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	34	82,737.16	84,721.70	2.40	16	39,210.04	41,194.57	3 - 180
18	PUNJAB	3	3,627.54	4,765.00	31.36	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	1	12,320.00	17,079.00	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	12	64,697.33	72,924.78	6 - 133
22	UTTAR PRADESH	42	1,11,806.06	1,16,702.16	4.38	15	38,372.65	42,417.85	2 - 40
23	WEST BENGAL	23	40,606.18	51,886.85	27.78	13	24,050.33	30,868.83	14 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
25	DELHI	7	50,481.91	58,224.75	15.34	2	2,613.73	3,394.52	17 - 31
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	7	37,249.02	48,139.42	3 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	4	18,278.97	19,345.48	9 - 32
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	23,343.06	31,505.53	15 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	3	13,026.06	13,303.46	7 - 156
30	MULTI STATE	59	2,87,449.36	3,89,331.54	35.44	24	72,929.36	1,10,865.93	4 - 252
Total		453	14,58,776.49	18,32,139.82	25.59	187	6,70,323.71	8,97,200.35	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	4	77,000.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	15	64,528.05	64,528.85	0.00	2	8,135.46	8,135.46	24 - 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	25,381.34	32,638.34	28.59	0	0.00	0.00	-
6	PETROLEUM	56	2,13,390.25	2,14,210.01	0.38	7	54,222.97	54,357.44	1 - 110
7	POWER	42	2,93,516.04	3,41,692.36	16.41	16	81,234.67	1,10,093.53	4 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	-
10	RAILWAYS	155	4,99,785.84	5,80,915.59	16.23	71	1,70,669.68	2,02,137.69	3 - 264
11	ROAD TRANSPORT AND HIGHWAYS	150	2,29,401.55	2,38,786.75	4.09	42	65,831.75	64,302.81	0 - 100
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	16	1,73,169.31	1,79,131.70	3.44	6	75,395.14	76,681.93	13 - 64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		453	16,19,432.77	18,32,139.82	13.13	151	5,58,441.71	6,78,736.73	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule RS.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	15	64,528.05	64,528.85	0.00	1	17,237.00	17,237.80	0.00
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	56	2,13,390.25	2,14,210.01	0.38	7	13,807.27	16,382.59	18.65
7	POWER	42	2,93,516.04	3,41,692.36	16.41	20	1,25,822.18	1,74,515.55	38.70
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0.00
10	RAILWAYS	155	4,99,785.84	5,80,915.59	16.23	80	1,08,865.21	1,98,987.97	82.78
11	ROAD TRANSPORT AND HIGHWAYS	150	2,29,401.55	2,38,786.75	4.09	23	29,367.89	44,043.87	49.97
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	16	1,73,169.31	1,79,131.70	3.44	5	26,335.97	32,298.36	22.64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		453	16,19,432.77	18,32,139.82	13.13	140	3,63,937.56	5,93,659.01	63.12

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	133- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	15	64,528.05	64,528.85	0.00	0	0.00	0.00	0- 0
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	0	0.00	0.00	0- 0
6	PETROLEUM	56	2,13,390.25	2,14,210.01	0.38	1	2,915.00	3,049.47	110- 110
7	POWER	42	2,93,516.04	3,41,692.36	16.41	12	69,284.06	98,142.92	12- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0- 0
10	RAILWAYS	155	4,99,785.84	5,80,915.59	16.23	33	46,509.79	83,244.45	6- 252
11	ROAD TRANSPORT AND HIGHWAYS	150	2,29,401.55	2,38,786.75	4.09	11	10,655.43	14,009.63	2- 33
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	16	1,73,169.31	1,79,131.70	3.44	2	6,401.00	7,687.79	17- 29
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		453	16,19,432.77	18,32,139.82	13.13	62	1,62,742.32	2,93,187.13	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	15	63,354.75	64,528.85	1.85	1	5,907.11	7,080.41	48- 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	62- 62
6	PETROLEUM	56	2,06,905.35	2,14,210.01	3.53	10	27,585.94	32,737.08	1- 110
7	POWER	42	2,68,238.12	3,41,692.36	27.38	20	1,31,034.29	1,89,928.11	12- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0- 0
10	RAILWAYS	155	3,92,364.27	5,80,915.59	48.06	46	66,807.56	1,48,981.34	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	150	2,20,454.23	2,38,786.75	8.32	15	17,085.22	23,201.79	1- 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	16	1,72,867.22	1,79,131.70	3.62	2	6,401.00	7,687.79	17- 29
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		453	14,58,776.49	18,32,139.82	25.59	100	3,21,102.16	5,53,468.39	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,48,859.72	50.68	4	13,770.48	61,355.13	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	1	2,496.90	7,927.34	118 - 118
3	ASSAM	8	11,678.49	14,282.38	22.30	1	385.20	1,532.00	12 - 12
4	BIHAR	23	58,263.22	91,887.56	57.71	6	29,019.12	53,158.97	12 - 118
5	GUJARAT	18	46,707.74	53,208.72	13.92	2	12,288.74	17,890.23	12 - 54
6	HARYANA	12	17,495.51	19,355.01	10.63	1	1,108.00	2,967.50	100 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	1	3,919.59	9,997.11	147 - 147
8	JAMMU AND KASHMIR	8	15,337.84	41,014.09	167.40	1	2,500.00	27,949.00	235 - 235
9	KARNATAKA	19	55,423.75	58,665.63	5.85	3	2,775.43	3,719.00	3 - 16
10	KERALA	9	30,871.86	34,193.65	10.76	4	12,006.19	13,673.75	15 - 33
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	5	16,734.90	22,184.39	6 - 26
12	MAHARASHTRA	52	1,54,949.73	1,67,635.94	8.19	12	21,516.05	28,222.69	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	34	82,737.16	84,721.70	2.40	9	22,712.87	28,196.97	3 - 180
18	PUNJAB	3	3,627.54	4,765.00	31.36	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	1	12,320.00	17,079.00	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	6	17,160.09	25,387.54	12 - 133
22	UTTAR PRADESH	42	1,11,806.06	1,16,702.16	4.38	4	13,450.10	17,668.28	5 - 40
23	WEST BENGAL	23	40,606.18	51,886.85	27.78	7	15,417.13	22,250.67	14 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
25	DELHI	7	50,481.91	58,224.75	15.34	1	1,219.21	2,000.00	17 - 17
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	5	32,792.00	43,984.42	9 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	2	16,090.78	17,157.29	9 - 27
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	3	7,127.06	15,289.53	76 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	1	1,266.60	1,544.00	36 - 36
30	MULTI STATE	59	2,87,449.36	3,89,331.54	35.44	17	53,851.56	91,788.13	8 - 178
Total		453	14,58,776.49	18,32,139.82	25.59	100	3,21,102.16	5,53,468.39	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

List of projects completed/dropped/Frozen during current month Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	198.59	03/2016	198.59	08/2019	169.15
2	GOKUL	11/2014	267.67	03/2018	267.67	08/2019	209.47
	<u>DEFENCE PRODUCTION</u>						
3	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	05/2018	167.69	08/2019	141.83
4	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	08/2020	285.95	08/2019	84.40
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
5	IMPROVEMENT FROM KM 0/0 TO 68/0 EPC	12/2013	319.80	10/2016	319.80	N.A.	268.01
6	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	03/2015	226.31	10/2017	226.31	N.A.	137.43
7	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA	07/2013	251.92	10/2015	251.92	N.A.	225.98
8	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	319.80	05/2016	320.00	N.A.	268.27
9	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA	07/2013	265.35	10/2015	265.35	N.A.	247.56
10	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2	08/2016	574.19	07/2017	574.19	07/2019	456.98
11	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA	03/2015	229.29	11/2015	229.29	N.A.	163.40
	<u>SHIPPING AND PORTS</u>						
12	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) Public Private (SPV)	10/2002	150.00	03/2006	600.00	N.A.	0.00
13	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB PPP (BOT)	01/2007	366.39	12/2010	669.46	N.A.	0.00
14	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	600.00	12/2017	257.90	08/2019	0.00
15	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI	07/2016	1,799.00	05/2021	1,799.00	05/2019	347.03

List of projects completed/dropped/Frozen during current month Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	KERALA						
16	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	05/2016	970.00	05/2020	970.00	05/2020	322.54
17	SETHUSAMUDRAM SHIP CHANNEL PROJECT Public Private (SPV)	06/2005	2,427.40	10/2008	2,427.40	N.A.	0.00
18	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED PPP (ANNUITY)	02/2015	244.50	12/2017	275.98	N.A.	0.00

TABLE-26

List of projects added Rs.150 Crore and above					(August 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	NORTH URIMARI EXPANSION OCP	3/2019	1,553.06	3/2023	1,553.06	3/2023
2	GANDHIGRAM UG MINE	8/2019	414.16	3/2026	414.16	3/2026
3	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	998.71	3/2023	998.71	3/2023
	<u>HEALTH AND FAMILY WELFARE</u>					
4	AIIMS BILASPUR	4/2018	1,351.00	9/2021	1,351.00	9/2021
	<u>PETROLEUM</u>					
5	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	248.55	6/2022	248.55	6/2022
	<u>POWER</u>					
6	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	1,885.13	12/2018	1,885.13	3/2020
7	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	529.68	11/2018	529.68	3/2020
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
8	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	269.69	9/2019	269.69	12/2019
9	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 PPP BOT (Hybrid Annuity))	11/2017	2,159.00	1/2019	2,159.00	-
10	ISMAILABAD-NARNAUL PKG-5	1/2019	1,051.91	/	1,051.91	-
11	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	1,979.00	/	1,979.00	-
12	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	218.90	3/2020	218.90	3/2020
13	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	388.83	12/2019	388.83	12/2019
14	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	2,926.42	/	2,926.42	-
15	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	178.13	/	178.13	-
16	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	743.88	/	743.88	-
17	CONSTRUCTION TO TWO LANE WITH PAVED	1/2019	264.50	3/2021	264.50	3/2021

List of projects added Rs.150 Crore and above					(August 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD					
18	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	351.00	6/2021	351.00	6/2021
19	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	1,049.51	/	1,049.51	-
20	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	243.89	/	243.89	-
21	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	281.45	/	281.45	-
22	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	306.59	/	306.59	-
23	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	296.50	9/2020	296.50	9/2020
24	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN	3/2018	288.30	8/2020	288.30	8/2020
25	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	185.18	2/2020	185.18	2/2020
26	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	263.89	4/2020	263.89	4/2020
27	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	209.10	10/2019	209.10	10/2019
28	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	208.88	10/2019	208.88	10/2019
29	ISMAILABAD-NARNAUL PKG-6	1/2019	1,120.06	/	1,120.06	-
30	ISMAILABAD-NARNAUL PKG-7	1/2019	1,137.42	/	1,137.42	-
31	ISMAILABAD-NARNAUL PKG-8	1/2019	1,033.19	/	1,033.19	-
32	ISMAILABAD-NARNAUL PKG-2	1/2019	1,243.45	/	1,243.45	-
33	ISMAILABAD-NARNAUL PKG-3	1/2019	889.36	/	889.36	-
34	ISMAILABAD-NARNAUL PKG-4	1/2019	1,018.79	/	1,018.79	-
35	ISMAILABAD-NARNAUL PKG-1	1/2019	996.65	/	996.65	-

TABLE-27

Milestones (Cumulative due & achieved) Rs.150 Crore and above

Total	5455
Achieved up to month	2789

TABLE-28

<u>List of projects reporting additional delayed Rs. 150 Crore and above</u>							(August 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 SCCL	413.84	413.84	03/2019	03/2021	03/2022	12
2	KAKATIYAKHANI OPENCASE-2 PROJECT SCCL	397.09	442.42	03/2019	09/2017	03/2020	30
3	KALYANIKHANI OPENCASE PROJECT SCCL	417.33	384.32	07/2016	04/2017	03/2020	35
4	RFR OF MANUGURU OC PROJECT SCCL	430.45	415.37	03/2016	12/2016	03/2020	39
	<u>PETROLEUM</u>						
5	HALDIA LPG IMPORT FACILITY BPCL	694.00	1,097.54	10/2018	11/2019	12/2019	1
6	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY IOCL	822.66	822.66	11/2018	07/2019	08/2019	1
7	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE MANGALORE REFIN	135.00	170.70	03/2019	08/2019	09/2019	1
8	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	08/2019	10/2019	2
9	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA OIL	543.91	682.90	02/2020	02/2020	06/2020	4
10	BS-VI PROJECT AT PANIPAT REFINERY IOCL	3,529.00	3,529.00	07/2019	07/2019	12/2019	5
	<u>POWER</u>						
11	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	7,927.34	12/2009	08/2019	10/2019	2
12	DARLIPALLI STPP STAGE-I (2X800 MW) NTPC	12,532.44	13,740.53	12/2018	06/2020	09/2020	3
	<u>RAILWAYS</u>						
13	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND SER	148.77	377.00	12/2016	11/2019	12/2019	1
14	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR ECR	180.82	726.31	N.A.	09/2019	10/2019	1
15	KHURDA ROAD-BOLANGIR(NL)ECOR ECR	2,923.13	3,791.66	03/2009	12/2023	03/2024	3


List of projects reporting additional delayed Rs. 150 Crore and above							(August 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	ALWAR-BANDIKUI DOUBLING NWR	242.09	410.00	02/2019	12/2019	05/2020	5
17	SAMBALPUR - ANGUL RLY. ELECTRIFICATION ECOR	155.81	238.03	03/2020	03/2020	03/2021	12
18	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE ECOR	701.61	810.02	11/2018	03/2021	03/2022	12
19	JHARSUGUDA-BILASPUR 4TH LINE SECR	1,973.00	1,973.66	03/2021	12/2021	12/2022	12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
20	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 NHDP EPC	445.89	653.29	03/2017	08/2019	09/2019	1
21	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 NHAI	602.95	507.70	06/2016	08/2019	09/2019	1
22	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	897.03	11/2018	11/2019	12/2019	1
23	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH MORTH	445.89	653.29	03/2017	08/2019	09/2019	1
24	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH PWD	164.54	164.54	08/2015	08/2019	09/2019	1
25	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP NHDP BOT (TOLL)	410.72	410.72	04/2015	08/2019	10/2019	2
26	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 NHAI	574.28	537.16	07/2018	07/2019	09/2019	2
27	HOSPET-BELLARY-KARNATAKA AP BORDER NHAI	1,167.42	870.00	03/2019	06/2020	08/2020	2
28	NALBARI T BIJNI (AS-7) NHAI	208.00	230.00	04/2008	12/2019	03/2020	3
29	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 NHAI PPP (BOT)	972.50	972.50	07/2017	07/2019	10/2019	3
30	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 NHAI	479.20	479.20	05/2018	09/2019	12/2019	3
31	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST NHAI	244.90	244.90	05/2019	09/2019	12/2019	3
32	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 NHAI	505.00	504.00	05/2018	05/2020	09/2020	4
33	PUNE-SATARA(NH-4) NHAI PPP (BOT)	1,724.55	1,724.55	03/2013	07/2019	12/2019	5

<u>List of projects reporting additional delayed Rs. 150 Crore and above</u>							(August 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
34	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION NHAI	227.49	227.49	01/2019	03/2019	08/2019	5
35	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 PWD	192.67	192.67	07/2019	07/2019	12/2019	5
36	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P MORTH	418.03	418.03	08/2018	02/2020	08/2020	6
37	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A NHAI	2,136.97	2,136.97	12/2018	10/2019	07/2020	9
38	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 NHIDCL	396.52	396.52	08/2016	08/2019	06/2020	10
39	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	174.34	03/2008	09/2019	08/2020	11
40	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 NHAI	720.00	720.00	N.A.	10/2019	10/2020	12
	<u>URBAN DEVELOPMENT</u>						
41	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN CPWD	549.31	559.47	07/2019	12/2019	02/2020	2
42	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR CPWD	790.79	800.00	03/2022	06/2021	03/2022	9


TABLE-29

<u>Sector wise analysis of projects Rs.150 Crore and above</u>					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	770,00.00	80,348.00	46,384.74
CIVIL AVIATION	13	8,607.51	86,07.51	8,734.44	1,353.49
COAL	106	1,02,335.60	1,035,08.90	1,02,788.94	35,560.62
FERTILISERS	5	1,299.07	12,99.07	1,310.72	685.62
INFORMATION AND BROADCASTING	3	969.43	9,69.43	969.43	29.80
MINES	5	7,078.62	70,78.62	7,078.62	587.94
STEEL	9	26,228.23	262,28.23	33,485.23	23,168.02
PETROLEUM	152	2,46,655.89	2,538,37.66	2,55,016.79	91,066.77
POWER	75	2,81,499.09	3,067,77.01	3,55,386.08	2,14,664.65
HEAVY INDUSTRY	1	1,554.00	15,54.00	1,554.00	335.03
HEALTH AND FAMILY WELFARE	21	9,480.23	94,80.23	9,597.52	3,377.82
RAILWAYS	315	4,61,117.38	5,692,90.78	6,60,824.02	1,90,365.20
ROAD TRANSPORT AND HIGHWAYS	855	5,09,411.08	5,261,11.43	5,30,872.20	2,55,947.17
SHIPPING AND PORTS	1	4,200.00	53,69.18	5,369.18	1,394.52
TELECOMMUNICATIONS	4	16,095.23	160,95.23	27,333.53	9,135.56
URBAN DEVELOPMENT	63	1,86,663.06	1,872,05.75	1,93,294.88	84,672.92
WATER RESOURCES	2	10,384.61	103,84.61	55,782.44	16,450.19
Grand total	1634	19,40,699.03	21,10,797.64	23,29,746.02	9,75,180.06

Graphical Presentation of All Projects w.r.t. Original Schedule

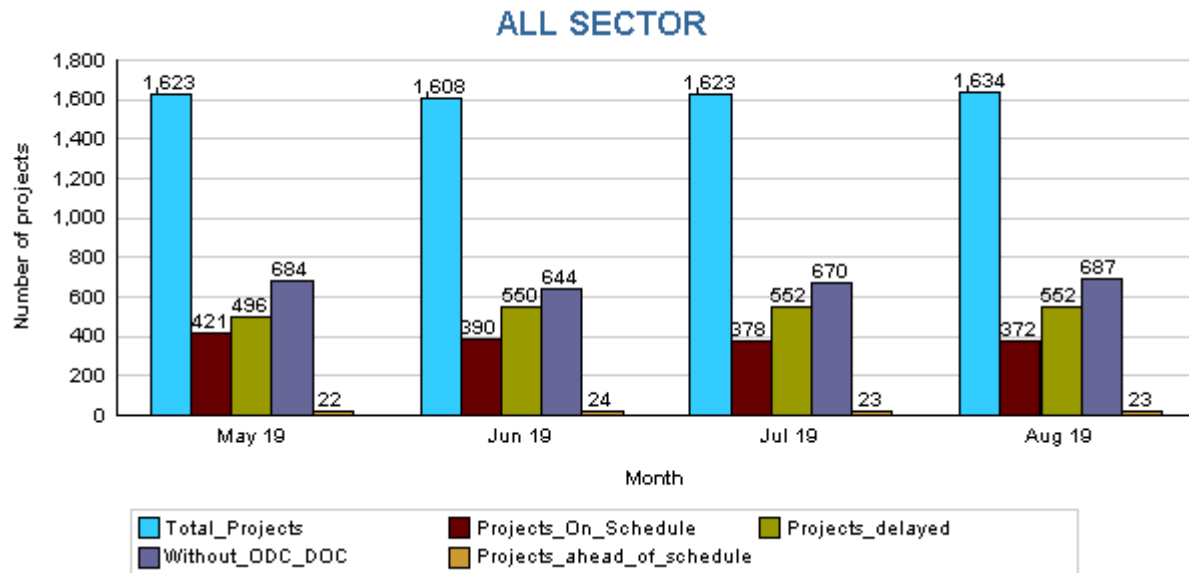


Break-up of 552 Delayed projects in August 2019

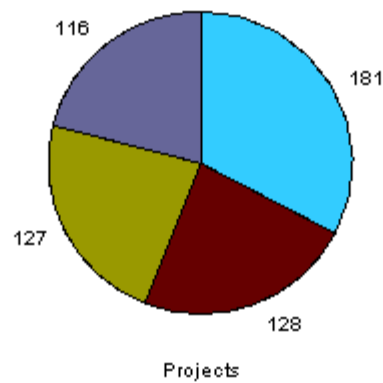


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

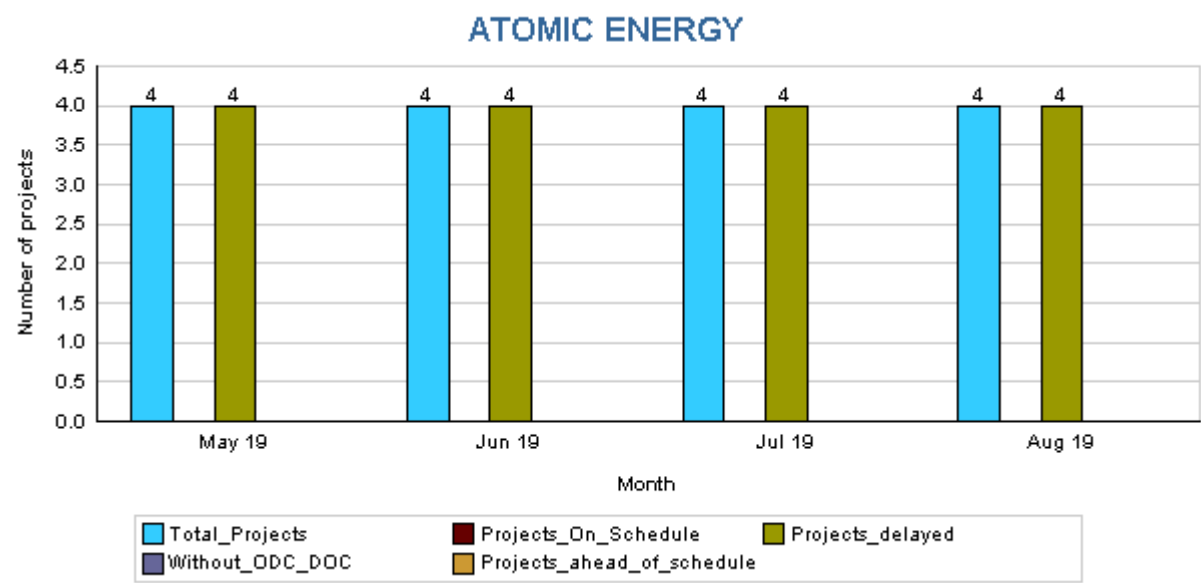


Break-up of 4 Delayed projects in August 2019

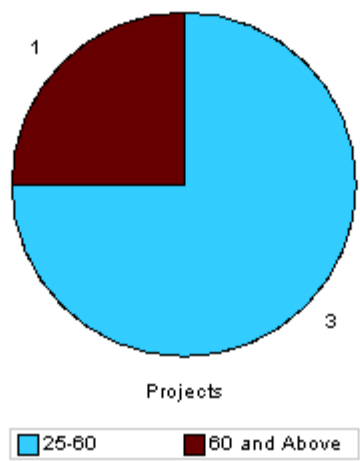


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

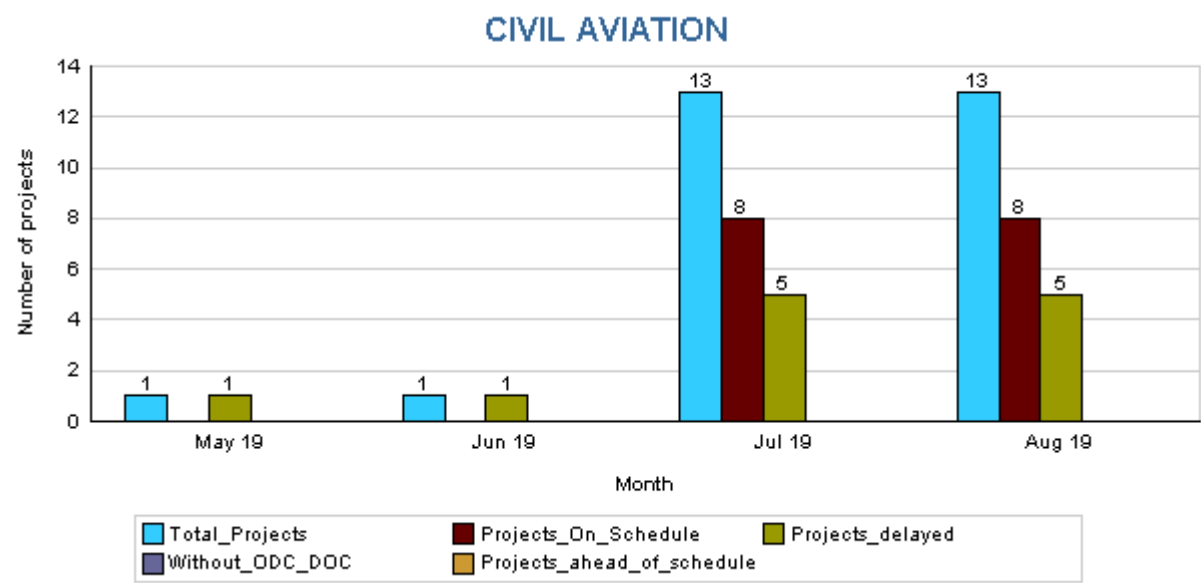


Break-up of 5 Delayed projects in August 2019

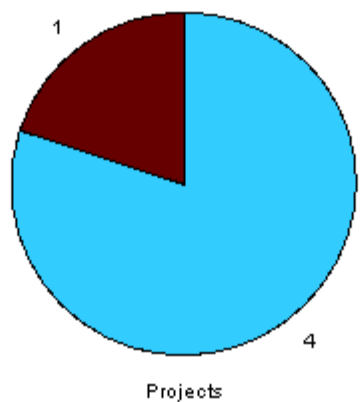


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

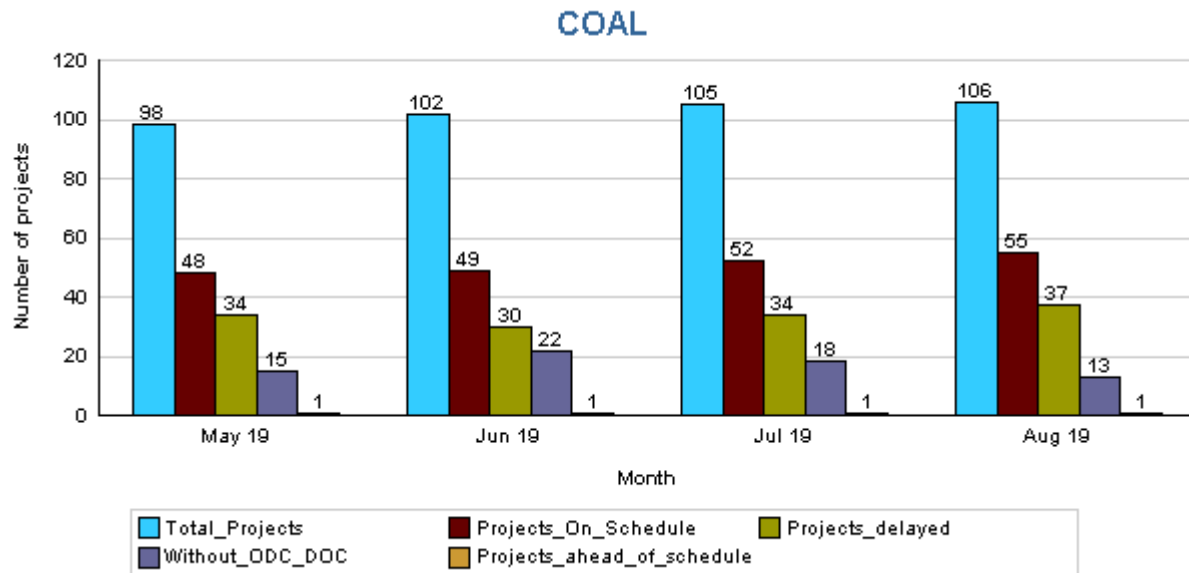


Break-up of 37 Delayed projects in August 2019

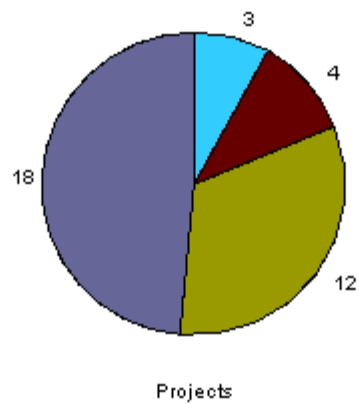


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

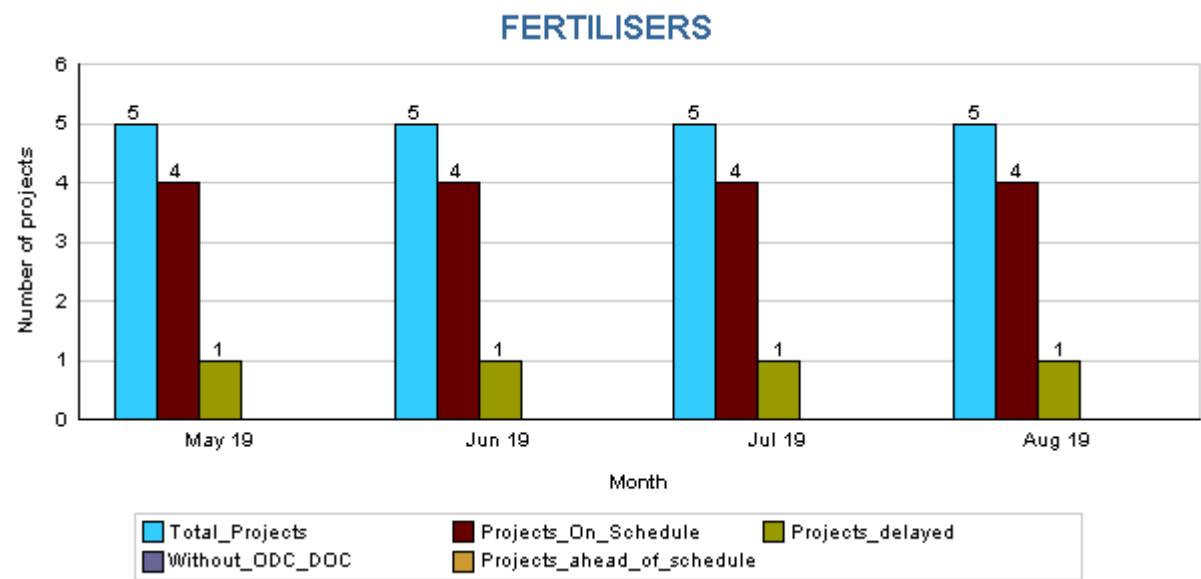


Break-up of 1 Delayed projects in August 2019



Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

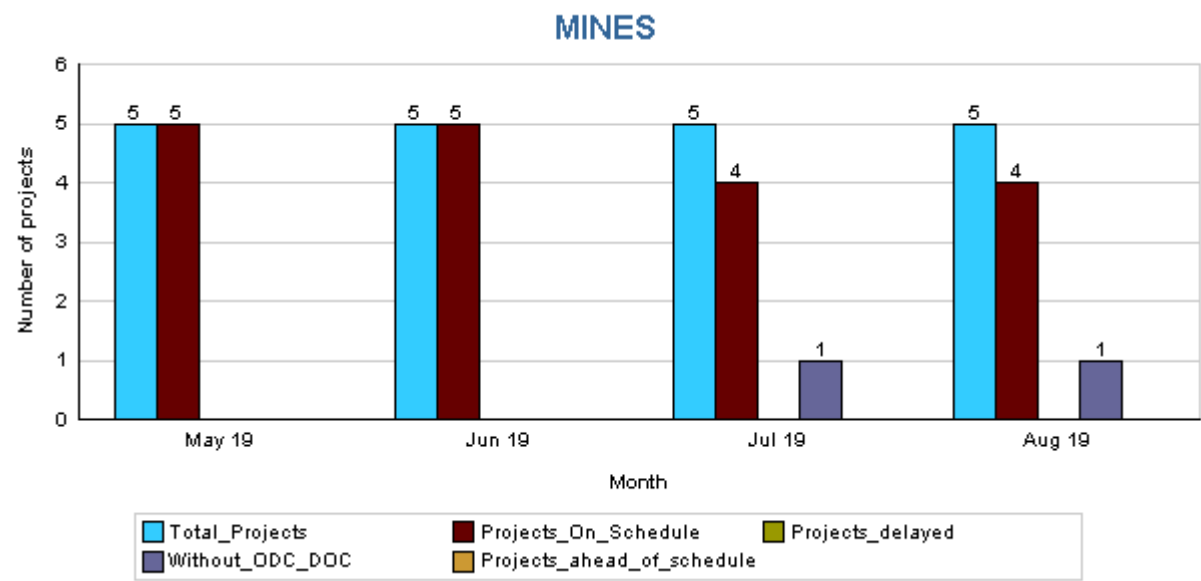


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

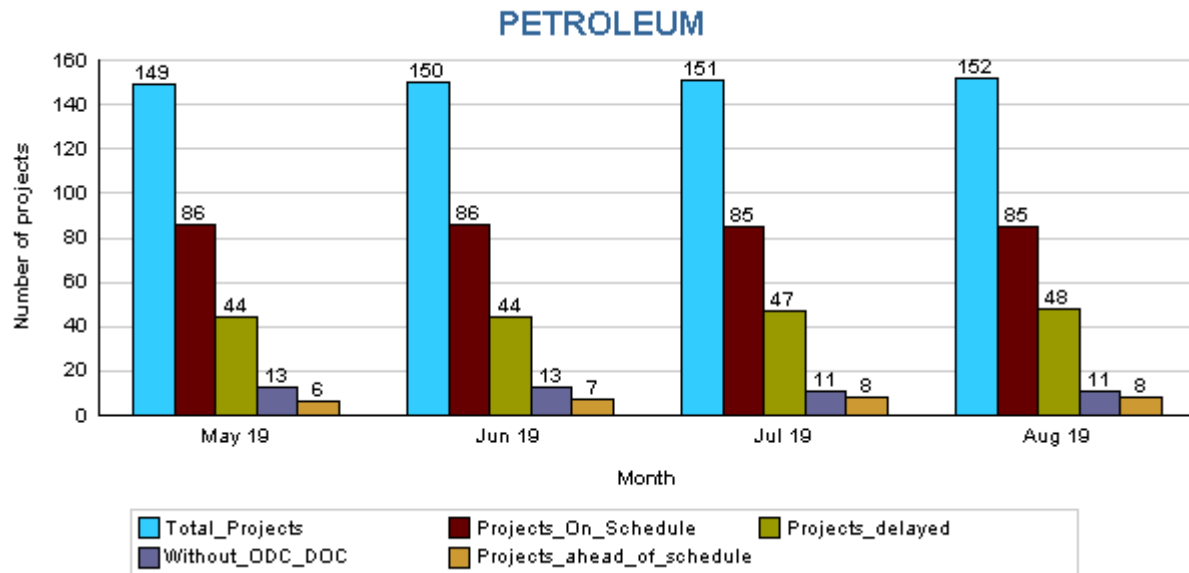


Break-up of 48 Delayed projects in August 2019

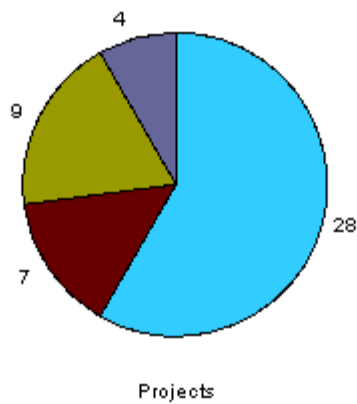


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

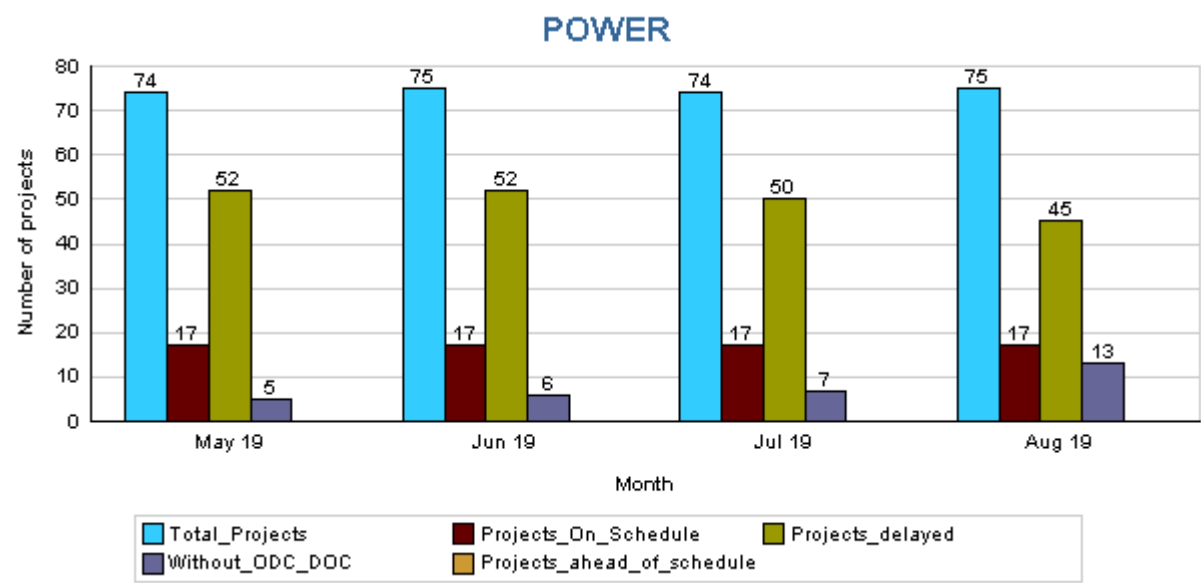


Break-up of 45 Delayed projects in August 2019

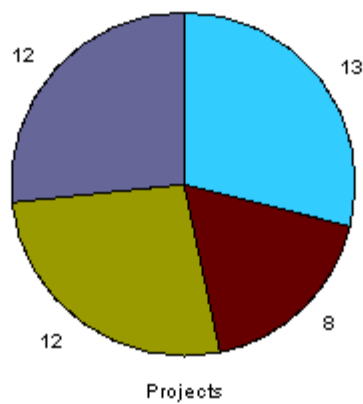

Delay in Months


Delay in Months	1-12	13-24	25-60	60 and Above
Projects	13	8	12	12

Graphical Presentation of All Projects w.r.t. Original Schedule

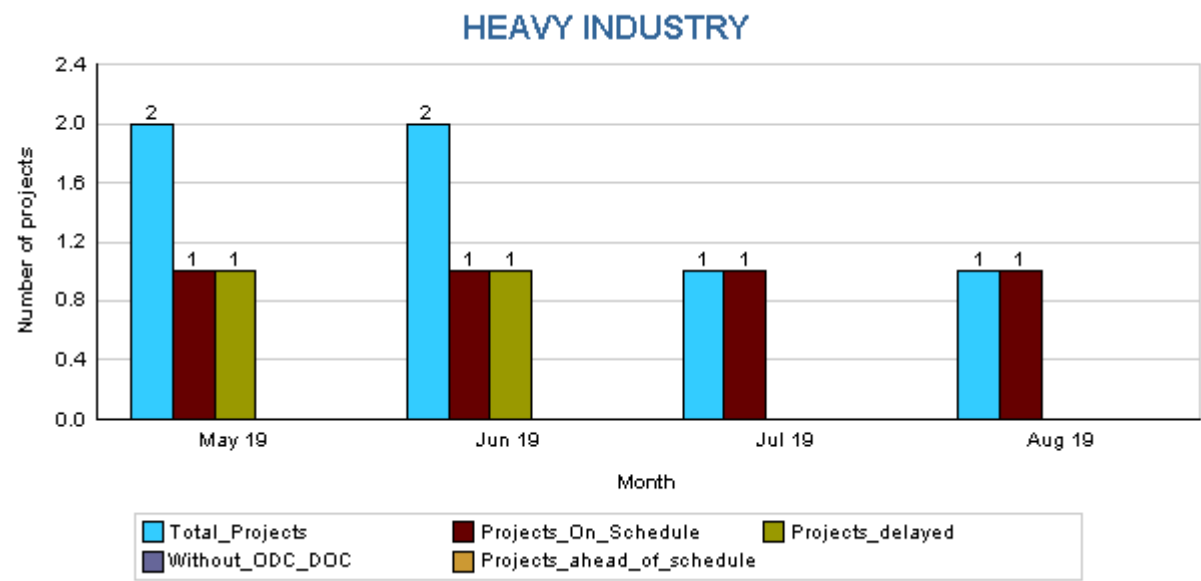


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

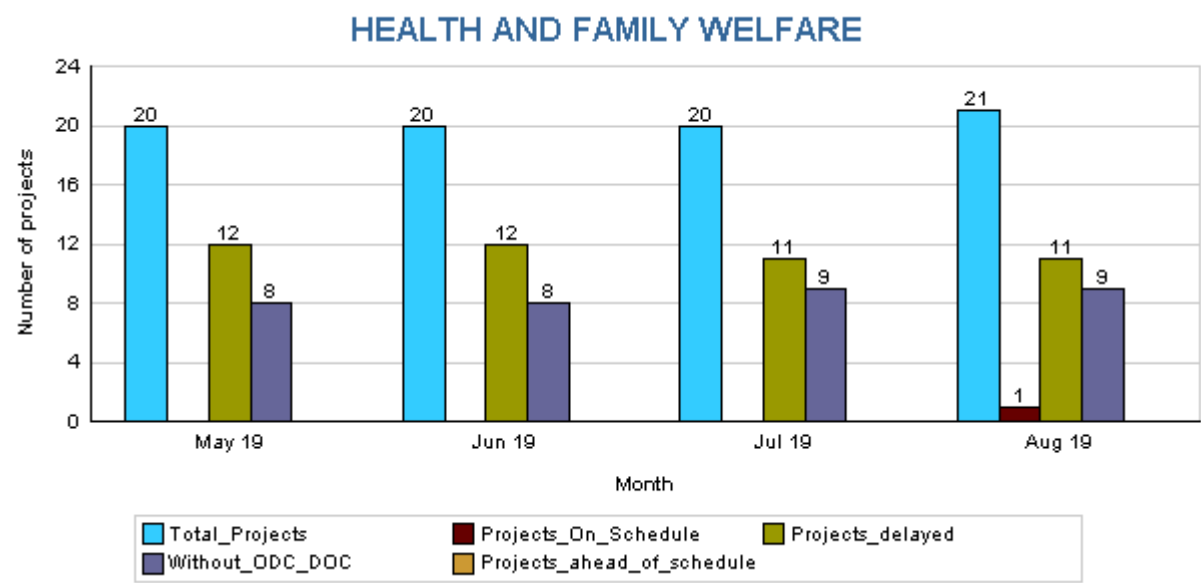


Break-up of 11 Delayed projects in August 2019

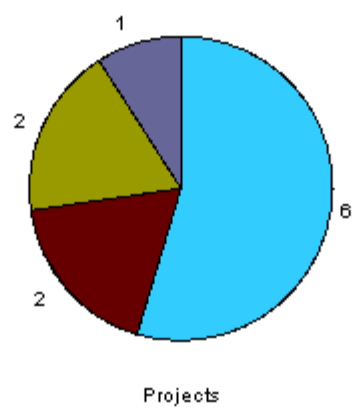


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	6	2	2	1

Graphical Presentation of All Projects w.r.t. Original Schedule

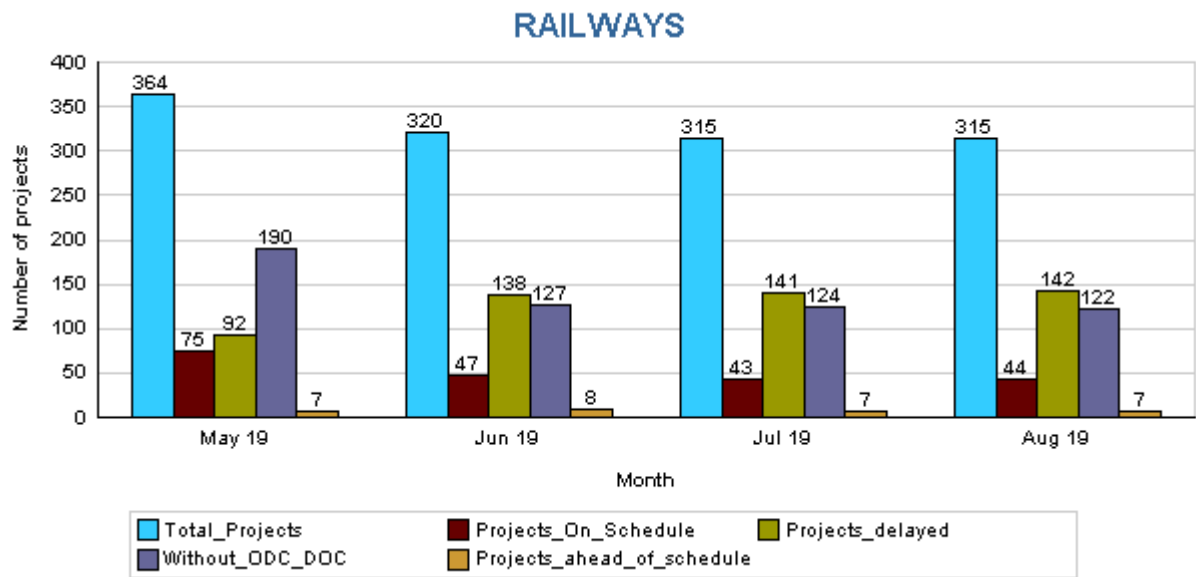


Break-up of 142 Delayed projects in August 2019

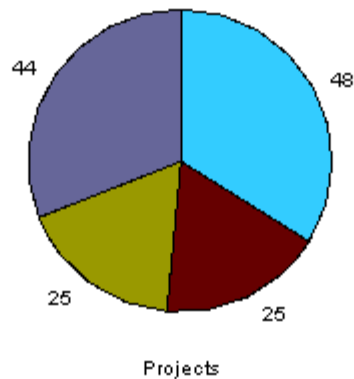


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	48	25	25	44

Graphical Presentation of All Projects w.r.t. Original Schedule

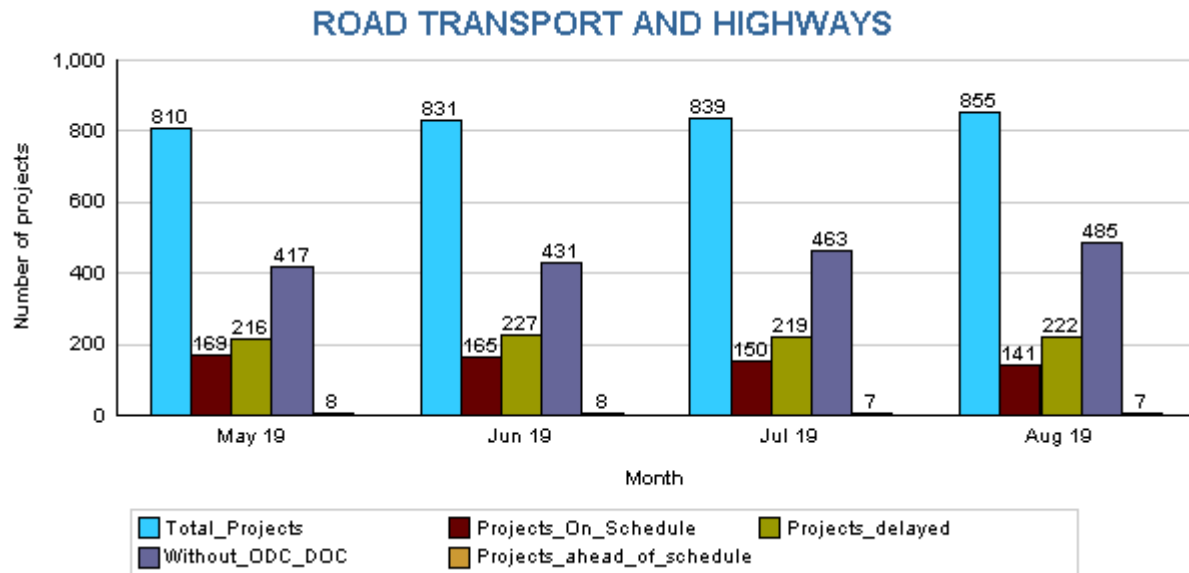


Break-up of 222 Delayed projects in August 2019

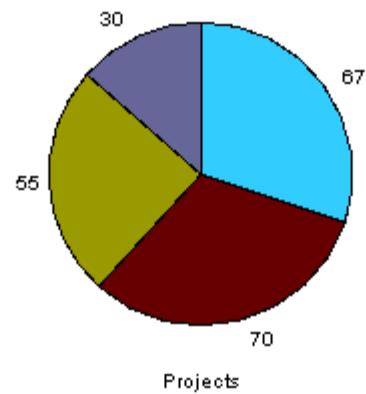

Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

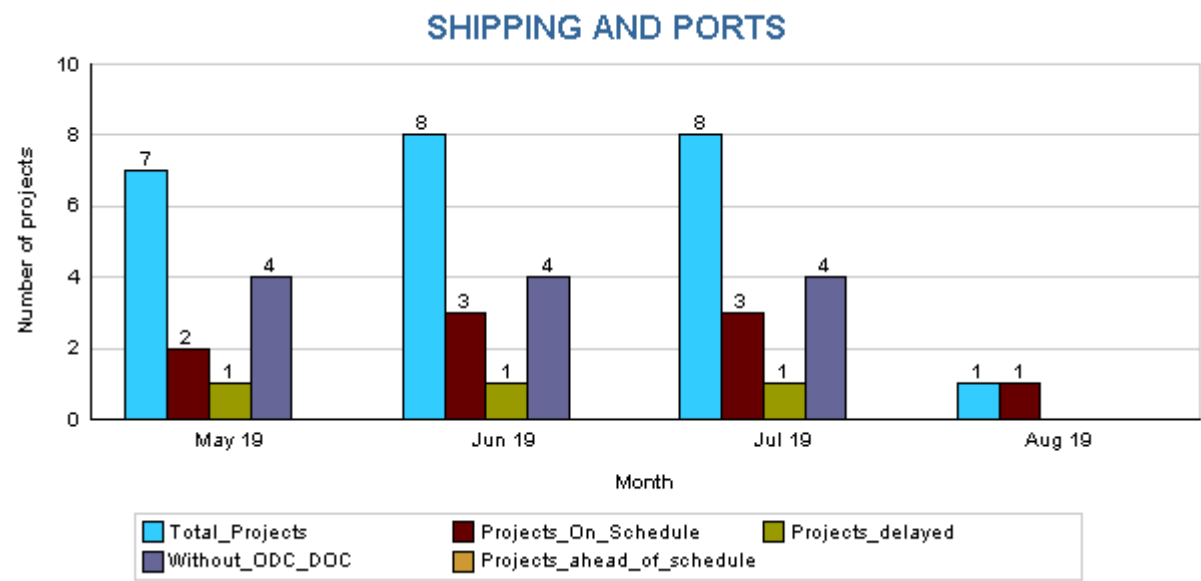


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

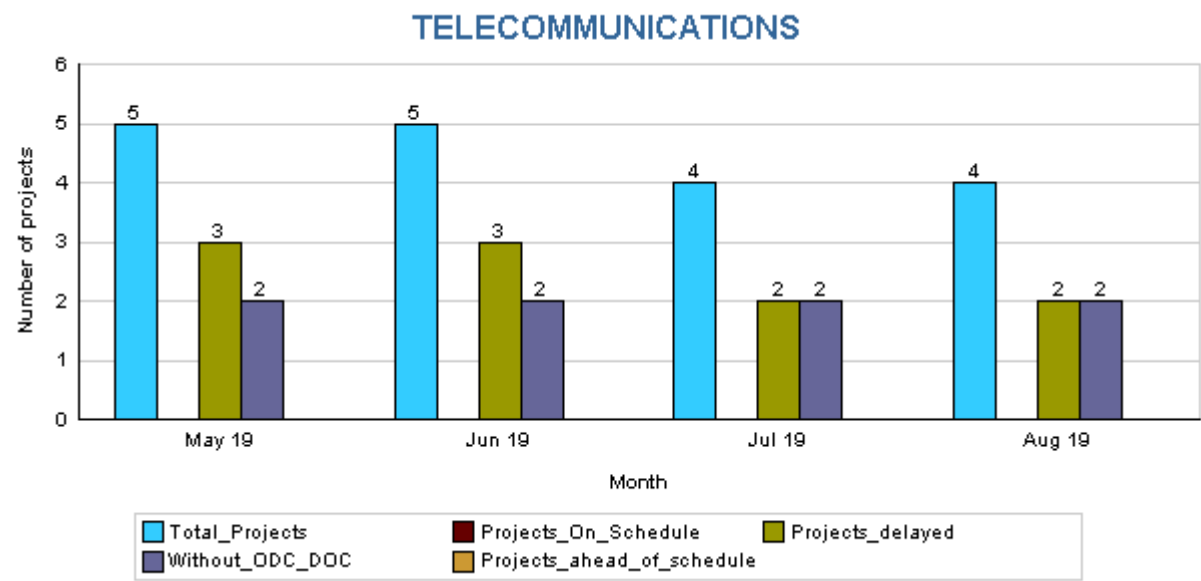


Break-up of 2 Delayed projects in August 2019




Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

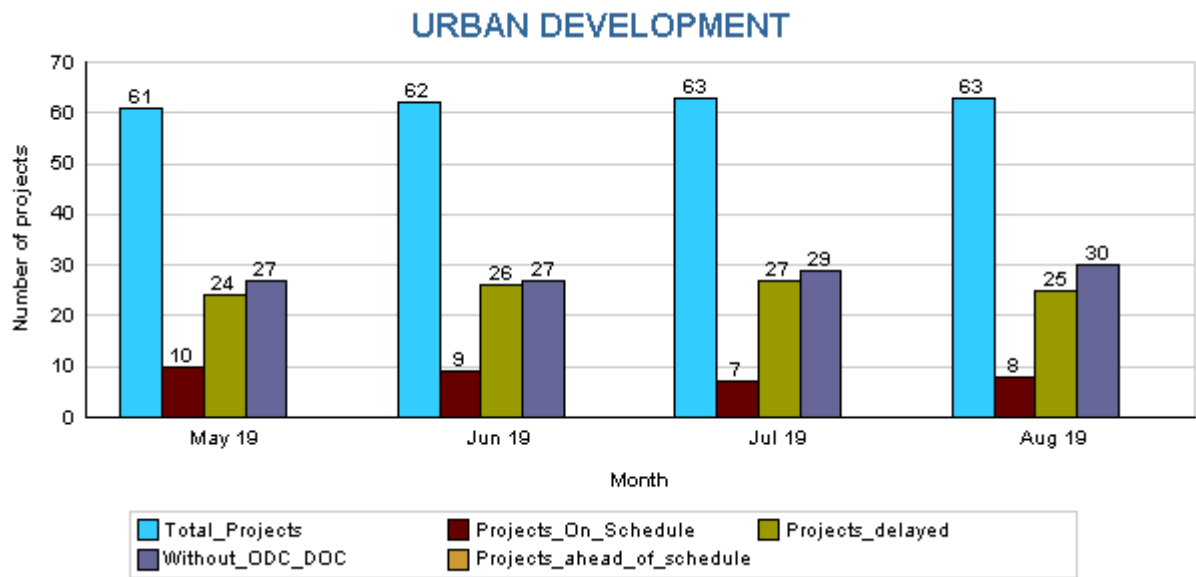


Break-up of 25 Delayed projects in August 2019

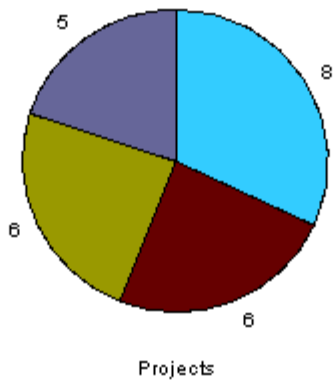


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

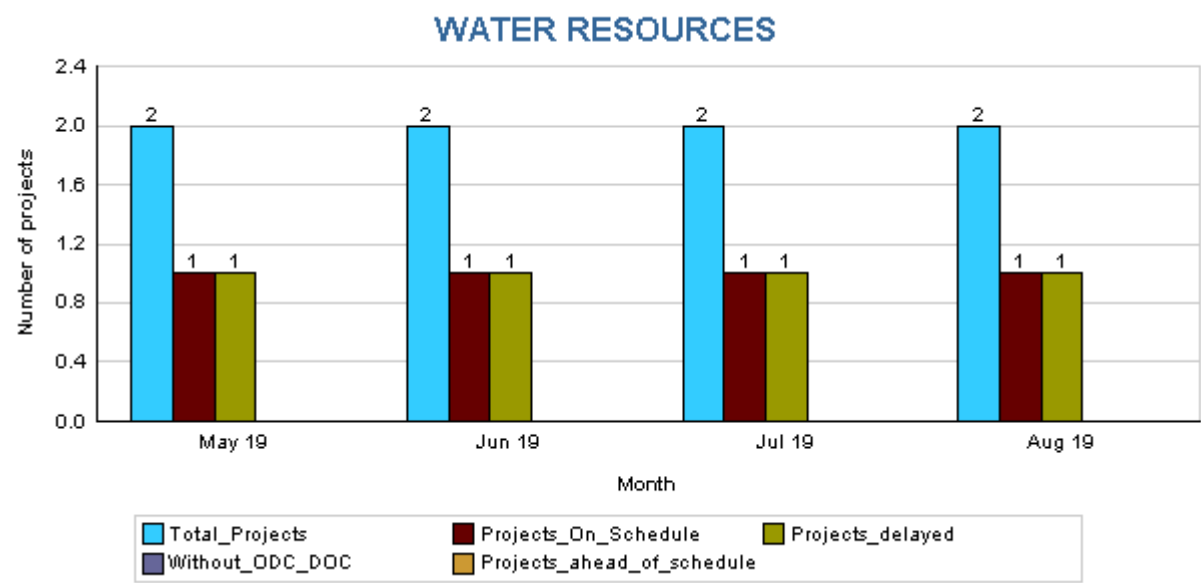


Break-up of 1 Delayed projects in August 2019



Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

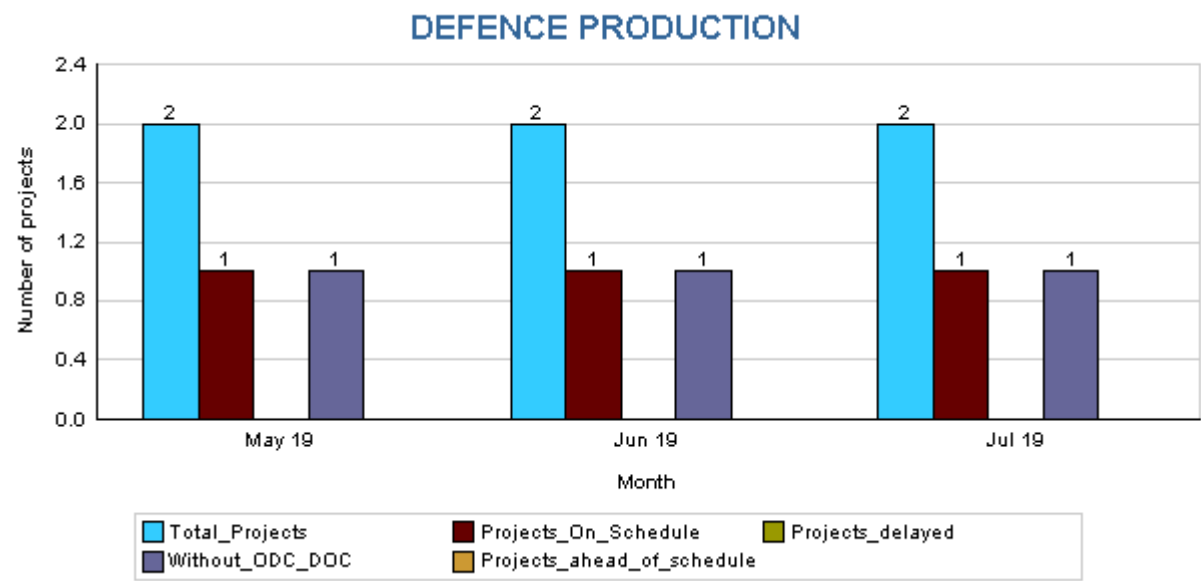

Delay in Months

TABLE-30

Detail of ongoing Projects Costing Rs. 150Crore and above.									
						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	13,971.00	12/2015 -	06/2020	54(O) -	53/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 17,079.00	17,079.00	11,234.00	12/2016 -	12/2020	48(O) -	40/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	15,395.00	11/2020 -	11/2023	36(O) -	23/76
	Total		67,120.00 -	80,348.00	46,384.74				199/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021	0(O) -	0/0
7	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	539.20 -	539.20	25.64	10/2022 -	10/2022	0(O) -	0/0
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8(O) -	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	323.19 -	323.19	10.00	09/2021 -	09/2021	0(O) -	0/0
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	358.89 -	358.89	29.73	04/2021 -	04/2021	0(O) -	0/0
11	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6(O) -	0/0
12	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	71.55	10/2021 -	10/2021	0(O) -	0/0
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6(O) -	0/0
14	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021	0(O) -	0/0
15	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	353.27 -	353.27	114.29	09/2020 -	09/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL ,	01/2016	219.91 -	219.91	61.61	03/2020 -	12/2020	9(O) -	0/0
17	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI, WEST BENGAL ,	01/2019	264.99 -	264.99	.42	11/2021 -	11/2021	0(O) -	0/0
	Total		8,607.51 -	8,734.44	1,353.49				0/0
	COAL								
18	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,881.14	03/2023 -	03/2023	0(O) -	14/19
19	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,044.21	03/2023 -	03/2023	0(O) -	7/21
20	PELMA OCP(15.00MTY) - [N06000045]SECL, CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023	0(O) -	1/12
21	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH ,	09/2008	152.43 -	459.49	191.51	03/2015 -	03/2020	60(O) -	6/10
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH ,	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72(O) -	2/8
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH ,	12/2009	321.50 -	321.50	194.57	03/2014 -	03/2021	84(O) -	0/5
24	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH ,	04/2012	258.56 -	258.56	178.86	03/2016 -	03/2020	48(O) -	4/7
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATISGARH ,	12/2013	610.63 -	610.63	97.29	03/2022 -	03/2022	0(O) -	2/10
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL, CHHATISGARH ,	05/2014	164.49 -	164.49	82.91	03/2020 -	03/2020	0(O) -	5/9
27	AMERA OC RCE - [N06000123]SECL, CHHATISGARH ,	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24(O) -	1/7
28	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH ,	07/2015	316.10 -	316.10	67.41	03/2020 -	03/2020	0(O) -	1/6
29	DURGAPUR OPENCAST PROJECT - [N06000136]SECL, CHHATISGARH ,	02/2015	916.24 -	916.24	4.02	03/2023 -	03/2023	0(O) -	1/11
30	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL, CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	1/5
31	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL, CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
32	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL, CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/1
33	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL, CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	1/1
34	MAGADH OC 20 MTY (CCL) - [N06000015]JCL, JHARKHAND ,	08/2008	706.40 -	706.40	354.66	07/2012 -	03/2022	116(O) -	5/6
35	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL, JHARKHAND ,	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120(O) -	4/6
36	TAPIN OCP (2.5 MTY) - [N06000086]JCL, JHARKHAND ,	08/2008	264.68 -	264.68	179.87	03/2012 -	03/2021	108(O) -	5/6
37	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCL, JHARKHAND ,	12/2009	510.85 -	510.85	362.47	03/2016 -	03/2021	60(O) -	5/6

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
38	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	89.85	03/2014 -	03/2021	84(O) -	6/6
39	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	-	-	4/7
40	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	386.80	04/2015 -	-	-	2/6
41	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	187.12	03/2020 -	03/2020	0(O) -	6/7
42	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.24	03/2021 -	03/2021	0(O) -	0/2
43	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
44	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	256.83	05/2014 -	03/2020	70(O) -	0/8
45	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	180.83	04/2014 -	11/2019	67(O) -	0/10
46	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	82.01	03/2022 -	03/2022	0(O) -	2/22
47	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	90.13	03/2024 -	03/2024	0(O) -	0/16
48	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	163.23	03/2023 -	03/2023	0(O) -	0/1
49	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021	-24(O) -	3/10
50	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/9
51	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	103.99	03/2021 -	03/2021	0(O) -	3/10
52	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	47.39	03/2021 -	03/2021	0(O) -	3/8
53	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/8
54	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	27.10	03/2023 -	03/2023	0(O) -	0/4
55	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	116.09	03/2021 -	03/2021	0(O) -	2/5
56	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	20.30	03/2022 -	03/2022	0(O) -	0/0
57	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	265.78	03/2021 -	03/2021	0(O) -	1/9
58	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022	0(O) -	1/9
59	SEMARIA OPENCAST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
60	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
61	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.00	03/2026 -	03/2026	0(O) -	0/7
62	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	213.24	03/2020 -	03/2020	0(O) -	8/11
64	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020	0(O) -	3/8
65	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	409.68	126.12	03/2023 -	03/2023	0(O) -	7/11
66	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	123.60	03/2019 -	-	-	10/13
67	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	121.74	03/2020 -	03/2020	0(O) -	6/10
68	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	200.77	03/2021 -	03/2021	0(O) -	2/6
69	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	268.57	03/2025 -	03/2025	0(O) -	5/13
70	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	21.02	03/2023 -	03/2024	12(O) -	3/10
71	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	313.34	115.50	03/2021 -	03/2024	36(O) -	3/6
72	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	182.51	03/2020 -	03/2020	0(O) -	2/6
73	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	183.61	03/2019 -	-	-	2/9
74	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	153.29	03/2019 -	-	-	2/8
75	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	319.93	03/2020 -	03/2020	0(O) -	0/0
76	SAONER I UG TO OC PHASE I - [N06000177]WCL,MAHARASHTRA ,	11/2016	162.10 -	162.10	50.56	03/2022 -	03/2022	0(O) -	0/6
77	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	146.45	03/2021 -	03/2021	0(O) -	0/4
78	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	42.94	03/2021 -	03/2021	0(O) -	0/3
79	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA ,	10/2016	164.96 -	164.96	93.37	03/2019 -	-	-	1/3
80	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	235.29	03/2022 -	03/2022	0(O) -	0/3
81	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	20.86	03/2022 -	03/2022	0(O) -	1/12
82	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	154.25	03/2021 -	03/2021	0(O) -	1/6
83	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120(O) -	10/10
84	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	501.82	03/2017 -	03/2020	36(O) -	11/12
85	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022	108(O) -	8/9
86	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022	144(O) -	3/4
87	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	228.90	03/2012 -	03/2021	108(O) -	5/7

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53	479.53	390.94	03/2013	03/2021	96(O)	6/9
89	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15	479.15	200.65	03/2019	03/2022	36(O)	2/9
90	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36	3,756.36	1,549.76	03/2026	03/2026	0(O)	7/15
91	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66	337.66	183.98	03/2019	03/2020	12(O)	5/6
92	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03	289.03	75.85	03/2018	03/2020	24(O)	4/6
93	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38	1,375.38	440.13	03/2021	03/2021	0(O)	6/9
94	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75	2,434.75	83.20	03/2027	03/2027	0(O)	2/12
95	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87	2,838.87	1,113.66	03/2029	03/2029	0(O)	0/9
96	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45	522.45	9.88	09/2019	09/2019	0(O)	0/0
97	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63	513.63	175.30	12/2019	12/2019	0(O)	0/0
98	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11	7,080.41	6,648.68	12/2015	12/2019	48(O)	31/35
99	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17	709.06	449.32	06/2015	09/2019	51(O)	5/7
100	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03	448.86	286.19	03/2012	03/2024	144(O)	35/42
101	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63	453.63	121.91	12/2012	-	-	11/44
102	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97	489.62	343.10	03/2012	03/2023	132(O)	0/2
103	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78	209.78	154.58	03/2015	03/2020	60(O)	30/31
104	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19	181.19	170.60	03/2012	-	-	6/6
105	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29	164.04	115.49	03/2015	03/2021	72(O)	2/5
106	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76	349.28	8.00	03/2015	03/2021	72(O)	4/29
107	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06	473.22	18.35	03/2015	03/2021	72(O)	8/13
108	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01	365.01	134.09	06/2015	12/2015	-	36/36
109	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33	384.32	92.60	07/2016	03/2020	44(O)	25/28
110	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45	415.37	186.99	03/2016	03/2020	48(O)	38/39
111	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09	442.42	92.09	03/2019	03/2020	12(O)	15/18
112	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79	426.79	.72	03/2018	03/2020	24(O)	0/9

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
113	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020	0(O) -	5/17
114	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	54.00	03/2019 -	03/2022	36(O) -	1/11
115	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	144.07	- 04/2017	03/2020	- 0	0/6
116	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA ,	08/2016	431.92 -	431.92	.00	- 03/2023	-	-	0/9
117	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA ,	02/2018	412.70 -	412.70	.11	- 03/2023	-	-	0/7
118	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	7,203.71	11/2021 -	11/2021	0(O) -	0/0
119	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	315.31	03/2022 -	03/2022	0(O) -	9/13
120	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	501.35	03/2018 -	03/2020	24(O) -	11/16
121	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/22
122	NAKRKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	.00	03/2029 -	03/2029	0(O) -	0/22
123	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.00	03/2027 -	03/2027	0(O) -	0/27
	Total		1,02,335.60 -	1,02,788.94	35,560.62				500/1095
	FERTILISERS								
124	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	106.43	11/2019 -	11/2019	0(O) -	0/2
125	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 -	209.44	164.78	11/2016 -	09/2019	34(O) -	3/13
126	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	175.19	04/2020 -	04/2020	0(O) -	1/14
127	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	113.95	11/2019 -	11/2019	0(O) -	0/2
128	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	125.27	11/2019 -	11/2019	0(O) -	0/2
	Total		1,299.07 -	1,310.72	685.62				4/33
	INFORMATION AND BROADCASTING								
129	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH ,	11/2016	204.32 -	204.32	.00	02/2019 -	11/2019	9(O) -	0/0
130	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA ,	11/2014	597.41 -	597.41	29.80	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC, MAHARASHTRA ,	12/2016	167.70 -	167.70	.00	03/2020 -	03/2020	0(O) -	0/0
	Total		969.43 -	969.43	29.80				0/0
	<u>MINES</u>								
132	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO, ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	102.61	04/2021 04/2021	04/2021	0(O) 0	3/3
133	UTKAL D AND E COAL BLOCK - [N10000011]NALCO, ODISHA ,	05/2016	534.00 534.00	534.00	318.13	01/2020 01/2020	01/2020	0(O) 0	1/2
134	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO, ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020	0(O) -	2/2
135	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO, ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.30	04/2021 04/2021	04/2021	0(O) 0	1/1
136	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO, TAMIL NADU ,	09/2017	166.62 -	166.62	134.98	06/2019 -	-	-	1/1
	Total		7,078.62 -	7,078.62	587.94				8/9
	<u>STEEL</u>								
137	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,344.76	12/2017 10/2019	10/2019	22(O) 0	5/6
138	CENTRAL DISPATCH YARD - [N12000119]RINL, ANDHRA PRADESH ,	08/2015	320.66 -	320.66	206.91	08/2018 10/2019	10/2019	14(O) 0	3/4
139	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH ,	01/2010	15,525.00 -	23,140.00	15,938.88	05/2015 07/2020	07/2020	62(O) 0	64/86
140	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND ,	03/2015	1,034.01 -	1,034.01	432.82	10/2017 06/2020	06/2020	32(O) 0	0/2
141	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND ,	05/2015	1,154.18 -	1,154.18	944.78	12/2017 11/2019	11/2019	23(O) 0	1/2
142	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND ,	11/2016	262.87 -	262.87	104.85	06/2019 06/2020	06/2020	12(O) 0	0/1
143	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA ,	04/2015	3,127.30 -	3,127.30	3,008.68	04/2018 11/2019	11/2019	19(O) 0	3/3
144	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,175.53	09/2018 09/2019	09/2019	12(O) 0	4/5
145	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL ,	12/2018	263.36 -	263.36	10.81	09/2020 -	09/2020	0(O) -	0/4
	Total		26,228.23 -	33,485.23	23,168.02				80/113
	<u>PETROLEUM</u>								

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
146	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	5,887.49	07/2020 -	07/2020	0(O) -	84/111
147	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	376.97	09/2019 -	09/2019	0(O) -	26/27
148	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	3,185.16	06/2020 -	08/2021	14(O) -	15/20
149	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
150	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
151	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 -	407.45	234.24	09/2018 09/2019	09/2019	12(O) 0	3/5
152	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	85.86	04/2021 -	04/2020	-12(O) -	0/0
153	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	84.34	04/2021 -	07/2021	3(O) -	0/0
154	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	14.07	04/2022 -	02/2023	10(O) -	0/0
155	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021	0(O) -	0/0
156	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	34.84	02/2021 -	02/2021	0(O) -	0/16
157	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81(O) 0	6/15
158	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 345.92	345.92	145.60	01/2014 -	11/2019	70(O) -	6/7
159	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	263.70	08/2019 -	09/2019	1(O) -	5/13
160	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,526.40	11/2019 -	11/2019	0(O) -	13/17
161	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 265.49	265.49	157.81	05/2020 -	05/2020	0(O) -	4/5
162	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8(O) -	0/0
163	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	531.40	09/2019 -	09/2019	0(O) -	6/7
164	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	682.90	8.75	02/2020 -	06/2020	4(O) -	1/14
165	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	178.05	02/2020 -	02/2020	0(O) -	1/5

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	224.75	3.30	08/2020 -	08/2020	0(O) -	0/0
167	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
168	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	822.02	11/2018 -	08/2019	9(O) -	8/8
169	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	600.82	12/2020 -	02/2020	-10(O) -	4/5
170	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	150.02	06/2020 -	03/2020	-3(O) -	3/4
171	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	13.88	03/2021 -	03/2021	0(O) -	11/26
172	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020	0(O) -	2/2
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	65.14	10/2022 -	10/2022	0(O) -	0/0
174	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	7.82	01/2021 -	01/2021	0(O) -	2/8
175	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	142.71	03/2021 -	03/2021	0(O) -	0/0
176	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR ,	06/2017	951.64 -	951.64	325.42	10/2019 -	10/2019	0(O) -	9/11
177	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021	0(O) -	0/0
178	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,784.40	05/2019 10/2019	10/2019	5(O) 0	13/14
179	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	142.00	04/2018 -	10/2019	18(O) -	18/20
180	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	1,162.56	371.09	03/2026 -	03/2026	0(O) -	7/10
181	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	108.00	07/2020 -	07/2020	0(O) -	10/10
182	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,	08/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020	0(O) -	1/1
183	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,	03/2018	3,380.00 -	3,380.00	1,872.71	09/2019 -	09/2019	0(O) -	7/9
184	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	85.08	02/2020 -	10/2020	8(O) -	4/8
185	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	588.20	.94	- -	08/2022	- -	8/17

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
186	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	225.54	.00	02/2021 -	02/2021	0(O) -	2/8
187	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]ONGC,GUJARAT ,	10/2018	156.67 -	156.67	.00	03/2021 -	03/2021	0(O) -	0/6
188	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	67.92	11/2020 -	11/2020	0(O) -	19/46
189	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	7.75	02/2020 -	02/2020	0(O) -	3/6
190	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	1,562.10	07/2019 -	12/2019	5(O) -	7/9
191	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	142.67	08/2020 -	08/2020	0(O) -	3/6
192	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	13.11	01/2021 -	01/2021	0(O) -	0/0
193	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	14.12	02/2020 -	02/2020	0(O) -	3/4
194	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 -	286.42	1.19	08/2020 09/2020	09/2020	1(O) 0	6/16
195	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	.00	06/2021 -	06/2021	0(O) -	0/3
196	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	147.35	09/2019 -	06/2019	-	4/4
197	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 910.23	910.23	340.16	03/2023 03/2022	03/2022	-12(O) 0	6/10
198	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	06/2020	0(O) -	0/0
199	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	48.29	10/2022 -	10/2022	0(O) -	11/17
200	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	43.56	10/2022 -	10/2022	0(O) -	0/0
201	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	22.55	06/2022 -	06/2022	0(O) -	0/0
202	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
203	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	0(O) -	0/0
204	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	185.00	164.61	04/2019 -	10/2018	-	8/8
205	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	154.03	03/2019 09/2019	09/2019	6(O) 1	11/11
206	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	726.57	12/2019 07/2020	07/2020	7(O) 0	8/9

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
207	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	621.00	68.27	03/2020 -	09/2020	6(O) -	2/3
208	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	.53	03/2021 -	03/2021	0(O) -	0/0
209	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	6.94	06/2022 -	06/2022	0(O) -	0/18
210	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022	0(O) -	0/0
211	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	355.02	10/2017 -	-	-	39/52
212	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	3,588.88	08/2018 11/2019	11/2019	15(O) 0	0/20
213	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	1,014.00	02/2020 10/2020	10/2020	8(O) 0	0/20
214	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	507.00	06/2019 -	02/2022	32(O) -	0/0
215	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	15.17	03/2023 -	03/2023	0(O) -	0/0
216	PROVISION OF 2ND SPUR FOR TWL GANTRY TWO FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	24.15	06/2020 -	08/2020	2(O) -	0/0
217	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 -	1,683.06	1,314.42	05/2013 12/2019	12/2019	79(O) 0	4/8
218	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,908.01	03/2015 12/2019	12/2019	57(O) 0	15/18
219	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019	8(O) 0	8/9
220	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020	14(O) 0	4/5
221	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	4,340.39	12/2017 03/2020	03/2020	27(O) 0	4/5
222	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,216.11	04/2018 05/2020	05/2020	25(O) 0	13/15
223	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	941.98	08/2021 -	08/2021	0(O) -	4/5
224	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	350.36	02/2020 -	09/2019	-5(O) -	0/10
225	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	155.28	12/2019 -	12/2019	0(O) -	0/17

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
226	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	38.55	01/2021 -	04/2021	3(O) -	0/0
227	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	30.75	01/2021 -	10/2021	9(O) -	0/0
228	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	41.42	01/2021 -	01/2021	0(O) -	0/0
229	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	2,592.90	03/2020 -	03/2020	0(O) -	107/135
230	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 565.15	565.15	442.18	11/2019 03/2020	03/2020	4(O) 0	4/5
231	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 -	511.30	463.01	11/2019 -	11/2019	0(O) -	4/5
232	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 -	1,033.95	912.74	11/2019 -	11/2019	0(O) -	4/5
233	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,475.92	2,770.16	05/2021 12/2021	12/2021	7(O) 0	11/15
234	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	121.12	08/2020 -	08/2020	0(O) -	0/15
235	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	58.33	06/2020 -	06/2020	0(O) -	0/0
236	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	440.41	12/2019 -	12/2019	0(O) -	4/5
237	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,292.46	275.27	05/2021 -	05/2021	0(O) -	4/6
238	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 -	3,228.80	428.31	03/2022 -	03/2022	0(O) -	4/6
239	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1(O) -	4/6
240	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	05/2019	2,494.68 -	2,494.68	.00	12/2021 -	03/2022	3(O) -	4/6
241	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	763.92	.00	12/2020 -	12/2020	0(O) -	4/5
242	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	703.45	10/2014 08/2019	08/2019	58(O) 0	40/40
243	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33(O) -	2/15
244	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	844.09	12/2020 -	12/2020	0(O) -	4/5

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
245	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	1,820.56	12/2020 -	08/2020	-4(O) -	4/5
246	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	602.02	10/2019 -	10/2019	0(O) -	5/6
247	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	278.51	07/2018 -	10/2020	27(O) -	23/36
248	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	1,460.00	06/2020 -	06/2020	0(O) -	18/24
249	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	87.00	10/2020 -	10/2020	0(O) -	6/12
250	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	173.61	12/2019 -	12/2019	0(O) -	6/22
251	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,271.82	12/2020 -	12/2020	0(O) -	19/24
252	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	1,396.84	12/2020 -	12/2020	0(O) -	16/24
253	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	1,229.31	12/2020 -	12/2020	0(O) -	17/24
254	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	3,049.47	2,515.46	12/2012 -	02/2022	110(O) -	19/42
255	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	837.13	03/2021 -	03/2021	0(O) -	9/26
256	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
257	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	1,123.85	12/2021 -	12/2021	0(O) -	10/20
258	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,573.02	09/2017 06/2019	07/2019	-	6/6
259	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,019.25	12/2020 -	12/2020	0(O) -	18/24
260	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	306.24	01/2019 -	12/2019	11(O) -	6/6
261	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	38.29	12/2019 -	07/2021	19(O) -	17/26
262	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	49.97	07/2022 -	07/2022	0(O) -	0/0
263	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	110.59	12/2021 -	12/2020	-12(O) -	2/3
264	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	28.80	07/2022 -	07/2022	0(O) -	0/0
265	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	242.10	10/2021 -	10/2021	0(O) -	2/10

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
266	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00 -	750.00	34.73	12/2020 -	12/2020	0(O) -	0/14
267	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	9.08	10/2021 -	10/2021	0(O) -	0/1
268	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	.00	09/2021 -	09/2021	0(O) -	0/0
269	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	284.31	08/2021 -	08/2021	0(O) -	2/11
270	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	.00	09/2022 -	09/2022	0(O) -	0/0
271	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
272	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	69.24	-	03/2021	-	9/26
273	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
274	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.00	11/2015 -	-	-	52/52
275	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56(O) -	0/0
276	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	650.82	394.21	03/2019 05/2020	05/2020	14(O) 0	4/5
277	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	465.60	12/2018 -	02/2021	26(O) -	4/5
278	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	12.28	06/2020 -	06/2020	0(O) -	4/5
279	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	951.55	12/2019 -	12/2019	0(O) -	0/0
280	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	123.76	08/2020 -	08/2020	0(O) -	0/0
281	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	30.95	10/2020 -	08/2021	10(O) -	0/0
282	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022	0(O) -	0/0
283	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	123.35	04/2022 -	04/2022	0(O) -	34/43
284	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	40.06	08/2021 -	11/2021	3(O) -	0/0
285	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	376.04	09/2019 -	09/2019	0(O) -	5/6
286	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	.71	08/2020 -	08/2020	0(O) -	1/1

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
287	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	96.35	12/2021 -	12/2021	0(O) -	2/3
288	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH ,	03/2014	204.00 -	204.00	139.25	09/2019 -	09/2019	0(O) -	2/6
289	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	13.47	12/2021 -	12/2021	0(O) -	0/0
290	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH ,	08/2016	154.84 -	154.84	118.06	11/2019 -	11/2019	0(O) -	37/40
291	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	41.22	02/2020 -	10/2020	8(O) -	18/26
292	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 1,097.54	1,097.54	698.76	10/2018 12/2019	12/2019	14(O) 1	0/15
293	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
294	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	173.41	12/2020 -	12/2020	0(O) -	12/24
295	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	50.84	04/2020 -	03/2021	11(O) -	17/26
296	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	1,569.01	09/2019 -	09/2019	0(O) -	10/11
297	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	189.41	09/2022 -	06/2021	-15(O) -	1/1
	Total		2,46,655.89 -	2,55,016.79	91,066.77				1078/1747
	<u>POWER</u>								
298	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,945.40	09/2010 -	-	-	0/0
299	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	7,516.58	12/2009 10/2019	10/2019	118(O) 2	30/30
300	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	16,331.92	10/2011 08/2021	08/2021	118(O) 0	29/47
301	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	9,996.59	7,861.51	07/2012 -	09/2020	98(O) -	12/25
302	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	13,716.26	05/2018 12/2021	12/2021	43(O) 0	35/45
303	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	777.63	01/2024 -	01/2024	0(O) -	16/19
304	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	12,349.43	10/2017 03/2020	03/2020	29(O) 0	35/41
305	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019	0(O) -	0/0
306	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	405.65	05/2017 -	12/2019	31(O) -	4/9

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
307	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	92.78	09/2018 -	09/2019	12(O) -	0/0
308	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT ,	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3(O) -	0/0
309	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,997.11	7,551.56	09/2009 -	12/2021	147(O) -	3/5
310	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND ,	02/2014	14,366.58 -	15,164.05	9,131.59	06/2019 09/2019	09/2021	27(O) 0	23/24
311	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,268.00	10/2017 -	-	-	0/0
312	PATRATU STPP-I (3X800MW) - [N18000275]NTPC, JHARKHAND ,	11/2017	18,668.00 -	18,668.00	1,904.30	03/2023 -	03/2023	0(O) -	1/1
313	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10(O) -	0/0
314	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC, MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	12,045.10	01/2018 03/2020	03/2020	26(O) 0	39/42
315	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC, MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	8,449.85	01/2020 -	01/2020	0(O) -	34/39
316	AMELIA COAL MINE - [N18000252]THDCIL, MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	306.71	09/2020 -	09/2020	0(O) -	9/16
317	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
318	LOKTAK D/S HEP (NHPC) - [180100078]NHPC, MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
319	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE ,	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 -	12/2019	86(O) -	8/11
320	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE ,	02/2009	11,130.19 -	14,719.10	12,804.46	08/2013 -	03/2022	103(O) -	23/26
321	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE ,	10/2011	487.49 -	639.46	540.12	06/2014 -	09/2019	63(O) -	10/12
322	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE ,	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 -	08/2019	40(O) -	8/12
323	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE ,	01/2014	374.63 -	374.63	210.72	04/2016 -	12/2019	44(O) -	0/0
324	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE ,	05/2014	522.29 -	546.36	465.21	11/2016 -	03/2020	40(O) -	8/12
325	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE ,	06/2014	5,151.37 -	5,151.37	3,115.72	03/2018 -	12/2019	21(O) -	9/12
326	EASTERN REGION STRENGTHENING SCHEME-IX - [N18000171]PGCIL, MULTI STATE ,	02/2014	196.58 -	225.28	162.30	02/2016 -	06/2019	-	16/17
327	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL, MULTI STATE ,	01/2015	268.80 -	340.88	251.33	03/2018 -	07/2019	-	1/3

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
328	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	548.30	10/2017 -	09/2019	23(O) -	0/5
329	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	190.80	07/2017 -	08/2019	25(O) -	3/5
330	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	81.97	03/2018 -	08/2019	17(O) -	0/0
331	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	513.85	01/2018 -	03/2020	26(O) -	0/0
332	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4(O) -	0/0
333	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019	0(O) -	0/0
334	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	392.96	03/2019 -	07/2019	-	0/0
335	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	185.94	06/2019 -	06/2019	-	0/0
336	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	187.60	11/2019 -	11/2019	0(O) -	0/0
337	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	266.03	01/2019 -	09/2019	8(O) -	0/0
338	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	407.79	04/2019 -	07/2019	-	0/0
339	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	116.76	02/2020 -	02/2020	0(O) -	0/0
340	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	153.70	02/2019 -	08/2019	6(O) -	0/0
341	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	117.15	06/2019 -	10/2019	4(O) -	0/0
342	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	52.63	12/2019 -	12/2019	0(O) -	0/0
343	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020	0(O) -	0/0
344	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	84.17	06/2019 -	07/2019	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
345	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12(O) -	0/0
346	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 -	12/2020	24(O) -	0/0
347	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,308.50	04/2019 -	07/2019	-	0/0
348	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020	0(O) -	0/0
349	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020	0(O) -	0/0
350	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5(O) -	0/0
351	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020	0(O) -	0/0
352	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	9,639.47	12/2018 02/2020	09/2020	21(O) 3	33/38
353	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	430.71	04/2019 -	08/2019	4(O) -	0/0
354	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15(O) -	0/0
355	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	1,011.38	01/2019 -	07/2019	-	0/0
356	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	08/2019	129(O) -	20/22
357	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2(O) -	0/0
358	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	5,382.09	11/2020 06/2021	06/2021	7(O) 0	23/24
359	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	6,397.93	07/2019 06/2020	06/2020	11(O) 0	33/35
360	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 -	294.60	302.76	02/2014 -	10/2019	68(O) -	7/8
361	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	9,749.00	02/2017 06/2020	06/2020	40(O) 0	33/40
362	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	511.64	09/2023 -	09/2023	0(O) -	0/0
363	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020	0(O) -	0/0
364	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	125.00	11/2020 -	11/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
365	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 -	5,024.35	3,003.16	02/2016 -	06/2022	76(O) -	16/30
366	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,155.88	03/2013 12/2020	12/2020	93(O) 0	6/15
367	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,397.80	1,733.13	06/2013 -	12/2022	114(O) -	10/13
368	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	148.91	08/2017 -	-	-	0/15
369	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	255.15	12/2021 -	12/2021	0(O) -	3/32
370	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL ,	09/2014	1,381.84 -	1,592.34	481.22	09/2019 02/2022	02/2022	29(O) 0	5/9
371	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL ,	04/2016	454.11 -	454.11	287.52	04/2018 -	01/2020	21(O) -	0/0
372	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL ,	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16(O) -	0/0
	Total		2,81,499.09 -	3,55,386.08	2,14,664.65				586/780
	<u>HEAVY INDUSTRY</u>								
373	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL, DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019	0(O) -	0/0
	Total		1,554.00 -	1,554.00	335.03				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
374	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS- MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC, ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7(O) -	0/0
375	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	85.04	- -	02/2020	- -	0/0
376	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC, ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
377	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES, ASSAM ,	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5(O) -	0/0
378	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI ,	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83(O) -	0/0
379	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI ,	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28(O) -	2/2
380	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI ,	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27(O) -	3/5
381	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI ,	12/2017	156.56 -	156.65	54.94	- -	02/2020	- -	0/0
382	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA , Central Sector Projects	01/2018	249.01 -	249.01	73.40	- -	05/2020	- -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
383	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	508.29	03/2018 -	-	-	1/2
384	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,351.00	137.87	09/2021 -	09/2021	0(O) -	0/0
385	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7(O) -	0/0
386	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	112.97	- -	02/2020	- -	0/0
387	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16(O) -	0/0
388	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19(O) -	1/1
389	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2(O) -	0/0
390	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	99.26	- -	04/2020	- -	0/0
391	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2(O) -	0/0
392	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	241.39	09/2018 -	-	-	0/0
393	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12(O) -	0/0
394	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	112.82	- -	02/2020	- -	0/0
	Total		9,480.23 -	9,597.52	3,377.82				7/10
	<u>RAILWAYS</u>								
395	NANDYAL-YERRAGUNTALA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
396	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168(O) -	0/0
397	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
398	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	- -	-	-	1/1
399	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36(O) -	0/1
400	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	1,402.19	03/2020 -	03/2022	24(O) -	0/0
401	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
402	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
403	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	925.36	12/2023 -	12/2023	0(O) -	0/0
404	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	3,382.95	373.22	03/2022 -	03/2022	0(O) -	0/0
405	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
406	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	11.11	03/2019 -	12/2020	21(O) -	0/0
407	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 1,532.00	1,532.00	629.19	03/2019 -	03/2020	12(O) -	0/0
408	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 728.00	728.00	704.09	03/2019 -	03/2020	12(O) -	0/0
409	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	654.38	03/2022 -	03/2020	-24(O) -	0/0
410	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	2,136.01	502.44	03/2021 -	03/2021	0(O) -	0/0
411	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 898.53	898.53	1,038.71	03/2012 -	03/2020	96(O) -	0/0
412	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 614.45	614.45	305.70	- -	03/2022	- -	0/0
413	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,405.48	- -	03/2023	- -	0/0
414	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 516.02	516.02	390.53	03/2020 -	03/2020	0(O) -	0/0
415	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
416	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 751.55	751.55	673.58	03/2012 -	03/2020	96(O) -	0/0
417	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12(O) -	0/0
418	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.67	- 03/2022	03/2022	- 0	0/0
419	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	03/2023	- -	0/0
420	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.28	- -	03/2024	- -	0/0
421	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.14	- -	03/2024	- -	0/0
422	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	1.91	- -	03/2024	- -	0/0
423	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 735.20	735.20	362.10	- -	03/2021	- -	0/0
424	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	2,609.00	376.63	- -	03/2022	- -	0/0
425	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	03/2024	- -	0/0
426	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.16	- -	03/2024	- -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
427	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62	678.62	17.20	-	03/2024	-	0/0
428	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
429	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17	1,605.17	23.49	-	03/2023	-	0/0
430	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56	192.56	.39	-	03/2024	-	0/0
431	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30	281.30	.60	-	03/2024	-	0/0
432	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14	1,470.50	761.68	-	03/2021	-	0/0
433	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00	819.01	488.95	03/2020	03/2022	24(O)	0/0
434	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01	425.17	397.41	-	01/2020	-	0/0
435	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00	519.33	138.35	-	02/2023	-	0/0
436	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR ,	08/2010	400.00	400.00	.00	03/2014	-	-	0/0
437	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR ,	07/2004	599.63	674.00	.00	12/2007	-	-	0/0
438	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20	1,200.20	396.80	03/2020	10/2021	19(O)	0/1
439	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47	1,491.47	438.38	03/2020	12/2022	33(O)	1/1
440	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15	546.71	541.07	07/2014	-	-	0/0
441	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04	1,215.54	54.14	03/2021	03/2022	12(O)	0/0
442	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64	1,185.73	32.31	03/2021	03/2022	12(O)	0/0
443	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82	726.31	497.81	-	10/2019	-	0/0
444	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39	1,483.14	845.59	-	12/2021	-	0/0
445	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00	1,160.83	682.29	03/2020	03/2023	36(O)	1/1
446	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02	1,100.00	1,029.98	03/2020	06/2020	3(O)	0/0
447	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00	207.00	153.83	03/2018	-	-	0/0
448	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00	1,226.51	1,044.67	12/2019	10/2019	-2(O)	0/0
449	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00	1,973.66	139.42	03/2021	12/2022	21(O)	0/1

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
450	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	619.50	03/2022 -	12/2022	9(O) -	0/1
451	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 -	12/2020	27(O) -	0/1
452	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	241.23	03/2020 -	03/2020	0(O) -	0/0
453	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	107.86	- -	03/2024	- -	0/0
454	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	79.53	- -	03/2023	- -	0/0
455	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,215.34	1,310.23	1,363.06	03/2020 03/2021	03/2021	12(O) 0	0/0
456	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120(O) 0	0/0
457	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	404.70	03/2011 -	03/2017	-	0/0
458	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	963.63	12/2021 -	12/2021	0(O) -	0/0
459	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	317.38	03/2021 -	03/2021	0(O) -	0/0
460	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 -	439.88	92.69	- -	03/2021	-	0/0
461	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36(O) 0	0/0
462	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	1,226.20	12/2021 -	12/2021	0(O) -	0/0
463	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,037.15	1,037.15	992.18	03/2021 03/2022	03/2022	12(O) 0	0/0
464	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	374.60	03/2021 03/2021	03/2021	0(O) 0	0/0
465	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9(O) -	0/0
466	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
467	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
468	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
469	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 809.07	809.07	616.90	03/2019 03/2020	03/2020	12(O) 0	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
470	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 663.29	663.29	163.85	03/2020 03/2021	03/2021	12(O) 0	0/0
471	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111(O) -	0/0
472	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	286.78	03/2019 -	03/2020	12(O) -	0/0
473	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	370.26	12/2026 -	12/2026	0(O) -	0/0
474	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	19,223.83	11/2002 -	06/2022	235(O) -	0/0
475	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,376.00	3,290.02	- -	03/2021	- -	0/0
476	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	498.90	- -	03/2021	- -	0/0
477	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	258.09	12/2018 12/2018	06/2020	18(O) 0	0/0
478	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019	36(O) 1	0/0
479	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,993.24	384.82	03/2021 -	12/2021	9(O) -	0/0
480	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	164.09	03/2021 -	12/2020	-3(O) -	0/0
481	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	144.76	- -	12/2024	- -	0/0
482	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
483	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,801.01	44.36	- -	12/2023	- -	0/0
484	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93(O) -	0/1
485	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	- -	12/2023	- -	0/0
486	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
487	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.35	- -	12/2023	- -	0/0
488	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,630.89	03/2023 -	03/2023	0(O) -	0/1
489	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	12/2023	- -	0/0
490	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72(O) -	0/0
491	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	- -	12/2023	- -	0/0
492	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93(O) -	0/0
493	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12(O) -	0/5
494	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	578.00	509.07	03/2020 -	03/2020	0(O) -	0/2

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
495	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36(O) -	0/0
496	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 2,815.62	2,815.62	264.28	- -	-	-	0/0
497	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 252.96	252.96	8.50	- -	-	-	0/0
498	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 189.24	189.24	6.72	- -	-	-	0/0
499	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 1,431.90	1,431.90	75.00	- 06/2022	-	-	0/0
500	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 828.50	828.50	.08	- -	-	-	0/0
501	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
502	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023	24(O) -	0/14
503	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 1,413.76	1,413.76	1,324.64	- 10/2019	10/2019	- 0	0/0
504	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 3,338.15	3,860.40	1,676.43	03/2022 03/2023	03/2023	12(O) 0	0/0
505	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,763.93	624.49	03/2020 -	03/2022	24(O) -	1/1
506	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	1,053.80	12/2020 -	12/2020	0(O) -	0/0
507	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	367.59	03/2022 -	03/2023	12(O) -	0/10
508	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,247.64	154.63	03/2022 -	09/2022	6(O) -	0/1
509	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	150.62	03/2019 -	02/2020	11(O) -	0/0
510	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 737.72	1,300.44	646.30	02/2019 03/2020	06/2020	16(O) 0	0/1
511	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.00	1,370.00	281.19	12/2021 12/2021	12/2021	0(O) 0	0/0
512	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	86.45	06/2020 06/2021	06/2021	12(O) 0	0/0
513	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	2,980.41	1,414.47	03/2004 -	03/2021	204(O) -	0/0
514	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	3,712.50	2,347.12	03/2021 -	03/2022	12(O) -	0/0
515	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 918.53	918.53	277.61	03/2014 03/2021	03/2021	84(O) 0	0/0
516	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
517	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,208.28	03/2023 -	03/2023	0(O) -	0/0
518	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	301.24	03/2021 -	03/2022	12(O) -	0/0
519	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	305.00	269.00	03/2019 12/2019	12/2019	9(O) 0	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
520	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	223.82	03/2022 -	03/2024	24(O) -	0/0
521	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
522	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
523	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	-	-	0/0
524	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,272.19	281.97	03/2022 -	03/2023	12(O) -	0/0
525	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	156.29	03/2023 -	03/2023	0(O) -	0/0
526	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	674.45	03/2024 -	03/2022	-24(O) -	0/0
527	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	94.83	03/2023 -	03/2023	0(O) -	0/0
528	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	76.32	03/2022 -	03/2024	24(O) -	0/0
529	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	56.45	03/2023 -	03/2024	12(O) -	0/0
530	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	1,950.00	1,858.81	03/2020 -	03/2020	0(O) -	0/0
531	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
532	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 2,686.63	2,686.63	443.56	03/2023 03/2023	03/2023	0(O) 0	0/1
533	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	260.88	03/2019 -	12/2019	9(O) -	0/0
534	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
535	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
536	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 403.00	860.92	39.69	12/2021 03/2023	03/2023	15(O) 0	0/1
537	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 13,809.00	12,524.00	9,123.93	03/2011 -	03/2020	108(O) -	0/0
538	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.00	261.76	03/2021 -	03/2021	0(O) -	0/0
539	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 4,968.00	5,021.45	3,075.08	03/2014 03/2022	03/2022	96(O) 0	0/0
540	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 1,756.92	1,756.92	1,661.79	04/2020 12/2020	12/2020	8(O) 0	0/1
541	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140(O) -	0/0
542	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252(O) -	0/0
543	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023	178(O) -	0/9

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
544	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 3,300.00	3,300.00	3,279.71	12/2008 -	03/2021	147(O) -	0/0
545	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024	133(O) -	0/0
546	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
547	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	106.55	12/2021 -	12/2021	0(O) -	0/0
548	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	328.19	01/2019 -	01/2020	12(O) -	0/0
549	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	719.73	03/2022 03/2022	03/2022	0(O) 0	0/0
550	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	682.91	03/2022 03/2023	03/2023	12(O) 0	0/0
551	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,079.15	185.11	- -	-	-	0/1
552	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33(O) -	0/3
553	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
554	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	-	-	0/0
555	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.54	- -	03/2024	-	0/0
556	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	2,496.67	.00	03/2019 -	-	-	0/0
557	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,300.00	2.28	- -	-	-	0/0
558	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 457.08	457.08	373.51	- -	-	-	0/0
559	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	68.15	03/2020 -	03/2020	0(O) -	0/0
560	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	272.88	- -	03/2021	-	0/0
561	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	122.05	03/2020 -	03/2020	0(O) -	0/0
562	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
563	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9(O) -	0/0
564	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228(O) -	0/0
565	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	9.31	- -	03/2025	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
566	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.73	-	03/2025	-	0/0
567	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	290.01	03/2022 -	03/2025	36(O) -	0/0
568	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	376.90	376.90	-	03/2020	-	0/0
569	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	471.81	459.69	-	05/2019	-	0/0
570	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	434.06	03/2016 -	03/2025	108(O) -	0/0
571	CHINPAI- SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	102.27	03/2017 -	03/2025	96(O) -	0/0
572	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.42	-	03/2025	-	0/0
573	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	155.33	03/2016 -	03/2025	108(O) -	0/0
574	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	212.51	03/2017 -	03/2025	96(O) -	0/0
575	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28(O) -	0/0
576	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.12	-	03/2025	-	0/0
577	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	-	03/2025	-	0/0
578	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	693.80	428.83	03/2020 -	03/2020	0(O) -	0/0
579	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	242.06	242.06	-	03/2021	-	0/0
580	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
581	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
582	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	-	03/2025	-	0/0
583	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	-	03/2025	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
584	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96	680.68	155.08	02/2012	03/2025	157(O)	0/0
585	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42	257.42	105.28	03/2014	03/2025	132(O)	0/0
586	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
587	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95	2,200.00	252.81	03/2023	03/2024	12(O)	0/0
588	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23	1,787.00	2.46	-	-	-	1/1
589	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91	800.00	512.67	-	03/2022	-	0/0
590	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00	466.65	.00	-	12/2023	-	0/0
591	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30	2,062.20	825.58	-	03/2022	-	0/2
592	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31	1,352.74	269.07	03/2020	03/2020	0(O)	1/1
593	KADAPA-BANGALORE (NL) KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77	2,132.77	331.17	03/2014	03/2024	120(O)	1/1
594	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93	310.70	257.06	-	03/2024	-	0/0
595	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00	685.99	47.07	03/2020	04/2022	25(O)	0/0
596	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43	860.43	697.21	03/2020	03/2020	0(O)	0/0
597	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59	1,870.41	914.00	03/2019	03/2021	24(O)	0/0
598	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54	678.54	466.93	03/2019	02/2021	23(O)	0/38
599	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00	28,181.00	.00	-	-	-	0/0
600	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03	2,063.03	675.97	03/2021	03/2023	24(O)	0/0
601	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38	636.38	.00	-	-	-	0/0
602	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00	1,08,000.00	4,115.87	12/2023	12/2023	0(O)	0/0
603	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00	51,101.00	22,485.00	03/2020	03/2020	0(O)	0/0
604	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14	1,540.00	233.84	03/2023	03/2023	0(O)	0/0
605	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00	845.58	834.59	03/2016	03/2021	60(O)	0/0
606	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52	3,000.00	781.71	03/2015	10/2021	79(O)	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
607	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00	4,274.00	.00	03/2020	03/2020	0(O)	0/0
608	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13	3,791.66	1,360.34	03/2009	03/2024	180(O)	0/0
609	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64	1,844.47	1,757.33	12/2017	03/2020	27(O)	0/0
610	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70	1,202.70	891.28	02/2015	12/2021	82(O)	0/0
611	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41	395.00	386.28	03/2009	12/2019	129(O)	1/1
612	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78	1,928.07	688.96	06/2021	03/2023	21(O)	0/0
613	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90	230.00	54.46	03/2015	-	-	0/0
614	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99	1,539.28	924.93	02/2019	03/2022	37(O)	0/0
615	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04	843.04	130.99	10/2020	03/2023	29(O)	0/0
616	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81	238.03	225.52	03/2020	03/2021	12(O)	0/0
617	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38	1,547.38	346.97	03/2022	03/2023	12(O)	0/0
618	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74	2,361.74	162.82	03/2022	03/2025	36(O)	0/0
619	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61	810.02	122.59	11/2018	03/2022	40(O)	0/0
620	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92	1,172.92	393.60	12/2018	03/2022	39(O)	0/0
621	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83	1,312.96	549.97	03/2020	06/2020	3(O)	0/0
622	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67	2,335.68	566.84	12/2024	12/2024	0(O)	0/0
623	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04	1,500.00	1,304.20	03/2020	03/2021	12(O)	0/0
624	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95	1,120.00	998.91	03/2019	03/2021	24(O)	0/0
625	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00	1,700.43	48.00	03/2020	06/2023	39(O)	0/0
626	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22	205.22	1.89	-	03/2024	-	0/0
627	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08	886.41	525.78	02/2019	03/2021	25(O)	0/0
628	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08	348.55	215.47	12/2019	06/2020	6(O)	0/0
629	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93	294.90	141.40	10/2018	10/2019	12(O)	0/0
630	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00	1,099.54	.00	-	-	-	0/1

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
631	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
632	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	420.18	160.53	03/2020 -	06/2020	3(O) -	0/0
633	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	303.56	262.32	11/2019 -	05/2020	6(O) -	0/0
634	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 281.03	410.00	351.23	02/2019 -	05/2020	15(O) -	0/0
635	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.25	- -	-	-	0/0
636	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	439.45	03/2018 -	03/2020	24(O) -	0/0
637	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	47.07	08/2022 -	09/2022	1(O) -	0/0
638	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	285.46	12/2015 -	-	-	0/0
639	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12(O) -	0/0
640	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	445.91	06/2013 -	-	-	1/4
641	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12(O) -	0/0
642	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	62.50	- -	-	-	0/0
643	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	241.39	- -	-	-	0/0
644	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	-	0/0
645	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	- -	-	-	0/0
646	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	303.72	- -	-	-	0/0
647	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
648	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	151.50	- -	03/2020	- -	0/0
649	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	951.24	724.96	- -	03/2020	- -	0/0
650	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71(O) -	0/0
651	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	927.86	03/2005 -	-	-	0/0
652	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	268.31	03/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
653	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
654	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022	0(O) -	0/0
655	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15(O) -	0/0
656	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.26	3.83	- -	-	-	0/0
657	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156(O) -	1/1
658	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	682.17	03/2016 -	12/2020	57(O) -	0/0
659	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
660	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	723.00 -	997.09	.00	- -	-	-	0/1
661	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	281.85	03/2021 -	03/2021	0(O) -	3/3
662	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	372.81	12/2024 -	12/2024	0(O) -	0/0
663	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022	0(O) -	0/0
664	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	650.00	45.24	03/2020 -	12/2021	21(O) -	2/3
665	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	03/2015	-	0/0
666	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
667	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
668	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
669	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,230.00	103.17	- -	03/2023	- -	0/0
670	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
671	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	328.56	03/2022 -	12/2019	-27(O) -	0/0
672	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020	0(O) -	4/6
673	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	750.56	343.30	03/2022 -	12/2024	33(O) -	0/0
674	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020	12(O) -	0/0
675	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	568.43	03/2023 -	12/2024	21(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
676	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	1,032.16	12/2020 -	03/2021	3(O) -	0/0
677	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	494.58	03/2020 -	03/2021	12(O) -	0/0
678	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	94.31	03/2019 -	12/2019	9(O) -	0/0
679	INDARA - DOHRGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	8.97	04/2016 -	06/2020	50(O) -	0/0
680	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
681	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
682	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
683	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	179.51	04/2017 -	01/2020	33(O) -	0/0
684	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
685	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	17.35	-	-	-	0/0
686	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	600.00	25.24	01/2022 -	01/2022	0(O) -	0/0
687	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16(O) -	0/0
688	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023	0(O) -	0/0
689	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021	0(O) -	0/6
690	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
691	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	229.48	-	06/2020	-	0/0
692	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,521.62	12/2024 -	03/2026	15(O) -	0/0
693	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12(O) -	0/0
694	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
695	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
696	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	863.39	03/2019 12/2009	03/2025	72(O) 0	0/0
697	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	834.72	12/2010 12/2017	03/2025	171(O) 0	7/7

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
698	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
699	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	2,106.00	03/2014 -	12/2025	141(O) -	0/0
700	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,226.44	03/2016 -	03/2025	108(O) -	0/0
701	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	2,913.50	847.45	03/2016 -	03/2025	108(O) -	0/0
702	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
703	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	- 0	0/0
704	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	- 0	0/0
705	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
706	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	154.98	- -	09/2021	- -	0/0
707	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	602.27 -	612.00	257.73	12/2021 -	03/2020	-21(O) -	0/0
708	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030	324(O) 0	0/0
709	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL ,	02/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-	-	0/0
	Total		4,61,117.38 -	6,60,824.02	1,90,365.20				27/137
	ROAD TRANSPORT AND HIGHWAYS								
710	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4
711	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	21.11	12/2017 -	-	-	0/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
712	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	148.80	04/2017 -	-	-	3/4
713	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	22.17	10/2018 -	-	-	0/4
714	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	19.87	10/2018 -	-	-	0/4
715	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019	0(O) -	0/0
716	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019	0(O) -	0/0
717	AJANTHA TO BULDHANA - [N24001008]MORTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	98.81	07/2019 -	07/2019	-	0/4
718	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
719	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65(O) -	0/0
720	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
721	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
722	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	152.72	10/2015 11/2019	10/2017	-	2/4
723	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
724	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
725	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	21.73	11/2018 -	-	-	0/0
726	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
727	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	1.15	03/2020 -	11/2019	-4(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
728	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	751.70	03/2020 -	05/2020	2(O) -	0/0
729	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	20.54	06/2017 -	11/2019	29(O) -	0/0
730	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	176.29	- -	11/2019	- -	0/0
731	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	326.24	- -	07/2021	- -	0/0
732	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	70.71	- -	-	-	0/0
733	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	586.73	- -	07/2021	- -	0/0
734	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 2,499.00	2,499.00	569.15	03/2021 -	04/2021	1(O) -	1/4
735	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	.00	- -	07/2021	- -	0/0
736	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	68.81	- -	02/2021	- -	0/0
737	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	24.90	- -	12/2020	- -	0/0
738	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	174.99	- -	03/2020	- -	0/0
739	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH ,	10/2015	333.21 -	333.21	263.88	12/2015 12/2019	12/2016	-	2/3
740	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	179.88	02/2017 12/2019	02/2019	-	2/4
741	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	237.18	01/2018 01/2020	01/2020	24(O) 0	3/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
742	REHABILITATION AND UPGRADE OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	69.47	05/2017 03/2020	05/2019	-	1/4
743	REHABILITATION AND UPGRADE OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	103.79	08/2017 03/2020	08/2019	24(O) -7	1/4
744	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	195.88	11/2017 03/2020	11/2019	24(O) 0	3/4
745	REHABILITATION AND UPGRADE OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	34.74	08/2018 03/2020	03/2020	19(O) 0	1/4
746	REHABILITATION AND UPGRADE OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	101.40	08/2018 02/2020	02/2020	18(O) 0	0/3
747	REHABILITATION AND UPGRADE OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	80.47	08/2018 02/2020	02/2020	18(O) 0	2/4
748	REHABILITATION AND UPGRADE OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MORTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	297.12	177.05	07/2018 01/2020	01/2020	18(O) 0	3/4
749	REHABILITATION AND UPGRADE OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	269.70	11/2018 05/2020	05/2020	18(O) 0	1/4
750	REHABILITATION AND UPGRADE OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	401.90	05/2016 03/2020	05/2018	-	2/4
751	REHABILITATION AND UPGRADE OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	129.17	08/2018 08/2020	08/2020	24(O) 6	2/4
752	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	303.71	01/2017 12/2019	07/2018	-	3/4
753	REHABILITATION AND UPGRADE OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	168.28	05/2016 08/2019	05/2018	-	2/4
754	REHABILITATION UPGRADE OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MORTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	157.26	08/2016 03/2020	08/2018	-	0/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
755	REHABILITATION AND UPGRADE OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	233.93	09/2016 03/2020	09/2018	-	2/4
756	REHABILITATION AND UPGRADE OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	189.59	08/2017 03/2020	08/2019	24(O) 0	2/4
757	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	87.58	09/2017 03/2020	09/2019	24(O) 0	0/4
758	REHABILITATION AND UPGRADE OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	196.46	01/2018 03/2020	01/2020	24(O) 0	1/4
759	REHABILITATION & UPGRADE OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/0
760	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	-	0/0
761	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
762	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 389.45	389.45	275.19	05/2012 06/2018	-	-	0/0
763	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	159.75	05/2018 -	08/2019	15(O) -	3/4
764	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	197.77	01/2019 -	-	-	4/4
765	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 197.16	197.16	66.17	10/2018 09/2015	09/2018	-	1/4
766	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21(O) -	1/3
767	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	90.29	11/2016 -	-	-	2/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
768	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	98.37	- -	09/2020	- -	0/4
769	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36(O) -	2/4
770	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	126.58	- -	12/2020	- -	2/4
771	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	17.43	01/2017 -	01/2020	36(O) -	2/4
772	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60(O) -	1/4
773	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	64.66	04/2017 03/2018	03/2021	47(O) 0	1/4
774	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	37.30	04/2017 -	-	-	1/4
775	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	49.12	04/2017 -	-	-	1/4
776	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	75.04	04/2017 -	-	-	1/4
777	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 168.32	168.32	28.67	04/2017 02/2018	02/2021	46(O) 0	1/4
778	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46(O) 0	0/4
779	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 216.71	216.71	15.77	04/2017 02/2018	02/2021	46(O) 0	0/4
780	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 167.28	167.28	18.70	04/2017 02/2018	02/2021	46(O) 0	1/1
781	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	24.14	04/2017 -	-	-	1/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
782	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
783	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	72.97	- -	-	-	0/0
784	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	154.14	- -	-	-	0/0
785	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH ,	05/2016	259.52 -	259.52	143.01	- -	-	-	0/0
786	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	125.96	- -	-	-	0/0
787	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	30.88	- -	-	-	0/0
788	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 175.06	175.06	6.58	- 04/2019	04/2022	- 0	0/0
789	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 176.12	176.12	5.63	- 04/2019	04/2022	- 0	0/0
790	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH ,	02/2017	199.02 199.02	199.02	9.65	- 02/2018	02/2021	- 0	0/0
791	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH ,	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	- 0	0/0
792	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	115.02	- 01/2016	01/2019	-	0/0
793	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH ,	07/2015	189.91 -	189.91	154.43	- -	-	-	0/4
794	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	108.75	- -	-	-	3/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
795	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
796	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MORTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	1,979.00	59.40	- -	-	-	0/0
797	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]PWD,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	30.04	- -	-	-	0/0
798	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 456.92	525.00	488.37	02/2009 -	-	-	0/0
799	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 340.14	340.14	319.96	04/2009 03/2011	08/2019	124(O) 0	0/0
800	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 408.77	408.77	395.78	11/2008 07/2011	01/2014	-	0/0
801	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 255.23	255.23	251.39	11/2008 01/2011	08/2013	-	0/0
802	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	224.28	03/2008 -	08/2020	149(O) -	0/0
803	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019	136(O) -	0/0
804	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020	143(O) -	0/0
805	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019	-	0/0
806	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 655.17	655.17	655.17	07/2009 -	-	-	0/0
807	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	451.15	04/2010 -	07/2019	-	0/0
808	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	120.86	05/2018 05/2020	12/2020	31(O) 0	2/4
809	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42(O) 0	0/4
810	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42(O) 0	0/4
811	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	304.28	01/2019 -	-	-	2/4
812	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	66.66	11/2018 -	-	-	4/4
813	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	356.31	11/2018 -	-	-	2/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
814	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	201.56	05/2017 -	-	-	0/0
815	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	344.32	02/2011 -	-	-	0/0
816	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 307.47	307.47	256.26	02/2018 -	-	-	0/0
817	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	26.00	12/2018 -	-	-	1/4
818	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	66.66	06/2018 -	-	-	1/4
819	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	50.39	- -	-	-	1/4
820	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	16.98	12/2018 -	-	-	0/4
821	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63(O) 0	1/4
822	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021	71(O) 0	0/4
823	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	292.24	01/2016 -	-	-	2/3
824	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	58.58	- -	06/2020	- -	0/4
825	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]PWD,ASSAM ,	09/2018	160.00 -	160.00	.50	09/2021 -	09/2021	0(O) -	0/0
826	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70(O) -	0/0
827	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	1,049.51	.00	- -	-	-	0/0
828	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	885.47	02/2013 -	-	-	0/0
829	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	329.40	05/2013 -	-	-	0/0
830	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
831	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
832	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	843.67	07/2013 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
833	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	566.60	11/2013 -	-	-	0/0
834	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	780.77	152.37	-	-	-	0/0
835	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	278.45	08/2016 -	-	-	0/0
836	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	323.60	10/2016 -	-	-	0/0
837	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	-	-	-	0/0
838	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	214.34	04/2019 -	-	-	0/0
839	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	384.48	-	01/2020	-	0/0
840	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24(O)	0/0
841	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	131.71	-	10/2020	-	0/0
842	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	113.26	-	12/2019	-	0/0
843	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6(O)	0/0
844	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	-	-	-	0/0
845	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	579.78	-	-	-	0/0
846	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	417.09	04/2018 -	-	-	0/0
847	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	-	-	-	0/0
848	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	369.77	113.67	-	-	-	0/0
849	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
850	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	596.44	07/2016 -	-	-	0/0
851	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
852	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	93.11	05/2016 -	-	-	0/0
853	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
854	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	267.22	05/2016 -	-	-	0/0
855	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	753.03	10/2016 -	-	-	0/0
856	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
857	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	280.00	11/2015 -	-	-	0/0
858	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	-	-	0/0
859	REHABILATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	719.20	12/2016 -	-	-	0/0
860	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
861	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	05/2021	14(O) -	0/0
862	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54(O) -	0/0
863	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
864	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
865	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
866	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
867	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
868	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD,BIHAR ,	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019	0(O) -	0/0
869	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR ,	03/2018	153.24 -	153.24	2.06	- -	-	-	0/0
870	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR ,	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52(O) -	0/0
871	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]PWD,BIHAR ,	02/2019	2,926.42 -	2,926.42	.00	- -	-	-	0/0
872	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	181.90	- -	-	-	0/0
873	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	445.75	12/2015 -	-	-	0/0
874	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	389.78	05/2018 10/2019	10/2019	17(O) 0	0/0
875	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 08/2018	08/2018	-	0/0
876	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23(O) 0	0/0
877	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	.00	- 03/2021	03/2021	- 0	0/0
878	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	-	-	0/0
879	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHDDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	12/2019	3(O) -	0/0
880	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
881	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	153.33	- -	-	-	0/4
882	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	91.39	- -	-	-	2/4
883	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	290.59	280.47	- -	-	-	3/4
884	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	262.25	- -	-	-	0/0
885	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	259.46	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
886	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	191.63	- -	-	-	0/0
887	PATRADEVI TO KARASWADA 4L - [N24001004]MORTH,GOA ,	03/2017	634.32 634.32	634.32	102.33	05/2020 -	05/2020	0(O) -	1/4
888	KARASWADA TO BAMBOLIM - [N24001005]MORTH,GOA ,	03/2017	852.67 852.67	852.67	108.04	12/2019 -	12/2019	0(O) -	1/4
889	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,187.21	09/2012 -	-	-	2/3
890	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	-	-	0/0
891	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 2,521.24	2,521.24	4,659.71	12/2015 -	-	-	3/3
892	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0
893	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	435.25	- -	08/2019	- -	0/0
894	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	140.44	- -	10/2019	- -	0/0
895	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	321.67	- -	09/2019	- -	0/0
896	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	357.12	- -	08/2019	- -	0/0
897	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	-	-	0/0
898	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	392.00	240.57	- -	12/2019	- -	0/0
899	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	75.08	- -	01/2020	- -	0/0
900	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	262.83	- -	09/2019	- -	0/0
901	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	- -	0/0
902	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2(O) -	0/0
903	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	11/2019	25(O) -	0/0
904	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 1,449.00	1,449.00	1,296.87	- -	01/2021	- -	0/0
905	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	- -	01/2021	- -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
906	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	.00	- -	07/2021	-	0/0
907	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
908	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN - [N24000920]PWD, GUJARAT ,	03/2016	223.67 -	223.67	112.81	02/2017 -	-	-	4/4
909	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD, GUJARAT , EPC	03/2016	208.34 -	208.34	112.87	02/2016 -	-	-	0/4
910	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD, GUJARAT , EPC	12/2017	867.97 -	867.97	90.63	11/2018 -	-	-	0/1
911	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]PWD, GUJARAT , EPC	03/2018	464.07 399.35	464.07	14.17	11/2018 -	-	-	0/1
912	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD, GUJARAT , EPC	10/2018	400.76 386.19	400.76	4.45	05/2019 -	-	-	0/0
913	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD, GUJARAT , EPC	08/2017	962.43 887.21	962.43	45.70	03/2018 -	-	-	0/1
914	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]PWD, GUJARAT ,	03/2018	351.00 -	351.00	.48	06/2021 -	06/2021	0(O) -	0/0
915	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118(O) -	0/0
916	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 2,967.50	2,967.50	3,982.72	11/2011 -	03/2020	100(O) -	0/0
917	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
918	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 507.70	507.70	494.29	06/2016 -	09/2019	39(O) -	0/0
919	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 537.16	537.16	491.45	07/2018 -	09/2019	14(O) -	0/0
920	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	971.24	04/2019 -	-	-	0/0
921	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
922	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA ,	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6(O) -	0/0
923	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	1,004.67	576.86	05/2019 -	02/2019	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
924	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	480.73	03/2020 -	09/2019	-6(O) -	0/0
925	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	45.34	- -	12/2020	- -	0/0
926	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	.00	- -	03/2020	- -	0/0
927	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	.00	- -	03/2020	- -	0/0
928	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 931.21	931.21	2.55	- -	07/2021	- -	0/0
929	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	80.90	- -	07/2021	- -	0/0
930	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	.00	- -	03/2020	- -	0/0
931	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	.00	- -	06/2020	- -	0/0
932	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	.00	- -	03/2020	- -	0/0
933	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA ,	01/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019	6(O) 0	0/0
934	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 07/2019	-	-	0/0
935	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	.00	- -	-	-	0/0
936	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	.00	- -	-	-	0/0
937	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	.00	- -	-	-	0/0
938	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	.00	- -	-	-	0/0
939	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	.00	- -	-	-	0/0
940	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	.00	- -	-	-	0/0
941	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	.00	- -	-	-	0/0
942	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	.00	- -	-	-	0/0
943	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
944	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	452.30	03/2018 -	-	-	0/0
945	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	267.38	02/2019 -	06/2019	-	0/0
946	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	234.67	- -	09/2020	- -	0/0
947	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	07/2020	- -	0/0
948	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	179.17	- -	11/2019	- -	0/0
949	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15(O) -	0/0
950	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	.00	- -	05/2021	- -	0/0
951	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,700.67	07/2015 12/2019	09/2020	62(O) 0	0/0
952	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 2,519.00	2,519.00	4,705.68	06/2015 -	-	-	0/0
953	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
954	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,075.87	06/2014 -	-	-	0/0
955	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	621.26	06/2019 -	12/2020	18(O) -	0/0
956	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 2,273.00	2,136.97	1,214.48	12/2018 12/2019	07/2020	19(O) 9	0/0
957	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	376.15	- -	01/2021	- -	1/3
958	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	70.31	08/2018 -	-	-	1/4
959	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	.00	11/2018 -	-	-	0/4
960	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	.00	07/2019 -	-	-	0/0
961	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
962	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	728.62	03/2019 -	07/2019	-	0/0
963	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	303.12	- 12/2017	12/2019	- 0	0/0
964	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17(O) -	0/0
965	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	117.09	03/2020 -	09/2019	-6(O) -	0/0
966	4 LANING OF KUTCERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	91.24	03/2020 -	06/2019	-	0/0
967	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
968	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0
969	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 1,073.10	1,005.08	.00	- 03/2019	03/2021	- 0	0/0
970	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD,JHARKHAND ,	03/2018	212.99 -	212.99	80.47	06/2020 -	06/2020	0(O) -	0/0
971	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18(O) -	3/3
972	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
973	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
974	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
975	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52(O) -	0/0
976	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,138.07	08/2018 -	03/2020	19(O) -	0/0
977	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20(O) -	0/0
978	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20(O) -	0/0
979	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	657.08	04/2020 -	04/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
980	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 870.00	870.00	254.96	03/2019 03/2017	08/2020	17(O) 2	0/0
981	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 1,008.00	1,108.00	1,353.61	08/2019 -	12/2020	16(O) -	0/0
982	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	567.90	03/2020 -	07/2020	4(O) -	0/0
983	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	626.56	03/2020 -	06/2020	3(O) -	0/0
984	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	113.59	- -	-	-	0/0
985	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 2,190.00	2,400.00	1,371.02	- 05/2019	11/2021	- 0	0/0
986	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 2,283.50	2,450.00	691.88	- 10/2019	-	-	0/0
987	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
988	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
989	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]PWD,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0
990	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
991	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
992	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0
993	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
994	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
995	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA ,	03/2018	325.86 -	325.86	62.54	10/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
996	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
997	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
998	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
999	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
1000	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
1001	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24(O) -	0/0
1002	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
1003	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24(O) -	0/0
1004	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]PWD,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
1005	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88(O) -	0/0
1006	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27(O) -	0/0
1007	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	814.55	- -	10/2019	- -	0/0
1008	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	425.58	06/2018 -	01/2020	19(O) -	0/0
1009	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	278.60	09/2017 -	06/2020	33(O) -	0/0
1010	6-LANNING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1011	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-	-	0/4
1012	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/3
1013	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1014	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	191.77	- -	03/2020	- -	0/0
1015	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36(O) -	0/0
1016	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1017	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54(O) -	0/0
1018	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	.00	04/2015 -	10/2019	54(O) -	0/0
1019	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 622.00	622.00	601.52	- -	10/2019	- -	0/0
1020	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 622.00	622.00	543.86	- -	10/2019	- -	0/0
1021	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	248.66	01/2020 -	01/2020	0(O) -	0/0
1022	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	467.50	02/2020 -	02/2020	0(O) -	0/0
1023	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	588.21	- 06/2015	06/2015	-	0/0
1024	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1025	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1026	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	623.93	- 06/2015	06/2015	-	0/0
1027	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	-	0/3
1028	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADHYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	240.05	08/2017 -	02/2020	30(O) -	0/0
1029	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	140.57	01/2019 -	08/2019	7(O) -	0/0
1030	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27(O) -	0/0
1031	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1032	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	17.41	09/2017 -	01/2021	40(O) -	0/0
1033	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	- -	-	-	0/0
1034	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	328.34	- -	08/2020	- -	0/0
1035	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	- -	-	-	0/0
1036	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH ,	03/2018	162.56 -	162.56	88.47	03/2018 -	12/2019	21(O) -	0/0
1037	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH ,	03/2018	166.21 -	166.21	26.72	08/2018 -	06/2020	22(O) -	0/0
1038	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH ,	02/2018	169.63 -	169.63	9.35	03/2018 -	07/2020	28(O) -	0/0
1039	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH ,	11/2017	235.91 -	235.91	97.39	02/2018 -	11/2019	21(O) -	0/0
1040	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH ,	11/2017	184.62 -	184.62	55.27	02/2018 -	11/2019	21(O) -	0/0
1041	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH ,	03/2018	191.21 -	191.21	72.02	11/2019 -	11/2019	0(O) -	0/0
1042	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH ,	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39(O) -	0/0
1043	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH ,	03/2018	214.69 -	214.69	19.35	03/2018 -	11/2019	20(O) -	0/0
1044	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH ,	03/2018	217.22 -	217.22	12.39	08/2018 -	06/2020	22(O) -	0/0
1045	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH ,	03/2018	233.04 -	233.04	95.28	03/2018 -	11/2019	20(O) -	0/0
1046	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH ,	11/2017	249.05 -	249.05	118.29	07/2018 -	01/2020	18(O) -	0/0
1047	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH ,	11/2017	254.17 -	254.17	139.41	02/2018 -	11/2019	21(O) -	0/0
1048	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH ,	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25(O) -	0/0
1049	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH ,	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1050	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH ,	01/2017	373.82 -	373.82	116.33	09/2019 -	05/2020	8(O) -	0/0
1051	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH ,	01/2016	809.16 -	809.16	219.42	07/2018 -	02/2020	19(O) -	0/0
1052	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH ,	03/2016	877.79 -	877.79	436.12	06/2019 -	11/2019	5(O) -	0/0
1053	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH ,	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	11(O) -	0/0
1054	ANJANGAON TO MAH/MP BORDER - [N24001007]MORTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	182.80	06/2019 -	-	-	0/4
1055	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH ,	11/2017	392.33 -	392.33	224.94	03/2018 -	11/2019	20(O) -	0/0
1056	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MORTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	.00	03/2021 -	03/2021	0(O) -	0/0
1057	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.88	.00	- -	-	-	0/0
1058	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019	81(O) -	0/0
1059	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1060	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	52.00	- -	-	-	0/4
1061	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1062	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	259.50	- -	-	-	3/4
1063	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1064	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1065	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	83.11	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1066	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1067	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020	24(O) -1	0/0
1068	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1069	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31(O) -	0/0
1070	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	134.18	03/2019 04/2021	04/2021	25(O) 0	0/0
1071	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	220.70	05/2018 04/2019	09/2020	28(O) 4	0/0
1072	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019	27(O) -	0/0
1073	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	750.87	11/2016 -	05/2020	42(O) -	0/0
1074	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	226.24	06/2006 -	-	-	0/0
1075	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 67.34	1,871.34	3,424.19	01/2018 12/2018	11/2019	22(O) 0	0/0
1076	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1077	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	22.27	07/2018 -	-	-	0/0
1078	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17(O) 0	0/0
1079	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17(O) 0	0/0
1080	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	726.85	- -	-	-	0/0
1081	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	- -	-	-	0/0
1082	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	336.37	- -	07/2021	- -	1/4
1083	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	07/2021	- -	0/4
1084	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23(O) -	0/0
1085	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1086	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 315.00	315.00	215.98	- 03/2020	03/2019	-	0/0
1087	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	243.33	05/2019 -	12/2019	7(O) -	0/0
1088	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 911.07	904.16	817.58	02/2020 11/2017	05/2020	3(O) 0	0/0
1089	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	02/2020	-1(O) -	0/0
1090	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1091	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2(O) -	0/0
1092	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5(O) -	0/0
1093	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 1,071.00	1,071.00	556.63	03/2017 05/2018	11/2020	44(O) 0	0/0
1094	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	248.60	03/2020 -	09/2019	-6(O) -	0/0
1095	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5(O) -	0/0
1096	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 448.18	404.94	102.43	- -	10/2020	- -	0/0
1097	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	120.17	- -	08/2021	- -	0/1
1098	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	303.91	- -	04/2021	- -	2/3
1099	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	30.82	- 11/2020	11/2020	- 0	0/0
1100	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	21.91	- -	11/2020	- -	0/0
1101	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	15.01	- -	07/2021	- -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1102	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	261.97	- -	12/2020	- -	0/0
1103	SARSAM TO KOTHARI - [N24001002]MORTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	65.01	07/2019 -	-	-	0/4
1104	AKOLA TO AKOT - [N24001003]MORTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	37.05	06/2019 -	-	-	0/4
1105	AKOT TO ANJANGAON - [N24001006]MORTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	182.98	06/2019 -	-	-	0/4
1106	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	102.79	05/2019 -	12/2019	7(O) -	0/0
1107	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	123.43	05/2019 -	12/2019	7(O) -	0/4
1108	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	202.08	05/2019 -	-	-	0/4
1109	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	287.00	06/2019 -	10/2019	4(O) -	0/4
1110	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	68.00	06/2019 -	06/2020	12(O) -	0/0
1111	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6(O) -	0/0
1112	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	153.29	06/2019 -	12/2019	6(O) -	0/0
1113	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	259.90	06/2019 -	-	-	0/0
1114	DAHEGAON TO KUHI - [N24001017]MORTH,MAHARASHTRA ,	01/2017	228.89 228.89	228.89	125.00	06/2019 -	-	-	3/4
1115	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	281.60	06/2019 -	-	-	0/0
1116	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	257.34	06/2019 -	08/2019	2(O) -	0/4
1117	AMD I TO SAONER - [N24001021]MORTH,MAHARASHTRA ,	01/2017	396.91 396.91	396.91	248.48	06/2019 -	08/2019	2(O) -	3/4
1118	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA ,	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12(O) -	1/4
1119	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	168.81	06/2019 -	12/2019	6(O) -	0/4
1120	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA ,	01/2017	457.52 457.52	457.52	202.98	07/2019 -	07/2020	12(O) -	2/4
1121	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA ,	01/2017	355.17 355.17	355.17	164.87	07/2019 -	12/2019	5(O) -	3/4
1122	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA ,	01/2017	376.19 376.19	376.19	29.03	05/2019 -	05/2020	12(O) -	1/4
1123	SHAHPUR PATGAON SECTION I - [N24001027]MORTH,MAHARASHTRA ,	01/2018	150.79 150.79	150.79	21.42	12/2019 -	12/2019	0(O) -	1/4
1124	PATGAON KHOPOLI SECTION I - [N24001028]MORTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	39.57	12/2019 -	12/2019	0(O) -	0/4
1125	AHMADPUR TO PIMPLA - [N24001029]MORTH,MAHARASHTRA ,	01/2017	422.38 422.38	422.38	169.58	08/2019 -	08/2019	0(O) -	2/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1126	PIMPLA TO MANJARUMBHA - [N24001030]MORTH,MAHARASHTRA ,	01/2017	595.77 595.77	595.77	132.44	08/2019 -	08/2019	0(O) -	2/4
1127	MANJUSUMBA TO CHUMBALI - [N24001031]MORTH,MAHARASHTRA ,	01/2017	228.54 228.54	228.54	99.30	08/2019 -	08/2019	0(O) -	2/4
1128	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	171.78	05/2019 -	05/2020	12(O) -	0/4
1129	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MORTH,MAHARASHTRA ,	01/2017	486.19 486.19	486.19	215.29	07/2019 -	07/2019	-	2/4
1130	PARTUR TO MAJALGAON - [N24001034]MORTH,MAHARASHTRA ,	01/2017	420.57 420.57	420.57	215.39	07/2019 -	07/2019	-	2/4
1131	MANSAR TO SALAIKHURD - [N24001035]MORTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	116.13	12/2019 -	12/2019	0(O) -	0/4
1132	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.33	07/2019 -	07/2019	-	0/0
1133	KAIJ TO KUSALAM - [N24001037]MORTH,MAHARASHTRA ,	01/2017	554.78 554.78	554.78	159.90	07/2019 -	07/2019	-	2/4
1134	MAHAD TO RAIGAD FORT - [N24001038]MORTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	8.34	05/2020 -	05/2020	0(O) -	0/4
1135	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA ,	01/2017	356.66 356.66	356.66	35.88	- -	-	-	0/4
1136	JAHIRABAD TO LATUR - [N24001040]MORTH,MAHARASHTRA ,	01/2017	461.96 461.96	461.96	151.43	11/2019 -	11/2019	0(O) -	2/4
1137	SHIROD SHAHPURER TO NANDED - [N24001041]MORTH,MAHARASHTRA ,	01/2017	211.34 211.34	211.34	101.83	07/2019 -	07/2019	-	2/4
1138	SALAIKHURD TO TIRORA - [N24001042]MORTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019	0(O) -	0/4
1139	NILAJPHATA TO BHANDARA - [N24001043]MORTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020	0(O) -	0/4
1140	KALMAB TO RALEGAON - [N24001044]MORTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	294.91	06/2019 -	-	-	0/4
1141	JALGAON TO BHADGAON - [N24001045]MORTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019	0(O) -	0/4
1142	RALEGAON TO RAMTIRTH - [N24001046]MORTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	106.69	07/2019 -	-	-	0/4
1143	BHADGAON TO CHALISGAON - [N24001047]MORTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019	0(O) -	0/0
1144	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	85.51	07/2019 -	-	-	0/0
1145	KARAD TO VITA - [N24001049]MORTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	68.04	12/2019 -	12/2019	0(O) -	0/4
1146	VITA TO NAGAJ - [N24001050]MORTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019	0(O) -	0/4
1147	NALDURG TO AKKALKOT - [N24001051]MORTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	61.39	12/2019 -	12/2019	0(O) -	0/4
1148	SANGOLA TO JATH - [N24001052]MORTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	61.15	12/2019 -	12/2019	0(O) -	0/4
1149	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	85.97	06/2019 -	06/2020	12(O) -	0/4
1150	TASGAON TO SHIRDHON - [N24001054]MORTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1151	HELWAK TO KARAD - [N24001055]MORTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	113.40	07/2019 -	-	-	0/4
1152	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	238.01	07/2019 -	-	-	0/0
1153	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12(O) -	0/4
1154	KARWANDI TO RAJURI - [N24001058]MORTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	81.47	12/2019 -	12/2019	0(O) -	0/4
1155	SHIVUR TO YEOLA - [N24001059]MORTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	2.50	12/2019 -	12/2019	0(O) -	0/4
1156	PALPHATA TO PHULAMBARI - [N24001060]MORTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	60.23	12/2019 -	12/2019	0(O) -	0/4
1157	CHIKALI TO DHAD - [N24001061]MORTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	21.54	12/2019 -	12/2019	0(O) -	0/4
1158	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MORTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	64.66	12/2019 -	12/2019	0(O) -	0/4
1159	WADIGODRI TO DHANGRIPIPRI - [N24001063]MORTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	68.23	02/2020 -	02/2020	0(O) -	0/4
1160	DHANGRIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MORTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	66.77	02/2020 -	02/2020	0(O) -	0/4
1161	PARBHANI TO GANGKHED - [N24001065]MORTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	40.85	12/2019 -	12/2019	0(O) -	0/4
1162	LATUR TO PANGAON - [N24001066]MORTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	109.48	12/2019 -	12/2019	0(O) -	0/4
1163	OMREGA TO AUSA - [N24001067]MORTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	124.24	12/2019 -	12/2019	0(O) -	0/4
1164	WASHIM TO DASTAPUR - [N24001068]MORTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	35.45	12/2019 -	12/2019	0(O) -	1/4
1165	NANDED TO JALKOT - [N24001069]MORTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	54.50	09/2019 -	09/2019	0(O) -	1/4
1166	DASTAPUR TO KARANJA - [N24001070]MORTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	83.40	12/2019 -	12/2019	0(O) -	2/4
1167	JALKOT TO TOGRI - [N24001071]MORTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020	0(O) -	0/4
1168	KHERDA TO NAGZARI - [N24001072]MORTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	70.50	12/2019 -	12/2019	0(O) -	0/4
1169	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020	0(O) -	0/0
1170	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	72.20	12/2019 -	12/2019	0(O) -	0/0
1171	OSMANNAGAR TO KUNDRAL - [N24001075]MORTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	33.02	08/2020 -	08/2020	0(O) -	0/4
1172	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	106.46	12/2019 -	12/2019	0(O) -	0/0
1173	KUNDRAL TO WAZAR - [N24001077]MORTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	121.75	12/2019 -	12/2019	0(O) -	2/4
1174	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	13.50	12/2019 -	12/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1175	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MORTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020	0(O) -	1/4
1176	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	15.50	12/2019 -	12/2019	0(O) -	0/0
1177	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MORTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	12.30	12/2019 -	12/2019	0(O) -	1/4
1178	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	21.42	12/2019 -	12/2019	0(O) -	0/0
1179	CHIKLI TO TAKARKHED - [N24001083]MORTH,MAHARASHTRA ,	03/2018	393.10 393.10	393.10	125.97	12/2019 -	12/2019	0(O) -	2/4
1180	PAHUR TO BODHWAD - [N24001084]MORTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	40.23	05/2020 -	05/2020	0(O) -	0/4
1181	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	87.26	06/2019 -	12/2019	6(O) -	0/4
1182	BODHWAD TO STATE BORDER - [N24001086]MORTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	118.95	07/2019 -	-	-	0/4
1183	MANGRUPHIR TO MAHAN - [N24001087]MORTH,MAHARASHTRA ,	03/2018	222.13 222.13	222.13	60.36	11/2019 -	11/2019	0(O) -	0/4
1184	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	55.69	12/2019 -	12/2019	0(O) -	0/0
1185	MALEGAON TO RISOD - [N24001089]MORTH,MAHARASHTRA ,	02/2018	303.24 303.24	303.24	107.97	12/2019 -	12/2019	0(O) -	0/4
1186	KOLDE TO KHETIYA - [N24001090]MORTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	175.93	07/2019 -	-	-	0/4
1187	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIYAKALA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019	0(O) -	0/0
1188	SATARA TO MHASWAD - [N24001092]MORTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	202.42	07/2019 -	-	-	0/4
1189	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019	0(O) -	0/0
1190	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	25.94	03/2019 -	12/2019	9(O) -	0/0
1191	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	188.77	- -	-	-	0/0
1192	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	32.71	03/2019 -	12/2019	9(O) -	0/0
1193	SELDOH TO PANVAR - [N24001097]MORTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020	0(O) -	0/4
1194	WARDHA TO HINGAGHAT - [N24001098]MORTH,MAHARASHTRA ,	01/2018	216.90 216.90	216.90	45.00	12/2019 -	12/2019	0(O) -	1/4
1195	MHASWAD TO TEMBHURNI - [N24001099]MORTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	182.71	07/2019 -	-	-	0/4
1196	AHMEDNAGAR TO BARAMATI - [N24001100]MORTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	338.50	08/2019 -	08/2019	0(O) -	0/4
1197	KURUDWADI TO PANDHARPUR - [N24001101]MORTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	148.17	07/2019 -	-	-	0/4
1198	PANDHARPUR TO SANGOLA - [N24001102]MORTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1199	SARAD VANI PIMPALGAON - [N24001103]MORTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	103.63	07/2019 -	-	-	0/4
1200	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12(O) -	2/4
1201	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	146.72	03/2019 -	-	-	0/4
1202	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	.00	03/2018 -	12/2019	21(O) -	0/4
1203	PANCHARAL TO MANDANGHAR - [N24001107]MORTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020	0(O) -	0/4
1204	CHALISGAON TO NANDGAON - [N24001108]MORTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	78.89	12/2019 -	12/2019	0(O) -	0/4
1205	KUSUMBA TO MALEGAON - [N24001109]MORTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	67.02	12/2019 -	12/2019	0(O) -	0/4
1206	BAMNI TO NAVAEGAON - [N24001110]MORTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	146.29	04/2020 -	04/2020	0(O) -	1/4
1207	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12(O) -	0/4
1208	NASRATPUR TO BARASGAON - [N24001112]MORTH,MAHARASHTRA ,	07/2016	406.54 406.54	406.54	142.00	09/2019 -	09/2019	0(O) -	2/4
1209	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	148.00	09/2018 -	04/2021	31(O) -	0/4
1210	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA ,	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3(O) -	1/4
1211	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA ,	01/2017	1,598.47 1,598.47	1,598.47	751.91	11/2019 -	03/2020	4(O) -	1/4
1212	GADCHIROLI TO MUL - [N24001116]MORTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	160.31	06/2019 -	-	-	2/4
1213	MUL TO CHANDRAPUR - [N24001117]MORTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019	-	1/4
1214	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA ,	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5(O) -	0/4
1215	NAGBHID TO ARMORI - [N24001119]MORTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	197.91	07/2019 -	-	-	0/4
1216	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12(O) -	0/4
1217	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12(O) -	0/4
1218	PAITHAN TO SHIRUR - [N24001122]MORTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	117.89	06/2019 -	-	-	0/4
1219	SHIRUR TO KHARDA - [N24001123]MORTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	100.79	06/2019 -	-	-	0/4
1220	AURANGABAD TO SILLOD - [N24001124]MORTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	91.75	06/2019 -	-	-	0/4
1221	SILLOD TO FARDAPUR - [N24001125]MORTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	39.22	06/2019 -	-	-	0/4
1222	FARDAPUR TO JALGAON - [N24001126]MORTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	56.74	06/2019 -	-	-	0/4
1223	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	281.03	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1224	BHOKAR TO SARSAM - [N24001128]MORTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	162.64	07/2019 -	-	-	0/4
1225	BHOGAN KHURD TO KASHEDI - [N24001132]MORTH,MAHARASHTRA ,	09/2017	743.21 743.21	743.21	131.87	06/2021 -	06/2021	0(O) -	1/4
1226	PARSHURAM GHAT TO ARAWALI - [N24001133]MORTH,MAHARASHTRA ,	04/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019	-1(O) -	1/4
1227	KANTE TO WAKED - [N24001134]MORTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.02	1,230.02	500.61	11/2019 -	11/2019	0(O) -	1/4
1228	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	357.60	02/2019 -	-	-	0/0
1229	TALGAON TO KALMATH - [N24001136]MORTH,MAHARASHTRA ,	10/2016	904.70 904.70	904.70	604.05	03/2020 -	03/2020	0(O) -	2/4
1230	KALMATH TO ZARAP - [N24001137]MORTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.13	1,338.13	959.51	03/2020 -	03/2020	0(O) -	3/5
1231	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA ,	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12(O) -	1/4
1232	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA ,	02/2018	355.99 355.99	355.99	112.97	12/2019 -	12/2019	0(O) -	0/0
1233	WARDHA TO ARVI - [N24001150]MORTH,MAHARASHTRA ,	02/2018	313.58 313.58	313.58	4.96	04/2020 -	04/2020	0(O) -	0/4
1234	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	119.56	10/2018 -	10/2021	36(O) -	1/4
1235	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]PWD,MANIPUR ,	10/2016	235.31 -	235.31	74.49	11/2020 -	11/2020	0(O) -	0/0
1236	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	708.82	05/2018 03/2018	12/2019	19(O) 3	0/0
1237	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	27.90	- -	09/2021	- -	0/4
1238	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	42.66	05/2019 -	-	-	0/0
1239	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105(O) -	0/0
1240	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110(O) -	0/0
1241	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLA) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116(O) -	0/0
1242	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	.00	09/2019 -	09/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1243	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	.00	09/2019 -	09/2019	0(O) -	0/0
1244	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	.00	09/2019 -	09/2019	0(O) -	0/0
1245	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	.00	09/2019 -	09/2019	0(O) -	0/0
1246	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	.00	09/2019 -	09/2019	0(O) -	0/0
1247	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	.00	09/2019 -	09/2019	0(O) -	0/0
1248	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	.00	09/2019 -	09/2019	0(O) -	0/0
1249	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	.00	09/2019 -	09/2019	0(O) -	0/0
1250	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM ,	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63(O) -	0/0
1251	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128(O) -	0/0
1252	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	303.71	08/2011 -	-	-	2/2
1253	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1254	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69(O) -	0/0
1255	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81(O) -	0/0
1256	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-	-	0/0
1257	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1258	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,326.00	-	02/2020	-	0/0
1259	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1260	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0
1261	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1262	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 387.00	373.07	203.77	08/2016 -	08/2019	36(O) -	2/4
1263	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 339.55	396.52	234.03	08/2016 -	06/2020	46(O) -	2/4
1264	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 340.00	429.52	166.55	08/2016 -	08/2019	36(O) -	2/4
1265	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	121.20	04/2017 -	-	-	1/4
1266	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	127.19	09/2018 -	-	-	1/4
1267	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	-	-	0/0
1268	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 233.35	339.57	.00	09/2018 07/2019	-	-	0/0
1269	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 05/2019	-	-	0/4
1270	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	-	-	0/0
1271	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	4.38	09/2018 -	-	-	0/2
1272	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	2.11	09/2018 -	-	-	0/2
1273	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 136.73	237.72	59.42	09/2018 11/2018	-	-	1/2
1274	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 160.10	251.97	13.42	09/2018 11/2018	-	-	0/2

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1275	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	12.76	09/2018 11/2018	-	-	0/2
1276	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	6.86	09/2018 -	-	-	1/2
1277	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	-	-	1/2
1278	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/0
1279	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/0
1280	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]PWD,NAGALAND ,	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020	0(O) -	0/0
1281	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]PWD,NAGALAND ,	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020	0(O) -	0/0
1282	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]PWD,NAGALAND ,	11/2016	336.25 369.96	336.25	62.64	09/2019 -	09/2019	0(O) -	0/0
1283	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]PWD,NAGALAND ,	03/2017	217.35 -	217.35	35.10	11/2020 -	11/2020	0(O) -	0/0
1284	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]PWD,NAGALAND ,	03/2019	237.51 -	237.51	.00	12/2022 -	12/2022	0(O) -	0/0
1285	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1286	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	-	-	0/0
1287	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1288	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1289	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1290	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	204.92	- -	04/2020	- -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1291	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	-	11/2019	-	0/0
1292	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22(O) -	0/0
1293	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52(O) -	0/0
1294	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	502.75	-	07/2019	-	0/0
1295	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	231.96	08/2019 -	08/2019	0(O) -	0/0
1296	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	449.84	-	07/2020	-	0/0
1297	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43(O) -	0/0
1298	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1299	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1300	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1301	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41(O) -	0/0
1302	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1303	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	348.24	03/2020 -	03/2021	12(O) -	0/0
1304	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 11/2020	06/2021	47(O) 0	0/0
1305	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	80.87	- 07/2020	06/2021	- 0	0/0
1306	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	-	-	-	0/0
1307	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	94.03	- 05/2020	06/2021	- 0	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1308	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	99.10	- 05/2020	06/2021	- 0	0/0
1309	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1310	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000733]NHAI,ODISHA ,	01/2018	614.48 -	614.48	31.00	- -	08/2021	-	0/0
1311	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	08/2021	-	0/0
1312	REHABILITATION AND UPGADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	71.38	- 03/2020	06/2021	- 0	0/0
1313	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1314	REHABILITATION AND UPGADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1315	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	06/2021	-	0/0
1316	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	4.03	- -	04/2021	-	0/0
1317	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1318	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1319	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1320	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1321	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1322	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1323	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1324	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	666.72	- 09/2019	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1325	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	1,086.94	- 09/2019	-	-	0/0
1326	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	904.82	722.92	- 12/2019	-	-	0/0
1327	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.59	- -	03/2020	-	0/0
1328	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019	24(O) 0	0/0
1329	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- -	-	-	0/0
1330	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019	0(O) 0	0/0
1331	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 1,367.00	1,169.61	1,063.10	- -	04/2020	-	0/0
1332	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	159.58	03/2020 -	04/2020	1(O) -	0/0
1333	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	62.85	- -	01/2021	-	0/0
1334	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 149.90	199.90	60.39	- -	-	-	0/0
1335	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	-	0/0
1336	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB ,	03/2018	322.48 -	322.48	48.73	07/2020 -	07/2020	0(O) -	0/0
1337	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB ,	03/2018	173.24 -	173.24	10.97	06/2020 -	06/2020	0(O) -	0/0
1338	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD,PUNJAB ,	03/2018	293.10 -	293.10	10.26	08/2020 -	08/2020	0(O) -	0/0
1339	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB ,	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019	0(O) -	0/0
1340	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]PWD,PUNJAB ,	03/2018	170.57 -	170.57	46.23	11/2020 -	11/2020	0(O) -	0/0
1341	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1342	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1343	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1344	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1345	REHABILITATION AND UPGRADE TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1346	REHABILITATION AND UPGRADE TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1347	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1348	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.00	06/2018 -	-	-	0/4
1349	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	37(O) 0	0/0
1350	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	605.33	10/2017 -	-	-	0/4
1351	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	-	-	0/0
1352	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	-	-	0/0
1353	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1354	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70(O) -	0/4
1355	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1356	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	257.52	- 02/2016	10/2019	- 0	0/0
1357	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	588.00	06/2019 -	09/2019	3(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1358	FOUR LANNING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5(O) -	0/0
1359	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	09/2019	3(O) -	0/0
1360	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN ,	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	- 0	0/0
1361	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1362	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN ,	08/2016	320.30 -	320.30	206.14	01/2019 -	-	-	0/4
1363	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	1,280.27	- -	05/2020	- -	0/4
1364	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	892.00	- -	12/2019	- -	0/0
1365	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI, RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1366	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN ,	04/2017	894.00 -	894.00	690.00	04/2020 -	11/2019	-5(O) -	0/0
1367	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI, RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	364.29	10/2017 -	11/2020	37(O) -	0/0
1368	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI, RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	12/2020	- -	0/0
1369	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	267.65	- -	09/2020	- -	0/0
1370	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1371	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN ,	02/2018	716.76 -	716.76	171.45	- -	-	-	0/0
1372	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN ,	03/2018	874.25 -	874.25	80.10	- -	-	-	0/0
1373	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	121.47	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1374	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD,RAJASTHAN ,	11/2017	187.82 -	187.82	53.02	04/2018 -	-	-	1/4
1375	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD,RAJASTHAN ,	10/2014	382.81 -	382.81	333.60	01/2015 -	-	-	3/4
1376	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD,RAJASTHAN ,	01/2017	179.32 -	179.32	96.12	11/2017 -	-	-	2/4
1377	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD,RAJASTHAN ,	03/2016	155.77 -	155.77	97.42	09/2016 -	-	-	3/4
1378	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD,RAJASTHAN ,	01/2012	378.07 478.73	478.73	188.98	01/2014 -	-	-	1/4
1379	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD,RAJASTHAN ,	10/2012	511.21 -	511.21	814.79	10/2013 -	-	-	3/4
1380	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD,RAJASTHAN ,	03/2009	501.00 671.54	671.54	659.98	09/2013 -	-	-	3/4
1381	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD,RAJASTHAN ,	11/2017	163.95 -	163.95	58.70	04/2018 -	-	-	3/4
1382	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD,RAJASTHAN ,	02/2018	370.30 -	370.30	192.00	06/2018 -	-	-	1/4
1383	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD,RAJASTHAN ,	02/2018	341.79 -	341.79	97.97	05/2018 -	-	-	1/4
1384	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD,RAJASTHAN ,	12/2015	621.43 -	621.43	426.36	10/2016 -	-	-	3/4
1385	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD,RAJASTHAN ,	01/2017	163.54 -	163.54	92.88	07/2017 -	-	-	2/4
1386	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MORTH,RAJASTHAN ,	03/2019	178.13 -	178.13	.00	- -	-	-	0/0
1387	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76(O) -	0/0
1388	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 203.26	166.27	141.31	08/2013 -	-	-	0/0
1389	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82(O) 0	0/0
1390	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	97.85	10/2017 -	-	-	2/4

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1391	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	97.85	11/2017 -	-	-	2/4
1392	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	77.39	- -	-	-	0/0
1393	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	34.86	11/2017 -	-	-	1/4
1394	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1395	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78(O) -	0/0
1396	DEVELOPMENT OF ADIUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86(O) 0	0/0
1397	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	-	-	0/0
1398	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	-	-	0/0
1399	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHT 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1400	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1401	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1402	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1403	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	974.13	11/2017 -	07/2019	-	0/0
1404	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	08/2019	20(O) -	0/0
1405	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1406	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	936.30	07/2008 -	-	-	0/0
1407	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	343.21	08/2018 -	03/2020	19(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1408	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	340.73	07/2018 -	05/2020	22(O) -	0/0
1409	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	64.68	03/2020 -	03/2020	0(O) -	0/0
1410	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	340.73	07/2016 -	05/2020	46(O) -	0/0
1411	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	122.89	08/2017 -	09/2020	37(O) -	0/0
1412	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	105.81	09/2017 -	11/2019	26(O) -	0/0
1413	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	159.23	09/2017 -	08/2020	35(O) -	0/0
1414	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	100.76	- -	03/2020	- -	0/0
1415	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	- -	02/2021	- -	0/0
1416	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	36.14	- -	11/2020	- -	0/0
1417	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	59.22	- -	11/2020	- -	0/0
1418	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	- -	0/0
1419	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	.00	- -	04/2021	- -	0/0
1420	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	-	- -	0/0
1421	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 1,544.00	1,544.00	1,446.45	09/2016 -	09/2019	36(O) -	0/0
1422	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	- -	1/4
1423	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	100.10	01/2017 -	09/2019	32(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1424	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA ,	12/2015	1,423.96 897.03	897.03	705.85	11/2018 07/2019	12/2019	13(O) 1	0/0
1425	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1426	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI, TELANGANA ,	03/2018	802.65 -	802.65	79.72	- -	-	-	0/0
1427	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA ,	03/2018	950.63 -	950.63	61.95	- -	-	-	0/0
1428	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA ,	03/2018	857.62 -	857.62	.03	- -	-	-	0/0
1429	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1430	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD, TELANGANA ,	10/2016	298.32 -	298.32	77.44	02/2019 -	12/2019	10(O) -	0/0
1431	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD, TELANGANA ,	10/2016	248.83 -	248.83	88.85	03/2019 -	12/2019	9(O) -	0/0
1432	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD, TELANGANA ,	01/2017	244.54 -	244.54	137.10	05/2019 09/2019	09/2019	4(O) 0	0/0
1433	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH - [N24000983]PWD, TELANGANA ,	01/2017	196.52 -	196.52	98.61	10/2019 -	10/2019	0(O) -	0/0
1434	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI - [N24000984]PWD, TELANGANA ,	01/2017	283.00 -	283.00	151.88	12/2019 -	12/2019	0(O) -	0/0
1435	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT - [N24000985]PWD, TELANGANA ,	01/2017	359.27 -	359.27	227.88	05/2019 -	08/2019	3(O) -	0/0
1436	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION - [N24000986]PWD, TELANGANA ,	01/2017	300.00 -	300.00	99.46	05/2019 -	12/2019	7(O) -	0/0
1437	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH- SAMSHABAD SECTION) OF HYDERABAD- SAMSHABAD SECTION OF NH - [N24000987]PWD, TELANGANA ,	01/2018	283.15 -	283.15	42.22	05/2020 -	05/2020	0(O) -	0/0
1438	WIDENING AND STRENGTHENING OF EXISTING 2- LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD, TELANGANA ,	01/2018	230.03 -	230.03	127.98	12/2019 -	12/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1439	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD,TELANGANA ,	02/2018	206.13 -	206.13	116.63	06/2020 -	06/2020	0(O) -	0/0
1440	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD,TELANGANA ,	02/2018	294.13 -	294.13	30.35	11/2019 -	11/2019	0(O) -	0/0
1441	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD,TELANGANA ,	02/2018	220.28 -	220.28	22.17	11/2019 -	11/2019	0(O) -	0/0
1442	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]PWD,TELANGANA ,	02/2018	426.52 -	426.52	200.79	04/2020 -	04/2020	0(O) -	0/0
1443	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD,TELANGANA ,	03/2018	322.81 -	322.81	1.66	09/2020 -	09/2020	0(O) -	0/0
1444	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD,TELANGANA ,	03/2018	626.76 -	626.76	80.66	07/2020 -	07/2020	0(O) -	0/0
1445	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD,TELANGANA ,	01/2017	605.08 -	605.08	260.32	10/2019 -	10/2019	0(O) -	0/0
1446	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA ,	03/2018	192.67 -	192.67	107.35	07/2019 -	12/2019	5(O) -	0/0
1447	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA ,	01/2019	193.19 -	193.19	.00	- -	-	-	0/0
1448	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	297.12	03/2018 12/2019	-	-	3/4
1449	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]PWD,TRIPURA ,	10/2016	171.90 -	171.90	14.77	08/2020 -	08/2020	0(O) -	0/0
1450	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1451	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1452	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	459.07	01/2014 -	-	-	0/0
1453	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-	-	0/0
1454	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1455	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 275.00	261.09	240.96	05/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1456	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	433.68	01/2016 -	-	-	0/0
1457	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	232.93	09/2016 03/2018	03/2018	-	0/0
1458	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	207.94	01/2016 -	-	-	0/0
1459	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	633.24	01/2016 -	-	-	0/0
1460	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019	30(O) -	0/0
1461	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2017 -	-	-	0/0
1462	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	902.00	03/2018 -	-	-	0/0
1463	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1464	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1465	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24(O) -	0/0
1466	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24(O) -	0/0
1467	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21(O) -	0/0
1468	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22(O) -	0/0
1469	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	89.14	08/2015 -	09/2019	49(O) -	0/0
1470	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	623.53	- -	-	-	0/0
1471	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 1,240.03	1,057.60	1,000.89	06/2019 12/2016	09/2019	3(O) 0	0/0
1472	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	632.21	04/2019 -	-	-	0/0
1473	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	92.37	- -	-	-	0/0
1474	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1475	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 10/2019	10/2019	6(O) 0	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1476	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	532.53	04/2019 07/2020	07/2020	15(O) 0	0/0
1477	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	- -	0/0
1478	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	07/2020	- -	0/0
1479	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	04/2020	- -	0/0
1480	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 11/2019	11/2019	7(O) 0	0/0
1481	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	09/2019	- -	0/0
1482	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1483	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8(O) -	0/4
1484	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5(O) -	0/4
1485	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 2,602.09	1,989.00	852.57	03/2020 11/2017	05/2020	2(O) 0	0/0
1486	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020	0(O) -	0/0
1487	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 3,207.63	1,087.00	473.11	- 02/2018	03/2020	- -2	0/0
1488	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1489	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1490	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 929.89	450.77	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1491	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1492	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1493	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0
1494	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 1,684.93	1,117.84	.00	- 12/2018	12/2021	- 0	0/0
1495	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0
1496	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	- -	-	-	0/0
1497	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	115.83	- -	-	-	0/0
1498	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	194.57	- -	-	-	0/0
1499	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 1,444.25	972.77	.00	- 02/2019	02/2022	- 0	0/0
1500	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	.00	- -	-	-	0/0
1501	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH ,	03/2016	208.50 -	208.50	123.66	11/2019 -	11/2019	0(O) -	0/0
1502	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	86.07	03/2020 -	03/2020	0(O) -	0/0
1503	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	157.79	09/2019 -	09/2019	0(O) -	0/0
1504	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	194.01	01/2020 -	01/2020	0(O) -	0/0
1505	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	132.45	10/2018 -	09/2019	11(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1506	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.29	464.05	03/2017 -	09/2019	30(O) -	0/0
1507	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	89.14	08/2015 -	09/2019	49(O) -	0/0
1508	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH ,	03/2016	249.50 -	249.50	150.70	05/2019 -	11/2019	6(O) -	0/0
1509	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD,UTTAR PRADESH ,	10/2016	239.63 -	239.63	211.57	02/2019 -	07/2019	-	0/0
1510	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH ,	03/2016	599.34 -	599.34	435.14	01/2020 -	01/2020	0(O) -	0/0
1511	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	715.78	01/2019 -	-	-	0/0
1512	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]PWD,UTTAR PRADESH ,	03/2016	388.83 -	388.83	280.17	12/2019 -	12/2019	0(O) -	0/0
1513	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]PWD,UTTAR PRADESH ,	10/2016	218.90 -	218.90	23.37	03/2020 -	03/2020	0(O) -	0/0
1514	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]PWD,UTTAR PRADESH ,	07/2016	208.88 -	208.88	36.25	10/2019 -	10/2019	0(O) -	0/0
1515	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]PWD,UTTAR PRADESH ,	12/2016	209.10 -	209.10	85.74	10/2019 -	10/2019	0(O) -	0/0
1516	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]PWD,UTTAR PRADESH ,	03/2018	263.89 -	263.89	119.70	04/2020 -	04/2020	0(O) -	0/0
1517	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]PWD,UTTAR PRADESH ,	03/2018	185.18 -	185.18	2.86	02/2020 -	02/2020	0(O) -	0/0
1518	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (JAN - [N24001208]PWD,UTTAR PRADESH ,	03/2018	288.30 -	288.30	.34	08/2020 -	08/2020	0(O) -	0/0
1519	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]PWD,UTTAR PRADESH ,	03/2016	296.50 -	296.50	.51	09/2020 -	09/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1520	REHABILITATION AND UPGADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]PWD,UTTAR PRADESH ,	03/2018	306.59 -	306.59	.00	-	-	-	0/0
1521	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]PWD,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	-	-	-	0/0
1522	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76(O) -	0/0
1523	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	278.01	- 10/2020	10/2020	- 12	0/0
1524	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	-	02/2020	-	0/0
1525	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19(O) 0	0/0
1526	CONSTRUCTION AND UPGADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	19.22	05/2018 -	-	-	1/4
1527	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	89.19	06/2018 -	-	-	1/4
1528	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	87.71	05/2018 -	-	-	1/4
1529	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019	0(O) -	0/0
1530	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019	0(O) -	0/0
1531	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019	0(O) -	0/0
1532	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6(O) -	0/0
1533	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019	0(O) -	0/0
1534	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1535	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019	0(O) -	0/0
1536	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	02/2020	0(O) -	0/0
1537	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	- -	-	-	0/0
1538	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1539	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1540	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	94.57	07/2018 -	-	-	0/5
1541	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24(O) -	0/0
1542	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76(O) -	0/0
1543	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82(O) -	0/0
1544	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63(O) -	0/0
1545	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71(O) -	0/0
1546	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1547	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
1548	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18(O) -	0/0
1549	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	3,059.39	- -	06/2019	-	0/0
1550	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13(O) -	0/0
1551	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13(O) -	0/0
1552	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	31.67	06/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1553	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0
1554	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL ,	08/2014	600.87 720.97	720.97	644.40	11/2017 05/2019	05/2019	-	0/0
1555	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]PWD, WEST BENGAL ,	08/2014	823.20 937.76	937.76	722.56	11/2017 06/2019	06/2019	-	0/0
1556	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL ,	03/2016	271.17 291.20	291.20	79.43	11/2018 11/2019	11/2019	12(O) 0	0/0
1557	REHABILITATION AND UPGRADE TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD, WEST BENGAL ,	01/2017	396.86 396.86	396.86	179.31	09/2019 -	09/2019	0(O) -	0/0
1558	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD, WEST BENGAL ,	03/2017	202.69 202.69	202.69	93.93	11/2019 -	11/2019	0(O) -	0/0
1559	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD, WEST BENGAL ,	02/2018	426.18 426.18	426.18	218.00	09/2020 -	09/2020	0(O) -	0/0
1560	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD, WEST BENGAL ,	02/2018	218.70 218.70	218.70	25.02	11/2020 -	11/2020	0(O) -	0/0
1561	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO) - [N24000883]PWD, WEST BENGAL ,	03/2018	254.30 254.30	254.30	20.26	10/2020 -	10/2020	0(O) -	0/0
1562	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) - [N24000885]PWD, WEST BENGAL ,	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24(O) -	0/0
1563	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24(O) -	0/0
1564	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD, WEST BENGAL ,	04/2014	279.70 398.52	398.52	314.63	08/2017 07/2019	07/2019	-	0/0
	Total		5,09,411.08 -	5,30,872.20	2,55,947.17				225/947
	<u>SHIPPING AND PORTS</u>								
1565	JAL MARG VIKAS PROJECT - [N25000072]JWAI, MULTI STATE ,	01/2018	4,200.00 5,369.18	5,369.18	1,394.52	03/2023 -	03/2023	0(O) -	0/0
	Total		4,200.00 -	5,369.18	1,394.52				0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	TELECOMMUNICATIONS								
1566	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	367.03	06/2017 -	-	-	0/0
1567	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 -	240.10	117.63	10/2018 09/2019	09/2019	11(O) 0	0/0
1568	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58(O) -	0/0
1569	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,095.23 -	27,333.53	9,135.56				0/70
	URBAN DEVELOPMENT								
1570	CONSTRUCTION OF 123 BLOCKS IN TELEANGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCIL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1571	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	169.16	163.98	03/2017 -	-	-	4/5
1572	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1573	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5(O) -	0/7
1574	IRRIGATION WORK OF BAGMATI - [N12000108]HSCIL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1575	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	85.74	06/2017 -	10/2020	40(O) -	0/0
1576	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,763.00	03/2016 -	-	-	0/0
1577	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	330.83	10/2019 -	03/2021	17(O) -	0/7
1578	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	703.90	12/2015 -	-	-	0/0
1579	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019	0(O) -	3/7
1580	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	42.30	04/2019 -	06/2020	14(O) -	0/2
1581	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1582	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	53.20	05/2020 -	05/2020	0(O) -	0/0
1583	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	146.45	06/2019 -	-	-	0/0
1584	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	14.20	- -	12/2020	-	0/0
1585	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	- 0	0/0
1586	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	33.39	04/2018 -	-	-	0/0
1587	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019	0(O) -	0/0
1588	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	.00	- -	-	-	0/0
1589	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
1590	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	10,773.00	5,854.77	12/2018 -	07/2020	19(O) -	0/0
1591	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59(O) -	2/8
1592	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1593	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1594	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0
1595	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1596	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	80.08	03/2016 -	09/2020	54(O) -	1/6
1597	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1598	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1599	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1600	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	65.84	02/2020 -	09/2020	7(O) -	0/0

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1601	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	89.66	10/2012 -	03/2020	89(O) -	1/6
1602	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29(O) -	0/0
1603	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 -	03/2020	0(O) -	2/7
1604	BHOPAL METRO RAIL - [N28000124]MPMRL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023	0(O) -	0/0
1605	INDORE METRO RAIL - [N28000125]MPMRL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023	0(O) -	0/0
1606	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	205.00	165.47	03/2012 -	-	-	18/20
1607	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	6,108.39	03/2018 -	12/2019	21(O) -	0/0
1608	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1609	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	33.01	07/2020 09/2020	09/2020	2(O) 0	3/14
1610	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	2,727.17	11/2021 01/2022	01/2022	2(O) 0	0/0
1611	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67(O) -	0/10
1612	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0
1613	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	800.00	2.56	03/2022 -	03/2022	0(O) -	0/0
1614	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	488.28	424.11	05/2017 -	09/2019	28(O) -	8/12
1615	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	195.83	04/2019 -	02/2020	10(O) -	4/8
1616	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	65.80	05/2020 -	01/2021	8(O) -	1/5
1617	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1618	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 559.47	559.47	335.76	07/2019 12/2019	02/2020	7(O) 2	0/0
1619	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-	-	12/24

Detail of ongoing Projects Costing Rs. 150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1620	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	130.62	10/2019 -	03/2020	5(O) -	1/6
1621	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/13
1622	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	12.00	- -	11/2021	- -	0/0
1623	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	35.79	03/2020 -	05/2021	14(O) -	0/5
1624	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1625	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1626	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1627	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1628	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020	0(O) -	0/0
1629	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1630	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1631	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38(O) -	10/16
1632	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	131.07	04/2018 -	07/2019	-	5/6
	Total		1,86,663.06 -	1,93,294.88	84,672.92				75/194
	<u>WATER RESOURCES</u>								
1633	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15(O) -	0/19
1634	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	12/2019	0(O) -	0/0
	Total		10,384.61 -	55,782.44	16,450.19				0/19
	Grand Total		19,40,699.0 3	23,29,746.0 2	9,75,180.06				2789/5455


Summary of projects in the Flash Report for the month of August, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1623
Number of Projects completed/dropped/frozen in Current Month	18
	0
Number of Projects not Reported in Current Month	6
Number of Projects Added in Current Month	36
Number of Projects in Current Month	1634

Brief Analysis

Project Status with respect to Original Schedule: Out of 1634 projects, 23 projects are ahead of schedule, 372 projects are on schedule 552 projects are delayed. 512 projects do not have fixed dates of commissioning. 175 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

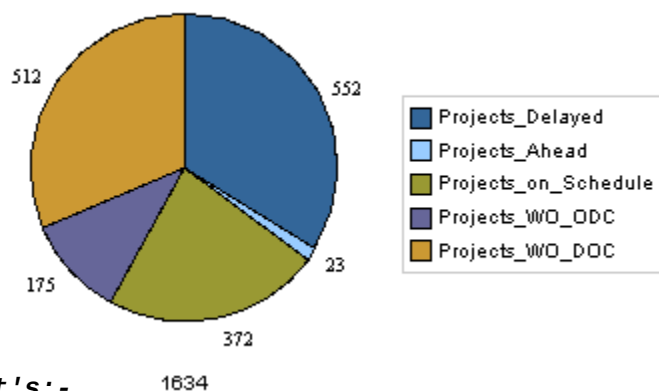


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1634 projects when sanctioned, was of the order of Rs. 1940947.58 crore but this was subsequently revised to Rs. 2329994.57 crore implying a cost overrun of 20%. The expenditure incurred on these projects till August, 2019 is Rs. 975202.61 crore, which is 41.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

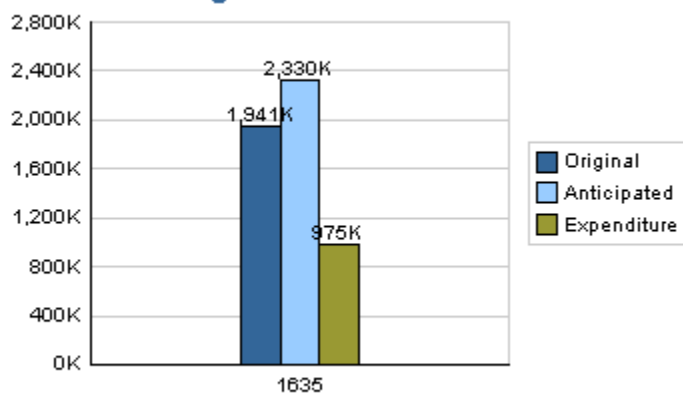

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

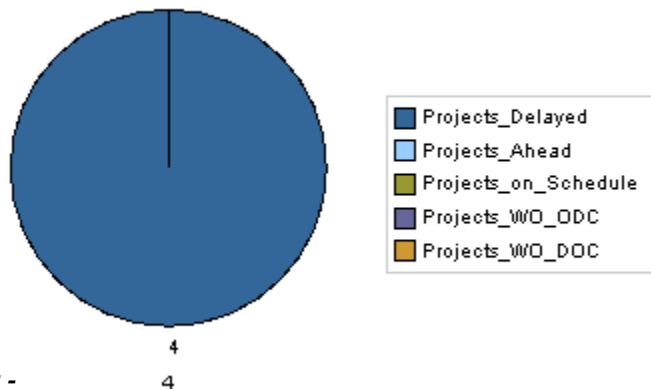

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till August, 2019 is Rs. 46384.74 crore, which is 57.7% of the anticipated cost of the projects.

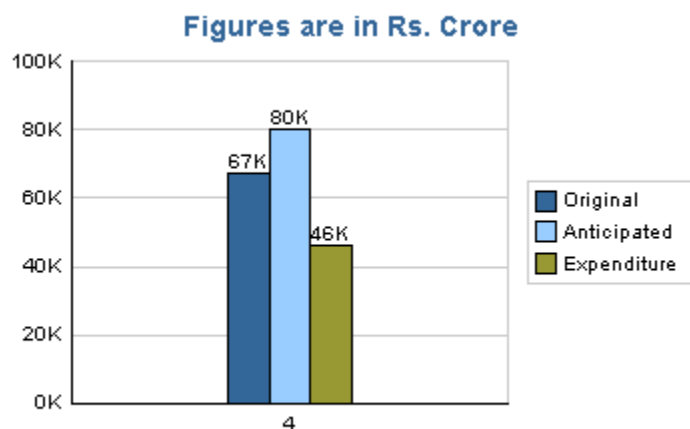

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	13
Number of Projects On Schedule	8
Number of Projects Delayed	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 8 projects are on schedule 5 projects are delayed.

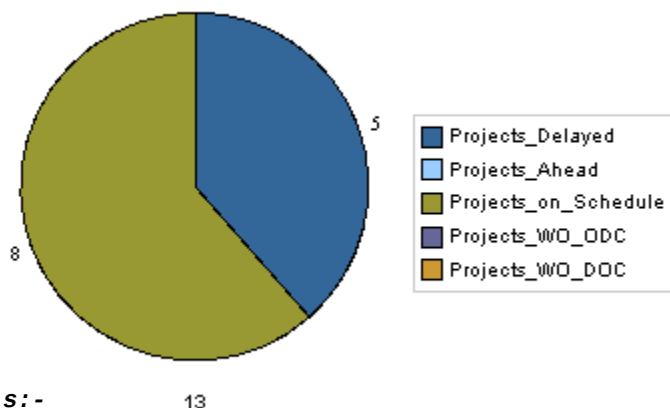


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 8607.51 crore but this was subsequently anticipated to Rs. 8734.44 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till August, 2019 is Rs. 1353.49 crore, which is 15.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

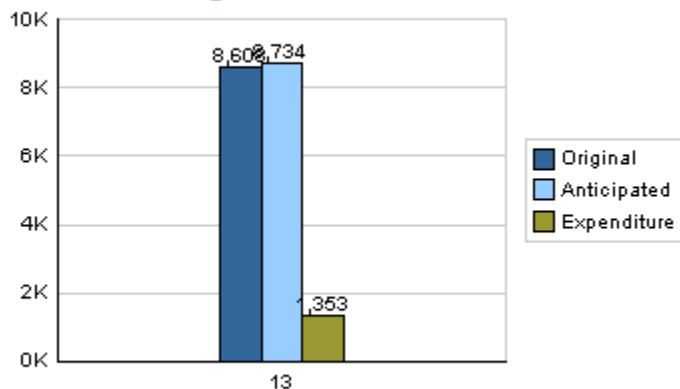

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	106
Number of Projects On Schedule	55
Number of Projects Delayed	37
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 106 projects, 1 project is ahead of schedule, 55 projects are on schedule 37 projects are delayed. 10 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

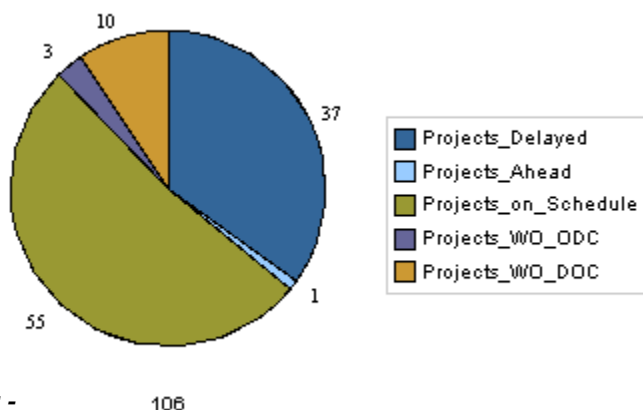


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 106 projects when sanctioned, was of the order of Rs. 102335.6 crore but this was subsequently anticipated to Rs. 102788.94 crore implying a cost overrun of .4%. The expenditure incurred on these projects till August, 2019 is Rs. 35560.62 crore, which is 34.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

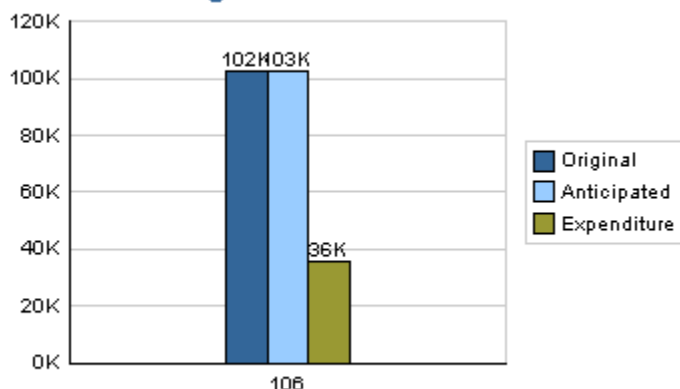

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	5
Number of Projects On Schedule	4
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project is delayed.

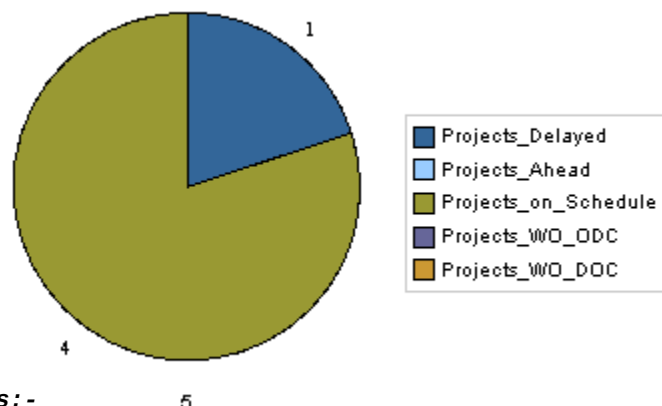


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1299.07 crore but this was subsequently anticipated to Rs. 1310.72 crore implying a cost overrun of .9%. The expenditure incurred on these projects till August, 2019 is Rs. 685.62 crore, which is 52.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

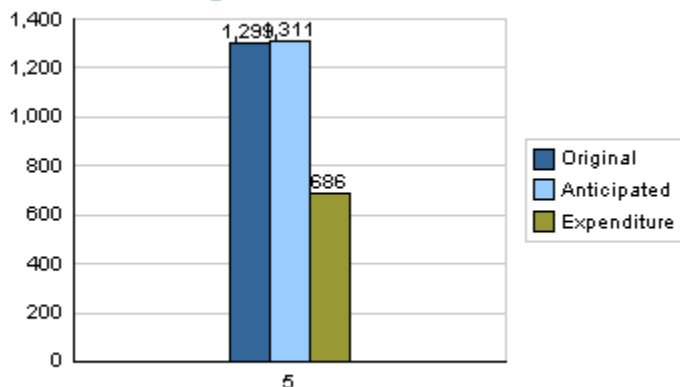

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	5
Number of Projects On Schedule	4

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project does not have fixed dates of commissioning.

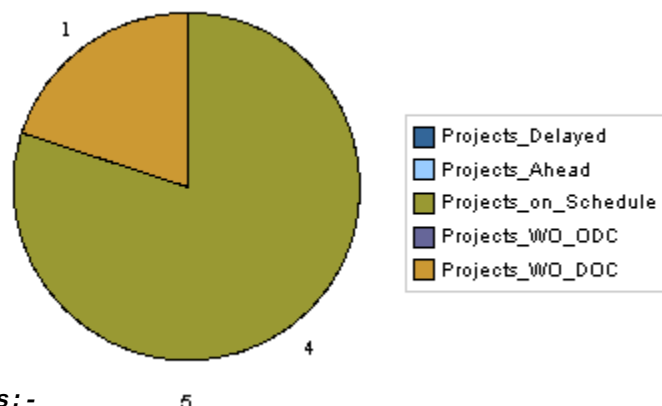


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore. The expenditure incurred on these projects till August, 2019 is Rs. 587.94 crore, which is 8.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

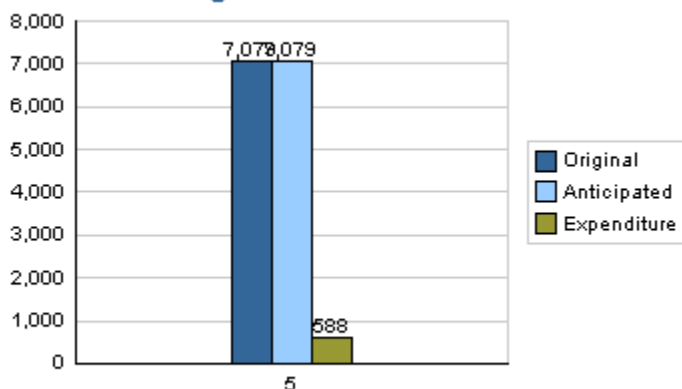

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 8 projects are delayed.

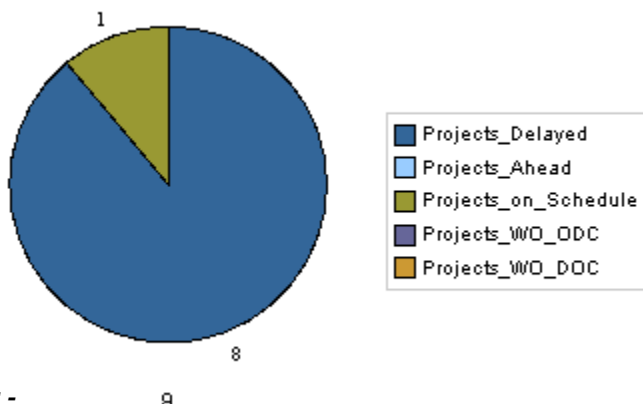


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 26228.23 crore but this was subsequently anticipated to Rs. 33485.23 crore implying a cost overrun of 27.7%. The expenditure incurred on these projects till August, 2019 is Rs. 23168.02 crore, which is 69.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

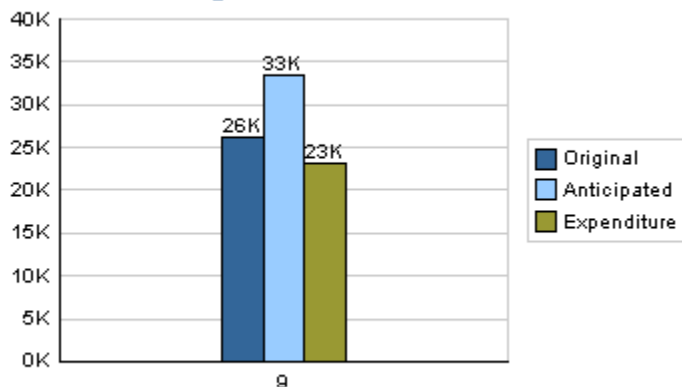

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	153
Number of Projects On Schedule	85
Number of Projects Delayed	48
Number of Projects Ahead	8
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	9

Brief Analysis

Project Status with respect to Original Schedule: Out of 152 projects, 8 projects are ahead of schedule, 85 projects are on schedule 48 projects are delayed. 9 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

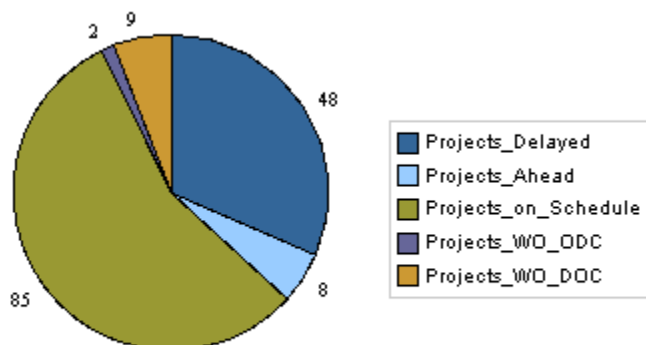


Total No Of Project's:-

152

Investment Scenario

Total original cost of implementation of 153 projects when sanctioned, was of the order of Rs. 246904.44 crore but this was subsequently anticipated to Rs. 255265.34 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till August, 2019 is Rs. 91089.32 crore, which is 35.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

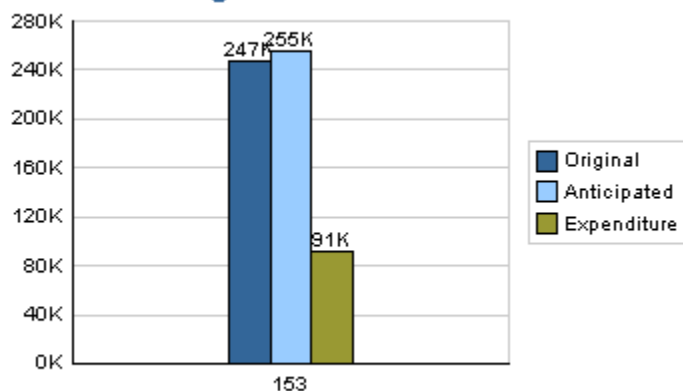

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	75
Number of Projects On Schedule	17
Number of Projects Delayed	45

Number of Projects Without Date Of Commissioning 13

Brief Analysis

Project Status with respect to Original Schedule: Out of 75 projects, 17 projects are on schedule 45 projects are delayed. 13 projects do not have fixed dates of commissioning.

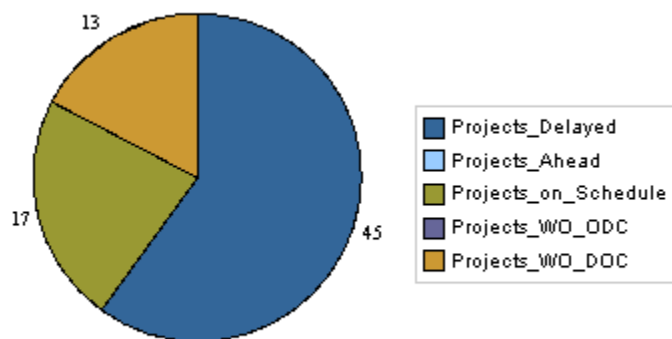


Total No Of Project's:-

75

Investment Scenario

Total original cost of implementation of 75 projects when sanctioned, was of the order of Rs. 281499.09 crore but this was subsequently anticipated to Rs. 355386.08 crore implying a cost overrun of 26.2%. The expenditure incurred on these projects till August, 2019 is Rs. 214664.65 crore, which is 60.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

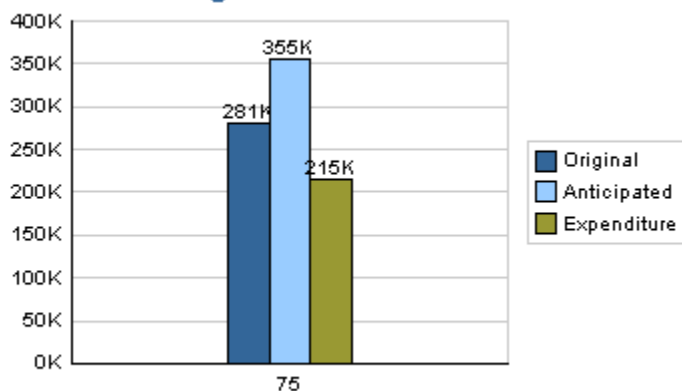

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1554 crore but this was subsequently anticipated to Rs. 1554 crore. The expenditure incurred on these projects till August, 2019 is Rs. 335.03 crore, which is 21.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

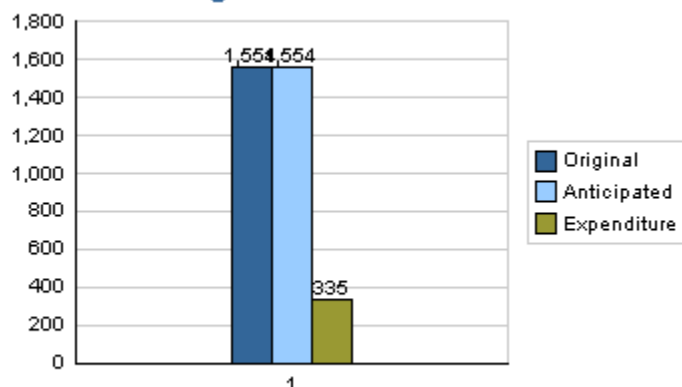

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	21
Number of Projects On Schedule	1
Number of Projects Delayed	11

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 21 projects, 1 project is on schedule 11 projects are delayed. 3 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

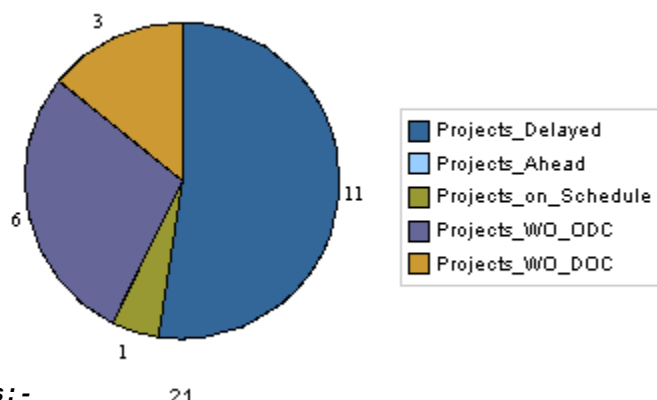


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 21 projects when sanctioned, was of the order of Rs. 9480.23 crore but this was subsequently anticipated to Rs. 9597.52 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till August, 2019 is Rs. 3377.82 crore, which is 35.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

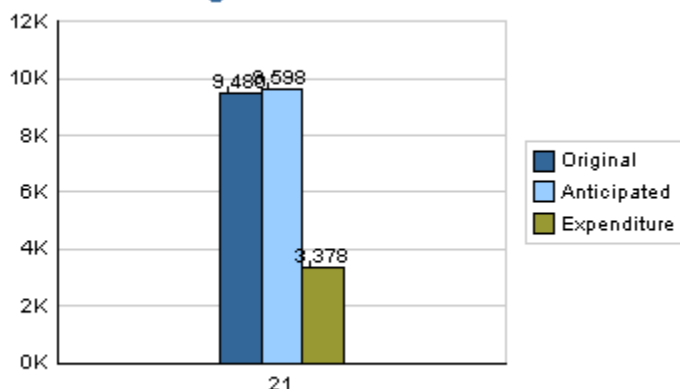

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	315
Number of Projects On Schedule	44
Number of Projects Delayed	142
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	59
Number of Projects Without Date Of Commissioning	63

Brief Analysis

Project Status with respect to Original Schedule: Out of 315 projects, 7 projects are ahead of schedule, 44 projects are on schedule 142 projects are delayed. 63 projects do not have fixed dates of commissioning. 59 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

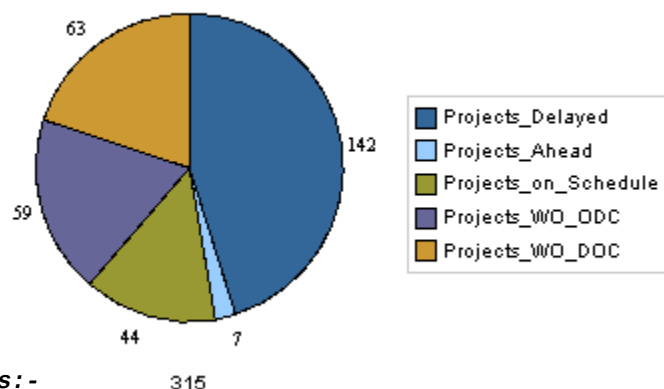


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 315 projects when sanctioned, was of the order of Rs. 461117.38 crore but this was subsequently anticipated to Rs. 660824.02 crore implying a cost overrun of 43.3%. The expenditure incurred on these projects till August, 2019 is Rs. 190365.2 crore, which is 28.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

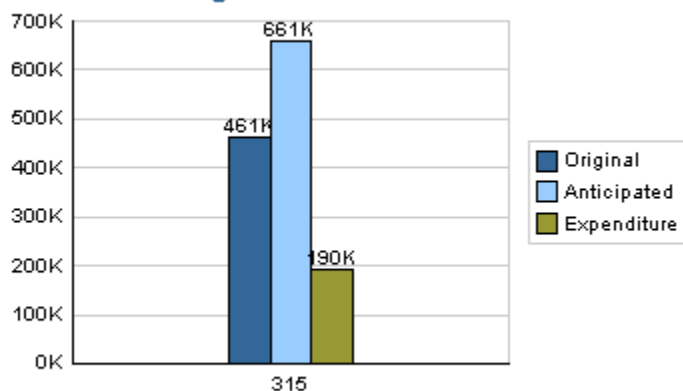

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	855
Number of Projects On Schedule	141
Number of Projects Delayed	222
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	102
Number of Projects Without Date Of Commissioning	383

Brief Analysis

Project Status with respect to Original Schedule: Out of 855 projects, 7 projects are ahead of schedule, 141 projects are on schedule 222 projects are delayed. 383 projects do not have fixed dates of commissioning. 102 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

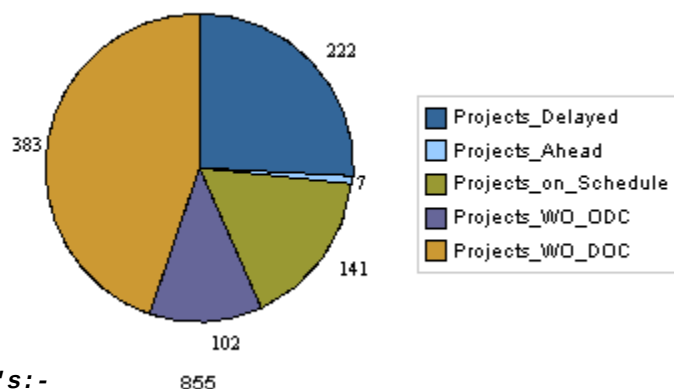

Investment Scenario

Total original cost of implementation of 855 projects when sanctioned, was of the order of Rs. 509411.08 crore but this was subsequently anticipated to Rs. 530872.2 crore implying a cost overrun of 4.2%. The expenditure incurred on these projects till August, 2019 is Rs. 255947.17 crore, which is 48.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

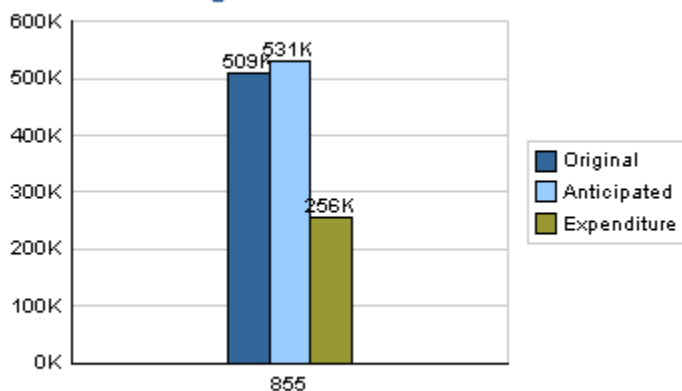

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 4200 crore but this was subsequently anticipated to Rs. 5369.18 crore implying a cost overrun of 27.8%. The expenditure incurred on these projects till August, 2019 is Rs. 1394.52 crore, which is 26% of the anticipated cost of the projects.

Figures are in Rs. Crore

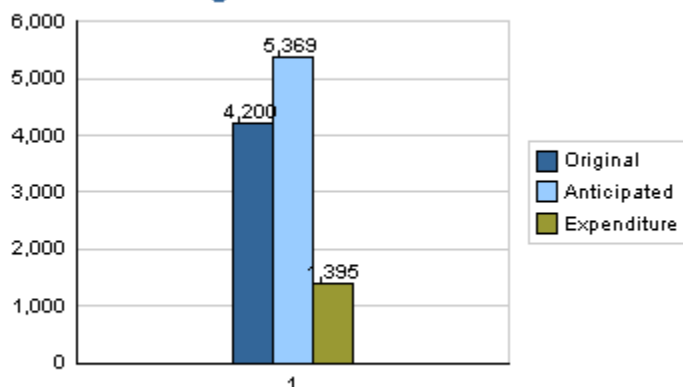

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	4
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

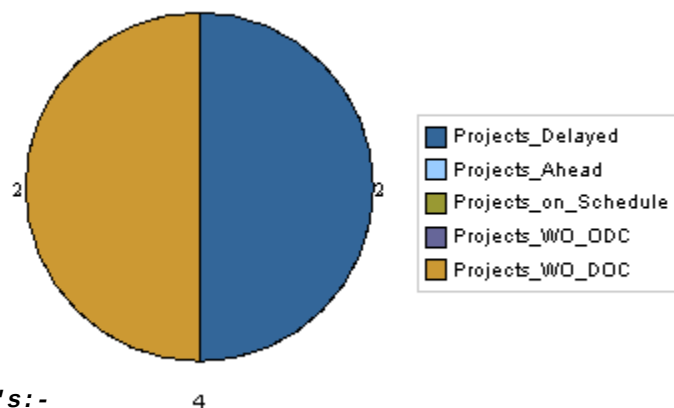


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 16095.23 crore but this was subsequently anticipated to Rs. 27333.53 crore implying a cost overrun of 69.8%. The expenditure incurred on these projects till August, 2019 is Rs. 9135.56 crore, which is 33.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

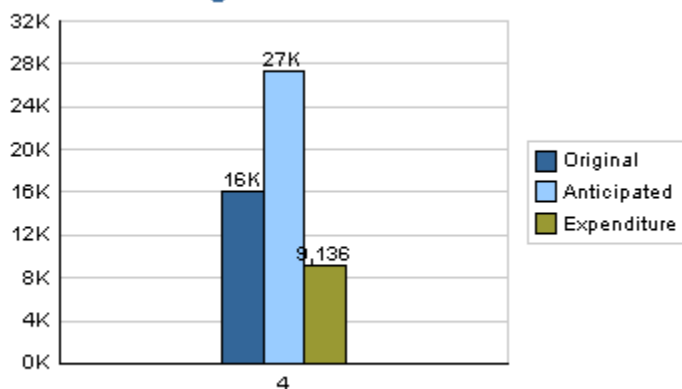

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	63
Number of Projects On Schedule	8
Number of Projects Delayed	25

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	27

Brief Analysis

Project Status with respect to Original Schedule: Out of 63 projects, 8 projects are on schedule 25 projects are delayed. 27 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

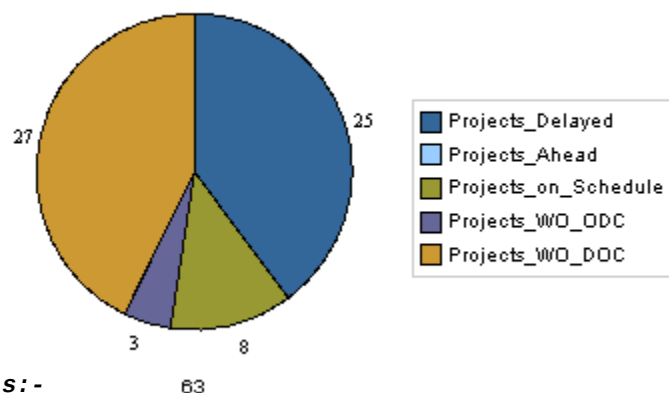


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 63 projects when sanctioned, was of the order of Rs. 186663.06 crore but this was subsequently anticipated to Rs. 193294.88 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till August, 2019 is Rs. 84672.92 crore, which is 43.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

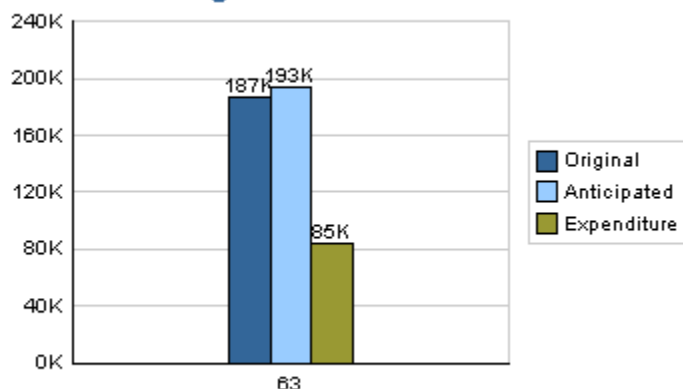

Sector wise current status of projects on the Flash Report


WATER RESOURCES

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.




Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 10384.61 crore but this was subsequently anticipated to Rs. 55782.44 crore implying a cost overrun of 437.2%. The expenditure incurred on these projects till August, 2019 is Rs. 16450.19 crore, which is 29.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

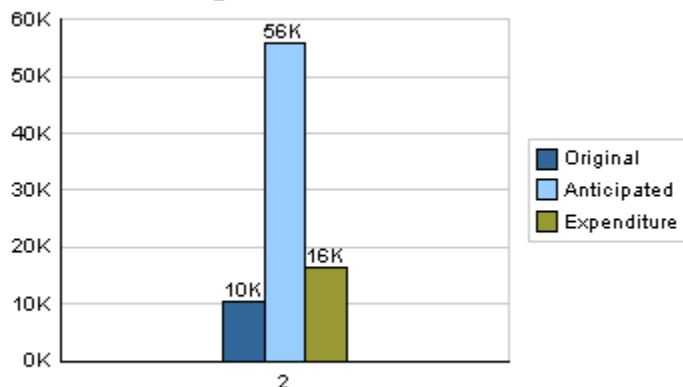

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (AUGUST 2019)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,786.01	2,893.59	445.12
2	ANDHRA PRADESH	75	1,19,490.46	1,69,432.76	45,043.69
3	ARUNACHAL PRADESH	40	21,795.08	40,754.39	21,825.98
4	ASSAM	48	26,216.03	31,003.54	14,430.84
5	BIHAR	94	90,608.62	1,27,647.16	62,115.16
6	CHHATISGARH	34	73,625.1	85,279.62	43,272.74
7	D & N HAVELI	1	6,086.08	5,842.31	4,784.4
8	DELHI	25	55,985.34	63,868.57	41,702.17
9	GOA	10	5,325.87	5,336.3	1,812.94
10	GUJARAT	56	64,665.47	71,517.57	44,901.92
11	HARYANA	40	30,880.96	33,245.93	12,134.26
12	HIMACHAL PRADESH	13	18,053.17	28,163.7	12,193.68
13	JAMMU AND KASHMIR	12	16,534.64	42,210.89	33,392.24
14	JHARKHAND	47	62,036.07	67,344.06	26,631.54
15	KARNATAKA	63	73,084.28	76,598.88	20,318.6
16	KERALA	20	36,309.6	39,755.52	13,881.1
17	MADHYA PRADESH	78	86,555.71	93,301.25	42,627.19
18	MAHARASHTRA	257	2,35,637.97	2,45,422.34	96,998.38
19	MANIPUR	5	6,002.36	14,012.39	9,369.98
20	MEGHALAYA	6	2,760.77	7,854.31	1,214.48
21	MIZORAM	13	7,757.62	11,189.69	4,763.58
22	MULTI STATE	131	3,17,640.98	4,24,187.55	1,33,552.79
23	NAGALAND	26	14,842.43	15,515.91	1,918.31
24	ODISHA	92	1,06,784.06	1,09,230.71	43,650.75
25	PUNJAB	27	13,539.35	15,038.78	9,145.61
26	RAJASTHAN	63	47,345.31	54,833.78	33,667.38
27	SIKKIM	9	3,476.73	6,368.17	1,116.97
28	TAMIL NADU	65	1,16,109.47	1,34,527.19	64,922.79
29	TELANGANA	56	39,959.69	42,435.36	13,263.48
30	TRIPURA	7	1,977.29	2,139.55	1,090.51
31	UTTAR PRADESH	118	1,44,722.96	1,49,516	65,524.42
32	UTTARAKHAND	31	35,661.33	44,552.75	14,832.07
33	WEST BENGAL	63	56,442.22	68,725.5	38,634.99
TOTAL		1,634	19,40,699.03	23,29,746.02	9,75,180.06

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021
	Total		3,492.00 -	6,840.00	5,784.74		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
2	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022
3	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	228.90	03/2012 -	03/2021
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	501.82	03/2017 -	03/2020
5	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	286.19	03/2012 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
7	JAGANNATHPOR OCP (3.00 MTY) - [N06000075]	9/2008	152.43 -	459.49	191.51	03/2015 -	03/2020
	Total		1,728.69 -	2,235.58	2,095.16		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
8	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	523.00	508.29	03/2018 -	-
	Total		505.58 -	523.00	508.29		
	<u>PETROLEUM</u>						
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>						
10	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,314.42	05/2013 12/2019	12/2019
	Total		1,854.79 -	3,376.06	2,864.27		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
11	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	9/2002	3,919.59 -	9,997.11	7,551.56	09/2009 -	12/2021
12	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	9/2003	6,285.33 -	19,496.34	10,945.40	09/2010 -	-
	<u>National Thermal Power Corporation</u>						
13	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	12,045.10	01/2018 03/2020	03/2020
14	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	1/2007	5,353.00 -	9,996.59	7,861.51	07/2012 -	09/2020
15	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,349.43	10/2017 03/2020	03/2020
	<u>Power Grid Corporation Of India Limited</u>						
16	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,804.46	08/2013 -	03/2022
17	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [N180100258]	5/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	08/2019
18	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	540.12	06/2014 -	09/2019
	<u>Thdc India Limited</u>						
19	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	5/2011	195.42 -	294.60	302.76	02/2014 -	10/2019
20	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	5,024.35	3,003.16	02/2016 -	06/2022
	Total		54,291.86 -	87,960.61	69,640.95		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
21	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	305.00	269.00	03/2019 12/2019	12/2019
22	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [N220100181]	2/1997	2,271.50 -	3,712.50	2,347.12	03/2021 -	03/2022
	<u>East Central Railways</u>						
23	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [N220100222]	3/1999	1,033.07 -	3,376.00	3,290.02	- -	03/2021
24	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [N220100240]	4/1997	324.73 -	898.53	1,038.71	03/2012 -	03/2020
25	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	425.17	397.41	- -	01/2020
26	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	845.59	- -	12/2021
	<u>East Coast Railway</u>						
27	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	225.52	03/2020 -	03/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Eastern Railways</u>						
28	DEOGHAR - SULTANGANJ (INL), ER - [N220100273]	4/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024
29	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	242.06	242.06	- -	03/2021
30	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	376.90	376.90	- -	03/2020
31	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	471.81	459.69	- -	05/2019
32	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	257.06	- -	03/2024
	<u>Metropolitan Rapid Transport Projects</u>						
33	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
34	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	<u>North Central Railway</u>						
35	ETAWAH-MAINPURI (NL),NCR - [N220100318]	4/1997	120.00 -	346.00	345.51	12/2008 -	03/2015
	<u>North East Frontier Railway</u>						
36	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	394.28	272.88	- -	03/2021
37	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	2/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-
38	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,871.00	1,082.01	- -	-
	<u>North Eastern Railway</u>						
39	HATHUA-BHATNI (N L) (NER) - [N220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
40	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	328.19	01/2019 -	01/2020
	<u>North Western Railway</u>						
41	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	303.56	262.32	11/2019 -	05/2020
42	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	410.00	351.23	02/2019 -	05/2020
	<u>Northern Railway</u>						
43	HARIDWAR-LAKSAR - [N22000289]	4/2012	219.83 -	346.63	229.48	- -	06/2020
44	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	845.58	834.59	03/2016 -	03/2021
45	NANGALDAM-TALWARA(NL),NR - [N220100188]	3/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024
	<u>Rail Vikas Nigam Ltd.</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
46	HARIDASPUR-PARADEEP(NL) - [220100285	4/1996	1,185.64 -	1,844.47	1,757.33	12/2017 -	03/2020
47	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	4/2000	133.41 207.00	395.00	386.28	03/2009 03/2009	12/2019
48	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	816.55	682.17	03/2016 -	12/2020
49	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	1,120.00	998.91	03/2019 -	03/2021
50	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	1,500.00	1,304.20	03/2020 -	03/2021
51	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	1,950.00	1,858.81	03/2020 -	03/2020
52	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020
	<u>South Central Railway</u>						
53	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
	<u>South Eastern Railway</u>						
54	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019
	<u>Southern Railway</u>						
55	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079	9/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020
56	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	4/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019
57	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	4/1999	198.68 -	556.64	303.72	- -	-
58	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	2/1996	268.87 -	950.00	927.86	03/2005 -	-
59	ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444	2/1999	257.00 257.00	257.00	268.31	03/2018 -	-
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	9/1995	303.98 -	980.00	669.21	03/2020 -	03/2021
	<u>West Central Railway</u>						
61	RAMGANJMONDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023
62	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	9/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023
	<u>Western Railway</u>						
63	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	202.35	404.70	03/2011 -	03/2017
64	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,310.23	1,363.06	03/2020 03/2021	03/2021
	Total		25,145.70 -	61,735.60	44,413.09		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
65	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	3/2015	280.16 -	290.59	280.47	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
66	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	197.77	01/2019 -	-
	<u>National Highways Authority Of India</u>						
67	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	525.00	488.37	02/2009 -	-
68	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019
69	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
70	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
71	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	325.00	469.54	05/2013 -	-
72	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	902.00	03/2018 -	-
73	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	844.08	04/2018 -	-
74	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432	9/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020
75	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	556.02	08/2016 -	-
76	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	605.33	10/2017 -	-
77	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367	4/2014	495.78 -	495.78	633.24	01/2016 -	-
78	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	351.34	433.68	01/2016 -	-
79	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-
80	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,521.24	4,659.71	12/2015 -	-
81	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020
82	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020
83	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,326.00	- -	02/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
84	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,353.61	08/2019 -	12/2020
85	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	9/2016	1,239.82 -	1,239.82	1,280.27	- -	05/2020
86	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	936.30	07/2008 -	-
87	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517	12/2015	479.20 -	479.20	708.82	05/2018 03/2018	12/2019
88	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	1,665.00	3,059.39	- -	06/2019
89	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
90	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	3,424.19	01/2018 12/2018	11/2019
91	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
92	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
93	NAGPUR - KONDHALI - [N24000472	9/2005	168.00 -	168.00	226.24	06/2006 -	-
94	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
95	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460	12/2015	611.65 -	611.65	728.24	06/2016 -	-
96	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019
97	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
98	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-
99	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	733.33	07/2014 -	06/2020
100	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	459.07	01/2014 -	-
101	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019
102	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	-
103	4-LANING OF BRAHAMPORE-FARAKA - [N24000203	2/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020
104	4-LANING OF FARAKA-RAIGANJ - [N24000202	2/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019
105	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	976.79	07/2013 -	-
106	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
108	PATNA-MUZZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	885.47	02/2013 -	-
109	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-
110	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,705.68	06/2015 -	-
111	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	2,700.67	07/2015 12/2019	09/2020
112	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-
113	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	1,509.10	3,187.21	09/2012 -	-
114	MUZZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019
115	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-
116	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,075.87	06/2014 -	-
117	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	566.60	11/2013 -	-
118	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	843.67	07/2013 -	-
119	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
120	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.73	03/2014 -	-
121	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019
122	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.53	10/2013 -	-
123	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-
124	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019
125	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020
126	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	451.15	04/2010 -	07/2019
127	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019
128	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]	2/2010	617.00 -	617.00	943.17	08/2012 -	12/2019
129	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,967.50	3,982.72	11/2011 -	03/2020
	<u>National Highways Development Project</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
130	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019
131	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020
	<u>Public Works Dept Of State</u>						
132	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019
133	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	305.61	275.06	09/2014 -	12/2019
134	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]	10/2012	511.21 -	511.21	814.79	10/2013 -	-
135	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019
136	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
137	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	8/2010	195.04 -	377.99	305.38	10/2010 -	06/2020
138	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]	11/2015	847.02 -	847.02	1,086.94	- 09/2019	-
139	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	8/2010	193.69 -	327.92	254.24	10/2010 -	12/2019
	Total		68,989.00 -	75,320.54	1,06,070.01		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
140	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	15,938.88	05/2015 07/2020	07/2020
	Total		15,525.00 -	23,140.00	15,938.88		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
141	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	488.28	424.11	05/2017 -	09/2019
142	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	169.16	163.98	03/2017 -	-
	<u>Chennai Metro Rail Ltd</u>						
143	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-
	<u>Hindustan Steelwork Construction Limited</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
144	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
145	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	175.94	178.65	12/2015 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>						
146	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019
	Total		21,246.24 -	26,692.51	23,393.25		
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
147	POLAVARAM IRRIGATION PROJECT - [N30000002]	2/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021
	Total		10,151.04 -	55,548.87	16,417.99		
	Grand Total		2,02,929.90	3,43,372.77	2,87,126.63		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021
	Total		1,186.64 -	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
2	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY [N16000260]	2/2016	554.00 -	554.00	350.36	02/2020 -	09/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,820.56	12/2020 -	08/2020
4	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	600.82	12/2020 -	02/2020
5	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	150.02	06/2020 -	03/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	110.59	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	189.41	09/2022 -	06/2021
8	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	85.86	04/2021 -	04/2020
	Total		8,274.58 -	9,275.58	3,307.62		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
9	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	674.45	03/2024 -	03/2022
	<u>East Central Railways</u>						
10	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	164.09	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
11	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	654.38	03/2022 -	03/2020
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	257.73	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
13	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	328.56	03/2022 -	12/2019

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
14	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	.19	12/2025 -	03/2025
	Total		8,829.49 -	8,788.90	2,079.40		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
15	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932	1/2017	319.28 -	319.28	103.79	08/2017 03/2020	08/2019
16	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	87.58	09/2017 03/2020	09/2019
17	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	1/2017	576.48 -	576.48	196.46	01/2018 03/2020	01/2020
18	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968	11/2016	376.25 -	376.25	189.59	08/2017 03/2020	08/2019
19	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43 -	429.43	195.88	11/2017 03/2020	11/2019
20	PARSHURAM GHAT TO ARAWALI - [N24001133	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
	<u>National Highways Authority Of India</u>						
21	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019
22	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019
23	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02	157.49	-	03/2020 -	02/2020
24	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19	254.00	248.60	03/2020 -	09/2019
25	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79	552.90	480.73	03/2020 -	09/2019
26	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32	503.10	1.15	03/2020 -	11/2019
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50	172.16	117.09	03/2020 -	09/2019
28	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	690.00	04/2020 -	11/2019
	<u>Public Works Dept Of State</u>						
29	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904	1/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019
	Total		7,921.73 -	9,001.16	5,156.23		
	Grand Total		26,212.44	27,269.46	10,660.80		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
2	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
3	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
4	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.00	09/2021 -	09/2021
5	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	0.42	11/2021 -	11/2021
6	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
7	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
	Total		5,033.68 -	5,033.82	694.69		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
10	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	163.23	03/2023 -	03/2023
11	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	187.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
12	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	315.31	03/2022 -	03/2022
14	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
15	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.13	03/2024 -	03/2024
16	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
17	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	82.01	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
18	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	440.13	03/2021 -	03/2021
19	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	83.20	03/2027 -	03/2027
20	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,549.76	03/2026 -	03/2026
21	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,113.66	03/2029 -	03/2029
	<u>Neyveli Lignite Corporation</u>						
22	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	7,203.71	11/2021 -	11/2021
23	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.88	09/2019 -	09/2019
24	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
25	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
26	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	265.78	03/2021 -	03/2021
27	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
28	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
29	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	116.09	03/2021 -	03/2021
31	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	103.99	03/2021 -	03/2021
32	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.10	03/2023 -	03/2023
33	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
34	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
35	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,881.14	03/2023 -	03/2023
36	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023
37	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	82.91	03/2020 -	03/2020
38	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	97.29	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
39	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
40	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
41	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
42	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	67.41	03/2020 -	03/2020
43	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.02	03/2023 -	03/2023
44	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,044.21	03/2023 -	03/2023
46	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.39	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
47	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
48	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	268.57	03/2025 -	03/2025
49	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
50	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020
51	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
52	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
53	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	42.94	03/2021 -	03/2021
54	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	50.56	03/2022 -	03/2022
55	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.93	03/2020 -	03/2020
56	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	20.30	03/2022 -	03/2022
57	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	126.12	03/2023 -	03/2023
58	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	200.77	03/2021 -	03/2021
59	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	235.29	03/2022 -	03/2022
60	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	182.51	03/2020 -	03/2020
61	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	146.45	03/2021 -	03/2021
62	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	154.25	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	-	03/2026 -	03/2026
	Total		75,877.66 -	76,100.20	19,864.47		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	125.27	11/2019 -	11/2019
65	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	113.95	11/2019 -	11/2019
66	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	106.43	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
67	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	175.19	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	520.84		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>National Building Construcion Corporation Ltd</u>						
68	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,351.00	137.87	09/2021 -	09/2021
	Total		1,351.00 -	1,351.00	137.87		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
69	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>INFORMATION AND BROADCASTING</u>						
	<u>National Building Construcion Corporation Ltd</u>						
70	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]	12/2016	167.70 -	167.70	-	03/2020 -	03/2020
	Total		167.70 -	167.70	.00		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
71	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	318.13	01/2020 01/2020	01/2020
72	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
73	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	0.30	04/2021 04/2021	04/2021
74	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	102.61	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	452.96		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
75	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	22.55	06/2022 -	06/2022
76	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	0.53	03/2021 -	03/2021
77	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20 -	580.20	34.84	02/2021 -	02/2021
78	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	155.28	12/2019 -	12/2019
79	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	13.47	12/2021 -	12/2021
80	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	15.17	03/2023 -	03/2023
81	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
82	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	121.12	08/2020 -	08/2020
	<u>Chennai Petroleum Corporation Limited</u>						
83	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	951.55	12/2019 -	12/2019
84	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	123.76	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
85	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	48.29	10/2022 -	10/2022
86	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1,123.85	12/2021 -	12/2021
87	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	123.35	04/2022 -	04/2022
88	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	49.97	07/2022 -	07/2022
89	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
90	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	-	02/2021 -	02/2021
91	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	43.56	10/2022 -	10/2022
92	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,019.25	12/2020 -	12/2020
93	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	65.14	10/2022 -	10/2022
94	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	173.41	12/2020 -	12/2020
95	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,229.31	12/2020 -	12/2020
96	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	28.80	07/2022 -	07/2022
97	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,396.84	12/2020 -	12/2020
98	LAYING OF VIJAI PUR-AURAIYA PIPELINE SECTION OF VIJAI PUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,271.82	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						
99	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	837.13	03/2021 -	03/2021
100	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	6.94	06/2022 -	06/2022
101	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	5,887.49	07/2020 -	07/2020
102	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021
103	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	376.97	09/2019 -	09/2019
104	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	67.92	11/2020 -	11/2020
105	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
106	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
107	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
108	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	118.06	11/2019 -	11/2019
109	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,592.90	03/2020 -	03/2020
110	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,460.00	06/2020 -	06/2020
	<u>Indian Oil Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
111	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	602.02	10/2019 -	10/2019
112	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	242.10	10/2021 -	10/2021
113	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,569.01	09/2019 -	09/2019
114	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	96.35	12/2021 -	12/2021
115	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
116	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	178.05	02/2020 -	02/2020
117	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,872.71	09/2019 -	09/2019
118	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
119	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	142.67	08/2020 -	08/2020
120	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	7.75	02/2020 -	02/2020
121	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	9.08	10/2021 -	10/2021
122	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	531.40	09/2019 -	09/2019
123	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	41.42	01/2021 -	01/2021
124	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
125	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	376.04	09/2019 -	09/2019
126	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	941.98	08/2021 -	08/2021
127	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	284.31	08/2021 -	08/2021
128	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	139.25	09/2019 -	09/2019
129	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	13.88	03/2021 -	03/2021
130	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
131	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
132	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	0.71	08/2020 -	08/2020
133	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	325.42	10/2019 -	10/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
134	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	12.28	06/2020 -	06/2020
135	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
136	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	7.82	01/2021 -	01/2021
137	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	142.71	03/2021 -	03/2021
138	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,526.40	11/2019 -	11/2019
139	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020
140	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
141	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	13.11	01/2021 -	01/2021
142	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	844.09	12/2020 -	12/2020
143	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	14.12	02/2020 -	02/2020
144	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
145	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	108.00	07/2020 -	07/2020
146	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
147	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
	<u>Oil & Natural Gas Corporation Limited</u>						
148	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	428.31	03/2022 -	03/2022
149	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	440.41	12/2019 -	12/2019
150	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	275.27	05/2021 -	05/2021
151	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	463.01	11/2019 -	11/2019
152	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	912.74	11/2019 -	11/2019
153	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	371.09	03/2026 -	03/2026
154	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	-	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
155	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	157.81	05/2020 -	05/2020
156	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]	10/2018	156.67 -	156.67	-	03/2021 -	03/2021
	<u>Oil India Limited</u>						
157	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	173.61	12/2019 -	12/2019
158	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	87.00	10/2020 -	10/2020
159	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	3.30	08/2020 -	08/2020
	Total		1,20,477.05 -	1,21,832.53	33,519.48		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
160	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
161	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019
162	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	8,449.85	01/2020 -	01/2020
163	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	1,904.30	03/2023 -	03/2023
164	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
	<u>Power Grid Corporation Of India Limited</u>						
165	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	116.76	02/2020 -	02/2020
166	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020
167	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALAR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019
168	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	52.63	12/2019 -	12/2019
169	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALAR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020
170	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020
171	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020
172	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	187.60	11/2019 -	11/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
173	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	777.63	01/2024 -	01/2024
174	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	255.15	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
175	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	511.64	09/2023 -	09/2023
176	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	306.71	09/2020 -	09/2020
	Total		83,212.44 -	83,973.74	27,358.73		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
177	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	156.29	03/2023 -	03/2023
178	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
179	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	94.83	03/2023 -	03/2023
180	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
181	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,208.28	03/2023 -	03/2023
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
182	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
183	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	390.53	03/2020 -	03/2020
	<u>East Coast Railway</u>						
184	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	3,382.95	373.22	03/2022 -	03/2022
	<u>Eastern Railways</u>						
185	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	693.80	428.83	03/2020 -	03/2020
	<u>North Central Railway</u>						
186	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
187	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021
188	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
189	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	502.44	03/2021 -	03/2021
190	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.76	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
191	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	122.05	03/2020 -	03/2020
192	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.15	03/2020 -	03/2020
193	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
194	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
195	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
196	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	25.24	01/2022 -	01/2022
197	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>Northern Railway</u>						
198	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
199	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	4,115.87	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
200	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]	2/2016	393.98 -	393.98	241.23	03/2020 -	03/2020
201	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
202	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,630.89	03/2023 -	03/2023
203	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	1,053.80	12/2020 -	12/2020
204	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	925.36	12/2023 -	12/2023
205	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	963.63	12/2021 -	12/2021
206	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.68	566.84	12/2024 -	12/2024
207	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	1,226.20	12/2021 -	12/2021
208	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	370.26	12/2026 -	12/2026
209	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	317.38	03/2021 -	03/2021
210	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) [N22000407]	3/2009	713.48 -	1,950.00	1,858.81	03/2020 -	03/2020
211	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	372.81	12/2024 -	12/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>South Central Railway</u>						
212	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	1,352.74	269.07	03/2020 -	03/2020
213	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
	<u>South East Central Railway</u>						
214	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	281.19	12/2021 12/2021	12/2021
215	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	443.56	03/2023 03/2023	03/2023
	<u>South Western Railway</u>						
216	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
217	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
	<u>Southern Railway</u>						
218	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>Western Railway</u>						
219	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	719.73	03/2022 03/2022	03/2022
220	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	374.60	03/2021 03/2021	03/2021
	Total		1,92,469.00 -	2,46,482.83	44,875.40		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
221	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
222	AHMADPUR TO PIMPLA - [N24001029]	1/2017	422.38 -	422.38	169.58	08/2019 -	08/2019
223	PUNE TO MALE VILLAGE - [N24001078]	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
224	MANGRUPHIR TO MAHAN - [N24001087]	3/2018	222.13 222.00	222.13	60.36	11/2019 -	11/2019
225	LATUR TO PANGAON - [N24001066]	3/2018	336.47 336.00	336.47	109.48	12/2019 -	12/2019
226	PARBHANI TO GANGKHED - [N24001065]	3/2018	238.19 238.00	238.19	40.85	12/2019 -	12/2019
227	JALGAON TO BHADGAON - [N24001045]	1/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019
228	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020
229	OMREGA TO AUSA - [N24001067]	3/2018	272.04 272.00	272.04	124.24	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
230	MAHAD TO RAIGAD FORT - [N24001038]	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
231	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
232	KUSUMBA TO MALEGAON - [N24001109]	3/2018	243.45 244.00	243.45	67.02	12/2019 -	12/2019
233	CHALISGAON TO NANDGAON - [N24001108]	3/2018	206.97 207.00	206.97	78.89	12/2019 -	12/2019
234	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	131.87	06/2021 -	06/2021
235	BHADGAON TO CHALISGAON - [N24001047]	1/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019
236	KOTHARI TO DHANORA - [N24001073]	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
237	NILAJPHATA TO BHANDARA - [N24001043]	1/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020
238	KARWANDI TO RAJURI - [N24001058]	3/2018	276.95 277.00	276.95	81.47	12/2019 -	12/2019
239	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	4.96	04/2020 -	04/2020
240	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
241	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
242	SHIVUR TO YEOLA - [N24001059]	3/2018	181.08 -	181.08	2.50	12/2019 -	12/2019
243	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	3/2018	217.14 217.00	217.14	66.77	02/2020 -	02/2020
244	PIMPLA TO MANJARUMBHA - [N24001030]	1/2017	595.77 -	595.77	132.44	08/2019 -	08/2019
245	JALGAON TO NANDURA - [N24001088]	3/2018	177.84 177.00	177.84	55.69	12/2019 -	12/2019
246	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
247	TASGAON TO SHIRDHON - [N24001054]	1/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019
248	AHMEDNAGAR TO BARAMATI - [N24001100]	1/2017	955.40 -	955.40	338.50	08/2019 -	08/2019
249	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
250	SANGOLA TO JATH - [N24001052]	1/2018	257.38 257.00	257.38	61.15	12/2019 -	12/2019
251	SALAIKHURD TO TIRORA - [N24001042]	1/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019
252	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	3/2018	336.21 336.00	336.21	64.66	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
253	MALEGAON TO RISOD - [N24001089]	2/2018	303.24 303.00	303.24	107.97	12/2019 -	12/2019
254	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020
255	KARAD TO VITA - [N24001049]	1/2018	344.85 245.00	344.85	68.04	12/2019 -	12/2019
256	DEULGAON SAKARSHA TO MEHKAR - [N24001076]	3/2018	219.91 -	219.91	106.46	12/2019 -	12/2019
257	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
258	KUNDRAL TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	121.75	12/2019 -	12/2019
259	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	500.61	11/2019 -	11/2019
260	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	70.50	12/2019 -	12/2019
261	PALPHATA TO PHULAMBARI - [N24001060]	3/2018	227.19 227.00	227.19	60.23	12/2019 -	12/2019
262	WARDHA TO HINGAGHAT - [N24001098]	1/2018	216.90 217.00	216.90	45.00	12/2019 -	12/2019
263	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
264	CHIKALI TO DHAD - [N24001061]	3/2018	189.46 189.00	189.46	21.54	12/2019 -	12/2019
265	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	112.97	12/2019 -	12/2019
266	KARASWADA TO BAMBOLIM - [N24001005]	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019
267	WASHIM TO DASTAPUR - [N24001068]	3/2018	165.51 -	165.51	35.45	12/2019 -	12/2019
268	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
269	CHIKLI TO TAKARKHED - [N24001083]	3/2018	393.10 393.00	393.10	125.97	12/2019 -	12/2019
270	VITA TO NAGAJ - [N24001050]	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019
271	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
272	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	146.29	04/2020 -	04/2020
273	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	33.02	08/2020 -	08/2020
274	NANDED TO JALKOT - [N24001069]	12/2017	456.93 457.00	456.93	54.50	09/2019 -	09/2019
275	ARNI TO NAIGAINBANDI - [N24001093]	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019
276	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	83.40	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
277	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
278	SHAHPUR PATGAON SECTION I - [N24001027	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
279	SELDOH TO PANVAR - [N24001097	7/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020
280	PATRADEVI TO KARASWADA 4L - [N24001004	3/2017	634.32 -	634.32	102.33	05/2020 -	05/2020
281	NASRATPUR TO BARASGAON - [N24001112	7/2016	406.54 407.00	406.54	142.00	09/2019 -	09/2019
282	JAHIRABAD TO LATUR - [N24001040	1/2017	461.96 -	461.96	151.43	11/2019 -	11/2019
283	MANSAR TO SALAIKHURD - [N24001035	1/2018	418.36 -	418.36	116.13	12/2019 -	12/2019
284	NALDURG TO AKKALKOT - [N24001051	2/2018	274.50 275.00	274.50	61.39	12/2019 -	12/2019
285	KALMATH TO ZARAP - [N24001137	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
286	WADIGODRI TO DHANGRIPIMPRI - [N24001063	3/2018	194.23 194.00	194.23	68.23	02/2020 -	02/2020
287	MANJUSUMBA TO CHUMBALI - [N24001031	1/2017	228.54 -	228.54	99.30	08/2019 -	08/2019
288	PAHUR TO BODHWAD - [N24001084	1/2017	244.93 -	244.93	40.23	05/2020 -	05/2020
289	HIMAYATNAGAR TO PHULSAWANGI - [N24001081	3/2018	294.87 295.00	294.87	12.30	12/2019 -	12/2019
290	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
291	PATGAON KHOPOLI SECTION I - [N24001028	1/2018	170.00 -	170.00	39.57	12/2019 -	12/2019
292	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
293	KHAMGAON TO DEULGAON SAKARSHA - [N24001074	3/2018	249.29 -	249.29	72.20	12/2019 -	12/2019
294	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
295	JALKOT TO TOGRI - [N24001071	7/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020
296	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
297	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	-	09/2019 -	09/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
298	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
299	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
300	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
301	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
302	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
303	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
304	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
305	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
306	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020
307	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	64.68	03/2020 -	03/2020
308	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
309	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	657.08	04/2020 -	04/2020
310	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	231.96	08/2019 -	08/2019
311	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	2,525.80	1,449.00	09/2019 03/2020	09/2019
	<u>National Highways Development Project</u>						
312	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	957.54 -	957.54	467.50	02/2020 -	02/2020
313	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	248.66	01/2020 -	01/2020
	<u>Public Works Dept Of State</u>						
314	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
315	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884	3/2018	191.21 -	191.21	72.02	11/2019 -	11/2019
316	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
317	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879	3/2017	202.69 -	202.69	93.93	11/2019 -	11/2019
318	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
319	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983	1/2017	196.52 -	196.52	98.61	10/2019 -	10/2019
320	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	116.63	06/2020 -	06/2020
321	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207	3/2018	185.18 -	185.18	2.86	02/2020 -	02/2020
322	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020
323	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	127.98	12/2019 -	12/2019
324	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910	3/2018	170.57 -	170.57	46.23	11/2020 -	11/2020
325	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	157.79	09/2019 -	09/2019
326	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205	12/2016	209.10 -	209.10	85.74	10/2019 -	10/2019
327	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
328	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204	7/2016	208.88 -	208.88	36.25	10/2019 -	10/2019
329	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020
330	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996	1/2017	605.08 -	605.08	260.32	10/2019 -	10/2019
331	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942	3/2016	208.50 -	208.50	123.66	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
332	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	20.26	10/2020 -	10/2020
333	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	86.07	03/2020 -	03/2020
334	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	194.01	01/2020 -	01/2020
335	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
336	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880	2/2018	426.18 -	426.18	218.00	09/2020 -	09/2020
337	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
338	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	151.88	12/2019 -	12/2019
339	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	0.48	06/2021 -	06/2021
340	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203	10/2016	218.90 -	218.90	23.37	03/2020 -	03/2020
341	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	74.49	11/2020 -	11/2020
342	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	336.25	62.64	09/2019 -	09/2019
343	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
344	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN - [N24001208	3/2018	288.30 -	288.30	0.34	08/2020 -	08/2020
345	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	200.79	04/2020 -	04/2020
346	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	80.47	06/2020 -	06/2020
347	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020
348	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	22.17	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
349	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882	2/2018	218.70 -	218.70	25.02	11/2020 -	11/2020
350	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH - - [N24001180	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
351	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	30.35	11/2019 -	11/2019
352	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019
353	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
354	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
355	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	435.14	01/2020 -	01/2020
356	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206	3/2018	263.89 -	263.89	119.70	04/2020 -	04/2020
357	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	0.50	09/2021 -	09/2021
358	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876	1/2017	396.86 -	396.86	179.31	09/2019 -	09/2019
359	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209	3/2016	296.50 -	296.50	0.51	09/2020 -	09/2020
360	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177	10/2016	171.90 -	171.90	14.77	08/2020 -	08/2020
361	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202	3/2016	388.83 -	388.83	280.17	12/2019 -	12/2019
	Total		56,200.29 -	58,001.10	16,752.37		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
362	JAL MARG VIKAS PROJECT - [N25000072	1/2018	4,200.00 -	5,369.18	1,394.52	03/2023 -	03/2023
	Total		4,200.00 -	5,369.18	1,394.52		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
363	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	10.81	09/2020 -	09/2020
	Total		263.36 -	263.36	10.81		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
364	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
365	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	53.20	05/2020 -	05/2020
366	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
367	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019
368	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BHERHAMPUR - [N28000126]	1/2019	790.79 -	800.00	2.56	03/2022 -	03/2022
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
369	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023
370	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023
	<u>National Building Construcion Corporation Ltd</u>						
371	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	Total		20,329.46 -	20,513.90	3,447.17		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
372	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Total		233.57 -	233.57	32.20		
	Grand Total		5,69,382.49	6,28,890.21	1,49,396.54		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63
	Total		27,271.00 -	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 -	860.00	03/2021 -	03/2021	.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
7	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
10	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
11	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42
12	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093 <u>South-Eastern Coal Fields Limited</u>	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
14	JAGANNATHPOR OCP(3.00MTY) - [N06000075 <u>Western Coal Fields Limited</u>	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
15	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
16	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
17	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		25,725.94 -	28,037.55			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
18	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
19	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
20	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
21	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
22	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	10/2018 -	12/2019	58.15
23	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33
24	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314 <u>Gas Authority Of India Limited</u>	12/2015	1,112.00 -	1,507.24	06/2019 -	02/2022	35.54
25	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
26	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
27	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	08/2019	133.50
28	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
29	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	09/2015	4,199.00 -	5,060.00	03/2020 -	03/2020	20.50
	<u>Indian Oil Corporation Limited</u>						
30	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
31	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	12/2020 -	12/2020	66.09
32	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	08/2020	43.82
33	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
35	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	09/2019	26.44
36	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
37	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45
38	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
39	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
40	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
41	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	03/2023 -	03/2022	10.56
42	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	265.49	05/2020 -	05/2020	6.26
43	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
44	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
45	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71
46	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17
	<u>Oil India Limited</u>						
47	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
48	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	06/2020	25.55
	Total		44,172.45 -	54,739.81			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
50	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
51	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
52	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
53	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	12/2020	96.99
54	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	09/2020	9.64
55	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55
56	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
57	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75
58	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	12/2021	33.47
59	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87
60	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16
61	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
62	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
63	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
64	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>						
65	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	12/2009 06/2016	10/2019	217.49
	<u>Power Grid Corporation Of India Limited</u>						
66	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
67	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
68	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	-	38.61
69	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
70	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	-	14.60
71	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	-	26.82
72	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	-	27.92
73	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17
74	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	-	22.93
75	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
76	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Thdc India Limited</u>						
77	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75
78	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
79	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,54,828.95 -	2,29,232.99			
	<u>RAILWAYS</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Central Railways</u>						
80	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73
81	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71
82	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44
83	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
84	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04
85	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
86	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
87	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	143.17
88	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>						
89	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
90	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	- -	03/2023	290.95
91	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	03/2012 -	03/2020	57.27
92	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	898.53	03/2012 -	03/2020	176.70
93	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	- -	03/2022	277.26
94	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
95	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	- -	02/2023	36.67
96	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]	07/2004	599.63 674.00	674.00	12/2007 -	-	12.40
97	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	- -	03/2021	253.52
98	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	03/2024	32.26
99	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15
100	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	- -	03/2021	126.22

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
101	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,609.00	- -	03/2022	589.19
102	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	03/2024	376.78
103	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) [N22000180]	04/2004	372.14 -	1,470.50	- -	03/2021	295.15
104	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2022	49.45
105	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	425.17	- -	01/2020	99.60
106	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	07/2014 -	-	64.60
107	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
108	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
109	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	726.31	- -	10/2019	301.68
110	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	12/2021	350.27
<u>East Coast Railway</u>							
111	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
112	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	03/2024	29.71
113	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
114	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07
115	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2021	52.77
116	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
117	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2022	15.45
<u>Eastern Railways</u>							
118	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22
119	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80
120	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
121	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2020	27.96
122	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	242.06	- -	03/2021	37.69
123	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
124	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01
125	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR- MINAKHAN VIA GHATAKAPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25
126	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15
127	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82
128	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	09/2021	6.48
129	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08
130	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30
131	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19
132	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
133	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	376.90	- -	03/2020	30.71
134	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	471.81	- -	05/2019	80.51
135	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75
136	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
137	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
<u>Metropolitan Rapid Transport Projects</u>							
138	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
139	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
140	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	-	48.06
141	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
142	ETAHWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	-	188.33
143	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
144	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	03/2020	1.69
	<u>North East Frontier Railway</u>						
145	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
146	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80
147	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,300.00	12/2008 -	03/2021	179.62
148	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,524.00	03/2011 -	03/2020	181.17
149	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
150	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
151	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
152	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2022	7.86
153	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95
154	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,496.67	03/2019 -	-	38.86
155	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2022	71.62
156	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11
157	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
158	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
159	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2021	63.25

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
160	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
161	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
162	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	728.00	03/2019 -	03/2020	131.85
163	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
164	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
165	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,871.00	04/2010 -	-	391.59
	<u>North Eastern Railway</u>						
166	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
167	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
168	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
169	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
170	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
171	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
172	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16
173	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91
174	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
175	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	03/2021	116.16
176	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
177	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64
178	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
179	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15	- -	-	95.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
180	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47
181	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
182	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
183	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	11/2019 -	05/2020	42.26
184	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	05/2020	69.36
	<u>Northern Railway</u>						
185	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	03/2024	25.87
186	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
187	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00	- -	03/2022	137.45
188	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	06/2020	57.68
189	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
190	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67
191	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	06/2022	1,017.96
192	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
193	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	03/2021	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
194	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
195	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	395.00	03/2009 03/2009	12/2019	196.08
196	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
197	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
200	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
201	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
202	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
203	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
204	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00	03/2020 -	03/2020	173.31
205	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
206	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22
207	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						
208	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
209	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
210	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
211	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
212	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
213	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
214	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	1,352.74	03/2020 -	03/2020	92.07
215	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
216	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
217	KONDAPALLI-KOTHAGUDEM - [N22000364]	04/2013	723.00 -	997.09	- -	-	37.91
218	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
	<u>South East Central Railway</u>						
219	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	- -	10/2019	268.37
220	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.92	04/2020 -	12/2020	243.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
221	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
222	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94
223	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95
224	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	12/2019 -	10/2019	40.65
225	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	1,973.66	03/2021 -	12/2022	.03
	<u>South Eastern Railway</u>						
226	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
227	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2019	153.41
228	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
229	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	-	54.99
230	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
231	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	12/2018 -	06/2020	38.92
232	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	03/2020 -	06/2020	35.38
233	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	03/2021 -	12/2021	15.60
234	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
235	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09
236	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
237	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
238	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
239	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
240	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
241	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
242	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
243	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
244	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
245	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80
246	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
247	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	- -	-	339.33
248	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
249	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
250	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
251	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
252	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
253	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	951.24	- -	03/2020	2.07
254	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
255	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
256	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	-	253.33
257	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
258	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35
259	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
260	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32
	<u>Western Railway</u>						
261	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
262	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	03/2011 -	-	72.42
263	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06
264	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
265	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
266	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70
	Total		1,78,466.58 -	3,89,829.96			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
267	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	- -	-	3.72
	<u>Ministry Of Road Transport And Highways</u>						
268	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	- -	-	58.68
269	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
270	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
271	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]	01/1991	675.00 -	780.77	- -	-	15.67
272	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	08/2016 -	-	14.02
273	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 -	377.64	10/2016 -	-	5.42
274	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26
275	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
276	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
277	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
278	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31
279	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	03/2017 -	09/2019	46.51
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
280	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
281	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
282	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	525.00	02/2009 -	-	87.50
283	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	04/2009 -	08/2019	70.23
284	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	408.77	11/2008 -	01/2014	143.84
285	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	08/2013	64.62
286	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
287	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	07/2009 -	-	234.27
288	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82
289	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82
290	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	03/2020	10.58
291	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	09/2019	21.90
292	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67
293	AHMEDABAD TO VADODARA SECTION - [N24000222	01/2013	2,125.24 -	2,521.24	12/2015 -	-	18.63
294	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
295	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	- -	10/2019	11.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
296	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
297	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	12/2017 -	12/2019	66.88
298	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	04/2019 -	10/2019	87.84
299	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	- -	12/2019	7.53
300	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	2,525.80	09/2019 -	09/2019	81.93
301	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
302	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	08/2019 -	12/2020	16.55
303	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	- -	03/2019	8.35
304	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25
305	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
306	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
307	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
308	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
309	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
310	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
311	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
312	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
313	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
314	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	09/2019	4.02

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
315	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
316	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
317	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
318	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
319	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	06/2020	9.67
320	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	-	-	30.09
321	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	-	11/2021	20.28
322	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	-	-	12.50
323	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	-	01/2021	37.71
324	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05
325	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	-	03/2021	22.44
326	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	-	04/2021	5.32
327	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	-	4.99
328	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	-	.12
329	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	-	07/2021	46.72
330	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	-	07/2021	.48
331	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	-	12/2020	25.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>National Highways Development Project</u>						
332	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 [N24000371]	10/2013	445.89 -	653.29	03/2017 -	09/2019	46.51
333	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 [N24000388]	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
	<u>Public Works Dept Of State</u>						
334	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
335	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
336	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
337	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 -	389.45	05/2012 -	-	88.11
338	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65
339	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	36.24
340	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	- -	-	1.75
341	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	02/2011 -	-	34.06
342	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 -	353.89	11/2015 -	-	6.21
343	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	307.47	02/2018 -	-	40.84
344	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
345	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	369.77	- -	-	15.67
346	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]	08/2014	600.87 720.97	720.97	11/2017 -	05/2019	19.99

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
347	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	11/2017 -	06/2019	13.92
348	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39
349	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51
350	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18
351	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	08/2017 -	07/2019	42.48
352	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954	01/2012	378.07 -	478.73	01/2014 -	-	26.62
353	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956	03/2009	501.00 -	671.54	09/2013 -	-	34.04
354	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46
	Total		62,106.81 -	86,941.38			
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
355	JAL MARG VIKAS PROJECT - [N25000072	01/2018	4,200.00 -	5,369.18	03/2023 -	03/2023	27.84
	Total		4,200.00 -	5,369.18			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
356	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
357	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	01/2018	231.80 -	240.10	10/2018 -	09/2019	3.58
	<u>Department Of Telecommunication</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
358	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,565.80 -	24,904.10			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
359	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85
360	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2021	64.04
361	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	06/2014	157.84 -	169.16	03/2017 -	-	7.17
362	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57
363	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
364	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	02/2020	1.85
365	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR [N28000126]	01/2019	790.79 -	800.00	03/2022 -	03/2022	1.16
	<u>Chennai Metro Rail Ltd</u>						
366	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
367	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
368	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
369	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
370	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Kochi Metro Rail Corporation Ltd</u>						
371	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
372	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		29,058.09 -	35,689.91			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
373	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		5,67,859.10	9,76,976.06			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	13,971.00	12/2015 -	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	11,234.00	12/2016 -	12/2020	48	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	15,395.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	46,384.74					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6	.02	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	0	
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	219.91 -	219.91	61.61	03/2020 -	12/2020	9	0	
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	0	
	Total		3,573.83 -	3,700.62	658.80					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
10	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	180.83	04/2014	11/2019	67	0	
11	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45	289.45	256.83	05/2014	03/2020	70	0	
	<u>Central Coal Fields Limited</u>									
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	106.41	03/2011	03/2021	120	0	
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	179.87	03/2012	03/2021	108	0	
14	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	362.47	03/2016	03/2021	60	0	
15	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	89.85	03/2014	03/2021	84	0	
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40	706.40	354.66	07/2012	03/2022	116	0	
	<u>Eastern Coal Fields Limited</u>									
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05	1,055.05	501.35	03/2018	03/2020	24	0	
	<u>Mahanadi Coal Fields Limited</u>									
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96	302.96	302.96	03/2010	03/2020	120	0	
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10	490.10	501.82	03/2017	03/2020	36	0	
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66	337.66	183.98	03/2019	03/2020	12	0	
21	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03	289.03	75.85	03/2018	03/2020	24	0	
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	228.90	03/2012	03/2021	108	0	
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.53	390.94	03/2013	03/2021	96	0	
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	539.59	03/2013	03/2022	108	0	
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	347.15	03/2010	03/2022	144	0	
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15	479.15	200.65	03/2019	03/2022	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Neyveli Lignite Corporation</u>									
27	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	709.06	449.32	06/2015 -	09/2019	51	-51.37	Due to unavailability of land, it was not possible to increase OB removal to the extent of 47.5 MM3 per annum as envisaged in Mining Plan to get 7.0 MTPA lignite exposures. Hence, it is required to keep Mine 1A expansion to 7.0 MTPA on hold till land is acquired and required OB removal capacity is attained. Land acquisition process was delayed due to lack of clarity about payment of compensation in the State land acquisition rules consequent to enactment of Acquisition, Rehabilitation and Resettlement Act, 2013 (Central Act 30 of 2013) and Land Acquisition Rehabilitation and resettlement (Amendment) Act 2015.
28	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,648.68	12/2015 -	12/2019	48	19.86	
	<u>Singareni Colliers Company Limited</u>									
29	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.58	03/2015 -	03/2020	60	0	
30	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	92.60	07/2016 -	03/2020	44	-7.91	
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	186.99	03/2016 -	03/2020	48	-3.5	
32	KAKATYAKHANI OPENCASE-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	92.09	03/2019 -	03/2020	12	11.42	
33	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	0	
34	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	115.49	03/2015 -	03/2021	72	-32.3	
35	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	8.00	03/2015 -	03/2021	72	114.6	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
36	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	5.85	
37	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	54.00	03/2019 -	03/2022	36	0	
38	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132	16.86	
39	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	286.19	03/2012 -	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
40	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	459.49	191.51	03/2015 -	03/2020	60	201.44	
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72	0	
42	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	178.86	03/2016 -	03/2020	48	0	
43	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24	0	
44	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	194.57	03/2014 -	03/2021	84	0	
	<u>Western Coal Fields Limited</u>									
45	ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA	08/2015	288.90 -	333.43	21.02	03/2023 -	03/2024	12	15.41	
46	KAMPTEE DEEP OC MINE - [N06000141]WCL, MAHARASHTRA	11/2015	277.65 -	313.34	115.50	03/2021 -	03/2024	36	12.85	
	Total		19,631.90 -	20,845.52	14,009.81					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
47	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA	10/2014	197.79 -	209.44	164.78	11/2016 -	09/2019	34	5.89	
	Total		197.79 -	209.44	164.78					
	<u>INFORMATION AND BROADCASTING</u>									
	<u>Central Public Works Department</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
48	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	0	
	Total		204.32 -	204.32	.00					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
49	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	23,140.00	15,938.88	05/2015 07/2020	07/2020	62	49.05	
	<u>Rastriya Ispat Nigam Limited</u>									
50	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,175.53	09/2018 09/2019	09/2019	12	0	no
51	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,344.76	12/2017 10/2019	10/2019	22	-12.53	No
52	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	206.91	08/2018 10/2019	10/2019	14	0	NO
	<u>Steel Authority Of India Limited (Sail)</u>									
53	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	3,008.68	04/2018 11/2019	11/2019	19	0	
54	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	944.78	12/2017 11/2019	11/2019	23	0	
55	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	432.82	10/2017 06/2020	06/2020	32	0	
56	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	104.85	06/2019 06/2020	06/2020	12	0	
	Total		25,964.87 -	33,221.87	23,157.21					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
57	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	3,588.88	08/2018 11/2019	11/2019	15	14.33	
58	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 1,097.54	1,097.54	698.76	10/2018 12/2019	12/2019	14	58.15	
59	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 3,288.96	3,288.96	1,014.00	02/2020 10/2020	10/2020	8	-73	
60	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	0	
61	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	507.00	06/2019 -	02/2022	32	35.54	
	<u>Gas Authority Of India Limited</u>									
62	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	142.00	04/2018 -	10/2019	18	-38.98	
63	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 -	286.42	1.19	08/2020 09/2020	09/2020	1	0	
64	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,515.46	12/2012 -	02/2022	110	4.61	
	<u>Hindustan Petroleum Corporation Limited</u>									
65	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	703.45	10/2014 08/2019	08/2019	58	133.5	
	<u>Indian Oil Corporation Limited</u>									
66	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	08/2019	9	0	
67	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	263.70	08/2019 -	09/2019	1	0	
68	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	306.24	01/2019 -	12/2019	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
69	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	1,562.10	07/2019 -	12/2019	5	0	
70	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	24.15	06/2020 -	08/2020	2	0	
71	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	278.51	07/2018 -	10/2020	27	0	
72	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	41.22	02/2020 -	10/2020	8	0	
73	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	85.08	02/2020 -	10/2020	8	0	
74	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	465.60	12/2018 -	02/2021	26	33.98	
75	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	50.84	04/2020 -	03/2021	11	0	
76	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	38.55	01/2021 -	04/2021	3	0	
77	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	38.29	12/2019 -	07/2021	19	0	
78	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	84.34	04/2021 -	07/2021	3	0	
79	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	30.95	10/2020 -	08/2021	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
80	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	30.75	01/2021 -	10/2021	9	0	
81	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	40.06	08/2021 -	11/2021	3	0	
82	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.07	04/2022 -	02/2023	10	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
83	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 170.70	170.70	154.03	03/2019 09/2019	09/2019	6	26.44	
84	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	726.57	12/2019 07/2020	07/2020	7	0	
85	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	68.27	03/2020 -	09/2020	6	6.88	
	<u>Oil & Natural Gas Corporation Limited</u>									
86	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 -	407.45	234.24	09/2018 09/2019	09/2019	12	-3.16	
87	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,784.40	05/2019 10/2019	10/2019	5	-4.01	
88	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	145.60	01/2014 -	11/2019	70	70.45	
89	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81	-3.5	
90	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	1,683.06	1,314.42	05/2013 12/2019	12/2019	79	95.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
91	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,908.01	03/2015 12/2019	12/2019	57	29.42	
92	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019	8	-12.72	
93	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	4,619.94	4,340.39	12/2017 03/2020	03/2020	27	0	
94	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 565.15	565.15	442.18	11/2019 03/2020	03/2020	4	3.48	
95	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020	14	0	
96	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,216.11	04/2018 05/2020	05/2020	25	1.77	
97	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	394.21	03/2019 05/2020	05/2020	14	0	
98	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1	2.17	
99	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	3,185.16	06/2020 -	08/2021	14	0	
100	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 -	4,475.92	2,770.16	05/2021 12/2021	12/2021	7	11.71	
101	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	-	12/2021 -	03/2022	3	0	
	<u>Oil India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
102	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	
103	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33	24.47	
104	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL, ASSAM	01/2018	543.91 -	682.90	8.75	02/2020 -	06/2020	4	25.55	
	Total		1,06,346.22 -	1,11,106.84	45,541.01					
	<u>POWER</u>									
	<u>National Hydro-Electric Power Corporation</u>									
105	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,551.56	09/2009 -	12/2021	147	155.05	
	<u>National Thermal Power Corporation</u>									
106	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH	12/2012	11,846.00 -	12,739.82	12,349.43	10/2017 03/2020	03/2020	29	7.55	
107	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC, MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	12,045.10	01/2018 03/2020	03/2020	26	10.55	
108	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15	0	
109	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16	0	
110	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	6,397.93	07/2019 06/2020	06/2020	11	0	
111	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	9,749.00	02/2017 06/2020	06/2020	40	24.87	
112	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC, ODISHA	02/2014	12,532.44 -	13,740.53	9,639.47	12/2018 02/2020	09/2020	21	9.64	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
113	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	9,996.59	7,861.51	07/2012 -	09/2020	98	86.75	
114	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,155.88	03/2013 12/2020	12/2020	93	96.99	
115	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	5,382.09	11/2020 06/2021	06/2021	7	0	
116	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	16,331.92	10/2011 08/2021	08/2021	118	145.16	
117	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,131.59	06/2019 09/2019	09/2021	27	5.55	
118	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	13,716.26	05/2018 12/2021	12/2021	43	33.47	
119	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	481.22	09/2019 02/2022	02/2022	29	15.23	
	<u>North East Electric Power Corporation</u>									
120	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	7,927.34	7,516.58	12/2009 10/2019	10/2019	118	217.49	
	<u>Power Grid Corporation Of India Limited</u>									
121	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	08/2019	129	22.93	
122	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 -	08/2019	40	38.61	
123	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	190.80	07/2017 -	08/2019	25	27.92	
124	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	81.97	03/2018 -	08/2019	17	0	
125	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	430.71	04/2019 -	08/2019	4	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
126	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	153.70	02/2019 -	08/2019	6	0	
127	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	639.46	540.12	06/2014 -	09/2019	63	31.17	
128	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	548.30	10/2017 -	09/2019	23	0	
129	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4	0	
130	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	266.03	01/2019 -	09/2019	8	0	
131	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	92.78	09/2018 -	09/2019	12	0	
132	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2	0	
133	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3	0	
134	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	117.15	06/2019 -	10/2019	4	0	
135	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 -	12/2019	86	5.14	
136	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	210.72	04/2016 -	12/2019	44	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
137	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	3,115.72	03/2018 -	12/2019	21	0	
138	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	405.65	05/2017 -	12/2019	31	0	
139	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12	90.82	
140	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10	0	
141	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	287.52	04/2018 -	01/2020	21	0	
142	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	0	
143	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	465.21	11/2016 -	03/2020	40	4.61	
144	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	513.85	01/2018 -	03/2020	26	0	
145	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 -	12/2020	24	34.61	
146	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	14,719.10	12,804.46	08/2013 -	03/2022	103	32.24	
	<u>Thdc India Limited</u>									
147	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	302.76	02/2014 -	10/2019	68	50.75	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
148	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	3,003.16	02/2016 -	06/2022	76	203.22	Renewal of lease for 3.0 Ha land at Asena Quarry and Transfer of additional 05 Ha. Forest land and permission for mining are pending. It needs to be expedited.
149	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,733.13	06/2013 -	12/2022	114	76.51	1) There have been frequent hindrances by local villagers since mobilization of works in Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Still regular support of Distt. Administration is required for smooth and unobstructed execution of the project works. 2) Approval of Gadi quarry and crusher plant is pending with District Administration/ GoUK.
	Total		1,70,427.67 -	2,29,653.46	1,61,837.24					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>HII Infra Tech Services Limited</u>									
150	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2	0	
151	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2	0	
152	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5	0	
	<u>Hospital Services Consultancy Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
153	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7	0	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
154	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27	0	
155	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	0	
156	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	0	
157	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	0	
158	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	0	
159	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	0	
160	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	24.1	
	Total		4,693.67 -	4,793.45	1,838.34					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
161	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	305.00	269.00	03/2019 12/2019	12/2019	9	65.71	
162	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,347.12	03/2021 -	03/2022	12	63.44	
163	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	301.24	03/2021 -	03/2022	12	73.73	
164	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	281.97	03/2022 -	03/2023	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
165	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	223.82	03/2022 -	03/2024	24	0	
166	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	76.32	03/2022 -	03/2024	24	0	
167	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	56.45	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									
168	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	260.88	03/2019 -	12/2019	9	0	
169	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	0	
170	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	150.62	03/2019 -	02/2020	11	0	
171	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	439.45	03/2018 -	03/2020	24	0	
172	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	286.78	03/2019 -	03/2020	12	0	
173	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	11.11	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
174	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	94.31	03/2019 -	12/2019	9	0	
175	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	898.53	1,038.71	03/2012 -	03/2020	96	176.7	
176	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	751.55	673.58	03/2012 -	03/2020	96	57.27	
177	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	466.93	03/2019 -	02/2021	23	0	
178	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	494.58	03/2020 -	03/2021	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
179	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	396.80	03/2020 -	10/2021	19	0	
180	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	488.95	03/2020 -	03/2022	24	49.45	
181	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	54.14	03/2021 -	03/2022	12	63.37	
182	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	32.31	03/2021 -	03/2022	12	62.06	
183	RAMPUR DUMRA - TAL - RAJENDRAPUR DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	438.38	03/2020 -	12/2022	33	0	
	<u>East Coast Railway</u>									
184	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	225.52	03/2020 -	03/2021	12	52.77	
185	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	924.93	02/2019 -	03/2022	37	38.43	
186	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	122.59	11/2018 -	03/2022	40	15.45	
187	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	393.60	12/2018 -	03/2022	39	0	
188	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	688.96	06/2021 -	03/2023	21	137.8	
189	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	130.99	10/2020 -	03/2023	29	0	
190	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	682.29	03/2020 -	03/2023	36	.07	
191	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	346.97	03/2022 -	03/2023	12	0	
192	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	1,360.34	03/2009 -	03/2024	180	29.71	
193	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	2,361.74	162.82	03/2022 -	03/2025	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Eastern Railways</u>									
194	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	0	
195	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024	133	134.8	
196	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	863.39	03/2019 12/2009	03/2025	72	36.22	1. Acquisition of land in stretch of 3.126 KM between Kamarpukur and Mayanapur and pending over of 5.679 KM stretch possession to Railway. 2. Villagers of Vill.Bhadadighi, Hooghly District, are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non availability of land
197	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	834.72	12/2010 12/2017	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 232.99 Cr. for their balance share towards project Katwa- BWN G.C.
198	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
199	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	290.01	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 158.50Cr. as share of expenditure incurred in this project..
200	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	434.06	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 For Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to religious structures in alignment and Amghata to Nabadwipghat work is held up due to 41 nos. of un authorized crossings.
201	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	102.27	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 km). The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
202	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	155.33	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
203	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	212.51	03/2017 -	03/2025	96	-18.82	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non availability of land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
204	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahat (9.75 Km) New line-- Work could not be started due to non availability of land
205	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	155.08	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Diamond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
206	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	105.28	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
207	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
208	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 -	12/2020	27	0	
209	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	619.50	03/2022 -	12/2022	9	117.23	
210	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39	-67.3	
	<u>Metropolitan Rapid Transport Projects</u>									
211	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,414.47	03/2004 -	03/2021	204	501.57	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
212	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 918.53	918.53	277.61	03/2014 03/2021	03/2021	84	-82.67	
213	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
	<u>North Central Railway</u>									
214	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	32.02	
	<u>North East Frontier Railway</u>									
215	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12	106.51	
216	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,123.93	03/2011 -	03/2020	108	181.17	
217	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 1,532.00	1,532.00	629.19	03/2019 -	03/2020	12	297.72	
218	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12	302.54	
219	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 728.00	728.00	704.09	03/2019 -	03/2020	12	131.85	
220	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 3,300.00	3,300.00	3,279.71	12/2008 -	03/2021	147	179.62	
221	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	3,000.00	781.71	03/2015 -	10/2021	79	28.95	
222	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	569.63 -	650.00	45.24	03/2020 -	12/2021	21	14.11	
223	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 4,968.00	5,021.45	3,075.08	03/2014 03/2022	03/2022	96	109.8	
	<u>North Eastern Railway</u>									
224	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	328.19	01/2019 -	01/2020	12	61.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
225	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	179.51	04/2017 -	01/2020	33	-31.45	
226	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	8.97	04/2016 -	06/2020	50	.16	
227	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-12.65	
228	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
229	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
	<u>North Western Railway</u>									
230	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	141.40	10/2018 -	10/2019	12	24.47	
231	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	262.32	11/2019 -	05/2020	6	42.26	
232	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	351.23	02/2019 -	05/2020	15	69.36	
233	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	215.47	12/2019 -	06/2020	6	41.64	
234	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	160.53	03/2020 -	06/2020	3	0	
235	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	525.78	02/2019 -	03/2021	25	116.16	
236	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	47.07	03/2020 -	04/2022	25	14.33	
237	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	47.07	08/2022 -	09/2022	1	0	
	<u>Northern Railway</u>									
238	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	141.81	
239	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	845.58	834.59	03/2016 -	03/2021	60	35.29	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
240	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	19,223.83	11/2002 -	06/2022	235	1017.96	
241	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE <u>Rail Vikas Nigam Ltd.</u>	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140	346.67	
242	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	395.00	386.28	03/2009 03/2009	12/2019	129	196.08	
243	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,757.33	12/2017 -	03/2020	27	55.57	
244	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020	12	29.45	
245	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,029.98	03/2020 -	06/2020	3	-21.54	
246	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	682.17	03/2016 -	12/2020	57	29.06	
247	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,304.20	03/2020 -	03/2021	12	58.22	
248	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	998.91	03/2019 -	03/2021	24	18.78	
249	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,032.16	12/2020 -	03/2021	3	0	
250	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	891.28	02/2015 -	12/2021	82	0	
251	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,402.19	03/2020 -	03/2022	24	0	
252	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	343.30	03/2022 -	12/2024	33	-20.46	
253	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	568.43	03/2023 -	12/2024	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
254	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,226.44	03/2016 -	03/2025	108	7.78	
255	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	847.45	03/2016 -	03/2025	108	0	
256	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	2,106.00	03/2014 -	12/2025	141	18.95	
257	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,521.62	12/2024 -	03/2026	15	0	
	<u>South Central Railway</u>									
258	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252	0	
259	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	102.85	
260	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	0	
261	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	0	
262	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	0	
263	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	18.47	
264	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	0	
265	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	0	
	<u>South East Central Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
266	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	646.30	02/2019 03/2020	06/2020	16	121.94	
267	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 1,756.92	1,756.92	1,661.79	04/2020 12/2020	12/2020	8	243.24	
268	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 1,973.66	1,973.66	139.42	03/2021 12/2022	12/2022	21	.03	
269	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 403.00	860.92	39.69	12/2021 03/2023	03/2023	15	275.95	
	<u>South Eastern Railway</u>									
270	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019	36	153.41	
271	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	258.09	12/2018 12/2018	06/2020	18	38.92	
272	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	549.97	03/2020 -	06/2020	3	35.38	
273	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	384.82	03/2021 -	12/2021	9	15.6	
274	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030	324	130.97	
	<u>South Western Railway</u>									
275	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	37.96	
276	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-1.38	
277	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	15.84	
278	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	0	
279	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	0	
280	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
281	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
282	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	0	
	<u>Southern Railway</u>									
283	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	1391.3	
284	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	185.98	
285	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	23.72	
286	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	222.39	
287	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	55.57	
288	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									
289	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	624.49	03/2020 -	03/2022	24	0	
290	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	154.63	03/2022 -	09/2022	6	114.32	
291	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023	178	2360.35	
292	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023	24	585.35	
293	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	367.59	03/2022 -	03/2023	12	0	
	<u>Western Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
294	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	809.07	616.90	03/2019 03/2020	03/2020	12	46.7	
295	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	1,310.23	1,363.06	03/2020 03/2021	03/2021	12	57.91	
296	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	663.29	163.85	03/2020 03/2021	03/2021	12	-4.13	
297	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	86.45	06/2020 06/2021	06/2021	12	-13.76	
298	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120	1.06	
299	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36	167.87	
300	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	1,037.15	992.18	03/2021 03/2022	03/2022	12	0	
301	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,338.15	3,860.40	1,676.43	03/2022 03/2023	03/2023	12	10.18	
302	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	682.91	03/2022 03/2023	03/2023	12	0	
	Total		1,75,002.73 -	2,56,024.18	1,13,834.55					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
303	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	103.79	08/2017 03/2020	08/2019	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
304	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	189.59	08/2017 03/2020	08/2019	24	0	
305	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA	01/2017	463.62 664.00	463.62	257.34	06/2019 -	08/2019	2	0	
306	AMDIT TO SAONER - [N24001021]MORTH,MAHARASHTRA	01/2017	396.91 396.91	396.91	248.48	06/2019 -	08/2019	2	0	
307	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	89.14	08/2015 -	09/2019	49	0	
308	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	87.58	09/2017 03/2020	09/2019	24	0	
309	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	464.05	03/2017 -	09/2019	30	46.51	
310	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	287.00	06/2019 -	10/2019	4	0	
311	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	.02	
312	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	195.88	11/2017 03/2020	11/2019	24	0	
313	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5	0	
314	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
315	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH, ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	.26	
316	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH, UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	0	
317	KHAMGAON TO SHEGAON - [N24001009]MORTH, MAHARASHTRA	02/2017	203.21 203.00	203.21	102.79	05/2019 -	12/2019	7	0	
318	SHEGAON TO DEORI PHATA - [N24001010]MORTH, MAHARASHTRA	02/2017	373.10 373.00	373.10	123.43	05/2019 -	12/2019	7	0	
319	NANDGAON TO MORSHI - [N24001014]MORTH, MAHARASHTRA	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6	0	
320	MORSHI TO ACHALPUR - [N24001015]MORTH, MAHARASHTRA	01/2017	341.16 341.00	341.16	153.29	06/2019 -	12/2019	6	0	
321	NAGAJ TO VAJJAPUR - [N24001023]MORTH, MAHARASHTRA	01/2017	376.72 377.00	376.72	168.81	06/2019 -	12/2019	6	0	
322	INDAPUR TO AGARDANDA - [N24001025]MORTH, MAHARASHTRA	01/2017	355.17 355.17	355.17	164.87	07/2019 -	12/2019	5	0	
323	TAKARKHED TO JALNA - [N24001085]MORTH, MAHARASHTRA	09/2017	417.90 418.00	417.90	87.26	06/2019 -	12/2019	6	0	
324	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH, MAHARASHTRA	12/2017	244.04 244.00	244.04	25.94	03/2019 -	12/2019	9	0	
325	TALEGAON TO GONAPUR - [N24001096]MORTH, MAHARASHTRA	01/2018	264.41 264.00	264.41	32.71	03/2019 -	12/2019	9	0	
326	PEN TO KHOPOLI - [N24001106]MORTH, MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	0	
327	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH, UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-11.07	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
328	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH	11/2016	378.24 -	378.24	237.18	01/2018 01/2020	01/2020	24	0	
329	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (-) [N24000938]MORTH,ANDHRA PRADESH	03/2018	297.12 294.00	297.12	177.05	07/2018 01/2020	01/2020	18	0	
330	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	196.46	01/2018 03/2020	01/2020	24	0	
331	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH	03/2018	244.95 245.00	244.95	101.40	08/2018 02/2020	02/2020	18	0	
332	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	80.47	08/2018 02/2020	02/2020	18	0	
333	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	0	
334	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	34.74	08/2018 03/2020	03/2020	19	0	
335	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	0	
336	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	751.91	11/2019 -	03/2020	4	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
337	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12	0	
338	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	269.70	11/2018 05/2020	05/2020	18	0	
339	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	29.03	05/2019 -	05/2020	12	0	
340	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	171.78	05/2019 -	05/2020	12	0	
341	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	68.00	06/2019 -	06/2020	12	0	
342	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	85.97	06/2019 -	06/2020	12	0	
343	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	0	
344	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	0	
345	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	0	
346	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	202.98	07/2019 -	07/2020	12	0	
347	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	129.17	08/2018 08/2020	08/2020	24	0	
348	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12	0	
349	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	148.00	09/2018 -	04/2021	31	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
350	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL, ARUNACHAL PRADESH	03/2015	194.11 -	194.11	159.75	05/2018 -	08/2019	15	0	
351	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 387.00	373.07	203.77	08/2016 -	08/2019	36	0	
352	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 340.00	429.52	166.55	08/2016 -	08/2019	36	0	
353	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL, ARUNACHAL PRADESH	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36	0	
354	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL, DELHI	07/2017	269.69 -	269.69	-	09/2019 -	12/2019	3	0	
355	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	17.43	01/2017 -	01/2020	36	11.57	
356	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21	0	
357	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 339.55	396.52	234.03	08/2016 -	06/2020	46	0	
358	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM	05/2015	454.89 -	454.89	120.86	05/2018 05/2020	12/2020	31	0	
359	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	28.67	04/2017 02/2018	02/2021	46	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
360	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46	0	
361	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	15.77	04/2017 02/2018	02/2021	46	0	
362	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	18.70	04/2017 02/2018	02/2021	46	0	
363	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	64.66	04/2017 03/2018	03/2021	47	0	
364	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63	0	
365	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	457.77	119.56	10/2018 -	10/2021	36	-11.55	
366	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42	0	
367	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42	0	
368	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021	71	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
369	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60	0	
	<u>National Highways Authority Of India</u>									
370	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [N240106278]NHAI,ASSAM	12/2003	199.81 340.14	340.14	319.96	04/2009 03/2011	08/2019	124	70.23	
371	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	140.57	01/2019 -	08/2019	7	0	
372	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	1,544.00	1,446.45	09/2016 -	09/2019	36	21.9	NIL
373	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	507.70	494.29	06/2016 -	09/2019	39	-15.8	
374	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	537.16	491.45	07/2018 -	09/2019	14	-6.46	
375	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 1,240.03	1,057.60	1,000.89	06/2019 12/2016	09/2019	3	-2.22	
376	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	588.00	06/2019 -	09/2019	3	0	
377	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	0	
378	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13	0	
379	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019	136	0	
380	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
381	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	37	0	
382	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019	27	0	
383	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	389.78	05/2018 10/2019	10/2019	17	0	
384	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	0	
385	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	2,982.00	276.87	04/2019 10/2019	10/2019	6	87.84	
386	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,424.19	01/2018 12/2018	11/2019	22	0	
387	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	0	
388	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 11/2019	11/2019	7	0	
389	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6	0	
390	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	20.54	06/2017 -	11/2019	29	0	
391	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	0	
392	4-LANNING OF OTTANCHATRAMP BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	105.81	09/2017 -	11/2019	26	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
393	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	0	
394	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	0	
395	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019	81	0	
396	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	0	
397	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81	0	
398	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	0	
399	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	0	
400	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	0	
401	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	897.03	705.85	11/2018 07/2019	12/2019	13	-37	
402	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019	24	66.88	
403	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	708.82	05/2018 03/2018	12/2019	19	0	
404	CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	0	
405	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	243.33	05/2019 -	12/2019	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
406	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	425.58	06/2018 -	01/2020	19	0	
407	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17	0	
408	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	0	
409	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76	-11	
410	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19	19.25	
411	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020	143	10.58	
412	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	0	
413	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,982.72	11/2011 -	03/2020	100	167.82	
414	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,138.07	08/2018 -	03/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
415	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23	-17.69	The CALA, Raipur had submitted proposal of additional 3A area for 12.6814 Ha (missing Khasra/plot no.) . 3A notification was published in Gazette on 04.07.2018 but CALA, Raipur did not provide revenue/ Khasra map to NHAI inspite of repeated request. In 680m length work was held up due to non-payment of land compensation to land owners, so NHAI has processed the 3D notification for 2.561Ha private land considering urgency at project site without revenue khasra map plan and balance 3D for area 10.1204 Ha was kept in hold due to non-receipt of Revenue Khasra map plan from CALA, Raipur. 3D of 2.561 Ha. land was published on 24.08.2018 . Inspite of repeated request to CALA, Raipur has not submitted revenue Khasra map plan showing 12.6814Ha land so the 3A notification dated 04.07.2018 balance area 10.1204Ha has lapsed on 03.07.2019. Some land owners (which land 3A was published on 04.07.2018 but 3D not published due to want of revenue Khasra map plan) have filed writ petition in Bilaspur High Court and Court passed order that land compensation should be paid to land owners within 09 months from the date of order after duly verification of land proposed in the acquisition. The land acquisition map showing RoW width for 25 villages are still not submitted by SDM Raipur & SDM Simga due to which 3A for balance 10.1204Ha of land could not be processed.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
416	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	343.21	08/2018 -	03/2020	19	0	
417	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	0	
418	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	0	
419	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	0	
420	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	159.58	03/2020 -	04/2020	1	.23	
421	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020	24	-12	
422	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	750.87	11/2016 -	05/2020	42	0	
423	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	340.73	07/2018 -	05/2020	22	0	
424	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	904.16	817.58	02/2020 11/2017	05/2020	3	0	
425	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	3.4	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
426	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	852.57	03/2020 11/2017	05/2020	2	0	
427	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	751.70	03/2020 -	05/2020	2	13.97	
428	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	340.73	07/2016 -	05/2020	46	0	
429	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78	0	
430	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	0	
431	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	0	
432	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	0	
433	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	0	
434	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	626.56	03/2020 -	06/2020	3	44.39	
435	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	278.60	09/2017 -	06/2020	33	9.67	
436	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,273.00	2,136.97	1,214.48	12/2018 12/2019	07/2020	19	0	Delay in handing over of land

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
437	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	532.53	04/2019 07/2020	07/2020	15	0	
438	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	567.90	03/2020 -	07/2020	4	41.54	
439	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	08/2020	149	-28.84	
440	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	0	
441	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	0	
442	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	254.96	03/2019 03/2017	08/2020	17	-25.48	Nil
443	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	10.58	
444	4-LANNING OF YAVATMAL- WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	5.56	
445	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	5.7	
446	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	0	
447	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	159.23	09/2017 -	08/2020	35	0	
448	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,700.67	07/2015 12/2019	09/2020	62	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
449	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	220.70	05/2018 04/2019	09/2020	28	-2	
450	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	122.89	08/2017 -	09/2020	37	0	
451	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	0	
452	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	0	
453	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	0	
454	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	1,071.00	556.63	03/2017 05/2018	11/2020	44	1.06	
455	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	364.29	10/2017 -	11/2020	37	0	
456	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31	0	
457	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	0	
458	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	621.26	06/2019 -	12/2020	18	0	The Funds disbursement by the state government is very slow. 1040 trees are to be cut from the forest/state land.
459	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
460	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17	0	
461	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,353.61	08/2019 -	12/2020	16	16.55	
462	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	17.41	09/2017 -	01/2021	40	0	Administrative assistance required for removal of Encroachments.
463	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	0	
464	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHATTI - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	0	
465	REHABILITATION AND UPGRADATION BY 4-LANNING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	348.24	03/2020 -	03/2021	12	10.24	
466	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	134.18	03/2019 04/2021	04/2021	25	0	
467	FOUR LANNING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	569.15	03/2021 -	04/2021	1	63.05	
468	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-3.27	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
469	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56 -	476.56	-	07/2017 11/2020	06/2021	47	0	
470	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	0	
471	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI, BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	0	
472	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	93.53	12/2017 -	08/2019	20	0	
	<u>National Highways Development Project</u>									
473	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019	30	46.51	
474	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH	01/2012	410.72 -	410.72	-	04/2015 -	10/2019	54	0	
475	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36	77.26	
	<u>Public Works Dept Of State</u>									
476	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70	0	
477	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD, KARNATAKA	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24	0	
478	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD, MADHYA PRADESH	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
479	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	359.27	227.88	05/2019 -	08/2019	3	0	
480	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	153.21	100.10	01/2017 -	09/2019	32	0	
481	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	0	
482	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019	6	0	
483	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	244.54	137.10	05/2019 09/2019	09/2019	4	0	
484	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	09/2019	11	0	
485	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	89.14	08/2015 -	09/2019	49	0	
486	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL	03/2016	271.17 291.20	291.20	79.43	11/2018 11/2019	11/2019	12	7.39	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
487	REHABILITATION AND UPGRADE OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	97.39	02/2018 -	11/2019	21	0	
488	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	55.27	02/2018 -	11/2019	21	0	
489	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	19.35	03/2018 -	11/2019	20	0	
490	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	95.28	03/2018 -	11/2019	20	0	
491	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	139.41	02/2018 -	11/2019	21	0	
492	REHABILITATION AND UPGRADE TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	0	
493	REHABILITATION AND UPGRADE OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	436.12	06/2019 -	11/2019	5	0	
494	REHABILITATION AND UPGRADE OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	249.50	150.70	05/2019 -	11/2019	6	0	
495	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	224.94	03/2018 -	11/2019	20	0	
496	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	36.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
497	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105	58.98	
498	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	69.3	
499	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76	0	
500	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	47.65	
501	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	0	
502	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	88.47	03/2018 -	12/2019	21	0	
503	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	77.44	02/2019 -	12/2019	10	0	
504	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	88.85	03/2019 -	12/2019	9	0	
505	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	99.46	05/2019 -	12/2019	7	0	
506	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA	03/2018	192.67 -	192.67	107.35	07/2019 -	12/2019	5	0	
507	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
508	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63	63.46	
509	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	118.29	07/2018 -	01/2020	18	0	
510	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	240.05	08/2017 -	02/2020	30	0	
511	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	219.42	07/2018 -	02/2020	19	0	
512	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54	0	
513	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	0	
514	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	373.82	116.33	09/2019 -	05/2020	8	0	
515	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	0	
516	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116	93.8	
517	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	26.72	08/2018 -	06/2020	22	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
518	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39	0	
519	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	12.39	08/2018 -	06/2020	22	0	
520	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	9.35	03/2018 -	07/2020	28	0	
521	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	0	
522	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	
523	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	33.51	
524	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	11.18	
	Total		1,34,093.27 -	1,41,413.50	89,552.02					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
525	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 -	240.10	117.63	10/2018 09/2019	09/2019	11	3.58	
	<u>Department Of Telecommunication</u>									
526	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	84.97	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2019)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		13,565.80	24,904.10	8,514.63					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
527	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00	10,773.00	5,854.77	12/2018	07/2020	19	0	
	<u>Bangalore Metro Rail Corporation Limited</u>									
528	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14	26,405.14	499.85	02/2019	03/2020	13	0	
	<u>Central Public Works Department</u>									
529	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58	206.58	82.23	03/2019	08/2019	5	0	
530	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00	488.28	424.11	05/2017	09/2019	28	25.85	
531	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57	156.57	156.13	08/2016	10/2019	38	0	
532	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83	270.83	199.91	11/2014	10/2019	59	0	
533	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013	10/2019	70	132.8	
534	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00	294.00	195.83	04/2019	02/2020	10	0	
535	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	335.76	07/2019 12/2019	02/2020	7	1.85	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
536	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	89.66	10/2012 -	03/2020	89	0	
537	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	130.62	10/2019 -	03/2020	5	0	
538	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	42.30	04/2019 -	06/2020	14	0	
539	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	80.08	03/2016 -	09/2020	54	0	
540	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	65.84	02/2020 -	09/2020	7	0	
541	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	33.01	07/2020 09/2020	09/2020	2	0	
542	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	0	
543	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	85.74	06/2017 -	10/2020	40	.57	
544	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	65.80	05/2020 -	01/2021	8	0	
545	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	330.83	10/2019 -	03/2021	17	64.04	
546	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 -	05/2021	14	0	
	<u>Hindustan Steelwork Construction Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
547	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
548	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	9.76	
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
549	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11,420.00	2,727.17	11/2021 01/2022	01/2022	2	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
550	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
551	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	6,108.39	03/2018 -	12/2019	21	0	
	Total		92,316.50 -	93,868.28	23,435.03					
	<u>WATER RESOURCES</u>									
	<u>Polavaram Project Authority</u>									
552	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	447.22	
	Total		10,151.04 -	55,548.87	16,417.99					
	Grand Total		8,23,289.61	10,55,842.45	5,45,346.15					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(August 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88	133
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63	48
	Total		27,271.00 -	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02	6
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		653.54 -	780.33				
	<u>COAL</u>							
	<u>Neyveli Lignite Corporation</u>							
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86	48
	<u>Singareni Colliers Company Limited</u>							
7	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
8	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42	12
9	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85	72
11	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
12	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
13	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
14	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
	Total		8,301.00 -	10,390.07				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89	34
	Total		197.79 -	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
16	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10	83
	Total		414.11 -	513.89				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
17	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	10/2018 -	12/2019	58.15	14
18	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	06/2019 -	02/2022	35.54	32
19	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33	15
	<u>Gas Authority Of India Limited</u>							
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61	110
	<u>Hindustan Petroleum Corporation Limited</u>							
21	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	10/2014 -	08/2019	133.50	58
	<u>Indian Oil Corporation Limited</u>							
22	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98	26
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
23	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE [N16000256	10/2015	135.00 171.00	170.70	03/2019 -	09/2019	26.44	6

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
24	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88	6
	<u>Oil & Natural Gas Corporation Limited</u>							
25	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45	70
26	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48	4
27	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30	79
28	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42	57
29	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77	25
30	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17	1
31	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71	7
	<u>Oil India Limited</u>							
32	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47	33
33	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	06/2020	25.55	4
	Total		30,257.31 -	36,284.99				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
34	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06	147
	<u>National Thermal Power Corporation</u>							
35	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23	29
36	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	12/2020	96.99	93
37	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75	98
38	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87	40
39	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
40	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55	26
41	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	09/2020	9.64	21
42	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55	27
43	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	12/2021	33.47	43
44	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16	118
	<u>North East Electric Power Corporation</u>							
45	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	12/2009 06/2016	10/2019	217.49	118
	<u>Power Grid Corporation Of India Limited</u>							
46	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	-	27.92	25
47	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61	40
48	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17	63
49	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	-	38.61	40
50	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	-	22.93	129
51	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14	86
52	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61	24
53	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82	12
54	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24	103
	<u>Thdc India Limited</u>							
55	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75	68
56	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51	114
57	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22	76
	Total		1,32,442.77 -	1,91,668.56				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
58	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71	9
59	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73	12
60	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44	12
	<u>Container Corporation Of India</u>							
61	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	03/2012 -	03/2020	57.27	96
63	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2022	49.45	24
64	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	898.53	03/2012 -	03/2020	176.70	96
65	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
66	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
	<u>East Coast Railway</u>							
67	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2021	52.77	12
68	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2022	15.45	40
69	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07	36
70	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43	37
71	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
72	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	03/2024	29.71	180
	<u>Eastern Railways</u>							
73	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
74	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE- PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
75	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
76	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
77	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
78	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
79	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
80	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
81	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
82	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23	9
	<u>Metropolitan Rapid Transport Projects</u>							
83	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57	204
84	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>							
85	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
86	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
87	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11	21
88	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	728.00	03/2019 -	03/2020	131.85	12
89	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
90	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
91	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95	79
92	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	3,300.00	12/2008 -	03/2021	179.62	147
93	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
94	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,524.00	03/2011 -	03/2020	181.17	108
	<u>North Eastern Railway</u>							
95	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16	50
96	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80	12
	<u>North Western Railway</u>							
97	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47	12
98	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	11/2019 -	05/2020	42.26	6
99	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64	6
100	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	05/2020	69.36	15
101	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33	25
102	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	03/2021	116.16	25
	<u>Northern Railway</u>							
103	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81	111
104	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	03/2021	35.29	60
105	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67	140
106	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	06/2022	1,017.96	235
	<u>Rail Vikas Nigam Ltd.</u>							
107	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	395.00	03/2009 03/2009	12/2019	196.08	129
108	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
109	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78	24
110	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45	12
111	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22	12
112	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57	27
113	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
114	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98	4,259.48	03/2016	03/2025	7.78	108
	<u>South Central Railway</u>							
115	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20	2,120.16	03/2009	03/2023	102.85	168
116	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95	2,200.00	03/2023	03/2024	18.47	12
	<u>South East Central Railway</u>							
117	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	860.92	12/2021	03/2023	275.95	15
118	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93	1,300.44	02/2019	06/2020	121.94	16
119	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86	1,756.92	04/2020	12/2020	243.24	8
120	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00	1,973.66	03/2021	12/2022	.03	21
	<u>South Eastern Railway</u>							
121	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20	358.68	12/2018	06/2020	38.92	18
122	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77	377.00	12/2016	12/2019	153.41	36
123	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83	1,312.96	03/2020	06/2020	35.38	3
124	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20	1,993.24	03/2021	12/2021	15.60	9
125	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40	2,373.00	03/2003	03/2030	130.97	324
	<u>South Western Railway</u>							
126	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78	889.52	03/2017	03/2020	37.96	36
127	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59	1,870.41	03/2019	03/2021	15.84	24
	<u>Southern Railway</u>							
128	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26	231.67	04/2014	03/2020	23.72	71
129	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98	980.00	03/2020	03/2021	222.39	12
130	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00	1,182.31	03/2020	06/2021	55.57	15
131	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70	1,800.00	03/2019	12/2019	1,391.30	9

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
132	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98	12
	<u>West Central Railway</u>							
133	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32	6
134	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
135	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
136	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06	120
137	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70	12
138	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
139	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91	12
140	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18	12
	Total		80,932.28 -	1,70,910.21				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways</u>							
141	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02	41
142	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26	43
143	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	03/2017 -	09/2019	46.51	30
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
144	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
145	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2020	10.58	143
146	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	04/2009 -	08/2019	70.23	124

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
147	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25	19
148	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	12/2017 -	12/2019	66.88	24
149	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
150	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
151	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
152	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
153	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	08/2019 -	12/2020	16.55	16
154	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
155	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54	4
156	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
157	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	09/2017 -	06/2020	9.67	33
158	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
159	REHABILITATION AND UPGRADE BY 4-LANNING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24	12
160	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
161	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	09/2019	21.90	36
162	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05	1
163	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82	100
164	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	04/2019 -	10/2019	87.84	6

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>National Highways Development Project</u>							
165	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	03/2017 -	09/2019	46.51	30
166	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26	36
	<u>Public Works Dept Of State</u>							
167	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) - [N24000885]	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51	24
168	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18	24
169	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65	82
170	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39	12
171	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46	63
172	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30	110
173	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	36.24	27
174	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80	116
175	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98	105
	Total		23,498.27 -	32,093.91				
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmdc)</u>							
176	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05	62
	Total		15,525.00 -	23,140.00				
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
177	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT [N26000113]	01/2018	231.80 -	240.10	10/2018 -	09/2019	3.58	11
	<u>Department Of Telecommunication</u>							
178	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58
	Total		13,565.80 -	24,904.10				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
179	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
180	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85	28
181	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57	40
182	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	02/2020	1.85	7
183	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2021	64.04	17
	<u>Kochi Metro Rail Corporation Ltd</u>							
184	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77	29
	Total		7,948.75 -	9,500.53				
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
185	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22	15
	Total		10,151.04 -	55,548.87				
	Grand Total		3,51,158.66	5,96,443.90				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-
2	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	-
3	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Singareni Colliers Company Limited</u>				
4	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	06/2015 -	12/2015
5	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
6	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 -	-
	<u>Western Coal Fields Limited</u>				
7	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
8	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
9	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
10	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA	10/2016	164.96 -	03/2019 -	-
	Total		4,522.05 -		
	<u>INFORMATION AND BROADCASTING</u>				
	<u>National Film Archive Of India</u>				
11	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA	11/2014	597.41 -	- -	-
	Total		597.41 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
12	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 -	06/2019 -	-
	Total		166.62 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
13	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
14	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				
15	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH	02/2016	151.00 -	09/2019 -	06/2019
16	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 06/2019	07/2019
17	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	10/2017 -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>				
19	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA	05/2015	224.00 207.00	04/2019 -	10/2018
	<u>Oil India Limited</u>				
20	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
21	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		9,916.77 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
24	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
25	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
26	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
	<u>Power Grid Corporation Of India Limited</u>				
27	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	02/2016 -	06/2019
28	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019
29	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	03/2018 -	07/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
30	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	07/2019
31	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	07/2019
32	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	07/2019
33	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	07/2019
34	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	07/2019
	Total		27,858.98 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
35	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
36	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	-
37	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	-
	Total		925.15 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
38	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
39	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
40	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
41	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
42	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
43	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR	07/2004	599.63 674.00	12/2007 -	-
44	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 546.71	07/2014 -	-
	<u>Eastern Railways</u>				
45	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
46	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
47	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
48	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	06/2013 -	-
49	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
50	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	03/2015
51	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TAMPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-
	<u>North East Frontier Railway</u>				
52	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	-
53	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	03/2019 -	-
54	NEW JALPAIGURI-SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-
55	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
	<u>North Eastern Railway</u>				
56	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
57	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
58	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
59	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
60	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
61	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH	04/2016	602.50 -	- -	-
	<u>North Western Railway</u>				
62	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
63	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
64	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
65	AJMER(NASIRABAD)-SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Rail India Technical And Economic Service</u>				
66	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
67	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
68	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
69	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
70	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
71	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
72	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
73	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
74	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 -	- -	-
75	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South Eastern Railway</u>				
76	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
77	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR	08/2010	400.00 -	03/2014 -	-
78	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
79	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	-
	<u>Southern Railway</u>				
80	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-
81	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
82	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
83	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
84	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
85	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
86	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
87	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
88	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-
89	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
90	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-
91	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-
92	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
93	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
94	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
95	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	03/2017
96	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
97	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
98	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
99	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
100	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		54,659.65 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
101	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
102	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
103	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
104	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 12/2019	12/2016
105	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH	03/2016	995.09 995.00	05/2016 03/2020	05/2018

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965])MORTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 08/2019	05/2018
107	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964])MORTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2019	07/2018
108	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966])MORTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 03/2020	08/2018
109	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967])MORTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 03/2020	09/2018
110	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929])MORTH,ANDHRA PRADESH	09/2016	372.68 -	02/2017 12/2019	02/2019
111	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931])MORTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 03/2020	05/2019
112	AJANTHA TO BULDHANA - [N24001008]MORTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	07/2019
113	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MORTH,MAHARASHTRA	01/2017	486.19 486.19	07/2019 -	07/2019
114	PARTUR TO MAJALGAON - [N24001034]MORTH,MAHARASHTRA	01/2017	420.57 420.57	07/2019 -	07/2019
115	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019
116	KAIJ TO KUSALAM - [N24001037]MORTH,MAHARASHTRA	01/2017	554.78 554.78	07/2019 -	07/2019
117	SHIROD SHAHPURER TO NANDED - [N24001041]MORTH,MAHARASHTRA	01/2017	211.34 211.34	07/2019 -	07/2019
118	MUL TO CHANDRAPUR - [N24001117]MORTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	07/2019
119	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600(JOB NO 992/15-16 - [N24000275])MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
120	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
121	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
122	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
123	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
124	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
125	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
126	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
127	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
128	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
129	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
130	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
131	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
132	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
133	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
134	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
135	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
136	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
137	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
138	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-
139	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
140	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
141	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
142	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
143	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUARI - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
144	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
145	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
146	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
147	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
148	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
149	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
150	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
151	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
152	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
153	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
154	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
155	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
156	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
157	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
158	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
159	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-
160	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-
161	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA	03/2016	165.06 -	12/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
162	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA - [N24000912]MORTH,ODISHA	08/2016	287.70 -	02/2017 -	-
163	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA	09/2016	295.67 -	02/2017 -	-
164	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA	12/2016	223.50 -	08/2018 -	-
165	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA	12/2016	206.88 -	04/2018 -	-
166	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA	03/2018	214.23 -	08/2018 -	-
167	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA	03/2018	199.16 -	08/2018 -	-
168	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR	09/2018	1,478.40 -	- -	-
169	SARSAM TO KOTHARI - [N24001002]MORTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
170	AKOLA TO AKOT - [N24001003]MORTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
171	AKOT TO ANJANGAON - [N24001006]MORTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
172	ANJANGAON TO MAH/MP BORDER - [N24001007]MORTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
173	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
174	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
175	DAHEGAON TO KUHI - [N24001017]MORTH,MAHARASHTRA	01/2017	228.89 228.89	06/2019 -	-
176	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
177	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA	01/2017	356.66 356.66	- -	-
178	KALMAB TO RALEGAON - [N24001044]MORTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
179	RALEGAON TO RAMTIRTH - [N24001046]MORTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
180	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
181	HELWAK TO KARAD - [N24001055]MORTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
182	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
183	BODHWAD TO STATE BORDER - [N24001086]MORTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
184	KOLDE TO KHETIYA - [N24001090]MORTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
185	SATARA TO MHASWAD - [N24001092]MORTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
186	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-
187	MHASWAD TO TEMBHURNI - [N24001099]MORTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
188	KURUDWADI TO PANDHARPUR - [N24001101]MORTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
189	PANDHARPUR TO SANGOLA - [N24001102]MORTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
190	SARAD VANI PIMPALGAON - [N24001103]MORTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
191	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
192	GADCHIROLI TO MUL - [N24001116]MORTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
193	NAGBHID TO ARMORI - [N24001119]MORTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
194	PAITHAN TO SHIRUR - [N24001122]MORTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
195	SHIRUR TO KHARDA - [N24001123]MORTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
196	AURANGABAD TO SILLOD - [N24001124]MORTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
197	SILLOD TO FARDAPUR - [N24001125]MORTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
198	FARDAPUR TO JALGAON - [N24001126]MORTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
199	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
200	BHOKAR TO SARSAM - [N24001128]MORTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
201	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
202	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MORTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- -	-
203	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MORTH,RAJASTHAN	03/2019	178.13 -	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
204	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
205	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
206	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
207	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
208	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
209	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
210	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 12/2019	-
211	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
212	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
213	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
214	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
215	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
216	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
217	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
218	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
219	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
220	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
221	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
222	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
223	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
224	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
225	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
226	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
227	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
228	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
229	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
230	(I) CONSTRUCTION OF FOUR/SIX LANE FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
231	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-
232	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-
233	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 05/2019	-
234	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
235	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
236	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
237	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 136.73	09/2018 11/2018	-
238	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 160.10	09/2018 11/2018	-
239	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 11/2018	-
240	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
241	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
242	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
243	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
244	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
245	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
246	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
247	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
248	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
249	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY- PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
250	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
251	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
252	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
253	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
254	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
255	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
256	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
257	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-
258	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
259	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
260	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH- 52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
261	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
262	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
263	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
<u>National Highways Authority Of India</u>					
264	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	06/2019
265	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	06/2019
266	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013
267	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 408.77	11/2008 07/2011	01/2014
268	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015
269	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
270	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018
271	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018
272	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019
273	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 315.00	- 03/2020	03/2019
274	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
275	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019
276	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	06/2019
277	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
278	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019
279	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	07/2019
280	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	07/2019
281	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 456.92	02/2009 -	-
282	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
283	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
284	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
285	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
286	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
287	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
288	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 2,519.00	06/2015 -	-
289	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
290	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	-
291	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	-
292	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
293	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-
294	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	-
295	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	-
296	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
297	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	-
298	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-
299	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 -	-
300	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-
301	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
302	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	-
303	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
304	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-
305	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
306	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	-
307	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
308	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
309	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 2,521.24	12/2015 -	-
310	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
311	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
312	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
313	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-
314	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
315	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
316	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
317	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
318	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
319	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
320	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
321	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-
322	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
323	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
324	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-
325	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-
326	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
327	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
328	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
329	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
330	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
331	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
332	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
333	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
334	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-
335	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
336	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
337	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
338	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
339	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
340	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
341	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
342	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
343	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
344	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
345	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
346	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
347	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
348	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
349	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
350	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	-
351	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
352	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
353	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
354	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
355	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
356	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
357	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
358	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
359	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
360	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
361	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
362	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
363	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
364	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
365	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
366	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
367	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
368	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
369	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 929.89	- -	-
370	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
371	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
372	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
373	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
374	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 -	- -	-
375	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
376	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
377	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
378	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN	02/2018	716.76 -	- -	-
379	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
380	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
381	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
382	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
383	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
384	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
385	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
386	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
387	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
388	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
389	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
390	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
391	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
392	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
393	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
394	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
395	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
396	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 149.90	- -	-
397	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
398	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
399	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
400	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
401	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
402	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
403	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
404	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
405	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
406	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	-
407	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-
<u>National Highways Development Project</u>					
408	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
409	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-
410	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
411	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Public Works Dept Of State</u>				
412	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017
413	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 11/2019	10/2017
414	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
415	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD, WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
416	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD, WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019
417	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD, UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019
418	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]PWD, TELANGANA	01/2014	270.00 -	03/2016 -	-
419	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD, MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
420	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD, ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
421	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD, CHHATISGARH	12/2015	291.05 -	- -	-
422	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD, ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
423	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH	11/2015	485.44 -	12/2015 -	-
424	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
425	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD, ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
426	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD, ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
427	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD, ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 06/2018	-
428	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD, SIKKIM	04/2013	166.27 203.26	08/2013 -	-
429	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD, NAGALAND	12/2010	1,296.00 -	02/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
430	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
431	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
432	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
433	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
434	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
435	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 307.47	02/2018 -	-
436	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
437	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
438	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
439	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
440	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
441	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
442	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
443	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-
444	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	03/2019 07/2019	-
445	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]PWD,GUJARAT	03/2016	223.67 -	02/2017 -	-
446	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD,GUJARAT	03/2016	208.34 -	02/2016 -	-
447	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD,GUJARAT	12/2017	867.97 -	11/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
448	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]PWD,GUJARAT	03/2018	464.07 399.35	11/2018 -	-
449	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 386.19	05/2019 -	-
450	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD,GUJARAT	08/2017	962.43 887.21	03/2018 -	-
451	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
452	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD,RAJASTHAN	10/2014	382.81 -	01/2015 -	-
453	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD,RAJASTHAN	01/2017	179.32 -	11/2017 -	-
454	CONSTRUCTION OF NAGOUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD,RAJASTHAN	03/2016	155.77 -	09/2016 -	-
455	NAGOUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD,RAJASTHAN	01/2012	378.07 478.73	01/2014 -	-
456	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD,RAJASTHAN	10/2012	511.21 -	10/2013 -	-
457	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD,RAJASTHAN	03/2009	501.00 671.54	09/2013 -	-
458	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD,RAJASTHAN	11/2017	163.95 -	04/2018 -	-
459	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
460	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
461	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD,RAJASTHAN	12/2015	621.43 -	10/2016 -	-
462	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD,RAJASTHAN	01/2017	163.54 -	07/2017 -	-
463	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA	01/2019	193.19 -	- -	-
464	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR	03/2018	153.24 -	- -	-
465	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA	08/2016	367.44 -	01/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
466	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA	08/2016	175.20 -	01/2017 -	-
467	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	-
468	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	-
469	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA	03/2018	159.97 -	06/2019 -	-
470	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	-
471	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	-
472	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	-
473	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	-
474	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	-
475	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	-
476	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	-
477	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	-
478	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	-
479	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	-
480	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]PWD,ARUNACHAL PRADESH	11/2016	243.89 -	- -	-
481	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]PWD,BIHAR	02/2019	2,926.42 -	- -	-
482	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]PWD,UTTAR PRADESH	03/2018	306.59 -	- -	-
483	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]PWD,UTTAR PRADESH	11/2018	281.45 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		2,29,546.37		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
484	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17	09/2014	-
	<u>Mahanagar Telephone Nigam Limited</u>				
485	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26	06/2017	-
	Total		2,529.43		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
486	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88	04/2018	07/2019
487	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00	03/2012	-
488	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84	03/2017	-
489	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	12/2015	-
490	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00	06/2019	-
491	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20	04/2018	-
492	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72	-	-
	<u>Chennai Metro Rail Ltd</u>				
493	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00	12/2015	-
494	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00	03/2018	-
	<u>Hindustan Steelwork Construction Limited</u>				
495	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015	-
496	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016	-
497	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016	-
498	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014	-
499	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
500	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	09/2017 -	-
501	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL, ANDHRA PRADESH	07/2014	232.00 -	- -	-
502	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	- -	-
503	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN	05/2015	189.00 -	03/2017 -	-
504	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL, JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
505	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL, JHARKHAND	12/2007	200.00 -	03/2018 -	-
506	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	12/2016 -	-
507	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL, JHARKHAND	04/2013	170.00 -	04/2018 -	-
508	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-
<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
509	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-
<u>Lucknow Metro Rail Corporation Limited</u>					
510	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
<u>Maharashtra Metro Rail Corporation Ltd.</u>					
511	DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI	09/2011	38,585.00 -	03/2016 -	-
<u>National Building Construction Corporation Ltd</u>					
512	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-
	Total		72,854.33 -		
	Grand Total		4,03,576.76		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	144.07	- 04/2017	03/2020	35(R3)	0/6
2	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA	08/2016	431.92 -	431.92	-	- 03/2023	-	-	0/9
3	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA	02/2018	412.70 -	412.70	.11	- 03/2023	-	-	0/7
	Total		1,117.35 -	1,117.35	144.18				0/22
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
4	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	69.24	- -	03/2021	-	9/26
5	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	588.20	.94	- -	08/2022	-	8/17
	Total		818.00 -	818.00	70.18				17/43
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation</u>								
6	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	601.02	85.04	- -	02/2020	-	0/0
7	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	582.99	112.97	- -	02/2020	-	0/0
8	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	651.99	112.82	- -	02/2020	-	0/0
9	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	268.84	99.26	- -	04/2020	-	0/0
10	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	249.01	73.40	- -	05/2020	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>								
11	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	156.65	54.94	- -	02/2020	-	0/0
	Total		2,510.41 -	2,510.50	538.43				0/0
	<u>RAILWAYS</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	East Central Railways								
12	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 726.31	726.31	497.81	- -	10/2019	-	0/0
13	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 367.17	425.17	397.41	- -	01/2020	-	0/0
14	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	3,376.00	3,290.02	- -	03/2021	-	0/0
15	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	498.90	- -	03/2021	-	0/0
16	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	362.10	- -	03/2021	-	0/0
17	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	761.68	- -	03/2021	-	0/0
18	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	1,483.14	845.59	- -	12/2021	-	0/0
19	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	305.70	- -	03/2022	-	0/0
20	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	2,609.00	376.63	- -	03/2022	-	0/0
21	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	138.35	- -	02/2023	-	0/0
22	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,405.48	- -	03/2023	-	0/0
23	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	633.87	.40	- -	03/2023	-	0/0
24	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	23.49	- 03/2023	03/2023	0(R3)	0/0
25	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	.28	- -	03/2024	-	0/0
26	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	03/2024	-	0/0
27	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	549.75	15.54	- -	03/2024	-	0/0
28	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	1.91	- -	03/2024	-	0/0
29	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.21	- -	03/2024	-	0/0
30	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	1,006.00	24.16	- -	03/2024	-	0/0
31	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.20	- -	03/2024	-	0/0
32	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
33	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	.39	-	03/2024	-	0/0
34	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	.60	-	03/2024	-	0/0
	<u>Eastern Railways</u>								
35	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	376.90	376.90	-	03/2020	-	0/0
36	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	242.06	242.06	-	03/2021	-	0/0
37	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	154.98	-	09/2021	-	0/0
38	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	257.06	-	03/2024	-	0/0
39	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	9.31	-	03/2025	-	0/0
40	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	10.73	-	03/2025	-	0/0
41	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.42	-	03/2025	-	0/0
42	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.12	-	03/2025	-	0/0
43	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	-	03/2025	-	0/0
44	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	-	03/2025	-	0/0
45	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	-	03/2025	-	0/0
46	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	-	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
47	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	-	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
48	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	394.28	272.88	-	03/2021	-	0/0
49	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.67	-	03/2022	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
50	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	0(R3)	0/0
	<u>Northern Railway</u>								
51	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	346.63	229.48	- -	06/2020	-	0/0
52	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91 791.39	800.00	512.67	- -	03/2022	-	0/0
53	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	295.68	79.53	- -	03/2023	-	0/0
54	UNCHAHAR-AMETHI - [N22000294]NR, UTTAR PRADESH	04/2012	1,229.00 -	1,230.00	103.17	- -	03/2023	-	0/0
55	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	197.17	107.86	- -	03/2024	-	0/0
56	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.89	- -	03/2024	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
57	RAYADURGA-TUMKUR NL - [N22000279]RVNL, MULTI STATE	04/2007	2,062.30 -	2,062.20	825.58	- -	03/2022	-	0/2
	<u>South East Central Railway</u>								
58	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 1,413.76	1,413.76	1,324.64	- 10/2019	10/2019	0(R3)	0/0
	<u>South Eastern Railway</u>								
59	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	0(R3)	0/0
	<u>South Western Railway</u>								
60	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01 -	1,801.01	44.36	- -	12/2023	-	0/0
61	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 -	692.43	-	- -	12/2023	-	0/0
62	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00 -	466.65	-	- -	12/2023	-	0/0
63	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	348.85 -	348.85	.35	- -	12/2023	-	0/0
64	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
65	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 -	367.77	-	- -	12/2023	-	0/0
66	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	2,315.00 -	2,135.00	144.76	- -	12/2024	-	0/0
	<u>Southern Railway</u>								
67	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41 -	450.00	151.50	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	951.24	724.96	- -	03/2020	-	0/0
69	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	1,431.90	75.00	- 06/2022	-	-	0/0
	<u>Western Railway</u>								
70	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	439.88	92.69	- -	03/2021	-	0/0
	Total		29,284.51 -	47,396.61	15,015.70				0/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
71	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	58.58	- -	06/2020	-	0/4
72	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	98.37	- -	09/2020	-	0/4
73	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	434.06	126.58	- -	12/2020	-	2/4
74	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	9.65	- 02/2018	02/2021	36(R3)	0/0
75	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	36(R3)	0/0
76	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	27.90	- -	09/2021	-	0/4
77	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	6.58	- 04/2019	04/2022	36(R3)	0/0
78	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	5.63	- 04/2019	04/2022	36(R3)	0/0
	<u>National Highways Authority Of India</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
79	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	998.18	435.25	- -	08/2019	-	0/0
80	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	763.08	357.12	- -	08/2019	-	0/0
81	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	723.64	321.67	- -	09/2019	-	0/0
82	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	417.19	262.83	- -	09/2019	-	0/0
83	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	531.00	433.62	- -	09/2019	-	0/0
84	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	941.00	814.55	- -	10/2019	-	0/0
85	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 622.00	622.00	601.52	- -	10/2019	-	0/0
86	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 622.00	622.00	543.86	- -	10/2019	-	0/0
87	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	275.90	257.52	- 02/2016	10/2019	44(R3)	0/0
88	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	834.64	140.44	- -	10/2019	-	0/0
89	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	752.28	-	- -	11/2019	-	0/0
90	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	30(R3)	0/0
91	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	447.75	179.17	- -	11/2019	-	0/0
92	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH	12/2017	328.67 -	328.67	176.29	- -	11/2019	-	0/0
93	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	1,167.45	113.26	- -	12/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
94	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	392.00	240.57	- -	12/2019	-	0/0
95	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	458.03	303.12	- 12/2017	12/2019	24(R3)	0/0
96	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	1,100.19	892.00	- -	12/2019	-	0/0
97	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
98	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	814.04	384.48	- -	01/2020	-	0/0
99	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	-	0/0
100	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	829.97	75.08	- -	01/2020	-	0/0
101	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	-	0/0
102	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	1,443.00	1,246.85	- -	02/2020	-	0/0
103	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	1,244.10	1,326.00	- -	02/2020	-	0/0
104	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	479.00	453.59	- -	03/2020	-	0/0
105	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI, TAMIL NADU	12/2017	379.90 -	379.90	100.76	- -	03/2020	-	0/0
106	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI, UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	473.11	- 02/2018	03/2020	25(R3)	0/0
107	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI, ANDHRA PRADESH	03/2018	557.30 -	557.30	174.99	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	275.12	-	-	03/2020	-	0/0
109	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	307.79	-	-	03/2020	-	0/0
110	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	198.05	-	-	03/2020	-	0/0
111	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	551.58	-	-	03/2020	-	0/0
112	4 LANNING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	204.92	-	04/2020	-	0/0
113	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	1,159.07	-	04/2020	-	0/0
114	4 LANNING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 - 1,367.00	1,169.61	1,063.10	-	04/2020	-	0/0
115	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	1,280.27	-	05/2020	-	0/4
116	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	181.78	-	-	06/2020	-	0/0
117	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	442.70	-	07/2020	-	0/0
118	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	-	-	07/2020	-	0/0
119	REHABILITATION AND UPGRADATION TO FOUR LANNING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	449.84	-	07/2020	-	0/0
120	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASTHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	-	08/2020	-	0/0
121	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	234.67	-	09/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
122	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	1,103.88	267.65	- -	09/2020	-	0/0
123	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	131.71	- -	10/2020	-	0/0
124	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	278.01	- 10/2020	10/2020	0(R3)	0/0
125	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	404.94	102.43	- -	10/2020	-	0/0
126	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	36.14	- -	11/2020	-	0/0
127	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	59.22	- -	11/2020	-	0/0
128	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	30.82	- 11/2020	11/2020	0(R3)	0/0
129	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	21.91	- -	11/2020	-	0/0
130	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	-	- -	12/2020	-	0/0
131	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	24.90	- -	12/2020	-	0/0
132	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	1,484.30	45.34	- -	12/2020	-	0/0
133	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	807.00	261.97	- -	12/2020	-	0/0
134	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
135	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	1,339.00	376.15	- -	01/2021	-	1/3
136	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	62.85	- -	01/2021	-	0/0
137	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 1,449.00	1,449.00	1,296.87	- -	01/2021	-	0/0
138	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,702.05	-	- -	01/2021	-	0/0
139	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,166.26	-	- -	02/2021	-	0/0
140	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	565.09	68.81	- -	02/2021	-	0/0
141	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	1,261.05	-	- 03/2021	03/2021	0(R3)	0/0
142	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	24(R3)	0/0
143	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	621.00	303.91	- -	04/2021	-	2/3
144	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	-	- -	04/2021	-	0/0
145	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	4.03	- -	04/2021	-	0/0
146	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	478.74	-	- -	05/2021	-	0/0
147	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	80.87	- 07/2020	06/2021	11(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
148	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	94.03	- 05/2020	06/2021	13(R3)	0/0
149	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	99.10	- 05/2020	06/2021	13(R3)	0/0
150	REHABILITATION AND UPGADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	71.38	- 03/2020	06/2021	15(R3)	0/0
151	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	-	- -	06/2021	-	0/0
152	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,071.61	336.37	- -	07/2021	-	1/4
153	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,064.88	-	- -	07/2021	-	0/4
154	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	326.24	- -	07/2021	-	0/0
155	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	586.73	- -	07/2021	-	0/0
156	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	-	- -	07/2021	-	0/0
157	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	-	- -	07/2021	-	0/0
158	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	931.21	2.55	- -	07/2021	-	0/0
159	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	80.90	- -	07/2021	-	0/0
160	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	15.01	- -	07/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
161	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	120.17	- -	08/2021	-	0/1
162	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	31.00	- -	08/2021	-	0/0
163	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	-	- -	08/2021	-	0/0
164	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,371.02	- 05/2019	11/2021	30(R3)	0/0
165	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 1,684.93	1,117.84	-	- 12/2018	12/2021	36(R3)	0/0
166	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	972.77	-	- 02/2019	02/2022	36(R3)	0/0
167	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	2,450.00	691.88	- 10/2019	-	-	0/0
168	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	960.24	328.34	- -	08/2020	-	0/0
National Highways Development Project									
169	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	390.51	191.77	- -	03/2020	-	0/0
Public Works Dept Of State									
170	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	766.36	666.72	- 09/2019	-	-	0/0
171	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	847.02	1,086.94	- 09/2019	-	-	0/0
172	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	904.82	722.92	- 12/2019	-	-	0/0
	Total		85,697.19 -	86,977.64	29,145.20				6/35

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>URBAN DEVELOPMENT</u>								
	<u>Central Public Works Department</u>								
173	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	14.20	- -	12/2020	-	0/0
174	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	7(R3)	0/0
175	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	348.77	12.00	- -	11/2021	-	0/0
	Total		1,162.77 -	1,162.77	38.76				0/0
	Grand Total		1,20,590.23	1,39,982.87	44,952.45				23/102

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	06/2019 -	12/2019	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
3	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	353.27 -	09/2020 -	09/2020	0/0
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	04/2020 -	12/2020	0/0
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	03/2020 -	12/2020	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	859.86 -	03/2021 -	03/2021	0/0
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	358.89 -	04/2021 -	04/2021	0/0
8	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2021	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR	07/2018	323.19 -	09/2021 -	09/2021	0/0
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	10/2021 -	10/2021	0/0
11	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	264.99 -	11/2021 -	11/2021	0/0
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	02/2022 -	08/2022	0/0
13	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	539.20 -	10/2022 -	10/2022	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
14	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
15	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
16	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Northern Coal Fields Limited</u>					
17	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]NCL,MADHYA PRADESH	07/2019	998.71 -	03/2023 -	03/2023	0/0
	<u>Western Coal Fields Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
18	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
19	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>INFORMATION AND BROADCASTING</u>					
	<u>Central Public Works Department</u>					
20	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	02/2019 -	11/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
21	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC,MAHARASHTRA	12/2016	167.70 -	03/2020 -	03/2020	0/0
	<u>National Film Archive Of India</u>					
22	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA	11/2014	597.41 -	-	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
23	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	03/2021 -	03/2021	0/0
24	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	10/2021	0/0
25	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH	12/2017	1,524.06 -	12/2021 -	12/2021	0/0
26	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
27	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
28	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
29	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
30	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
31	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
32	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 -	07/2022 -	07/2022	0/0
33	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20 -	07/2022 -	07/2022	0/0
34	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
35	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL, JHARKHAND <u>Hindustan Petroleum Corporation Limited</u>	10/2017	221.45 -	10/2022 -	10/2022	0/0
36	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL, MAHARASHTRA	06/2017	249.26 -	06/2020 -	06/2020	0/0
37	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL, JHARKHAND	06/2017	161.50 -	06/2020 -	06/2020	0/0
38	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL, CHHATTISGARH	12/2016	300.00 -	04/2021 -	04/2021	0/0
39	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL, KARNATAKA <u>Indian Oil Corporation Limited</u>	12/2018	854.00 -	12/2022 -	12/2022	0/0
40	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2020	0/0
41	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
42	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 -	06/2020 -	08/2020	0/0
43	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
44	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL, MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
45	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL, HARYANA	01/2019	909.00 -	01/2021 -	01/2021	0/0
46	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
47	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
48	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL, BIHAR	04/2018	522.00 -	03/2021 -	03/2021	0/0
49	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
50	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
51	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
52	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL, ODISHA	11/2018	462.30 -	09/2021 -	09/2021	0/0
53	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
54	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL, ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
55	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
56	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL, TELANGANA	12/2018	611.00 -	04/2022 -	04/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
57	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 -	09/2022 -	09/2022	0/0
58	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
	<u>Indian Strategic Petroleum Reserves Ltd</u>					
59	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
	<u>Oil India Limited</u>					
60	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
61	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	08/2020	0/0
62	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>National Hydro-Electric Power Corporation</u>					
63	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
64	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>National Thermal Power Corporation</u>					
65	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
66	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	12/2018 -	03/2020	0/0
67	DURGAPUR PP-III (2X200 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	11/2018 -	03/2020	0/0
68	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	09/2020	0/0
69	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	11/2020	0/0
70	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
71	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
72	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	07/2019	0/0
73	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	07/2019	0/0
74	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	07/2019	0/0
75	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
76	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	07/2019	0/0
77	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	08/2019	0/0
78	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	08/2019	0/0
79	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 -	08/2019	0/0
80	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	09/2019	0/0
81	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	09/2019	0/0
82	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 -	09/2019	0/0
83	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	09/2019	0/0
84	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 -	09/2019	0/0
85	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	10/2019	0/0
86	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
87	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
88	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	12/2019	0/0
89	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
90	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
91	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	12/2019	0/0
92	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 -	01/2020	0/0
93	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
94	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
95	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	02/2020	0/0
96	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 -	03/2020	0/0
97	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
98	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
99	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE <u>Thdc India Limited</u>	12/2014	5,111.33 -	12/2018 -	12/2020	0/0
101	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH <u>HEAVY INDUSTRY</u> <u>Bharat Heavy Electricals Limited</u>	03/2019	11,089.42 -	09/2023 -	09/2023	0/0
102	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI <u>HEALTH AND FAMILY WELFARE</u> <u>HII Infra Tech Services Limited</u>	08/2016	1,554.00 -	09/2019 -	09/2019	0/0
103	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	06/2020	0/0
104	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	08/2020	0/0
105	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM <u>Hospital Services Consultancy Corporation</u>	05/2017	875.00 -	05/2021 -	10/2021	0/0
106	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	10/2019	0/0
107	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	02/2020	0/0
108	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	02/2020	0/0
109	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	02/2020	0/0
110	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
111	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA <u>Hospital Services Consultancy Corporation Ltd</u>	01/2018	249.01 -	- -	05/2020	0/0
112	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	09/2019	0/0
113	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	10/2019	0/0
114	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	02/2020	0/0
115	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2020	0/0
116	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	10/2020	0/0
117	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
118	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	-	0/0
	<u>National Building Construcion Corporation Ltd</u>					
119	AIIMS BILASPUR - [N21000028]NBCC, HIMACHAL PRADESH	04/2018	1,351.00 -	09/2021 -	09/2021	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
120	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 199.12	03/2019 12/2019	12/2019	0/0
121	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2022	0/0
122	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2022	0/0
123	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR, MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2022	0/0
124	WARDHA-NANDED MAHARASHTRA - [N22000231]CR, MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
125	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
126	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR, MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2023	0/0
127	DAUND - MANMAD (236 KM) - [N22000360]CR, MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
128	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
129	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR, MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
130	PUNE-NASIK (265 KM) - [N22000354]CR, MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
131	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR, MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
132	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR, MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
133	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-	0/0
	<u>Container Corporation Of India</u>					
134	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2019	0/0
135	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
136	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	02/2020	0/0
137	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020	0/0
138	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	03/2019 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
139	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
140	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
141	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
142	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
143	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	<u>East Central Railways</u>					
144	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 726.31	- -	10/2019	0/0
145	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
146	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 367.17	- -	01/2020	0/0
147	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	03/2012 -	03/2020	0/0
148	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	03/2020	0/0
149	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012 -	03/2020	0/0
150	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
151	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	- -	03/2021	0/0
152	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	- -	03/2021	0/0
153	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	03/2021	0/0
154	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2021	0/0
155	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
156	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	- -	12/2021	0/0
157	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	- -	03/2022	0/0
158	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
159	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	03/2020 -	03/2022	0/0
160	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	03/2021 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
161	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	03/2021 -	03/2022	0/0
162	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	- -	02/2023	0/0
163	HAJIPUR-SUGAU LI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- -	03/2023	0/0
164	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	03/2023	0/0
165	ARARIA-SUPAU LI (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	- 03/2023	03/2023	0/0
166	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	03/2024	0/0
167	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	03/2024	0/0
168	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	03/2024	0/0
169	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
170	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	03/2024	0/0
171	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	03/2024	0/0
172	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	03/2024	0/0
173	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
174	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	03/2024	0/0
175	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	03/2024	0/0
176	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
177	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR	07/2004	599.63 674.00	12/2007 -	-	0/0
178	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 546.71	07/2014 -	-	0/0
	<u>East Coast Railway</u>					
179	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2021	0/0
180	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	03/2022	0/0
181	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	03/2022	0/0
182	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2022	0/0
183	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
184	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	03/2023	0/0
185	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 -	03/2023	0/0
186	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2022 -	03/2023	0/0
187	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	03/2024	0/0
188	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2022 -	03/2025	0/0
	<u>Eastern Railways</u>					
189	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
190	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2020	0/0
191	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2020	0/0
192	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
193	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2021	0/0
194	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	09/2021	0/0
195	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
196	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
197	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
198	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
199	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
200	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
201	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
202	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR -CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
203	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
204	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
205	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
206	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
207	BARIARPIUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
208	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
209	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
210	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
211	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
212	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
213	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
214	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
215	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
	<u>Indian Railway Construction Company Limited</u>					
216	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	06/2023	0/0
	<u>Kolkata Metro Rail Corporation Limited</u>					
217	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
218	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2021	0/0
219	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 918.53	03/2014 03/2021	03/2021	0/0
220	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
221	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
222	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
223	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
224	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	03/2015	0/0
225	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
226	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
227	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
228	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	03/2011 -	03/2020	0/0
229	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	03/2019 -	03/2020	0/0
230	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	03/2019 -	03/2020	0/0
231	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
232	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
233	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
234	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	03/2019 -	03/2020	0/0
235	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
236	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
237	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	12/2008 -	03/2021	0/0
238	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
239	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	03/2021	0/0
240	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
241	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	10/2021	0/0
242	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 4,968.00	03/2014 03/2022	03/2022	0/0
243	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- 03/2022	03/2022	0/0
244	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- 03/2022	03/2022	0/0
245	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-	0/0
246	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	-	0/0
247	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
248	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
<u>North Eastern Railway</u>						
249	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019	0/0
250	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
251	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	01/2020	0/0
252	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	06/2020	0/0
253	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
254	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
255	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
256	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2022	0/0
257	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
258	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
259	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
260	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
261	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
262	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
263	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
264	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
265	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
<u>North Western Railway</u>						
266	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2019	0/0
267	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	05/2020	0/0
268	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	02/2019 -	05/2020	0/0
269	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2020	0/0
270	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2020	0/0
271	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	03/2021	0/0
272	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
273	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
274	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
275	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
276	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	06/2020	0/0
277	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	03/2021	0/0
278	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	03/2021	0/0
279	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	- -	03/2022	0/0
280	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	06/2022	0/0
281	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	03/2023	0/0
282	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
283	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
284	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0
285	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
286	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
	<u>National High Speed Rail Corporation Limited</u>					
287	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
288	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	03/2020 -	03/2020	0/0
289	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
290	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
291	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
292	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2020	0/0
293	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	06/2020	0/0
294	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
295	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2020	0/0
296	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
297	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	03/2021	0/0
298	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
299	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
300	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	12/2021	0/0
301	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
302	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2021	0/0
303	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
304	VIJAYWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
305	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
306	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
307	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
308	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2024	0/0
309	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
310	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
311	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
312	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
313	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2026	0/0
314	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2026	0/0
<u>Railway Electrification</u>						
315	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
316	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
317	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
318	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2023	0/0
319	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2023	0/0
320	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2023	0/0
321	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
322	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
323	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
324	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
325	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
326	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,413.76	- 10/2019	10/2019	0/0
327	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	12/2019 10/2019	10/2019	0/0
328	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.00	12/2021 12/2021	12/2021	0/0
<u>South Eastern Railway</u>						
329	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 08/2018	12/2019	0/0
330	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	12/2018 12/2018	06/2020	0/0
331	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 -	06/2020	0/0
332	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2021	0/0
333	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- 03/2025	03/2025	0/0
334	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 03/2030	03/2030	0/0
335	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
336	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR	08/2010	400.00 -	03/2014 -	-	0/0
337	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
338	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	-	0/0
<u>South Western Railway</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
339	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	03/2020	0/0
340	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	03/2020	0/0
341	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	03/2021	0/0
342	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
343	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
344	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
345	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
346	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
347	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
348	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
349	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
350	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
351	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
352	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	12/2024	0/0
<u>Southern Railway</u>						
353	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2019	0/0
354	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2020	0/0
355	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
356	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- -	03/2020	0/0
357	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
358	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2021	0/0
359	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2021	0/0
360	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
361	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
362	ANGAMALI-SABARIMALA (N.L.)(SR) - [N220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-	0/0
363	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
364	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
365	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
366	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
367	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
368	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
369	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-	0/0
370	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-	0/0
371	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
372	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-	0/0
373	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	- 06/2022	-	0/0
374	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-	0/0
375	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
376	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
377	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
<u>Western Railway</u>						
378	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	03/2017	0/0
379	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	03/2019 03/2020	03/2020	0/0
380	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	03/2020 03/2021	03/2021	0/0
381	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	- -	03/2021	0/0
382	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 03/2021	03/2021	0/0
383	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	03/2020 03/2021	03/2021	0/0
384	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 06/2021	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
385	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 321.62	03/2012 03/2022	03/2022	0/0
386	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2022	03/2022	0/0
387	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 858.56	03/2019 03/2022	03/2022	0/0
388	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	1,037.15 1,037.15	03/2021 03/2022	03/2022	0/0
389	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	3,503.69 3,338.15	03/2022 03/2023	03/2023	0/0
390	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
391	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR, GUJARAT	03/2017	243.60 -	- -	-	0/0
392	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR, MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
393	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR, MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
394	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR, GUJARAT	03/2012	248.26 -	- -	-	0/0
395	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR, GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
396	MAJALGAON TO KAIJ - [N24001036]MORTH, MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019	0/0
397	WIDENING WITH PS AND STRONG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	09/2019	0/0
398	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH, UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	09/2019	0/0
399	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH, ODISHA	08/2013	171.96 172.00	06/2016 -	11/2019	0/0
400	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH, UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
401	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2-LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH, UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
402	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH, UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
403	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH, A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
404	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH, A & N ISLANDS	11/2017	257.34 -	11/2019 -	11/2019	0/0
405	BHADGAON TO CHALISGAON - [N24001047]MORTH, MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
406	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	12/2019	0/0
407	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
408	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
409	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
410	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2019	0/0
411	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	12/2019	0/0
412	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	12/2019	0/0
413	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2019	0/0
414	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	12/2019	0/0
415	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0
416	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	12/2019	0/0
417	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	12/2019	0/0
418	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	12/2019	0/0
419	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	12/2019	0/0
420	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	12/2019	0/0
421	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	12/2019	0/0
422	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2019	0/0
423	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	12/2019	0/0
424	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2019	0/0
425	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA	02/2018	355.99 355.99	12/2019 -	12/2019	0/0
426	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
427	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
428	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	06/2020	0/0
429	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	08/2020	0/0
430	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MORTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 -	03/2021	0/0
431	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
432	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
433	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
434	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
435	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
436	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
437	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
438	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
439	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
440	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
441	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
442	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
443	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
444	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
445	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
446	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
447	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
448	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
449	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
450	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
451	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
452	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
453	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
454	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
455	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
456	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
457	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
458	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
459	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
460	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
461	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
462	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
463	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
464	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
465	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
466	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
467	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
468	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
469	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
470	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
471	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
472	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
473	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
474	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
475	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
476	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
477	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
478	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
479	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
480	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
481	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
482	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
483	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
484	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
485	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
486	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
487	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MORTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- -	-	0/0
488	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MORTH,RAJASTHAN	03/2019	178.13 -	- -	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
489	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019	0/0
490	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019	0/0
491	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019	0/0
492	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019	0/0
493	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019	0/0
494	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
495	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019	0/0
496	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019	0/0
497	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019	0/0
498	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	12/2019	0/0
499	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	- 02/2018	02/2021	0/0
500	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	- 02/2018	02/2021	0/0
501	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	- 04/2019	04/2022	0/0
502	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	- 04/2019	04/2022	0/0
503	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0
504	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-	0/0
505	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-	0/0
506	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-	0/0
507	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-	0/0
508	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-	0/0
509	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
510	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-	0/0
511	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-	0/0
512	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
513	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
514	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
515	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
516	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
517	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0
<u>National Highways Authority Of India</u>						
518	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	06/2019	0/0
519	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	08/2019	0/0
520	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	08/2019	0/0
521	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013	0/0
522	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 408.77	11/2008 07/2011	01/2014	0/0
523	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015	0/0
524	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
525	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018	0/0
526	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018	0/0
527	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019	0/0
528	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 315.00	- 03/2020	03/2019	0/0
529	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
530	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019	0/0
531	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI, JHARKHAND	03/2017	239.68 -	03/2020 -	06/2019	0/0
532	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
533	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019	0/0
534	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 -	03/2019 -	07/2019	0/0
535	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	07/2019	0/0
536	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 340.14	04/2009 03/2011	08/2019	0/0
537	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	01/2019 -	08/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
538	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0
539	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	09/2016 -	09/2019	0/0
540	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	06/2016 -	09/2019	0/0
541	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	07/2018 -	09/2019	0/0
542	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 1,240.03	06/2019 12/2016	09/2019	0/0
543	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
544	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
545	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
546	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 2,525.80	09/2019 03/2020	09/2019	0/0
547	FOUR LANNING OF CHICHA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	09/2019	0/0
548	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
549	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	09/2019	0/0
550	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	09/2019	0/0
551	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	09/2019	0/0
552	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	09/2019	0/0
553	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	10/2019	0/0
554	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	10/2019	0/0
555	TWO LANING WITH PAVED SHOULDER OF KARAU - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 09/2014	10/2019	0/0
556	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	10/2019	0/0
557	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	10/2019	0/0
558	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 622.00	- -	10/2019	0/0
559	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 622.00	- -	10/2019	0/0
560	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 10/2019	10/2019	0/0
561	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	10/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
562	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- 02/2016	10/2019	0/0
563	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 10/2019	10/2019	0/0
564	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	10/2019	0/0
565	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	11/2019	0/0
566	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	01/2018 12/2018	11/2019	0/0
567	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	11/2019	0/0
568	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	- 05/2017	11/2019	0/0
569	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 11/2019	11/2019	0/0
570	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	11/2019	0/0
571	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	11/2019	0/0
572	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	11/2019	0/0
573	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	11/2019	0/0
574	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	11/2019	0/0
575	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	11/2019	0/0
576	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	11/2019	0/0
577	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	11/2019	0/0
578	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019	0/0
579	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2019	0/0
580	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2019	0/0
581	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2019	0/0
582	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2019	0/0
583	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2019	0/0
584	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	12/2019	0/0
585	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	11/2018 07/2019	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
586	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	12/2017 06/2020	12/2019	0/0
587	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
588	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 03/2018	12/2019	0/0
589	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	12/2019	0/0
590	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	12/2019	0/0
591	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- 12/2017	12/2019	0/0
592	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	12/2019	0/0
593	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	12/2019	0/0
594	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	01/2020	0/0
595	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	01/2020	0/0
596	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	01/2020	0/0
597	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	01/2020	0/0
598	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
599	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	01/2020	0/0
600	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	01/2020	0/0
601	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 149.90	- -	01/2020	0/0
602	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	02/2020	0/0
603	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
604	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
605	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 12/2019	02/2020	0/0
606	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	02/2020	0/0
607	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	03/2020	0/0
608	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2020	0/0
609	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	11/2011 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
610	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2020	0/0
611	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	03/2020	0/0
612	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 598.13	04/2018 03/2020	03/2020	0/0
613	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2020	0/0
614	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
615	4-LANNING OF BODHRE-DHULE SECTION (KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
616	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
617	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
618	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2020	0/0
619	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	- 02/2018	03/2020	0/0
620	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	03/2020	0/0
621	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	03/2020	0/0
622	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	03/2020	0/0
623	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	03/2020	0/0
624	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	03/2020	0/0
625	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	04/2020	0/0
626	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	07/2018 -	04/2020	0/0
627	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	06/2018 -	04/2020	0/0
628	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
629	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
630	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	04/2020	0/0
631	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
632	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
633	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 03/2019	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
634	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	05/2020	0/0
635	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	05/2020	0/0
636	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 11/2017	05/2020	0/0
637	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
638	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	03/2020 11/2017	05/2020	0/0
639	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
640	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	05/2020	0/0
641	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	06/2020	0/0
642	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	06/2020	0/0
643	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	06/2020	0/0
644	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	06/2018 -	06/2020	0/0
645	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	06/2018 -	06/2020	0/0
646	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
647	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
648	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	06/2020	0/0
649	FOUR LANING OF UDHAMR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,273.00	12/2018 12/2019	07/2020	0/0
650	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 07/2020	07/2020	0/0
651	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
652	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
653	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	07/2020	0/0
654	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	07/2020	0/0
655	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
656	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	08/2020	0/0
657	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 01/2019	08/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
658	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	03/2019 03/2017	08/2020	0/0
659	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
660	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
661	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
662	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	08/2020	0/0
663	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	08/2020	0/0
664	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 12/2019	09/2020	0/0
665	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 04/2019	09/2020	0/0
666	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
667	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	09/2020	0/0
668	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
669	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0
670	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- 10/2020	10/2020	0/0
671	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	- -	10/2020	0/0
672	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	11/2020	0/0
673	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
674	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	03/2017 05/2018	11/2020	0/0
675	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
676	FOUR LANINIG OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	11/2020	0/0
677	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	11/2020	0/0
678	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 11/2020	11/2020	0/0
679	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	11/2020	0/0
680	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	12/2020	0/0
681	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
682	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
683	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 12/2020	12/2020	0/0
684	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 12/2020	12/2020	0/0
685	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	08/2019 -	12/2020	0/0
686	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2020	0/0
687	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	12/2020	0/0
688	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	12/2020	0/0
689	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	12/2020	0/0
690	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	01/2021	0/0
691	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	01/2021	0/0
692	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	01/2021	0/0
693	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 1,449.00	- -	01/2021	0/0
694	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	01/2021	0/0
695	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
696	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	02/2021	0/0
697	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
698	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
699	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2021	0/0
700	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- 03/2021	03/2021	0/0
701	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2019	03/2021	0/0
702	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 04/2021	04/2021	0/0
703	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	04/2021	0/0
704	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
705	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
706	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	05/2021	0/0
707	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 11/2020	06/2021	0/0
708	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- 07/2020	06/2021	0/0
709	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- 05/2020	06/2021	0/0
710	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- 05/2020	06/2021	0/0
711	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- 03/2020	06/2021	0/0
712	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
713	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
714	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	07/2021	0/0
715	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	07/2021	0/0
716	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
717	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	- -	07/2021	0/0
718	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
719	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
720	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
721	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	08/2021	0/0
722	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
723	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	- 05/2019	11/2021	0/0
724	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 1,684.93	- 12/2018	12/2021	0/0
725	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
726	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	- 02/2019	02/2022	0/0
727	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 456.92	02/2009 -	-	0/0
728	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 -	-	0/0
729	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
730	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 2,519.00	06/2015 -	-	0/0
731	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
732	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
733	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
734	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
735	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
736	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
737	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
738	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
739	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
740	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
741	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
742	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
743	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
744	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
745	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
746	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
747	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
748	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
749	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
750	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
751	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
752	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
753	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
754	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
755	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
756	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
757	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
758	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
759	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
760	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-	0/0
761	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
762	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
763	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
764	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-	0/0
765	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
766	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0
767	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
768	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
769	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
770	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
771	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-	0/0
772	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
773	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
774	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
775	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
776	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
777	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
778	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-	0/0
779	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
780	MEERUT-BULANDSHAHR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	-	-	0/0
781	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
782	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
783	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
784	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	-	-	0/0
785	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	-	-	0/0
786	SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	-	-	0/0
787	BALANCE WORK OF 4 LANING OF GORAKHPUR - GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
788	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A (NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
789	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI, DELHI	09/2015	771.18 -	-	-	0/0
790	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
791	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	-	-	0/0
792	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI, MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
793	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI, MADHYA PRADESH	12/2017	950.27 -	-	-	0/0
794	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI, BIHAR	12/2017	2,598.00 -	-	-	0/0
795	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA	12/2017	417.51 -	-	-	0/0
796	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI, ANDHRA PRADESH	12/2017	357.00 -	-	-	0/0
797	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	-	-	0/0
798	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	-	-	0/0
799	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	-	-	0/0
800	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
801	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
802	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
803	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
804	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
805	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
806	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
807	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 929.89	- -	-	0/0
808	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
809	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
810	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
811	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-I) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
812	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	- 10/2019	-	0/0
813	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
814	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
815	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
816	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
817	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
818	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
819	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
820	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
821	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
822	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
823	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
824	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
825	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
826	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
827	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
828	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
829	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
830	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
831	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
832	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
833	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
834	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
835	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 149.90	- -	-	0/0
836	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
837	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-	0/0
838	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
839	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
840	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
841	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-	0/0
842	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-	0/0
843	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-	0/0
844	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
845	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	-	0/0
846	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-	0/0
847	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	08/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
848	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	08/2020	0/0
	<u>National Highways Development Project</u>					
849	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	09/2019	0/0
850	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	10/2019	0/0
851	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	01/2020 -	01/2020	0/0
852	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	02/2020	0/0
853	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	03/2020	0/0
854	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2020	0/0
855	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
	<u>Public Works Dept Of State</u>					
856	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017	0/0
857	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	08/2017 -	08/2019	0/0
858	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
859	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0
860	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019	0/0
861	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - [N24001147]PWD,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019	0/0
862	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019	0/0
863	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	05/2019 -	08/2019	0/0
864	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	09/2019	0/0
865	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	09/2019	0/0
866	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAL-CHAN - [N24000876]PWD,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	09/2019	0/0
867	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	03/2019 03/2020	09/2019	0/0
868	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	05/2019 09/2019	09/2019	0/0
869	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
870	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	09/2019	0/0
871	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	09/2019	0/0
872	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]PWD,NAGALAND	11/2016	336.25 369.96	09/2019 -	09/2019	0/0
873	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB	10/2017	1,069.59 -	10/2019 -	10/2019	0/0
874	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]PWD,TELANGANA	01/2017	196.52 -	10/2019 -	10/2019	0/0
875	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD,TELANGANA	01/2017	605.08 -	10/2019 -	10/2019	0/0
876	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD,BIHAR	11/2016	230.34 -	10/2019 -	10/2019	0/0
877	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]PWD,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	10/2019	0/0
878	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]PWD,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	10/2019	0/0
879	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL	03/2016	271.17 291.20	11/2018 11/2019	11/2019	0/0
880	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	02/2018 -	11/2019	0/0
881	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	11/2019	0/0
882	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	02/2018 -	11/2019	0/0
883	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	11/2019	0/0
884	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	11/2019	0/0
885	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	11/2019	0/0
886	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	02/2018 -	11/2019	0/0
887	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	01/2019 -	11/2019	0/0
888	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	06/2019 -	11/2019	0/0
889	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	11/2019	0/0
890	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD,TELANGANA	02/2018	294.13 -	11/2019 -	11/2019	0/0
891	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD,TELANGANA	02/2018	220.28 -	11/2019 -	11/2019	0/0
892	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
893	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	03/2018 -	11/2019	0/0
894	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	12/2019	0/0
895	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	12/2019	0/0
896	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	12/2019	0/0
897	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	08/2013 -	12/2019	0/0
898	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	02/2013 09/2017	12/2019	0/0
899	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	12/2019	0/0
900	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	12/2019	0/0
901	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	02/2019 -	12/2019	0/0
902	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	03/2019 -	12/2019	0/0
903	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]PWD,TELANGANA	01/2017	283.00 -	12/2019 -	12/2019	0/0
904	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	05/2019 -	12/2019	0/0
905	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD,TELANGANA	01/2018	230.03 -	12/2019 -	12/2019	0/0
906	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA	03/2018	192.67 -	07/2019 -	12/2019	0/0
907	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	02/2014 -	12/2019	0/0
908	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	09/2014 -	12/2019	0/0
909	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]PWD,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	12/2019	0/0
910	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	01/2020	0/0
911	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	01/2020	0/0
912	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	01/2020	0/0
913	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	02/2020	0/0
914	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	02/2020	0/0
915	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]PWD,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	02/2020	0/0
916	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
917	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	03/2020	0/0
918	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]PWD,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2020	0/0
919	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	04/2020	0/0
920	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]PWD,TELANGANA	02/2018	426.52 -	04/2020 -	04/2020	0/0
921	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]PWD,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	04/2020	0/0
922	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	05/2020	0/0
923	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]PWD,TELANGANA	01/2018	283.15 -	05/2020 -	05/2020	0/0
924	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	05/2018 -	05/2020	0/0
925	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	06/2020	0/0
926	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	06/2020	0/0
927	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	06/2020	0/0
928	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	08/2018 -	06/2020	0/0
929	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB	03/2018	173.24 -	06/2020 -	06/2020	0/0
930	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD,TELANGANA	02/2018	206.13 -	06/2020 -	06/2020	0/0
931	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD,JHARKHAND	03/2018	212.99 -	06/2020 -	06/2020	0/0
932	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	07/2020	0/0
933	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB	03/2018	322.48 -	07/2020 -	07/2020	0/0
934	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD,TELANGANA	03/2018	626.76 -	07/2020 -	07/2020	0/0
935	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD,PUNJAB	03/2018	293.10 -	08/2020 -	08/2020	0/0
936	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
937	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
938	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]PWD,TRIPURA	10/2016	171.90 -	08/2020 -	08/2020	0/0
939	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN - [N24001208]PWD,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	08/2020	0/0
940	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	09/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
941	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD,TELANGANA	03/2018	322.81 -	09/2020 -	09/2020	0/0
942	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]PWD,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	09/2020	0/0
943	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]PWD,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	10/2020	0/0
944	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	11/2020	0/0
945	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]PWD,PUNJAB	03/2018	170.57 -	11/2020 -	11/2020	0/0
946	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]PWD,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
947	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]PWD,NAGALAND	03/2017	217.35 -	11/2020 -	11/2020	0/0
948	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	08/2016 -	12/2020	0/0
949	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]PWD,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020	0/0
950	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]PWD,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020	0/0
951	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
952	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]PWD,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021	0/0
953	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	08/2021	0/0
954	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL	06/2016	236.78 263.26	08/2019 -	08/2021	0/0
955	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]PWD,ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
956	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]PWD,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
957	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
958	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
959	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
960	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
961	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 06/2018	-	0/0
962	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 203.26	08/2013 -	-	0/0
963	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
964	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
965	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
966	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- 09/2019	-	0/0
967	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- 09/2019	-	0/0
968	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- 12/2019	-	0/0
969	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
970	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
971	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
972	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 307.47	02/2018 -	-	0/0
973	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
974	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
975	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
976	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
977	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
978	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
979	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
980	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-	0/0
981	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	03/2019 07/2019	-	0/0
982	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 386.19	05/2019 -	-	0/0
983	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA	01/2019	193.19 -	- -	-	0/0
984	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR	03/2018	153.24 -	- -	-	0/0
985	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
986	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
987	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
988	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
989	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
990	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
991	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
992	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
993	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
994	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
995	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
996	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
997	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
998	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
999	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
1000	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]PWD,ARUNACHAL PRADESH	11/2016	243.89 -	- -	-	0/0
1001	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]PWD,BIHAR	02/2019	2,926.42 -	- -	-	0/0
1002	REHABILITATION AND UPGRADEMENT OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]PWD,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0
1003	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]PWD,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Inland Waterways Authority Of India</u>					
1004	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	4,200.00 5,369.18	03/2023 -	03/2023	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
1005	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 -	10/2018 09/2019	09/2019	0/0
	<u>Department Of Telecommunication</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1006	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00	07/2015	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
1007	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26	06/2017	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
1008	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00	12/2018	07/2020	0/0
	<u>Bangalore Metro Rail Corporation Limited</u>					
1009	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14	02/2019	03/2020	0/0
	<u>Central Public Works Department</u>					
1010	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013	10/2019	0/0
1011	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90	11/2019	11/2019	0/0
1012	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	07/2019 12/2019	02/2020	0/0
1013	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72	03/2020	03/2020	0/0
1014	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56	05/2020	05/2020	0/0
1015	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31	02/2020	09/2020	0/0
1016	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017	10/2020	0/0
1017	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00	-	12/2020	0/0
1018	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00	- 08/2020	03/2021	0/0
1019	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77	-	11/2021	0/0
1020	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79	03/2022	03/2022	0/0
1021	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	12/2015	-	0/0
1022	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00	06/2019	-	0/0
1023	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20	04/2018	-	0/0
1024	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72	-	-	0/0
	<u>Hindustan Steelwork Construction Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1025	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1026	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1027	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
1028	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1029	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
1030	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1031	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
1032	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1033	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
1034	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1035	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1036	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1037	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0
1038	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1039	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1040	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1041	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1042	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1043	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 01/2022	01/2022	0/0
1044	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1045	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1046	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1047	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1048	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
1049	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1050	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2019	0/0
	Total		11,41,600.62 -			0/0
	Grand Total		11,41,600.62			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021
	Total		1,186.64 -	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
2	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	350.36	02/2020 -	09/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,820.56	12/2020 -	08/2020
4	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL [N16000252]	5/2016	664.00 -	664.00	600.82	12/2020 -	02/2020
5	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	150.02	06/2020 -	03/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY [N16000308]	8/2017	315.00 -	315.00	110.59	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	189.41	09/2022 -	06/2021
8	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	85.86	04/2021 -	04/2020
	Total		8,274.58 -	9,275.58	3,307.62		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
9	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	674.45	03/2024 -	03/2022
	<u>East Central Railways</u>						
10	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	164.09	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
11	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	654.38	03/2022 -	03/2020
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	612.00	257.73	12/2021 -	03/2020

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North Eastern Railway</u>						
13	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42 -	1,295.42	328.56	03/2022 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
14	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
	Total		8,829.49 -	8,788.90	2,079.40		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
15	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932	1/2017	319.28 -	319.28	103.79	08/2017 03/2020	08/2019
16	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	87.58	09/2017 03/2020	09/2019
17	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	1/2017	576.48 -	576.48	196.46	01/2018 03/2020	01/2020
18	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968	11/2016	376.25 -	376.25	189.59	08/2017 03/2020	08/2019
19	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43 -	429.43	195.88	11/2017 03/2020	11/2019
20	PARSHURAM GHAT TO ARAWALI - [N24001133	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
	<u>National Highways Authority Of India</u>						
21	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019
22	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019
23	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02	157.49	-	03/2020 -	02/2020
24	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19	254.00	248.60	03/2020 -	09/2019
25	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79	552.90	480.73	03/2020 -	09/2019
26	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32	503.10	1.15	03/2020 -	11/2019
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50	172.16	117.09	03/2020 -	09/2019
28	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	690.00	04/2020 -	11/2019

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Public Works Dept Of State</u>						
29	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904	1/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019
	Total		7,921.73 -	9,001.16	5,156.23		
	Grand Total		26,212.44	27,269.46	10,660.80		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
2	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
3	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.00	09/2021 -	09/2021
4	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
5	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	.42	11/2021 -	11/2021
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
	Total		5,033.68 -	5,033.82	694.69		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	187.12	03/2020 -	03/2020
11	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	163.23	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
12	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	315.31	03/2022 -	03/2022
13	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	82.01	03/2022 -	03/2022
14	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
15	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.13	03/2024 -	03/2024
16	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
17	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
	<u>Mahanadi Coal Fields Limited</u>						
18	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,549.76	03/2026 -	03/2026
19	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	440.13	03/2021 -	03/2021
20	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,113.66	03/2029 -	03/2029
21	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	83.20	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
22	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.88	09/2019 -	09/2019
23	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	7,203.71	11/2021 -	11/2021
24	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
25	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	265.78	03/2021 -	03/2021
26	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
27	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
28	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
	<u>Singareni Colliers Company Limited</u>						
29	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
30	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023
31	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	103.99	03/2021 -	03/2021
32	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
33	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.02	03/2023 -	03/2023
34	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
35	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
37	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	116.09	03/2021 -	03/2021
38	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,881.14	03/2023 -	03/2023
39	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,044.21	03/2023 -	03/2023
40	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	67.41	03/2020 -	03/2020
41	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.39	03/2021 -	03/2021
42	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
43	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	82.91	03/2020 -	03/2020
44	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	97.29	03/2022 -	03/2022
45	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
46	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.10	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
47	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	182.51	03/2020 -	03/2020
48	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	42.94	03/2021 -	03/2021
49	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	146.45	03/2021 -	03/2021
50	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
51	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	50.56	03/2022 -	03/2022
52	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.93	03/2020 -	03/2020
53	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	154.25	03/2021 -	03/2021
54	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
55	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	235.29	03/2022 -	03/2022
56	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	20.30	03/2022 -	03/2022
57	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
58	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	268.57	03/2025 -	03/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	200.77	03/2021 -	03/2021
60	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	-	03/2026 -	03/2026
61	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020
62	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	126.12	03/2023 -	03/2023
63	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
	Total		75,877.66 -	76,100.20	19,864.47		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	106.43	11/2019 -	11/2019
65	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	113.95	11/2019 -	11/2019
66	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	125.27	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
67	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	175.19	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	520.84		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>National Building Construcion Corporation Ltd</u>						
68	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,351.00	137.87	09/2021 -	09/2021
	Total		1,351.00 -	1,351.00	137.87		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
69	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>INFORMATION AND BROADCASTING</u>						
	<u>National Building Construcion Corporation Ltd</u>						
70	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]	12/2016	167.70	167.70	-	03/2020	03/2020
	Total		167.70	167.70	.00		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
71	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00	5,540.00	102.61	04/2021	04/2021
72	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00	483.00	.30	04/2021	04/2021
73	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00	534.00	318.13	01/2020	01/2020
74	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00	355.00	31.92	11/2020	11/2020
	Total		6,912.00	6,912.00	452.96		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
75	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00	1,097.54	698.76	10/2018	12/2019
76	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55	248.55	22.55	06/2022	06/2022
77	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06	1,524.06	13.47	12/2021	12/2021
78	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20	580.20	34.84	02/2021	02/2021
79	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26	206.26	.53	03/2021	03/2021
80	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00	11,130.00	15.17	03/2023	03/2023
81	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00	750.00	34.73	12/2020	12/2020
82	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64	282.64	121.12	08/2020	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
83	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	1,014.00	02/2020 10/2020	10/2020
84	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	155.28	12/2019 -	12/2019
85	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	3,588.88	08/2018 11/2019	11/2019
	<u>Chennai Petroleum Corporation Limited</u>						
86	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	951.55	12/2019 -	12/2019
87	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	123.76	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
88	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
89	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,271.82	12/2020 -	12/2020
90	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,019.25	12/2020 -	12/2020
91	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,229.31	12/2020 -	12/2020
92	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	173.41	12/2020 -	12/2020
93	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	1.19	08/2020 09/2020	09/2020
94	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECT - [N16000349]	9/2018	225.54 -	225.54	-	02/2021 -	02/2021
95	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1,123.85	12/2021 -	12/2021
96	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	43.56	10/2022 -	10/2022
97	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	48.29	10/2022 -	10/2022
98	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	28.80	07/2022 -	07/2022
99	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	65.14	10/2022 -	10/2022
100	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	49.97	07/2022 -	07/2022
101	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	123.35	04/2022 -	04/2022
102	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,396.84	12/2020 -	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Hindustan Petroleum Corporation Limited</u>						
103	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	703.45	10/2014 08/2019	08/2019
104	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	376.97	09/2019 -	09/2019
105	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021
106	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
107	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
108	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	6.94	06/2022 -	06/2022
109	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	118.06	11/2019 -	11/2019
110	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
111	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	67.92	11/2020 -	11/2020
112	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	837.13	03/2021 -	03/2021
113	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,592.90	03/2020 -	03/2020
114	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,460.00	06/2020 -	06/2020
115	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	5,887.49	07/2020 -	07/2020
	<u>Indian Oil Corporation Limited</u>						
116	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
117	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	602.02	10/2019 -	10/2019
118	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020
119	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	.71	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
120	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,569.01	09/2019 -	09/2019
121	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	7.75	02/2020 -	02/2020
122	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	531.40	09/2019 -	09/2019
123	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	13.88	03/2021 -	03/2021
124	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,872.71	09/2019 -	09/2019
125	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
126	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	376.04	09/2019 -	09/2019
127	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	12.28	06/2020 -	06/2020
128	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	108.00	07/2020 -	07/2020
129	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	41.42	01/2021 -	01/2021
130	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
131	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
132	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
133	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	941.98	08/2021 -	08/2021
134	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
135	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
136	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	284.31	08/2021 -	08/2021
137	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
138	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	139.25	09/2019 -	09/2019
139	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	14.12	02/2020 -	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
140	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	13.11	01/2021 -	01/2021
141	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
142	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
143	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	325.42	10/2019 -	10/2019
144	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	9.08	10/2021 -	10/2021
145	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	142.71	03/2021 -	03/2021
146	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	142.67	08/2020 -	08/2020
147	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	178.05	02/2020 -	02/2020
148	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	242.10	10/2021 -	10/2021
149	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	7.82	01/2021 -	01/2021
150	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	96.35	12/2021 -	12/2021
151	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,526.40	11/2019 -	11/2019
152	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	844.09	12/2020 -	12/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
153	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	154.03	03/2019 09/2019	09/2019
154	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	726.57	12/2019 07/2020	07/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
155	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019
156	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019
157	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,314.42	05/2013 12/2019	12/2019
158	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,340.39	12/2017 03/2020	03/2020
159	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	428.31	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
160	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	275.27	05/2021 -	05/2021
161	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	440.41	12/2019 -	12/2019
162	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,475.92	2,770.16	05/2021 12/2021	12/2021
163	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	912.74	11/2019 -	11/2019
164	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	463.01	11/2019 -	11/2019
165	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	565.15	442.18	11/2019 03/2020	03/2020
166	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	407.45	234.24	09/2018 09/2019	09/2019
167	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	371.09	03/2026 -	03/2026
168	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	157.81	05/2020 -	05/2020
169	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	340.16	03/2023 03/2022	03/2022
170	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]	11/2015	650.82 -	650.82	394.21	03/2019 05/2020	05/2020
171	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]	10/2018	156.67 -	156.67	-	03/2021 -	03/2021
172	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	-	12/2020 -	12/2020
173	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,216.11	04/2018 05/2020	05/2020
174	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,908.01	03/2015 12/2019	12/2019
175	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020
176	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,784.40	05/2019 10/2019	10/2019
Oil India Limited							
177	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	87.00	10/2020 -	10/2020
178	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	173.61	12/2019 -	12/2019
179	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CCGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	3.30	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,66,232.36	1,70,017.90	68,287.22		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
180	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55	12,865.92	12,045.10	01/2018 03/2020	03/2020
181	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89	12,176.28	9,749.00	02/2017 06/2020	06/2020
182	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98	10,598.98	5,382.09	11/2020 06/2021	06/2021
183	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51	11,148.86	8,449.85	01/2020	01/2020
184	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00	12,739.82	12,349.43	10/2017 03/2020	03/2020
185	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97	21,312.11	16,331.92	10/2011 08/2021	08/2021
186	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60	17,304.00	13,716.26	05/2018 12/2021	12/2021
187	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48	5,867.38	4,155.88	03/2013 12/2020	12/2020
188	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84	1,592.34	481.22	09/2019 02/2022	02/2022
189	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98	9,188.98	6,397.93	07/2019 06/2020	06/2020
190	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00	18,668.00	1,904.30	03/2023	03/2023
191	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00	349.00	125.00	11/2020	11/2020
192	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44	587.44	250.00	09/2020	09/2020
193	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00	3,004.00	1,610.00	11/2019	11/2019
	<u>North East Electric Power Corporation</u>						
194	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	7,927.34	7,516.58	12/2009 10/2019	10/2019
	<u>Power Grid Corporation Of India Limited</u>						
195	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37	14,733.37	7,922.74	11/2019	11/2019
196	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72	283.72	187.60	11/2019	11/2019
197	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95	379.95	52.63	12/2019	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
198	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020
199	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020
200	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020
201	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020
202	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	116.76	02/2020 -	02/2020
	<u>Satluj Jal Vidyut Nigam Limited</u>						
203	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	777.63	01/2024 -	01/2024
204	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	255.15	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
205	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	306.71	09/2020 -	09/2020
206	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	511.64	09/2023 -	09/2023
	Total		1,64,750.63 -	1,95,546.89	1,15,484.14		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
207	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,208.28	03/2023 -	03/2023
208	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
209	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	156.29	03/2023 -	03/2023
210	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	94.83	03/2023 -	03/2023
211	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
212	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	305.00	269.00	03/2019 12/2019	12/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
213	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
214	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	390.53	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
215	ARARIA-SUPAUL (NL) - [N22000177] <u>East Coast Railway</u>	4/2008	1,605.17 -	1,605.17	23.49	- 03/2023	03/2023
216	KOTTAVALSA - KORAPUT DOUBLING - [N22000377] <u>Eastern Railways</u>	4/2015	2,499.71 -	3,382.95	373.22	03/2022 -	03/2022
217	HANSDIHA-GODDA NL - [N22000236] <u>Metropolitan Rapid Transport Projects</u>	4/2011	542.18 -	693.80	428.83	03/2020 -	03/2020
218	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092] <u>North Central Railway</u>	4/2008	5,300.00 -	918.53	277.61	03/2014 03/2021	03/2021
219	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
220	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
221	JHANSI BINA DOUBLING - [N22000496] <u>North East Frontier Railway</u>	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021
222	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	5,021.45	3,075.08	03/2014 03/2022	03/2022
223	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	4/2008	333.76 -	360.00	6.67	- 03/2022	03/2022
224	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.15	03/2020 -	03/2020
225	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	502.44	03/2021 -	03/2021
226	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	122.05	03/2020 -	03/2020
227	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.76	03/2021 -	03/2021
228	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
229	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193] <u>North Eastern Railway</u>	4/2010	221.42 -	380.00	38.18	- 03/2022	03/2022
230	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
231	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	25.24	01/2022 -	01/2022
232	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
233	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131] <u>Northern Railway</u>	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
234	CHANDIGARH-BADDI - [N22000467 <u>National High Speed Rail Corporation Limited</u>	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
235	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463 <u>Rail India Technical And Economic Service</u>	12/2015	1,08,000.00 -	1,08,000.00	4,115.87	12/2023 12/2023	12/2023
236	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
237	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498 <u>Rail Vikas Nigam Ltd.</u>	2/2016	393.98 -	393.98	241.23	03/2020 -	03/2020
238	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99 -	7,000.00	370.26	12/2026 -	12/2026
239	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00 -	2,900.00	1,630.89	03/2023 -	03/2023
240	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,082.32	963.63	12/2021 -	12/2021
241	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	1,950.00	1,858.81	03/2020 -	03/2020
242	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,485.85	1,053.80	12/2020 -	12/2020
243	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	1/1991	2,335.67 -	2,335.68	566.84	12/2024 -	12/2024
244	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	773.94 -	773.94	372.81	12/2024 -	12/2024
245	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.67	925.36	12/2023 -	12/2023
246	PALANPUR-SAMAKHAYALI (DL) - [N22000144	4/2013	1,548.66 -	1,548.66	1,226.20	12/2021 -	12/2021
247	DHASA-JETALSAR (GC) - [N22000141 <u>South Central Railway</u>	4/2012	644.38 -	644.38	317.38	03/2021 -	03/2021
248	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	4/2010	704.31 -	1,352.74	269.07	03/2020 -	03/2020
249	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432 <u>South East Central Railway</u>	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
250	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	4/2005	383.79 -	1,413.76	1,324.64	- 10/2019	10/2019
251	ANUPPUR-KATNI - [N22000485	4/2015	1,370.00 -	1,370.00	281.19	12/2021 12/2021	12/2021
252	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	4/2015	1,973.00 -	1,973.66	139.42	03/2021 12/2022	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
253	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,226.51	1,044.67	12/2019 10/2019	10/2019
254	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	860.92	39.69	12/2021 03/2023	03/2023
255	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	443.56	03/2023 03/2023	03/2023
256	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.92	1,661.79	04/2020 12/2020	12/2020
	<u>South Eastern Railway</u>						
257	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.99	- 03/2025	03/2025
258	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	4/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030
	<u>South Western Railway</u>						
259	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
260	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
	<u>Southern Railway</u>						
261	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>Western Railway</u>						
262	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	3,860.40	1,676.43	03/2022 03/2023	03/2023
263	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	321.62	125.76	03/2012 03/2022	03/2022
264	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,310.23	1,363.06	03/2020 03/2021	03/2021
265	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	682.91	03/2022 03/2023	03/2023
266	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,037.15	992.18	03/2021 03/2022	03/2022
267	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	663.29	163.85	03/2020 03/2021	03/2021
268	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	86.45	06/2020 06/2021	06/2021
269	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	809.07	616.90	03/2019 03/2020	03/2020
270	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	374.60	03/2021 03/2021	03/2021
271	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH- KODINAR (GC) - [N22000143]	4/1994	320.66 -	858.96	534.00	03/2019 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
272	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	719.73	03/2022 03/2022	03/2022
	Total		2,17,364.17 -	2,76,402.20	59,543.21		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
273	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
274	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
275	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
276	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
277	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
278	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
279	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	4.96	04/2020 -	04/2020
280	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	112.97	12/2019 -	12/2019
281	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
282	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
283	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	500.61	11/2019 -	11/2019
284	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	131.87	06/2021 -	06/2021
285	SELDOH TO PANVAR - [N24001097]	7/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020
286	ARNI TO NAIGAINBANDI - [N24001093]	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019
287	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
288	MALEGAON TO RISOD - [N24001089]	2/2018	303.24 303.00	303.24	107.97	12/2019 -	12/2019
289	JALGAON TO NANDURA - [N24001088]	3/2018	177.84 177.00	177.84	55.69	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
290	MANGRUPHIR TO MAHAN - [N24001087]	3/2018	222.13 222.00	222.13	60.36	11/2019 -	11/2019
291	PAHUR TO BODHWAD - [N24001084]	1/2017	244.93 -	244.93	40.23	05/2020 -	05/2020
292	CHIKLI TO TAKARKHED - [N24001083]	3/2018	393.10 393.00	393.10	125.97	12/2019 -	12/2019
293	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
294	NASRATPUR TO BARASGAON - [N24001112]	7/2016	406.54 407.00	406.54	142.00	09/2019 -	09/2019
295	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	146.29	04/2020 -	04/2020
296	KUSUMBA TO MALEGAON - [N24001109]	3/2018	243.45 244.00	243.45	67.02	12/2019 -	12/2019
297	CHALISGAON TO NANDGAON - [N24001108]	3/2018	206.97 207.00	206.97	78.89	12/2019 -	12/2019
298	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020
299	AHMEDNAGAR TO BARAMATI - [N24001100]	1/2017	955.40 -	955.40	338.50	08/2019 -	08/2019
300	WARDHA TO HINGAGHAT - [N24001098]	1/2018	216.90 217.00	216.90	45.00	12/2019 -	12/2019
301	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]	3/2018	294.87 295.00	294.87	12.30	12/2019 -	12/2019
302	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
303	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020
304	PUNE TO MALE VILLAGE - [N24001078]	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
305	DEULGAON SAKARSHA TO MEHKAR - [N24001076]	3/2018	219.91 -	219.91	106.46	12/2019 -	12/2019
306	KUNDRAL TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	121.75	12/2019 -	12/2019
307	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]	3/2018	249.29 -	249.29	72.20	12/2019 -	12/2019
308	MAHAD TO RAIGAD FORT - [N24001038]	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
309	JAHIRABAD TO LATUR - [N24001040]	1/2017	461.96 -	461.96	151.43	11/2019 -	11/2019
310	MANSAR TO SALAIKHURD - [N24001035]	1/2018	418.36 -	418.36	116.13	12/2019 -	12/2019
311	MANJUSUMBA TO CHUMBALI - [N24001031]	1/2017	228.54 -	228.54	99.30	08/2019 -	08/2019
312	PIMPLA TO MANJARSUMBHA - [N24001030]	1/2017	595.77 -	595.77	132.44	08/2019 -	08/2019
313	AHMADPUR TO PIMPLA - [N24001029]	1/2017	422.38 -	422.38	169.58	08/2019 -	08/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
314	PATGAON KHOPOLI SECTION I - [N24001028]	1/2018	170.00 -	170.00	39.57	12/2019 -	12/2019
315	SHAHNUR PATGAON SECTION I - [N24001027]	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
316	KARASWADA TO BAMBOLIM - [N24001005]	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019
317	TASGAON TO SHIRDHON - [N24001054]	1/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019
318	SANGOLA TO JATH - [N24001052]	1/2018	257.38 257.00	257.38	61.15	12/2019 -	12/2019
319	NALDURG TO AKKALKOT - [N24001051]	2/2018	274.50 275.00	274.50	61.39	12/2019 -	12/2019
320	VITA TO NAGAJ - [N24001050]	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019
321	KARAD TO VITA - [N24001049]	1/2018	344.85 245.00	344.85	68.04	12/2019 -	12/2019
322	BHADGAON TO CHALISGAON - [N24001047]	1/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019
323	JALGAON TO BHADGAON - [N24001045]	1/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019
324	NILAJPHATA TO BHANDARA - [N24001043]	1/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020
325	SALAUKHURD TO TIRORA - [N24001042]	1/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019
326	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	33.02	08/2020 -	08/2020
327	KOTHARI TO DHANORA - [N24001073]	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
328	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	70.50	12/2019 -	12/2019
329	JALKOT TO TOGRI - [N24001071]	7/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020
330	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	83.40	12/2019 -	12/2019
331	NANDED TO JALKOT - [N24001069]	12/2017	456.93 457.00	456.93	54.50	09/2019 -	09/2019
332	WASHIM TO DASTAPUR - [N24001068]	3/2018	165.51 -	165.51	35.45	12/2019 -	12/2019
333	OMREGA TO AUSA - [N24001067]	3/2018	272.04 272.00	272.04	124.24	12/2019 -	12/2019
334	LATUR TO PANGAON - [N24001066]	3/2018	336.47 336.00	336.47	109.48	12/2019 -	12/2019
335	PARBHANI TO GANGKHED - [N24001065]	3/2018	238.19 238.00	238.19	40.85	12/2019 -	12/2019
336	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	3/2018	217.14 217.00	217.14	66.77	02/2020 -	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
337	WADIGODRI TO DHANGRIPIMPRI - [N24001063]	3/2018	194.23 194.00	194.23	68.23	02/2020 -	02/2020
338	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	3/2018	336.21 336.00	336.21	64.66	12/2019 -	12/2019
339	CHIKALI TO DHAD - [N24001061]	3/2018	189.46 189.00	189.46	21.54	12/2019 -	12/2019
340	PALPHATA TO PHULAMBARI - [N24001060]	3/2018	227.19 227.00	227.19	60.23	12/2019 -	12/2019
341	SHIVUR TO YEOLA - [N24001059]	3/2018	181.08 -	181.08	2.50	12/2019 -	12/2019
342	KARWANDI TO RAJURI - [N24001058]	3/2018	276.95 277.00	276.95	81.47	12/2019 -	12/2019
343	PATRADEVI TO KARASWADA 4L - [N24001004]	3/2017	634.32 -	634.32	102.33	05/2020 -	05/2020
344	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]	1/2018	418.03 -	418.03	129.17	08/2018 08/2020	08/2020
345	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	3/2018	504.19 504.00	504.19	269.70	11/2018 05/2020	05/2020
346	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	3/2018	297.12 294.00	297.12	177.05	07/2018 01/2020	01/2020
347	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]	3/2018	289.67 290.00	289.67	80.47	08/2018 02/2020	02/2020
348	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]	3/2018	244.95 245.00	244.95	101.40	08/2018 02/2020	02/2020
349	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]	3/2018	228.32 -	228.32	34.74	08/2018 03/2020	03/2020
350	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]	11/2016	378.24 -	378.24	237.18	01/2018 01/2020	01/2020
351	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
352	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
353	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
354	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
355	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
356	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583	1/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021
357	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
358	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
359	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
360	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
361	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
362	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
363	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
364	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
365	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442	12/2015	649.50 -	649.50	134.18	03/2019 04/2021	04/2021
366	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	532.53	04/2019 07/2020	07/2020
367	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	3/2016	1,587.49 -	2,982.00	276.87	04/2019 10/2019	10/2019
368	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510	12/2015	726.67 -	598.13	414.73	04/2018 03/2020	03/2020
369	FOUR LANING OF SIMGA - SARAGAON - [N24000495	12/2015	596.67 -	596.67	389.78	05/2018 10/2019	10/2019
370	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
371	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]	3/2018	291.53 -	291.53	30.82	- 11/2020	11/2020
372	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	3/2018	1,029.96 -	1,261.05	-	- 03/2021	03/2021
373	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020
374	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
375	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
376	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	64.68	03/2020 -	03/2020
377	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	231.96	08/2019 -	08/2019
378	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]	8/2016	2,016.00 -	2,016.00	1,996.00	04/2019 11/2019	11/2019
379	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	657.08	04/2020 -	04/2020
380	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020
381	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]	3/2016	720.00 -	720.00	278.01	- 10/2020	10/2020
National Highways Development Project							
382	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	248.66	01/2020 -	01/2020
383	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	957.54 -	957.54	467.50	02/2020 -	02/2020
Public Works Dept Of State							
384	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	3/2016	271.17 291.20	291.20	79.43	11/2018 11/2019	11/2019
385	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]	3/2018	191.21 -	191.21	72.02	11/2019 -	11/2019
386	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
387	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	151.88	12/2019 -	12/2019
388	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983	1/2017	196.52 -	196.52	98.61	10/2019 -	10/2019
389	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982	1/2017	244.54 -	244.54	137.10	05/2019 09/2019	09/2019
390	REHABILITATION AND UPGRADATION OF HARPALPUR-SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942	3/2016	208.50 -	208.50	123.66	11/2019 -	11/2019
391	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
392	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
393	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910	3/2018	170.57 -	170.57	46.23	11/2020 -	11/2020
394	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
395	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020
396	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	74.49	11/2020 -	11/2020
397	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	.50	09/2021 -	09/2021
398	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	435.14	01/2020 -	01/2020
399	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	194.01	01/2020 -	01/2020
400	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	157.79	09/2019 -	09/2019
401	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	86.07	03/2020 -	03/2020
402	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	80.47	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
403	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C [N24000999]	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019
404	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR) - [N24000996]	1/2017	605.08 -	605.08	260.32	10/2019 -	10/2019
405	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS [N24001209]	3/2016	296.50 -	296.50	.51	09/2020 -	09/2020
406	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN) - [N24001208]	3/2018	288.30 -	288.30	.34	08/2020 -	08/2020
407	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]	3/2018	185.18 -	185.18	2.86	02/2020 -	02/2020
408	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]	3/2018	263.89 -	263.89	119.70	04/2020 -	04/2020
409	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404) - [N24001205]	12/2016	209.10 -	209.10	85.74	10/2019 -	10/2019
410	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]	7/2016	208.88 -	208.88	36.25	10/2019 -	10/2019
411	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]	10/2016	218.90 -	218.90	23.37	03/2020 -	03/2020
412	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]	3/2016	388.83 -	388.83	280.17	12/2019 -	12/2019
413	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]	3/2018	351.00 -	351.00	.48	06/2021 -	06/2021
414	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
415	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
416	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]	11/2016	336.25 -	336.25	62.64	09/2019 -	09/2019
417	WIDENING TO 2-LANE WITH PAVED SHOULDER INC. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]	10/2016	171.90 -	171.90	14.77	08/2020 -	08/2020
418	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
419	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020
420	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
421	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020
422	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]	2/2018	426.52 -	426.52	200.79	04/2020 -	04/2020
423	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]	2/2018	220.28 -	220.28	22.17	11/2019 -	11/2019
424	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]	2/2018	294.13 -	294.13	30.35	11/2019 -	11/2019
425	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]	2/2018	206.13 -	206.13	116.63	06/2020 -	06/2020
426	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]	1/2018	230.03 -	230.03	127.98	12/2019 -	12/2019
427	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
428	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
429	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]	3/2018	254.30 -	254.30	20.26	10/2020 -	10/2020
430	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]	1/2017	396.86 -	396.86	179.31	09/2019 -	09/2019
431	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]	3/2017	202.69 -	202.69	93.93	11/2019 -	11/2019
432	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]	2/2018	218.70 -	218.70	25.02	11/2020 -	11/2020
433	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]	2/2018	426.18 -	426.18	218.00	09/2020 -	09/2020
	Total		67,594.66 -	69,775.10	21,187.50		
	SHIPPING AND PORTS						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Inland Waterways Authority Of India</u>						
434	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	5,369.18	1,394.52	03/2023 -	03/2023
	Total		4,200.00 -	5,369.18	1,394.52		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
435	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	15,938.88	05/2015 07/2020	07/2020
	<u>Rastrya Ispat Nigam Limited</u>						
436	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	1,175.53	09/2018 09/2019	09/2019
437	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,500.00	1,344.76	12/2017 10/2019	10/2019
438	CENTRAL DISPATCH YARD - [N12000119]	8/2015	320.66 -	320.66	206.91	08/2018 10/2019	10/2019
	<u>Steel Authority Of India Limited (Sail)</u>						
439	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	3,008.68	04/2018 11/2019	11/2019
440	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	10.81	09/2020 -	09/2020
441	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	104.85	06/2019 06/2020	06/2020
442	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT [N12000096]	5/2015	1,154.18 -	1,154.18	944.78	12/2017 11/2019	11/2019
443	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	432.82	10/2017 06/2020	06/2020
	Total		26,228.23 -	33,485.23	23,168.02		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
444	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	240.10	117.63	10/2018 09/2019	09/2019
	Total		231.80 -	240.10	117.63		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
445	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	53.20	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
446	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
447	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]	1/2018	223.37 -	223.37	33.01	07/2020 09/2020	09/2020
448	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019
449	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
450	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	1/2019	790.79 -	800.00	2.56	03/2022 -	03/2022
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
451	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	2,727.17	11/2021 01/2022	01/2022
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
452	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023
453	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023
	<u>National Building Construcion Corporation Ltd</u>						
454	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	Total		31,972.83 -	32,157.27	6,207.35		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
455	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Total		233.57 -	233.57	32.20		
	Grand Total		7,70,805.57	8,75,447.44	3,17,427.65		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	Total		3,492.00 -	6,840.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 -	860.00	03/2021 -	03/2021	.02
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
8	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42
9	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
13	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
14	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		19,818.83 -	20,957.14			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
16	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45
18	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
19	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
21	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
22	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
24	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
25	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
26	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
27	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
28	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71
	<u>Oil India Limited</u>						
29	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
30	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
31	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	06/2020	25.55
	Total		16,950.80 -	20,051.58			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
32	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
34	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
35	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	09/2020	9.64
36	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55
37	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
38	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75
39	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
40	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55
41	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
42	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
43	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
44	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
45	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
46	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	-	38.61
47	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
48	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	-	14.60
49	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	-	26.82
50	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	-	27.92
51	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17
52	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	-	22.93
53	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
54	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Thdc India Limited</u>						
55	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75
56	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
57	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,27,696.00 -	1,76,822.16			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
58	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73
59	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71
60	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44
61	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
62	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04
63	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2022	.01
64	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
65	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
66	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
67	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	03/2024	32.26
68	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15
69	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,609.00	- -	03/2022	589.19
70	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	03/2024	376.78
71	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2022	49.45
72	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	425.17	- -	01/2020	99.60
73	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	12/2021	350.27
	<u>East Coast Railway</u>						
74	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
75	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	03/2024	29.71
76	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
77	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2021	52.77
79	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
80	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2022	15.45
	<u>Eastern Railways</u>						
81	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22
82	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80
83	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46
84	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2020	27.96
85	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	242.06	- -	03/2021	37.69
86	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
87	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01
88	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25
89	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15
90	MONIGRAM- NIMITTA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82
91	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	09/2021	6.48
92	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08
93	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30
94	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19
95	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
96	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	376.90	- -	03/2020	30.71
97	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	471.81	- -	05/2019	80.51

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75
99	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20
	<u>Indian Railway Construction Company Limited</u>						
100	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
	<u>Metropolitan Rapid Transport Projects</u>						
101	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
102	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57
103	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	-	48.06
104	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
105	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	346.00	12/2008 -	-	188.33
106	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
107	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	03/2020 -	03/2020	1.80
	<u>North East Frontier Railway</u>						
108	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
109	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80
110	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
111	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	- -	03/2022	7.86
112	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95
113	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,496.67	03/2019 -	-	38.86
114	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	- -	03/2022	71.62
115	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11
116	NEW BG LINE FROM BYRNIAH TO SHILLONG - [N22000205	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
117	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
118	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2021	63.25
119	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
120	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
121	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
122	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
123	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,871.00	04/2010 -	-	391.59
<u>North Eastern Railway</u>							
124	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
125	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
126	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
127	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
128	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
129	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
130	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16
131	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91
132	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
<u>North Western Railway</u>							
133	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	03/2021	116.16
134	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
135	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64
136	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
137	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15	- -	-	95.85
138	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47
139	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
140	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
141	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	11/2019 -	05/2020	42.26
142	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	05/2020	69.36
	Northern Railway						
143	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	03/2024	25.87
144	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
145	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00	- -	03/2022	137.45
146	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	06/2020	57.68
147	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
148	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67
149	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
150	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	03/2021	35.29
	Rail Vikas Nigam Ltd.						
151	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
152	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	395.00	03/2009 03/2009	12/2019	90.82
153	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
154	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
155	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
156	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
157	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
158	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
159	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
160	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
161	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00	03/2020 -	03/2020	173.31
162	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
163	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22
164	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	Railway Electrification						
165	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	South Central Railway						
166	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
167	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
168	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
169	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
170	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
171	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	1,352.74	03/2020 -	03/2020	92.07
172	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
173	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	1,723.00	03/2000 -	03/2021	1,72,200.00
174	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
175	KONDAPALLI-KOTHAGUDEM - [N22000364]	04/2013	723.00 -	997.09	- -	-	37.91
	South East Central Railway						
176	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94
177	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>South Eastern Railway</u>						
178	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [N220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
179	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2019	153.41
180	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
181	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	-	54.99
182	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
183	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	03/2021 -	12/2021	15.60
184	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
185	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09
186	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
187	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
188	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
189	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
190	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
191	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98
192	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
193	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
194	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
195	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
196	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	- -	-	339.33
197	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
198	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	-	-	180.17
199	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	-	-	295.05
200	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	-	03/2020	173.71
201	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	951.24	-	03/2020	2.07
202	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
203	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
204	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	950.00	03/2005 -	-	253.33
205	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
<u>West Central Railway</u>							
206	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35
207	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
208	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32
<u>Western Railway</u>							
209	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18
210	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	03/2011 -	-	2.74
211	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
212	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,30,447.94 -	2,38,856.43			
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
<u>Dept Of Road Transport & Highways</u>							
213	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	-	-	3.72
<u>Ministry Of Road Transport And Highways</u>							

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
214	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	- -	-	9.23
215	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
216	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382	01/1991	675.00 -	780.77	- -	-	15.67
217	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	08/2016 -	-	14.02
218	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42
219	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00	157.30	06/2018 -	-	.19
220	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
221	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
222	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00	297.12	07/2018 -	01/2020	1.06
223	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	05/2020	.04
224	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	05/2018	.01
225	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	12/2019	.10
226	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	12/2019	.03
227	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.15
228	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	10/2019	.01
229	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	06/2020	.02
230	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	12/2019	.05
231	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	12/2019	40.76
232	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	12/2019	.15

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
233	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00	422.02	07/2019 -	-	.00
234	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00	407.19	06/2019 -	06/2020	.05
235	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00	227.19	12/2019 -	12/2019	.08
236	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00	189.46	12/2019 -	12/2019	.24
237	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00	336.21	12/2019 -	12/2019	.06
238	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00	194.23	02/2020 -	02/2020	.12
239	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00	217.14	02/2020 -	02/2020	.06
240	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00	238.19	12/2019 -	12/2019	.08
241	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00	336.47	12/2019 -	12/2019	.14
242	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00	272.04	12/2019 -	12/2019	.01
243	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00	301.38	08/2020 -	08/2020	.13
244	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00	344.25	08/2020 -	08/2020	.07
245	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00	225.25	12/2019 -	12/2019	.11
246	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	06/2020 -	06/2020	.01
247	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00	177.84	12/2019 -	12/2019	.47
248	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00	536.65	12/2019 -	12/2019	50.74
249	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00	244.04	03/2019 -	12/2019	.02
250	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00	264.41	03/2019 -	12/2019	.16
251	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00	404.33	05/2020 -	05/2020	.08
252	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00	381.08	05/2020 -	05/2020	26.19
253	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	07/2019 -	-	.31
254	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	03/2017 -	09/2019	.04

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
255	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687	03/2016	396.52	396.52	08/2016	06/2020	.00
256	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688	03/2016	429.52	429.52	08/2016	08/2019	.00
257	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00	447.37	10/2017	-	15.30
258	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754	03/2018	339.57	339.57	09/2018	-	.00
259	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759	03/2018	237.72	237.72	09/2018	-	.00
260	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760	03/2018	251.97	251.97	09/2018	-	.00
	<u>National Highways Authority Of India</u>						
261	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00	525.00	02/2009	-	87.50
262	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00	167.98	05/2008	06/2019	4.99
263	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61	360.84	04/2010	07/2019	65.82
264	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00	230.00	04/2008	03/2020	10.58
265	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22	2,945.00	04/2015	-	52.73
266	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24	941.00	-	10/2019	11.33
267	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00	1,601.77	11/2015	-	51.83
268	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	07/2015	1,871.34	1,871.34	01/2018	11/2019	.00
269	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49	2,982.00	04/2019	10/2019	87.84
270	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56	392.00	-	12/2019	7.53
271	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609	09/2015	771.18	7,558.00	-	-	880.06
272	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69	1,108.00	08/2019	12/2020	16.55

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
273	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25
274	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
275	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
276	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
277	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
278	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
279	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
280	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
281	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
282	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	09/2019	4.02
283	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
284	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
285	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
286	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48/O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
287	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	09/2017 -	06/2020	9.67
288	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 -	1,853.42	-	-	30.09
289	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 -	2,400.00	-	11/2021	20.28
290	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 -	2,450.00	-	-	12.50

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
291	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	-	03/2021	22.44
292	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	-	04/2021	5.32
293	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	-	4.99
294	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	-	.12
295	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842	03/2018	199.90 -	199.90	-	-	.00
296	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	-	07/2021	.48
297	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843	03/2018	196.05 -	196.05	-	01/2020	.00
298	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	-	12/2020	25.68
National Highways Development Project							
299	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017	09/2019	46.51
300	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017	05/2020	77.26
Public Works Dept Of State							
301	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011	12/2019	58.98
302	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010	12/2019	69.30
303	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017	12/2019	.12
304	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	-	-	1.75
305	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011	-	34.06

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
306	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21
307	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
308	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67
309	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923	03/2018	464.07 -	464.07	11/2018 -	-	.00
310	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925	10/2018	400.76 -	400.76	05/2019 -	-	.00
311	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926	08/2017	962.43 -	962.43	03/2018 -	-	.00
312	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	09/2019	.07
313	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	01/2020	.13
314	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46
	Total		60,734.69 -	77,379.59			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmdc)</u>						
315	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
316	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	01/2018	231.80 -	240.10	10/2018 -	09/2019	3.58
	<u>Department Of Telecommunication</u>						
317	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,565.80 -	24,904.10			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(August 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
318	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85
319	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2021	64.04
320	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	06/2014	157.84 -	169.16	03/2017 -	-	7.17
321	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.60
322	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR [N28000126]	01/2019	790.79 -	800.00	03/2022 -	03/2022	1.16
	<u>Chennai Metro Rail Ltd</u>						
323	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
324	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
325	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Kochi Metro Rail Corporation Ltd</u>						
326	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
327	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		28,016.42 -	34,430.73			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
328	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		4,29,185.96	6,81,973.91			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above						(August 2019)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	13,971.00	12/2015 -	06/2020	54	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	11,234.00	12/2016 -	12/2020	48	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	15,395.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	46,384.74				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI,DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	-
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	219.91	61.61	03/2020 -	12/2020	9	-
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	-
	Total		3,573.83 -	3,700.62	658.80				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
10	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	180.83	04/2014 -	11/2019	67	-
11	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	256.83	05/2014 -	03/2020	70	-
	<u>Central Coal Fields Limited</u>								
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120	-
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	179.87	03/2012 -	03/2021	108	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	362.47	03/2016 -	03/2021	60	-
15	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.85	03/2014 -	03/2021	84	-
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	354.66	07/2012 -	03/2022	116	-
	<u>Eastern Coal Fields Limited</u>								
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	501.35	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	-
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	501.82	03/2017 -	03/2020	36	-
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12	-
21	KULDA EXPN OC. (5.00 MTY) - [N060000115]MCL,ODISHA	06/2014	289.03 -	289.03	75.85	03/2018 -	03/2020	24	-
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	228.90	03/2012 -	03/2021	108	-
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	390.94	03/2013 -	03/2021	96	-
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022	108	-
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022	144	-
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	200.65	03/2019 -	03/2022	36	-
	<u>Neyveli Lignite Corporation</u>								
27	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	709.06	449.32	06/2015 -	09/2019	51	-
28	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,648.68	12/2015 -	12/2019	48	-
	<u>Singareni Colliers Company Limited</u>								
29	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.58	03/2015 -	03/2020	60	-
30	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	92.60	07/2016 -	03/2020	44	-
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	186.99	03/2016 -	03/2020	48	-
32	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	92.09	03/2019 -	03/2020	12	-
33	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	-
34	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	144.07	- 04/2017	03/2020	-	35
35	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	115.49	03/2015 -	03/2021	72	-
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	8.00	03/2015 -	03/2021	72	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	-
38	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	54.00	03/2019 -	03/2022	36	-
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132	-
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	286.19	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
41	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.49	191.51	03/2015 -	03/2020	60	-
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72	-
43	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	178.86	03/2016 -	03/2020	48	-
44	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24	-
45	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	194.57	03/2014 -	03/2021	84	-
	<u>Western Coal Fields Limited</u>								
46	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	21.02	03/2023 -	03/2024	12	-
47	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	115.50	03/2021 -	03/2024	36	-
	Total		19,904.63 -	21,118.25	14,153.88				
	<u>FERTILISERS</u>								
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
48	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	209.44	164.78	11/2016 -	09/2019	34	-
	Total		197.79 -	209.44	164.78				
	<u>INFORMATION AND BROADCASTING</u>								
	<u>Central Public Works Department</u>								
49	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	-
	Total		204.32 -	204.32	.00				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
50	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	-
51	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	507.00	06/2019 -	02/2022	32	-
	<u>Gas Authority Of India Limited</u>								

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
52	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	142.00	04/2018 -	10/2019	18	-
53	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,515.46	12/2012 -	02/2022	110	-
	<u>Indian Oil Corporation Limited</u>								
54	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	08/2019	9	-
55	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	263.70	08/2019 -	09/2019	1	-
56	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	306.24	01/2019 -	12/2019	11	-
57	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	1,562.10	07/2019 -	12/2019	5	-
58	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	24.15	06/2020 -	08/2020	2	-
59	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	278.51	07/2018 -	10/2020	27	-
60	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	41.22	02/2020 -	10/2020	8	-
61	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	85.08	02/2020 -	10/2020	8	-
62	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	465.60	12/2018 -	02/2021	26	-
63	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	50.84	04/2020 -	03/2021	11	-
64	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	38.55	01/2021 -	04/2021	3	-
65	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	38.29	12/2019 -	07/2021	19	-
66	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	84.34	04/2021 -	07/2021	3	-
67	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	30.95	10/2020 -	08/2021	10	-
68	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	30.75	01/2021 -	10/2021	9	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
69	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	40.06	08/2021 -	11/2021	3	-
70	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.07	04/2022 -	02/2023	10	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
71	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	68.27	03/2020 -	09/2020	6	-
	<u>Oil & Natural Gas Corporation Limited</u>								
72	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	145.60	01/2014 -	11/2019	70	-
73	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1	-
74	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	3,185.16	06/2020 -	08/2021	14	-
75	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	-	12/2021 -	03/2022	3	-
	<u>Oil India Limited</u>								
76	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
77	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33	-
78	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	682.90	8.75	02/2020 -	06/2020	4	-
	Total		61,414.18 -	63,831.70	11,113.43				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
79	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,551.56	09/2009 -	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
80	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15	-
81	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16	-
82	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	9,639.47	12/2018 02/2020	09/2020	21	7
83	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	9,996.59	7,861.51	07/2012 -	09/2020	98	-
84	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,131.59	06/2019 09/2019	09/2021	27	24
	<u>Power Grid Corporation Of India Limited</u>								
85	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	08/2019	129	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
86	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 -	08/2019	40	-
87	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	190.80	07/2017 -	08/2019	25	-
88	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	81.97	03/2018 -	08/2019	17	-
89	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	430.71	04/2019 -	08/2019	4	-
90	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	153.70	02/2019 -	08/2019	6	-
91	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	639.46	540.12	06/2014 -	09/2019	63	-
92	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	548.30	10/2017 -	09/2019	23	-
93	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4	-
94	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	266.03	01/2019 -	09/2019	8	-
95	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	92.78	09/2018 -	09/2019	12	-
96	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2	-
97	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3	-
98	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	117.15	06/2019 -	10/2019	4	-
99	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 -	12/2019	86	-
100	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	210.72	04/2016 -	12/2019	44	-
101	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	3,115.72	03/2018 -	12/2019	21	-
102	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	405.65	05/2017 -	12/2019	31	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
103	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12	-
104	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10	-
105	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	287.52	04/2018 -	01/2020	21	-
106	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	-
107	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	465.21	11/2016 -	03/2020	40	-
108	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	513.85	01/2018 -	03/2020	26	-
109	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 -	12/2020	24	-
110	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	14,719.10	12,804.46	08/2013 -	03/2022	103	-
	<u>Thdc India Limited</u>								
111	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	302.76	02/2014 -	10/2019	68	-
112	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	3,003.16	02/2016 -	06/2022	76	-
113	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,733.13	06/2013 -	12/2022	114	-
	Total		88,889.48 -	1,18,080.31	73,711.83				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>HII Infra Tech Services Limited</u>								
114	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2	-
115	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2	-
116	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5	-
	<u>Hospital Services Consultancy Corporation</u>								
117	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
118	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
119	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	-
120	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	-
121	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	-
122	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	-
123	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	-
124	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	-
	Total		4,693.67 -	4,793.45	1,838.34				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
125	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,347.12	03/2021 -	03/2022	12	-
126	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	301.24	03/2021 -	03/2022	12	-
127	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	281.97	03/2022 -	03/2023	12	-
128	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	223.82	03/2022 -	03/2024	24	-
129	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	76.32	03/2022 -	03/2024	24	-
130	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	56.45	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
131	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	260.88	03/2019 -	12/2019	9	-
132	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	-
133	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	150.62	03/2019 -	02/2020	11	-
134	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	439.45	03/2018 -	03/2020	24	-
135	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	286.78	03/2019 -	03/2020	12	-
136	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	11.11	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
137	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	94.31	03/2019 -	12/2019	9	-
138	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	898.53	1,038.71	03/2012 -	03/2020	96	-
139	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	751.55	673.58	03/2012 -	03/2020	96	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
140	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	466.93	03/2019 -	02/2021	23	-
141	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	494.58	03/2020 -	03/2021	12	-
142	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	396.80	03/2020 -	10/2021	19	-
143	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	488.95	03/2020 -	03/2022	24	-
144	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	54.14	03/2021 -	03/2022	12	-
145	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	32.31	03/2021 -	03/2022	12	-
146	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	438.38	03/2020 -	12/2022	33	-
	<u>East Coast Railway</u>								
147	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	225.52	03/2020 -	03/2021	12	-
148	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	924.93	02/2019 -	03/2022	37	-
149	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	122.59	11/2018 -	03/2022	40	-
150	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	393.60	12/2018 -	03/2022	39	-
151	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	688.96	06/2021 -	03/2023	21	-
152	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	130.99	10/2020 -	03/2023	29	-
153	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	682.29	03/2020 -	03/2023	36	-
154	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	346.97	03/2022 -	03/2023	12	-
155	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	1,360.34	03/2009 -	03/2024	180	-
156	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	2,361.74	162.82	03/2022 -	03/2025	36	-
	<u>Eastern Railways</u>								
157	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	-
158	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024	133	-
159	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	863.39	03/2019 12/2009	03/2025	72	183
160	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,091.59	834.72	12/2010 12/2017	03/2025	171	87
161	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
162	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	290.01	03/2022 -	03/2025	36	-
163	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	434.06	03/2016 -	03/2025	108	-
164	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	102.27	03/2017 -	03/2025	96	-
165	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	155.33	03/2016 -	03/2025	108	-
166	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	212.51	03/2017 -	03/2025	96	-
167	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
168	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	155.08	02/2012 -	03/2025	157	-
169	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	105.28	03/2014 -	03/2025	132	-
170	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
171	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 -	12/2020	27	-
172	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	619.50	03/2022 -	12/2022	9	-
173	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39	-
	<u>Metropolitan Rapid Transport Projects</u>								
174	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,414.47	03/2004 -	03/2021	204	-
175	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
	<u>North Central Railway</u>								
176	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
177	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
178	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,123.93	03/2011 -	03/2020	108	-
179	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	1,532.00	629.19	03/2019 -	03/2020	12	-
180	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12	-
181	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	728.00	704.09	03/2019 -	03/2020	12	-
182	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	3,300.00	3,279.71	12/2008 -	03/2021	147	-
183	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	3,000.00	781.71	03/2015 -	10/2021	79	-
184	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	650.00	45.24	03/2020 -	12/2021	21	-
<u>North Eastern Railway</u>									
185	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	328.19	01/2019 -	01/2020	12	-
186	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	179.51	04/2017 -	01/2020	33	-
187	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	8.97	04/2016 -	06/2020	50	-
188	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-
189	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
190	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
<u>North Western Railway</u>									
191	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	141.40	10/2018 -	10/2019	12	-
192	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	262.32	11/2019 -	05/2020	6	-
193	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	351.23	02/2019 -	05/2020	15	-
194	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	215.47	12/2019 -	06/2020	6	-
195	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	160.53	03/2020 -	06/2020	3	-
196	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	525.78	02/2019 -	03/2021	25	-
197	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	47.07	03/2020 -	04/2022	25	-
198	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	47.07	08/2022 -	09/2022	1	-
<u>Northern Railway</u>									

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
199	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	-
200	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	845.58	834.59	03/2016 -	03/2021	60	-
201	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	19,223.83	11/2002 -	06/2022	235	-
202	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140	-
	<u>Rail Vikas Nigam Ltd.</u>								
203	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	395.00	386.28	03/2009 03/2009	12/2019	129	129
204	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,757.33	12/2017 -	03/2020	27	-
205	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020	12	-
206	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,029.98	03/2020 -	06/2020	3	-
207	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	682.17	03/2016 -	12/2020	57	-
208	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,304.20	03/2020 -	03/2021	12	-
209	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	998.91	03/2019 -	03/2021	24	-
210	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,032.16	12/2020 -	03/2021	3	-
211	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	891.28	02/2015 -	12/2021	82	-
212	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,402.19	03/2020 -	03/2022	24	-
213	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	343.30	03/2022 -	12/2024	33	-
214	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	568.43	03/2023 -	12/2024	21	-
215	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,226.44	03/2016 -	03/2025	108	-
216	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.50	847.45	03/2016 -	03/2025	108	-
217	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	2,106.00	03/2014 -	12/2025	141	-
218	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,521.62	12/2024 -	03/2026	15	-
	<u>South Central Railway</u>								
219	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
220	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	-
221	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	-
222	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	-
223	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	-
224	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	-
225	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	-
226	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	-
	<u>South East Central Railway</u>								
227	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	646.30	02/2019 03/2020	06/2020	16	3
	<u>South Eastern Railway</u>								
228	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019	36	16
229	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	258.09	12/2018 12/2018	06/2020	18	18
230	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	549.97	03/2020 -	06/2020	3	-
231	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	384.82	03/2021 -	12/2021	9	-
	<u>South Western Railway</u>								
232	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	-
233	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-
234	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	-
235	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	-
236	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	-
237	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-
238	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
239	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	-
	<u>Southern Railway</u>								
240	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	-
241	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
242	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	-
243	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	-
244	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	-
245	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	<u>West Central Railway</u>								
246	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	624.49	03/2020 -	03/2022	24	-
247	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	154.63	03/2022 -	09/2022	6	-
248	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023	178	-
249	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023	24	-
250	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	367.59	03/2022 -	03/2023	12	-
	Total		1,53,791.07 -	2,31,710.25	1,01,645.38				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
251	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA	01/2017	463.62 664.00	463.62	257.34	06/2019 -	08/2019	2	-
252	AMD I TO SAONER - [N24001021]MORTH,MAHARASHTRA	01/2017	396.91 396.91	396.91	248.48	06/2019 -	08/2019	2	-
253	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	89.14	08/2015 -	09/2019	49	-
254	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	464.05	03/2017 -	09/2019	30	-
255	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	287.00	06/2019 -	10/2019	4	-
256	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	-
257	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5	-
258	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12	-
259	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
260	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	-
261	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	102.79	05/2019 -	12/2019	7	-
262	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	123.43	05/2019 -	12/2019	7	-
263	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6	-
264	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	153.29	06/2019 -	12/2019	6	-
265	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	168.81	06/2019 -	12/2019	6	-
266	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA	01/2017	355.17 355.17	355.17	164.87	07/2019 -	12/2019	5	-
267	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	87.26	06/2019 -	12/2019	6	-
268	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	25.94	03/2019 -	12/2019	9	-
269	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	32.71	03/2019 -	12/2019	9	-
270	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	-
271	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-
272	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	-
273	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	-
274	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	751.91	11/2019 -	03/2020	4	-
275	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12	-
276	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	29.03	05/2019 -	05/2020	12	-
277	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	171.78	05/2019 -	05/2020	12	-
278	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	68.00	06/2019 -	06/2020	12	-
279	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	85.97	06/2019 -	06/2020	12	-
280	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	-
281	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	-
282	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	-
283	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	202.98	07/2019 -	07/2020	12	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
284	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12	-
285	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	148.00	09/2018 -	04/2021	31	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
286	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	194.11	159.75	05/2018 -	08/2019	15	-
287	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 387.00	373.07	203.77	08/2016 -	08/2019	36	-
288	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 340.00	429.52	166.55	08/2016 -	08/2019	36	-
289	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36	-
290	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	269.69	-	09/2019 -	12/2019	3	-
291	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	17.43	01/2017 -	01/2020	36	-
292	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21	-
293	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 339.55	396.52	234.03	08/2016 -	06/2020	46	-
294	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	120.86	05/2018 05/2020	12/2020	31	7
295	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	28.67	04/2017 02/2018	02/2021	46	36
296	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46	36
297	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	15.77	04/2017 02/2018	02/2021	46	36
298	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	18.70	04/2017 02/2018	02/2021	46	36

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
299	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	9.65	- 02/2018	02/2021	-	36
300	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	-	36
301	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	64.66	04/2017 03/2018	03/2021	47	36
302	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63	26
303	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	119.56	10/2018 -	10/2021	36	-
304	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42	12
305	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42	11
306	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60	-
307	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	6.58	- 04/2019	04/2022	-	36
308	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	5.63	- 04/2019	04/2022	-	36
	National Highways Authority Of India								
309	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 340.14	340.14	319.96	04/2009 03/2011	08/2019	124	101
310	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	140.57	01/2019 -	08/2019	7	-
311	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	1,544.00	1,446.45	09/2016 -	09/2019	36	-
312	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	507.70	494.29	06/2016 -	09/2019	39	-
313	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	537.16	491.45	07/2018 -	09/2019	14	-
314	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 1,240.03	1,057.60	1,000.89	06/2019 12/2016	09/2019	3	33

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
315	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	588.00	06/2019 -	09/2019	3	-
316	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	-
317	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13	-
318	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019	136	-
319	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	-
320	TWO LANING WITH PAVED SHOULDER OF KARAU - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	37	61
321	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019	27	-
322	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	-
323	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	257.52	- 02/2016	10/2019	-	44
324	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,424.19	01/2018 12/2018	11/2019	22	11
325	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	-
326	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	-	30
327	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6	-
328	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	20.54	06/2017 -	11/2019	29	-
329	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	-
330	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	105.81	09/2017 -	11/2019	26	-
331	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	-
332	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	-
333	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019	81	-
334	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
335	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81	-
336	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	-
337	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	-
338	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	-
339	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 897.03	897.03	705.85	11/2018 07/2019	12/2019	13	5
340	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	479.20	708.82	05/2018 03/2018	12/2019	19	21
341	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	-
342	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	458.03	303.12	- 12/2017	12/2019	-	24
343	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	244.90	243.33	05/2019 -	12/2019	7	-
344	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	804.97	425.58	06/2018 -	01/2020	19	-
345	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17	-
346	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	-
347	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76	-
348	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19	2
349	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020	143	-
350	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	-
351	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,982.72	11/2011 -	03/2020	100	-
352	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	1,388.00	1,138.07	08/2018 -	03/2020	19	-
353	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	707.82	343.21	08/2018 -	03/2020	19	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
354	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	473.11	- 02/2018	03/2020	-	25
355	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	-
356	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	-
357	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	-
358	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	159.58	03/2020 -	04/2020	1	-
359	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020	24	14
360	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	750.87	11/2016 -	05/2020	42	-
361	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	340.73	07/2018 -	05/2020	22	-
362	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	904.16	817.58	02/2020 11/2017	05/2020	3	30
363	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	-
364	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	852.57	03/2020 11/2017	05/2020	2	30
365	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	751.70	03/2020 -	05/2020	2	-
366	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	340.73	07/2016 -	05/2020	46	-
367	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78	-
368	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	-
369	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	-
370	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	-
371	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	-

Costing Rs. 150 Crore and above

(August 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
372	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	626.56	03/2020 -	06/2020	3	-
373	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	278.60	09/2017 -	06/2020	33	-
374	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,273.00	2,136.97	1,214.48	12/2018 12/2019	07/2020	19	7
375	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	567.90	03/2020 -	07/2020	4	-
376	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	08/2020	149	-
377	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	-
378	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	19
379	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	254.96	03/2019 03/2017	08/2020	17	41
380	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	-
381	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	-
382	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	-
383	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	-
384	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	159.23	09/2017 -	08/2020	35	-
385	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,700.67	07/2015 12/2019	09/2020	62	9
386	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	220.70	05/2018 04/2019	09/2020	28	17
387	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	122.89	08/2017 -	09/2020	37	-
388	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	-
389	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	-
390	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
391	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	1,071.00	556.63	03/2017 05/2018	11/2020	44	30
392	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	364.29	10/2017 -	11/2020	37	-
393	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31	-
394	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	-
395	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	621.26	06/2019 -	12/2020	18	-
396	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,353.61	08/2019 -	12/2020	16	-
397	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	17.41	09/2017 -	01/2021	40	-
398	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	-
399	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	-
400	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	348.24	03/2020 -	03/2021	12	-
401	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	-	24
402	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	569.15	03/2021 -	04/2021	1	-
403	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-
404	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 11/2020	06/2021	47	7
405	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	80.87	- 07/2020	06/2021	-	11

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
406	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	94.03	- 05/2020	06/2021	-	13
407	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	99.10	- 05/2020	06/2021	-	13
408	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	71.38	- 03/2020	06/2021	-	15
409	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	-
410	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,371.02	- 05/2019	11/2021	-	30
411	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 1,684.93	1,117.84	-	- 12/2018	12/2021	-	36
412	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	-
413	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	972.77	-	- 02/2019	02/2022	-	36
414	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	93.53	12/2017 -	08/2019	20	-
<u>National Highways Development Project</u>									
415	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019	30	-
416	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	410.72	-	04/2015 -	10/2019	54	-
417	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36	-
<u>Public Works Dept Of State</u>									
418	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70	-
419	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24	-
420	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	11	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
421	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	359.27	227.88	05/2019 -	08/2019	3	-
422	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	153.21	100.10	01/2017 -	09/2019	32	-
423	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	-
424	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	09/2019	11	-
425	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	89.14	08/2015 -	09/2019	49	-
426	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	97.39	02/2018 -	11/2019	21	-
427	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	55.27	02/2018 -	11/2019	21	-
428	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	19.35	03/2018 -	11/2019	20	-
429	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	95.28	03/2018 -	11/2019	20	-
430	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	139.41	02/2018 -	11/2019	21	-
431	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	-
432	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	436.12	06/2019 -	11/2019	5	-
433	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	249.50	150.70	05/2019 -	11/2019	6	-
434	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	224.94	03/2018 -	11/2019	20	-
435	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
436	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105	-
437	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	-
438	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76	-
439	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	27
440	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	-
441	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	88.47	03/2018 -	12/2019	21	-
442	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	77.44	02/2019 -	12/2019	10	-
443	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	88.85	03/2019 -	12/2019	9	-
444	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	99.46	05/2019 -	12/2019	7	-
445	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA	03/2018	192.67 -	192.67	107.35	07/2019 -	12/2019	5	-
446	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	-
447	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63	-
448	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	118.29	07/2018 -	01/2020	18	-
449	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	240.05	08/2017 -	02/2020	30	-
450	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	219.42	07/2018 -	02/2020	19	-
451	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54	-
452	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
453	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	373.82	116.33	09/2019 -	05/2020	8	-
454	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	-
455	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116	-
456	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	26.72	08/2018 -	06/2020	22	-
457	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39	-
458	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	12.39	08/2018 -	06/2020	22	-
459	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	9.35	03/2018 -	07/2020	28	-
460	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	-
461	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
462	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	-
463	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	-
	Total		1,32,168.82 -	1,38,163.36	85,942.17				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
464	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
465	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	5,854.77	12/2018 -	07/2020	19	-
	<u>Bangalore Metro Rail Corporation Limited</u>								

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
466	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
467	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5	-
468	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	488.28	424.11	05/2017 -	09/2019	28	-
469	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38	-
470	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59	-
471	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
472	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	195.83	04/2019 -	02/2020	10	-
473	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	335.76	07/2019 12/2019	02/2020	7	2
474	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	89.66	10/2012 -	03/2020	89	-
475	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	130.62	10/2019 -	03/2020	5	-
476	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	42.30	04/2019 -	06/2020	14	-
477	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	80.08	03/2016 -	09/2020	54	-
478	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	65.84	02/2020 -	09/2020	7	-
479	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	-
480	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	85.74	06/2017 -	10/2020	40	-
481	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	65.80	05/2020 -	01/2021	8	-
482	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	330.83	10/2019 -	03/2021	17	-

Costing Rs. 150 Crore and above

(August 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
483	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	-	7
484	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 -	05/2021	14	-
	<u>Hindustan Steelwork Construction Limited</u>								
485	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
486	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
487	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	<u>Nagpur Metro Rail Corporation Ltd</u>								
488	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	6,108.39	03/2018 -	12/2019	21	-
	Total		81,065.13 -	82,616.91	20,687.41				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
489	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	-
	Total		10,151.04 -	55,548.87	16,417.99				
	Grand Total		6,36,507.96	8,24,989.48	3,81,115.75				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	06/2019	12/2019	338.93	6
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	12/2020	219.91	9
7	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	08/2022	2467	6
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
9	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	12/2020	233.38	8

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
10	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
11	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2020	430.45	48
12	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2020	258.56	48
13	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
14	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
15	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2022	457.77	108
16	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
17	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
18	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
19	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2021	479.53	96
20	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2020	209.78	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2022	172.08	144
22	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	48
23	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
24	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2020	426.79	24
25	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
26	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2022	706.4	116
27	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
28	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2021	163.51	120
29	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2021	264.68	108
30	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2021	162.46	84
31	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
32	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
33	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
34	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
35	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
36	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
37	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2022	479.15	36
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2020	337.66	12
39	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
40	AMERA OC RCE	SECL	02/2015	03/2018	03/2020	335.97	24
41	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	03/2020	289.45	70
42	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2019	269.82	67
43	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2020	397.09	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
45	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2020	302.96	120
46	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2021	510.85	60

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	09/2019	197.79	34

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	09/2019	363.99	16
49	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	09/2019	204.44	28
50	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	08/2019	293.65	27
51	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	09/2019	152.95	19
52	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	03/2020	355.15	12
53	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	10/2019	274.19	7
54	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	10/2019	272.19	7
55	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	10/2020	414.11	83

INFORMATION AND BROADCASTING

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
56	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	CPWD	11/2016	02/2019	11/2019	204.32	9

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
57	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
58	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
59	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	ONGC	04/2017	09/2018	09/2019	420.76	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
61	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
62	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	79
63	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	MANGALORE REFI	10/2015	03/2019	09/2019	135	6
64	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	07/2020	1810	7
65	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
66	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
67	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	12/2019	429	11
68	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	7
69	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	03/2021	163.02	11
70	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2020	906	8
71	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
72	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	09/2020	581	6
73	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	12/2019	2465.15	81
74	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	12/2019	352.56	33
75	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	12/2019	6068.8	8
76	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
77	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
78	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	58
79	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	12/2019	694	14
80	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	15
81	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2020	4619.94	27
82	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2020	3190.69	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
83	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2020	160.1	8
84	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	07/2021	161.59	19
85	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
86	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	10/2019	327.78	18
87	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	10/2021	678	56
88	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2020	650.82	14
89	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
90	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	IOCL	07/2015	11/2018	08/2019	822.66	9
91	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497	26
92	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
93	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	03/2020	529.68	16
94	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	12964.6	43
95	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	40
96	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
97	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	86
98	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	11638.55	26
99	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
100	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	40
101	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2019	374.63	44
102	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2020	522.29	40
103	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	12/2019	5151.37	21
105	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	06/2020	9188.98	11
106	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	09/2020	12532.44	21
107	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	14366.58	27
108	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
109	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
110	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	08/2019	203.28	25
111	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	08/2019	197.4	17
112	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2019	1394.52	31
113	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	10/2019	195.42	68
114	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353	98
115	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	114
116	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2019	2496.9	118
117	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657	76
118	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	63
119	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	08/2019	1779.29	129
120	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	118
121	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	11846	29
122	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	06/2021	10598.98	7
123	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	09/2019	175.64	12
124	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	12/2019	445.89	10
125	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2020	808.63	26

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
126	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
127	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	08/2019	322.3	6
128	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	09/2019	408.46	8
129	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	01/2020	454.11	21
130	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	24
131	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	03/2020	1885.13	15

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
132	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	03/2021	691.84	12
133	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	06/2020	213	50
134	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
135	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
136	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
137	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
138	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
139	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
140	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229	15
141	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2022	1973	21
142	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	40
143	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2022	1172.92	39
144	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2023	2063.03	24
145	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
146	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
147	BANKURA DAMODAR VALLEY RLY LINE	SER	04/1998	03/2003	03/2030	1027.4	324

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	96 KM GC WITH 6MMS FOR NL						
148	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
149	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
150	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	03/2026	16216	15
151	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
152	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
153	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
154	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
155	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
156	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.6	24
157	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
158	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	129
159	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	21
160	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI- THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	12
161	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
162	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	96
163	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
164	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2023	1160.48	156
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
166	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
167	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
168	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
169	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
170	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	12
171	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
172	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
173	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
174	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
175	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	9
176	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
177	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
178	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
179	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287	111
180	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
181	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
182	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2132.77	120
183	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
184	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
185	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.5	12
186	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	204
187	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
188	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	96
189	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	147
190	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2024	2923.13	180
191	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	108
192	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
193	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
194	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
195	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	03/2021	5300	84
196	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	03/2021	410.08	25
197	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450	140
198	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	06/2022	2500	235
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
200	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
201	MUNEERABAD-MAHABOONNAGAR(NL),SCR	SCR	04/1997	03/2000	03/2021	1723	252
202	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	8
203	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
204	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2021	303.98	12
205	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2022	318.24	120
206	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	12
207	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
208	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
209	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2023	843.04	29
210	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
211	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2021	155.81	12
212	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2019	148.77	36
213	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
214	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
215	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
216	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	02/2021	678.54	23
217	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314	12
218	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
219	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2019	120.7	9
220	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
221	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
222	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
223	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
224	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
225	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2022	1491.47	33
226	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
227	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	63
228	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	6
229	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
230	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
231	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	03/2022	1037.15	12
232	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
233	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	10/2019	236.93	12
234	AJMER-BANGURGRAM	NWR	04/2011	11/2019	05/2020	213.39	6
235	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	05/2020	242.09	15
236	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2020	258.2	18
237	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
238	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	12/2021	569.63	21
239	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2022	1763.93	24
240	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
241	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
242	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
243	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
244	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
245	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
246	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2025	2361.74	36
247	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	12
248	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
249	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
250	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	6
251	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
252	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	06/2023	5200	39
253	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
254	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2020	493.17	24
255	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	12/2019	305	9
256	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2020	346.32	12
257	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	02/2020	174	11
258	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
259	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
260	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
261	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
262	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760	15
263	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625	60
264	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2020	3055	27
265	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288	9
266	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
267	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	12
268	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	06/2021	700	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
269	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	12/2019	186.96	63
270	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	PWD	02/2017	05/2019	05/2021	157.32	24
271	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	PWD	01/2017	08/2017	08/2019	291.49	24
272	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	PWD	05/2018	05/2018	05/2020	171.6	24
273	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	PWD	11/2010	02/2014	12/2019	197.37	70
274	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	PWD	11/2017	03/2018	11/2019	392.33	20
275	REHABILITATION AND UPGRADE OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	PWD	03/2016	05/2019	11/2019	249.5	6
276	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	PWD	05/2013	08/2015	09/2019	164.54	49
277	REHABILITATION AND UPGRADE OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	09/2019	445.89	30
278	REHABILITATION AND UPGRADE OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	PWD	10/2016	10/2018	09/2019	176.94	11
279	PARLI PIMPLA DAHIGUDA	MORTH	02/2017	06/2019	06/2020	205.72	12
280	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	MORTH	08/2016	12/2017	12/2019	234.88	24
281	NASHIK TO PETH	MORTH	12/2015	11/2018	11/2019	289.6	12
282	AKKALKOT TO DHUDHNI	MORTH	04/2016	02/2019	02/2020	211.42	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
283	BARASGAON TO RAHATEE	MORTH	07/2016	09/2018	04/2021	289.11	31
284	KOLHA TO NASRATPUR	MORTH	04/2016	04/2019	04/2020	281.78	12
285	PEN TO KHOPOLI	MORTH	03/2018	03/2018	12/2019	301.39	21
286	MALEWADA TO CHIMUR	MORTH	10/2016	06/2019	06/2020	322.55	12
287	TALEGAON TO GONAPUR	MORTH	01/2018	03/2019	12/2019	264.41	9
288	NAIGAONBANDI TO MANGRULPIR	MORTH	12/2017	03/2019	12/2019	244.04	9
289	TAKARKHED TO JALNA	MORTH	09/2017	06/2019	12/2019	417.9	6
290	KARAD PATAN CHIPLUN GUHAGAR	MORTH	02/2017	06/2019	06/2020	407.19	12
291	KARAD TO TAGAON	MORTH	01/2017	06/2019	06/2020	537.81	12
292	DEORI TO AMGAON	MORTH	01/2017	05/2019	05/2020	409.62	12
293	WAKAN PALI KHOPOLI	MORTH	01/2017	05/2019	05/2020	376.19	12
294	MANGAON TO DIGHI PORT	MORTH	01/2017	07/2019	07/2020	457.52	12
295	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	105
296	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	110
297	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	PWD	01/2013	02/2013	12/2019	182.28	82
298	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	116
299	FOUR LANNING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	05/2020	641.17	46
300	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
301	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	09/2020	1176.37	37
302	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
303	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	11/2019	648.33	29
304	JUNAGADH BYPASS	NHAI	10/2017	10/2017	11/2019	232.49	25
305	FOUR LANNING BALANCE WORK FOR	NHAI	10/2017	10/2017	01/2020	639.97	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.						
306	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	11/2020	964.17	37
307	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
308	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	01/2021	990.61	40
309	4-LANNING OF OTTANCHATRAM BYPASS	NHAI	09/2017	09/2017	11/2019	244.27	26
310	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	08/2020	1227.87	35
311	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	12/2020	454.89	31
312	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
313	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
314	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	NHIDCL	03/2015	05/2018	08/2019	194.11	15
315	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	03/2020	394	21
316	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	PWD	03/2015	01/2017	09/2019	153.21	32
317	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	12/2019	255.75	27
318	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	09/2019	445.89	30
319	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	36
320	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	09/2019	164.54	49
321	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	PWD	03/2015	08/2017	02/2020	511.83	30
322	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	PWD	12/2011	11/2017	09/2019	159.39	22
323	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	12/2019	191.08	52
324	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	04/2021	294.17	63
325	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	12/2021	252	71
326	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	03/2020	954.43	54
327	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	10/2019	410.72	54
328	NH 79 CHITTORGARH NEEMUCH MP BORDER	PWD	09/2012	10/2013	08/2019	511	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING						
329	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	08/2020	604	128
330	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	09/2020	1987	62
331	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	06/2020	702.16	71
332	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	03/2020	486	118
333	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108	100
334	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2019	617	88
335	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2019	1724.55	81
336	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	09/2019	1266.6	36
337	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	06/2020	1250	78
338	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
339	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	10/2019	1535	65
340	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
341	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2019	1078.84	76
342	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2020	998.79	82
343	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2019	1396.18	63
344	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	10/2019	972.5	27
345	4-LANING OF SOLAPUR - MAHARASHTRA/KARNATKA SECTION	NHAI	06/2014	11/2016	05/2020	923.04	42
346	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
347	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	03/2020	1388	19
348	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	11/2019	1871.34	22
349	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	08/2019	199.81	124
350	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	PWD	04/2013	08/2013	12/2019	151.59	76

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
351	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	08/2020	245	149
352	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2020	208	143
353	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	10/2019	225	136
354	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	12/2019	946	18
355	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	08/2020	600	86
356	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	02/2020	478.51	76
357	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	10/2019	425.19	37
358	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	08/2019	563.92	20
359	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	05/2020	414.51	24
360	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	12/2020	593.26	31
361	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	04/2021	649.5	25
362	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	09/2019	602.95	39
363	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	09/2019	574.28	14
364	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	09/2020	505	28
365	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	12/2019	1083	18
366	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
367	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	12/2019	1423.96	13
368	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	07/2020	2136.97	19
369	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	06/2020	815.28	24
370	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	NHAI	01/2016	06/2018	06/2020	1027.53	24
371	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	10/2019	596.67	17
372	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	04/2020	667	21
373	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	04/2020	667	22

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
374	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
375	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	24
376	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	03/2020	726.67	23
377	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	12/2019	479.2	19
378	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6
379	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	10/2019	1587.49	6
380	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	11/2020	701.4	20
381	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	11/2018	12/2019	229.37	13
382	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
383	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2020	707.82	19
384	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	07/2020	899	15
385	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	05/2020	641.17	22
386	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2020	546	17
387	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2020	591.66	17
388	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	01/2020	804.97	19
389	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	01/2020	323.72	17
390	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	NHAI	08/2016	01/2019	08/2019	227.49	7
391	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	08/2020	1167.42	17
392	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
393	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	NHAI	08/2016	05/2019	11/2019	248.97	6
394	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	NHIDCL	04/2016	10/2016	10/2019	198	36
395	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	NHAI	09/2016	08/2018	09/2019	767.03	13
396	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
397	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	02/2021	400.25	23
398	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	03/2021	446.17	24
399	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	19
400	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	MORTH	03/2014	05/2016	12/2019	191.5	43
401	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	MORTH	08/2013	06/2016	11/2019	171.96	41
402	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	NHAI	01/2017	05/2019	12/2019	244.9	7
403	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
404	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
405	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
406	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	12
407	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
408	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
409	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
410	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	02/2021	168.32	46
411	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
412	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	02/2021	216.71	46
413	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46
414	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
415	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	06/2020	396.52	46
416	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
417	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
418	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MORTH	06/2017	06/2019	12/2019	282.08	6
419	NAGAJ TO VAIJAPUR	MORTH	01/2017	06/2019	12/2019	376.72	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
420	WADI TO ASOLA	MORTH	01/2017	09/2019	09/2020	363.82	12
421	MORSHI TO ACHALPUR	MORTH	01/2017	06/2019	12/2019	341.16	6
422	NANDGAON TO MORSHI	MORTH	01/2017	06/2019	12/2019	385.87	6
423	DIGRAS DARWAH KARANJA	MORTH	01/2017	06/2019	06/2020	391.06	12
424	SHEGAON TO DEORI PHATA	MORTH	02/2017	05/2019	12/2019	373.1	7
425	KHAMGAON TO SHEGAON	MORTH	02/2017	05/2019	12/2019	203.21	7
426	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	PWD	05/2014	08/2016	12/2020	199.98	52
427	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	PWD	01/2017	05/2019	12/2019	300	7
428	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	PWD	10/2016	03/2019	12/2019	248.83	9
429	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	PWD	10/2016	02/2019	12/2019	298.32	10
430	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MORTH	01/2017	01/2018	01/2020	576.48	24
431	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MORTH	01/2017	09/2017	09/2019	263.45	24
432	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MORTH	11/2016	08/2017	08/2019	376.25	24
433	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MORTH	01/2018	08/2018	08/2020	418.03	24
434	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	PWD	09/2016	09/2018	08/2019	178.23	11
435	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	MORTH	03/2018	11/2018	05/2020	504.19	18
436	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	MORTH	03/2018	07/2018	01/2020	297.12	18
437	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MORTH	03/2018	08/2018	02/2020	289.67	18
438	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	MORTH	03/2018	08/2018	02/2020	244.95	18
439	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MORTH	03/2018	08/2018	03/2020	228.32	19
440	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MORTH	02/2017	11/2017	11/2019	429.43	24
441	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN	MORTH	01/2017	08/2017	08/2019	319.28	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	CH. 0/000 TO 60/025 EXCLUD						
442	REHABILITATION AND UPGRADE OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	MORTH	11/2016	01/2018	01/2020	378.24	24
443	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	PWD	01/2017	03/2019	09/2019	247.25	6
444	REHABILITATION AND UPGRADE OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	PWD	01/2016	07/2018	02/2020	809.16	19
445	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	PWD	01/2017	09/2019	05/2020	373.82	8
446	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	PWD	09/2016	01/2019	11/2019	287.34	10
447	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	PWD	02/2018	03/2018	04/2020	279.44	25
448	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	254.17	21
449	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	PWD	11/2017	07/2018	01/2020	249.05	18
450	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	233.04	20
451	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	217.22	22
452	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	214.69	20
453	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	PWD	01/2017	03/2017	06/2020	205.05	39
454	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	PWD	06/2016	08/2019	08/2021	236.78	24
455	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	PWD	03/2016	08/2019	08/2021	160.27	24
456	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	184.62	21
457	REHABILITATION AND UPGRADE OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	PWD	11/2017	02/2018	11/2019	235.91	21
458	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	PWD	02/2018	03/2018	07/2020	169.63	28
459	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	PWD	03/2016	11/2018	11/2019	271.17	12
460	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	166.21	22
461	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	PWD	03/2018	03/2018	12/2019	162.56	21
462	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
463	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	10/2019	320.66	14
464	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	11/2019	3127.3	19
465	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	15525	62
466	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
467	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2019	2858	22
468	FORGED WHEEL PLANT	RINL	04/2014	09/2018	09/2019	1682.85	12
469	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2019	1154.18	23
470	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
471	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
472	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	BSNL	01/2018	10/2018	09/2019	231.8	11

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
473	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	07/2020	10773	19
474	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2020	216.69	67
475	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	09/2019	388	28
476	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	10/2019	156.57	38
477	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2019	270.83	59
478	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2020	171.86	54
479	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	17
480	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2020	165.23	89
481	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
482	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
483	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
484	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
485	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
486	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2020	197.33	14
487	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
488	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2020	496.18	40
489	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	CPWD	12/2016	07/2019	02/2020	549.31	7
490	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
491	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
492	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	02/2020	294	10
493	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	01/2021	430	8

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
494	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	10151.04	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7080.41	1173.3
7	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
8	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
9	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	345.92	142.98
13	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	4006.83	4475.92	469.09
14	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	3049.47	134.47
15	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
16	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
17	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
18	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	694	1097.54	403.54

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
20	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
21	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
22	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	682.9	138.99
23	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
24	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1683.06	821.27
25	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
26	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
27	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9997.11	6077.52
28	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	12865.92	1227.37
29	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
30	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
31	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
32	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6880.36	1769.03
33	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9072.36	4317.94
34	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
35	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4397.8	1906.22
38	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
39	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
40	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	9996.59	4643.59

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1592.34	210.5
42	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15164.05	797.47
43	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13740.53	1208.09
44	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
45	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
46	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
47	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
48	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
49	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
50	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	5024.35	3367.35
51	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
52	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
53	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3376	2342.93
54	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
55	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
56	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
57	RAMGANJMUHDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
58	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
59	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
60	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
61	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5021.45	2627.98

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
62	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
63	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
64	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
65	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
66	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
67	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	395	261.59
68	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
69	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
70	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
71	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	800	463.09
72	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
73	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	694	407
74	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
75	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
76	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
77	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	410.08	886.41	476.33
78	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
79	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	3000	673.48
80	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
81	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
82	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
83	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12524	8069.83
84	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
85	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	3300	2119.81
86	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
87	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4079.15	1996.4
88	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
89	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
90	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
91	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
92	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
93	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
94	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
95	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
96	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
97	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
98	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
99	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
100	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
101	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
102	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
103	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
104	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1300.44	714.51
105	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
106	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
108	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1500	551.96
109	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	1950	1236.52
110	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1200	272.99
111	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
112	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	1724.2	1993.24	269.04
113	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
114	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	2136.01	1265.05
115	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
116	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	2499.71	3382.95	883.24
117	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
118	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
119	KONDAPALLI-KOTHAGUDEM	SCR	04/2013	N.A.	723	997.09	274.09
120	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
121	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
122	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
123	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
124	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
125	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	471.81	210.43
126	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
127	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
128	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
129	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
131	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	728	414
132	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
133	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
134	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
135	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
136	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
137	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
138	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
139	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
140	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
141	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
142	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
143	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2300	1776.48
144	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
145	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2496.67	698.67
146	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	425.17	212.16
147	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
148	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
149	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
150	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	2609	2230.44
151	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
152	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
154	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
155	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
156	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
157	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	410	167.91
158	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
159	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
160	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
161	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
162	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
163	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
164	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
165	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
166	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
167	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1310.23	480.49
168	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	NFR	02/1999	04/2010	380.6	1871	1490.4
169	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	845.58	220.58
170	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
171	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	809.07	257.56
172	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
173	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
174	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	860.92	631.92
175	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
176	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	980	676.02
177	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
178	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756.92	1245.06
179	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
181	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
183	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2010	1560
184	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
185	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	898.53	573.8
186	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
187	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
188	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
189	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773
190	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
191	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	1352.74	648.43
192	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	305	120.94
193	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
194	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	693.8	151.62
195	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
196	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59
197	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	3860.4	356.71
198	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	346	226

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
199	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
200	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
201	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	525	245
202	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
203	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
204	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
205	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
206	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	PWD	03/2012	05/2012	207.03	389.45	182.42
207	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
208	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
209	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
210	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
211	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
212	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
213	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
214	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
215	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
216	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
217	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	186.96	305.61	118.65
218	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653.29	207.4
219	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	PWD	03/2009	09/2013	501	671.54	170.54
220	NAGOUR-BIKANER OF NH-11 (2L+PS) UNDER	PWD	01/2012	01/2014	378.07	478.73	100.66

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	PPP.						
221	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	279.7	398.52	118.82
222	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	PWD	08/2014	11/2017	823.2	937.76	114.56
223	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	PWD	08/2014	11/2017	600.87	720.97	120.1
224	FOUR LANNING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
225	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
226	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
227	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
228	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
229	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
230	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
231	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2525.8	1137.46
232	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
233	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
234	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
235	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
236	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
237	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
238	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
239	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	195.04	377.99	182.95
240	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	PWD	11/2010	02/2011	470.2	630.36	160.16
241	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	497.05	881.05	384
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	MORTH	01/1991	N.A.	675	780.77	105.77

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
243	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	445.89	653.29	207.4
244	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
245	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	2125.24	2521.24	396
246	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
247	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
248	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	193.69	327.92	134.23
249	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	624.41	992.67	368.26
250	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	408.77	241.13
251	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
252	JAL MARG VIKAS PROJECT	IWAI	01/2018	03/2023	4200	5369.18	1169.18

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
253	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	23140	7615

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
254	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
255	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
256	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79
257	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	5687.79	506
258	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
259	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
260	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
261	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	388	488.28	100.28

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
262	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	1,2320.00	1,7079.00	4759	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6840.00	3348	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	7080.41	1173.3	48
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144
8	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
10	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	4475.92	469.09	7
11	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497.00	6025.00	1528	26
12	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	723.40	413.59	58
13	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57
14	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	12/2019	694.00	1097.54	403.54	14

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	5245.96	657.67	15
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	3049.47	134.47	110
17	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	345.92	142.98	70
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	1683.06	821.27	79

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
19	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	6880.36	1769.03	24
20	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	1,18,46.00	1,27,39.82	893.82	29
21	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	2,13,12.11	1,26,19.1	118
22	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9072.36	4,317.94	12
23	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	08/2019	1779.29	2187.32	408.03	129
24	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	4397.80	1,906.22	114
25	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	5071.94	247.82	86
26	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	1,16,38.55	1,28,65.92	1,227.37	26
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,11,30.19	1,47,19.10	3,588.91	103
28	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	1891.41	526.89	40
29	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	5867.38	2,888.9	93
30	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	09/2020	1,25,32.44	1,37,40.53	1,208.09	21

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	1,4366.58	1,5164.05	797.47	27
32	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	1592.34	210.5	29
33	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353.00	9996.59	4643.59	98
34	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	1,2964.60	1,7304.00	4339.4	43
35	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	1,2176.28	2425.39	40
36	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9997.11	6077.52	147
37	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2019	2496.90	7927.34	5430.44	118
38	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657.00	5024.35	3367.35	76
39	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	639.46	151.97	63

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
40	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625.00	845.58	220.58	60
41	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288.00	4970.11	2682.11	9
42	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	809.07	257.56	12
43	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
44	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12
45	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.20	1993.24	269.04	9
46	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	NL								
47	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1200.00	272.99	12
48	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	1500.00	551.96	12
49	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	1120.00	177.05	24
50	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	1247.64	665.51	6
51	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	1300.44	714.51	16
52	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760.00	1182.31	422.31	15
53	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
54	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2024	2923.13	3791.66	868.53	180
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	1,2524.00	8069.83	108
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
57	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
58	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	3000.00	673.48	79
59	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	03/2021	410.08	886.41	476.33	25
60	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450.00	2010.00	1560	140
61	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	06/2022	2500.00	2,7949.00	25449	235
62	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
63	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
65	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
66	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
67	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
68	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
69	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	395.00	261.59	129
70	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	1928.07	1117.29	21
71	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	2072.50	1347.81	12
72	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	5021.45	2627.98	96
73	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	751.55	273.67	96
74	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	3860.40	356.71	12
75	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	1377.48	584.59	12
76	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR -BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
77	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	305.00	120.94	9
78	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12
79	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287.00	694.00	407	111
80	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.50	3712.50	1441	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
81	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	2980.41	2484.97	204
82	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
83	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	898.53	573.8	96
84	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	3300.00	2119.81	147
85	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
86	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	1756.92	1245.06	8
87	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2021	303.98	980.00	676.02	12
88	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	1310.23	480.49	12
89	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
90	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2019	148.77	377.00	228.23	36
91	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
92	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
93	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
94	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	348.55	102.47	6
95	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
96	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
97	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	05/2020	242.09	410.00	167.91	15
98	MANOHARPUR-BONDAMUNDA 3RD LINE	SER	04/2012	12/2018	06/2020	258.20	358.68	100.48	18

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	DOUBLING								
99	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548.00	819.01	271.01	24
100	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314.00	728.00	414	12
101	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
102	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2019	120.70	1800.00	1679.3	9
103	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
104	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
105	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
106	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	810.02	108.41	40
107	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229.00	860.92	631.92	15

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
108	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	12/2019	186.96	305.61	118.65	63
109	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	881.05	384	36
110	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108.00	2967.50	1859.5	100
111	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	09/2019	1266.60	1544.00	277.4	36
112	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	08/2019	199.81	340.14	140.33	124
113	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	1108.00	157.31	16
114	4-LANNING OF VARANASI	NHAI	03/2016	04/2019	10/2019	1587.49	2982.00	1394.51	6

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]								
115	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	746.43	299.14	24
116	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	09/2019	445.89	653.29	207.4	30
117	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	1420.00	131.93	12
118	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	992.67	368.26	105
119	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	327.92	134.23	110
120	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	377.99	182.95	116
121	4-LANING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	1232.76	108.65	33
122	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	09/2019	445.89	653.29	207.4	30
123	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	722.46	116.62	19

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
124	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	1,5525.00	2,3140.00	7615	62

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
125	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
126	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
127	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	09/2019	388.00	488.28	100.28	28

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
128	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	5687.79	506	29
129	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	2000.00	780.79	17

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
130	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	1,0151.04	5,5548.87	45397.8	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above					(August 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	-	.00	0
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	-	.00	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2020	.00	118
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	-	.00	0
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	-	.00	0
10	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
11	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
12	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	-	.00	0
13	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	08/2020	.00	128
14	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2019	.00	88
15	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
16	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
17	PATNA-MUZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	-	.00	0
18	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	06/2020	.00	71

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(August 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
19	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2019	.00	81
20	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
21	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	-	.00	0
22	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	05/2020	.00	42
23	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	0
24	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	10/2019	.00	27
25	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	06/2020	.00	82
26	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
27	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	-	.00	0
28	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	12/2019	.00	76
29	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	-	.00	0
30	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
31	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
32	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	06/2020	.00	78
33	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	0
34	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	03/2020	.00	19
35	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	12/2019	.00	63
36	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	-	.00	0
37	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
38	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (August 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	10/2019	.00	65
40	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	09/2019	21.90	36
41	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
42	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	-	.00	5
43	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
44	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
45	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	-	.00	0
46	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	-	.00	0
47	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
48	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
49	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	12/2019	.00	81
50	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
51	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	11/2019	.00	22
52	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
53	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	09/2020	.00	62
54	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	-	.00	0
55	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,159.00	01/2019	-	.00	0
56	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	05/2019	-	.00	0
57	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0
58	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,519.00	06/2015	-	16.67	0
59	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,521.24	12/2015	-	18.63	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (August 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
60	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	12/2019	.00	69
61	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73	0
62	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82	100
	Total		75,918.12 -	80,374.57				
	Grand Total		75,918.12	80,374.57				

State-wise Central Sector Project List

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					31.08.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	21.11 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [7/2019]	401.00 (401.00) [401.00]	98.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	148.80 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	22.17 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	19.87 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
10	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [2/2020]	601.02 (-) [601.02]	85.04 (0.00) [-]
11	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [10/2019]	272.19 (-) [272.19]	140.58 (0.00) [7]
	<u>Information And Broadcasting</u>				
12	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	2/2019 (-) [11/2019]	204.32 (-) [204.32]	0.00 (0.00) [9]
	<u>Petroleum</u>				
13	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD	1/2015	3/2021 (-)	342.00 (-)	0.00 (0.00)

	PIPELINE		[3/2021]	[342.00]	[0]
14	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	84.34 (0.00) [3]
15	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2020]	384.58 (-) [384.58]	85.86 (0.00) [-12]
16	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [2/2021]	580.20 (-) [580.20]	34.84 (0.00) [0]
17	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (9/2019) [9/2019]	420.76 (-) [407.45]	234.24 (-13.31) [12]
18	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (-) [8/2021]	34,012.00 (-) [34,012.00]	3,185.16 (0.00) [14]
19	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	14.07 (0.00) [10]
20	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
21	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	14.78 (0.00) [0]
22	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	5,887.49 (0.00) [0]
23	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	376.97 (0.00) [0]
	<u>Railways</u>				
24	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
25	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
26	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
27	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (-) [3,631.00]	407.42 (0.00) [12]
28	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (-) [2,120.16]	412.87 (1,074.96) [168]
29	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (-) [3,382.95]	373.22 (883.24) [0]
30	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	11.11 (0.50) [21]
31	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
32	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,288.70]	667.03 (0.00) [36]
33	NANDYAL-YERRAGUNTLA(NL),SCR	3/1996	2/2009 (-)	164.36 (-)	999.64 (885.64)

			[0/0]	[1,050.00]	[0]
34	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	925.36 (302.41) [0]
35	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	1,402.19 (0.00) [24]
	Road Transport And Highways				
36	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [11/2019]	328.67 (-) [328.67]	176.29 (0.00) [-]
37	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	70.71 (0.00) [0]
38	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [3/2020]	557.30 (-) [557.30]	174.99 (0.00) [-]
39	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (3/2020) [9/2019]	263.45 (-) [263.45]	87.58 (0.00) [24]
40	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (3/2020) [11/2019]	429.43 (-) [429.43]	195.88 (0.00) [24]
41	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [12/2020]	314.43 (-) [314.43]	24.90 (0.00) [-]
42	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (12/2019) [7/2018]	350.61 (-) [350.61]	303.71 (0.00) [0]
43	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
44	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]
45	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
46	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (12/2019) [12/2016]	333.21 (-) [333.21]	263.88 (0.00) [0]
47	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [4/2021]	1,532.62 (2,499.00) [2,499.00]	569.15 (966.38) [1]
48	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [11/2019]	648.33 (-) [648.33]	20.54 (0.00) [29]
49	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	21.73 (0.00) [0]
50	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (3/2020) [1/2020]	576.48 (-) [576.48]	196.46 (0.00) [24]
51	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (3/2020) [8/2018]	348.95 (-) [348.95]	157.26 (0.00) [0]
52	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [2/2017]	251.55 (-) [251.55]	7.74 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740	1/2016	5/2016 (8/2019)	386.09 (-)	168.28 (0.00)

	OF NH214(NH21		[5/2018]	[386.09]	[0]
54	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (3/2020) [5/2019]	290.15 (-) [290.15]	69.47 (0.00) [0]
55	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	68.81 (0.00) [-]
57	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (3/2020) [5/2018]	995.09 (995.00) [995.09]	401.90 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (3/2020) [9/2018]	444.84 (-) [444.84]	233.93 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (3/2020) [8/2019]	376.25 (-) [376.25]	189.59 (0.00) [24]
60	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (1/2020) [1/2020]	297.12 (294.00) [297.12]	177.05 (0.00) [18]
61	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (2/2020) [2/2020]	289.67 (290.00) [289.67]	80.47 (0.00) [18]
62	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (5/2020) [5/2020]	504.19 (504.00) [504.19]	269.70 (0.00) [18]
63	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (11/2019) [10/2017]	271.45 (-) [271.45]	152.72 (0.00) [0]
64	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (3/2020) [8/2019]	319.28 (-) [319.28]	103.79 (0.00) [24]
65	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [11/2019]	648.32 (-) [503.10]	1.15 (-145.22) [-4]
66	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (2/2020) [2/2020]	244.95 (245.00) [244.95]	101.40 (0.00) [18]
67	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (12/2019) [2/2019]	372.68 (-) [372.68]	179.88 (0.00) [0]
68	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2020) [3/2020]	228.32 (-) [228.32]	34.74 (0.00) [19]
69	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (8/2020) [8/2020]	418.03 (-) [418.03]	129.17 (0.00) [24]
70	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (1/2020) [1/2020]	378.24 (-) [378.24]	237.18 (0.00) [24]
71	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [7/2021]	1,959.00 (-) [1,959.00]	586.73 (0.00) [-]
72	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [7/2021]	1,323.15 (-) [1,323.15]	326.24 (0.00) [-]
73	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [7/2021]	1,550.98 (-) [1,550.98]	0.00 (0.00) [-]

74	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [10/2019]	1,535.00 (-) [1,535.00]	3,220.15 (0.00) [65]
75	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	751.70 (145.48) [2]
76	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
77	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
78	CENTRAL DISPATCH YARD	8/2015	8/2018 (10/2019) [10/2019]	320.66 (-) [320.66]	206.91 (0.00) [14]
79	COKE OVEN BATTERY-5	12/2011	12/2017 (10/2019) [10/2019]	2,858.00 (-) [2,500.00]	1,344.76 (-358.00) [22]
	<u>Urban Development</u>				
80	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [8/2019]	206.58 (-) [206.58]	82.23 (0.00) [5]
81	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
82	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [169.16]	163.98 (11.32) [0]
83	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>Water Resources</u>				
84	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (-) [6/2021]	10,151.04 (-) [55,548.87]	16,417.99 (45,397.83) [15]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
85	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (10/2019) [10/2019]	2,496.90 (7,927.34) [7,927.34]	7,516.58 (5,430.44) [118]
86	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,945.40 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
87	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	108.75 (0.00) [0]
88	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	272.92 (0.00) [21]
89	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	159.75 (0.00) [15]
90	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
91	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	115.02 (0.00) [0]
92	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM	1/2016	11/2016	183.65	90.29

	583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450		(-) [0/0]	(-) [183.65]	(0.00) [0]
93	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/	243.89	30.04
			(-) [0/0]	(-) [243.89]	(0.00) [0]
94	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/	189.91	154.43
			(-) [0/0]	(-) [189.91]	(0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/	259.52	143.01
			(-) [0/0]	(-) [259.52]	(0.00) [0]
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/	200.44	72.97
			(-) [0/0]	(-) [200.44]	(0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/	568.92	125.96
			(-) [0/0]	(-) [568.92]	(0.00) [0]
98	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/	188.78	30.88
			(-) [0/0]	(-) [188.78]	(0.00) [0]
99	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017	138.93	17.43
			(-) [1/2020]	(155.00) [155.00]	(16.07) [36]
100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	98.37
			(-) [9/2020]	(-) [245.79]	(0.00) [-]
101	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016	198.00	195.67
			(-) [10/2019]	(-) [198.00]	(0.00) [36]
102	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018	197.16	66.17
			(9/2015) [9/2018]	(197.16) [197.16]	(0.00) [0]
103	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	154.14
			(-) [0/0]	(-) [1,718.59]	(0.00) [0]
104	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017	1,253.10	211.21
			(-) [3/2022]	(-) [1,253.10]	(0.00) [60]
105	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017	167.28	18.70
			(2/2018) [2/2021]	(167.28) [167.28]	(0.00) [46]
106	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017	216.71	15.77
			(2/2018) [2/2021]	(216.71) [216.71]	(0.00) [46]
107	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
108	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	126.58
			(-) [12/2020]	(-) [434.06]	(0.00) [-]
109	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	64.66
			(3/2018) [3/2021]	(284.09) [284.09]	(0.00) [47]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	37.30
			(-) [0/0]	(-) [195.23]	(0.00) [0]
111	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	49.12
			(-) [0/0]	(-) [203.36]	(0.00) [0]
112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA)	1/2017	4/2017	194.66	75.04
			(-)	(-)	(0.00)

	TO KM.		[0/0]	[194.66]	[0]
113	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	24.14 (0.00) [0]
114	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (389.45) [389.45]	275.19 (182.42) [0]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	13.73 (0.00) [46]
116	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	28.67 (0.00) [46]
117	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
118	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
119	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
120	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	6.58 (0.00) [-]
121	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	5.63 (0.00) [-]
122	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	9.65 (0.00) [-]
123	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	6.19 (0.00) [-]
124	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (-) [0/0]	1,979.00 (-) [1,979.00]	59.40 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
125	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	<u>Health And Family Welfare</u>				
126	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
127	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
128	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
129	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	178.05 (0.00) [0]
130	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	531.40 (0.00) [0]
131	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CCGS, MADHUBAN	6/2016	8/2020 (-)	224.75 (-)	3.30 (0.00)

			[8/2020]	[224.75]	[0]
132	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
133	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (345.92) [345.92]	145.60 (142.98) [70]
134	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	263.70 (0.00) [1]
135	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2020]	543.91 (-) [682.90]	8.75 (138.99) [4]
136	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,526.40 (0.00) [0]
137	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	157.81 (15.64) [0]
138	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
139	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	704.09 (414.00) [12]
140	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	654.38 (-50.32) [-24]
141	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	502.44 (1,265.05) [0]
142	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	629.19 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
143	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	201.56 (0.00) [0]
144	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
145	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
146	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	66.66 (0.00) [0]
147	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	50.39 (0.00) [0]
148	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	356.31 (0.00) [0]
149	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	16.98 (0.00) [0]
150	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [12/2021]	252.00 (-) [252.00]	4.74 (0.00) [71]
151	4 LANING OF JORHAT TO JHANJI SECTION FROM KM.	6/2015	6/2018	437.39	9.30

	453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)		(12/2020) [12/2021]	(-) [437.39]	(0.00) [42]
152	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (2/2019) [4/2021]	294.17 (-) [294.17]	63.00 (0.00) [63]
153	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	451.15 (143.23) [0]
154	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
155	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.68 (7.98) [0]
156	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	304.28 (0.00) [0]
157	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	66.66 (0.00) [0]
158	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	58.58 (0.00) [-]
159	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	22.32 (0.00) [42]
160	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	292.24 (0.00) [0]
161	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	120.86 (0.00) [31]
162	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (456.92) [525.00]	488.37 (245.00) [0]
163	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
164	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
165	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [124]
166	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (408.77) [408.77]	395.78 (241.13) [0]
167	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	337.76 (22.00) [143]
168	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	328.47 (0.00) [136]
169	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	0.00 (0.00) [0]
170	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	224.28 (-70.66) [149]
171	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE	11/2014	2/2018 (-)	218.31 (307.47)	256.26 (89.16)

	KARIMGANJ		[0/0]	[307.47]	[0]
172	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
173	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	539.20 (-) [539.20]	25.64 (0.00) [0]
	<u>Petroleum</u>				
174	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	600.82 (0.00) [-10]
175	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	65.14 (0.00) [0]
176	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	142.71 (0.00) [0]
177	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	9.49 (0.00) [0]
178	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [8/2019]	822.66 (-) [822.66]	822.02 (0.00) [9]
179	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (-) [10/2019]	951.64 (-) [951.64]	325.42 (0.00) [0]
180	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	7.82 (0.00) [0]
181	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	13.88 (0.00) [0]
182	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [3/2020]	324.00 (-) [324.00]	150.02 (0.00) [-3]
	<u>Power</u>				
183	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (8/2021) [8/2021]	8,692.97 (21,312.11) [21,312.11]	16,331.92 (12,619.14) [118]
184	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (-) [9/2020]	5,353.00 (-) [9,996.59]	7,861.51 (4,643.59) [98]
185	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	777.63 (0.00) [0]
186	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (12/2021) [12/2021]	12,964.60 (17,304.00) [17,304.00]	13,716.26 (4,339.40) [43]
	<u>Railways</u>				
187	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [3/2023]	633.87 (-) [633.87]	0.40 (0.00) [-]
188	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (1,605.17) [1,605.17]	23.49 (0.00) [-]
189	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	1.91 (2,668.81) [-]
190	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/	378.56	376.63

			(-) [3/2022]	(-) [2,609.00]	(2,230.44) [-]
191	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR	7/2004	12/2007 (-) [0/0]	599.63 (674.00) [674.00]	0.00 (74.37) [0]
192	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12)	8/2010	3/2014 (-) [0/0]	400.00 (-) [400.00]	0.00 (0.00) [0]
193	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
194	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [3/2024]	205.00 (-) [205.00]	5.21 (0.00) [-]
195	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF,	4/1991	/ (-) [12/2021]	329.39 (803.11) [1,483.14]	845.59 (1,153.75) [-]
196	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [3/2024]	445.25 (-) [445.25]	1.14 (0.00) [-]
197	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (-) [1/2020]	213.01 (367.17) [425.17]	397.41 (212.16) [-]
198	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [3/2023]	528.65 (2,066.78) [2,066.78]	1,405.48 (1,538.13) [-]
199	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [3/2020]	324.73 (898.53) [898.53]	1,038.71 (573.80) [96]
200	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (-) [3/2022]	548.00 (-) [819.01]	488.95 (271.01) [24]
201	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [3/2022]	162.87 (614.45) [614.45]	305.70 (451.58) [-]
202	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/ (3/2022) [3/2022]	333.76 (-) [360.00]	6.67 (26.24) [-]
203	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [10/2021]	1,200.20 (1,200.20) [1,200.20]	396.80 (0.00) [19]
204	KOSI BRIDGE (NL), ECR	4/2002	3/2020 (-) [3/2020]	499.41 (516.02) [516.02]	390.53 (16.61) [0]
205	KURSELA-BIHARIGANJ (NL)	4/2008	/ (-) [3/2024]	192.56 (-) [192.56]	0.39 (0.00) [-]
206	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012 (-) [3/2020]	477.88 (751.55) [751.55]	673.58 (273.67) [96]
207	MOTIHARI-SITAMARHI (NL)	4/2006	/ (-) [3/2024]	211.00 (-) [1,006.00]	24.16 (795.00) [-]
208	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	4/2016	3/2021 (-) [3/2022]	731.64 (1,185.73) [1,185.73]	32.31 (454.09) [12]
209	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/ (-) [3/2024]	281.30 (-) [281.30]	0.60 (0.00) [-]
210	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/ (-)	228.05 (-)	1.53 (0.00)

			[3/2024]	[228.05]	[-]
211	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (546.71) [546.71]	541.07 (214.56) [0]
212	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [3/2024]	620.57 (-) [620.57]	0.28 (0.00) [-]
213	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2020]	532.87 (2,145.00) [2,145.00]	932.80 (1,612.13) [12]
214	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (-) [10/2019]	180.82 (726.31) [726.31]	497.81 (545.49) [-]
215	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [12/2022]	1,491.47 (-) [1,491.47]	438.38 (0.00) [33]
216	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [3/2022]	744.04 (1,215.54) [1,215.54]	54.14 (471.50) [12]
217	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (735.20) [735.20]	362.10 (410.20) [-]
218	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2021]	372.14 (1,470.50) [1,470.50]	761.68 (1,098.36) [-]
219	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [2/2023]	380.00 (519.33) [519.33]	138.35 (139.33) [-]
220	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [3/2024]	678.62 (-) [678.62]	17.20 (0.00) [-]
	<u>Road Transport And Highways</u>				
221	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013 (-) [0/0]	351.54 (-) [351.54]	329.40 (0.00) [0]
222	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [0/0]	511.54 (-) [511.54]	566.60 (0.00) [0]
223	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
224	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [0/0]	575.00 (-) [575.00]	843.67 (0.00) [0]
225	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	77.43 (0.00) [0]
226	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	0.00 (0.00) [0]
227	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	0.00 (0.00) [0]
228	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015 (-) [0/0]	288.24 (-) [288.24]	280.00 (0.00) [0]
229	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (-) [0/0]	2,598.00 (-) [2,598.00]	0.00 (0.00) [0]
230	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER	3/2017	3/2020 (-)	235.48 (-)	0.00 (-7.71)

	GHAT NEAR MUNGE		[5/2021]	[227.77]	[14]
231	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [496.20]	0.00 (0.00) [0]
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [683.83]	596.44 (0.00) [0]
233	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
234	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [553.30]	267.22 (0.00) [0]
235	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	93.11 (0.00) [0]
236	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	113.26 (0.00) [-]
237	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [10/2020]	642.41 (-) [642.41]	131.71 (0.00) [-]
238	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [4/2020]	322.09 (-) [322.09]	77.53 (0.00) [24]
239	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	753.03 (0.00) [0]
240	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [814.04]	384.48 (0.00) [-]
241	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
242	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	214.34 (0.00) [0]
243	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
244	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	885.47 (0.00) [0]
245	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	719.20 (0.00) [0]
246	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
247	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
248	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
249	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	113.67 (50.09) [0]
250	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]

251	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	278.45 (39.60) [0]
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	323.60 (19.42) [0]
253	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [780.77]	152.37 (105.77) [0]
254	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
255	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
256	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	102.51 (0.00) [54]
257	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	2.06 (0.00) [0]
258	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
259	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [10/2019]	399.54 (-) [399.54]	195.59 (0.00) [6]
260	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [854.80]	579.78 (0.00) [0]
261	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [516.13]	417.09 (0.00) [0]
262	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
263	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	153.43 (0.00) [52]
264	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [10/2019]	230.34 (-) [230.34]	178.39 (0.00) [0]
	<u>Urban Development</u>				
265	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [10/2020]	496.18 (496.00) [498.99]	85.74 (2.81) [40]
266	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
267	AMERA OC RCE	2/2015	3/2018 (-) [3/2020]	335.97 (-) [335.97]	51.25 (0.00) [24]
268	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	67.41 (0.00) [0]
269	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2020]	258.56 (-) [258.56]	178.86 (0.00) [48]
270	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020	164.49	82.91

			(-) [3/2020]	(-) [164.49]	(0.00) [0]
271	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	97.29 (0.00) [0]
272	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	4.02 (0.00) [0]
273	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,881.14 (0.00) [0]
274	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (-) [3/2020]	152.43 (-) [459.49]	191.51 (307.06) [60]
275	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
276	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	2.88 (0.00) [72]
277	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,044.21 (0.00) [0]
278	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
279	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
280	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	194.57 (0.00) [84]
281	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.42 (0.00) [0]
282	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
283	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	1.09 (0.00) [0]
	<u>Power</u>				
284	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (3/2020) [3/2020]	11,846.00 (-) [12,739.82]	12,349.43 (893.82) [29]
285	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,610.00 (0.00) [0]
	<u>Railways</u>				
286	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (10/2019) [10/2019]	872.00 (1,226.51) [1,226.51]	1,044.67 (354.51) [-2]
287	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [3/2020]	393.98 (-) [393.98]	241.23 (0.00) [0]
288	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [12/2022]	2,288.00 (-) [4,970.11]	619.50 (2,682.11) [9]
289	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2022)	1,973.00 (1,973.66)	139.42 (0.66)

			[12/2022]	[1,973.66]	[21]
290	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [12/2020]	3,055.00 (-) [3,055.00]	1,729.64 (0.00) [27]
291	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2023]	1,160.00 (-) [1,160.83]	682.29 (0.83) [36]
292	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
293	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [6/2020]	1,402.02 (-) [1,100.00]	1,029.98 (-302.02) [3]
	<u>Road Transport And Highways</u>				
294	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (3/2021) [3/2021]	1,029.96 (-) [1,261.05]	0.00 (231.09) [-]
295	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (3/2020) [3/2020]	726.67 (598.13) [598.13]	414.73 (-128.54) [23]
296	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (8/2018) [8/2018]	509.13 (-) [509.13]	412.66 (0.00) [0]
297	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (10/2019) [10/2019]	596.67 (-) [596.67]	389.78 (0.00) [17]
298	REHABILITATION AND UP GRADATION OF NH-12A FROM KM.191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	181.90 (0.00) [0]
299	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	445.75 (0.00) [0]
	<u>Steel</u>				
300	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2020) [7/2020]	15,525.00 (-) [23,140.00]	15,938.88 (7,615.00) [62]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
301	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,784.40 (-243.77) [5]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
302	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [12/2020]	233.38 (-) [233.38]	84.73 (0.00) [8]
	<u>Health And Family Welfare</u>				
303	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [9/2019]	204.44 (-) [204.44]	188.00 (0.00) [28]
304	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [8/2019]	293.65 (-) [293.65]	290.71 (0.00) [27]
305	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [2/2020]	156.56 (-) [156.65]	54.94 (0.09) [-]
306	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [10/2020]	414.11 (-) [513.89]	147.00 (99.78) [83]
	<u>Heavy Industry</u>				
307	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL	8/2016	9/2019	1,554.00	335.03

	TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA		(-) [9/2019]	(-) [1,554.00]	(0.00) [0]
	<u>Power</u>				
308	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (-) [12/2019]	1,394.52 (-) [1,394.52]	405.65 (0.00) [31]
	<u>Railways</u>				
309	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [3/2023]	295.68 (-) [295.68]	79.53 (0.00) [-]
310	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [197.17]	107.86 (40.52) [-]
	<u>Road Transport And Highways</u>				
311	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/ (-) [0/0]	771.18 (-) [7,558.00]	261.77 (6,786.82) [0]
312	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019 (-) [12/2019]	269.69 (-) [269.69]	0.00 (0.00) [3]
	<u>Telecommunications</u>				
313	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	367.03 (0.00) [0]
	<u>Urban Development</u>				
314	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (-) [6/2020]	197.33 (-) [197.33]	42.30 (0.00) [14]
315	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	/ (-) [0/0]	218.72 (-) [218.72]	0.00 (0.00) [0]
316	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	703.90 (0.00) [0]
317	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [11/2019]	271.90 (-) [271.90]	33.56 (0.00) [0]
318	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [0/0]	188.00 (-) [188.00]	146.45 (0.00) [0]
319	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [0/0]	38,585.00 (-) [38,585.00]	34,763.00 (0.00) [0]
320	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2021]	1,219.21 (-) [2,000.00]	330.83 (780.79) [17]
321	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (-) [238.56]	53.20 (0.00) [0]
322	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [11/2019]	4,264.00 (-) [4,439.23]	3,246.53 (175.23) [0]
323	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/ (8/2020) [3/2021]	392.00 (-) [392.00]	12.56 (0.00) [-]
324	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/ (-) [12/2020]	422.00 (-) [422.00]	14.20 (0.00) [-]
325	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [0/0]	2,694.00 (-) [2,694.00]	0.00 (0.00) [0]

326	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018 (-) [0/0]	248.20 (-) [248.20]	33.39 (0.00) [0]
	<u>GOA</u>				
	<u>Health And Family Welfare</u>				
327	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/	249.01	73.40
			(-) [5/2020]	(-) [249.01]	(0.00) [-]
	<u>Road Transport And Highways</u>				
328	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/	280.16	280.47
			(-) [0/0]	(-) [290.59]	(10.43) [0]
329	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/	184.05	91.39
			(-) [0/0]	(-) [184.05]	(0.00) [0]
330	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/	936.40	262.25
			(-) [0/0]	(-) [936.40]	(0.00) [0]
331	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/	298.33	153.33
			(-) [0/0]	(-) [298.33]	(0.00) [0]
332	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018	297.00	290.64
			(-) [0/0]	(-) [297.00]	(0.00) [0]
333	KARASWADA TO BAMBOLIM	3/2017	12/2019	852.67	108.04
			(-) [12/2019]	(852.67) [852.67]	(0.00) [0]
334	PATRADEVI TO KARASWADA 4L	3/2017	5/2020	634.32	102.33
			(-) [5/2020]	(634.32) [634.32]	(0.00) [0]
335	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/	773.98	259.46
			(-) [0/0]	(-) [773.98]	(0.00) [0]
336	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/	819.95	191.63
			(-) [0/0]	(-) [819.95]	(0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
337	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11,459.00	13,971.00
			(-) [6/2020]	(16,580.00) [16,580.00]	(5,121.00) [54]
	<u>Petroleum</u>				
338	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/	588.20	0.94
			(-) [8/2022]	(-) [588.20]	(0.00) [-]
339	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019	3,380.00	1,872.71
			(-) [9/2019]	(-) [3,380.00]	(0.00) [0]
340	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018	327.78	142.00
			(-) [10/2019]	(-) [200.00]	(-127.78) [18]
341	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020	1,342.00	6.30
			(-) [8/2020]	(-) [1,342.00]	(0.00) [0]
342	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020	906.00	85.08
			(-) [10/2020]	(-) [906.00]	(0.00) [8]
343	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK)	10/2018	3/2021	156.67	0.00
			(-) [3/2021]	(-) [156.67]	(0.00) [0]
344	INFRASTRUCTURE DEVLOPMENT TO FACILITATE GRID	9/2016	7/2020	208.35	108.00

	POWER IMPORT AT 220KV AT GUJARAT REFINERY		(-) [7/2020]	(-) [208.35]	(0.00) [0]
345	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [1,162.56]	371.09 (0.00) [0]
346	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [2/2021]	225.54 (-) [225.54]	0.00 (0.00) [0]
	<u>Power</u>				
347	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [9/2019]	193.14 (-) [193.14]	72.38 (0.00) [3]
348	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (-) [9/2019]	175.64 (-) [175.64]	92.78 (0.00) [12]
	<u>Railways</u>				
349	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	963.63 (106.70) [0]
350	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2021) [3/2021]	829.74 (1,215.34) [1,310.23]	1,363.06 (480.49) [12]
351	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [3/2017]	117.36 (196.95) [202.35]	404.70 (84.99) [0]
352	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (3/2020) [3/2020]	551.51 (809.07) [809.07]	616.90 (257.56) [12]
353	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2022) [3/2022]	318.24 (321.62) [321.62]	125.76 (3.38) [120]
354	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (3/2021) [3/2021]	691.84 (663.29) [663.29]	163.85 (-28.55) [12]
355	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	317.38 (0.00) [0]
356	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
357	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (-) [3/2021]	844.10 (-) [439.88]	92.69 (-404.22) [-]
358	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	222.83 (0.00) [9]
359	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
360	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2021]	1,548.66 (-) [1,548.66]	1,226.20 (0.00) [0]
361	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2022) [3/2022]	320.66 (858.56) [858.96]	534.00 (538.30) [36]
362	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2021) [3/2021]	1,002.39 (1,002.39) [1,002.39]	374.60 (0.00) [0]
363	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (3/2022) [3/2022]	1,037.15 (1,037.15) [1,037.15]	992.18 (0.00) [12]

364	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
Road Transport And Highways					
365	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	262.83 (0.00) [-]
366	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [1/2020]	829.97 (-) [829.97]	75.08 (0.00) [-]
367	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [8/2020]	1,958.88 (-) [1,958.88]	1,116.85 (0.00) [2]
368	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (2,521.24) [2,521.24]	4,659.71 (396.00) [0]
369	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [12/2019]	364.56 (-) [392.00]	240.57 (27.44) [-]
370	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
371	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	0.00 (0.00) [-]
372	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [1/2021]	2,702.05 (-) [2,702.05]	0.00 (0.00) [-]
373	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (386.19) [400.76]	4.45 (0.00) [0]
374	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (887.21) [962.43]	45.70 (0.00) [0]
375	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	90.63 (0.00) [0]
376	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [8/2019]	998.18 (-) [998.18]	435.25 (0.00) [-]
377	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [9/2019]	723.64 (-) [723.64]	321.67 (0.00) [-]
378	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [10/2019]	834.64 (-) [834.64]	140.44 (0.00) [-]
379	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [8/2019]	763.08 (-) [763.08]	357.12 (0.00) [-]
380	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,187.21 (0.00) [0]
381	JUNAGADH BYPASS	10/2017	10/2017 (-) [11/2019]	232.49 (-) [232.49]	0.00 (0.00) [25]
382	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [0/0]	953.88 (-) [953.88]	976.79 (0.00) [0]
383	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (1,449.00) [1,449.00]	1,296.87 (396.79) [-]

384	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [1/2021]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [-]
385	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
386	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	0.48 (0.00) [0]
387	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN	3/2018	11/2018 (-) [0/0]	464.07 (399.35) [464.07]	14.17 (0.00) [0]
388	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON	3/2016	2/2016 (-) [0/0]	208.34 (-) [208.34]	112.87 (0.00) [0]
389	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
390	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN	3/2016	2/2017 (-) [0/0]	223.67 (-) [223.67]	112.81 (0.00) [0]
	<u>Urban Development</u>				
391	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [7/2020]	10,773.00 (-) [10,773.00]	5,854.77 (0.00) [19]
392	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
393	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	106.43 (0.00) [0]
	<u>Health And Family Welfare</u>				
394	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [0/0]	505.58 (-) [523.00]	508.29 (17.42) [0]
	<u>Petroleum</u>				
395	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (-) [1/2021]	909.00 (-) [909.00]	13.11 (0.00) [0]
396	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [12/2019]	3,529.00 (-) [3,529.00]	1,562.10 (0.00) [5]
397	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	7.75 (0.00) [0]
398	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	67.92 (0.00) [0]
399	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (-) [2/2020]	598.00 (-) [598.00]	14.12 (0.00) [0]
400	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (-) [6/2021]	278.60 (-) [278.60]	0.00 (0.00) [0]
401	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	142.67 (0.00) [0]
402	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (9/2020)	286.42 (-)	1.19 (0.00)

			[9/2020]	[286.42]	[1]
	<u>Railways</u>				
403	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2020]	346.32 (-) [346.32]	286.78 (0.00) [12]
404	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [3/2021]	287.00 (-) [694.00]	220.42 (407.00) [111]
	<u>Road Transport And Highways</u>				
405	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [9/2019]	602.95 (507.70) [507.70]	494.29 (-95.25) [39]
406	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [9/2019]	574.28 (537.16) [537.16]	491.45 (-37.12) [14]
407	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [9/2019]	639.79 (-) [552.90]	480.73 (-86.89) [6]
408	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [0/0]	2,128.72 (-) [2,128.72]	971.24 (0.00) [0]
409	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (7/2019) [0/0]	276.01 (-) [276.01]	187.39 (0.00) [0]
410	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (3/2020) [9/2019]	247.25 (-) [247.25]	144.71 (0.00) [6]
411	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [11/2019]	248.97 (-) [248.97]	241.69 (0.00) [6]
412	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [12/2020]	1,484.30 (-) [1,484.30]	45.34 (0.00) [-]
413	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [2/2019]	1,004.67 (-) [1,004.67]	576.86 (0.00) [0]
414	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [118]
415	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
416	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
417	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	0.00 (0.00) [0]
418	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (-) [0/0]	1,243.45 (-) [1,243.45]	0.00 (0.00) [0]
419	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (-) [0/0]	889.36 (-) [889.36]	0.00 (0.00) [0]
420	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (-) [0/0]	1,018.79 (-) [1,018.79]	0.00 (0.00) [0]
421	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (-) [0/0]	1,051.91 (-) [1,051.91]	0.00 (0.00) [0]
422	ISMAILABAD-NARNAUL PKG-6	1/2019	/	1,120.06	0.00

			(-) [0/0]	(-) [1,120.06]	(0.00) [0]
423	ISMAILABAD-NARNAUL PKG-7	1/2019	/	1,137.42	0.00
			(-) [0/0]	(-) [1,137.42]	(0.00) [0]
424	ISMAILABAD-NARNAUL PKG-8	1/2019	/	1,033.19	0.00
			(-) [0/0]	(-) [1,033.19]	(0.00) [0]
425	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011	1,108.00	3,982.72
			(-) [3/2020]	(2,967.50) [2,967.50]	(1,859.50) [100]
426	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/	551.58	0.00
			(-) [3/2020]	(-) [551.58]	(0.00) [-]
427	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/	275.12	0.00
			(-) [3/2020]	(-) [275.12]	(0.00) [-]
428	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI	3/2018	/	307.79	0.00
			(-) [3/2020]	(-) [307.79]	(0.00) [-]
429	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/	181.78	0.00
			(-) [6/2020]	(-) [181.78]	(0.00) [-]
430	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/	198.05	0.00
			(-) [3/2020]	(-) [198.05]	(0.00) [-]
431	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/	795.50	80.90
			(-) [7/2021]	(-) [799.30]	(3.80) [-]
432	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/	634.70	2.55
			(-) [7/2021]	(931.21) [931.21]	(296.51) [-]
	<u>HIMACHAL PRADESH</u>				
	<u>Health And Family Welfare</u>				
433	AIIMS BILASPUR	4/2018	9/2021	1,351.00	137.87
			(-) [9/2021]	(-) [1,351.00]	(0.00) [0]
	<u>Petroleum</u>				
434	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019	151.00	147.35
			(-) [6/2019]	(-) [151.00]	(0.00) [0]
	<u>Power</u>				
435	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009	3,919.59	7,551.56
			(-) [12/2021]	(-) [9,997.11]	(6,077.52) [147]
	<u>Railways</u>				
436	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026	2,966.99	370.26
			(-) [12/2026]	(-) [7,000.00]	(4,033.01) [0]
	<u>Road Transport And Highways</u>				
437	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019	273.20	267.38
			(-) [6/2019]	(-) [273.20]	(0.00) [0]
438	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020	2,485.93	704.29
			(-) [9/2021]	(-) [2,485.93]	(0.00) [15]
439	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016	1,916.79	1,948.92
			(-) [0/0]	(-) [1,916.79]	(0.00) [0]
440	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018	934.46	452.30
			(-)	(-)	(0.00)

			[0/0]	[934.46]	[0]
441	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/	478.74	0.00
			(-)	(-)	(0.00)
			[5/2021]	[478.74]	[-]
442	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/	1,273.71	0.00
			(-)	(-)	(0.00)
			[7/2020]	[1,273.71]	[-]
443	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/	447.75	179.17
			(-)	(-)	(0.00)
			[11/2019]	[447.75]	[-]
444	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/	1,583.18	234.67
			(-)	(-)	(0.00)
			[9/2020]	[1,583.18]	[-]
	<u>Urban Development</u>				
445	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	270.83	199.91
			(-)	(-)	(0.00)
			[10/2019]	[270.83]	[59]
	<u>JAMMU AND KASHMIR</u>				
	<u>Civil Aviation</u>				
446	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021	323.19	10.00
			(-)	(-)	(0.00)
			[9/2021]	[323.19]	[0]
	<u>Railways</u>				
447	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002	2,500.00	19,223.83
			(-)	(27,949.00)	(25,449.00)
			[6/2022]	[27,949.00]	[235]
	<u>Road Transport And Highways</u>				
448	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/	1,471.75	376.15
			(-)	(1,339.00)	(-132.75)
			[1/2021]	[1,339.00]	[-]
449	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019	2,168.66	621.26
			(-)	(-)	(0.00)
			[12/2020]	[2,168.66]	[18]
450	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018	2,136.97	1,214.48
			(12/2019)	(2,273.00)	(0.00)
			[7/2020]	[2,136.97]	[19]
451	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013	1,813.76	2,393.99
			(-)	(-)	(0.00)
			[0/0]	[1,813.76]	[0]
452	NASHRI- CHANANI	5/2011	6/2015	2,159.00	4,705.68
			(-)	(2,519.00)	(360.00)
			[0/0]	[2,519.00]	[0]
453	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015	1,987.00	2,700.67
			(12/2019)	(-)	(0.00)
			[9/2020]	[1,987.00]	[62]
454	SRINAGAR TO BANIHAL	6/2011	6/2014	1,100.70	2,075.87
			(-)	(-)	(0.00)
			[0/0]	[1,100.70]	[0]
455	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019	253.44	0.00
			(-)	(-)	(0.00)
			[0/0]	[253.44]	[0]
456	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018	404.17	70.31
			(-)	(-)	(0.00)
			[0/0]	[404.17]	[0]
457	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018	216.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[216.00]	[0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
458	AMRAPALI OC(12MTY)	2/2012	3/2020	858.11	187.12
			(-)	(-)	(0.00)

			[3/2020]	[858.11]	[0]
459	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	90.13 (0.00) [0]
460	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2021]	163.51 (-) [163.51]	106.41 (0.00) [120]
461	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	82.01 (0.00) [0]
462	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
463	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2021]	162.46 (-) [162.46]	89.85 (0.00) [84]
464	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [3/2020]	289.45 (-) [289.45]	256.83 (0.00) [70]
465	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2022]	706.40 (-) [706.40]	354.66 (0.00) [116]
466	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [0/0]	1,230.27 (-) [1,230.27]	386.80 (0.00) [0]
467	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [0/0]	339.88 (-) [339.88]	12.08 (0.00) [0]
468	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.24 (0.00) [0]
469	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	163.23 (0.00) [0]
470	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [11/2019]	269.82 (-) [269.82]	180.83 (0.00) [67]
471	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2021]	510.85 (-) [510.85]	362.47 (0.00) [60]
472	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2021]	264.68 (-) [264.68]	179.87 (0.00) [108]
	<u>Petroleum</u>				
473	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	17.78 (0.00) [0]
474	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	43.56 (0.00) [0]
475	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	48.29 (0.00) [0]
476	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (910.23) [910.23]	340.16 (86.96) [-12]
477	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	22.55 (0.00) [0]
	<u>Power</u>				
478	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019	14,366.58	9,131.59

			(9/2019) [9/2021]	(-) [15,164.05]	(797.47) [27]
479	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,268.00 (314.04) [0]
480	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2023]	18,668.00 (-) [18,668.00]	1,904.30 (0.00) [0]
	<u>Railways</u>				
481	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2021]	1,724.20 (-) [1,993.24]	384.82 (269.04) [9]
482	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	164.09 (0.00) [-3]
483	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	3/1999	/ (-) [3/2021]	1,033.07 (3,020.95) [3,376.00]	3,290.02 (2,342.93) [-]
484	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2021]	459.91 (1,625.87) [1,625.87]	498.90 (1,165.96) [-]
485	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (12/2018) [6/2020]	258.20 (358.68) [358.68]	258.09 (100.48) [18]
486	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [12/2019]	148.77 (-) [377.00]	180.95 (228.23) [36]
	<u>Road Transport And Highways</u>				
487	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [6/2019]	239.68 (-) [235.90]	91.24 (-3.78) [0]
488	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [9/2019]	165.50 (-) [172.16]	117.09 (6.66) [-6]
489	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (3/2019) [3/2021]	1,005.08 (1,073.10) [1,005.08]	0.00 (0.00) [-]
490	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [7/2019]	997.15 (-) [997.15]	728.62 (0.00) [0]
491	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
492	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [1/2020]	323.72 (-) [323.72]	252.99 (0.00) [17]
493	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
494	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [6/2020]	212.99 (-) [212.99]	80.47 (0.00) [0]
495	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
496	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (12/2017) [12/2019]	458.03 (-) [458.03]	303.12 (0.00) [-]
	<u>Steel</u>				
497	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (11/2019)	1,154.18 (-)	944.78 (0.00)

			[11/2019]	[1,154.18]	[23]
498	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (6/2020) [6/2020]	1,034.01 (-) [1,034.01]	432.82 (0.00) [32]
499	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (6/2020) [6/2020]	262.87 (-) [262.87]	104.85 (0.00) [12]
	<u>Urban Development</u>				
500	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [9/2020]	171.86 (-) [171.86]	80.08 (0.00) [54]
501	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
502	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
503	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
504	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
505	BSVI UPGRADATION	9/2016	12/2019 (7/2020) [7/2020]	1,810.00 (1,810.00) [1,810.00]	726.57 (0.00) [7]
506	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [10/2018]	224.00 (207.00) [185.00]	164.61 (-39.00) [0]
507	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	38.34 (0.00) [0]
508	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	606.89 (93.00) [0]
509	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	6.94 (0.00) [0]
510	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (9/2019) [9/2019]	135.00 (170.70) [170.70]	154.03 (35.70) [6]
511	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	0.53 (0.00) [0]
512	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [9/2020]	581.00 (-) [621.00]	68.27 (40.00) [6]
513	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
514	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [12/2019]	445.89 (-) [445.89]	272.00 (0.00) [10]
	<u>Railways</u>				
515	ARSIKERE-TUMKUR	3/2015	3/2020 (-) [3/2020]	578.00 (-) [578.00]	509.07 (0.00) [0]
516	BAGALKOT-KUDACHI NL	4/2010	3/2016	986.30	297.70

			(-) [12/2023]	(-) [986.30]	(0.00) [93]
517	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
518	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [367.77]	0.00 (40.52) [-]
519	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [692.43]	0.00 (134.43) [-]
520	GADAG-WADI NL	4/2013	12/2018 (-) [12/2024]	2,841.84 (-) [2,841.84]	113.63 (0.00) [72]
521	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,900.00]	1,630.89 (773.00) [0]
522	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [3/2021]	1,156.94 (-) [1,140.93]	786.13 (-16.01) [12]
523	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [2,135.00]	144.76 (-180.00) [-]
524	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (-) [889.52]	438.39 (244.74) [36]
525	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	28.51 (0.00) [93]
526	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
527	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
528	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [1,801.01]	44.36 (0.00) [-]
529	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (-) [348.85]	0.35 (0.00) [-]
	Road Transport And Highways				
530	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (3/2017) [8/2020]	1,167.42 (870.00) [870.00]	254.96 (-297.42) [17]
531	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	113.59 (0.00) [0]
532	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [52]
533	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [11/2020]	701.40 (-) [701.40]	29.48 (0.00) [20]
534	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [20]
535	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]
536	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE	5/2018	5/2018	171.60	0.86

	FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT		(-) [5/2020]	(-) [171.60]	(0.00) [24]
537	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [3/2020]	1,388.00 (-) [1,388.00]	1,138.07 (0.00) [19]
538	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	657.08 (0.00) [0]
539	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [12/2019]	946.00 (-) [946.00]	818.53 (0.00) [18]
540	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	62.54 (0.00) [0]
541	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
542	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
543	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
544	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
545	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	626.56 (440.84) [3]
546	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [7/2020]	831.58 (-) [1,177.00]	567.90 (345.42) [4]
547	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (10/2019) [0/0]	2,177.80 (2,283.50) [2,450.00]	691.88 (272.20) [0]
548	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (5/2019) [11/2021]	1,995.34 (2,190.00) [2,400.00]	1,371.02 (404.66) [-]
549	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
550	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
551	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [12/2020]	950.69 (1,008.00) [1,108.00]	1,353.61 (157.31) [16]
552	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
553	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
554	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
555	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
556	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-	9/2017	10/2018 (-)	191.60 (-)	26.24 (0.00)

	HULIYAR		[0/0]	[191.60]	[0]
557	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [8/2019]	291.49 (-) [291.49]	130.00 (0.00) [24]
558	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
559	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
560	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
561	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
562	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
563	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	<u>Urban Development</u>				
564	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
565	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
566	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
567	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [9/2020]	246.31 (-) [246.31]	65.84 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
568	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	507.00 (395.24) [32]
569	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [0/0]	607.06 (-) [714.25]	355.02 (107.19) [0]
570	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	1,014.00 (-24.04) [8]
571	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [11/2019]	4,588.29 (5,245.96) [5,245.96]	3,588.88 (657.67) [15]
572	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	15.17 (0.00) [0]
	<u>Railways</u>				
573	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (2,815.62) [2,815.62]	264.28 (1,249.62) [0]
574	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (189.24) [189.24]	6.72 (0.00) [0]
575	KUMBALAM-TURAVUR	4/2011	/ (-)	252.96 (252.96)	8.50 (0.00)

			[0/0]	[252.96]	[0]
576	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
577	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (6/2022) [0/0]	1,431.90 (1,431.90) [1,431.90]	75.00 (0.00) [0]
578	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (828.50) [828.50]	0.08 (-171.50) [0]
	<u>Road Transport And Highways</u>				
579	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [10/2019]	845.24 (-) [941.00]	814.55 (95.76) [-]
580	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [1/2020]	804.97 (-) [804.97]	425.58 (0.00) [19]
581	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,232.76]	278.60 (108.65) [33]
582	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
583	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [12/2019]	255.75 (348.00) [348.43]	290.12 (92.68) [27]
584	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [88]
	<u>Urban Development</u>				
585	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
586	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	89.66 (0.00) [89]
587	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [12/2019]	5,181.79 (-) [5,687.79]	5,188.00 (506.00) [29]
	<u>MADHYA PRADESH</u>				
	<u>Coal</u>				
588	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	116.09 (0.00) [0]
589	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
590	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
591	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2021]	1,186.64 (-) [203.82]	117.55 (-982.82) [-24]
592	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	0.00 (0.00) [0]
593	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	20.30 (0.00) [0]
594	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-)	1,255.17 (-)	94.84 (0.00)

			[3/2022]	[1,255.17]	[0]
595	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	0.00 (0.00) [0]
596	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	265.78 (0.00) [0]
597	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	47.39 (0.00) [0]
598	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	27.10 (0.00) [0]
599	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	103.99 (0.00) [0]
600	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
601	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
602	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [8/2020]	236.00 (-) [236.00]	24.15 (0.00) [2]
	<u>Power</u>				
603	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [1,587.16]	306.71 (-517.05) [0]
604	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (3/2020) [3/2020]	11,638.55 (-) [12,865.92]	12,045.10 (1,227.37) [26]
605	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [1/2020]	9,870.51 (-) [11,148.86]	8,449.85 (1,278.35) [0]
	<u>Railways</u>				
606	ANUPPUR-KATNI	4/2015	12/2021 (12/2021) [12/2021]	1,370.00 (1,370.00) [1,370.00]	281.19 (0.00) [0]
607	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.85 (-) [1,485.85]	1,053.80 (0.00) [0]
608	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (10/2019) [10/2019]	383.79 (1,413.76) [1,413.76]	1,324.64 (1,029.97) [-]
609	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (3/2020) [6/2020]	585.93 (737.72) [1,300.44]	646.30 (714.51) [16]
610	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (6/2021) [6/2021]	700.00 (603.69) [603.69]	86.45 (-96.31) [12]
611	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2022]	1,763.93 (-) [1,763.93]	624.49 (0.00) [24]
612	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [9/2022]	582.13 (-) [1,247.64]	154.63 (665.51) [6]
613	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2023]	2,478.23 (-) [2,478.23]	367.59 (0.00) [12]

614	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [2/2020]	174.00 (-) [174.00]	150.62 (0.00) [11]
615	RAMGANJMUUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2023]	424.60 (-) [2,909.99]	1,926.25 (2,485.39) [24]
616	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2023) [3/2023]	3,503.69 (3,338.15) [3,860.40]	1,676.43 (356.71) [12]
	Road Transport And Highways				
617	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [11/2019]	191.21 (-) [191.21]	72.02 (0.00) [0]
618	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (-) [1/2020]	249.05 (-) [249.05]	118.29 (0.00) [18]
619	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	182.80 (0.00) [0]
620	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN)	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	0.00 (0.00) [0]
621	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (-) [11/2019]	392.33 (-) [392.33]	224.94 (0.00) [20]
622	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [8/2019]	227.49 (-) [227.49]	140.57 (0.00) [7]
623	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]
624	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	17.41 (0.00) [40]
625	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
626	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2020]	390.51 (-) [390.51]	191.77 (0.00) [-]
627	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [0/0]	743.88 (-) [743.88]	0.00 (0.00) [0]
628	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [6/2020]	205.05 (-) [205.05]	73.22 (0.00) [39]
629	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (-) [3/2021]	264.50 (-) [264.50]	0.00 (0.00) [0]
630	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (-) [6/2019]	1,583.79 (-) [1,583.79]	1,568.11 (0.00) [0]
631	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [8/2020]	960.24 (-) [960.24]	328.34 (0.00) [-]
632	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
633	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]

634	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (6/2015) [6/2015]	928.83 (-) [928.83]	588.21 (0.00) [0]
635	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [10/2019]	794.30 (622.00) [622.00]	543.86 (-172.30) [-]
636	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [10/2019]	795.76 (622.00) [622.00]	601.52 (-173.76) [-]
637	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	623.93 (0.00) [0]
638	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	274.24 (0.00) [27]
639	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	0.00 (0.00) [0]
640	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (-) [2/2020]	957.54 (-) [957.54]	467.50 (0.00) [0]
641	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [5/2020]	497.05 (-) [881.05]	544.84 (384.00) [36]
642	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
643	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,342.77 (0.00) [0]
644	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (-) [1/2020]	628.45 (-) [628.45]	248.66 (0.00) [0]
645	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [10/2019]	410.72 (-) [410.72]	0.00 (0.00) [54]
646	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [7/2020]	169.63 (-) [169.63]	9.35 (0.00) [28]
647	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [8/2019]	178.23 (-) [178.23]	114.16 (0.00) [11]
648	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (-) [11/2019]	287.34 (-) [287.34]	148.65 (0.00) [10]
649	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [11/2019]	877.79 (-) [877.79]	436.12 (0.00) [5]
650	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (-) [11/2019]	235.91 (-) [235.91]	97.39 (0.00) [21]
651	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [2/2020]	809.16 (-) [809.16]	219.42 (0.00) [19]
652	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
653	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [3/2020]	954.43 (-) [954.43]	298.00 (0.00) [54]
654	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA	3/2015	8/2017	511.83	240.05

	PRADESH KM 68/4 TO 142/200		(-) [2/2020]	(-) [511.83]	(0.00) [30]
655	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	254.17 (-) [254.17]	139.41 (0.00) [21]
656	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	233.04 (-) [233.04]	95.28 (0.00) [20]
657	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [4/2020]	279.44 (-) [279.44]	76.00 (0.00) [25]
658	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	166.21 (-) [166.21]	26.72 (0.00) [22]
659	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	184.62 (-) [184.62]	55.27 (0.00) [21]
660	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	214.69 (-) [214.69]	19.35 (0.00) [20]
661	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	217.22 (-) [217.22]	12.39 (0.00) [22]
662	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [12/2019]	162.56 (-) [162.56]	88.47 (0.00) [21]
663	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [5/2020]	373.82 (-) [373.82]	116.33 (0.00) [8]
	<u>Urban Development</u>				
664	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	34.12 (0.00) [0]
665	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	42.62 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
666	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	358.89 (-) [358.89]	29.73 (0.00) [0]
	<u>Coal</u>				
667	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	21.02 (44.53) [12]
668	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	183.61 (0.00) [0]
669	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	200.77 (0.00) [0]
670	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	268.57 (0.00) [0]
671	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [3/2021]	252.71 (-) [252.71]	42.94 (0.00) [0]
672	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	126.12 (221.74) [0]
673	BHATADI EXPANSION OC MINE	2/2016	3/2019	304.52	153.29

			(-) [0/0]	(-) [304.52]	(0.00) [0]
674	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	413.13 (0.00) [0]
675	GAURI DEEP OC	10/2016	3/2019 (-) [0/0]	164.96 (-) [164.96]	93.37 (0.00) [0]
676	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2024]	277.65 (-) [313.34]	115.50 (35.69) [36]
677	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	319.93 (0.00) [0]
678	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	182.51 (0.00) [0]
679	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [0/0]	295.56 (-) [295.56]	123.60 (0.00) [0]
680	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	213.24 (0.00) [0]
681	SAONER I UG TO OC PHASE I	11/2016	3/2022 (-) [3/2022]	162.10 (-) [162.10]	50.56 (0.00) [0]
682	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	121.74 (0.00) [0]
683	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	318.14 (-) [318.14]	146.45 (0.00) [0]
	Fertilisers				
684	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	175.19 (0.00) [0]
685	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (-) [9/2019]	197.79 (-) [209.44]	164.78 (11.65) [34]
	Health And Family Welfare				
686	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [2/2020]	582.99 (-) [582.99]	112.97 (0.00) [-]
687	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA	8/2017	3/2019 (-) [10/2019]	274.19 (-) [274.19]	169.93 (0.00) [7]
	Information And Broadcasting				
688	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	3/2020 (-) [3/2020]	167.70 (-) [167.70]	0.00 (0.00) [0]
689	NATIONAL FILM HERITAGE MISSION	11/2014	/ (-) [0/0]	597.41 (-) [597.41]	29.80 (0.00) [0]
	Petroleum				
690	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	58.33 (0.00) [0]
691	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (-) [11/2019]	968.61 (-) [1,033.95]	912.74 (65.34) [0]
692	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR	5/2016	1/2021	261.00	41.42

	CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI		(-) [1/2021]	(-) [261.00]	(0.00) [0]
693	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	38.55 (0.00) [3]
694	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	30.75 (0.00) [9]
695	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2019) [12/2019]	861.79 (-) [1,683.06]	1,314.42 (821.27) [79]
696	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (3/2020) [3/2020]	546.15 (565.15) [565.15]	442.18 (19.00) [4]
697	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (-) [11/2019]	511.30 (-) [511.30]	463.01 (0.00) [0]
698	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,292.46]	275.27 (0.00) [0]
699	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (12/2021) [12/2021]	4,006.83 (-) [4,475.92]	2,770.16 (469.09) [7]
700	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (-) [4,619.94]	4,340.39 (0.00) [27]
701	HEERA REDEVELOPMENT - PHASE III	5/2019	12/2021 (-) [3/2022]	2,494.68 (-) [2,494.68]	0.00 (0.00) [3]
702	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [9/2019]	554.00 (-) [554.00]	350.36 (0.00) [-5]
703	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,908.01 (606.02) [57]
704	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	941.98 (0.00) [0]
705	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2020) [5/2020]	3,190.69 (-) [3,247.19]	2,216.11 (56.50) [25]
706	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	155.28 (0.00) [0]
707	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (-) [3/2022]	3,228.80 (-) [3,228.80]	428.31 (0.00) [0]
708	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (12/2019) [12/2019]	6,068.80 (-) [5,296.93]	4,758.62 (-771.87) [8]
709	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	2/2019	4/2021 (-) [5/2021]	3,660.71 (3,740.05) [3,740.05]	126.66 (79.34) [1]
710	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [3/2020]	4,199.00 (5,060.00) [5,060.00]	2,592.90 (861.00) [0]
711	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	2,230.96 (0.00) [14]
712	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (-)	763.92 (-)	0.00 (0.00)

			[12/2020]	[763.92]	[0]
713	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	440.41 (0.00) [0]
714	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	121.12 (0.00) [0]
	Power				
715	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
	Railways				
716	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (12/2019) [12/2019]	184.06 (199.12) [305.00]	269.00 (120.94) [9]
717	AHMEDNAGAR-PARLI VAJINATH(NL) CR	2/1997	3/2021 (-) [3/2022]	2,271.50 (-) [3,712.50]	2,347.12 (1,441.00) [12]
718	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2021]	495.44 (1,781.98) [2,980.41]	1,414.47 (2,484.97) [204]
719	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	94.83 (205.27) [0]
720	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	713.48 (-) [1,950.00]	1,858.81 (1,236.52) [0]
721	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
722	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
723	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (-) [2,449.91]	156.29 (0.00) [0]
724	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2022]	792.89 (-) [1,377.48]	301.24 (584.59) [12]
725	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	76.32 (0.00) [24]
726	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2019]	305.00 (-) [305.00]	260.88 (0.00) [9]
727	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
728	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (3/2021) [3/2021]	5,300.00 (918.53) [918.53]	277.61 (-4,381.47) [84]
729	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2022]	3,627.47 (3,627.00) [3,627.47]	674.45 (0.00) [-24]
730	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
731	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (3/2023) [3/2023]	1,908.51 (2,686.63) [2,686.63]	443.56 (778.12) [0]
732	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016	714.10	65.20

			(-) [0/0]	(-) [714.10]	(0.00) [0]
733	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
734	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
735	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (3/2023) [3/2023]	229.00 (403.00) [860.92]	39.69 (631.92) [15]
736	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	56.45 (0.00) [12]
737	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,272.19]	281.97 (0.00) [12]
738	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,208.28 (0.00) [0]
739	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	223.82 (0.00) [24]
	<u>Road Transport And Highways</u>				
740	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
741	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
742	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [10/2019]	972.50 (-) [972.50]	1,492.00 (0.00) [27]
743	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	120.17 (0.00) [-]
744	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [4/2021]	621.00 (-) [621.00]	303.91 (0.00) [-]
745	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [5/2020]	923.04 (-) [923.04]	750.87 (0.00) [42]
746	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
747	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,071.61]	336.37 (0.00) [-]
748	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	38.97 (0.00) [24]
749	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [8/2020]	1,098.06 (-) [1,160.64]	1,082.97 (62.58) [5]
750	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	726.85 (0.00) [0]
751	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	0.00 (0.00) [0]
752	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43	11/2016	3/2019	400.25	64.89

	(FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI		(-) [2/2021]	(-) [400.25]	(0.00) [23]
753	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/	1,064.88	0.00
			(-) [7/2021]	(-) [1,064.88]	(0.00) [-]
754	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (5/2018) [11/2020]	1,059.73 (1,071.00) [1,071.00]	556.63 (11.27) [44]
755	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [5/2020]	1,030.44 (-) [1,065.51]	1,027.16 (35.07) [2]
756	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (-) [1,043.28]	1,094.73 (54.94) [5]
757	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [9/2020]	505.00 (-) [504.00]	220.70 (-1.00) [28]
758	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [8/2019]	422.38 (422.38) [422.38]	169.58 (0.00) [0]
759	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [8/2019]	955.40 (-) [955.40]	338.50 (0.00) [0]
760	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [2/2020]	211.42 (-) [211.42]	131.85 (0.00) [12]
761	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	37.05 (0.00) [0]
762	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	182.98 (0.00) [0]
763	AMD I TO SAONER	1/2017	6/2019 (-) [8/2019]	396.91 (396.91) [396.91]	248.48 (0.00) [2]
764	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2020]	426.06 (426.00) [426.06]	66.97 (0.00) [0]
765	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [12/2019]	309.94 (310.00) [309.94]	51.32 (0.00) [0]
766	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	91.75 (0.00) [0]
767	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	22.27 (0.00) [0]
768	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [4/2020]	241.69 (242.00) [241.69]	146.29 (0.00) [0]
769	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	148.00 (0.00) [31]
770	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [11/2019]	259.55 (260.00) [259.55]	145.00 (0.00) [0]
771	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	281.60 (0.00) [0]
772	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-)	743.21 (743.21)	131.87 (0.00)

			[6/2021]	[743.21]	[0]
773	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	162.64 (0.90) [0]
774	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	118.95 (0.00) [0]
775	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [12/2019]	206.97 (207.00) [206.97]	78.89 (0.00) [0]
776	CHIKALI TO DHAD	3/2018	12/2019 (-) [12/2019]	189.46 (189.00) [189.46]	21.54 (0.00) [0]
777	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [10/2019]	548.03 (548.00) [548.03]	287.00 (0.00) [4]
778	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2019]	393.10 (393.10) [393.10]	125.97 (0.00) [0]
779	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	146.72 (0.00) [0]
780	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	15.01 (0.00) [-]
781	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (4/2021) [4/2021]	649.50 (-) [649.50]	134.18 (0.00) [25]
782	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (11/2020) [11/2020]	291.53 (-) [291.53]	30.82 (0.00) [-]
783	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [12/2019]	244.90 (-) [244.90]	243.33 (0.00) [7]
784	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH- 53 (OLD NH-6)	3/2018	/ (-) [11/2020]	289.21 (-) [289.21]	21.91 (0.00) [-]
785	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (-) [12/2020]	593.26 (-) [593.26]	484.48 (0.00) [31]
786	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
787	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	52.00 (0.00) [0]
788	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
789	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [2/2020]	247.02 (-) [157.49]	0.00 (-89.53) [-1]
790	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (3/2019) [5/2020]	414.51 (-) [414.00]	531.36 (-0.51) [24]
791	DAHEGAON TO KUHI	1/2017	6/2019 (-) [0/0]	228.89 (228.89) [228.89]	125.00 (0.00) [0]
792	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [12/2019]	182.63 (-) [182.63]	83.40 (0.00) [0]

793	DEORI TO AMGAON	1/2017	5/2019 (-) [5/2020]	409.62 (410.00) [409.62]	171.78 (0.00) [12]
794	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	106.46 (0.00) [0]
795	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [9/2019]	296.19 (-) [254.00]	248.60 (-42.19) [-6]
796	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [12/2019]	336.21 (336.00) [336.21]	64.66 (0.00) [0]
797	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [2/2020]	217.14 (217.00) [217.14]	66.77 (0.00) [0]
798	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [6/2020]	391.06 (391.00) [391.06]	68.00 (0.00) [12]
799	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	56.74 (0.00) [0]
800	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
801	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [807.00]	261.97 (164.87) [-]
802	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (12/2018) [11/2019]	1,871.34 (67.34) [1,871.34]	3,424.19 (0.00) [22]
803	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (11/2017) [5/2020]	904.16 (911.07) [904.16]	817.58 (0.00) [3]
804	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	160.31 (0.00) [0]
805	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	113.40 (0.00) [0]
806	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [12/2019]	294.87 (295.00) [294.87]	12.30 (0.00) [0]
807	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [12/2019]	355.17 (355.17) [355.17]	164.87 (0.00) [5]
808	INDAPUR TO VADPALE	1/2017	12/2019 (-) [3/2020]	1,202.52 (1,202.52) [1,202.52]	635.90 (0.00) [3]
809	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [11/2019]	461.96 (461.96) [461.96]	151.43 (0.00) [0]
810	JALGAON TO BHADGAON	1/2018	11/2019 (-) [11/2019]	307.54 (308.00) [307.54]	124.59 (0.00) [0]
811	JALGAON TO NANDURA	3/2018	12/2019 (-) [12/2019]	177.84 (177.00) [177.84]	55.69 (0.00) [0]
812	JALKOT TO TOGRI	7/2018	8/2020 (-) [8/2020]	299.92 (300.00) [299.92]	4.20 (0.00) [0]
813	JINTUR TO PARBHANI	1/2017	/	356.66	35.88

			(-) [0/0]	(356.66) [356.66]	(0.00) [0]
814	KAIJ TO KUSALAM	1/2017	7/2019 (-) [7/2019]	554.78 (554.78) [554.78]	159.90 (0.00) [0]
815	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	294.91 (0.00) [0]
816	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (1,338.13) [1,338.13]	959.51 (0.00) [0]
817	KANTE TO WAKED	3/2016	11/2019 (-) [11/2019]	1,230.02 (1,230.02) [1,230.02]	500.61 (0.00) [0]
818	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [6/2020]	407.19 (407.00) [407.19]	25.00 (0.00) [12]
819	KARAD TO TAGAON	1/2017	6/2019 (-) [6/2020]	537.81 (538.00) [537.81]	85.97 (0.00) [12]
820	KARAD TO VITA	1/2018	12/2019 (-) [12/2019]	344.85 (245.00) [344.85]	68.04 (0.00) [0]
821	KARWANDI TO RAJURI	3/2018	12/2019 (-) [12/2019]	276.95 (277.00) [276.95]	81.47 (0.00) [0]
822	KATOL TO WARUD	1/2017	6/2019 (-) [8/2019]	463.62 (664.00) [463.62]	257.34 (0.00) [2]
823	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [12/2019]	249.29 (-) [249.29]	72.20 (0.00) [0]
824	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [12/2019]	203.21 (203.00) [203.21]	102.79 (0.00) [7]
825	KHERDA TO NAGZARI	3/2018	12/2019 (-) [12/2019]	181.30 (-) [181.30]	70.50 (0.00) [0]
826	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	175.93 (0.00) [0]
827	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [4/2020]	281.78 (282.00) [281.78]	47.73 (0.00) [12]
828	KOTHARI TO DHANORA	9/2018	8/2020 (-) [8/2020]	301.38 (301.00) [301.38]	41.00 (0.00) [0]
829	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	281.03 (0.00) [0]
830	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [12/2019]	225.25 (225.00) [225.25]	121.75 (0.00) [0]
831	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	148.17 (0.00) [0]
832	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [12/2019]	243.45 (244.00) [243.45]	67.02 (0.00) [0]
833	LATUR TO PANGAON	3/2018	12/2019 (-)	336.47 (336.00)	109.48 (0.00)

			[12/2019]	[336.47]	[0]
834	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [5/2020]	237.40 (-) [237.40]	8.34 (0.00) [0]
835	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [7/2019]	413.99 (-) [413.99]	299.33 (0.00) [0]
836	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [12/2019]	256.15 (-) [256.15]	15.50 (0.00) [0]
837	MALEGAON TO RISOD	2/2018	12/2019 (-) [12/2019]	303.24 (303.24) [303.24]	107.97 (0.00) [0]
838	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2020]	322.55 (-) [322.55]	156.91 (0.00) [12]
839	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [7/2020]	457.52 (457.52) [457.52]	202.98 (0.00) [12]
840	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [11/2019]	222.13 (222.13) [222.13]	60.36 (0.00) [0]
841	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [8/2019]	228.54 (228.54) [228.54]	99.30 (0.00) [0]
842	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [12/2019]	418.36 (-) [418.36]	116.13 (0.00) [0]
843	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [7/2019]	486.19 (486.19) [486.19]	215.29 (0.00) [0]
844	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	85.51 (0.00) [0]
845	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	202.08 (0.00) [0]
846	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	182.71 (0.00) [0]
847	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2019]	341.16 (341.00) [341.16]	153.29 (0.00) [6]
848	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	259.90 (0.00) [0]
849	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [7/2019]	162.34 (-) [162.34]	32.80 (0.00) [0]
850	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [12/2019]	376.72 (377.00) [376.72]	168.81 (0.00) [6]
851	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	197.91 (0.00) [0]
852	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	226.24 (0.00) [0]
853	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (12/2020) [12/2020]	546.00 (-) [546.00]	269.67 (0.00) [17]

854	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (12/2020) [12/2020]	591.66 (-) [591.66]	310.56 (0.00) [17]
855	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2019]	244.04 (244.00) [244.04]	25.94 (0.00) [9]
856	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2019]	274.50 (275.00) [274.50]	61.39 (0.00) [0]
857	NANDED TO JALKOT	12/2017	9/2019 (-) [9/2019]	456.93 (457.00) [456.93]	54.50 (0.00) [0]
858	NANDGAON TO MORSHI	1/2017	6/2019 (-) [12/2019]	385.87 (386.00) [385.87]	203.75 (0.00) [6]
859	NASHIK TO PETH	12/2015	11/2018 (-) [11/2019]	289.60 (-) [289.60]	118.81 (0.00) [12]
860	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [9/2019]	406.54 (406.54) [406.54]	142.00 (0.00) [0]
861	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [5/2020]	420.63 (421.00) [420.63]	17.60 (0.00) [0]
862	OMREGA TO AUSA	3/2018	12/2019 (-) [12/2019]	272.04 (272.00) [272.04]	124.24 (0.00) [0]
863	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [8/2020]	344.25 (344.00) [344.25]	33.02 (0.00) [0]
864	PAHUR TO BODHWAD	1/2017	5/2020 (-) [5/2020]	244.93 (-) [244.93]	40.23 (0.00) [0]
865	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	117.89 (0.00) [0]
866	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [12/2019]	227.19 (227.00) [227.19]	60.23 (0.00) [0]
867	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [5/2020]	381.08 (302.00) [381.08]	13.00 (0.00) [0]
868	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
869	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [12/2019]	238.19 (238.00) [238.19]	40.85 (0.00) [0]
870	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2020]	205.72 (205.72) [205.72]	30.42 (0.00) [12]
871	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [11/2019]	983.14 (983.14) [983.14]	655.15 (0.00) [-1]
872	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [7/2019]	420.57 (420.57) [420.57]	215.39 (0.00) [0]
873	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [12/2019]	170.00 (-) [170.00]	39.57 (0.00) [0]
874	PEN TO KHOPOLI	3/2018	3/2018	301.39	0.00

			(-) [12/2019]	(302.00) [301.39]	(0.00) [21]
875	PIMPLA TO MANJARUMBHA	1/2017	8/2019 (-) [8/2019]	595.77 (595.77) [595.77]	132.44 (0.00) [0]
876	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [12/2019]	223.46 (-) [223.46]	21.42 (0.00) [0]
877	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [12/2019]	228.31 (-) [228.31]	13.50 (0.00) [0]
878	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [12/2019]	1,724.55 (-) [1,724.55]	2,387.46 (0.00) [81]
879	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	106.69 (0.00) [0]
880	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	259.50 (0.00) [0]
881	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	83.11 (0.00) [0]
882	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (-) [12/2019]	536.65 (356.00) [536.65]	42.25 (0.00) [0]
883	RISOD TO HINGOLI	2/2018	12/2019 (-) [12/2019]	355.99 (355.99) [355.99]	112.97 (0.00) [0]
884	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [11/2019]	362.96 (362.96) [362.96]	37.83 (0.00) [5]
885	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [12/2019]	415.25 (415.25) [415.25]	82.22 (0.00) [0]
886	SANGOLA TO JATH	1/2018	12/2019 (-) [12/2019]	257.38 (257.00) [257.38]	61.15 (0.00) [0]
887	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	103.63 (0.00) [0]
888	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	65.01 (0.00) [0]
889	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	188.77 (0.00) [0]
890	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	202.42 (0.00) [0]
891	SELDOH TO PANVAR	7/2018	5/2020 (-) [5/2020]	404.33 (404.00) [404.33]	30.19 (0.00) [0]
892	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [12/2019]	150.79 (150.79) [150.79]	21.42 (0.00) [0]
893	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [12/2019]	373.10 (373.00) [373.10]	123.43 (0.00) [7]
894	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-)	211.34 (211.34)	101.83 (0.00)

			[7/2019]	[211.34]	[0]
895	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	100.79 (0.00) [0]
896	SHIVUR TO YEOLA	3/2018	12/2019 (-) [12/2019]	181.08 (-) [181.08]	2.50 (0.00) [0]
897	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	39.22 (0.00) [0]
898	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (448.18) [404.94]	102.43 (0.00) [-]
899	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE	11/2016	/ (3/2020) [3/2019]	290.73 (315.00) [315.00]	215.98 (24.27) [0]
900	TAKARKHED TO JALNA	9/2017	6/2019 (-) [12/2019]	417.90 (418.00) [417.90]	87.26 (0.00) [6]
901	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [12/2019]	264.41 (264.00) [264.41]	32.71 (0.00) [9]
902	TALGAON TO KALMATH	10/2016	3/2020 (-) [3/2020]	904.70 (904.70) [904.70]	604.05 (0.00) [0]
903	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [11/2019]	195.64 (196.00) [195.64]	169.73 (0.00) [0]
904	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	238.01 (0.00) [0]
905	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [3/2020]	1,598.47 (1,598.47) [1,598.47]	751.91 (0.00) [4]
906	VITA TO NAGAJ	3/2018	12/2019 (-) [12/2019]	304.58 (305.00) [304.58]	9.16 (0.00) [0]
907	WADI TO ASOLA	1/2017	9/2019 (-) [9/2020]	363.82 (363.82) [363.82]	41.10 (0.00) [12]
908	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [2/2020]	194.23 (194.00) [194.23]	68.23 (0.00) [0]
909	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [5/2020]	376.19 (376.19) [376.19]	29.03 (0.00) [12]
910	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	357.60 (0.00) [0]
911	WARDHA TO ARVI	2/2018	4/2020 (-) [4/2020]	313.58 (313.58) [313.58]	4.96 (0.00) [0]
912	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [12/2019]	216.90 (216.90) [216.90]	45.00 (0.00) [0]
913	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [12/2019]	165.51 (-) [165.51]	35.45 (0.00) [0]
914	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]

915	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Telecommunications</u>				
916	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (9/2019) [9/2019]	231.80 (-) [240.10]	117.63 (8.30) [11]
	<u>Urban Development</u>				
917	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2020) [9/2020]	223.37 (-) [223.37]	33.01 (0.00) [2]
918	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
919	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	6,108.39 (0.00) [21]
920	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (1/2022) [1/2022]	11,420.00 (-) [11,420.00]	2,727.17 (0.00) [2]
921	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	6/2010	3/2012 (-) [0/0]	205.00 (-) [205.00]	165.47 (0.00) [0]
	<u>Water Resources</u>				
922	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2019]	233.57 (-) [233.57]	32.20 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
923	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
924	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (13,809.00) [12,524.00]	9,123.93 (8,069.83) [108]
	<u>Road Transport And Highways</u>				
925	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	74.49 (0.00) [0]
926	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	119.56 (-59.80) [36]
	<u>Urban Development</u>				
927	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
928	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
929	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.76 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
930	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	42.66 (0.00) [0]
931	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM	12/2015	5/2018	479.20	708.82

	BORDER SECTION OF NH-44		(3/2018) [12/2019]	(-) [479.20]	(0.00) [19]
932	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	<u>Urban Development</u>				
933	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
934	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,075.08 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
935	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	305.38 (182.95) [116]
936	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	275.06 (118.65) [63]
937	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
938	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
939	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
940	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
941	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
942	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
943	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
944	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
945	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
946	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	853.82 (368.26) [105]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
947	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	20.86 (0.00) [0]
948	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	154.25 (0.00) [0]
949	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-)	319.76 (-)	235.29 (0.00)

			[3/2022]	[319.76]	[0]
	<u>Petroleum</u>				
950	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
951	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (3,027.90) [3,027.90]	844.09 (1,204.90) [0]
952	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	173.61 (0.00) [0]
953	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	1,123.85 (0.00) [0]
954	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,229.31 (0.00) [0]
955	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,396.84 (0.00) [0]
956	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	837.13 (0.00) [0]
957	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [10/2019]	890.00 (-) [887.00]	602.02 (-3.00) [0]
958	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (-) [2/2022]	2,915.00 (2,915.00) [3,049.47]	2,515.46 (134.47) [110]
959	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [12/2020]	2,881.40 (-) [2,000.00]	1,271.82 (-881.40) [0]
960	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,460.00 (0.00) [0]
961	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	1,820.56 (1,017.00) [-4]
962	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (-) [10/2020]	690.00 (-) [690.00]	278.51 (0.00) [27]
963	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	87.00 (0.00) [0]
964	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [12/2019]	352.56 (-) [438.84]	230.43 (86.28) [33]
965	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (8/2019) [8/2019]	309.81 (723.40) [723.40]	703.45 (413.59) [58]
	<u>Power</u>				
966	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [2/2020]	198.49 (-) [198.49]	83.31 (0.00) [5]
967	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2019]	4,754.42 (-) [9,072.36]	1,211.92 (4,317.94) [12]
968	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	38.90 (0.00) [0]
969	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016	196.58	162.30

			(-) [6/2019]	(-) [225.28]	(28.70) [0]
970	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (-) [8/2019]	1,364.52 (-) [1,891.41]	1,259.05 (526.89) [40]
971	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (-) [3/2020]	522.29 (-) [546.36]	465.21 (24.07) [40]
972	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	1,399.20 (0.00) [0]
973	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [10/2019]	235.53 (-) [235.53]	117.15 (0.00) [4]
974	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [8/2019]	322.30 (-) [322.30]	153.70 (0.00) [6]
975	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [8/2019]	197.40 (-) [197.40]	81.97 (0.00) [17]
976	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D	5/2016	5/2019 (-) [9/2019]	3,519.59 (-) [3,519.59]	2,431.00 (0.00) [4]
977	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	2,516.66 (0.00) [0]
978	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	7,922.74 (0.00) [0]
979	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	933.96 (0.00) [0]
980	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	185.94 (0.00) [0]
981	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2020]	5,111.33 (-) [6,880.36]	1,367.68 (1,769.03) [24]
982	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (-) [3/2022]	11,130.19 (-) [14,719.10]	12,804.46 (3,588.91) [103]
983	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	187.60 (0.00) [0]
984	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (-) [7/2019]	562.25 (-) [562.25]	392.96 (0.00) [0]
985	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [7/2019]	3,654.00 (-) [3,654.00]	3,308.50 (0.00) [0]
986	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [7/2019]	608.24 (-) [608.24]	407.79 (0.00) [0]
987	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [8/2019]	203.28 (-) [260.03]	190.80 (56.75) [25]
988	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [12/2019]	379.95 (-) [379.95]	52.63 (0.00) [0]
989	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-)	337.75 (-)	84.17 (0.00)

			[7/2019]	[337.75]	[0]
990	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [9/2019]	487.49 (-) [639.46]	540.12 (151.97) [63]
991	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (-) [12/2019]	4,824.12 (-) [5,071.94]	4,558.05 (247.82) [86]
992	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	3/2018 (-) [7/2019]	268.80 (-) [340.88]	251.33 (72.08) [0]
993	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (-) [9/2019]	871.62 (-) [871.62]	548.30 (0.00) [23]
994	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (-) [9/2019]	408.46 (-) [408.46]	266.03 (0.00) [8]
995	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [12/2019]	5,151.37 (-) [5,151.37]	3,115.72 (0.00) [21]
996	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (-) [3/2020]	808.63 (-) [808.63]	513.85 (0.00) [26]
997	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (-) [12/2019]	374.63 (-) [374.63]	210.72 (0.00) [44]
998	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (-) [2/2020]	195.05 (-) [195.05]	116.76 (0.00) [0]
	<u>Railways</u>				
999	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	4,115.87 (0.00) [0]
1000	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2020]	288.35 (-) [376.90]	376.90 (88.55) [-]
1001	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.12 (-200.00) [-]
1002	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (-) [3/2020]	704.31 (-) [1,352.74]	269.07 (648.43) [0]
1003	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [1,787.00]	2.46 (863.77) [0]
1004	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2021]	175.80 (-) [242.06]	242.06 (66.26) [-]
1005	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	233.84 (1,211.86) [0]
1006	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1007	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,300.00]	2.28 (1,776.48) [0]
1008	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	328.19 (182.31) [12]
1009	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-)	243.78 (-)	106.55 (651.22)

			[12/2021]	[895.00]	[0]
1010	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	102.27 (173.89) [96]
1011	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2022) [3/2022]	1,347.26 (1,347.26) [1,347.26]	719.73 (0.00) [0]
1012	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	682.91 (0.00) [12]
1013	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [296.43]	212.51 (-68.74) [96]
1014	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2022]	336.91 (791.39) [800.00]	512.67 (463.09) [-]
1015	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	637.72 (818.35) [133]
1016	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1017	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [0/0]	651.00 (-) [1,009.00]	7.96 (358.00) [0]
1018	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1019	GAYA-CHATRA (NL)	4/2008	/ (-) [3/2024]	415.67 (-) [549.75]	15.54 (134.08) [-]
1020	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (12/2020) [12/2020]	511.86 (1,756.92) [1,756.92]	1,661.79 (1,245.06) [8]
1021	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1022	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	137.90 (932.64) [33]
1023	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [2/2021]	678.54 (678.54) [678.54]	466.93 (0.00) [23]
1024	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2020]	542.18 (-) [693.80]	428.83 (151.62) [0]
1025	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	10.73 (88.07) [-]
1026	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1027	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2021]	1,614.59 (-) [1,870.41]	914.00 (255.82) [24]
1028	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.75 (0.00) [28]
1029	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [3/2025]	166.89 (-) [166.89]	0.02 (0.00) [-]

1030	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [3/2021]	625.00 (-) [845.58]	834.59 (220.58) [60]
1031	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2024]	2,132.77 (-) [2,132.77]	331.17 (0.00) [120]
1032	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	434.06 (71.58) [108]
1033	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [3/2025]	174.56 (-) [174.56]	71.42 (0.00) [-]
1034	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2023]	2,063.03 (-) [2,063.03]	675.97 (0.00) [24]
1035	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [2,200.00]	252.81 (343.05) [12]
1036	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (457.08) [457.08]	373.51 (186.94) [0]
1037	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	148.43 (138.71) [228]
1038	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [6,093.31]	1,835.18 (5,845.65) [178]
1039	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	105.28 (0.00) [132]
1040	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	4/2011	3/2019 (-) [12/2019]	120.70 (-) [1,800.00]	170.47 (1,679.30) [9]
1041	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	155.08 (180.72) [157]
1042	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	257.06 (59.77) [-]
1043	MUNEERABAD-MAHABOONNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2021]	1,723.00 (1.00) [1,723.00]	1,368.46 (0.00) [252]
1044	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	122.05 (246.16) [0]
1045	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (-) [2,010.00]	654.07 (1,560.00) [140]
1046	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	32.00 (0.05) [240]
1047	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	68.15 (228.78) [0]
1048	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [3/2021]	241.52 (-) [394.28]	272.88 (152.76) [-]
1049	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [0/0]	1,798.00 (-) [2,496.67]	0.00 (698.67) [0]
1050	NEW JALPAIGURI SILIGURI NEW BONGAIGAON	4/1999	/	819.23	1,082.01

	INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI		(-) [0/0]	(-) [1,871.00]	(1,051.77) [0]
1051	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2021]	1,180.19 (3,300.00) [3,300.00]	3,279.71 (2,119.81) [147]
1052	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	47.07 (85.99) [25]
1053	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [471.81]	459.69 (210.43) [0]
1054	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	290.01 (1,221.83) [36]
1055	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1056	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,079.15]	185.11 (1,996.40) [0]
1057	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	2,062.30 (-) [2,062.20]	825.58 (-0.10) [-]
1058	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR- MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [298.22]	52.09 (0.75) [-]
1059	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	155.33 (-10.96) [108]
1060	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
1061	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	9.31 (811.34) [-]
1062	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1063	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1064	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [3/2020]	860.43 (-) [860.43]	697.21 (0.00) [0]
	<u>Road Transport And Highways</u>				
1065	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1066	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	3,070.11 (1,016.78) [0]
1067	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
1068	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1069	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [962.00]	0.00 (-36.70) [0]
1070	GWALIOR-JHANSI, NH-75	12/2003	12/2009	604.00	423.83

			(-) [8/2020]	(-) [604.00]	(0.00) [128]
1071	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [12/2019]	754.00 (-) [754.00]	1,364.18 (0.00) [81]
1072	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	1,326.00 (0.00) [-]
1073	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	303.71 (0.00) [0]
1074	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2019]	2,848.00 (-) [2,848.00]	1,159.10 (0.00) [69]
	<u>Shipping And Ports</u>				
1075	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	4,200.00 (5,369.18) [5,369.18]	1,394.52 (1,169.18) [0]
	<u>Telecommunications</u>				
1076	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	8,397.00 (11,330.00) [58]
1077	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1078	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1079	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [3,000.00]	781.71 (673.48) [79]
	<u>Road Transport And Highways</u>				
1080	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
1081	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
1082	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (-) [282.98]	12.76 (0.00) [0]
1083	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	127.19 (0.00) [0]
1084	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
1085	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
1086	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	121.20 (0.00) [0]
1087	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [339.57]	0.00 (0.00) [0]
1088	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	4.38 (0.00) [0]

1089	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	2.11 (0.00) [0]
1090	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	6.86 (0.00) [0]
1091	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
1092	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
1093	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
1094	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (11/2018) [0/0]	251.97 (160.10) [251.97]	13.42 (0.00) [0]
1095	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	59.42 (0.00) [0]
1096	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (387.00) [373.07]	203.77 (0.00) [36]
1097	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [396.52]	234.03 (0.00) [46]
1098	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (340.00) [429.52]	166.55 (0.00) [36]
1099	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (369.96) [336.25]	62.64 (0.00) [0]
1100	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	42.15 (0.00) [0]
1101	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	45.02 (0.00) [0]
1102	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1103	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1104	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	228.90 (0.00) [108]
1105	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2022]	172.08 (-) [172.08]	347.15 (0.00) [144]
1106	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2022]	479.15 (-) [479.15]	200.65 (0.00) [36]
1107	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	501.82 (0.00) [36]
1108	GARJANBAHAL OCP	11/2014	3/2021 (-)	1,375.38 (-)	440.13 (0.00)

			[3/2021]	[1,375.38]	[0]
1109	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2021]	479.53 (-) [479.53]	390.94 (0.00) [96]
1110	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	83.20 (0.00) [0]
1111	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2020]	337.66 (-) [337.66]	183.98 (0.00) [12]
1112	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2022]	457.77 (-) [457.77]	539.59 (0.00) [108]
1113	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	75.85 (0.00) [24]
1114	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2020]	302.96 (-) [302.96]	302.96 (0.00) [120]
1115	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,113.66 (0.00) [0]
1116	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,549.76 (0.00) [0]
	<u>Mines</u>				
1117	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	102.61 (0.00) [0]
1118	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	31.92 (0.00) [0]
1119	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.30 (0.00) [0]
1120	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	318.13 (0.00) [0]
	<u>Petroleum</u>				
1121	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	34.73 (0.00) [0]
1122	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	0.00 (0.00) [0]
1123	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2020]	315.00 (-) [315.00]	110.59 (0.00) [-12]
1124	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	49.97 (0.00) [0]
1125	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	28.80 (0.00) [0]
1126	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	1,019.25 (0.00) [0]
1127	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	242.10 (0.00) [0]
1128	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021	3,361.00	284.31

			(-) [8/2021]	(-) [3,361.00]	(0.00) [0]
1129	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [12/2019]	429.00 (-) [429.00]	306.24 (0.00) [11]
1130	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (-) [9/2022]	371.00 (-) [371.00]	0.00 (0.00) [0]
1131	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [7/2021]	161.59 (-) [161.59]	38.29 (0.00) [19]
1132	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	9.08 (0.00) [0]
1133	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (6/2019) [7/2019]	3,150.00 (-) [3,150.00]	2,573.02 (0.00) [0]
	<u>Power</u>				
1134	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (2/2020) [9/2020]	12,532.44 (-) [13,740.53]	9,639.47 (1,208.09) [21]
1135	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (-) [8/2019]	844.64 (-) [844.64]	430.71 (0.00) [4]
1136	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [3/2020]	1,885.13 (-) [1,885.13]	527.90 (0.00) [15]
	<u>Railways</u>				
1137	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [1,120.00]	998.91 (177.05) [24]
1138	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2023]	843.04 (-) [843.04]	130.99 (0.00) [29]
1139	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2022]	1,172.92 (-) [1,172.92]	393.60 (0.00) [39]
1140	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1141	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [6/2023]	5,200.00 (-) [1,700.43]	48.00 (-3,499.57) [39]
1142	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,757.33 (658.83) [27]
1143	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2023]	1,547.38 (-) [1,547.38]	346.97 (0.00) [12]
1144	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2022]	701.61 (-) [810.02]	122.59 (108.41) [40]
1145	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2019]	133.41 (207.00) [395.00]	386.28 (261.59) [129]
1146	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [3/2024]	2,923.13 (-) [3,791.66]	1,360.34 (868.53) [180]
1147	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2025]	2,361.74 (-) [2,361.74]	162.82 (0.00) [36]

1148	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [6/2020]	969.83 (1,312.96) [1,312.96]	549.97 (343.13) [3]
1149	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2021]	155.81 (-) [238.03]	225.52 (82.22) [12]
1150	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2021]	948.04 (-) [1,500.00]	1,304.20 (551.96) [12]
1151	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2022]	1,111.99 (-) [1,539.28]	924.93 (427.29) [37]
1152	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (-) [1,202.70]	891.28 (0.00) [82]
1153	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2023]	810.78 (-) [1,928.07]	688.96 (1,117.29) [21]
1154	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (-) [2,335.68]	566.84 (0.01) [0]
	<u>Road Transport And Highways</u>				
1155	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [4/2020]	1,282.94 (-) [1,282.94]	204.92 (0.00) [-]
1156	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [8/2019]	2,510.04 (-) [2,510.04]	231.96 (0.00) [0]
1157	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
1158	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [7/2019]	1,069.65 (-) [1,069.65]	502.75 (0.00) [0]
1159	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,935.14 (0.00) [0]
1160	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [7/2020]	1,008.96 (-) [1,008.96]	449.84 (0.00) [-]
1161	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	0.00 (0.00) [-]
1162	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (11/2020) [6/2021]	476.56 (-) [476.56]	0.00 (0.00) [47]
1163	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
1164	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (5/2020) [6/2021]	953.09 (-) [953.09]	94.03 (0.00) [-]
1165	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (5/2020) [6/2021]	668.86 (-) [668.86]	99.10 (0.00) [-]
1166	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	31.00 (0.00) [-]
1167	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	258.91 (0.00) [0]

1168	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	0.00 (0.00) [0]
1169	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	0.00 (0.00) [-]
1170	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2021]	1,288.07 (-) [1,420.00]	348.24 (131.93) [12]
1171	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (7/2020) [6/2021]	686.65 (-) [686.65]	80.87 (0.00) [-]
1172	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (3/2020) [6/2021]	686.65 (-) [686.65]	71.38 (0.00) [-]
1173	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [0/0]	417.51 (-) [417.51]	0.00 (0.00) [0]
1174	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	258.91 (-0.05) [0]
1175	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [0/0]	999.00 (-) [999.00]	0.00 (0.00) [0]
1176	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [11/2019]	171.96 (172.00) [172.00]	88.30 (0.04) [41]
1177	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1178	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1179	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [0]
1180	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	4.03 (0.00) [-]
1181	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [12/2019]	191.50 (192.00) [192.00]	136.19 (0.50) [43]
1182	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1183	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1184	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1185	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [9/2019]	159.39 (-) [159.39]	210.29 (0.00) [22]
1186	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [12/2019]	191.08 (-) [191.08]	99.98 (0.00) [52]
1187	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1188	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN	3/2018	8/2018	214.23	23.44

	THE STATE OF ODISHA		(-) [0/0]	(-) [214.23]	(0.00) [0]
1189	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1190	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1191	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1192	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1193	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	<u>Steel</u>				
1194	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (11/2019) [11/2019]	3,127.30 (-) [3,127.30]	3,008.68 (0.00) [19]
	<u>Urban Development</u>				
1195	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [3/2022]	790.79 (-) [800.00]	2.56 (9.21) [0]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1196	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	113.95 (0.00) [0]
1197	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	125.27 (0.00) [0]
	<u>Health And Family Welfare</u>				
1198	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [8/2020]	703.00 (-) [703.00]	184.93 (0.00) [2]
1199	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [9/2019]	152.95 (-) [152.95]	118.23 (0.00) [19]
	<u>Railways</u>				
1200	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [205.22]	1.89 (0.00) [-]
	<u>Road Transport And Highways</u>				
1201	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (1,367.00) [1,169.61]	1,063.10 (0.00) [-]
1202	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (9/2019) [0/0]	847.02 (-) [847.02]	1,086.94 (0.00) [0]
1203	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (12/2019) [0/0]	889.24 (-) [904.82]	722.92 (15.58) [0]
1204	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (3/2020) [9/2019]	1,388.34 (2,525.80) [2,525.80]	1,449.00 (1,137.46) [0]
1205	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [4/2020]	754.54 (-) [756.27]	159.58 (1.73) [1]
1206	DEVELOPMENT TO FOUR LANE WITH PAVED	12/2015	/	766.36	666.72

	SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS		(9/2019) [0/0]	(-) [766.36]	(0.00) [0]
1207	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (6/2020) [12/2019]	447.29 (746.43) [746.43]	596.50 (299.14) [24]
1208	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [1/2021]	261.76 (-) [207.00]	62.85 (-54.76) [-]
1209	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [3/2020]	479.00 (-) [479.00]	453.59 (0.00) [-]
1210	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [10/2019]	1,069.59 (-) [1,069.59]	629.87 (0.00) [0]
1211	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [1/2020]	196.05 (149.90) [196.05]	143.03 (0.00) [-]
1212	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (149.90) [199.90]	60.39 (0.00) [0]
1213	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [11/2020]	170.57 (-) [170.57]	46.23 (0.00) [0]
1214	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020 (-) [6/2020]	173.24 (-) [173.24]	10.97 (0.00) [0]
1215	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020 (-) [7/2020]	322.48 (-) [322.48]	48.73 (0.00) [0]
1216	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1217	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1218	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [8/2020]	293.10 (-) [293.10]	10.26 (0.00) [0]
1219	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	648.44 (0.00) [0]
	<u>Urban Development</u>				
1220	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (-) [9/2019]	388.00 (-) [488.28]	424.11 (100.28) [28]
1221	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [1/2021]	430.00 (-) [430.00]	65.80 (0.00) [8]
1222	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [2/2020]	294.00 (-) [294.00]	195.83 (0.00) [10]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1223	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2020]	12,320.00 (17,079.00) [17,079.00]	11,234.00 (4,759.00) [48]
	<u>Coal</u>				
1224	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	175.30 (0.00) [0]
1225	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019	522.45	9.88

			(-) [9/2019]	(-) [522.45]	(0.00) [0]
	<u>Petroleum</u>				
1226	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1227	LPG BP PROJECT JODHPUR	3/2018	/	229.80	69.24
			(-) [3/2021]	(-) [229.80]	(0.00) [-]
	<u>Power</u>				
1228	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (-) [7/2019]	1,429.38 (-) [1,429.38]	1,011.38 (0.00) [0]
	<u>Railways</u>				
1229	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/	873.71	4.25
			(-) [0/0]	(-) [1,980.21]	(1,106.50) [0]
1230	AJMER-BANGURGRAM	4/2011	11/2019 (-) [5/2020]	213.39 (-) [303.56]	262.32 (90.17) [6]
1231	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/	822.00	0.00
			(-) [0/0]	(-) [1,099.54]	(277.54) [0]
1232	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [5/2020]	242.09 (281.03) [410.00]	351.23 (167.91) [15]
1233	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2020]	246.08 (-) [348.55]	215.47 (102.47) [6]
1234	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [3/2021]	410.08 (780.98) [886.41]	525.78 (476.33) [25]
1235	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	47.07 (0.00) [1]
1236	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2020]	420.18 (-) [420.18]	160.53 (0.00) [3]
1237	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	439.45 (0.00) [24]
1238	PUSHKAR-MERTA	4/2013	/	323.00	0.00
			(-) [0/0]	(-) [432.22]	(109.22) [0]
1239	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [10/2019]	236.93 (-) [294.90]	141.40 (57.97) [12]
	<u>Road Transport And Highways</u>				
1240	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	605.33 (0.00) [0]
1241	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [0/0]	320.30 (-) [320.30]	206.14 (0.00) [0]
1242	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [0/0]	530.07 (-) [530.07]	556.02 (0.00) [0]
1243	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/	688.70	701.76
			(5/2017) [11/2019]	(881.00) [688.70]	(0.00) [-]
1244	6-LANNING OF KISHANGARH TO GULABPURA SECTION	12/2016	/	1,031.95	367.00

	OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-		(-) [8/2020]	(-) [1,031.95]	(0.00) [-]
1245	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/	178.13	0.00
			(-) [0/0]	(-) [178.13]	(0.00) [0]
1246	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018	822.90	844.08
			(-) [0/0]	(-) [822.90]	(0.00) [0]
1247	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP.	10/2012	10/2013	511.21	814.79
			(-) [0/0]	(-) [511.21]	(0.00) [0]
1248	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/	1,158.35	121.47
			(-) [0/0]	(-) [1,158.35]	(0.00) [0]
1249	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC.	12/2015	10/2016	621.43	426.36
			(-) [0/0]	(-) [621.43]	(0.00) [0]
1250	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE.	3/2016	9/2016	155.77	97.42
			(-) [0/0]	(-) [155.77]	(0.00) [0]
1251	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018	163.95	58.70
			(-) [0/0]	(-) [163.95]	(0.00) [0]
1252	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/	716.76	171.45
			(-) [0/0]	(-) [716.76]	(0.00) [0]
1253	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/	741.86	0.00
			(-) [0/0]	(-) [741.86]	(0.00) [0]
1254	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	3/2009	9/2013	501.00	659.98
			(-) [0/0]	(671.54) [671.54]	(170.54) [0]
1255	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/	1,308.73	0.00
			(-) [12/2020]	(-) [1,308.73]	(0.00) [-]
1256	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019	763.23	216.17
			(-) [11/2019]	(-) [763.23]	(0.00) [5]
1257	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019	649.00	0.00
			(-) [9/2019]	(-) [649.00]	(0.00) [3]
1258	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017	964.17	364.29
			(-) [11/2020]	(-) [964.17]	(0.00) [37]
1259	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011	1,673.70	3,326.93
			(-) [0/0]	(-) [1,673.70]	(0.00) [0]
1260	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP.	1/2012	1/2014	378.07	188.98
			(-) [0/0]	(478.73) [478.73]	(100.66) [0]
1261	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC.	10/2014	1/2015	382.81	333.60
			(-) [0/0]	(-) [382.81]	(0.00) [0]
1262	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013	511.00	492.00
			(-) [8/2019]	(-) [511.00]	(0.00) [70]
1263	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013	511.00	2,323.04
			(-) [0/0]	(-) [511.00]	(0.00) [0]
1264	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014	278.87	0.00
			(-)	(-)	(0.00)

			[0/0]	[278.87]	[0]
1265	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1266	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [12/2019]	1,100.19 (-) [1,100.19]	892.00 (0.00) [-]
1267	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	1,280.27 (0.00) [-]
1268	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [11/2019]	894.00 (-) [894.00]	690.00 (0.00) [-5]
1269	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR	9/2014	9/2016 (9/2014) [10/2019]	425.19 (-) [425.19]	276.40 (0.00) [37]
1270	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (2/2016) [10/2019]	275.90 (-) [275.90]	257.52 (0.00) [-]
1271	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1272	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	588.00 (0.00) [3]
1273	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE	1/2017	7/2017 (-) [0/0]	163.54 (-) [163.54]	92.88 (0.00) [0]
1274	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN	1/2017	11/2017 (-) [0/0]	179.32 (-) [179.32]	96.12 (0.00) [0]
1275	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	80.10 (0.00) [0]
1276	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	192.00 (0.00) [0]
1277	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	267.65 (0.00) [-]
1278	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	97.97 (0.00) [0]
1279	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1280	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	224.68 (0.00) [0]
1281	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1282	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	387.00 (0.00) [0]
1283	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	53.02 (0.00) [0]
	Urban Development				
1284	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION	5/2015	3/2017 (-)	189.00 (-)	0.00 (0.00)

	OF GOVT. DIS		[0/0]	[189.00]	[0]
1285	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (12/2019) [2/2020]	549.31 (559.47) [559.47]	335.76 (10.16) [7]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1286	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [0]
	<u>Road Transport And Highways</u>				
1287	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (9/2017) [12/2019]	182.28 (269.14) [269.14]	185.49 (86.86) [82]
1288	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [76]
1289	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (203.26) [166.27]	141.31 (0.00) [0]
1290	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
1291	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	34.86 (0.00) [0]
1292	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	97.85 (0.00) [0]
1293	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1294	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	97.85 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1295	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	15,395.00 (0.00) [36]
1296	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2021]	3,492.00 (-) [6,840.00]	5,784.74 (3,348.00) [133]
	<u>Civil Aviation</u>				
1297	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [8/2022]	2,467.00 (-) [2,467.00]	213.17 (0.00) [6]
1298	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [10/2021]	951.28 (-) [951.28]	71.55 (0.00) [0]
	<u>Coal</u>				
1299	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [9/2019]	1,458.17 (-) [709.06]	449.32 (-749.11) [51]
1300	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [12/2019]	5,907.11 (7,080.41) [7,080.41]	6,648.68 (1,173.30) [48]
	<u>Mines</u>				
1301	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (-) [0/0]	166.62 (-) [166.62]	134.98 (0.00) [0]
	<u>Petroleum</u>				

1302	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	12.28 (0.00) [0]
1303	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	951.55 (0.00) [0]
1304	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	30.95 (0.00) [10]
1305	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2021]	4,497.00 (6,025.00) [6,025.00]	465.60 (1,528.00) [26]
1306	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1307	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2020) [5/2020]	650.82 (-) [650.82]	394.21 (0.00) [14]
1308	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [10/2021]	678.00 (-) [678.00]	5.57 (0.00) [56]
1309	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	123.76 (0.00) [0]
1310	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.00 (0.00) [0]
	<u>Power</u>				
1311	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (-) [8/2019]	1,779.29 (-) [2,187.32]	2,237.45 (408.03) [129]
1312	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [9/2019]	186.17 (-) [186.17]	103.12 (0.00) [2]
	<u>Railways</u>				
1313	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [257.00]	268.31 (0.00) [0]
1314	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1315	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIE	4/2007	/ (-) [3/2020]	931.98 (-) [951.24]	724.96 (19.26) [-]
1316	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	303.72 (357.96) [0]
1317	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1318	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [0/0]	495.74 (-) [734.01]	445.91 (238.27) [0]
1319	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2021]	760.00 (-) [1,182.31]	406.32 (422.31) [15]
1320	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	151.50 (285.59) [-]
1321	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-)	1,700.00 (-)	167.73 (-697.00)

			[3/2022]	[1,003.00]	[0]
1322	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2020]	724.69 (-) [2,072.50]	1,386.59 (1,347.81) [12]
1323	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	108.34 (44.41) [71]
1324	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]
1325	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [950.00]	927.86 (681.13) [0]
1326	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [0/0]	582.83 (-) [2,300.00]	241.39 (1,717.17) [0]
1327	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [900.00]	62.50 (672.60) [0]
1328	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2021]	303.98 (-) [980.00]	669.21 (676.02) [12]
1329	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	Road Transport And Highways				
1330	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [0/0]	485.00 (-) [485.00]	406.68 (0.00) [0]
1331	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1332	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [11/2019]	244.27 (-) [244.27]	105.81 (0.00) [26]
1333	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [8/2020]	1,227.87 (-) [1,227.87]	159.23 (0.00) [35]
1334	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1335	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1336	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (1/2019) [8/2020]	600.00 (-) [600.00]	329.92 (0.00) [86]
1337	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [4/2021]	1,016.92 (-) [1,071.00]	0.00 (54.08) [-]
1338	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [7/2019]	1,387.11 (-) [1,387.11]	974.13 (0.00) [0]
1339	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [11/2020]	628.71 (-) [628.71]	59.22 (0.00) [-]
1340	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1341	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-)	1,166.26 (-)	0.00 (0.00)

			[2/2021]	[1,166.26]	[-]
1342	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [5/2020]	641.17 (-) [641.17]	340.73 (0.00) [46]
1343	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [11/2020]	505.35 (-) [505.35]	36.14 (0.00) [-]
1344	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [9/2020]	1,176.37 (-) [1,176.37]	122.89 (0.00) [37]
1345	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2020]	707.82 (-) [707.82]	343.21 (0.00) [19]
1346	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	64.68 (0.00) [0]
1347	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [5/2020]	641.17 (-) [641.17]	340.73 (0.00) [22]
1348	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1349	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2020]	379.90 (-) [379.90]	100.76 (0.00) [-]
1350	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [6/2020]	1,250.00 (-) [1,250.00]	1,333.68 (0.00) [78]
1351	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1352	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	936.30 (0.00) [0]
1353	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [0/0]	374.00 (-) [374.00]	237.00 (0.00) [0]
1354	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1355	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [8/2019]	563.92 (-) [563.92]	93.53 (0.00) [20]
	<u>Urban Development</u>				
1356	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [3/2020]	209.00 (-) [209.00]	130.62 (0.00) [5]
1357	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1358	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.87 (4,458.00) [0]
1359	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [11/2021]	348.77 (-) [348.77]	12.00 (0.00) [-]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1360	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	2.11 (0.00) [0]

1361	KOYAGUDEM OPENCAS T PROJECT	10/2015	3/2018 (-) [3/2020]	426.79 (-) [426.79]	0.72 (0.00) [24]
1362	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2021]	447.06 (-) [473.22]	18.35 (26.16) [72]
1363	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1364	KAKATIYAKHANI OPENCAS T III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	54.00 (0.00) [36]
1365	KAKATIYAKHANI OPENCAS T-2 PROJECT	5/2015	3/2019 (-) [3/2020]	397.09 (-) [442.42]	92.09 (45.33) [12]
1366	KALYANIKHANI OPENCAS T PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [384.32]	92.60 (-33.01) [44]
1367	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	115.49 (-78.25) [72]
1368	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	170.60 (0.00) [0]
1369	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	343.10 (70.65) [132]
1370	RAMPURAM SHAFT BLOCK	8/2016	/ (3/2023) [0/0]	431.92 (-) [431.92]	0.00 (0.00) [0]
1371	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	8.00 (186.52) [72]
1372	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2020]	430.45 (-) [415.37]	186.99 (-15.08) [48]
1373	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [12/2015]	365.01 (-) [365.01]	134.09 (0.00) [0]
1374	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2020]	209.78 (-) [209.78]	154.58 (0.00) [60]
1375	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2024]	249.03 (-) [448.86]	286.19 (199.83) [144]
1376	SRAVANAPALLI OPENCAS T PROJECT	2/2018	/ (3/2023) [0/0]	412.70 (-) [412.70]	0.11 (0.00) [0]
1377	SRP OC-II EXPANSION PROJECT	11/2016	/ (4/2017) [3/2020]	272.73 (-) [272.73]	144.07 (0.00) [-]
	<u>Petroleum</u>				
1378	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [4/2022]	611.00 (-) [611.00]	1.68 (0.00) [0]
	<u>Power</u>				
1379	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (6/2021) [6/2021]	10,598.98 (-) [10,598.98]	5,382.09 (0.00) [7]
	<u>Railways</u>				
1380	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II	4/2012	3/2016	632.68	682.17

	HYDERABAD		(-) [12/2020]	(-) [816.55]	(183.87) [57]
1381	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	281.85 (0.00) [0]
1382	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	723.00 (-) [997.09]	0.00 (274.09) [0]
1383	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-) [0/0]	458.25 (-) [458.26]	3.83 (0.01) [0]
1384	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	3.67 (65.24) [0]
1385	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2023]	1,160.48 (-) [1,160.48]	288.38 (0.00) [156]
1386	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1387	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	372.81 (0.00) [0]
	<u>Road Transport And Highways</u>				
1388	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [9/2019]	1,266.60 (1,544.00) [1,544.00]	1,446.45 (277.40) [36]
1389	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [5/2020]	283.15 (-) [283.15]	42.22 (0.00) [0]
1390	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [7/2020]	626.76 (-) [626.76]	80.66 (0.00) [0]
1391	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [9/2019]	153.21 (-) [153.21]	100.10 (0.00) [32]
1392	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1393	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	0.03 (0.00) [0]
1394	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	79.72 (0.00) [0]
1395	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	61.95 (0.00) [0]
1396	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (-) [0/0]	828.29 (-) [828.29]	0.00 (0.00) [0]
1397	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [12/2019]	1,423.96 (897.03) [897.03]	705.85 (-526.93) [13]
1398	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [12/2019]	192.67 (-) [192.67]	107.35 (0.00) [5]
1399	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [10/2019]	605.08 (-) [605.08]	260.32 (0.00) [0]
1400	REHABILITATION AND UPGRADATION OF HYDERABAD	2/2018	4/2020	426.52	200.79

	OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN		(-) [4/2020]	(-) [426.52]	(0.00) [0]
1401	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1402	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [11/2019]	294.13 (-) [294.13]	30.35 (0.00) [0]
1403	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [11/2019]	220.28 (-) [220.28]	22.17 (0.00) [0]
1404	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [9/2020]	322.81 (-) [322.81]	1.66 (0.00) [0]
1405	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [12/2019]	248.83 (-) [248.83]	88.85 (0.00) [9]
1406	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [12/2019]	298.32 (-) [298.32]	77.44 (0.00) [10]
1407	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [12/2019]	230.03 (-) [230.03]	127.98 (0.00) [0]
1408	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [6/2020]	206.13 (-) [206.13]	116.63 (0.00) [0]
1409	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	0.00 (0.00) [0]
1410	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [10/2019]	196.52 (-) [196.52]	98.61 (0.00) [0]
1411	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019 (-) [12/2019]	283.00 (-) [283.00]	151.88 (0.00) [0]
1412	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (9/2019) [9/2019]	244.54 (-) [244.54]	137.10 (0.00) [4]
1413	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT	1/2017	5/2019 (-) [8/2019]	359.27 (-) [359.27]	227.88 (0.00) [3]
1414	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (-) [12/2019]	300.00 (-) [300.00]	99.46 (0.00) [7]
	<u>Urban Development</u>				
1415	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	35.79 (0.00) [14]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1416	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [12/2019]	338.93 (-) [339.00]	213.50 (0.07) [6]
	<u>Railways</u>				
1417	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [12/2021]	569.63 (-) [650.00]	45.24 (80.37) [21]
	<u>Road Transport And Highways</u>				
1418	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	297.12 (0.00) [0]

1419	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	14.77 (0.00) [0]
	<u>Urban Development</u>				
1420	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1421	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1422	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1423	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2021]	1,383.00 (-) [1,383.00]	210.62 (0.00) [0]
	<u>Coal</u>				
1424	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	7,203.71 (0.80) [0]
	<u>Health And Family Welfare</u>				
1425	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [6/2020]	785.00 (-) [785.00]	244.66 (0.00) [2]
1426	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	99.26 (0.00) [-]
	<u>Petroleum</u>				
1427	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	9/2019 (-) [9/2019]	204.00 (-) [204.00]	139.25 (0.00) [0]
1428	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	96.35 (0.00) [0]
1429	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	376.04 (0.00) [0]
1430	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	123.35 (0.00) [0]
1431	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	0.71 (0.00) [0]
1432	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	13.47 (0.00) [0]
1433	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY	8/2016	11/2019 (-) [11/2019]	154.84 (-) [154.84]	118.06 (0.00) [0]
1434	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	40.06 (0.00) [3]
	<u>Power</u>				
1435	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-) [9/2020]	587.44 (-) [587.44]	250.00 (0.00) [0]
1436	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (-) [11/2020]	349.00 (-) [349.00]	125.00 (0.00) [0]

1437	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (-) [10/2019]	195.42 (-) [294.60]	302.76 (99.18) [68]
1438	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [9/2023]	11,089.42 (-) [11,089.42]	511.64 (0.00) [0]
1439	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [6/2020]	9,750.89 (-) [12,176.28]	9,749.00 (2,425.39) [40]
1440	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (6/2020) [6/2020]	9,188.98 (-) [9,188.98]	6,397.93 (0.00) [11]
	<u>Railways</u>				
1441	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1442	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2022]	600.00 (-) [600.00]	25.24 (0.00) [0]
1443	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1444	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	1,032.16 (0.00) [3]
1445	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	17.35 (111.84) [0]
1446	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1447	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1448	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [3/2015]	120.00 (-) [346.00]	345.51 (226.00) [0]
1449	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1450	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [6/2020]	213.00 (-) [213.35]	8.97 (0.35) [50]
1451	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	416.59 (0.00) [0]
1452	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	3.90 (0.00) [0]
1453	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1454	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [12/2019]	528.57 (-) [528.57]	94.31 (0.00) [9]
1455	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [1,200.00]	1,147.34 (272.99) [12]
1456	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [3/2020]	668.70 (668.00) [680.00]	330.00 (11.30) [0]

1457	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	568.43 (0.00) [21]
1458	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1459	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1460	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [1/2020]	622.50 (427.00) [426.74]	179.51 (-195.76) [33]
1461	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	494.58 (0.00) [12]
1462	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [12/2019]	1,295.42 (-) [1,295.42]	328.56 (0.00) [-27]
1463	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	26.06 (-149.01) [16]
1464	UNCHAHAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,230.00]	103.17 (1.00) [-]
1465	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [750.56]	343.30 (-193.04) [33]
<u>Road Transport And Highways</u>					
1466	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (3/2018) [3/2018]	368.73 (-) [368.73]	232.93 (0.00) [0]
1467	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
1468	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	433.68 (0.00) [0]
1469	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	633.24 (0.00) [0]
1470	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [291.36]	459.07 (0.00) [0]
1471	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	207.94 (0.00) [0]
1472	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (11/2019) [11/2019]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [7]
1473	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,120.57]	0.00 (0.00) [0]
1474	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [1/2020]	1,668.00 (-) [1,668.00]	946.08 (0.00) [-]
1475	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1476	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [7/2020]	1,408.00 (-) [1,408.00]	442.70 (0.00) [-]

1477	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [-]
1478	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	92.37 (0.00) [0]
1479	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (10/2019) [10/2019]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [6]
1480	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1481	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [0/0]	1,657.20 (-) [1,657.20]	2,345.00 (0.00) [0]
1482	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [3/2020]	2,064.99 (-) [2,447.00]	1,653.62 (382.01) [0]
1483	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1484	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	632.21 (0.00) [0]
1485	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [0/0]	1,046.00 (-) [1,046.00]	805.19 (0.00) [0]
1486	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (2/2019) [2/2022]	972.77 (1,444.25) [972.77]	0.00 (0.00) [-]
1487	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [9/2019]	534.55 (-) [531.00]	433.62 (-3.55) [-]
1488	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1489	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (12/2018) [12/2021]	1,117.84 (1,684.93) [1,117.84]	0.00 (0.00) [-]
1490	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1491	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1492	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (12/2016) [9/2019]	1,081.57 (1,240.03) [1,057.60]	1,000.89 (-23.97) [3]
1493	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (2/2018) [3/2020]	1,232.21 (3,207.63) [1,087.00]	473.11 (-145.21) [-]
1494	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (11/2017) [5/2020]	1,989.00 (2,602.09) [1,989.00]	852.57 (0.00) [2]
1495	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018 (-) [0/0]	785.78 (-) [785.78]	902.00 (0.00) [0]
1496	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	1,998.25 (0.00) [0]
1497	FOR REHABILITATION AND UPGRADATION FROM 2-LANE	2/2018	/	670.50	0.00

	TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP		(-) [0/0]	(-) [670.50]	(0.00) [0]
1498	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/	809.07	0.00
			(-) [0/0]	(-) [809.07]	(0.00) [0]
1499	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/	925.40	0.00
			(-) [0/0]	(-) [925.40]	(0.00) [0]
1500	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018	667.00	549.07
			(-) [4/2020]	(3,007.86) [667.00]	(0.00) [22]
1501	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018	667.00	464.05
			(-) [4/2020]	(2,257.49) [667.00]	(0.00) [21]
1502	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018	1,027.53	601.13
			(-) [6/2020]	(2,433.38) [1,027.53]	(0.00) [24]
1503	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018	815.28	520.89
			(-) [6/2020]	(2,182.03) [815.28]	(0.00) [24]
1504	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017	261.09	240.96
			(-) [0/0]	(275.00) [261.09]	(0.00) [0]
1505	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN	3/2018	8/2020	288.30	0.34
			(-) [8/2020]	(-) [288.30]	(0.00) [0]
1506	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020	1,373.28	571.96
			(-) [11/2020]	(-) [1,373.28]	(0.00) [8]
1507	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020	1,184.71	563.15
			(-) [8/2020]	(-) [1,310.00]	(125.29) [5]
1508	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019	899.00	532.53
			(7/2020) [7/2020]	(-) [899.00]	(0.00) [15]
1509	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013	1,141.00	1,715.42
			(-) [0/0]	(-) [1,141.00]	(0.00) [0]
1510	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/	281.45	0.00
			(-) [0/0]	(-) [281.45]	(0.00) [0]
1511	MEERUT-BULANDSHAHR	1/2016	/	683.24	623.53
			(-) [0/0]	(-) [683.24]	(0.00) [0]
1512	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019	209.10	85.74
			(-) [10/2019]	(-) [209.10]	(0.00) [0]
1513	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/	326.99	0.00
			(-) [0/0]	(327.00) [326.99]	(0.00) [0]
1514	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020	296.50	0.51
			(-) [9/2020]	(-) [296.50]	(0.00) [0]
1515	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/	1,025.80	115.83
			(-) [0/0]	(-) [677.07]	(-348.73) [0]
1516	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/	1,115.28	194.57
			(-) [0/0]	(-) [770.04]	(-345.24) [0]
1517	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E	10/2016	2/2019	239.63	211.57
			(-)	(-)	(0.00)

	TO 2-		[7/2019]	[239.63]	[0]
1518	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [12/2019]	388.83 (-) [388.83]	280.17 (0.00) [0]
1519	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2020]	263.89 (-) [263.89]	119.70 (0.00) [0]
1520	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [11/2019]	208.50 (-) [208.50]	123.66 (0.00) [0]
1521	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [9/2019]	445.89 (653.00) [653.29]	464.05 (207.40) [30]
1522	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [1/2020]	599.34 (-) [599.34]	435.14 (0.00) [0]
1523	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [2/2020]	185.18 (-) [185.18]	2.86 (0.00) [0]
1524	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [11/2019]	249.50 (-) [249.50]	150.70 (0.00) [6]
1525	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [3/2020]	218.90 (-) [218.90]	23.37 (0.00) [0]
1526	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1527	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [9/2019]	215.16 (215.00) [215.16]	157.79 (0.00) [0]
1528	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [1/2020]	240.30 (240.00) [240.30]	194.01 (0.00) [0]
1529	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [3/2020]	218.94 (219.00) [218.94]	86.07 (0.00) [0]
1530	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [9/2019]	176.94 (177.00) [176.94]	132.45 (0.00) [11]
1531	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [10/2019]	208.88 (-) [208.88]	36.25 (0.00) [0]
1532	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [9/2019]	445.89 (-) [653.29]	464.05 (207.40) [30]
1533	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	715.78 (0.00) [0]
1534	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1535	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (929.89) [450.77]	0.00 (0.00) [0]
1536	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [9/2019]	164.54 (165.00) [164.54]	89.14 (0.00) [49]
1537	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [9/2019]	164.54 (-) [164.54]	89.14 (0.00) [49]

	<u>Steel</u>				
1538	FORGED WHEEL PLANT	4/2014	9/2018 (9/2019) [9/2019]	1,682.85 (-) [1,682.85]	1,175.53 (0.00) [12]
	<u>Urban Development</u>				
1539	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	32.00 (0.00) [0]
1540	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1541	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2020]	353.27 (-) [353.27]	114.29 (0.00) [0]
	<u>Petroleum</u>				
1542	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [10/2020]	160.10 (-) [160.10]	41.22 (0.00) [8]
	<u>Power</u>				
1543	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	148.91 (274.07) [0]
1544	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	255.15 (0.00) [0]
1545	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (5,867.38) [5,867.38]	4,155.88 (2,888.90) [93]
1546	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2022]	1,657.00 (-) [5,024.35]	3,003.16 (3,367.35) [76]
1547	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2022]	2,491.58 (-) [4,397.80]	1,733.13 (1,906.22) [114]
	<u>Railways</u>				
1548	HARIDWAR-LAKSAR	4/2012	/ (-) [6/2020]	219.83 (-) [346.63]	229.48 (126.80) [-]
1549	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1550	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2026]	16,216.00 (-) [16,216.00]	1,521.62 (0.00) [15]
	<u>Road Transport And Highways</u>				
1551	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	89.19 (0.00) [0]
1552	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	87.71 (0.00) [0]
1553	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (12/2019) [2/2020]	605.84 (-) [722.46]	722.46 (116.62) [19]
1554	4-LANNING OF CHUTMALPUR-GANESHPUK SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [-]
1555	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO	3/2018	5/2018 (-)	274.31 (-)	19.22 (0.00)

	KM 399		[0/0]	[274.31]	[0]
1556	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	94.57 (0.00) [0]
1557	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1558	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (10/2020) [10/2020]	720.00 (-) [720.00]	278.01 (0.00) [-]
1559	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [2/2020]	478.51 (-) [478.00]	315.11 (-0.51) [76]
1560	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	59.44 (0.00) [0]
1561	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [283.51]	126.38 (0.00) [0]
1562	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	62.79 (0.00) [0]
1563	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [12/2019]	282.08 (-) [282.08]	77.05 (0.00) [6]
1564	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	31.00 (0.00) [0]
1565	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	88.00 (0.00) [0]
1566	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	144.27 (0.00) [0]
1567	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [12/2019]	234.88 (-) [208.89]	118.26 (-25.99) [24]
1568	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1569	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1570	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1571	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1572	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (-) [11/2021]	264.99 (-) [264.99]	0.42 (0.00) [0]
1573	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (-) [12/2020]	219.91 (-) [219.91]	61.61 (0.00) [9]
	<u>Coal</u>				
1574	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-)	602.86 (-)	315.31 (0.00)

			[3/2022]	[602.86]	[0]
1575	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.00 (0.00) [0]
1576	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1577	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	501.35 (0.00) [24]
1578	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.00 (0.00) [0]
	<u>Health And Family Welfare</u>				
1579	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [0/0]	244.00 (-) [244.00]	241.39 (0.00) [0]
1580	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [2/2020]	651.99 (-) [651.99]	112.82 (0.00) [-]
1581	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2020]	355.15 (-) [355.15]	148.84 (0.00) [12]
	<u>Petroleum</u>				
1582	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,696.00]	189.41 (-16.00) [-15]
1583	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-) [9/2019]	2,934.40 (-) [2,934.40]	1,569.01 (0.00) [0]
1584	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	173.41 (0.00) [0]
1585	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1586	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (12/2019) [12/2019]	694.00 (1,097.54) [1,097.54]	698.76 (403.54) [14]
1587	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [3/2021]	163.02 (-) [163.02]	50.84 (0.00) [11]
	<u>Power</u>				
1588	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [3/2020]	529.68 (-) [529.68]	140.10 (0.00) [16]
1589	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (-) [1/2020]	454.11 (-) [454.11]	287.52 (0.00) [21]
1590	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,592.34]	481.22 (210.50) [29]
	<u>Railways</u>				
1591	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (3/2030) [3/2030]	1,027.40 (-) [2,373.00]	485.04 (1,345.60) [324]
1592	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (12/2017) [3/2025]	1,106.62 (-) [1,091.59]	834.72 (-15.03) [171]
1593	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-)	255.64 (-)	154.98 (16.56)

			[9/2021]	[272.20]	[-]
1594	BOWAICHANDI-ARAMBAGH	4/2010	/ (3/2025) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1595	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1596	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1597	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1598	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (3/2022) [3/2022]	221.42 (-) [380.00]	38.18 (158.58) [-]
1599	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (-) [614.00]	274.97 (316.68) [12]
1600	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,871.00]	1,087.60 (1,490.40) [0]
1601	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	257.73 (9.73) [-21]
1602	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	2,106.00 (435.44) [141]
1603	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [2,913.50]	847.45 (-0.01) [108]
1604	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1605	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,226.44 (307.50) [108]
1606	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	863.39 (430.57) [72]
1607	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
Road Transport And Highways					
1608	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [12/2019]	1,083.00 (-) [1,083.00]	26.64 (0.00) [18]
1609	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2020]	998.79 (-) [998.79]	1,775.04 (0.00) [82]
1610	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [12/2019]	1,078.84 (-) [1,078.84]	2,173.80 (0.00) [76]
1611	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [12/2019]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [63]
1612	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2020]	361.15 (-) [361.15]	144.71 (0.00) [-]
1613	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND	3/2017	6/2018 (-)	158.65 (-)	31.67 (0.00)

	PANITNAKI I		[0/0]	[158.65]	[0]
1614	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (11/2019) [11/2019]	271.17 (291.20) [291.20]	79.43 (20.03) [12]
1615	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [8/2021]	160.27 (213.97) [213.97]	20.11 (53.70) [24]
1616	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [12/2019]	229.37 (-) [229.37]	78.31 (0.00) [13]
1617	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [8/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [24]
1618	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [10/2020]	254.30 (254.30) [254.30]	20.26 (0.00) [0]
1619	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (-) [767.03]	502.91 (0.00) [13]
1620	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [6/2020]	702.16 (-) [702.16]	733.33 (0.00) [71]
1621	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	644.40 (120.10) [0]
1622	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	722.56 (114.56) [0]
1623	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,261.98]	0.00 (0.00) [0]
1624	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (7/2019) [7/2019]	279.70 (398.52) [398.52]	314.63 (118.82) [0]
1625	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (-) [9/2019]	396.86 (396.86) [396.86]	179.31 (0.00) [0]
1626	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1627	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [6/2019]	1,665.00 (-) [1,665.00]	3,059.39 (0.00) [0]
1628	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [11/2019]	202.69 (202.69) [202.69]	93.93 (0.00) [0]
1629	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [11/2020]	218.70 (218.70) [218.70]	25.02 (0.00) [0]
1630	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [9/2020]	426.18 (426.18) [426.18]	218.00 (0.00) [0]
	<u>Steel</u>				
1631	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [9/2020]	263.36 (-) [263.36]	10.81 (0.00) [0]
	<u>Urban Development</u>				
1632	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [10/2019]	156.57 (-) [156.57]	156.13 (0.00) [38]
1633	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR	8/2012	3/2016	185.37	178.30

	24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG		(-) [0/0]	(-) [185.37]	(0.00) [0]
1634	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	131.07 (0.00) [0]
	Total			19,40,699.03 (5,01,732.60) [23,29,746.02]	9,75,180.06 (3,89,046.99)

North-East Central Sector Project Detail's

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					31.08.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (10/2019) [10/2019]	2,496.90 (7,927.34) [7,927.34]	7,516.58 (5,430.44) [118]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,945.40 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	108.75 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	272.92 (0.00) [21]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	159.75 (0.00) [15]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
7	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	115.02 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	90.29 (0.00) [0]
9	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [0/0]	243.89 (-) [243.89]	30.04 (0.00) [0]
10	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	154.43 (0.00) [0]
11	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	143.01 (0.00) [0]
12	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	72.97 (0.00) [0]
13	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	125.96 (0.00) [0]
14	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	30.88 (0.00) [0]

15	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	17.43 (16.07) [36]
16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	98.37
			(-) [9/2020]	(-) [245.79]	(0.00) [-]
17	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2019]	198.00 (-) [198.00]	195.67 (0.00) [36]
18	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	66.17 (0.00) [0]
19	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	154.14
			(-) [0/0]	(-) [1,718.59]	(0.00) [0]
20	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	211.21 (0.00) [60]
21	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (2/2018) [2/2021]	167.28 (167.28) [167.28]	18.70 (0.00) [46]
22	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (2/2018) [2/2021]	216.71 (216.71) [216.71]	15.77 (0.00) [46]
23	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
24	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	126.58
			(-) [12/2020]	(-) [434.06]	(0.00) [-]
25	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	64.66 (0.00) [47]
26	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	37.30 (0.00) [0]
27	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	49.12 (0.00) [0]
28	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	75.04 (0.00) [0]
29	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	24.14 (0.00) [0]
30	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (389.45) [389.45]	275.19 (182.42) [0]
31	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	13.73 (0.00) [46]
32	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	28.67 (0.00) [46]
33	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
34	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
35	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON	1/2017	/	256.66	24.14

	EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI		(-) [0/0]	(-) [256.66]	(0.00) [0]
36	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	6.58 (0.00) [-]
37	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	5.63 (0.00) [-]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	9.65 (0.00) [-]
39	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	6.19 (0.00) [-]
40	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (-) [0/0]	1,979.00 (-) [1,979.00]	59.40 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
41	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	<u>Health And Family Welfare</u>				
42	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
43	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
44	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
45	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	178.05 (0.00) [0]
46	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	531.40 (0.00) [0]
47	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	3.30 (0.00) [0]
48	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
49	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (345.92) [345.92]	145.60 (142.98) [70]
50	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	263.70 (0.00) [1]
51	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2020]	543.91 (-) [682.90]	8.75 (138.99) [4]
52	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,526.40 (0.00) [0]
53	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	157.81 (15.64) [0]
54	UPGRADATION OF CRUDE OIL PUMP STATIONS OF	9/2012	3/2015	871.35	565.63

	NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE		(-) [0/0]	(-) [1,200.00]	(328.65) [0]
	<u>Railways</u>				
55	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	704.09 (414.00) [12]
56	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	654.38 (-50.32) [-24]
57	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	502.44 (1,265.05) [0]
58	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	629.19 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
59	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	201.56 (0.00) [0]
60	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
61	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
62	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	66.66 (0.00) [0]
63	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	50.39 (0.00) [0]
64	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	356.31 (0.00) [0]
65	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	16.98 (0.00) [0]
66	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [12/2021]	252.00 (-) [252.00]	4.74 (0.00) [71]
67	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (12/2020) [12/2021]	437.39 (-) [437.39]	9.30 (0.00) [42]
68	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (2/2019) [4/2021]	294.17 (-) [294.17]	63.00 (0.00) [63]
69	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	451.15 (143.23) [0]
70	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
71	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.68 (7.98) [0]
72	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	304.28 (0.00) [0]
73	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	66.66 (0.00) [0]

74	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	58.58 (0.00) [-]
75	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	22.32 (0.00) [42]
76	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	292.24 (0.00) [0]
77	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	120.86 (0.00) [31]
78	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (456.92) [525.00]	488.37 (245.00) [0]
79	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
80	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
81	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [124]
82	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (408.77) [408.77]	395.78 (241.13) [0]
83	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	337.76 (22.00) [143]
84	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	328.47 (0.00) [136]
85	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	0.00 (0.00) [0]
86	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	224.28 (-70.66) [149]
87	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (307.47) [307.47]	256.26 (89.16) [0]
88	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
<u>MANIPUR</u>					
<u>Power</u>					
89	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
<u>Railways</u>					
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (13,809.00) [12,524.00]	9,123.93 (8,069.83) [108]
<u>Road Transport And Highways</u>					
91	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	74.49 (0.00) [0]
92	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	119.56 (-59.80) [36]

	<u>Urban Development</u>				
93	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
94	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
95	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.76 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
96	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	42.66 (0.00) [0]
97	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (3/2018) [12/2019]	479.20 (-) [479.20]	708.82 (0.00) [19]
98	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	<u>Urban Development</u>				
99	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
100	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,075.08 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
101	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	305.38 (182.95) [116]
102	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	275.06 (118.65) [63]
103	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
104	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
105	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
106	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
107	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
108	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
109	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
110	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED	4/2017	9/2019	640.07	0.00

	SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO		(-) [9/2019]	(-) [640.07]	(0.00) [0]
111	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
112	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	853.82 (368.26) [105]
	<u>NAGALAND</u>				
	<u>Railways</u>				
113	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
114	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [3,000.00]	781.71 (673.48) [79]
	<u>Road Transport And Highways</u>				
115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
117	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (-) [282.98]	12.76 (0.00) [0]
118	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	127.19 (0.00) [0]
119	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
120	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
121	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	121.20 (0.00) [0]
122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [339.57]	0.00 (0.00) [0]
123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	4.38 (0.00) [0]
124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	2.11 (0.00) [0]
125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	6.86 (0.00) [0]
126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900	3/2018	9/2018 (11/2018)	251.97 (160.10)	13.42 (0.00)

	TO KM40.0		[0/0]	[251.97]	[0]
130	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	59.42 (0.00) [0]
131	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (387.00) [373.07]	203.77 (0.00) [36]
132	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [396.52]	234.03 (0.00) [46]
133	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (340.00) [429.52]	166.55 (0.00) [36]
134	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (369.96) [336.25]	62.64 (0.00) [0]
135	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	42.15 (0.00) [0]
136	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	45.02 (0.00) [0]
137	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
138	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
139	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [0]
	<u>Road Transport And Highways</u>				
140	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (9/2017) [12/2019]	182.28 (269.14) [269.14]	185.49 (86.86) [82]
141	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [76]
142	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (203.26) [166.27]	141.31 (0.00) [0]
143	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
144	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	34.86 (0.00) [0]
145	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	97.85 (0.00) [0]
146	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
147	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	97.85 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
148	CONSTRUCTION OF NEW INTEGRATED TERMINAL	9/2015	6/2019	338.93	213.50

	BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT		(-) [12/2019]	(-) [339.00]	(0.07) [6]
	<u>Railways</u>				
149	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [12/2021]	569.63 (-) [650.00]	45.24 (80.37) [21]
	<u>Road Transport And Highways</u>				
150	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	297.12 (0.00) [0]
151	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	14.77 (0.00) [0]
	<u>Urban Development</u>				
152	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
153	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
154	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			84,828.31 (38,265.99) [1,28,837.95]	55,730.65 (44,009.64)
