

दलनह; {k= dh ifj;kt ukvk
CENTRAL SECTOR PROJECTS

**₹150 djkm vkj vf/kd ykxr okyh
(₹ 150 Crore and above)**

**362oh ¶Yk'k fj ikVl@362nd Flash Report
fn lEcj] 2015@December, 2015**



Hkkjr ljdkj / Government of India

lkf[;dh vkj dk;Øe dk;kUo;u e=ky ;

Ministry of Statistics and Programme Implementation

**vk/kkjh ljpuk vkj ifj;kt uk i=ck/ku iHkkx
Infrastructure and Project Monitoring Division**

l jnkj iV;y Hkou] lln ekx]

Sardar Patel Bhavan, Sansad Marg,

ub] fnYyh / New Delhi-110001

oc lkbV / Website- www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

	Pages
Executive Summary Hindi	1-22
Executive Summary English	23-41
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2015-2016	42-46
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2015-2016	47-48
Summary of projects	49-78
Graphical Presentation of All Projects	79-92
Sector wise Analysis of Projects	93-145
Sector wise Graph	146-158
Annexures	160-160
Status of central sector projects costing Rs.150 Crore and above	161-161
List of projects in which expenditure is more than approved cost	162-172
Details of Projects Ahead of Schedule w.r.t. Original Schedule	173-173
Details of On Schedule Projects w.r.t. Original Schedule	174-186
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	187-198
Details of Delayed Projects w.r.t. Original and Revised Schedule	199-228
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	229-233
Details of Projects Without Date of Commissioning	234-253
Details of projects without original Date of Commissioning	254-255
Details of projects without Milestones w.r.t. original schedule	256-289
List of Projects Ahead of Schedule w.r.t. Latest Schedule	290-291
List of Projects on schedule w.r.t. Latest Schedule	292-307
List of ongoing projects having cost overrun w.r.t. to revised schedule	308-317
List of Delayed Projects w.r.t. Latest Schedule	318-332
Details of Central Sector Projects Showing Time overruns of 6 Months and More	333-347
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	348-356
Details Of Central Sector Projects Showing Time Overruns of 6 Months and More and cost overruns of Rs. 100 Crore and above	357-361
Details of 20 Railways Projects	362-363

कार्यकारी सारांश

1. दिसंबर, 2015 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 1058 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। दिसंबर 2015 के दौरान, 9 परियोजनाओं (पेट्रोलियम क्षेत्र की 4 परियोजनाएं, पोत परिवहन एवं पत्तन, दूरसंचार, विद्युत, नागर विमानन तथा कोयला क्षेत्र की प्रत्येक में 1 परियोजना) के पूरा होने की सूचना दी गई है।
2. संदर्भाधीन माह के दौरान, 1058 परियोजनाओं में से, 334 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 51 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 51 परियोजनाओं में से, 13 परियोजनाएं ₹1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	सड़क परिवहन एवं राजमार्ग	411	125	7	1
2.	रेलवे	297	33	4	2
3.	विद्युत	105	58	13	5
4.	कोयला	87	44	4	0
5.	पेट्रोलियम	59	33	6	2
6.	इस्पात	36	12	10	1
7.	शहरी विकास	31	14	3	1
8.	स्वास्थ्य और परिवार कल्याण	9	3	2	0
9.	पोत परिवहन एवं पत्तन	8	3	1	0
10.	नागर विमानन	4	1	0	0
11.	परमाणु ऊर्जा	4	4	0	0
12.	खान	3	1	1	1
13.	उर्वरक	1	0	0	0
14.	दूरसंचार	1	1	0	0
15.	पेट्रोरसायन	1	1	0	0
16.	भारी उद्योग	1	1	0	0
कुल		1058	334	51	13

3. 1058 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹ 11,68,413.82 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 13,79,878.25 करोड़ होने की संभावना है, जो

₹ 2,11,464.43 करोड़ (मूल लागत का 18.10%) की समग्र लागत वृद्धि को दर्शाता है। दिसंबर, 2015 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,89,925.05 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 42.75% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31.12.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ ₹.)	अनुमानित लागत (करोड़ ₹.)	लागत वृद्धि (%)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं.56 एनओएस एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	12.18
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	87.58
3	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
4	रामगुंडम ओसी-II विस्तार	12/2009	418.97	489.62	16.86
5	मनुगुरु ओसी परियोजना का आरएफआर	11/2012	430.45	486.27	12.97
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	9965.00	82.49
पेट्रोलियम					
1	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
2	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62

3	कोरबा में विपणन टीओपी	01/2011	141.86	219.00	54.38
4	उरान चाकन/शिकरापुर एलपीजी पाइपलाइन	12/2009	309.81	462.79	49.38
5	रिंग सागर सम्राट से मोबाइल ऑफशोर प्रोडक्शन यूनिट (एमओपीएस) का रुपांतरण	03/2011	861.79	1256.72	45.83
विद्युत					
1	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
2	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी))	09/2003	6285.33	18063.89	187.40
3	कामेंग जल विद्युत परियोजना (नीपको	12/2004	2496.90	6085.84	143.74
4	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.57	139.32
5	रघुनाथपुर ताप विद्युत स्टेशन फेज-I	04/2007	4122.00	9606.82	133.06
रेलवे					
1	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
2	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
3	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	09/1998	247.66	3500.00	1313.23
4	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
5	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर छः लेन (96 किमी. से 387.1 किमी.)	05/2009	1108.00	2288.00	106.50
2	एचओजे के दो लेनिंग-अरुणाचल प्रदेश के अंतर्गत अरुणाचल प्रदेश में एनएच-229 (19.06 किमी) का पोतिन सेक्शन	12/2009	82.73	165.00	99.44
3	यूपिया के दो लेनिंग अरुणाचल प्रदेश के अंतर्गत अरुणाचल प्रदेश में एचओजे सेक्शन (20.40 किमी)	12/2009	104.00	201.00	93.27
4	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
5	मैबंग से लुमडिंग (एएस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
पोत परिवहन एवं पत्तन					

1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	150.00	600.00	300.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
3	कोचीन पोर्ट ट्रस्ट के वल्लारपाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	66.82
4	कामराजर पोर्ट लिमिटेड में कोल बर्थ-4 का निर्माण	02/2015	244.50	258.33	5.66
इस्पात					
1	सिंटर मशीनों - 1 और 2 की रिक्विजिटिंग	12/2009	343.00	488.40	42.39
2	गुलबर्गा में चिकित्सा महाविद्यालय तथा अस्पताल का निर्माण	05/2005	768.88	1060.00	37.86
3	पीएमजीएसवाई फेज VIII के तहत ग्रामीण सड़क का निर्माण एवं रखरखाव	10/2011	175.49	207.00	17.96
4	पीएमजीएसवाई फेज V के तहत ग्रामीण सड़क का निर्माण एवं रखरखाव	03/2007	149.73	173.00	15.54
5	पीएमजीएसवाई फेज VI के तहत ग्रामीण सड़क का निर्माण एवं रखरखाव	12/2007	202.61	227.00	12.04
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	13845.01	116.50

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार हैं:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.12.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
	परमाणु ऊर्जा				

1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं.56 एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	26.50
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	227.17
3	रामगुंडम ओसी-II विस्तार	12/2009	418.97	489.62	70.65
4	मनुगुरु ओसी परियोजनाओं के आरएफआर	11/2012	430.45	486.27	55.82
5	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	48.00
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोसायन					
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	9965.00	4504.39
पेट्रोलियम					
1	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
2	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
3	वशिष्टा तथा एस-1 क्षेत्रों का समेकित विकास	05/2013	4124.35	4941.49	817.14
4	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
5	बी-127 क्षेत्रों का समेकित विकास	12/2011	2059.63	2665.65	606.02
विद्युत					
1	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	18063.89	11778.56
2	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	रघुनाथपुर थर्मल पावर स्टेशन फेज-I	04/2007	4122.00	9606.82	5484.82
4	पार्वती एचईपी (4x200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7818.68	3899.09

5	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6085.84	3588.94
रेलवे					
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
2	जिरिबाम से इम्फाल (तुपुई)(एनएल)(एनईएफआर)	04/2003	727.56	6570.75	5843.19
3	लुमडिंग-सिलचर जिरिबाम, बदरपुर- बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
4	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
5	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	09/1998	247.66	3500.00	3252.34
सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
2	मैंबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
3	हरंगाजो से मैंबंग, एनएच-54	12/2003	196.00	331.23	135.23
4	मैंबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी. एनएच-54	12/2003	155.04	280.13	125.09
5	एलडब्ल्यूई एस के तहत एनएच-202 पर अप्रोच रोड सहित वेंकटपुरम के समीप गोदावरी नदी पुल का निर्माण	03/2011	218.31	339.82	121.51
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	150.00	600.00	450.00
2	ऑफशोर कंटेनर बर्थ का निर्माण तथा मुंबई में बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
3	कोचीन पोर्ट ट्रस्ट के वल्लारपाड़म में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	164.16
4	कामराजर पोर्ट लिमिटेड पर कोल बर्थ-4 का निर्माण	02/2015	244.50	258.33	13.83
इस्पात					
1	गुलबर्गा में चिकित्सा महाविद्यालय तथा अस्पताल का निर्माण	05/2005	768.88	1060.00	291.12
2	सिंटर मशीनों - 1 और 2 की रिवैम्पिंग	12/2009	343.00	488.40	145.40
3	पीएमजीएसवाई फेज VIII के तहत ग्रामीण सड़क का निर्माण एवं रखरखाव	10/2011	175.49	207.00	31.51

4	पीएमजीएसवाई फेज VI के तहत ग्रामीण सड़क का निर्माण एवं रखरखाव	12/2007	202.61	227.00	24.39
5	पीएमजीएसवाई फेज V के तहत ग्रामीण सड़क का निर्माण एवं रखरखाव	03/2007	149.73	173.00	23.27
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	13845.01	7450.01

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 1058 परियोजनाओं में से, 8 परियोजनाएं समय से पहले चल रही हैं, 261 समय पर तथा 334 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 295 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 30 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 425 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 334 विलंबित परियोजनाओं में से, 54 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 78 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 130 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 72 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31.12.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीने में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	06/2016	90
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	09/2010	09/2016	72
3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	10/2017	22
	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700	10/2009	12/2016	05/2018	17

1	पाकयांग (सिक्किम) हवाई अड्डा में नए हवाई अड्डे का निर्माण	01/2009	01/2011	09/2017	80
2	नई अंतर्राष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	03/2015	34
3	विभिन्न हवाई अड्डों पर 56 एनओएस एयरफील्ड फायर टैंडरर्स की आपूर्ति	10/2012	03/2015	09/2015	6
कोयला					
1	रामगुंडम ओसी-II विस्तार	12/2009	03/2012	03/2023	132
2	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	07/2012	03/2021	104
3	कुल्दा ओसीपी (महानदी कोल्डफील्ड लिमि.)	01/2005	03/2010	03/2017	84
4	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
5	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
स्वास्थ्य और परिवार कल्याण					
1	एम्स-रायबरेली- हाऊसिंग	10/2013	11/2013	03/2016	28
2	एलजीबीआरआईएमएच-तेजपुर, असम	07/2012	12/2014	03/2016	15
3	एलएचएमसी नई दिल्ली-पुनर्विकास	02/2013	11/2013	11/2014	12
4	सफदरजंग अस्पताल पुनर्विकास और अन्य सुपर स्पेशलिटी ब्लॉक	09/2013	12/2015	03/2016	3
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
खान					
1	सीएपीएसी के वर्तमान ओपन कास्ट खान के तहत भूमिगत खान के मलंजखंड खान-विकास का विस्तार	09/2011	09/2017	04/2020	31
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2015	44
पेट्रोलियम					
1	फुलपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	12/2018	71
2	12 ऑफशोर आपूर्ति उपकरणों का निर्माण (ओएसवी)	06/2007	09/2011	10/2016	61
3	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	12/2009	06/2011	03/2016	57
4	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	03/2016	53
5	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	01/2012	05/2016	52
विद्युत					
1	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2016	123

2	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
3	कुंडनकुलम एपीपी पारेषण प्रणाली (पीजीसीआईएल)	05/2005	11/2008	12/2016	97
4	बाढ़ एसटीपीपी (3X660 मेवा) एनटीपीसी	02/2005	01/2011	05/2018	88
5	तीस्ता लो डैम एचईपी, स्टेज-IV (4X40 मेवा) (एनएचपीसी)	09/2005	09/2009	06/2016	81
रेलवे					
1	गोंदिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
2	गुना-इटावा वाया शिवपुरी-ग्वारियर-भिंड एनएल, (एनसीआर)	04/1986	03/1994	03/2015	252
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	11/2002	12/2018	193
4	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
5	तमलुक-दीघा लाइन दोहरीकरण, (एसईआर)	03/1984	06/2005	12/2019	174
सड़क परिवहन एवं राजमार्ग					
1	बिजनी से असम/प.बं. सीमा फेज.II, 30.00 किमी से 0.00 किमी, एनएच-31 सी	12/2003	06/2005	12/2016	138
2	हरंगार्जों से मेंबंग, किमी 164.08-190.587 एनएच-54	12/2003	09/2007	12/2016	111
3	नलबारी से बिजनी (एएस-7)	12/2003	04/2008	01/2017	105
4	आगरा-बाईपास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	09/2007	03/2016	102
5	गुवाहाटी से नलबारी (एएस-4)	12/2003	04/2008	07/2016	99
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	03/2006	01/2016	118
2	कोचीन पोर्ट ट्रस्ट के वल्लारपाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	04/2009	08/2016	88
3	मुंबई में बीओटी आधार पर कंटेनर टर्मिनल का विकास और ऑफशोर कंटेनर बर्थ का निर्माण	01/2007	12/2010	01/2016	61
इस्पात					
1	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	10/2016	43
2	45 एमवीए साफ्ट से जुड़े अन्य संबद्ध सुविधाओं की स्थापना	12/2011	10/2013	06/2016	32
3	7.0 एमटीपीए कुमारस्वामी लौह अयस्क खान परियोजना (एनएमडीसी)	02/2011	05/2013	08/2015	27
4	1.2 एमटीपीए पेलेट संयंत्र परियोजना (एनएमडीसी)	04/2011	04/2013	06/2015	26
5	एसएमएस -1 कन्वर्टर्स रिवैम्पिंग	05/2012	07/2015	06/2017	23
दूरसंचार					

1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	03/2017	20
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	06/2011	06/2016	60
2	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी प.बं. में शैक्षिक सहित आवासीय परिसर	01/2009	06/2012	03/2016	45
3	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	06/2016	37
4	सेंट्रल एकेडमी पुलिस ट्रेनिंग (सीएपीटी) भोपाल का निर्माण	12/2012	12/2014	12/2016	24
5	प्रगति मैदान से जुड़े भूमि में भारत के उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	01/2016	17

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल 2015 में, इस मंत्रालय की निगरानी पर चल रहे 758 परियोजनाओं में से, 231 परियोजनाओं के संबंध में लागतवृद्धि तथा 323 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि दिसंबर 2015 के दौरान, 1058 परियोजनाओं में से 236 परियोजनाओं के संबंध में लागतवृद्धि तथा 334 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है । अप्रैल 2015 की तुलना में, **लागतवृद्धि** दर्शाने वाली **परियोजनाओं** की संख्या **30.47%** से **घटकर 22.31%** हो गई, जबकि **समयवृद्धि** दर्शाने वाली **परियोजनाओं** के संबंध में **42.61%** से **घटकर 31.57%** हो गई है ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.12.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	309.46	408.55	01/2011	09/2017
2	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण, गोवा	05/2010	335.61	318.00	305.01	05/2012	03/2015
3	विभिन्न हवाई अड्डों पर सं. 56 एयरफील्ड फायर टैंडर की आपूर्ति	10/2012	217.60	244.10	30.62	03/2015	09/2015
4	वीएसआई एयरपोर्ट पर नई एकीकृत टर्मिनल भवन का निर्माण	10/2013	314.61	314.61	18.02	एन.ए.	09/2018
कोयला							
1	हुरा-सी ओसी (3 एमटीवाई)	10/2015	359.69	359.69	6.49	03/2022	03/2022
2	मदननगर ओसीपी	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
उर्वरक							
1	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	197.79	43.68	11/2016	11/2016
स्वास्थ्य और परिवार कल्याण							
1	एलजीबीआरआईएमएच-तेजपुर	07/2012	175.57	175.57	106.20	12/2014	03/2016
2	एलएचएमसी-अस्पताल	02/2013	414.11	414.11	210.91	11/2013	11/2014
3	सफदरजंग एसएसबी	09/2013	444.70	444.70	268.07	12/2015	03/2016
4	रायबरेली-हाउसिंग	10/2013	159.50	159.50	118.95	11/2013	03/2016
5	सफदरजंग अस्पताल नई दिल्ली पुनर्विकास तथा अन्य इमरजेंसी ब्लॉक	11/2013	196.70	196.70	157.61	01/2016	01/2016
भारी उद्योग							
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	0.00	09/2011	12/2017

खान							
1	मलंजखंड खान का विस्तार- वर्तमान ओपन कास्ट खान के तहत भूमिगत खान का विकास	09/2011	1856.00	1176.00	2.86	09/2017	04/2020
2	डब्ल्यूपीपीएमएच	12/2015	355.13	355.13	0.00	11/2016	11/2016
3	डब्ल्यूपीपीआरजे	12/2015	344.50	344.50	0.00	11/2016	11/2016
पेट्रोलियम							
1	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	1029.66	10/2011	03/2016
2	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1446.59	01/2012	05/2016
3	एन्नोर में नई विपणन टर्मिनल	11/2006	171.83	171.83	0.00	एन.ए.	एन.ए.
4	12 ऑफशोर सप्लाई वेजेल्स (ओएसवी) का निर्माण	06/2007	736.65	736.65	498.95	09/2011	10/2016
5	सं. बीस फीडर गैस पाइपलाइन	03/2009	228.64	214.19	137.49	12/2016	12/2016
विद्युत							
1	सुबनसिरी लोअर एच.ई.पी (8x250 मेवा.) (एनएचपीसी)	09/2003	6285.33	18063.89	7934.88	09/2010	एन.ए.
2	बीटीपीएस-ए	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	आरटीपीएस चरण-I	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	नॉर्थ ईआर में फाइबर ऑप्टिक संचार प्रणाली की स्थापना	03/2012	198.63	198.63	93.03	09/2014	06/2016
5	यूआरटीडीएसएम फेज-I	01/2014	374.63	374.63	16.00	04/2016	11/2016
रेलवे							
1	हावड़ा-आमता-चंपादंगा एनएल (एसईआर)	04/1974	393.46	1026.00	181.48	03/2007	03/2015
2	नांगलडैम-तलवारा (एनएल), एनआर	03/1981	450.00	2100.00	391.95	07/2012	एन.ए.
3	एकलाखी-बलूरघाट सहित जी से नई बीजी रेलवे लाइन	04/1983	36.80	1336.57	255.55	एन.ए.	03/2019
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	गुना-इटावा वाया शिवपुर- ग्वालियर-भिंड एनएल, (एनसीआर)	04/1986	158.77	608.02	602.10	03/1994	03/2015
सड़क परिवहन एवं राजमार्ग							
1	"मधुगिरी-मुलबागल (किमी 400.330 से किमी 483.151) –	01/1991	219.40	219.40	0.00	01/2018	01/2018

	एलओटी-II"						
2	अनिसाबाद-औरंगाबाद-हरिहरगंज (किमी 0.000 से किमी 62.000)- एलओटी	01/1991	282.41	282.41	0.00	08/2016	08/2016
3	अनिसाबाद-औरंगाबाद-हरिहरगंज (किमी 62.000 से किमी 154.625) -	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	बख्तियारपुर-मोकामा	01/1991	1167.45	1167.45	0.00	एन.ए.	एन.ए.
5	बेंकुआरा-पुरुलिया (किमी 0.000 से किमी 84.000)	01/1991	322.00	322.00	0.00	03/2018	03/2018
पोत परिवहन एवं पत्तन							
1	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	01/2016
2	सेतुसमुंद्रम शिप चैनल प्रोजेक्ट	06/2005	2427.40	2427.40	837.90	10/2008	एन.ए.
3	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	412.00	12/2010	01/2016
4	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	360.35	04/2009	08/2016
5	कामराजर पोर्ट लिमिटेड में कोल बर्थ -3 का निर्माण	10/2013	198.94	198.94	37.70	06/2017	06/2017
इस्पात							
1	गुलबर्गा में चिकित्सा महाविद्यालय और अस्पताल	05/2005	768.88	1060.00	1070.97	02/2014	एन.ए.
2	बागमती के सिंचाई कार्य	10/2005	956.00	956.00	646.65	03/2015	एन.ए.
3	ग्रामीण सड़क का निर्माण एवं रखरखाव	03/2007	149.73	173.00	175.89	12/2015	12/2015
4	ग्रामीण सड़क का निर्माण एवं रखरखाव	12/2007	202.61	227.00	195.46	12/2016	12/2016
5	गिरिडीह, कोडरमा में सड़क और पुल का निर्माण	12/2007	200.00	200.00	126.65	03/2018	03/2018
दूरसंचार							
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	13334.00	13334.00	1360.00	07/2015	03/2017
शहरी विकास							
1	मिलिटरी एम में मैरेड अकोमोडेशन का निर्माण	08/2005	191.24	191.24	0.00	08/2007	एन.ए.

2	आरएस के अंतर्गत बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	2727.89	2727.89	0.00	03/2010	एन.ए.
3	मुसी(जोन में) के दक्षिण में पुराने शहरी क्षेत्र में सीवेरेज प्रणाली के पुनर्वास एवं सुदृढीकरण	08/2007	246.90	246.90	0.00	एन.ए.	एन.ए.
4	संसदीय सौध भवन परिसर में भवन के विस्तार हेतु निर्माण कार्य	05/2009	261.85	261.85	0.00	05/2013	06/2016
5	एनआईटी कालीकट केईआर के लिए मेगा होस्टल II का निर्माण	01/2010	165.23	165.23	0.00	10/2012	एन.ए.

एन.ए. : उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं । बिना संशोधित लागत अनुमानों वाली शुरुआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-12-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	21025.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	0.00	5129.59
नागर विमानन					
1	पाक्यांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	0.00	408.55

	पेट्रोरसायन				
1	असम गैस क्रेकर परियोजना	04/2006	5460.61	8920.00	9103.96
	पेट्रोलियम				
1	कोरबा में विपणन टीओपी	01/2011	141.86	0.00	160.78
	विद्युत				
1	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	5367.65
2	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7934.88
3	तीस्ता लो डैम एचईपी, चरण-IV (4X40 मेवा) (एनएचपीसी)	09/2005	1061.38	0.00	1937.70
4	किशनगंगा एचईपी (3X110 मेवा.)	01/2009	3642.04	0.00	4351.15
5	उत्तरी क्षेत्र प्रणाली सुदृढीकरण स्कीम- XVIII	02/2009	509.66	0.00	523.76
	रेलवे				
1	एकलाखी-बलूरघाट सहित गजोली-ईटाहार (एनएल), एनईएफआर से नई बीजी रेलवे लाइन	04/1983	36.80	36.38	255.55
2	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	155.66	0.00	201.26
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	12/1994	124.43	0.00	712.02
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10658.34
5	कटक-बारंग (एलडी)	04/1995	127.13	0.00	193.37
	सड़क परिवहन एवं राजमार्ग				
1	हरंगाजो से मेबंग (एएस-23), किमी.126.450 से किमी.140.700	12/2003	280.00	0.00	389.31
2	मेबंग से लुमडिंग (एएस-26), किमी.60.500 से किमी.83.400, एनएच-54	12/2003	167.64	0.00	231.27
3	गुवाहाटी से नलबारी (एएस-4)	12/2003	175.96	0.00	304.17
4	गुवाहाटी से नलबारी (एएस-5)	12/2003	198.16	0.00	242.40
5	ब्रह्मपुत्र पुल, एनएच सं-31	12/2003	217.61	309.56	370.66
	इस्पात				
1	गुलबर्गा में चिकित्सा महाविद्यालय तथा अस्पताल का निर्माण	05/2005	768.88	1060.00	1070.97
2	पीएमजीएसवाई फेज V के तहत ग्रामीण सड़क का निर्माण तथा रखरखाव	03/2007	149.73	173.00	175.89

3	बैटरी ब्लॉक 5ए का पुनर्निर्माण तथा बैटरी ब्लॉक 5ए का पुनर्निर्माण	11/2012	313.05	0.00	314.87
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	13427.27

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.12.2015 की स्थिति के अनुसार)

क्र.सं.	क्षेत्र/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	नया अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	एन.ए.	03/2015
2	विभिन्न हवाई अड्डों पर 56 एनओएस एयरफील्ड फायर टैंडर की सप्लाई	10/2012	03/2015	एन.ए.	09/2015
कोयला					
1	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.ए.	एन.ए.
स्वास्थ्य और परिवार कल्याण					
1	एलएचएमसी नई दिल्ली- पुनःविकास	02/2013	11/2013	एन.ए.	11/2014
पेट्रोलियम					
1	एन्नोर में नई विपणन टर्मिनल	11/2006	एन.ए.	एन.ए.	एन.ए.
2	कोच्ची-कूटनाड बंगलोर मंगलोर पाइपलाइन परियोजना	06/2009	12/2012	एन.ए.	06/2015
3	एक ईटीपी तथा तीन ईटीपी सह वाटर इंजेक्शन प्लांट (डब्ल्यूआईपी) का	06/2010	01/2014	एन.ए.	एन.ए.

	निर्माण				
4	एन्नोर-त्रिची-मदुरै एलपीजी पाइपलाइन	05/2013	एन.ए.	एन.ए.	एन.ए.
5	पारादीप-हल्दिया-दुर्गापुर एलपीजी पाइपलाइन का संवर्धन तथा पटना से मुजफ्फरपुर तक इसका विस्तार	01/2015	एन.ए.	एन.ए.	एन.ए.
विद्युत					
1	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	09/2010	एन.ए.	एन.ए.
2	एसआर का प्रणाली सुदृढीकरण-XII	02/2010	06/2012	एन.ए.	एन.ए.
3	आंध्र प्रदेश भाग-ए1 के वैमागिरी क्षेत्र में आईएसजीएस परियोजनाओं से जुड़ी साझा प्रणाली	03/2012	06/2014	एन.ए.	एन.ए.
रेलवे					
1	हावड़ा-आमता-चंपादंगा एनएल (एसईआर)	04/1974	03/2007	03/2007	03/2015
2	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.ए.	एन.ए.
3	गुना-इटावा वाया शिवपुरी-ग्वालियर-भिंड एनएल, (एनसीआर)	04/1986	03/1994	एन.ए.	03/2015
4	नामखाना चंद्रनगर काकद्वीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना के बाद एमएम	04/1987	एन.ए.	एन.ए.	एन.ए.
5	विरमगम-भिल्डी (डब्ल्यू आर), जीसी	04/1990	एन.ए.	03/2010	एन.ए.
सड़क परिवहन एवं राजमार्ग					
1	एनएच-66 का पांडिचेरी से टिंडीवनम खंड	01/1991	01/2008	एन.ए.	11/2011
2	पेव्ड शोल्डर्स के विन्यास तथा सुदृढीकरण के साथ 2 लाइन्स-2 लेन के पुनर्वास तथा उन्नयन	01/1991	04/2014	एन.ए.	04/2014
3	बिरपुर-बिहपुर के पेव्ड शोल्डर्स विन्यास के साथ 2 लाइन्स-2 लेन के पुनर्वास तथा उन्नयन	01/1991	एन.ए.	एन.ए.	एन.ए.
4	ईपीसी आधार पर एनएच-37 के नेगांव बाईपास की समाप्ति से रंगागारा के लिए 4 लेनिंग (किमी. 278.60 से किमी. 297.00)	01/1991	एन.ए.	एन.ए.	एन.ए.
5	गोहपुर से होलॉगी सेक्शन तक एनएच 52 के 264.10 किमी से एनएच 52ए के 20.37 किमी तक 4 लेनिंग	01/1991	एन.ए.	एन.ए.	एन.ए.
पोत परिवहन एवं पत्तन					
1	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	एन.ए.	एन.ए.

इस्पात					
1	गुलबर्गा में चिकित्सा महाविद्यालय और अस्पताल का निर्माण	05/2005	02/2014	एन.ए.	एन.ए.
2	बागमती में सिंचाई कार्य	10/2005	03/2015	एन.ए.	एन.ए.
3	7.0 एमटीपीए कुमारस्वामी आयरन ओर माइन प्रोजेक्ट (एनएमडीसी)	02/2011	05/2013	01/2015	08/2015
4	1.2 एमटीपीए पिल्लेट प्लांट प्रोजेक्ट, डोनिमलाई(एनएमडीसी)	04/2011	04/2013	09/2014	06/2015
5	नेशनल इंस्टिट्यूट ऑफ फार्मास्यूटिकल एजुकेशन एंड रिसर्च के लिए परिसर और भवन का निर्माण	01/2013	एन.ए.	एन.ए.	एन.ए.
शहरी विकास					
1	सैन्य रक्षा मंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय का निर्माण	08/2005	08/2007	एन.ए.	एन.ए.
2	आरएसवीवाई पटना के अंतर्गत बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	03/2010	एन.ए.	एन.ए.
3	मूसी के दक्षिण में पुराने शहर क्षेत्र में सेवरेज सिस्टम की पुनर्स्थापना और इसका सुदृढीकरण (2 जोन में)	08/2007	एन.ए.	एन.ए.	एन.ए.
4	आईआईटी हौजखास नई दिल्ली में लेक्चर थिएटर और लैब कम्प्लेक्स	01/2010	07/2012	एन.ए.	एन.ए.
5	एनआईटी कालीकट केरल के लिए मेगा हॉस्टल II का निर्माण	01/2010	10/2012	एन.ए.	एन.ए.

एन.ए.: उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार कार्य शुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

- कोयला क्षेत्र में, 87 परियोजनाओं में से 44 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 12-84 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'कुल्दा ओसीपी, एमसीएल', आरएफआर ऑफ मनुगुरु ओ सी परियोजना, एससीसीएल', मगध ओसी 20 एमटीवाई, सीसीएल' और 'रामागुंडम ओसी-II एक्सटेंशन, एसीसीसीएल' ने क्रमशः कोयला निकालने संबंधी समस्या, वन भूमि के अन्यत्र प्रयोग एवं अधिग्रहण, कानून एवं व्यवस्था

की समस्या और भूमि अधिग्रहण में विलंब की वजह से 12 माह, 24 माह, 60 माह और 84 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

- ii) **रेलवे क्षेत्र** में, 297 परियोजनाओं में से 33 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 18-57 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 4 में से 2 मेगा परियोजनाएं हैं । परियोजना 'मल्टी मॉडल ट्रांसपोर्ट सिस्टम (एमएमटीएस), चरण-II, हैदराबाद, एमआरटीपी', 'जोका से बिर्नॉय बादल दिनेश बाग, तक मेट्रो रेल के निर्माण के लिए नया कार्य, आरवीएनएल' और 'एनएससीबी एयरपोर्ट से राजारहाट (एमटीपी), हेते हुए न्यू गरिया तक मेट्रो रेल के निर्माण के लिए नया कार्य, आरवीएनएल' ने क्रमशः भूमि अधिग्रहण में विलंब, भूमि के हस्तांतरण में विलंब और भूमि अधिग्रहण में विलंब के कारण क्रमशः 21 माह, 33 माह और 57 माह के अतिरिक्त विलंब की सूचना दी है । परियोजना 'भोपाल बीमा 3डी लाइन दोहरीकरण, आरवीएनएल' ने 18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।
- iii) **पेट्रोलियम क्षेत्र** में, 59 परियोजनाओं में से 33 परियोजनाएं विलंबित हैं । माह के दौरान 06 परियोजनाओं के संबंध में 1-4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 6 परियोजना में से 2 मेगा परियोजनाएं हैं । परियोजना 'माउंडेड बुलेट परियोजना, सीपीसीएल और डब्ल्यूओ-16 कलस्टर फील्ड्स का विकास, ओएनजीसी ने क्रमशः बुलेट और वेल्डिंग के निर्माण में विलंब और ठेकेदारों द्वारा धीमी प्रगति के कारण प्रत्येक ने 1 माह के अतिरिक्त विलंब की सूचना दी है । परियोजनाएं 'स्ट्रेटजिक क्रूड ऑयल भंडारण परियोजना, पादुर, आीएसपीआरएल' और गुजरात रिफाइनरी, आईओसीएल में ईटीपी के लिए रिवर्स ऑसमोसिस प्लांट ने क्रमशः अप्रत्याशित भारी वर्षा और ठेकेदारों द्वारा धीमी प्रगति के कारण प्रत्येक ने 2 माह के विलंब की सूचना दी है । परियोजनाएं 'पारादीप-हल्दिया-बरौनी पाइपलाइन, आईओसीएल का संबर्धन' और 12 ऑफशोर सप्लाय वेसल्स (ओएसवी), ओएनजीसी' ने क्रमशः भूमि अधिग्रहण और ठेका प्रदान करने में विलंब के कारण 3 माह और 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- iv) **विद्युत क्षेत्र** में, 105 परियोजनाओं में से 58 परियोजनाएं विलंबित हैं । माह के दौरान, 13 परियोजनाओं के संबंध में 1-6 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 13 परियोजनाओं में से 5 मेगा परियोजनाएं हैं । परियोजना 'झारखंड और पश्चिम बंगाल भाग- क1, पीजीसीआईएल में चरण-I उत्पादन परियोजनाओं के लिए पारेषण प्रणाली; कृष्णापट्टनम यूएमपीपी-भाग ख, पीजीसीआईएल से संबद्ध पारेषण प्रणाली और उत्तरी क्षेत्रीय प्रणाली सुदृढीकरण योजना-XXVIL, पीजीसीआईएल' में भूमि ग्रहण समस्याओं के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'त्रिपुरा गैस आधारित विद्युत परियोजना, नीपको में गैस की अपेक्षित मात्रा में आपूर्ति नहीं होने की वजह से 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XIX,

पीजीसीआईएल और धुकवान लघु जल परियोजना, टीएचडीसीआईएल ने क्रमशः आरओडब्ल्यू समस्या, किसानों के आंदोलन और तीसरे ट्रांसफॉर्मर की स्थापना में विलंब के कारण क्रमशः 2 माह और 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'एस्सार पावर गुजरात लि. की कनेक्टिविटी के लिए पारेषण प्रणाली और मौदा एसटीपीपी चरण-II, एनटीपीसी ने आरओडब्ल्यू समस्या और कार्य की धीमी प्रगति के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना सिक्किम में उत्पादन परियोजना से एनआर/डब्ल्यूआर भाग-क को विद्युत के ट्रांसफर हेतु पारेषण प्रणाली जैसलमेर (राजस्थान) में लखमाना स्थित विंड पॉवर प्रोजेक्ट, 50 मेगावाट, एनएचपीसी, पारे जल विद्युत परियोजना, नीपको, कुदगी टीपीएस, पीजीसीआईएल से पावर के इवैकुएशन के लिए अपेक्षित पारेषण प्रणाली से जुड़े सब-स्टेशन विस्तार कार्य और पल्लाटाना जीबीपीपी और बीपीटीएस के साथ संबद्ध पारेषण प्रणाली ने क्रमशः 1 माह, 1 माह, 2 माह, 3 माह और 6 माह के विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं) ।

- v) **इस्पात क्षेत्र में**, 36 परियोजनाओं में से 12 परियोजनाएं विलंबित हैं । माह के दौरान 10 परियोजनाओं ने 1-8 माह के अतिरिक्त विलंब की सूचना दी है । 10 परियोजनाओं में से 1 मेगा परियोजना है । परियोजना 'कोल्ड रिपेयर ऑफ कोक ओवन बैटरी-9, बीएसपी, भिलाई, छत्तीसगढ़, सेल'; 'इंस्टालेशन ऑफ एडीशनल हीट ट्रीटमेंट फेसलिटीज इन एसपीपी, सेल' और 'अपग्रेडेशन ऑफ ब्लास्ट फर्नेस-1, आरएसपी, सेल' ने क्रमशः निर्माण सामग्री की आपूर्ति में विलंब, उपस्कर और नियंत्रण केबल की आपूर्ति में विलंब तथा सामग्री के आपूर्ति और इरक्सन में विलंब के कारण प्रत्येक में 1 माह के विलंब की सूचना दी है । परियोजना 'अन्य संबद्ध सुविधाओं के साथ 45 एमवीए एसएफटी, सेल' और 'एसएमएस-1 कन्वर्टरस रिवैम्पिंग, आरआईएनएल' ने क्रमशः एचएससीएल की धीमी प्रगति और बीओएफ के स्टील ढांचे के सुदृढीकरण में विलंब के कारण प्रत्येक ने 3 माह के अतिरिक्त विलंब की सूचना दी है परियोजना 'भिलाई इस्पात संयंत्र, सेल का विस्तार' और 'राउरकेला, ओडिशा में सेल में कोक ओवन बैटरी आरएसपी में 3 के पुनर्निर्माण' में क्रमशः एचईसी द्वारा क्रेन की आपूर्ति में विलंब और कोक ओवन गैस की अपर्याप्त आपूर्ति के कारण प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना दी है । परियोजना 'बैटरी ब्लॉक 5ए के पुनर्निर्माण और बैटरी ब्लॉक 5बी, सेल' के पुनर्निर्माण में बैटरी एरिया में पाइपलाइन डाले जाने में डिजाइन में परिवर्तन के कारण 2 माह के अतिरिक्त विलंब की सूचना दी है । परियोजना 'तीसरे कन्वर्टर और चौथे कास्टर, आरआईएनएल' और 'रिवैम्पिंग ऑफ सिनिस्टर मशीन-1 और 2, आरआईएनएल' ने क्रमशः 5 माह और 8 माह के अतिरिक्त विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किया गया है) ।

- vi) **शहरी विकास क्षेत्र में**, 31 परियोजनाओं में से, 14 परियोजनाएं विलंबित हैं। माह के दौरान, 3 परियोजनाओं ने 3-13 माह के अतिरिक्त विलंब की सूचना दी है। परियोजना 'हरिनघाटा कल्याणी, पश्चिम बंगाल में आईआईएसईआर, के लिए शैक्षणिक व आवासीय परिसर, कोलकाता, सीपीडब्ल्यूडी'; आईएसएम, धनबाद में '2,000 लड़कों के छात्रावास (1000 डबल बिस्तर वाले कमरे), सीपीडब्ल्यूडी' और 'बंगलौर मेट्रो रेल परियोजना फेज-II, बीएमआरसीएल' ने क्रमशः 3 माह, 12 माह तथा 13 माह के अतिरिक्त विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं)। 3 परियोजनाओं में से, 1 मेगा परियोजना है।
- vii) **सड़क परिवहन एवं राजमार्ग क्षेत्र में**, 411 परियोजनाओं में से, 125 परियोजनाएं विलंबित हैं। माह के दौरान, 7 परियोजनाओं ने 1-7 माह के अतिरिक्त विलंब की सूचना दी है। परियोजना 'गुवाहाटी से नलबारी (एस-5), एनएचआई और 'पीएस लांबिया-जैतरन-रायपुर की 2-लेनिंग, एनएचआई' ने क्रमशः 1 माह और 5 के अतिरिक्त विलंब की सूचना दी है। परियोजना 'ब्रह्मपुत्र पुल, एनएच सं-31, एनएचआई', अहमदाबाद से वडोदरा सेक्शन, एनएचआई और एनएच 4ए (एनएच-748) की किमी 118-125 तक खांडियापार पुल, एनएचडीपी की 4 लेनिंग सहित 4 लेनिंग में प्रत्येक ने 6 माह के अतिरिक्त विलंब की सूचना दी है। परियोजना 'गुवाहाटी से नालबाड़ी (एस-4), एनएचआई और 'धर्मतुल से सोनारपुर, किमी 205-183 (एस-20), एनएचआई' ने प्रत्येक में 7 माह के अतिरिक्त विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं)। 7 परियोजनाओं में से 1 मेगा परियोजना है।
- viii) **पोत परिवहन और पत्तन क्षेत्र में**, 8 परियोजनाओं में से, 3 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना 'एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल प्रपज व्हीकल (एसपीवी) पार्ट ट्रस्ट ने अतिक्रमण समस्या के कारण 1 माह के अतिरिक्त विलंब की सूचना दी है।
- ix) **स्वास्थ्य एवं परिवार कल्याण क्षेत्र में**, 9 परियोजनाओं में से, 3 परियोजनाएं विलंबित हैं। माह के दौरान, 2 परियोजनाओं 'सफदरजंग रि-डेवलपमेंट एवं अदर्स सुपर स्पेशलिटी ब्लॉक, एचएससीसी' और 'एम्स-रायबरेली हाऊसिंग, एचएससीसी' ने क्रमशः बाधाओं और स्थानीय अवरोधों के कारण क्रमशः 3 माह और 6 माह का अतिरिक्त विलंब हुआ है।
- x) **खान क्षेत्र में**, 3 परियोजनाओं में से, 1 परियोजना जो मेगा परियोजना है, विलंबित है। माह के दौरान, 1 परियोजना 'एक्सपेंशन ऑफ मलजखंड माइन डिवलपमेंट ऑफ अंडरग्राउंड माइन अंडर इग्जिस्टिंग ऑपन कास्ट माइन ऑफ सीएपीएसी, एचसीएल ने सांविधिक स्वीकृतियां प्रदान किए जाने में विलंब के कारण 31 माह के अतिरिक्त विलंब की सूचना दी है।

12. रेल मंत्रालय ने अपनी सभी चालू (297) परियोजनाओं के संबंध में मासिक स्थिति रिपोर्ट प्रदान करने की परंपरा को 01 जनवरी, 2015 से समाप्त कर दिया है। रेल मंत्रालय ने अपनी केवल उन 20

परियोजनाओं के संबंध में नवीनतम सूचना प्रदान की है जिनकी सांख्यिकी और कार्यक्रम कार्यान्वयन के स्तर पर निगरानी के लिए पहचान की गई है। इसलिए, रेलवे क्षेत्र की शेष परियोजनाओं के संबंध में उपलब्ध सूचना/आंकड़ा (जनवरी, 2015 की स्थिति के अनुसार) प्रयोग किया गया है।

13. सड़क परिवहन और राजमार्ग मंत्रालय (एमओआरटीएच) ने जून 2015 से अपनी परियोजनाओं के संबंध में आंकड़ा उपलब्ध करवाना बंद कर दिया था। तथापि, एमओआरटीएच और एनएचएआई ने स्वेच्छा से फरवरी 2015 (रिपोर्टिंग माह दिसंबर 2015) से अपनी सभी चालू परियोजनाओं को अद्यतन करना पुनः शुरू कर दिया है। एमओआरटीएच और एनएचएआई, दोनों ने सड़क क्षेत्र के अंतर्गत 251 नई परियोजनाएं जोड़ी हैं। मंत्रालय, एनएचएआई द्वारा प्रदत्त सूचना के अनुसार पीपीपी/बीओटी परियोजनाओं का अलग से वर्गीकरण कर रहा है।

14. दिनांक 31.12.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

15. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for December 2015 contains information on the status of the 1058 Central Sector Infrastructure Projects costing ₹150 crore and above. During December 2015, 9 projects (4 projects in Petroleum and 1 project each in Shipping and Ports, Telecommunications, Power, Civil Aviation and Coal sector) have reported completion.

2. During the reference month, out of 1058 projects, 334 projects are delayed with respect to original schedule and 51 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 51 projects, 13 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	411	125	7	1
2	RAILWAYS	297	33	4	2
3	POWER	105	58	13	5
4	COAL	87	44	4	0
5	PETROLEUM	59	33	6	2
6	STEEL	36	12	10	1
7	URBAN DEVELOPMENT	31	14	3	1
8	HEALTH AND FAMILY WELFARE	9	3	2	0
9	SHIPPING AND PORTS	8	3	1	0
10	CIVIL AVIATION	4	1	0	0
11	ATOMIC ENERGY	4	4	0	0
12	MINES	3	1	1	1
13	FERTILISERS	1	0	0	0
14	TELECOMMUNICATIONS	1	1	0	0
15	PETROCHEMICALS	1	1	0	0
16	HEAVY INDUSTRIES	1	1	0	0
Total		1058	334	51	13

3. Total original cost of implementation of the 1058 projects was ₹11,68,413.82 crore and their anticipated completion cost is likely to be ₹13,79,878.25 crore, which reflects overall cost overruns of ₹2,11,464.43 crore (18.10% of original cost). The expenditure incurred on these projects till December 2015 is ₹5,89,925.05 crore, which is 42.75% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-12-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
3	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
4	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	16.86
5	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	82.49
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
3	MARKETING TOP AT KORBA	01/2011	141.86	219.00	54.38
4	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	12/2009	309.81	462.79	49.38
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	45.83
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	187.40
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6085.84	143.74
4	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.57	139.32
5	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	133.06
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
2	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
3	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	3500.00	1313.23
4	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
5	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50

2	TWO LANING OF HOJ - POTIN SECTION OF NH-229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH	12/2009	82.73	165.00	99.44
3	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
4	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	66.82
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	5.66
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	37.86
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	207.00	17.96
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	15.54
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	13845.01	116.50

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)

(as on 31-12-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	70.65
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82

5	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	48.00
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	4504.39
PETROLEUM					
1	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
2	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
3	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	05/2013	4124.35	4941.49	817.14
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
5	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	11778.56
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	5484.82
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7818.68	3899.09
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6085.84	3588.94
RAILWAYS					
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
4	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	3500.00	3252.34
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
3	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
5	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	121.51
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	164.16
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	13.83
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	291.12

2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	207.00	31.51
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	23.27
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	13845.01	7450.01

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1058 projects, 8 projects are ahead of schedule, 261 are on schedule and 334 are delayed with respect to their original schedule. However, the number of delayed projects decreases to 295 if delay is calculated on the basis of latest schedule of completion. Further, 30 projects have been sanctioned without original commissioning schedule date and for 425 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 334 delayed projects, 54 projects have overall delay in the range of 1 to 12 months, 78 projects have delay in the range of 13 to 24 months, 130 projects have delay in the range of 25 to 60 months and 72 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 31-12-2015)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	06/2016	90
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	05/2018	17
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	03/2015	34
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	09/2015	6
COAL					
1	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
2	MAGADH OC 20 MTY (CCL)	08/2008	07/2012	03/2021	104
3	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
4	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
5	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
HEALTH AND FAMILY WELFARE					
1	AIIMS-RAEBARELI-HOUSING	10/2013	11/2013	03/2016	28

2	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	03/2016	15
3	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	11/2014	12
4	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	12/2015	03/2016	3
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	09/2011	12/2017	75
MINES					
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	09/2011	09/2017	04/2020	31
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2015	44
PETROLEUM					
1	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	10/2016	61
3	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	03/2016	53
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	05/2016	52
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2016	97
4	BARH STPP(3X660MW) NTPC	02/2005	01/2011	05/2018	88
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	09/2009	06/2016	81
RAILWAYS					
1	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	03/2015	252
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
4	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
5	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
ROAD TRANSPORT AND HIGHWAYS					
1	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2016	138
2	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	09/2007	12/2016	111
3	NALBARI T BIJNI (AS-7)	12/2003	04/2008	01/2017	105
4	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	03/2016	102
5	GUWHATI TO NALBARI (AS-4)	12/2003	04/2008	07/2016	99
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	01/2016	118
2	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	08/2016	88
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	01/2016	61
STEEL					

1	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	10/2016	43
2	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	06/2016	32
3	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	08/2015	27
4	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	04/2011	04/2013	06/2015	26
5	SMS-1 CONVERTERS REVAMPING	05/2012	07/2015	06/2017	23
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2017	20
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	06/2016	60
2	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	03/2016	45
3	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	06/2016	37
4	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	12/2014	12/2016	24
5	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	01/2016	17

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during December 2015, out of 1058 projects, 236 projects reported cost overruns and 334 projects reported time overruns. In comparison to April 2015, number of **projects** reporting **cost overruns** has gone **down** from **30.47%** to **22.31%** whereas **projects** reporting **time overruns** have **decreased** from **42.61%** to **31.57%**.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-12-2015)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIR	01/2009	309.46	309.46	408.55	01/2011	09/2017
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	318.00	305.01	05/2012	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	30.62	03/2015	09/2015
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRP	10/2013	314.61	314.61	18.02	N.A.	09/2018
COAL							
1	HURA - C OC (3 MTY)	10/2015	359.69	359.69	6.49	03/2022	03/2022
2	MADANNAGAR OCP	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
FERTILISERS							
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	197.79	43.68	11/2016	11/2016
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR	07/2012	175.57	175.57	106.20	12/2014	03/2016
2	LHMC - HOSPITAL	02/2013	414.11	414.11	210.91	11/2013	11/2014
3	SAFDARJUNG SSB	09/2013	444.70	444.70	268.07	12/2015	03/2016
4	RAEBARELI-HOUSING	10/2013	159.50	159.50	118.95	11/2013	03/2016
5	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	196.70	157.61	01/2016	01/2016
HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUN	09/2011	1856.00	1176.00	2.86	09/2017	04/2020

	D MINE UNDER EXISTING OPEN CAST MINE						
2	WPPMH	12/2015	355.13	355.13	0.00	11/2016	11/2016
3	WPPRJ	12/2015	344.50	344.50	0.00	11/2016	11/2016
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	1029.66	10/2011	03/2016
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1446.59	01/2012	05/2016
3	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	171.83	0.00	N.A.	N.A.
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	498.95	09/2011	10/2016
5	TWENTY NOS. FEEDER GAS LINES	03/2009	228.64	214.19	137.49	12/2016	12/2016
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	7934.88	09/2010	N.A.
2	BTPS-A	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	RTPS PH-I	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER	03/2012	198.63	198.63	93.03	09/2014	06/2016
5	URTD SM PHASE-I	01/2014	374.63	374.63	16.00	04/2016	11/2016
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	181.48	03/2007	03/2015
2	NANGALDAM-TALWARA(NL),N R	03/1981	450.00	2100.00	391.95	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING G	04/1983	36.80	1336.57	255.55	N.A.	03/2019
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	602.10	03/1994	03/2015
ROAD TRANSPORT AND HIGHWAYS							
1	"MADHUGIRI-MULBAGAL (KM 400.330 TO KM 483.151) - LOT-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018

2	ANISABAD-AURANGABAD-HARIHARGANJ (KM 0.000 TO KM 62.000)- LOT	01/1991	282.41	282.41	0.00	08/2016	08/2016
3	ANISABAD-AURANGABAD-HARIHARGANJ (KM 62.000 TO KM 154.625) -	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	BAKHTIYARPUR - MOKAMA	01/1991	1167.45	1167.45	0.00	N.A.	N.A.
5	BANKUARA-PURULIA (KM 0.000 TO KM 84.000)	01/1991	322.00	322.00	0.00	03/2018	03/2018
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI	10/2002	150.00	600.00	139.80	03/2006	01/2016
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	837.90	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF	01/2007	366.39	669.46	412.00	12/2010	01/2016
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	409.83	360.35	04/2009	08/2016
5	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	198.94	37.70	06/2017	06/2017
STEEL							
1	MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	1070.97	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	646.65	03/2015	N.A.
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER	03/2007	149.73	173.00	175.89	12/2015	12/2015
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER	12/2007	202.61	227.00	195.46	12/2016	12/2016
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERM	12/2007	200.00	200.00	126.65	03/2018	03/2018
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	13334.00	1360.00	07/2015	03/2017
URBAN DEVELOPMENT							
1	CONSTRUCTION OF MARRIED ACCOMODATIO	08/2005	191.24	191.24	0.00	08/2007	N.A.

	N AT MILITARY M						
2	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RS	11/2006	2727.89	2727.89	0.00	03/2010	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE)	08/2007	246.90	246.90	0.00	N.A.	N.A.
4	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEX	05/2009	261.85	261.85	0.00	05/2013	06/2016
5	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KER	01/2010	165.23	165.23	0.00	10/2012	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-12-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	21025.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5129.59
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	01/2009	309.46	0.00	408.55
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	8920.00	9103.96
PETROLEUM					
1	MARKETING TOP AT KORBA	01/2011	141.86	0.00	160.78
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5367.65
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7934.88
3	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1937.70
4	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	4351.15

5	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	02/2009	509.66	0.00	523.76
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	36.38	255.55
2	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	0.00	201.26
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	0.00	712.02
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
5	CUTTACK - BARANG (LD)	04/1995	127.13	0.00	193.37
ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	389.31
2	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	0.00	231.27
3	GUWHATI TO NALBARI (AS-4)	12/2003	175.96	0.00	304.17
4	GUWAHATI TO NALBARI (AS-5)	12/2003	198.16	0.00	242.40
5	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	370.66
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	1070.97
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	175.89
3	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	11/2012	313.05	0.00	314.87
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	13427.27

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31-12-2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	N.A.	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015
COAL					
1	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.

2	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	06/2009	12/2012	N.A.	06/2015
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.A.	N.A.	N.A.
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	N.A.	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	SYSTEM STRENGTHENING XII OF SR	02/2010	06/2012	N.A.	N.A.
3	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	03/2015
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	N.A.	03/2015
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.A.	03/2010	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	PONDICHERRY TO TINDIVANAM SECTION OF NH-66	01/1991	01/2008	N.A.	11/2011
2	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	04/2014
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
4	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON	01/1991	N.A.	N.A.	N.A.

	EPC BASIS				
5	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	01/1991	N.A.	N.A.	N.A.
SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	N.A.	N.A.
3	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	01/2015	08/2015
4	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	04/2011	04/2013	09/2014	06/2015
5	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(	01/2013	N.A.	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.A.	N.A.
2	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	03/2010	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWWRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
4	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.A.	N.A.
5	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Coal Sector**, out of 87 projects, 44 projects are delayed. During the month, 4 projects have reported additional delay in the range of 12-84 months. The project 'Kulda OCP, MCL', 'RFR of Manuguru OC Project, SCCL,' 'Magadh OC 20 MTY, CCL' and 'Ramagundum OC –II Extension, SCCL' have reported additional delay of 12 months, 24 months, 60 months and 84 months respectively due to Coal evacuation problem, delay in diversion and acquisition of forest land, law and order problem and delay in land acquisition respectively.
- ii) In the **Railways Sector**, out of 297 projects, 33 projects are delayed. During the month, 4 projects have reported additional delay in the range of 18-57 months. Out of 4 projects, 2 projects are mega projects. The project 'Multi Modal Transport system (MMTS) Phase – II, Hyderabad, MRTTP', 'New Work For Construction of Metro Railway from Joka to Binoy Badal Dinesh Bagh, RVNL' and 'New Work for Construction of Metro Railway from NSCB Airport to New Garia via Rajarhat (MTP), RVNL' have reported additional delay of 21 months, 33 months and 57 months respectively due to delay in land acquisition, delay in handing over the land and delay in land acquisition respectively. The project 'Bhopal Bina 3D Line Doubling, RVNL' has reported additional delay of 18 months (however, no specific reason has been reported by the project implementing agency for the delay in the project).
- iii) In the **Petroleum Sector**, out of 59 projects, 33 projects are delayed. During the month, 6 projects have reported additional delays in the range of 1-4 months. Out of 6 projects, 2 projects are mega projects. The projects 'Mounded Bullet Project at CPCL' and 'Development of WO-16 Cluster Fields, ONGC', have reported additional delay of 1 month each due to delay in erection of bullets and welding and slow progress by contractors respectively. The Projects 'Strategic Crude Oil Storage Project at Padur, ISPRL' and 'Reverse Osmosis Plant for ETP at Gujarat Refinery, IOCL' have reported delay of 2 months each due to unprecedented heavy rain and slow progress by contractors respectively. The projects 'Augmentation of Paradip –Haldia -Barauni Pipeline, IOCL' and 'Construction of 12 Offshore supply Vessels (OSV), ONGC' have reported delay of 3 months and 4 months respectively due to delay in land acquisition and delay in awarding of contract respectively.
- iv) In the **Power Sector**, out of 105 projects, 58 projects are delayed. During the month, 13 projects have reported additional delay in the range of 1-6 months. Out of 13 projects, 5 are mega projects. The projects 'Transmission System for Phase – I Generation Projects in Jharkhand and West Bengal – Part – A1, PGCIL', 'Transmission System Associated with Krishnapatnam UMPP- Part B, PGCIL' and 'Northern Region System Strengthening Scheme – XXVII, PGCIL' are delayed by 1 month each due to land acquisition problems. The project 'Tripura Gas Based Power Project, NEEPCO' is delayed by 1 month due to non-supply of requisite quantum of gas. The projects

‘Northern Region System Strengthening Scheme – XIX, PGCIL’ and ‘Dhukwan Small Hydro Project, THDCIL’ have reported delay of 2 months and 5 months respectively due to ROW problem, farmers’ agitation and delay in installation of 3rd transformer respectively. The projects ‘Transmission System for Connectivity of ESSAR Power Gujarat Limited, PGCIL’ and ‘Mouda STPP Stage –II, NTPC’ have reported additional delay of 3 months each due to delay in Row problem, and slow progress of work respectively. The projects ‘Transmission System for Transfer of Power from Gen. Project in Sikkim to NR/WR Part – A’, ‘Wind Power Project at Lakhmana in Jaisalmir (Rajasthan) 50 MW, NHPC’, ‘Pare Hydro Electric Project, NEEPCO,’ ‘Sub- Station Ext. Works Associated with Trans. System Required for Evacuation of Power from Kudgi TPS, PGCIL’ and ‘Transmission System Associated with Pallatana GBPP and BPTS, PGCIL’ have reported delay of 1 month, 1 month, 2 months, 3 months and 6 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

- v) In the **Steel Sector**, out of 36 projects, 12 projects are delayed. During the month, 10 projects have reported additional delay in the range of 1-8 months. Out of 10 projects, 1 project is mega project. The projects ‘Cold Repair of Coke Oven Battery – 9 at BSP, Bhilai, Chhatisgarh, SAIL’, ‘Installation of Additional Heat Treatment Facilities in SPP at RSP, SAIL’ and ‘Upgradation of Blast Furnace -1 at RSP, SAIL’ have reported additional delay of 1 month each due to delay in supply of structural material, delay in supply of instrumentation and control cable and delay in supply and erection of material respectively. The projects ‘Installation of 45 MVA SAFT With other Associated Facilities, SAIL’ and ‘SMS-1 Converters Revamping, RINL’ have reported additional delay of 3 months each due to poor progress by HSCL and delay due to strengthening of steel structure of BOF respectively. The projects ‘Expansion of Bhilai Steel Plant, SAIL’ and ‘Rebuilding of Coke Oven Battery – 3 at RSP, Rourkela, Odisha, SAIL’ have reported additional delay of 4 months each due to delay in supply of crane by HEC and inadequate supply of Coke oven gas respectively. The project ‘Rebuilding of Battery Block 5A and Reconstruction of Battery Block 5B, SAIL’ has reported additional delay of 2 month due to design changes in laying of pipelines of battery area. The projects ‘3RD Convertor and 4th Caster, RINL’ and ‘Revamping of Sinister Machines-1 and 2, RINL’ have reported additional delay of 5 months and 8 months respectively (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- vi) In the **Urban Development Sector**, out of 31 projects, 14 projects are delayed. During the month, 3 projects have reported additional delay in the range of 3-13 months. The projects ‘Academic Cum Residential Campus at Haringhata Kalyani WB for IISER, Kolkata, CPWD’, ‘2000 Boys Hostel (1000 Double Bedded Room) at ISM, Dhanbad,

CPWD' and 'Bangalore Metro Rail Project Phase – II, BMRCL' have reported additional delay of 3 months, 12 months and 13 months respectively (however, no specific reason has been reported by the project implementing agency for the delay in these projects). Out of 3 projects, 1 project is mega project.

- vii) In the **Road Transport & Highways Sector**, out of 411 projects, 125 projects are delayed. During the month, 7 projects have reported additional delay in the range of 1-7 months. The projects 'Guwahati to Nalbari (AS -5), NHAI' and '2 - Laning with PS Lambia- Jaitran- Raipur, NHAI' have reported delay of 1 month and 5 months respectively. The projects 'Brahmaputra Bridge, NH No – 31, NHAI', 'Ahmedabad to Vadodara Section, NHAI' and 'Four Laning of NH 4A (NH -748) from KM 118 to 125 Incl. Four Lane Khndeapar Bridge, NHDP' have reported additional delay of 6 months each. The projects 'Guwahati to Nalbari (AS – 4), NHAI' and 'Dharamtul to Sonarpur, KM 205 -183 (AS -20), NHAI' have reported additional delay of 7 months each. However, no specific reason has been reported by the project implementing agency for the delay in all above said projects of Road Transport & Highways sector. Out of 7 projects, 1 project is mega project.
- viii) In the **Shipping and Ports sector**, out of 8 projects, 3 projects are delayed. During the month 1 project 'Ennore Manali Express Way, F/O Special Purpose Vehicle (SPV) Port Trust' has reported additional delay of 1 month due to encroachment problem.
- ix) In the **Health and Family Welfare Sector**, out of 9 projects, 3 projects are delayed. During the month 2 projects 'Safdarjung Hospital Re-development and Others Super Speciality Block, HSCC' and 'AIIMS- Raibarelli Housing, HSCC' have reported additional delay of 3 months and 6 months respectively due to fund constraints and local disturbances respectively.
- x) In the **Mines sector**, out of 3 projects, 1 project which is a mega project, is delayed. During the month 1 project 'Expansion of Malanjkhand Mine Development of Underground Mine Under Existing Open Cast Mine of CAPAC, HCL' has reported additional delay of 31 month due to delay in grant of statutory clearances.

12. Ministry of Railways have **discontinued** the practice of furnishing monthly status reports on all its on-going (297) projects to this Ministry w.e.f 1st January 2015. The Ministry of Railways have provided latest information of their 20 projects only which have been identified to be monitored at MoSPI level. Therefore, the available information/data (**as on January 2015**) has been used in respect of remaining projects of Railways sector.

14. Ministry of Road Transport & Highways (MoRTH) & National Highways Authority of India (NHAI) had stopped providing data on their project w.e.f. June 2015. However, MoRTH & NHAI have voluntarily resumed updating of all their on-going projects from the month of February 2016 (Reporting month December 2015). Both MoRTH and NHAI have added 251

new projects under Road sector. This Ministry is separately classifying PPP/BOT projects as per information given by NHAI.


15. The status as on 31.12.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

16. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	411	7
2	RAILWAYS	297	4
3	POWER	105	13
4	COAL	87	4
5	PETROLEUM	59	6
6	STEEL	36	10
7	URBAN DEVELOPMENT	31	3
8	HEALTH AND FAMILY WELFARE	9	2
9	SHIPPING AND PORTS	8	1
10	ATOMIC ENERGY	4	0
11	CIVIL AVIATION	4	0
12	MINES	3	1
13	FERTILISERS	1	0
14	PETROCHEMICALS	1	0
15	HEAVY INDUSTRY	1	0
16	TELECOMMUNICATIONS	1	0
	Total	1058	51

Sectoral break up of on-going infrastructure projects.

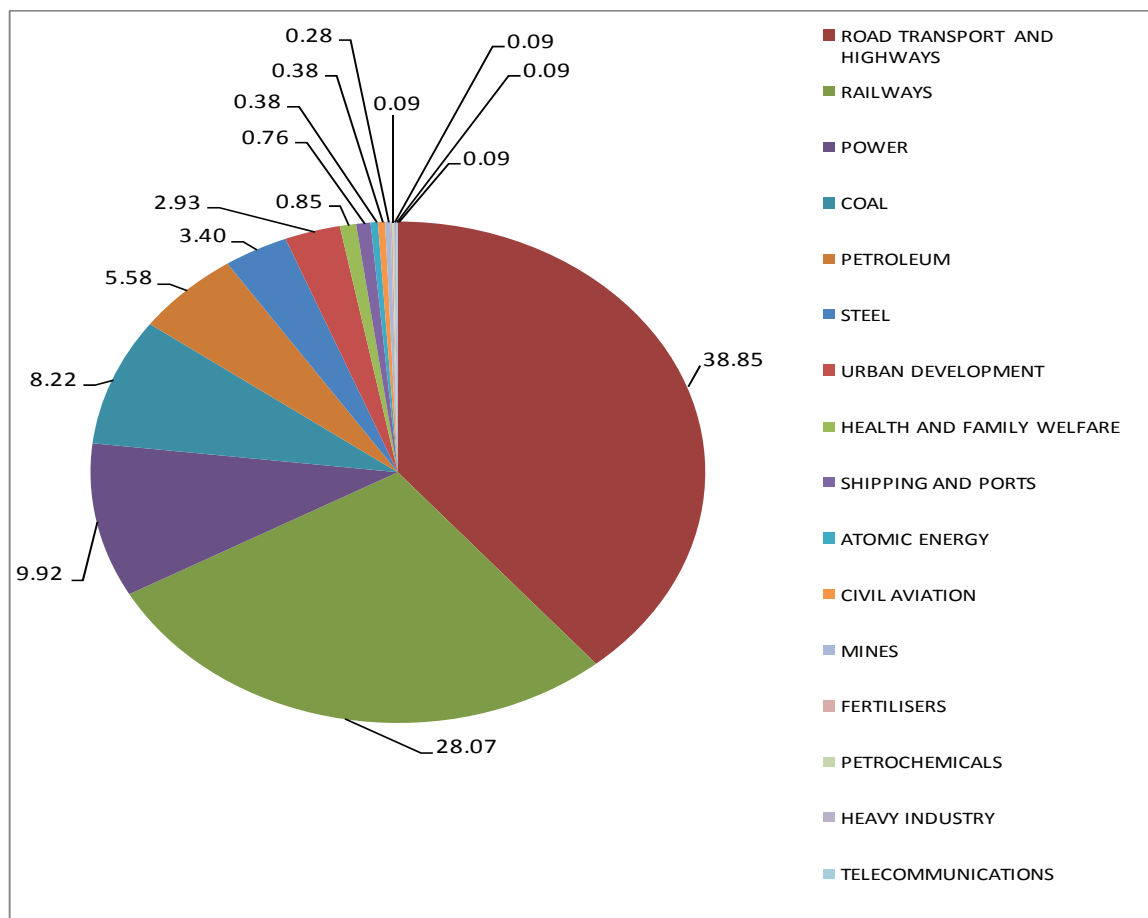

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May,2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
	June,2015			
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30
	July,2015			
	<u>STEEL</u>			
15	AUGMENTATION OF IRON ORE STORAGE IN RMHP (RASTRIYA ISPAT NIGAM LIMITED) - [N12000053]	480.00	09/2009	388.52
	<u>PETROLEUM</u>			
16	SURAT PARADIP PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000163]	10,281.00	04/2015	1.49
	<u>POWER</u>			
17	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000130]	1,263.26	11/2014	1,131.58
	August,2015			
	<u>CIVIL AVIATION</u>			
18	GAGAN PROJECT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000065]	626.00	06/2013	483.53
	<u>COAL</u>			
19	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) (NEYVELI LIGNITE CORPORATION) - [060100087]	2,030.78	06/2009	3,215.91
20	TUTICORIN THERMAL POWER PROJECT- 2X500 MW (NEYVELI LIGNITE CORPORATION) - [N06000047]	4,904.54	03/2012	6,426.43
	<u>PETROLEUM</u>			
21	DEVELOPMENT OF G1 AND GS-15 (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100231]	429.82	04/2006	3,439.38
22	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000098]	288.04	08/2012	229.16
23	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000123]	331.20	08/2013	190.04
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000156]	672.00	10/2011	1,082.12

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
25	BARH STPP STAGE -II (NATIONAL THERMAL POWER CORPORATION) - [N18000047]	7,341.04	10/2013	8,962.00
26	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000076]	4,672.99	11/2012	3,769.57
27	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000096]	2,569.25	03/2014	2,876.57
28	VINDHYACHAL STPP STAGE-V (NATIONAL THERMAL POWER CORPORATION) - [N18000134]	3,180.40	08/2015	2,042.00
	September,2015			
	<u>STEEL</u>			
29	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000018]	607.17	12/2011	394.89
30	EXPANSION OF BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000055]	6,325.00	12/2011	5,256.65
	<u>PETROLEUM</u>			
31	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000132]	5,608.40	05/2015	4,457.47
	<u>POWER</u>			
32	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000124]	213.78	03/2014	204.54
33	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000154]	1,315.90	10/2016	632.97
34	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000156]	296.87	12/2014	318.66
	October,2015			
	<u>CIVIL AVIATION</u>			
35	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000070]	452.00	03/2015	449.41
	<u>STEEL</u>			
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) (RASTRIYA ISPAT NIGAM LIMITED) - [120100067]	8,692.00	10/2009	11,483.12
37	CAPTIVE POWER PLANT - 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000087]	677.00	09/2013	537.19

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>PETROLEUM</u>			
38	102 MW WIND POWER PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000119]	1,106.00	06/2012	437.69
	<u>POWER</u>			
39	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [180100246]	588.25	12/2007	1,020.81
40	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000093]	2,743.19	12/2013	2,827.00
	<u>URBAN DEVELOPMENT</u>			
41	FARIDABAD EXTENSION (DELHI METRO RAIL CORPORATION LTD) - [N28000057]	2,494.00	09/2014	1,311.53
	November,2015			
	<u>POWER</u>			
42	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N16000144]	1,508.74	03/2015	1,211.48
	December,2015			
	<u>CIVIL AVIATION</u>			
43	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000072]	344.28	03/2014	80.60
	<u>COAL</u>			
44	CHURCHA ROUG(1.35MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000046]	462.35	03/2014	497.01
	<u>PETROLEUM</u>			
45	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000142]	1,419.00	12/2014	1,291.63
46	REWARI KANPUR PIPELINE PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000145]	1,210.64	11/2015	1,249.03
47	MARKETING TERMINAL AT PARADEEP (INDIAN OIL CORPORATION LIMITED) - [N16000168]	199.75	07/2013	211.72
48	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000182]	429.06	10/2014	439.02
	<u>POWER</u>			
49	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000160]	243.53	08/2016	185.63

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>SHIPPING AND PORTS</u>			
50	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN(SHIPPING CRP. OF INDIA) - [N25000064]	994.82	11/2013	427.54
	<u>TELECOMMUNICATIONS</u>			
51	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS (BHARAT SANCHAR NIGAM LIMITED) - [N26000096]	384.00	10/2010	74.74

Month wise List of Deleted Projects Costing Rs.150crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2015			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000103]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000120]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000121]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000122]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000181]	2,913.10	05/2016	13.86
	June,2015			
7	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
8	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N26000065]	1,077.00	03/2009	.00
	August,2015			
	<u>SHIPPING AND PORTS</u>			
9	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21
10	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	October,2015			
	<u>PETROLEUM</u>			
11	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>SHIPPING AND PORTS</u>			
12	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21

Month wise List of Deleted Projects Costing Rs.150crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	December,2015			
	<u>PETROLEUM</u>			
14	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	667.40
15	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
16	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000270]	297.78	02/2015	37.72
17	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000271]	297.78	02/2015	37.72
18	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T(PUBLIC WORKS DEPT OF STATE) - [N24000285]	297.78	02/2015	37.72
19	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG(PUBLIC WORKS DEPT OF STATE) - [N24000400]	282.41	08/2016	.00
	<u>SHIPPING AND PORTS</u>			
20	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL (MUMBAI PORT TRUST) - [N25000016]	1,228.00	12/2010	1,038.00
	<u>TELECOMMUNICATIONS</u>			
21	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C(INDIAN TELEPHONE INDUSTRY) - [N26000102]	2,111.17	09/2014	1,360.00


Summary of projects in the Flash Report for the month of December, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	787
Number of Projects completed/dropped/frozen in Current Month	17
Number of Projects elevated to the status of Major project during the current month	18
Number of Projects Added in Current Month	270
Number of Projects in Current Month	1058


Brief Analysis

Project Status with respect to Original Schedule: Out of 1058 projects, 8 projects are ahead of schedule, 261 projects are on schedule 334 projects are delayed. 425 projects do not have fixed dates of commissioning. 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

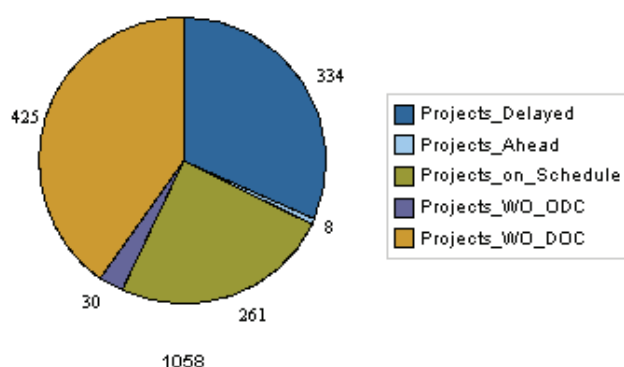

Investment Scenario

Total original cost of implementation of 1058 projects when sanctioned, was of the order of Rs. 1168413.82 crore but this was subsequently revised to Rs. 1379878.25 crore implying a cost overrun of 18.1%. The expenditure incurred on these projects till December, 2015 is Rs. 589925.05 crore, which is 42.8% of the revised cost of the projects.

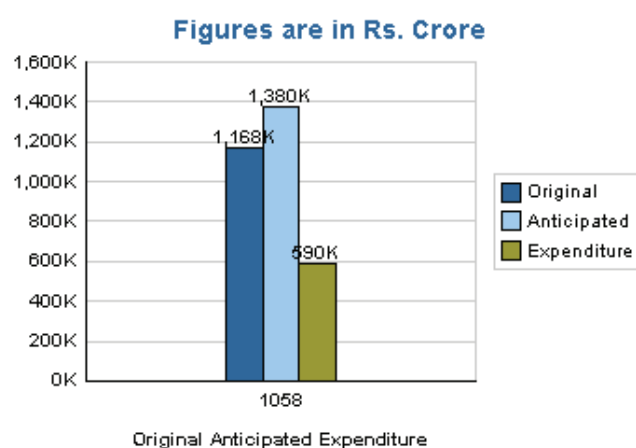

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	787
No of Projects Completed/Dropped/Frozen in Current Month	17
No of Projects added in Current Month	270
No of Projects elevated to the status of Major Projects during current month	18
No of Projects in Current Month	1058

Project status

Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	334	8	261	30	425	1058	31.57
Latest Approved (Date)	295	10	298	30	425	1058	27.88

Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	926	9,38,542.40	10,20,557.77	3,87,161.21	37.90	82,015.37	8.70
Project with Revision in Cost	132	3,00,102.94	3,59,320.48	2,02,763.84	56.40	59,217.54	19.70
Total	1,058	12,38,645.34	13,79,878.25	5,89,925.05	42.75	141232.91	11.40
Original Cost of All Projects							
Original Cost	1058	11,68,413.82	13,79,878.25	5,89,925.05	42.75	2,11,464.43	18.10

Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	334	604,276.84	730,240.13	449,662.43	61.60	125,963.29	20.80
Latest Approved (RCE)	295	555,941.03	620,804.68	391,686.95	63.10	64,863.65	11.70

Additional Delayed Project Cost						
(All Cost/ Expenditure in Rs. crore)						
Cost overrun						
No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
51	84,941.61	85,888.10	44,435.19	51.70	946.49	1.10
51	84,941.61	85,888.10	44,435.19	51.74	946.49	1.11

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun ^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	87	61,587.45	62,537.14	1.54	5	1,471.75	2,889.44	96.33
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	36	54,570.11	55,086.01	0.95	7	2,218.50	2,734.40	23.25
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	59	128,876.79	138,276.44	7.29	15	63,099.10	74,422.00	17.94
9	POWER	105	294,222.64	341,026.11	15.91	21	60,901.26	107,768.34	76.96
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS *	297	172,717.67	298,204.43	72.65	160	81,779.00	210,420.06	157.30
13	ROAD TRANSPORT AND HIGHWAYS	411	248,089.13	250,598.57	1.01	18	4,995.43	7,530.59	50.75
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	4	1,006.56	1,937.62	92.50
15	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	136,783.82	144,233.70	5.45	1	6,395.00	13,845.01	116.50
Total		1058	1,168,413.82	1,379,878.25	18.10	236	245,925.81	463,722.86	88.56

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun ^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	46	21,019.05	22,854.09	8.73	5	1,263.14	3,108.40	146.09
2	ARUNACHAL PRADESH	14	11,676.43	28,030.85	140.06	6	9,699.58	26,054.00	168.61
3	ASSAM	49	27,764.34	43,467.68	56.56	14	15,918.17	31,722.22	99.28
4	BIHAR	65	60,600.22	74,378.42	22.74	15	13,737.73	28,243.47	105.59
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	0.00
6	GUJARAT	28	29,665.99	30,663.63	3.36	5	2,873.48	3,998.44	39.15
7	HARYANA	20	13,986.73	15,957.35	14.09	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	8,088.55	13,907.75	71.94	2	4,966.47	10,785.67	117.17
9	JAMMU AND KASHMIR	9	25,620.25	44,540.93	73.85	2	6,142.04	25,062.72	308.05
10	KARNATAKA	41	71,364.99	88,854.89	24.51	19	14,794.54	32,290.60	118.26
11	KERALA	16	25,825.82	30,300.97	17.33	8	17,335.36	21,810.51	25.82
12	MADHYA PRADESH	50	44,409.65	46,089.94	3.78	5	2,404.35	5,184.88	115.65
13	MAHARASHTRA	71	113,214.96	121,960.10	7.72	11	17,222.10	27,220.66	58.06
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	6	6,970.03	8,194.91	17.57	1	4,083.02	5,307.90	30.00
16	MIZORAM	6	2,188.16	5,402.06	146.88	2	988.06	4,201.96	325.27
17	NAGALAND	3	6,420.00	8,757.12	36.40	2	5,124.00	7,461.12	45.61
18	ODISHA	49	73,735.51	83,247.71	12.90	13	35,239.75	44,773.29	27.05
19	PUNJAB	23	11,714.51	11,718.51	0.03	1	573.96	605.00	5.41
20	RAJASTHAN	57	39,614.10	40,097.55	1.22	6	2,574.16	3,142.63	22.08
21	SIKKIM	5	2,149.08	4,999.32	132.63	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	56	68,607.63	88,218.97	28.58	20	23,494.59	43,105.93	83.47
23	TRIPURA	9	3,776.07	7,486.36	98.26	7	2,909.18	6,619.47	127.54
24	UTTAR PRADESH	60	52,378.07	55,394.73	5.76	8	2,576.25	5,641.17	118.97
25	WEST BENGAL	46	49,641.04	62,788.63	26.49	13	8,617.64	24,016.70	178.69
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	16	49,963.05	49,963.05	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	41	88,321.18	89,633.53	1.49	6	3,494.57	4,807.22	37.56
29	JHARKHAND	44	41,826.84	44,389.67	6.13	7	3,739.10	6,343.67	69.66
30	UTTARAKHAND	6	9,351.89	11,651.71	24.59	3	4,855.31	7,155.13	47.37
31	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	0.00	0	0.00	0.00	0.00
32	TELANGANA	31	11,908.91	14,943.51	25.48	9	2,836.21	5,870.81	106.99
33	MULTI STATE	174	185,283.98	214,831.94	15.95	41	34,762.45	64,824.36	86.48
Total		1058	1,168,413.82	1,379,878.25	18.10	236	245,925.81	463,722.86	88.56

Extent of time overrun in projects with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	17 - 90
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	87	61,587.45	62,537.14	1.54	44	25,908.61	27,019.10	8 - 132
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	36	54,570.11	55,086.01	0.95	12	37,329.16	37,474.56	5 - 43
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44 - 44
8	PETROLEUM	59	128,876.79	138,276.44	7.29	33	75,080.24	82,459.83	1 - 71
9	POWER	105	294,222.64	341,026.11	15.91	58	161,207.08	196,080.02	2 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	3	779.77	779.77	3 - 28
12	RAILWAYS *	297	172,717.67	298,204.43	72.65	33	37,532.74	92,383.86	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,089.13	250,598.57	1.01	125	90,538.15	92,365.10	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	3	762.06	1,679.29	61 - 118
15	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	1	13,334.00	13,334.00	20 - 20
16	URBAN DEVELOPMENT	31	136,783.82	144,233.70	5.45	14	112,018.96	119,468.84	4 - 60
Total		1058	1,168,413.82	1,379,878.25	18.10	334	604,276.84	730,240.13	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning
 ^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	17 - 90
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	87	61,587.45	62,537.14	1.54	41	18,511.83	19,395.15	8 - 132
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	36	54,570.11	55,086.01	0.95	4	2,599.65	2,745.05	5 - 23
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44 - 44
8	PETROLEUM	59	128,876.79	138,276.44	7.29	20	50,502.45	55,815.58	1 - 71
9	POWER	105	294,222.64	341,026.11	15.91	52	144,559.27	169,600.97	2 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	3	779.77	779.77	3 - 28
12	RAILWAYS *	297	172,717.67	298,204.43	72.65	30	31,057.74	79,859.86	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,089.13	250,598.57	1.01	121	89,661.99	91,488.94	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	3	762.06	1,679.29	61 - 118
15	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	1	13,334.00	13,334.00	20 - 20
16	URBAN DEVELOPMENT	31	136,783.82	144,233.70	5.45	12	111,460.43	118,910.31	8 - 60
Total		1058	1,168,413.82	1,379,878.25	18.10	295	513,015.26	620,804.68	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	44,541.00	51,918.00	16.56	2	20,762.00	28,139.00	35.53
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	87	62,466.79	62,537.14	0.11	1	418.97	489.62	16.86
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	36	54,940.61	55,086.01	0.26	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,965.00	11.72	1	8,920.00	9,965.00	11.72
8	PETROLEUM	59	135,681.23	138,276.44	1.91	4	15,590.77	18,373.55	17.85
9	POWER	105	321,700.03	341,026.11	6.01	7	28,130.34	47,456.42	68.70
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS *	297	193,381.23	298,204.43	54.21	152	85,890.60	194,083.93	125.97
13	ROAD TRANSPORT AND HIGHWAYS	411	248,909.04	250,598.57	0.68	13	3,887.63	5,884.15	51.36
14	SHIPPING AND PORTS	8	4,561.87	5,048.81	10.67	3	781.22	1,268.16	62.33
15	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	141,997.69	144,233.70	1.57	1	11,609.00	13,845.01	19.26
Total		1058	1,238,645.34	1,379,878.25	11.40	187	178,269.13	324,064.64	81.78

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of time & cost overrun in projects with respect to latest schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns ^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	1	13,171.00	22,462.00	90- 90
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	87	61,587.45	62,537.14	1.54	1	259.40	486.57	60- 60
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	36	54,570.11	55,086.01	0.95	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44- 44
8	PETROLEUM	59	128,876.79	138,276.44	7.29	6	37,798.58	44,719.73	12- 38
9	POWER	105	294,222.64	341,026.11	15.91	13	32,204.09	50,018.93	0- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS *	297	172,717.67	298,204.43	72.65	4	5,873.07	10,121.84	48- 174
13	ROAD TRANSPORT AND HIGHWAYS	411	248,089.13	250,598.57	1.01	2	425.61	517.56	76- 105
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	1	245.67	409.83	88- 88
15	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	136,783.82	144,233.70	5.45	1	6,395.00	13,845.01	60- 60
Total		1058	1168413.82	1379878.25	18.10	30	101833.03	152546.47	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time & cost overrun in projects with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns ^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 90
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	87	61,587.45	62,537.14	1.54	4	1,321.16	2,690.85	24- 132
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	36	54,570.11	55,086.01	0.95	1	343.00	488.40	8- 8
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44- 44
8	PETROLEUM	59	128,876.79	138,276.44	7.29	9	40,394.93	48,839.73	12- 53
9	POWER	105	294,222.64	341,026.11	15.91	19	54,128.44	89,064.99	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS *	297	172,717.67	298,204.43	72.65	28	22,680.85	79,140.68	3- 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,089.13	250,598.57	1.01	8	2,586.46	4,438.02	55- 88
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	3	762.06	1,679.29	61- 118
15	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	136,783.82	144,233.70	5.45	1	6,395.00	13,845.01	60- 60
Total		1058	1168413.82	1379878.25	18.10	77	152453.51	282118.27	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

List of projects completed/dropped/Frozen during current month							
(All Cost /Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>CIVIL AVIATION</u>						
1	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	02/2010	344.28	03/2014	344.28	05/2015	80.60
	<u>COAL</u>						
2	CHURCHA ROUG(1.35MTY)	06/2008	462.35	03/2014	497.01	03/2016	497.01
	<u>PETROLEUM</u>						
3	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	12/2012	3,513.07	02/2016	4,619.94	12/2017	667.40
4	MARKETING TERMINAL AT PARADEEP	07/2009	199.75	07/2013	239.73	10/2015	211.72
5	REWARI KANPUR PIPELINE PROJECT	02/2012	1,210.64	11/2015	1,446.34	11/2015	1,249.03
6	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY	03/2012	1,419.00	12/2014	1,419.00	11/2015	1,291.63
7	IMPROVED OIL RECOVERY OF B-173A FIELD	01/2012	352.49	03/2014	352.49	N.A.	.00
8	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	10/2013	429.06	10/2014	429.06	11/2015	439.02
	<u>POWER</u>						
9	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII	02/2014	243.53	08/2016	243.53	12/2015	185.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
10	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	10/2014	297.78	02/2015	297.78	02/2017	37.72
11	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T	10/2014	297.78	02/2015	297.78	02/2015	37.72
12	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	08/2016	282.41	08/2016	.00
13	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	10/2014	297.78	02/2015	297.78	02/2017	37.72
	<u>SHIPPING AND PORTS</u>						
14	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1,228.00	12/2010	1,460.00	09/2017	1,038.00
15	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES	10/2010	994.82	11/2013	402.24	03/2015	427.54

List of projects completed/dropped/Frozen during current month							
(All Cost /Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	CO.LTD.,CHIN						
	<u>TELECOMMUNICATIONS</u>						
16	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	10/2010	384.00	11/2015	74.74
17	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	09/2014	2,111.17	09/2014	13,334.00	03/2017	1,360.00

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	EXPANSION OF MINE-I (LEASE AREA) AND MINE-II A (3.0 TO 7.0 MTPA)	4/2013	1,458.17	6/2015	1,458.17	8/2019
2	MALACHUA OPENCAST PROJECT	10/2015	488.33	3/2023	488.33	3/2023
3	MADANNAGAR OPENCAST PROJECT	10/2015	1,875.32	3/2024	1,875.32	3/2024
4	KAMPTEE DEEP OC MINE	11/2015	277.65	3/2021	277.65	3/2021
5	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	498.42	3/2018	498.42	3/2018
6	HURA - C OC (3 MTY)	10/2015	359.69	3/2022	359.69	3/2022
	<u>HEALTH AND FAMILY WELFARE</u>					
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	5/2017	204.44	5/2017
8	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	5/2017	168.90	5/2017
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	505.58	3/2018	505.58	3/2018
10	AIIMS - OPD(NEW)	8/2014	293.65	5/2017	293.65	5/2017
	<u>MINES</u>					
11	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR	12/2015	355.13	11/2016	355.13	11/2016
12	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT	12/2015	344.50	11/2016	344.50	11/2016
	<u>PETROLEUM</u>					
13	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES	5/2015	2,443.00	12/2017	2,443.00	12/2017
	<u>POWER</u>					
14	PATAN WIND FARM SITE, GUJARAT 50 MW	10/2015	315.00	10/2016	315.00	10/2016
	<u>RAILWAYS</u>					
15	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	4/1997	836.26	/	1,072.51	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
16	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	10/2014	297.78	2/2015	297.78	2/2017
17	FOUR LANEING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	333.21	12/2015	333.21	12/2016
18	CONSTRUCION OF 2 LANE ROAD FROM KM.	12/2010	169.26	12/2012	169.26	12/2012

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-					
19	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI-KAWARDHA SECTION.	12/2015	291.05	12/2015	291.05	12/2015
20	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	195.45	11/2014	195.45	11/2016
21	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I	11/2014	262.54	3/2015	262.54	3/2015
22	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV	10/2014	298.34	3/2015	298.34	3/2015
23	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI-KANKER SECTION.	10/2014	213.47	3/2015	213.47	3/2015
24	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	3/2011	185.82	/	185.82	-
25	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	156.26	/	156.26	-
26	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	289.60	/	289.60	-
27	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	3/2015	309.01	9/2015	309.01	8/2017
28	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	2/2015	224.83	5/2015	224.83	5/2017
29	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	383.40	3/2015	383.40	-
30	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	376.52	4/2014	376.52	4/2014
31	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	278.87	5/2014	278.87	5/2014
32	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	257.09	1/2015	257.09	1/2015
33	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	269.22	1/2015	269.22	1/2015
34	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	10/2015	480.21	/	480.21	-

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
35	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	573.96	/	605.00	-
36	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	157.18	7/2015	162.00	7/2015
37	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	258.97	8/2015	258.97	8/2015
38	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	1,296.00	2/2011	1,296.00	2/2011
39	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	182.28	2/2013	182.00	2/2013
40	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	166.27	8/2013	166.27	8/2013
41	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	151.59	8/2013	151.59	8/2013
42	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	207.03	5/2012	207.03	5/2012
43	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	2/2015	377.83	7/2017	377.83	7/2017
44	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	193.69	10/2010	193.69	10/2010
45	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	165.67	11/2015	165.67	11/2017
46	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	621.43	6/2018	621.43	6/2018
47	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	225.81	/	225.81	-
48	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	282.41	3/2016	282.41	3/2016
49	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	3/2015	629.74	/	629.74	-
50	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	497.89	4/2017	497.89	4/2017
51	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	369.00	3/2018	369.00	3/2018
52	2 LANING FROM LONGDING TO KANUBARI OF	3/2015	394.00	6/2018	394.00	6/2018

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH					
53	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	197.16	10/2018	197.16	10/2018
54	PADI - DAHOD	11/2014	279.14	5/2017	279.14	5/2017
55	JODHPUR - BARMER SECTION OF PACKAGE -I	10/2014	264.72	4/2017	264.72	4/2017
56	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50)	7/2015	455.60	7/2017	455.60	7/2017
57	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	563.92	12/2017	563.92	12/2017
58	JALANDHAR - AMRITSAR	1/2014	523.85	1/2016	523.85	1/2016
59	JAISALMER - BARMER	8/2015	482.27	2/2018	482.27	2/2018
60	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	1,387.11	11/2017	1,387.11	11/2017
61	KOTWA TO DEWAPUR (LMNHP-10)	11/2005	240.00	11/2008	240.00	11/2008
62	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	723.54	2/2018	723.54	2/2018
63	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	2/2015	486.74	/	486.74	-
64	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	305.49	3/2017	305.49	3/2017
65	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	2/2015	616.36	/	616.36	-
66	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	445.89	3/2017	445.89	3/2017
67	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	2/2015	483.38	/	483.38	-
68	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	1/1991	269.26	10/2016	269.26	10/2016
69	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	11/2014	563.92	11/2016	563.92	11/2016
70	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	495.78	1/2016	495.78	1/2016
71	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM	6/2015	996.37	12/2017	996.37	12/2017
72	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	6/2015	532.49	5/2017	532.49	5/2017

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
73	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	889.24	/	889.24	-
74	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	268.08	5/2017	268.08	5/2017
75	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	847.02	/	847.02	-
76	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	497.05	5/2017	497.05	5/2017
77	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	264.16	/	264.16	-
78	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	766.36	/	766.36	-
79	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K	7/2014	319.80	/	319.80	-
80	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	3/2015	312.79	/	312.79	-
81	FOUR LANING OF PATNA TO KOILWAR	8/2015	556.07	/	556.07	-
82	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	1,673.70	10/2011	1,673.70	1/2016
83	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	9/2015	273.06	/	273.06	-
84	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	628.45	3/2018	628.45	3/2018
85	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	2/2015	327.32	5/2017	327.32	5/2017
86	NAGPUR - KONDHALI	9/2005	168.00	6/2006	168.00	12/2008
87	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	2,168.66	6/2019	2,168.66	6/2019
88	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	511.00	10/2013	511.00	9/2015
89	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	794.30	/	794.30	-
90	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	795.76	/	795.76	-
91	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	511.00	10/2013	511.00	3/2013
92	PONDICHERRY TO TINDIVANAM SECTION OF NH-66	1/1991	285.00	1/2008	285.00	11/2011
93	FOUR LANING OF SHIVPURI TO GUNA SECTION	3/2015	830.36	1/2016	830.36	1/2016

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY					
94	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	1,083.00	6/2018	1,083.00	6/2018
95	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	1,655.01	8/2016	1,655.01	8/2016
96	4-LANING OF PUNJAB/HARYANA BORDER-JIND	12/2012	438.75	9/2016	438.75	9/2016
97	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	611.65	6/2016	611.65	6/2018
98	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	845.24	/	845.24	-
99	4 LANING OF GUNA TO BIAORA	6/2015	1,012.90	/	1,012.90	-
100	4 LANING OF OBEDULLAGANJ-BETUL SECTION	2/2012	912.00	8/2016	912.00	8/2016
101	4-LANING OF ROHTAK - HISSAR SECTION	3/2013	959.25	6/2016	959.25	6/2016
102	4 LANING OF GOMTI CHAURAHA - UDAIPUR	3/2012	914.50	10/2015	914.50	2/2016
103	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	923.04	11/2016	923.04	12/2016
104	4-LANING OF SOLAPUR - YEDISHI SECTION OF NH-211	1/2015	972.50	7/2017	972.50	7/2017
105	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1,657.20	/	1,657.20	-
106	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	505.00	/	505.00	-
107	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	785.78	3/2018	785.78	3/2018
108	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	2,128.72	/	2,128.72	-
109	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	574.28	7/2018	574.28	7/2018
110	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	11/2011	670.82	2/2015	670.82	2/2015
111	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	788.51	3/2018	788.51	3/2018
112	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	822.90	4/2018	822.90	4/2018
113	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	602.95	6/2016	602.95	6/2016
114	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	936.40	/	936.40	-
115	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	649.50	/	649.50	-
116	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV)	9/2015	789.31	3/2018	789.31	3/2018
117	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	593.26	/	593.26	-
118	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	1,885.74	/	1,885.74	-

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
119	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	1/1991	289.99	/	289.99	-
120	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	361.15	/	361.15	-
121	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V)	9/2015	664.53	3/2018	664.53	3/2018
122	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	531.13	/	531.13	-
123	4 LANING OF BIAORA - DEWAS	6/2015	583.79	/	583.79	-
124	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI)	9/2015	768.56	3/2018	768.56	3/2018
125	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	414.00	/	414.00	-
126	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	520.01	/	520.01	-
127	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	1/1991	223.30	/	223.30	-
128	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	1/1991	225.02	/	225.02	-
129	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR	6/2014	569.38	6/2016	569.38	6/2016
130	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	530.07	8/2016	530.07	8/2016
131	4 LANING OF BAHARAGORA - SINGHARA	7/2015	1,282.94	/	1,282.94	-
132	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	2,288.18	/	2,288.18	-
133	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	597.00	10/2017	597.00	10/2017
134	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	235.08	5/2018	235.08	5/2018
135	2-LANING OF SHILLONG – NONGSTOIN SECTION OF NH 44 AND NONGSTOIN – TURA STATE ROAD UNDER PHASE 'A' OF	12/2010	1,494.48	2/2011	1,494.48	2/2011
136	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	9/2010	201.00	9/2010
137	TWO LANING OF HOJ - POTIN SECTION OF NH-229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH	12/2009	82.73	9/2010	165.00	9/2010
138	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	10/2013	493.94	3/2017	493.94	3/2017
139	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	342.05	1/2017	342.05	1/2017

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
140	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	2/2015	224.83	4/2015	224.83	5/2016
141	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	195.04	10/2010	195.04	10/2010
142	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	229.41	5/2018	229.41	5/2018
143	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	319.80	10/2016	319.80	10/2016
144	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	381.86	4/2015	381.86	4/2016
145	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	218.31	2/2018	218.31	2/2018
146	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	6/2015	641.02	12/2017	641.02	12/2017
147	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	176.22	2/2018	176.22	2/2018
148	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	333.21	11/2015	333.21	11/2015
149	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	1/1991	208.87	5/2016	208.87	5/2016
150	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	3/2015	789.83	/	789.83	-
151	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	12/2015	578.38	/	578.38	-
152	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	10/2013	283.45	10/2016	283.45	10/2016
153	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	358.22	10/2016	358.22	10/2016
154	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	319.68	/	319.68	-
155	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40	1/1991	154.62	/	154.62	-
156	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	207.88	/	207.88	-
157	TRICHY - KARUR	3/2007	516.00	7/2008	516.00	7/2008
158	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO	12/2011	191.08	8/2015	191.08	3/2018

List of projects added

(All Cost in Rs. crore)

Sl.No	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	471-900 (BERHMAPUR-TAPTA					
159	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	6/2015	899.21	/	899.21	-
160	ROHTAK - BAWAL(APPROVED LENGTH 97 KM)	2/2010	650.00	/	650.00	-
161	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	892.17	/	892.17	-
162	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	159.39	11/2017	159.39	11/2017
163	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR	8/2015	516.13	/	516.13	-
164	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ	8/2015	854.80	/	854.80	-
165	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	275.90	/	275.90	-
166	REHABILITATION AND UPGRADING TO 2 LANES- 2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	478.35	/	478.35	-
167	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	8/2015	399.54	/	399.54	-
168	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	479.20	/	479.20	-
169	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	511.83	8/2017	511.83	8/2017
170	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	819.95	/	819.95	-
171	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	1,665.00	/	1,665.00	-
172	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	773.98	/	773.98	-
173	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	207.88	/	207.88	-
174	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	164.54	8/2015	164.54	3/2016
175	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	726.67	/	726.67	-
176	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	1,170.52	6/2012	1,170.52	8/2016
177	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1,871.34	1/2018	1,871.34	1/2018
178	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	1/1991	1,167.45	/	1,167.45	-
179	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	642.41	/	642.41	-
180	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE	6/2015	1,583.79	/	1,583.79	-

List of projects added

(All Cost in Rs. crore)

Sl.No	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	STATE OF MADHYA PR					
181	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	810.22	/	810.22	-
182	FOUR LANING OF CHADIGARH - KHARAR	10/2015	447.29	12/2017	447.29	12/2017
183	FOUR LANING OF SARAGAON - BILASPUR	12/2015	509.13	/	509.13	-
184	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	322.09	/	322.09	-
185	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I	1/2016	830.36	7/2018	830.36	7/2018
186	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	667.00	6/2018	667.00	6/2018
187	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	667.00	7/2018	667.00	7/2018
188	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD	3/2015	830.36	1/2019	830.36	1/2016
189	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	1,012.90	3/2016	1,012.90	3/2016
190	FOUR LANING OF SIMGA - SARAGAON	12/2015	596.67	/	596.67	-
191	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	1,055.00	11/2015	1,055.00	1/2016
192	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	1,027.53	6/2018	1,027.53	6/2018
193	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	867.66	11/2015	867.66	1/2016
194	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	815.28	6/2018	815.28	6/2018
195	FOUR LANING OF HOSPET - CHITRADURGA	1/1991	1,388.00	/	1,388.00	-
196	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	928.83	/	928.83	-
197	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	2,136.97	12/2018	2,136.97	12/2018
198	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	7/2015	1,393.00	/	1,393.00	-
199	FOUR LANING OF YADGIRI - WARANGAL	12/2015	1,423.96	/	1,423.96	-
200	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	752.28	/	752.28	-
201	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21	12/2015	239.23	12/2017	239.23	12/2017
202	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	479.00	/	479.00	-
203	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	814.04	/	814.04	-
204	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	2/2013	1,232.00	8/2015	1,232.00	3/2016
205	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	1,041.10	/	1,041.10	-
206	FOUR LANING OF PARWANOO -SOLAN	9/2015	934.46	3/2018	934.46	3/2018
207	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	927.54	6/2018	927.54	6/2018

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
208	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	871.15	9/2015	871.15	8/2016
209	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	282.41	8/2016	282.41	8/2016
210	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43	10/2013	317.76	3/2017	317.76	3/2017
211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	282.41	8/2016	282.41	8/2016
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	322.00	3/2018	322.00	3/2018
213	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	470.20	2/2011	470.20	2/2011
214	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	257.80	5/2015	257.00	5/2015
215	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	6/2015	774.57	3/2018	774.57	3/2018
216	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	675.00	/	675.00	-
217	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	3/2013	257.80	2/2016	257.80	2/2016
218	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	704.26	5/2015	704.26	5/2015
219	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	218.63	10/2017	218.63	10/2017
220	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	390.51	2/2015	390.51	2/2015
221	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150	1/2014	397.04	10/2016	397.04	10/2016
222	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	219.40	1/2018	219.40	1/2018
223	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	320.48	8/2015	320.48	9/2016
224	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	301.04	1/2016	301.04	1/2016
225	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	368.73	9/2016	368.73	9/2016
226	VADODARA-SURAT SECTION	3/2014	503.16	8/2016	503.16	8/2016
227	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	351.34	1/2016	351.34	1/2016
228	THIRUMAYAM - MANAMADURAI SECTION	7/2014	401.11	1/2017	401.11	1/2017
229	PHALODI -JAISALMER SECTION OF NH-15 TO	9/2015	567.51	3/2018	567.51	3/2018

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	TWO/FOUR LANE WITH PS					
230	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA-BARWALA - PANCHKULA(PKG - 2)	10/2015	562.34	4/2018	562.34	4/2018
231	FOUR LANING OF VARANASI BYPASS	5/2015	261.09	5/2017	261.09	5/2017
232	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	425.19	9/2016	425.19	9/2016
233	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23	9/2015	341.61	9/2017	341.61	9/2017
234	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	709.00	9/2017	709.00	9/2017
235	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH-	12/2014	451.58	6/2017	451.58	6/2017
236	JODHPUR - BARMER SECTION OF PACKAGE -II	10/2014	206.12	4/2017	206.12	4/2017
237	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N	8/2015	538.08	2/2018	538.08	2/2018
238	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	10/2014	227.74	10/2016	227.74	10/2016
239	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	159.12	11/2015	159.12	11/2017
240	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	179.82	1/2019	179.82	1/2019
241	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	194.11	5/2018	194.11	5/2018
242	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	588.95	11/2018	588.95	11/2018
243	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	168.39	11/2018	168.39	11/2018
244	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	3/2015	829.00	3/2018	829.00	3/2018
245	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	10/2014	463.49	6/2018	463.49	6/2018
246	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	10/2014	437.39	6/2018	437.39	6/2018
247	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	154.14	8/2015	154.14	8/2015
248	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL	11/2010	305.49	3/2011	305.49	3/2011

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	PRADESH UNDER ARUNACHAL PRADESH P					
249	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	156.63	2/2012	276.00	2/2012
250	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	624.41	3/2011	624.41	3/2011
251	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	10/2014	454.89	5/2018	454.89	5/2018
252	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	186.96	/	186.96	-
253	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	2/2014	417.61	6/2014	417.61	6/2016
254	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	333.21	12/2015	333.21	12/2016
255	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	271.45	10/2015	271.45	10/2017
256	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	11/2014	463.65	/	463.65	-
257	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	1/2015	279.68	/	279.68	-
258	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	3/2015	435.90	/	435.90	-
259	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	3/2015	422.34	3/2015	422.34	3/2015
260	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	485.44	12/2015	485.44	12/2015
261	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T	10/2014	297.78	2/2015	297.78	2/2015
262	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA-SIMGA SECTION.	12/2014	394.20	/	394.20	-
263	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	2/2014	170.21	11/2014	170.21	11/2016
264	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR	7/2015	314.43	/	314.43	-

List of projects added						
(All Cost in Rs. crore)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
265	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	2/2015	266.00	/	266.00	-
266	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	10/2014	297.78	2/2015	297.78	2/2017
	<u>SHIPPING AND PORTS</u>					
267	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	6/2017	198.94	6/2017
268	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	244.50	12/2017	258.33	12/2017
269	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED	12/2014	274.85	4/2017	274.85	4/2017
270	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED	9/2015	210.00	1/2018	210.00	1/2018

Milestones (Total & achieved)

Total	3755
Achieved up to month	1768

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	KULDA OCP (MAHANADI COALFIELDS LTD) MCL	302.96	302.96	03/2010	03/2016	03/2017	12
2	RFR OF MANUGURU OC PROJECT SCCL	430.45	486.27	03/2016	03/2016	03/2018	24
3	MAGADH OC 20 MTY (CCL) CCL	706.40	706.40	07/2012	03/2016	03/2021	60
4	RAMAGUNDAM OC-II EXTENSION SCCL	418.97	489.62	03/2012	03/2016	03/2023	84
	<u>MINES</u>						
5	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC HCL	1,856.00	1,176.00	09/2017	09/2017	04/2020	31
	<u>STEEL</u>						
6	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH SAIL	332.65	332.65	08/2014	01/2016	02/2016	1
7	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP SAIL	160.48	160.48	09/2014	12/2015	01/2016	1
8	UPGRADATION OF BLAST FURNACE-1 AT RSP SAIL	708.91	708.91	04/2016	08/2016	09/2016	1
9	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B SAIL	313.05	313.05	06/2015	12/2015	02/2016	2
10	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES SAIL	187.33	187.33	10/2013	03/2016	06/2016	3
11	SMS-1 CONVERTERS REVAMPING RINL	404.16	404.16	07/2015	03/2017	06/2017	3
12	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	06/2016	10/2016	4
13	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA SAIL	237.09	237.09	12/2014	01/2016	05/2016	4
14	3RD CONVERTER AND 4TH CASTER RINL	974.76	974.76	07/2016	07/2016	12/2016	5
15	REVAMPING OF SINTER MACHINES - 1 AND 2 RINL	343.00	488.40	10/2016	10/2016	06/2017	8
	<u>PETROLEUM</u>						
16	DEVELOPMENT OF WO-16 CLUSTER FIELDS ONGC	2,523.00	2,523.00	01/2014	12/2015	01/2016	1

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
17	MOUNDED BULLET PROJECT AT CPCL CPCL	279.00	279.00	12/2014	12/2015	01/2016	1
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR ISPRL	993.00	1,693.00	01/2012	03/2016	05/2016	2
19	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY IOCL	160.00	160.00	02/2016	03/2016	05/2016	2
20	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	586.00	586.00	08/2015	12/2015	03/2016	3
21	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	06/2016	10/2016	4
	<u>POWER</u>						
22	TRIPURA GAS BASED POWER PROJECT NEEPCO	421.01	1,007.57	07/2013	12/2015	01/2016	1
23	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	250.03	250.03	01/2013	01/2016	02/2016	1
24	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 PGCIL	558.26	558.26	11/2013	02/2016	03/2016	1
25	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B PGCIL	1,927.16	1,927.16	10/2014	01/2016	02/2016	1
26	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	05/2015	01/2016	02/2016	1
27	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW NHPC	302.49	302.49	02/2016	12/2015	01/2016	1
28	PARE HYDRO ELECTRIC PROJECT NEEPCO	573.99	1,262.27	08/2013	05/2016	07/2016	2
29	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX PGCIL	410.29	410.29	02/2012	12/2015	02/2016	2
30	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED PGCIL	552.44	552.44	02/2014	12/2015	03/2016	3
31	MOUDA STPP STAGE 2 NTPC	7,921.47	7,921.47	09/2016	09/2016	12/2016	3
32	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS PGCIL	167.40	167.40	12/2015	12/2015	03/2016	3
33	DHUKWAN SMALL HYDRO PROJECT THDCIL	195.42	195.42	02/2014	09/2017	02/2018	5


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
34	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. PGCIL	2,144.00	2,144.00	12/2012	06/2016	12/2016	6
	<u>HEALTH AND FAMILY WELFARE</u>						
35	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK HSCC	444.70	444.70	12/2015	12/2015	03/2016	3
36	AIIMS-RAEBARELI-HOUSING HSCC	159.50	159.50	11/2013	09/2015	03/2016	6
	<u>RAILWAYS</u>						
37	BHOPAL BINA 3D LINE DOUBLING RVNL	687.20	950.00	03/2010	12/2015	06/2017	18
38	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD MRTD	632.68	816.55	03/2016	03/2016	12/2017	21
39	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. RVNL	2,913.51	2,095.20	03/2016	03/2016	12/2018	33
40	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) RVNL	3,951.98	3,161.58	03/2016	03/2016	12/2020	57
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
41	GUWAHATI TO NALBARI (AS-5) NHAI	198.16	198.16	04/2008	12/2015	01/2016	1
42	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR NHAI	158.04	158.04	12/2015	12/2015	05/2016	5
43	BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	309.56	04/2010	02/2016	08/2016	6
44	AHMEDABAD TO VADODARA SECTION NHAI	2,125.24	2,125.24	12/2015	12/2015	06/2016	6
45	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE NHDP	297.00	297.00	N.A.	10/2017	04/2018	6
46	GUWHATI TO NALBARI (AS-4) NHAI	175.96	175.96	04/2008	12/2015	07/2016	7
47	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	12/2015	07/2016	7
	<u>SHIPPING AND PORTS</u>						
48	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) PORT TRUST	150.00	600.00	03/2006	12/2015	01/2016	1
	<u>URBAN DEVELOPMENT</u>						


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
49	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA CPWD	225.81	225.81	06/2012	12/2015	03/2016	3
50	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD CPWD	171.86	171.86	03/2016	05/2016	05/2017	12
51	BANGALORE METRO RAIL PROJECT PHASE-2 BMRCL	26,405.14	26,405.01	02/2019	02/2019	03/2020	13

Graphical Presentation of All Projects w.r.t. Original Schedule

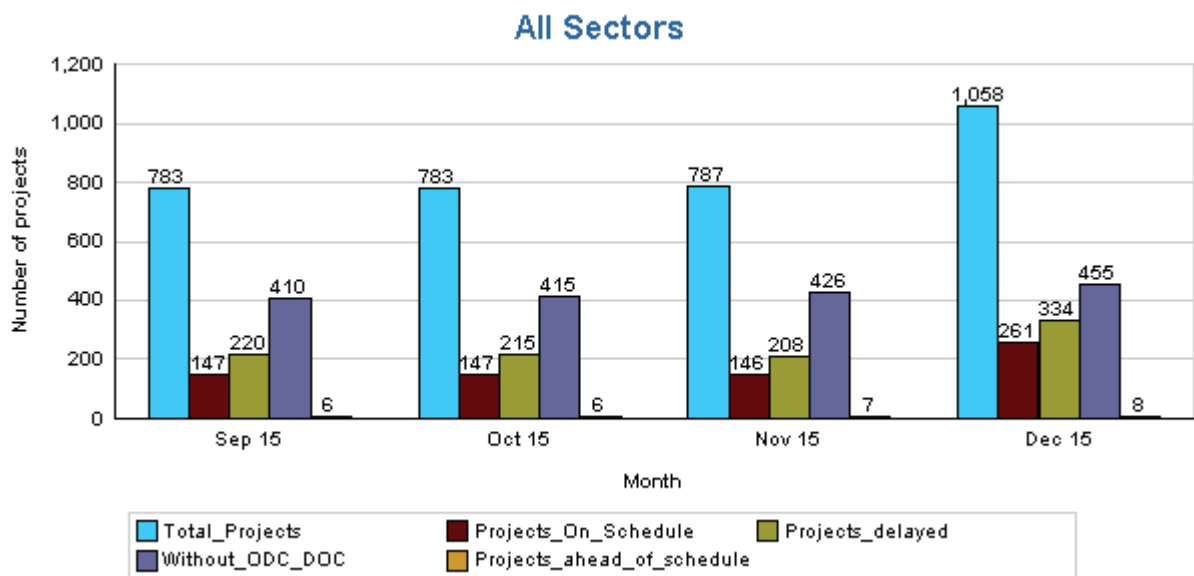


Break-up of 334 Delayed projects in December 2015

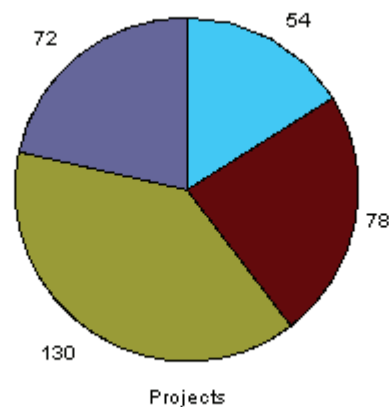


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

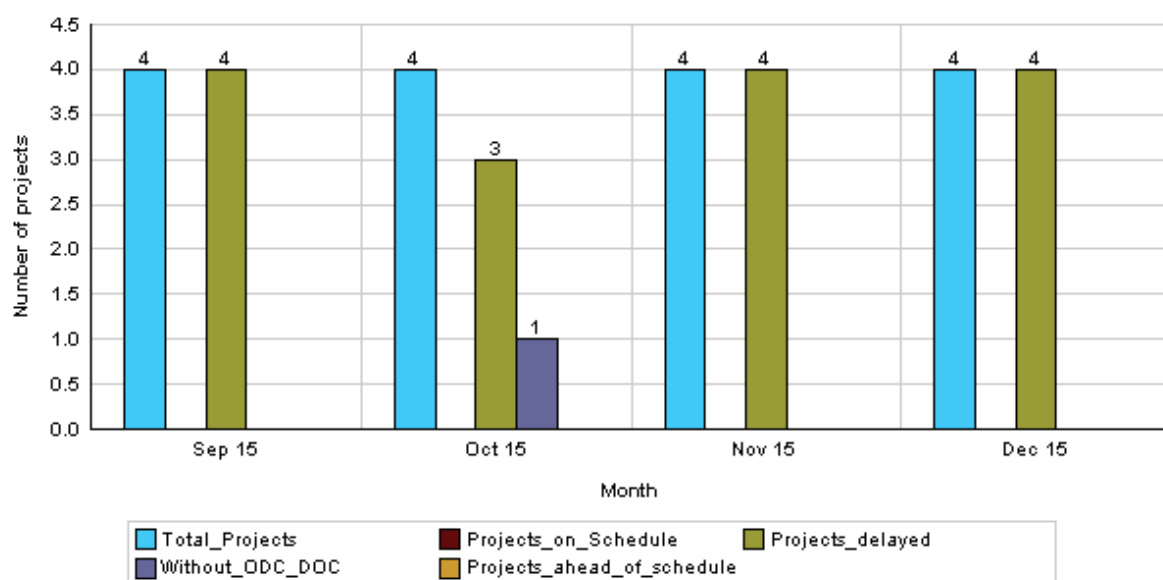


Break-up of 4 Delayed projects in December 2015

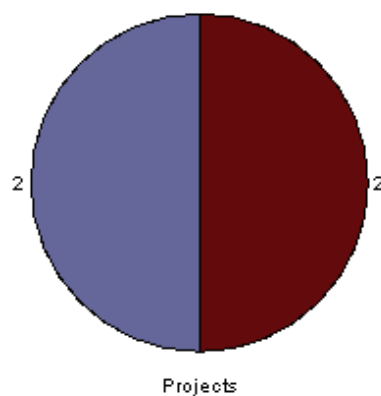


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of CIVIL AVIATION Sector

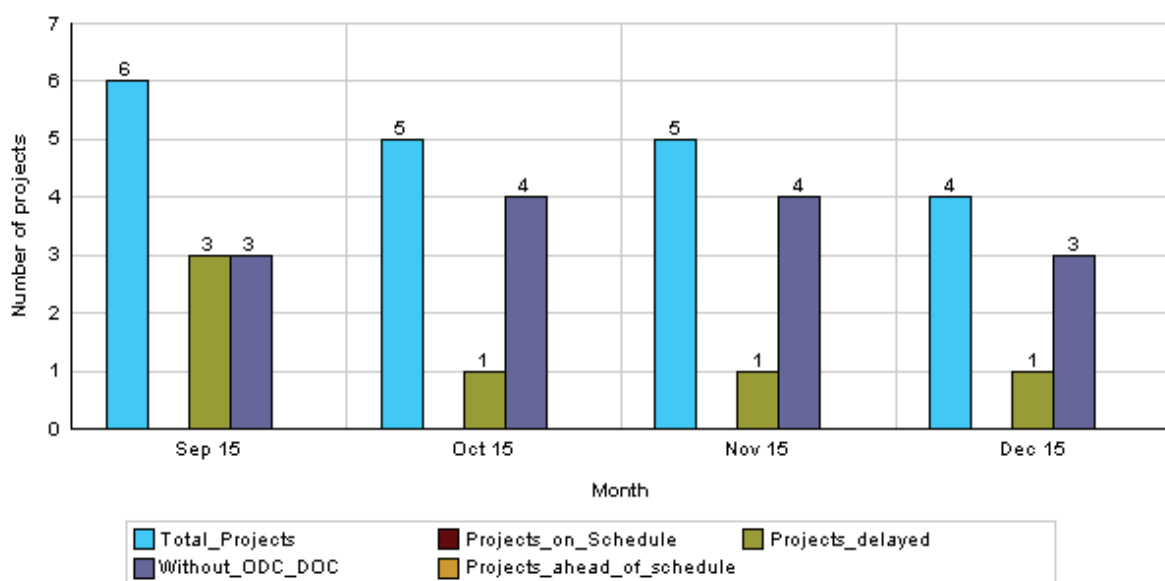


Break-up of 1 Delayed projects in December 2015

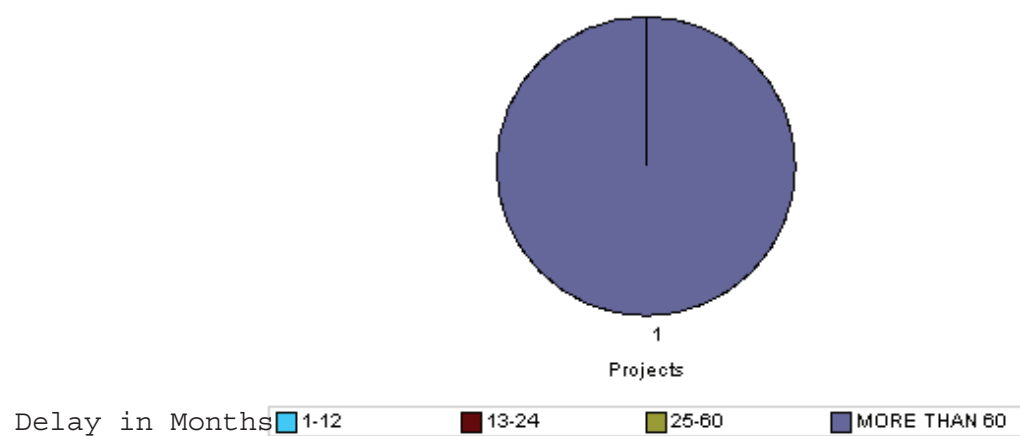


Graphical Presentation of COAL Sector

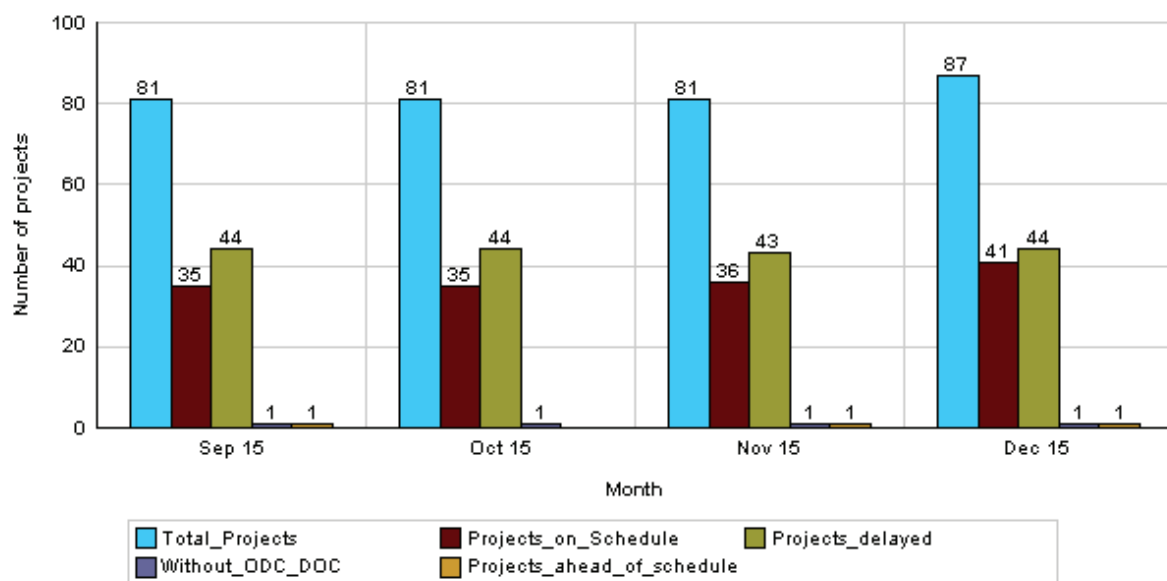


Break-up of 44 Delayed projects in December 2015

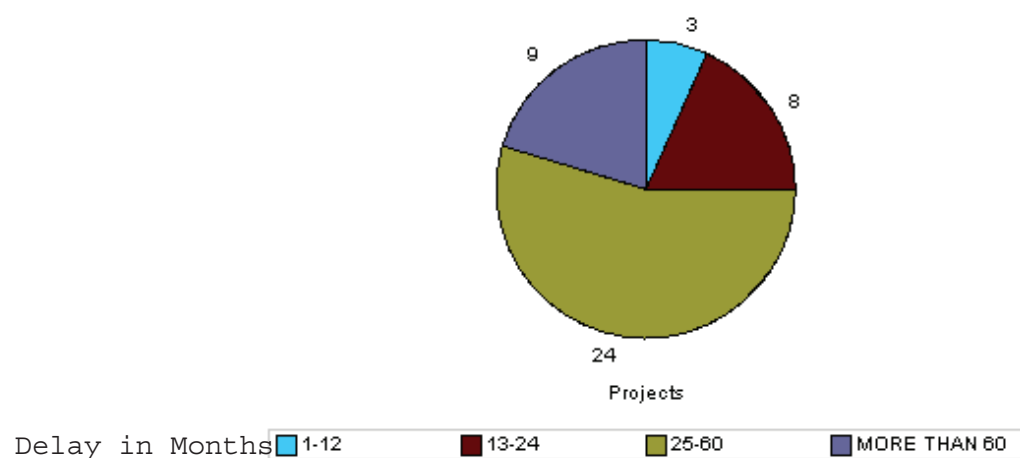

Graphical Presentation of STEEL Sector

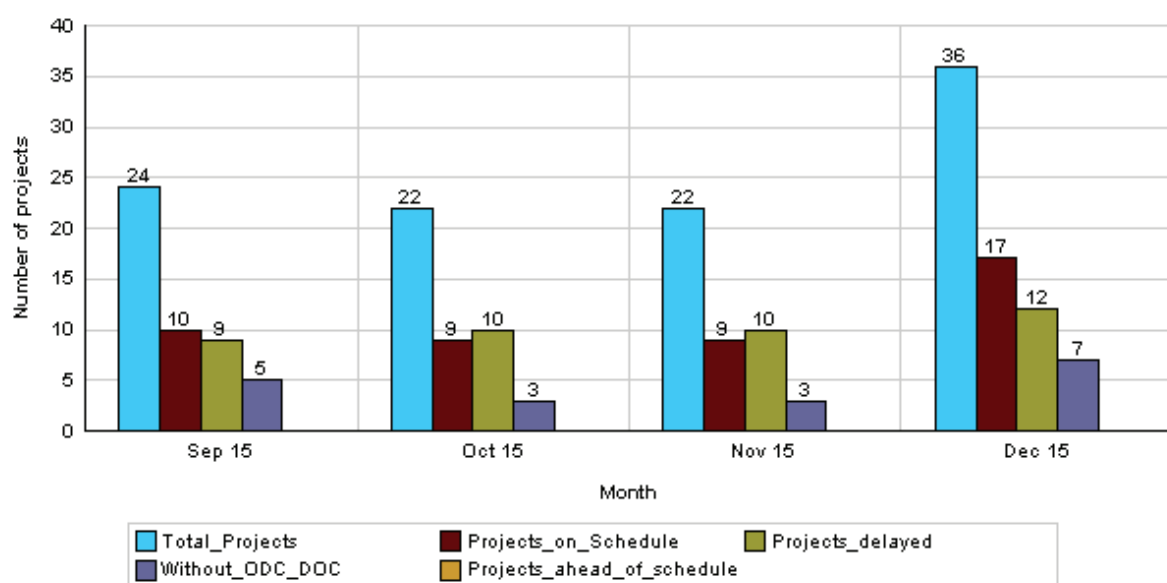


Break-up of 12 Delayed projects in December 2015

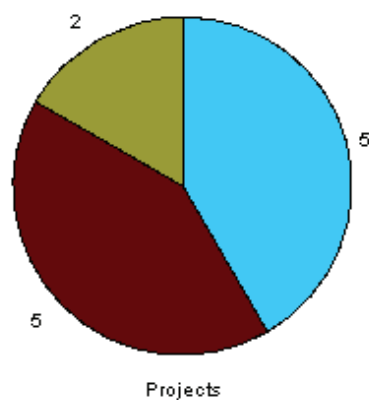


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

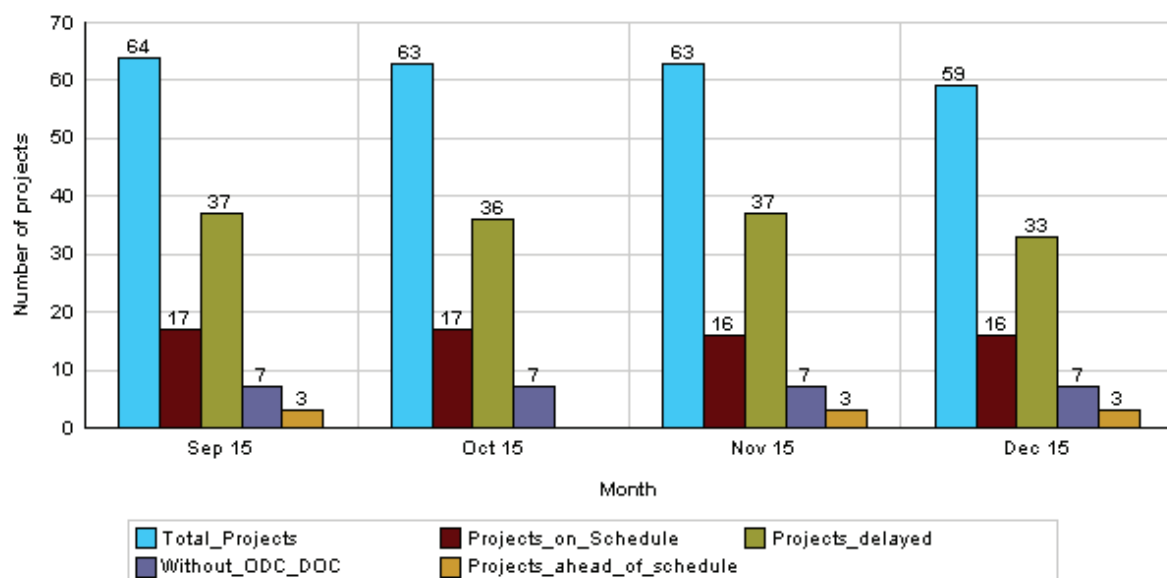


Break-up of 33 Delayed projects in December 2015

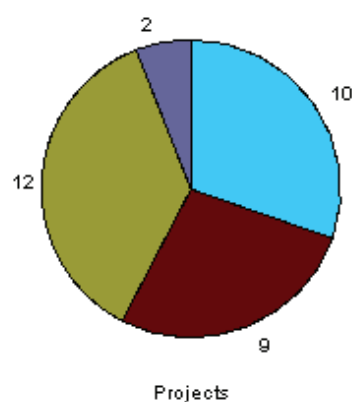


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

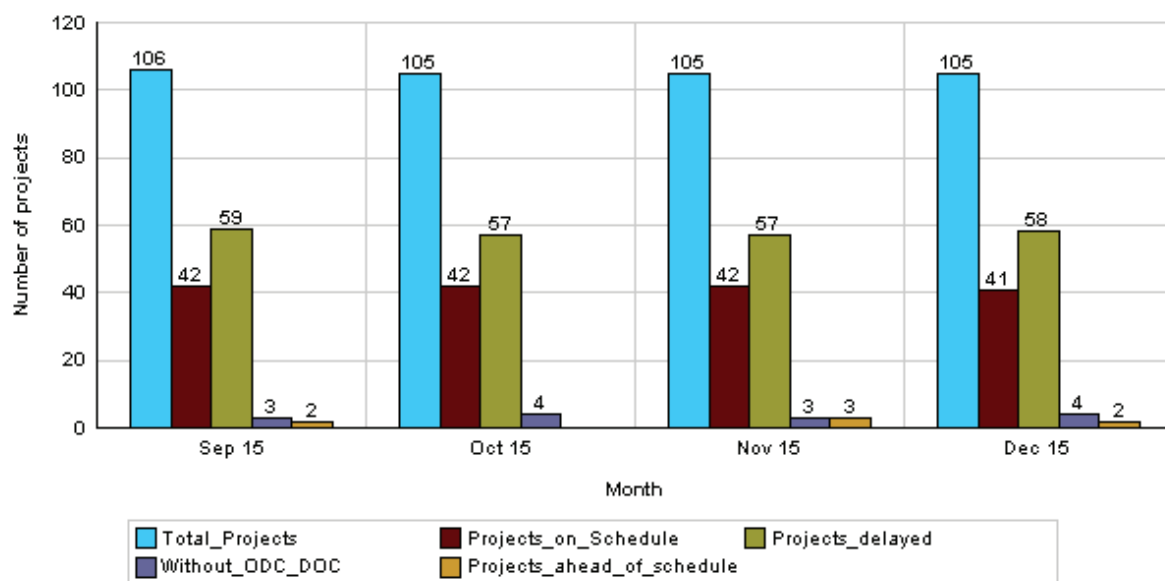


Break-up of 58 Delayed projects in December 2015

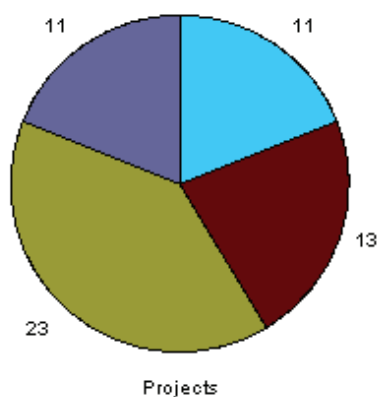


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of RAILWAYS Sector

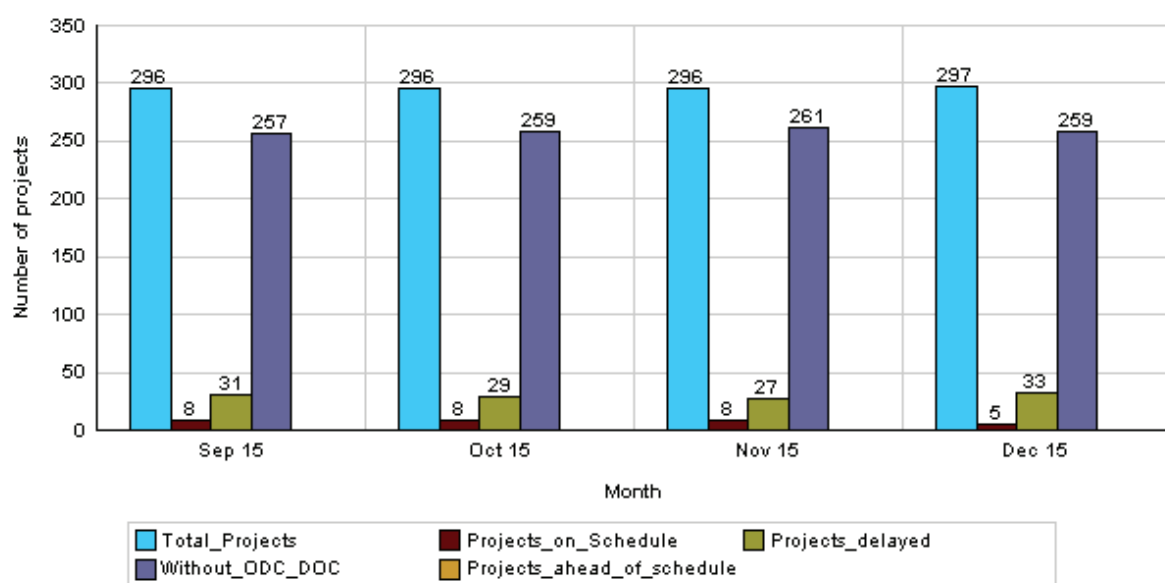


Break-up of 33 Delayed projects in December 2015

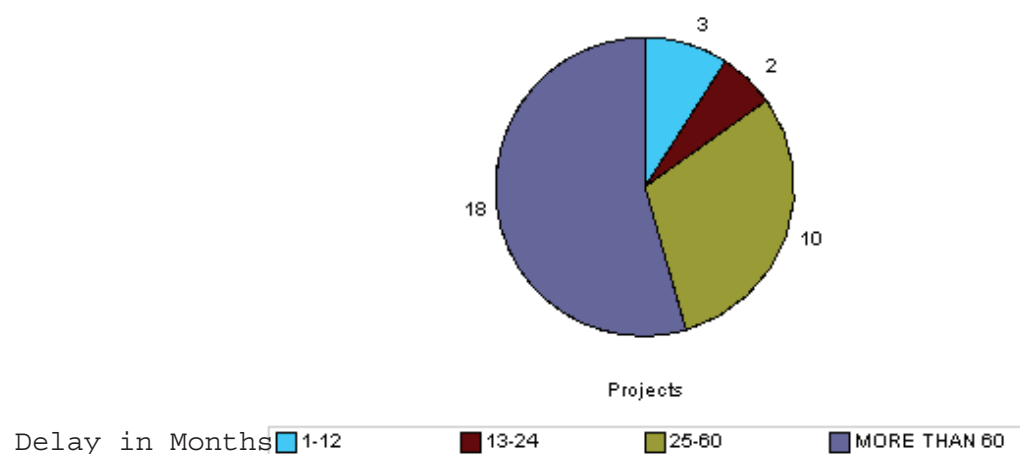


Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

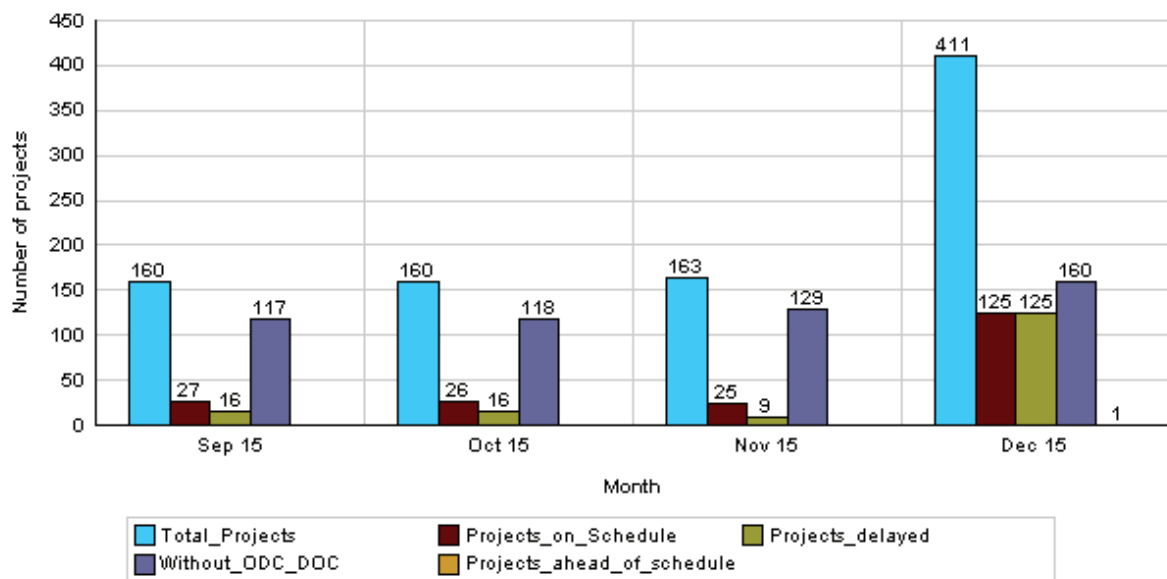


Break-up of 125 Delayed projects in December 2015

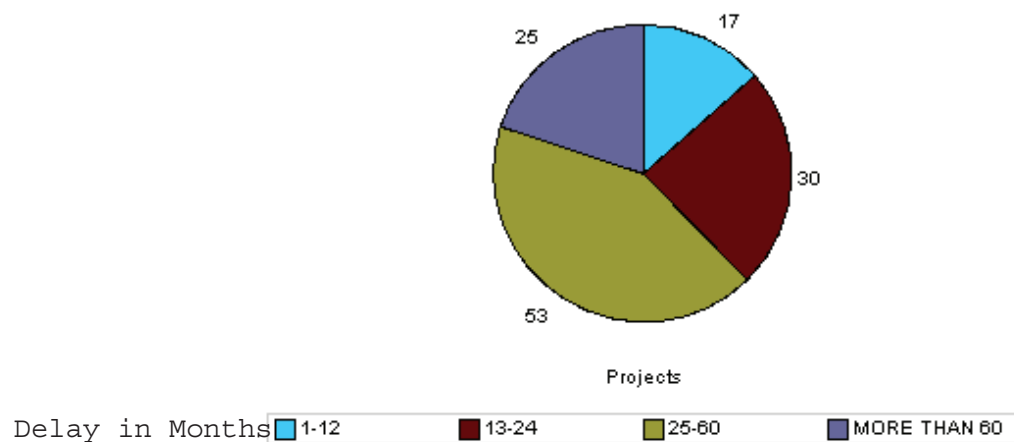


Graphical Presentation of SHIPPING AND PORTS Sector

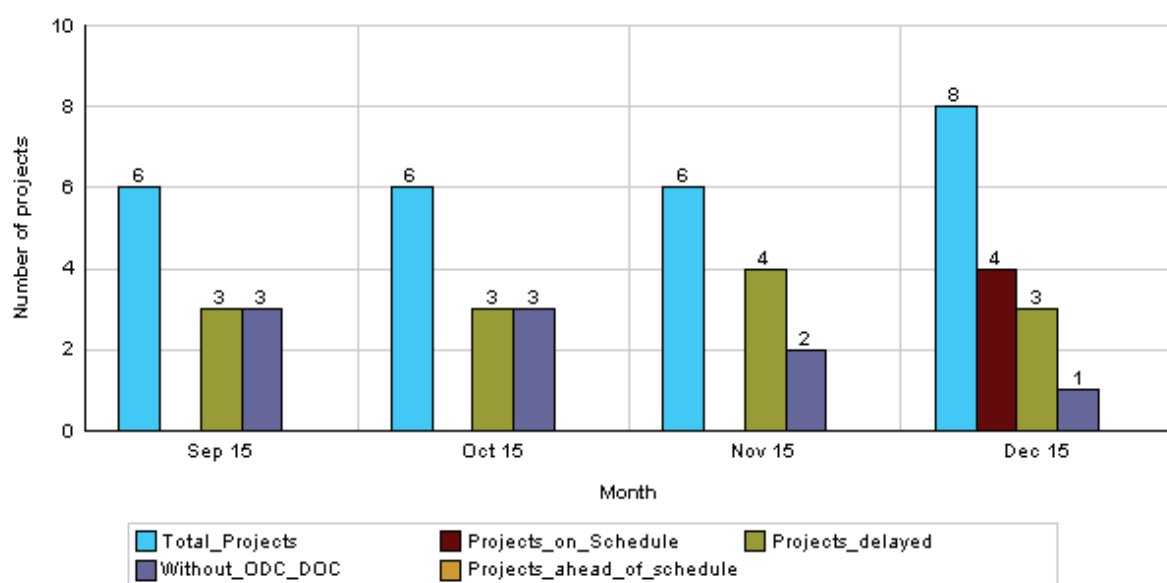


Break-up of 3 Delayed projects in December 2015

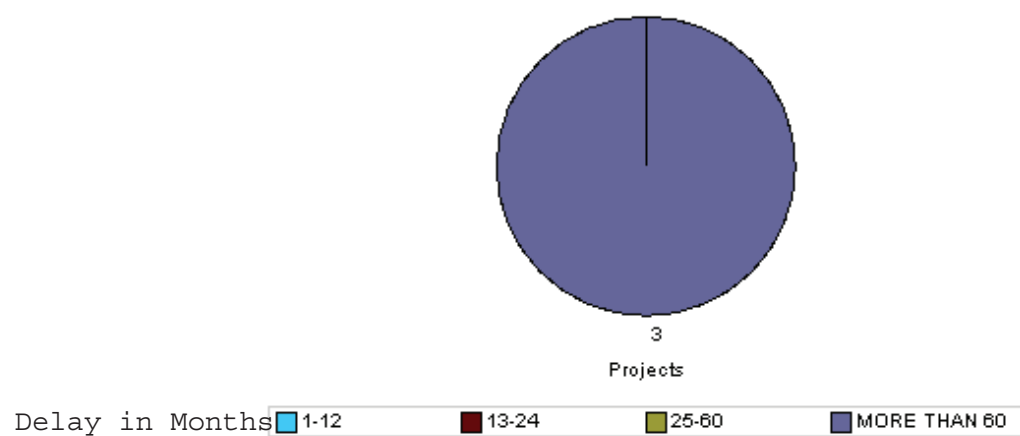


Graphical Presentation of TELECOMMUNICATIONS Sector

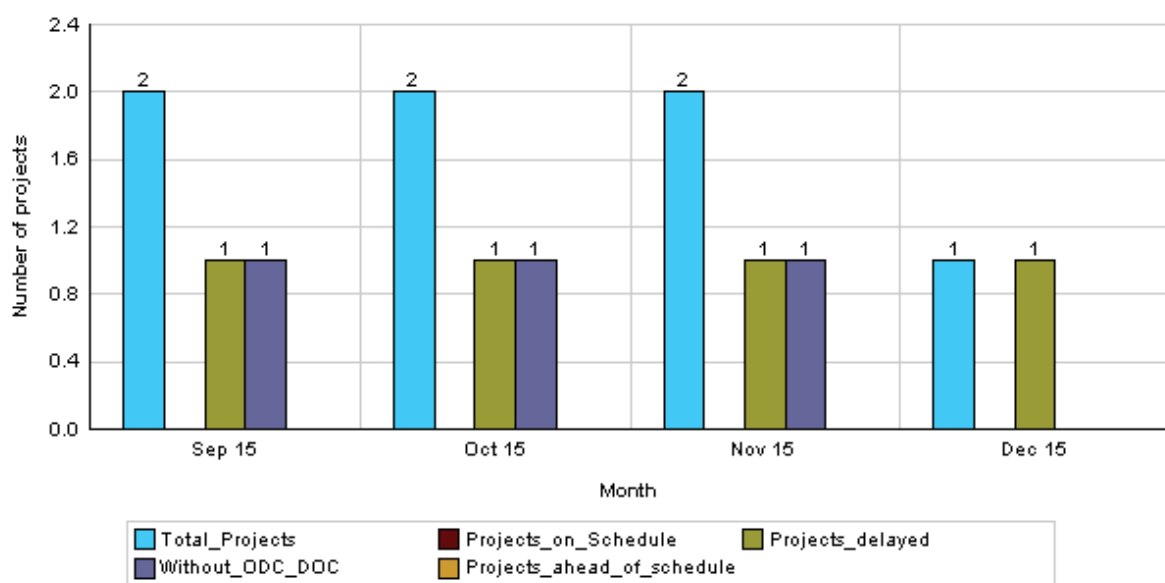


Break-up of 1 Delayed projects in December 2015

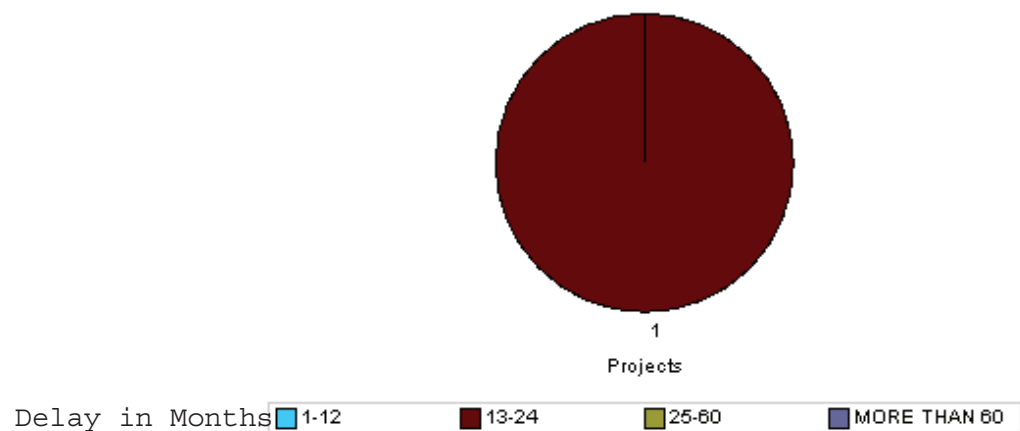


Graphical Presentation of URBAN DEVELOPMENT Sector

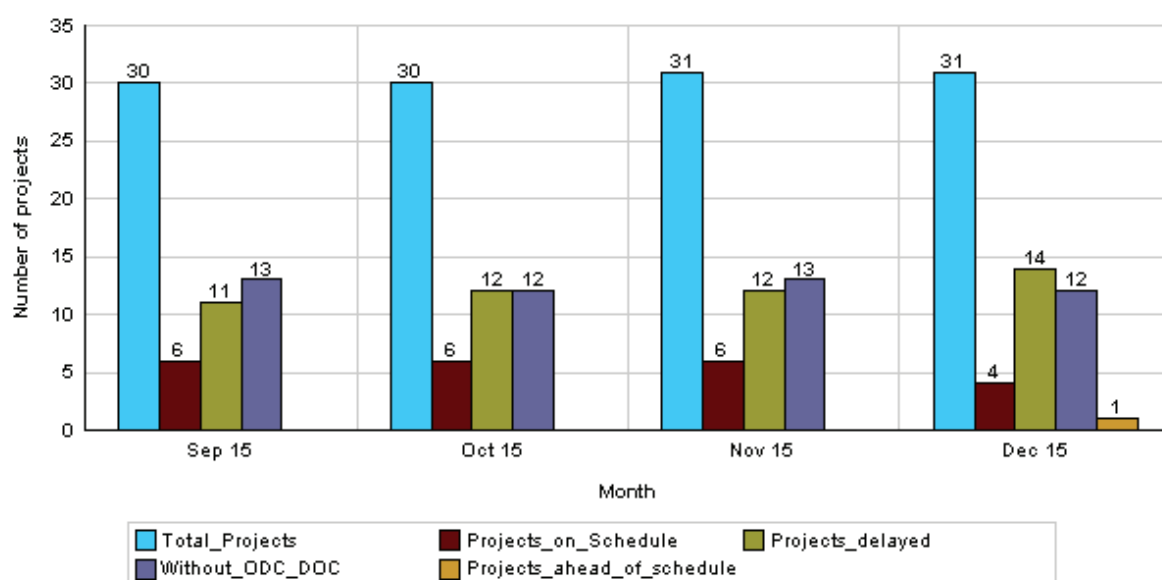


Break-up of 14 Delayed projects in December 2015

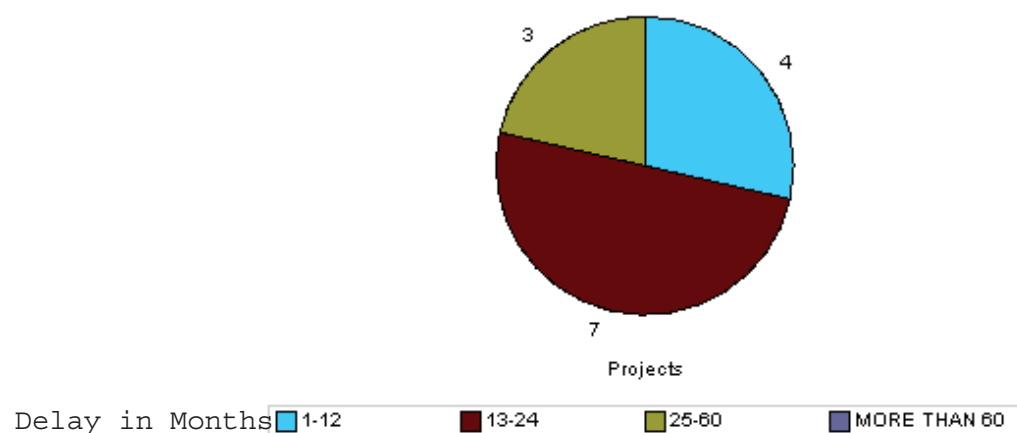


Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

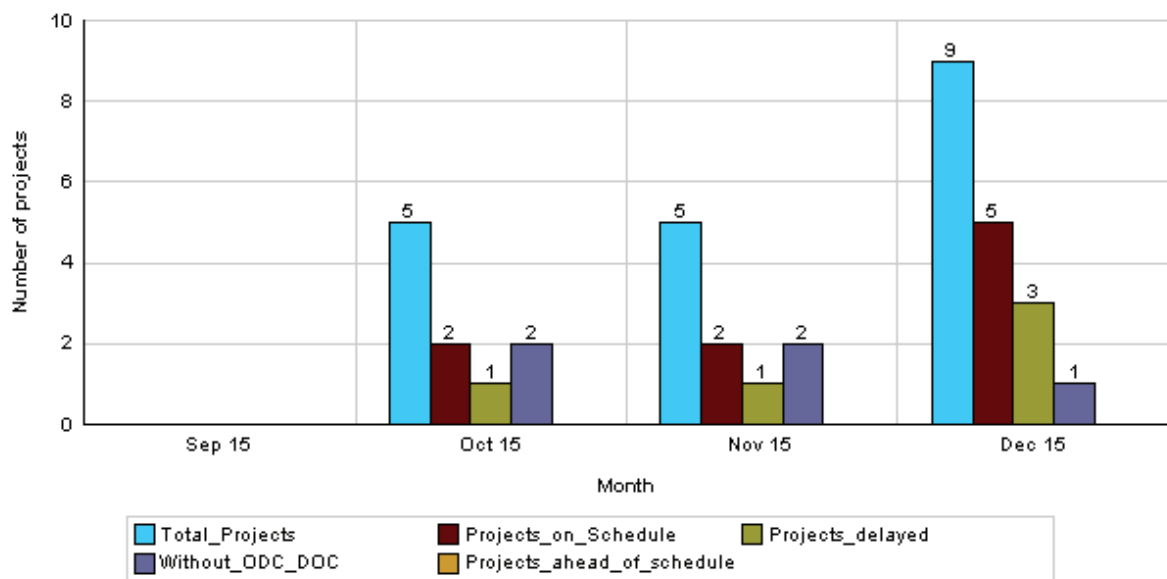


Break-up of 3 Delayed projects in December 2015

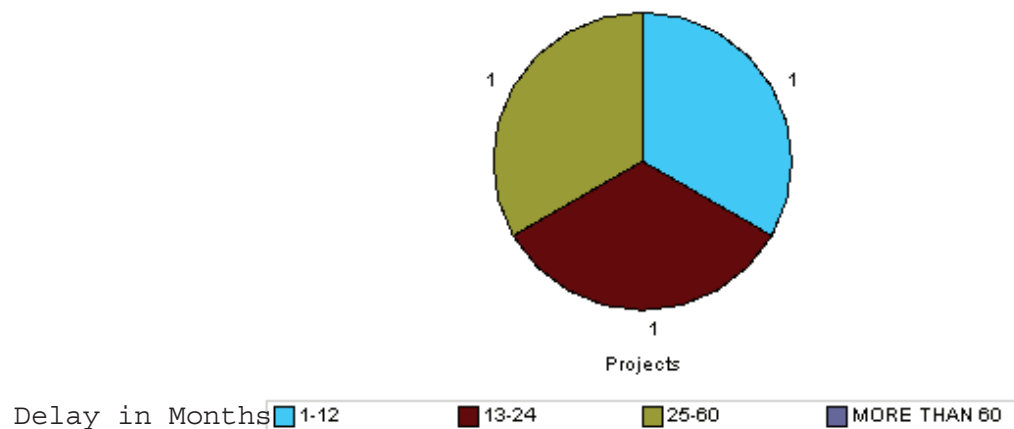

Graphical Presentation of MINES Sector

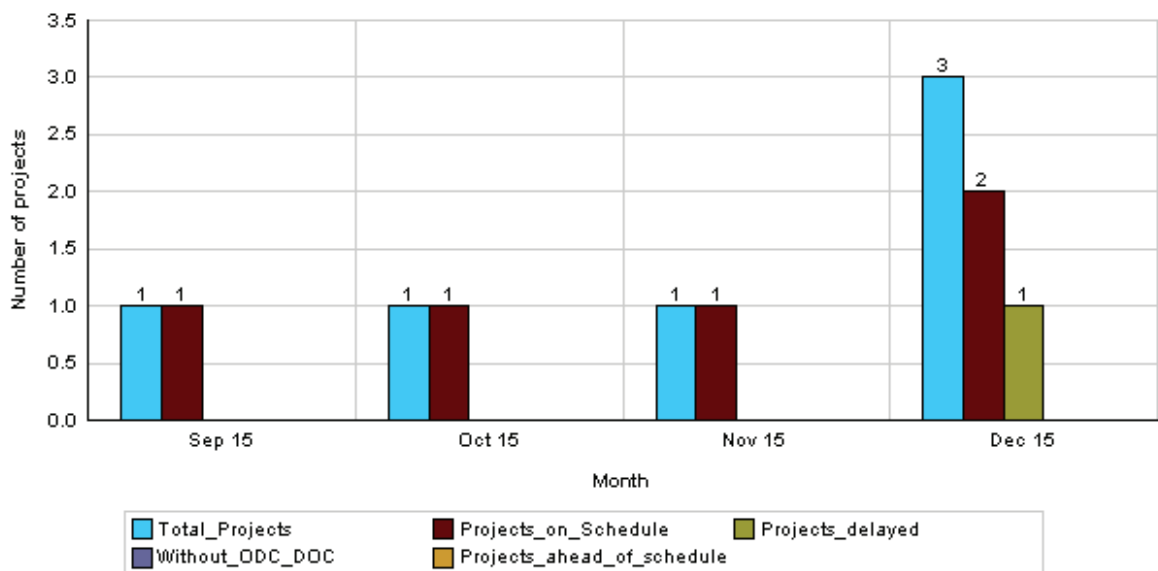

Break-up of 1 Delayed projects in December 2015

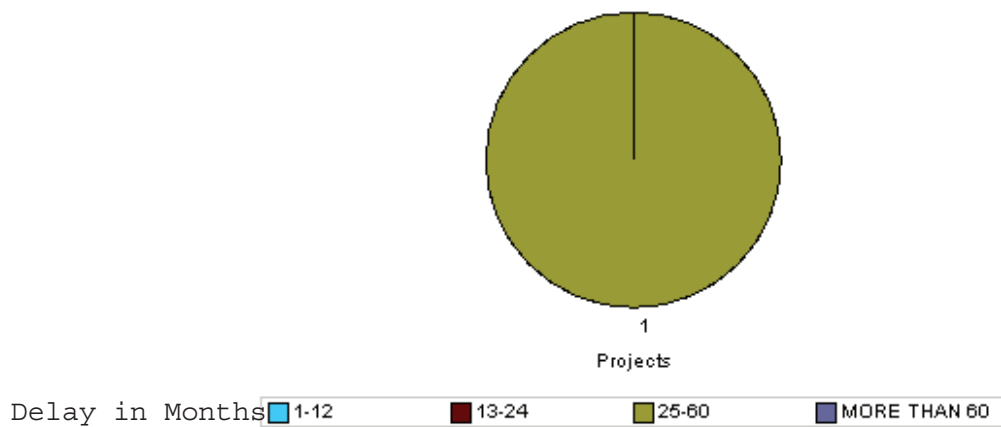

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	44,541.00	51,918.00	39,268.59
CIVIL AVIATION	4	1,177.28	1,177.28	1,186.17	762.20
COAL	87	61,587.45	62,466.79	62,537.14	15,120.59
FERTILISERS	1	197.79	197.79	197.79	43.68
MINES	3	2,555.63	2,555.63	1,875.63	2.86
STEEL	36	54,570.11	54,940.61	55,086.01	30,243.76
PETROCHEMICALS	1	5,460.61	8,920.00	9,965.00	9,103.96
PETROLEUM	59	128,876.79	135,681.23	138,276.44	65,197.50
POWER	105	294,222.64	321,700.03	341,026.11	171,005.75
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	2,563.15	929.79
RAILWAYS *	297	172,717.67	193,381.23	298,204.43	93,596.86
ROAD TRANSPORT AND HIGHWAYS	411	248,089.13	248,909.04	250,598.57	112,808.43
SHIPPING AND PORTS	8	4,117.75	4,561.87	5,048.81	1,788.41
TELECOMMUNICATIONS	1	13,334.00	13,334.00	13,334.00	1,360.00
URBAN DEVELOPMENT	31	136,783.82	141,997.69	144,233.70	48,692.67
Grand total	1058	1,168,413.82	1,238,645.34	1,379,878.25	589,925.05

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN, .	10/2009	12,320.00 -	12,320.00	5,403.00	12/2016 04/2017	05/2018	17(O) 13(R)	29/69
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU, .	12/2001	13,171.00 17,270.00	22,462.00	21,025.00	12/2008 10/2013	06/2016	90(O) 32(R)	54/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU, .	09/2003	3,492.00 -	5,677.00	5,129.59	09/2010 -	09/2016	72(O) -	12/88
4	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT, .	10/2009	11,459.00 -	11,459.00	7,711.00	12/2015 10/2016	10/2017	22(O) 12(R)	41/70
	Total		40,442.00 -	51,918.00	39,268.59				136/329
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA, .	05/2010	335.61 -	318.00	305.01	05/2012 -	03/2015	-	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM, .	01/2009	309.46 -	309.46	408.55	01/2011 06/2016	09/2017	80(O) 15(R)	0/0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE, .	10/2012	217.60 -	244.10	30.62	03/2015 -	09/2015	-	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS, .	10/2013	314.61 -	314.61	18.02	- -	09/2018	- -	0/0
	Total		1,177.28 -	1,186.17	762.20				0/0
	<u>COAL</u>								
9	JALLARAM SHAFT PROJECT - [N06000025]SCCL, TELANGANA, .	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA, .	01/2005	302.96 -	302.96	297.62	03/2010 -	03/2017	84(O) -	8/10
11	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH, .	06/2010	2,675.67 -	2,675.67	1,925.28	03/2014 -	03/2016	24(O) -	11/16
12	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH, .	12/2009	1,943.66 -	1,943.66	1,713.30	03/2014 -	03/2016	24(O) -	11/13
13	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL, JHARKHAND, .	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72(O) -	2/5
14	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH, .	06/2011	789.88 741.62	741.62	498.75	03/2013 -	03/2016	36(O) -	2/5
15	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH, .	08/2013	7,612.33 7,612.33	7,612.33	784.34	03/2023 03/2023	03/2023	0(O) 0(R)	1/17
16	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH, .	06/2011	746.04 535.10	535.10	424.18	03/2015 -	03/2016	12(O) -	3/6

Sector Wise Details									
(December 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH , .	12/2009	1,352.04 1,143.54	1,143.54	808.54	03/2016 -	03/2016	0(O) -	4/6
18	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , .	08/2008	706.40 -	706.40	77.78	07/2012 -	03/2021	104(O) -	1/3
19	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA , .	12/2009	212.34 1,228.39	1,228.39	866.72	03/2013 09/2012	03/2016	36(O) 42(R)	21/22
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , .	10/2006	249.03 -	249.03	76.98	03/2012 -	03/2018	72(O) -	29/42
21	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL , .	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72(O) -	9/15
22	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , .	10/2007	259.40 486.57	486.57	75.15	03/2012 03/2018	03/2017	60(O) -12(R)	1/1
23	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , .	12/2007	490.10 -	490.10	203.82	03/2017 -	03/2017	0(O) -	11/11
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , .	12/2007	457.77 -	457.77	208.05	03/2013 -	03/2017	48(O) -	8/9
25	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA , .	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	2/13
26	TALABIRA OCP - [N06000043]MCL,ODISHA , .	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
27	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , .	12/2007	172.08 -	172.08	150.27	03/2010 -	03/2017	84(O) -	2/4
28	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH , .	11/2014	1,624.59 1,624.59	1,624.59	5.43	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
29	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , .	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51(O) -	11/44
30	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH , .	08/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023	0(O) -	1/9
31	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND , .	09/2009	153.82 -	153.82	69.02	03/2014 -	03/2016	24(O) -	3/9
32	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , .	09/2014	441.82 -	441.82	131.57	03/2020 -	03/2020	0(O) -	5/13
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , .	08/2008	207.28 -	207.28	205.98	03/2012 -	03/2017	60(O) -	4/5
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , .	11/2008	479.53 -	479.53	175.70	03/2013 -	03/2017	48(O) -	4/8
35	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH , .	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60(O) -	1/7
36	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH , .	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
37	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , .	12/2009	418.97 -	489.62	411.47	03/2012 -	03/2023	132(O) -	0/2
38	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , .	03/2010	209.78 -	209.78	76.28	03/2015 -	03/2016	12(O) -	8/31
39	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , .	03/2010	181.19 -	181.19	67.47	03/2012 -	03/2016	48(O) -	5/6
40	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH , .	12/2009	321.50 -	321.50	209.59	03/2014 -	03/2018	48(O) -	4/7
41	AMLA OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH , .	11/2009	150.59 198.59	198.59	125.13	03/2016 -	03/2016	0(O) -	3/7

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND , .	08/2007	163.51 -	163.51	36.08	03/2011 -	03/2016	60(O) -	0/3
43	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND , .	12/2007	179.87 -	179.87	91.85	03/2012 -	03/2017	60(O) -	3/3
44	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND , .	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48(O) -	4/4
45	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND , .	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48(O) -	2/4
46	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND , .	12/2009	510.85 -	510.85	224.43	03/2016 -	03/2016	0(O) -	2/4
47	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND , .	06/2009	162.46 -	162.46	70.20	03/2014 -	03/2017	36(O) -	3/4
48	KISTARAM OCP - [N06000089]SCCL,TELANGANA , .	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36(O) -	0/5
49	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH , .	06/2011	1,131.28 1,131.28	1,131.28	140.70	03/2018 -	03/2018	0(O) -	6/9
50	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , .	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36(O) -	4/29
51	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , .	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/13
52	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , .	02/2011	339.88 -	339.88	12.06	04/2014 -	03/2016	23(O) -	4/7
53	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH , .	04/2012	258.56 -	258.56	96.39	03/2016 -	03/2018	24(O) -	3/6
54	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , .	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21(O) -	18/51
55	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , .	07/2012	417.33 -	417.33	14.18	07/2016 -	03/2017	8(O) -	6/28
56	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , .	11/2012	430.45 486.27	486.27	93.51	03/2016 -	03/2018	24(O) -	7/39
57	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND , .	02/2012	858.11 -	858.11	108.45	03/2020 -	03/2020	0(O) -	3/3
58	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH , .	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	0(O) -	1/7
59	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , .	02/2014	555.52 -	555.52	3.52	03/2021 -	03/2017	-48(O) -	0/2
60	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL , .	08/2012	1,055.05 -	1,055.05	197.01	03/2018 -	03/2018	0(O) -	1/8
61	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU , .	04/2012	364.75 -	364.75	183.91	10/2014 -	03/2016	17(O) -	8/10
62	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH , .	05/2014	164.49 -	164.49	76.43	03/2020 -	03/2020	0(O) -	2/6
63	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , .	05/2014	479.15 -	479.15	10.25	03/2019 -	03/2019	0(O) -	1/9
64	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , .	05/2014	3,756.36 -	3,756.36	620.51	03/2026 -	03/2026	0(O) -	3/15
65	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , .	05/2014	337.66 -	337.66	0.29	03/2019 -	03/2019	0(O) -	2/6
66	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , .	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
67	GARJANBAHAL OCP - [N06000117]MCL,ODISHA , .	11/2014	1,375.38	1,375.38	158.47	03/2021	03/2021	0(O)	1/9
68	DINESH OCP - [N06000118]WCL,MAHARASHTRA , .	11/2014	611.16	611.16	194.04	03/2020	03/2020	0(O)	3/15
69	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , .	09/2014	266.23	266.23	94.45	03/2021	03/2021	0(O)	4/14
70	GOKUL - [N06000120]WCL,MAHARASHTRA , .	11/2014	267.67	267.67	176.63	03/2018	03/2018	0(O)	2/8
71	BHANEAGON OC - [N06000121]WCL,MAHARASHTRA , .	02/2015	187.94	187.94	49.30	03/2023	03/2023	0(O)	6/11
72	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , .	02/2015	481.60	481.60	-	03/2023	03/2023	0(O)	0/7
73	AMERA OC RCE - [N06000123]SECL,CHHATISGARH , .	02/2015	335.97	335.97	30.90	03/2018	03/2018	0(O)	0/4
74	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , .	12/2014	357.80	357.80	108.44	03/2021	03/2021	0(O)	0/7
75	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , .	12/2014	371.04	371.04	28.78	03/2021	03/2021	0(O)	0/6
76	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , .	05/2015	295.56	295.56	79.03	03/2019	03/2019	0(O)	4/14
77	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA , .	05/2015	397.09	397.09	-	03/2019	03/2019	0(O)	5/18
78	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , .	06/2015	205.49	205.49	1.37	03/2020	03/2020	0(O)	4/12
79	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , .	06/2015	483.69	483.69	39.36	03/2021	03/2021	0(O)	3/9
80	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , .	08/2015	727.28	727.28	61.37	03/2025	03/2025	0(O)	3/13
81	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , .	08/2015	288.90	288.90	-	03/2023	03/2023	0(O)	3/15
82	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , .	07/2015	231.92	231.92	-	03/2022	03/2022	0(O)	0/1
83	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH , .	07/2015	316.10	316.10	15.85	03/2020	03/2020	0(O)	0/5
84	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH , .	02/2015	916.24	916.24	-	03/2023	03/2023	0(O)	0/8
85	MALACHUA OPENCAS PROJECT - [N06000139]SECL,MADHYA PRADESH , .	10/2015	488.33	488.33	-	03/2023	03/2023	0(O)	0/8
86	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH , .	10/2015	1,875.32	1,875.32	-	03/2024	03/2024	0(O)	0/0
87	KAMPTTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , .	11/2015	277.65	277.65	-	03/2021	03/2021	0(O)	0/9
88	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , .	11/2015	498.42	498.42	-	03/2018	03/2018	0(O)	1/9
89	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , .	10/2015	359.69	359.69	6.49	03/2022	03/2022	0(O)	0/0
90	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , .	06/2011	5,907.11	5,907.11	1,297.62	12/2015 04/2018	04/2018	28(O) 0(R)	11/35
91	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , .	08/2011	1,230.27	1,230.27	47.76	04/2015 04/2019	04/2019	48(O) 0(R)	2/11
92	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , .	08/2011	988.35	988.35	45.26	04/2017	04/2017	0(O)	0/2

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU , .	04/2013	1,458.17 -	1,458.17	8.68	06/2015 -	08/2019	50(O) -	1/7
94	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND , .	08/2010	289.45 -	289.45	99.28	05/2014 -	10/2016	29(O) -	0/8
95	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND , .	10/2012	269.82 -	269.82	62.95	04/2014 -	11/2016	31(O) -	0/10
	Total		61,587.45 -	62,537.14	15,120.59				326/1012
	<u>FERTILISERS</u>								
96	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA , .	10/2014	197.79 197.79	197.79	43.68	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	197.79	43.68				0/0
	<u>MINES</u>								
97	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL, MADHYA PRADESH , .	09/2011	1,856.00 -	1,176.00	2.86	09/2017 -	04/2020	31(O) -	0/0
98	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO, MAHARASHTRA , Private	12/2015	355.13 -	355.13	-	11/2016 -	11/2016	0(O) -	0/0
99	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO, RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 -	344.50	-	11/2016 -	11/2016	0(O) -	0/0
	Total		2,555.63 -	1,875.63	2.86				0/0
	<u>STEEL</u>								
100	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL, KARNATAKA , .	05/2005	768.88 1,060.00	1,060.00	1,070.97	02/2014 -	-	-	0/0
101	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL, ANDHRA PRADESH , .	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
102	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL, GUJARAT , .	01/2013	175.00 -	175.00	-	- -	-	-	0/0
103	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR , .	10/2005	956.00 -	956.00	646.65	03/2015 -	-	-	0/0
104	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA , .	10/2012	160.48 -	160.48	143.50	09/2014 01/2016	01/2016	16(O) 0(R)	2/3
105	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATTISGARH , .	07/2012	332.65 -	332.65	229.56	08/2014 02/2016	02/2016	18(O) 0(R)	4/5
106	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL , .	11/2012	313.05 -	313.05	314.87	06/2015 02/2016	02/2016	8(O) 0(R)	3/4

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
107	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND , .	03/2015	255.19 -	255.19	22.05	03/2018 -	03/2018	0(O) -	0/0
108	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UPGRADE OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN , .	05/2015	189.00 -	189.00	-	03/2017 -	03/2017	0(O) -	0/0
109	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , .	12/2007	200.00 -	200.00	126.65	03/2018 -	03/2018	0(O) -	0/0
110	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA , .	04/2015	3,127.30 -	3,127.30	232.80	04/2018 -	04/2018	0(O) -	0/0
111	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , .	04/2013	170.00 -	170.00	88.90	04/2018 -	04/2018	0(O) -	0/0
112	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA , .	06/2012	237.09 -	237.09	220.15	12/2014 05/2016	05/2016	17(O) 0(R)	2/3
113	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , .	10/2013	245.67 -	245.67	79.89	05/2016 -	05/2016	0(O) -	1/3
114	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA , .	04/2011	572.00 -	572.00	482.21	04/2013 09/2014	06/2015	-	18/19
115	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA , .	12/2011	187.33 -	187.33	173.07	10/2013 06/2016	06/2016	32(O) 0(R)	2/5
116	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH , .	07/2011	877.73 -	877.73	370.73	07/2015 -	06/2016	11(O) -	2/2
117	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH , .	05/2012	404.16 -	404.16	248.38	07/2015 -	06/2017	23(O) -	0/1
118	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , .	12/2009	343.00 -	488.40	36.00	10/2016 -	06/2017	8(O) -	0/0
119	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , .	12/2007	253.92 254.00	254.00	192.96	06/2016 -	06/2016	0(O) -	0/0
120	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA , .	02/2011	898.55 -	898.55	408.94	05/2013 01/2015	08/2015	-	19/20
121	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA , .	06/2014	708.91 -	708.91	290.11	04/2016 09/2016	09/2016	5(O) 0(R)	2/2
122	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH , .	12/2009	280.00 -	280.00	19.87	09/2016 -	09/2016	0(O) -	1/1
123	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , .	02/2014	4,749.00 -	4,749.00	2.61	09/2017 -	09/2017	0(O) -	0/0
124	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA , .	04/2014	151.33 -	151.33	4.84	09/2017 -	09/2017	0(O) -	0/0
125	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , .	08/2010	17,265.00 -	17,265.00	15,431.95	03/2013 10/2016	10/2016	43(O) 0(R)	31/35
126	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , .	03/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017	0(O) -	0/0
127	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH , .	01/2010	15,525.00 -	15,525.00	8,318.82	05/2015 12/2016	12/2016	19(O) 0(R)	28/81
128	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH , .	07/2011	974.76 -	974.76	215.52	07/2016 -	12/2016	5(O) -	0/1

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
129	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND , .	05/2015	1,154.18 -	1,154.18	27.45	12/2017 -	12/2017	0(O) -	0/0
130	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA , .	03/2007	149.73 173.00	173.00	175.89	12/2015 -	12/2015	0(O) -	0/0
131	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA , .	12/2007	202.61 227.00	227.00	195.46	12/2016 -	12/2016	0(O) -	0/0
132	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA , .	10/2011	175.49 207.00	207.00	129.17	12/2016 -	12/2016	0(O) -	0/0
133	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , .	07/2011	324.87 325.00	325.00	263.57	12/2015 -	12/2015	0(O) -	0/0
134	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , .	02/2014	787.29 -	787.29	23.83	12/2016 -	12/2016	0(O) -	0/0
135	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , .	04/2014	188.93 -	188.93	56.39	04/2015 -	-	-	1/3
	Total		54,570.11 -	55,086.01	30,243.76				116/188
	<u>PETROCHEMICALS</u>								
136	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM , .	04/2006	5,460.61 8,920.00	9,965.00	9,103.96	04/2012 12/2013	12/2015	44(O) 24(R)	21/26
	Total		5,460.61 -	9,965.00	9,103.96				21/26
	<u>PETROLEUM</u>								
137	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU , .	05/2013	711.00 -	711.00	7.48	- -	-	-	0/0
138	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU , .	11/2006	171.83 -	171.83	-	- -	-	-	0/0
139	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , .	01/2015	1,823.00 -	1,823.00	0.86	- -	-	-	0/0
140	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE , .	01/2015	2,321.00 -	2,321.00	1.50	- -	-	-	0/0
141	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE , .	02/2015	890.00 -	890.00	0.76	- -	-	-	0/0
142	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA , .	02/2009	29,777.00 34,555.00	34,555.00	30,818.63	11/2012 11/2013	01/2016	38(O) 26(R)	96/100
143	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE , .	06/2010	2,523.00 2,523.00	2,523.00	1,663.75	01/2014 12/2015	01/2016	24(O) 1(R)	2/13
144	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU , .	12/2012	279.00 -	279.00	186.98	12/2014 -	01/2016	13(O) -	57/58
145	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE , .	04/2010	270.00 -	215.66	-	06/2012 -	01/2016	43(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
146	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM, .	03/2009	2,465.15 2,378.89	2,378.89	1,789.87	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
147	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE, .	08/2009	1,793.00 -	1,793.00	1,261.12	09/2012 -	03/2016	42(O) -	6/7
148	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA, .	12/2009	1,584.00 -	1,584.00	1,366.24	08/2015 -	03/2016	7(O) -	3/12
149	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE, .	12/2009	463.32 -	463.32	315.82	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
150	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT, .	03/2009	317.64 -	240.95	123.32	09/2012 03/2016	03/2016	42(O) 0(R)	0/5
151	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE, .	08/2011	586.00 -	586.00	407.88	08/2015 -	03/2016	7(O) -	3/12
152	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE, .	12/2009	309.81 462.79	462.79	258.68	10/2014 03/2017	03/2017	29(O) 0(R)	28/40
153	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPL, KARNATAKA, .	01/2006	732.00 1,227.00	1,227.00	1,029.66	10/2011 -	03/2016	53(O) -	0/0
154	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE, .	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
155	MARKETING TOP AT KORBA - [N16000186]IOCL, CHHATISGARH, .	01/2011	141.86 -	219.00	160.78	09/2016 -	03/2016	-6(O) -	0/12
156	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA, .	11/2014	6,068.80 -	6,068.80	523.70	04/2019 -	03/2019	-1(O) -	0/0
157	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI, .	08/2014	6,086.08 -	6,086.08	586.87	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
158	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA, .	03/2014	238.50 -	238.50	1.07	03/2017 -	03/2017	0(O) -	0/0
159	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA, .	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
160	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA, .	03/2011	861.79 1,256.72	1,256.72	995.12	05/2013 04/2016	04/2016	35(O) 0(R)	1/5
161	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA, .	12/2011	2,059.63 2,665.65	2,665.65	1,282.07	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
162	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA, .	03/2012	2,592.17 2,592.17	2,592.17	830.50	05/2014 05/2016	05/2016	24(O) 0(R)	0/21
163	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE, .	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
164	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE, .	01/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016	26(O) 0(R)	0/3
165	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA, .	03/2012	14,225.00 -	16,504.00	9,397.86	05/2016 -	05/2016	0(O) -	0/30
166	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA, .	03/2013	1,138.50 686.58	686.58	552.58	04/2015 04/2015	05/2016	13(O) 13(R)	0/0
167	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL, KERALA, .	01/2006	993.00 1,693.00	1,693.00	1,446.59	01/2012 -	05/2016	52(O) -	0/0
168	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC, MULTI STATE, .	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5

Sector Wise Details

(December 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
169	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC, MAHARASHTRA, .	06/2014	5,706.47 5,813.25	5,813.25	2,268.83	05/2017 05/2017	05/2017	0(O) 0(R)	6/16
170	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL, GUJARAT, .	12/2011	160.00 -	160.00	35.07	02/2016 02/2016	05/2016	3(O) 3(R)	0/0
171	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA, .	02/2015	2,899.93 2,098.43	2,098.43	502.37	05/2017 -	05/2017	0(O) -	0/0
172	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE, .	06/2009	2,915.00 -	2,915.00	1,379.87	12/2012 -	06/2015	-	7/14
173	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL, ANDHRA PRADESH, .	07/2014	419.04 -	419.04	254.80	01/2017 -	06/2016	-7(O) -	11/16
174	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC, GUJARAT, .	09/2011	202.25 -	160.16	68.96	07/2016 -	07/2016	0(O) -	5/12
175	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL, BIHAR, .	04/2013	480.00 -	480.00	126.43	02/2016 -	07/2016	5(O) -	5/6
176	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM, .	02/2014	163.88 -	163.88	50.18	07/2016 -	07/2016	0(O) -	4/6
177	RESID UPGRADEATION PROJECT - [N16000184]CPCL, TAMIL NADU, .	02/2011	3,110.36 -	3,110.36	1,292.13	11/2015 07/2016	07/2016	8(O) 0(R)	44/52
178	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL, MULTI STATE, .	01/2015	690.00 -	690.00	-	07/2018 -	07/2018	0(O) -	1/31
179	UPGRADEATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM, .	09/2012	871.35 -	1,200.00	455.47	03/2015 11/2015	08/2016	17(O) 9(R)	0/5
180	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL, ODISHA, .	03/2014	3,150.00 -	3,150.00	111.66	09/2017 -	09/2017	0(O) -	0/0
181	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE, .	06/2007	736.65 -	736.65	498.95	09/2011 10/2016	10/2016	61(O) 0(R)	0/0
182	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA, .	10/2015	607.06 714.25	714.25	59.42	10/2017 10/2017	10/2017	0(O) 0(R)	21/48
183	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, KARNATAKA, .	02/2012	666.00 838.08	838.08	570.28	11/2015 11/2016	11/2016	12(O) 0(R)	25/29
184	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU, .	05/2015	257.87 -	257.87	34.49	11/2016 -	11/2016	0(O) -	9/22
185	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT, .	05/2015	1,671.22 1,881.22	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
186	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE, .	07/2009	3,957.00 3,561.00	3,561.00	25.93	01/2013 -	12/2018	71(O) -	11/38
187	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE, .	02/2011	913.00 -	913.00	460.06	08/2015 -	12/2016	16(O) -	0/0
188	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE, .	05/2013	4,124.35 4,941.49	4,941.49	521.23	04/2016 12/2017	12/2017	20(O) 0(R)	0/6
189	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL, .	03/2014	3,076.00 -	3,076.00	164.88	09/2017 03/2018	12/2017	3(O) -3(R)	0/0
190	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE, .	03/2014	2,476.82 -	2,476.82	368.95	12/2018 -	12/2018	0(O) -	3/9
191	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM, .	03/2009	228.64 -	214.19	137.49	12/2016 -	12/2016	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
192	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE , .	10/2011	725.00 -	725.00	100.19	11/2016 -	12/2016	1(O) -	0/14
193	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA , .	05/2015	2,443.00 -	2,443.00	81.45	12/2017 -	12/2017	0(O) -	0/0
194	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM , .	06/2010	202.94 -	202.94	2.95	01/2014 -	-	-	0/2
195	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , .	04/2011	191.96 -	191.96	98.84	05/2015 -	12/2015	7(O) -	0/12
	Total		128,876.79 -	138,276.44	65,197.50				366/721
	POWER								
196	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , .	07/2009	421.01 1,007.57	1,007.57	953.59	07/2013 01/2016	01/2016	30(O) 0(R)	25/26
197	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE , .	03/2010	965.58 -	965.58	757.94	11/2012 -	01/2016	38(O) -	7/10
198	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA , .	09/2010	2,074.86 2,348.37	2,348.37	1,950.24	03/2013 06/2015	01/2016	34(O) 7(R)	11/11
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE , .	08/2010	1,677.57 -	1,677.57	1,444.82	04/2013 -	01/2016	33(O) -	9/11
200	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , .	01/2013	12,964.60 -	12,964.60	4,822.73	01/2018 -	01/2018	0(O) -	21/24
201	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL , .	04/2007	4,122.00 8,781.00	9,606.82	1,353.36	02/2011 -	01/2017	71(O) -	0/0
202	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , .	02/2015	302.49 302.00	302.49	229.19	02/2016 -	01/2016	-1(O) -	0/1
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE , .	02/2009	410.29 -	410.29	360.37	02/2012 -	02/2016	48(O) -	7/10
204	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE , .	05/2010	250.03 -	250.03	184.20	01/2013 -	02/2016	37(O) -	10/15
205	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE , .	12/2011	2,422.66 -	2,422.66	2,307.76	08/2014 -	02/2016	18(O) -	9/14
206	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE , .	12/2011	297.33 346.79	346.79	302.97	08/2014 06/2015	02/2016	18(O) 8(R)	8/10
207	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMP-PART B - [N18000122]PGCIL,MULTI STATE , .	02/2012	1,927.16 -	1,927.16	1,573.17	10/2014 -	02/2016	16(O) -	5/7
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE , .	09/2012	524.40 -	524.40	282.92	05/2015 -	02/2016	9(O) -	8/12
209	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , .	08/2014	288.49 -	288.49	53.40	02/2017 -	02/2017	0(O) -	0/12
210	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , .	02/2014	14,366.58 -	14,366.58	2,287.00	02/2019 -	02/2019	0(O) -	9/11
211	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , .	05/2011	195.42 -	195.42	44.00	02/2014 -	02/2018	48(O) -	1/1

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
212	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM, .	01/2008	4,375.35 6,749.18	6,749.18	5,642.00	09/2011 -	03/2017	66(O) -	17/37
213	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL, MULTI STATE, .	12/2009	1,216.83 -	1,216.83	1,062.99	08/2012 -	03/2016	43(O) -	3/5
214	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN. PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL, MULTI STATE, .	03/2011	1,585.12 -	1,585.12	1,570.76	11/2013 -	03/2016	28(O) -	8/12
215	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND, .	10/2011	558.26 -	558.26	520.31	11/2013 -	03/2016	28(O) -	8/12
216	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT, .	12/2011	552.44 -	552.44	574.60	02/2014 -	03/2016	25(O) -	8/10
217	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA, .	01/2012	15,166.19 -	15,166.19	9,969.00	01/2017 -	03/2017	2(O) -	30/37
218	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE, .	09/2013	680.69 -	680.69	431.09	03/2016 -	03/2016	0(O) -	10/12
219	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL, KARNATAKA, .	02/2014	167.40 -	167.40	88.20	12/2015 -	03/2016	3(O) -	6/8
220	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE, .	03/2014	155.57 -	155.57	2.30	03/2016 -	03/2016	0(O) -	1/6
221	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE, .	06/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018	0(O) -	8/12
222	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL, ANDHRA PRADESH, .	08/2014	188.75 -	188.75	70.80	02/2017 -	03/2016	-11(O) -	0/2
223	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH, .	09/2014	9,188.98 -	9,188.98	939.00	03/2019 -	03/2019	0(O) -	14/15
224	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL, MULTI STATE, .	01/2015	268.80 -	268.80	22.60	03/2018 -	03/2018	0(O) -	0/3
225	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE, .	03/2015	197.40 -	197.40	-	03/2018 -	03/2018	0(O) -	0/0
226	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL, ANDHRA PRADESH, .	03/2015	550.06 -	550.06	4.60	03/2018 -	03/2018	0(O) -	0/3
227	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR, .	03/2010	3,984.03 -	3,984.03	3,125.22	01/2013 -	03/2016	38(O) -	0/1
228	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND, .	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51(O) -	0/0
229	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE, .	10/2013	1,364.52 -	1,364.52	430.87	04/2016 -	04/2016	0(O) -	8/12
230	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL, MULTI STATE, .	06/2014	400.47 -	400.47	45.19	04/2017 -	04/2017	0(O) -	0/3

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
231	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPC,JAMMU AND KASHMIR , .	10/2014	8,112.12 -	8,112.12	115.70	04/2020 -	04/2020	0(O) -	0/0
232	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , .	12/2014	6,517.36 -	6,517.36	243.10	04/2018 -	04/2018	0(O) -	3/12
233	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , .	04/2015	3,705.61 -	3,705.61	175.30	04/2018 -	04/2018	0(O) -	4/9
234	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , .	04/2015	1,479.30 -	1,479.30	67.10	04/2017 -	04/2017	0(O) -	2/8
235	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , .	02/2005	8,692.97 15,095.67	15,095.67	11,070.00	01/2011 10/2014	05/2018	88(O) 43(R)	27/48
236	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE , .	09/2013	1,575.30 -	1,575.30	623.05	05/2016 -	05/2016	0(O) -	8/13
237	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE , .	01/2015	3,662.02 -	3,662.02	295.10	05/2018 -	05/2018	0(O) -	0/5
238	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , .	03/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017	0(O) -	0/9
239	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH , .	05/2015	312.94 -	312.94	10.00	05/2016 -	05/2016	0(O) -	0/0
240	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH , .	12/2004	2,496.90 6,085.84	6,085.84	4,303.08	12/2009 06/2016	06/2016	78(O) 0(R)	16/27
241	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL , .	09/2005	1,061.38 -	1,929.15	1,937.70	09/2009 -	06/2016	81(O) -	2/6
242	WESTERN REGION SYSTEM STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , .	12/2007	477.69 721.81	721.81	577.79	09/2010 06/2013	06/2016	69(O) 36(R)	4/8
243	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE , .	02/2009	509.66 -	509.66	523.76	11/2011 -	06/2016	55(O) -	8/11
244	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE , .	07/2010	752.64 689.03	689.03	541.02	07/2013 11/2015	06/2016	35(O) 7(R)	7/9
245	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH , .	05/2011	1,961.87 -	1,961.87	1,784.85	05/2014 -	06/2016	25(O) -	8/12
246	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU , .	09/2011	1,940.13 -	1,940.13	1,888.96	09/2014 -	06/2016	21(O) -	8/13
247	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH , .	11/2011	2,127.51 -	2,127.51	2,303.03	07/2014 -	06/2016	23(O) -	6/8
248	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH , .	12/2011	1,746.65 2,228.71	2,228.71	1,475.53	08/2014 12/2015	06/2016	22(O) 6(R)	7/11
249	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH , .	01/2012	1,422.85 -	1,422.85	1,373.62	01/2015 -	06/2016	17(O) -	9/11

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
250	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE , .	03/2012	198.63 -	198.63	93.03	09/2014 -	06/2016	21(O) -	0/0
251	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH , .	03/2012	9,569.76 -	9,569.76	5,337.19	06/2015 -	06/2016	12(O) -	21/30
252	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE , .	11/2011	723.63 -	723.63	583.62	11/2014 -	06/2016	19(O) -	7/10
253	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE , .	02/2012	3,201.44 -	3,201.44	2,893.07	10/2014 -	06/2016	20(O) -	8/17
254	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH , .	12/2012	11,846.00 -	11,846.00	5,419.00	06/2017 -	06/2017	0(O) -	22/40
255	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE , .	02/2014	539.82 -	539.82	101.70	06/2016 -	06/2016	0(O) -	8/11
256	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE , .	02/2014	908.08 -	908.08	116.00	06/2016 -	06/2016	0(O) -	9/18
257	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE , .	02/2014	196.58 -	196.58	17.60	02/2016 -	06/2016	4(O) -	7/17
258	PARE HYDRO ELECTRIC PROJECT - [N18000045]NPEPCO,ARUNACHAL PRADESH , .	12/2008	573.99 1,262.27	1,262.27	1,085.04	08/2013 07/2016	07/2016	35(O) 0(R)	28/38
259	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE , .	05/2014	303.07 -	303.07	19.70	07/2016 -	07/2016	0(O) -	2/9
260	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE , .	01/2015	203.28 -	203.28	18.38	07/2017 -	07/2017	0(O) -	0/5
261	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI , .	05/2015	780.33 -	780.33	0.90	07/2017 -	07/2017	0(O) -	0/0
262	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE , .	07/2015	2,247.37 -	2,247.37	16.00	07/2018 -	07/2018	0(O) -	0/0
263	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA , .	03/2012	9,395.18 -	9,395.18	5,749.00	11/2016 -	08/2017	9(O) -	26/27
264	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND , .	07/2012	1,527.00 -	1,527.00	142.00	08/2017 -	08/2017	0(O) -	0/9
265	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE , .	03/2013	514.20 -	514.20	291.60	06/2015 -	08/2016	14(O) -	7/10
266	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE , .	06/2012	1,909.24 -	1,909.24	989.03	06/2015 -	08/2016	14(O) -	3/5
267	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , .	05/2014	829.98 -	829.98	64.00	08/2016 -	08/2016	0(O) -	0/4
268	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , .	02/2014	12,532.44 -	12,532.44	2,378.00	08/2018 -	08/2018	0(O) -	17/17
269	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , .	07/2006	1,657.00 2,978.86	2,978.86	1,545.54	02/2016 09/2019	09/2019	43(O) 0(R)	10/21
270	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , .	03/2013	11,638.55 -	11,638.55	4,611.00	09/2017 -	09/2017	0(O) -	19/41

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
271	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL, .	09/2014	1,381.84 -	1,381.84	153.00	09/2019 -	09/2019	0(O) -	3/4
272	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE, .	03/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017	0(O) -	0/0
273	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR, .	01/2007	5,353.00 -	5,353.00	5,206.93	05/2014 -	09/2017	40(O) -	0/4
274	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH, .	04/2012	9,750.89 -	9,750.89	4,382.19	12/2016 -	09/2017	9(O) -	25/28
275	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM, .	07/1998	368.72 1,381.71	1,381.71	930.00	07/2006 10/2016	10/2016	123(O) 0(R)	5/13
276	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL, GUJARAT, .	02/2014	378.71 -	378.71	113.10	10/2016 -	10/2016	0(O) -	8/11
277	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE, .	01/2015	871.62 -	871.62	3.10	10/2017 -	10/2017	0(O) -	0/5
278	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL, GUJARAT, .	10/2015	315.00 -	315.00	-	10/2016 -	10/2016	0(O) -	0/1
279	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR, .	01/2009	3,642.04 -	5,497.72	4,351.15	01/2016 -	11/2016	10(O) -	7/9
280	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE, .	01/2014	374.63 -	374.63	16.00	04/2016 -	11/2016	7(O) -	0/0
281	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE, .	05/2014	522.29 -	522.29	47.20	11/2016 -	11/2016	0(O) -	1/12
282	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL, MULTI STATE, .	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/3
283	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN, .	07/2015	307.18 -	307.18	0.80	11/2017 -	11/2017	0(O) -	0/0
284	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH, .	09/2002	3,919.59 -	7,818.68	5,367.65	09/2009 -	12/2018	111(O) -	2/3
285	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, TAMIL NADU, .	05/2005	1,779.29 2,159.07	2,159.07	1,903.55	11/2008 03/2012	12/2016	97(O) 57(R)	20/22
286	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND, .	11/2006	2,978.48 3,846.30	3,846.30	2,661.00	03/2013 -	12/2018	69(O) -	2/15
287	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND, .	08/2008	2,491.58 -	2,491.58	775.12	06/2013 -	12/2019	78(O) -	4/8
288	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE, .	10/2008	4,824.12 -	4,824.12	4,204.18	10/2012 -	12/2016	50(O) -	7/11
289	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE, .	02/2009	11,130.19 13,762.80	13,762.80	11,225.70	08/2013 12/2017	12/2017	52(O) 0(R)	17/26
290	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL, .	04/2010	4,404.57 -	4,404.57	2,357.96	01/2015 -	12/2016	23(O) -	8/16
291	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL, MULTI STATE, .	02/2010	2,144.00 -	2,144.00	2,253.90	12/2012 -	12/2016	48(O) -	11/23
292	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL, MULTI STATE, .	07/2010	1,272.80 -	1,272.80	1,228.13	11/2012 -	12/2016	49(O) -	8/13

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
293	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , .	03/2012	7,921.47 -	7,921.47	4,779.00	09/2016 -	12/2016	3(O) -	28/33
294	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , .	03/2013	2,514.88 -	2,514.88	1,043.56	12/2015 -	12/2016	12(O) -	15/18
295	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , .	07/2013	3,363.12 -	3,363.12	965.00	12/2016 -	12/2016	0(O) -	15/18
296	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN, BIHAR , .	05/2015	436.68 -	436.68	434.29	12/2016 -	12/2016	0(O) -	0/1
297	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH , .	09/2003	6,285.33 -	18,063.89	7,934.88	09/2010 -	-	-	0/0
298	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , .	02/2010	232.34 -	232.34	213.29	06/2012 -	-	-	1/4
299	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , .	10/2011	487.49 639.46	639.46	431.02	06/2014 03/2016	-	-	10/12
300	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH , .	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
	Total		294,222.64 -	341,026.11	171,005.75				772/1247
	HEAVY INDUSTRY								
301	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE , .	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	.00				0/0
	HEALTH AND FAMILY WELFARE								
302	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI , .	11/2013	196.70 -	196.70	157.61	01/2016 -	01/2016	0(O) -	0/0
303	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI , .	09/2013	444.70 -	444.70	268.07	12/2015 -	03/2016	3(O) -	0/0
304	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH , .	10/2013	159.50 -	159.50	118.95	11/2013 -	03/2016	28(O) -	0/0
305	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM , .	07/2012	175.57 -	175.57	106.20	12/2014 -	03/2016	15(O) -	0/0
306	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA , .	09/2014	505.58 -	505.58	9.74	03/2018 -	03/2018	0(O) -	0/0
307	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI , .	12/2013	204.44 -	204.44	21.73	05/2017 -	05/2017	0(O) -	0/0
308	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI , .	08/2014	293.65 -	293.65	36.53	05/2017 -	05/2017	0(O) -	0/0
309	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL , .	12/2014	168.90 -	168.90	0.05	05/2017 -	05/2017	0(O) -	0/0
310	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI , .	02/2013	414.11 -	414.11	210.91	11/2013 -	11/2014	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		2,563.15 -	2,563.15	929.79				0/0
	<u>RAILWAYS</u>								
311	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE , .	09/1998	247.66 3,500.00	3,500.00	645.61	05/2008 -	-	-	0/0
312	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT , .	04/2013	1,266.89 -	1,266.89	-	-	-	-	0/0
313	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345],UTTAR PRADESH , .	04/1997	836.26 -	1,072.51	888.87	-	-	-	0/0
314	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL , .	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
315	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE , .	04/2006	96.16 -	260.16	240.21	-	01/2015	-	0/0
316	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA , .	12/1994	124.43 -	925.30	712.02	-	02/2014	-	0/0
317	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE , .	02/1996	240.00 -	579.37	599.40	-	02/2012	-	0/0
318	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE , .	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
319	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE , .	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
320	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE , .	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
321	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL , .	04/1983	36.80 36.38	1,336.57	255.55	-	03/2019	-	0/0
322	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA , .	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144(O) -	0/0
323	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR,ANDHRA PRADESH , .	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
324	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , .	03/1997	677.97 1,062.36	1,651.54	1,621.40	-	03/2018	-	0/0
325	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE , .	04/1997	218.24 236.41	645.00	309.19	-	03/2015	-	0/0
326	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL , .	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	-	0/0
327	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR , .	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
328	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA , .	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0
329	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE , .	04/1999	744.71 -	744.71	576.86	-	03/2016	-	1/1
330	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE , .	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
331	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR , .	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
332	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND , .	04/1996	768.87 -	768.87	682.31	- 03/2010	03/2010	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
333	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH , .	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	- -	0/0
334	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH , .	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	- -	0/0
335	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU , .	09/2006	343.17 -	914.98	846.18	- -	03/2016	- -	0/0
336	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM , .	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	- -	0/0
337	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR , .	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	- -	0/0
338	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH , .	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
339	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA , .	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
340	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH , .	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
341	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA , .	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
342	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM , .	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
343	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR , .	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
344	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM , .	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
345	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN , .	04/2008	829.74 -	829.74	96.76	03/2015 -	03/2015	- -	0/0
346	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND , .	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
347	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM , .	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
348	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM , .	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0
349	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND , .	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
350	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE , .	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	- -	0/0
351	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL , .	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	- -	0/0
352	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA , .	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108(O) -	0/0
353	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , .	04/2012	252.00 -	886.65	-	- -	03/2018	- -	0/0
354	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND , .	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	- -	0/0
355	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL , .	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
356	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL , .	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
357	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU , .	04/2007	247.00 -	951.24	619.87	- -	03/2015	-	0/0
358	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA , .	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
359	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE , .	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
360	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE , .	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
361	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE , .	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
362	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE , .	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
363	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM , .	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
364	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM , .	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
365	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA , .	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11(O) -	0/0
366	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE , .	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	-	0/0
367	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE , .	04/2011	299.60 -	299.60	-	03/2017 -	03/2017	0(O) -	0/0
368	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE , .	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
369	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE , .	04/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	0(O) -	0/0
370	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , .	04/2007	98.74 -	203.00	227.84	- -	03/2015	-	0/0
371	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH , .	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
372	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA , .	04/1999	166.16 -	325.50	348.66	02/2009 02/2009	04/2016	86(O) 86(R)	0/0
373	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM , .	09/1997	1,500.00 4,996.19	4,996.19	4,102.70	04/2008 12/2011	06/2017	110(O) 66(R)	0/0
374	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH , .	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	-	0/0
375	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU , .	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
376	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , .	09/2007	687.20 -	950.00	890.25	03/2010 -	06/2017	87(O) -	0/0
377	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL , .	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(O) -	0/0
378	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL , .	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
379	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA , .	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
380	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA , .	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
381	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , .	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	-	0/0
382	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL , .	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	-	0/0
383	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA , .	04/2010	203.40 -	203.40	153.29	- -	09/2015	-	0/0
384	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR , .	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	-	0/0
385	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , .	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	-	0/0
386	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA , .	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
387	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA , .	04/2000	133.41 207.00	318.33	322.05	03/2009 03/2009	10/2016	91(O) 91(R)	0/0
388	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL , .	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
389	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , .	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O) -	0/0
390	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , .	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
391	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND , .	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138(O) -	0/0
392	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL , .	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
393	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , .	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
394	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR , .	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
395	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , .	09/2006	324.90 -	385.54	328.12	03/2010 -	12/2017	93(O) -	0/0
396	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL , .	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
397	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL , .	04/2010	3,951.98 -	3,161.58	850.74	03/2016 -	12/2020	57(O) -	0/0
398	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL , .	04/2010	2,913.51 -	2,095.20	614.96	03/2016 -	12/2018	33(O) -	0/0
399	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , .	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	- -	0/0
400	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA , .	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
401	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , .	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	- -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
402	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA , .	04/2012	632.68 -	816.55	130.80	03/2016 -	12/2017	21(O) -	0/0
403	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA , .	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
404	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , .	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
405	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE , .	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
406	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH , .	04/1995	304.00 -	631.78	235.92	12/2012 -	-	-	0/0
407	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , .	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
408	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR,MAHARASHTRA , .	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
409	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA , .	02/1997	295.00 -	1,289.92	1,092.98	- -	-	-	0/0
410	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN , .	02/1997	410.08 -	410.08	297.58	- -	-	-	0/0
411	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE , .	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
412	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU , .	02/1997	155.55 -	800.00	800.70	- -	-	-	0/0
413	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA , .	04/1997	227.00 997.58	2,135.00	117.24	- -	-	-	0/0
414	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND , .	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005 -	-	-	0/0
415	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR , .	04/1997	501.69 501.69	1,043.56	819.19	03/2012 -	-	-	0/0
416	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , .	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
417	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , .	04/1997	162.87 -	541.00	158.58	- -	-	-	0/0
418	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE , .	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
419	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU , .	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
420	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , .	03/1998	280.00 -	1,122.00	889.95	- -	-	-	0/6
421	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH , .	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
422	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL , .	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
423	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , .	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
424	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL , .	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
425	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE , .	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
426	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA , .	04/1996	138.00 -	1,382.78	2.81	-	-	-	0/0
427	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA , .	04/1994	470.21 -	1,995.25	355.02	-	-	-	0/0
428	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA , .	04/1996	301.64 -	1,185.64	577.84	-	-	-	0/0
429	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR , .	04/2003	528.65 -	324.66	227.03	-	-	-	0/0
430	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR , .	04/2002	322.95 -	341.41	325.36	03/2012	-	-	0/0
431	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND , .	04/2002	459.91 -	418.17	260.67	-	-	-	0/0
432	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR , .	04/2001	406.92 -	339.00	204.83	-	-	-	0/0
433	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR , .	04/2003	218.19 -	343.00	216.17	-	-	-	0/0
434	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE , .	04/2005	230.03 -	230.03	172.58	-	-	-	0/0
435	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA , .	04/1998	183.23 -	1,202.70	185.46	02/2015	-	-	0/0
436	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA , .	04/2005	810.78 -	810.80	160.80	-	-	-	0/0
437	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH , .	04/2003	136.62 -	360.00	357.91	12/2007	-	-	0/0
438	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR , .	04/1996	332.92 -	477.88	498.37	03/2012	-	-	0/0
439	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA , .	04/2006	378.56 -	791.59	5.41	-	-	-	0/0
440	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND , .	03/1997	261.70 -	360.00	242.62	02/2006	-	-	0/0
441	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH , .	07/2006	743.00 -	732.81	743.47	03/2008	-	-	0/0
442	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU , .	09/2007	404.19 -	1,383.45	457.88	-	-	-	0/0
443	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE , .	12/2006	170.00 -	485.00	417.70	03/2011	-	-	0/0
444	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU , .	09/2006	125.00 -	490.00	67.57	-	-	-	0/0
445	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU , .	09/2006	456.00 -	1,080.00	194.61	-	-	-	0/0
446	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL , .	04/2007	1,106.62 -	1,106.62	244.99	12/2010	-	-	0/0
447	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL , .	04/2010	2,298.42 -	1,655.68	38.32	03/2014	-	-	0/0
448	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN , PPP (BOT)	04/2008	653.19 -	653.55	258.78	03/2014	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
449	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN , .	04/2008	516.23 732.06	516.23	597.72	03/2014 -	-	-	0/0
450	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND , .	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
451	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL , .	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
452	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL , .	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
453	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH , .	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
454	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT , .	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
455	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT , .	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
456	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT , .	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
457	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT , .	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
458	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH , .	03/2013	307.00 -	307.00	-	- -	-	-	0/0
459	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE , .	03/2007	243.78 -	243.78	30.05	- -	-	-	0/0
460	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH , .	03/2008	195.64 -	195.64	94.11	- -	-	-	0/0
461	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH , .	03/2012	199.75 -	199.75	76.08	- -	-	-	0/0
462	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE , .	03/2013	295.00 -	494.92	4.22	- -	-	-	0/0
463	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH , .	03/2013	643.00 -	643.00	-	- -	-	-	0/0
464	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN , .	04/2012	246.08 -	246.08	4.20	- -	-	-	0/0
465	CHOTTADEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE , .	04/2007	1,347.26 -	1,347.26	164.55	- -	-	-	0/0
466	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE , .	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
467	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT , .	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
468	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT , .	04/2012	376.59 -	376.59	4.58	- -	-	-	0/0
469	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT , .	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
470	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , .	04/1994	320.66 913.48	913.48	457.67	- -	-	-	0/0
471	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , .	04/2011	446.00 -	685.17	206.59	- -	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
472	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , .	04/2010	279.40 -	279.40	249.02	-	-	-	0/0
473	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE , .	04/2011	2,082.75 -	3,500.00	54.23	-	-	-	0/0
474	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , .	04/2013	236.93 -	262.00	0.41	-	-	-	0/0
475	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN , .	04/2013	822.00 -	822.00	-	-	-	-	0/0
476	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , .	04/2013	323.00 -	323.00	-	-	-	-	0/0
477	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN , .	04/2013	456.00 -	855.16	557.82	-	-	-	0/0
478	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , .	04/2010	739.65 -	872.22	794.11	-	-	-	0/0
479	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN , .	04/2011	239.73 -	179.32	75.76	-	-	-	0/0
480	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , .	04/2011	213.39 -	218.39	23.63	-	-	-	0/0
481	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , .	04/2012	288.97 -	288.97	1.09	-	-	-	0/0
482	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , .	04/2013	242.09 -	242.09	0.39	-	-	-	0/0
483	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL , .	04/2010	267.37 -	434.00	35.90	-	-	-	0/0
484	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL , .	04/2011	289.64 -	760.00	0.09	-	-	-	0/0
485	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , .	04/2008	490.80 -	490.80	0.39	-	-	-	0/0
486	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR , .	04/2008	620.57 -	620.57	-	-	-	-	0/0
487	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR , .	04/2008	445.25 -	445.25	1.14	-	-	-	0/0
488	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE , .	04/2008	415.67 -	415.67	14.00	-	-	-	0/0
489	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR , .	04/2008	326.20 -	326.20	1.68	-	-	-	0/0
490	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR , .	04/1999	175.69 -	325.00	258.31	-	-	-	0/0
491	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR , .	04/2006	285.07 -	378.56	111.87	-	-	-	0/0
492	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECOR,BIHAR , .	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
493	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR , .	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
494	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR , .	04/2008	678.62 -	239.32	17.17	-	-	-	0/0
495	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR , .	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
496	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR , .	04/2008	304.41 -	304.41	0.19	-	-	-	0/0

Sector Wise Details									
(December 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
497	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR , .	04/2008	192.56 -	192.56	0.38	-	-	-	0/0
498	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR , .	04/2008	281.30 -	281.30	0.58	-	-	-	0/0
499	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , .	04/2004	372.14 -	355.81	294.07	-	-	-	0/0
500	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR , .	04/2009	470.00 -	470.00	40.00	-	-	-	0/0
501	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR , .	04/2013	213.01 -	367.17	17.19	-	-	-	0/0
502	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU , .	04/2008	446.87 -	528.00	2.96	-	-	-	0/0
503	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE , .	04/2008	523.52 -	1,200.00	2.07	-	-	-	0/0
504	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , .	04/2013	839.00 -	1,500.00	0.01	-	-	-	0/0
505	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU , .	04/1999	198.68 -	556.64	268.56	-	-	-	0/0
506	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU , .	04/1998	271.24 -	520.00	462.69	-	-	-	0/0
507	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE , .	04/2008	822.39 -	1,280.83	1,031.83	-	-	-	0/0
508	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE , .	04/2007	270.14 -	346.15	14.61	-	-	-	0/0
509	KUMBALAM-TURAVUR - [N22000191]SR,KERALA , .	04/2011	252.96 -	252.96	1.48	-	-	-	0/0
510	ERODE-PALANI - [N22000199]SR,TAMIL NADU , .	04/2008	288.57 -	603.22	1.64	-	-	-	0/0
511	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , .	04/2008	164.41 -	450.00	16.97	-	-	-	0/0
512	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , .	04/2006	191.72 -	222.95	112.40	-	-	-	0/0
513	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , .	04/2010	189.24 -	189.24	1.52	-	-	-	0/0
514	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL , .	04/2009	573.78 -	573.78	166.89	-	-	-	0/0
515	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE , .	04/2011	601.43 -	800.00	0.69	-	-	-	0/0
516	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , .	04/1987	406.99 -	406.99	141.55	-	-	-	0/0
517	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , .	04/2007	450.00 -	450.00	7.91	-	-	-	0/0
518	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , .	04/2010	172.03 -	172.03	5.86	-	-	-	0/0
519	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , .	04/2013	915.98 -	915.98	0.09	-	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
520	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , .	04/2011	288.35 -	288.35	9.60	- -	-	-	0/0
521	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , .	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
522	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE , .	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
523	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , .	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
524	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , .	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
525	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , .	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
526	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , .	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
527	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , .	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
528	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , .	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
529	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , .	04/2008	499.30 -	2,501.05	84.11	- -	-	-	0/0
530	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , .	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0
531	BARIAPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , .	04/2007	450.55 -	450.55	13.53	- -	-	-	0/0
532	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , .	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
533	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , .	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
534	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , .	04/2011	193.44 -	193.44	53.01	- -	-	-	0/0
535	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , .	04/2011	175.80 -	175.80	1.46	- -	-	-	0/0
536	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , .	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
537	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE , .	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
538	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE , .	04/2003	337.96 -	337.96	61.36	- -	-	-	0/0

Sector Wise Details

(December 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
539	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , .	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
540	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA , .	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
541	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , .	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
542	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , .	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
543	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA , .	04/2012	297.85 -	297.85	7.17	- -	-	-	0/0
544	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , .	04/2011	913.00 -	1,801.01	1.47	- -	-	-	0/0
545	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , .	04/2007	179.65 -	1,350.91	380.62	- -	-	-	0/0
546	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA , .	04/2010	377.93 -	986.30	100.76	- -	-	-	0/0
547	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , .	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
548	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE , .	04/2013	723.00 -	723.00	-	- -	-	-	0/0
549	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE , .	04/2012	1,054.35 -	1,054.35	8.06	- -	-	-	0/0
550	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE , .	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
551	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , .	04/2012	923.23 -	923.23	1.01	- -	-	-	0/0
552	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH , .	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
553	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , .	04/2012	377.44 -	377.44	7.50	- -	-	-	0/0
554	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB , .	04/2009	396.04 -	369.00	188.93	- -	-	-	0/0
555	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , .	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
556	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH , .	04/2013	654.00 -	654.00	-	- -	-	-	0/0
557	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , .	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
558	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , .	04/2012	287.00 -	576.18	3.40	- -	-	-	0/0
559	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH , .	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
560	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , .	04/2007	336.91 -	336.91	144.25	- -	-	-	0/0
561	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , .	04/2013	558.00 -	692.43	-	- -	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
562	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , .	04/2013	296.00 -	466.65 -	-	-	-	-	0/0
563	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , .	04/2011	562.74 -	832.47 -	0.94	-	-	-	0/0
564	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE , .	04/2007	970.34 -	1,743.00 -	359.06	-	-	-	0/0
565	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , .	04/2011	341.05 -	348.85 -	0.34	-	-	-	0/0
566	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]JNR,DELHI , .	04/2012	295.68 -	295.68 -	0.86	-	-	-	0/0
567	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , .	04/2013	829.00 -	829.00 -	-	-	-	-	0/0
568	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA , .	04/2011	390.60 -	390.60 -	4.69	-	-	-	0/0
569	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , .	04/2011	1,313.48 -	1,313.48 -	5.13	-	-	-	0/0
570	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , .	04/2010	337.49 -	337.50 -	0.21	-	-	-	0/0
571	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE , .	04/2008	2,050.00 -	2,050.00 -	194.45	-	-	-	0/0
572	HARIDWAR-LAKSAR - [N22000289]JNR,UTTARAKHAND , .	04/2012	219.83 -	329.97 -	2.38	-	-	-	0/0
573	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]JNR,MULTI STATE , .	04/2010	338.54 -	338.54 -	129.14	-	-	-	0/0
574	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]JNR,MULTI STATE , .	04/2008	162.96 -	162.96 -	143.62	-	-	-	0/0
575	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]JNR,HARYANA , .	04/2013	400.00 -	400.00 -	-	-	-	-	0/0
576	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]JNR,MULTI STATE , .	04/2013	876.00 -	876.00 -	-	-	-	-	0/0
577	UNCHAHAR-AMETHI - [N22000294]JNR,UTTAR PRADESH , .	04/2012	380.00 -	380.00 -	1.38	-	-	-	0/0
578	QADIAN-BEAS - [N22000295]JNR,PUNJAB , .	04/2011	205.22 -	205.22 -	1.54	-	-	-	0/0
579	CHANDIGARH-BADDI NL - [N22000296]JNR,MULTI STATE , .	04/2007	328.14 -	328.14 -	0.31	-	-	-	0/0
580	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA , .	04/2010	2,127.00 -	2,127.00 -	325.00	-	-	-	0/0
581	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , .	04/2011	146.75 -	167.50 -	0.32	-	-	-	0/0
582	GADAG-WADI NL - [N22000299]SWR,KARNATAKA , .	04/2013	1,117.00 -	1,922.00 -	1.89	-	-	-	0/0
583	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , .	04/2013	327.25 -	367.77 -	-	-	-	-	0/0
584	MONIGRAM- NIMTITA - [N22000301]JNR,MULTI STATE , .	04/2012	250.93 -	250.93 -	0.14	-	-	-	0/0
585	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]JNR,WEST BENGAL , .	04/2012	255.64 -	255.64 -	-	-	-	-	0/0
586	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU , .	04/1999	460.94 -	1,030.00 -	-	01/1999 -	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
587	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , .	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
588	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , .	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
589	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , .	04/2012	285.57 -	279.54	1.38	01/1999 -	-	-	0/0
590	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL , .	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
591	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , PPP (BOT)	03/2012	1,503.71 -	1,503.71	169.75	-	-	-	0/0
592	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA , .	03/2011	679.27 -	1,111.99	60.31	-	-	-	0/0
593	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA , .	03/2013	858.67 -	837.33	1.15	-	-	-	0/0
594	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA , .	03/2006	201.00 -	230.00	218.67	-	-	-	0/0
595	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA , .	03/2011	165.16 -	234.71	137.01	03/2015 -	-	-	0/0
596	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH , .	04/2014	182.92 -	197.73	-	-	-	-	0/0
597	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU , .	04/2011	190.10 -	190.10	33.19	-	-	-	0/0
598	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA , .	03/2015	1,900.00 -	1,900.00	-	-	-	-	0/0
599	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE , .	05/2015	600.00 -	600.00	-	-	-	-	0/0
600	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE , .	03/2015	1,830.00 -	1,830.00	-	-	-	-	0/0
601	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE , .	05/2015	860.43 -	860.43	-	-	-	-	0/0
602	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR , .	05/2015	380.00 -	380.00	-	-	-	-	0/0
603	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN , .	05/2015	873.71 -	873.71	-	-	-	-	0/0
604	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA , .	05/2015	400.00 -	400.00	-	-	-	-	0/0
605	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA , .	03/2015	960.00 -	960.00	-	-	-	-	0/0
606	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE , .	03/2015	1,618.00 -	1,618.00	-	-	-	-	0/0
607	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE , .	05/2015	720.00 -	720.00	-	-	-	-	0/0
	Total		172,717.67 -	298,204.43	93,596.86				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
608	SILCHAR-UDARBANDH (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM , .	12/2003	157.47 -	157.47	-	09/2007 -	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
609	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR , .	12/2003	300.00 -	300.00	-	10/2008 -	-	-	0/0
610	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH , .	12/2003	251.03 -	251.03	-	10/2008 -	-	-	0/0
611	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL , .	12/2003	225.00 -	225.00	-	07/2008 -	-	-	0/0
612	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
613	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
614	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	-	-	0/0
615	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA , .	03/2005	557.00 -	557.00	932.30	02/2010 -	-	-	0/0
616	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	-	-	2/2
617	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH , .	05/2009	572.30 -	572.30	761.40	10/2011 -	-	-	0/0
618	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , .	09/2010	946.00 -	946.00	-	-	-	-	3/3
619	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU , PPP (BOT)	09/2010	1,655.00 -	1,655.00	641.78	09/2013 -	-	-	0/0
620	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
621	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND , .	08/2010	625.07 -	625.07	-	01/2013 -	-	-	0/0
622	KUNDUPUR-SURATHKAL AND MANGLORE - [N24000146]NHAI,KARNATAKA , PPP (BOT)	09/2010	671.00 -	671.00	-	-	-	-	2/3
623	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA , .	04/2011	807.00 -	807.00	-	10/2014 -	-	-	0/0
624	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA , .	12/2010	453.00 -	453.00	487.90	-	-	-	1/1
625	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA , .	12/2010	480.00 -	480.00	438.00	-	-	-	2/2
626	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA , .	11/2010	680.00 -	680.00	-	-	-	-	2/2
627	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT , PPP (BOT)	03/2011	785.50 -	785.50	919.56	08/2013 -	-	-	0/3
628	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA , .	02/2011	226.00 -	226.00	-	02/2014 -	-	-	0/0
629	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR , .	12/2011	325.00 -	325.00	160.20	05/2014 -	-	-	0/0
630	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND , .	02/2012	398.00 -	398.00	-	02/2014 -	-	-	0/0
631	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH , .	10/2011	209.00 -	209.00	-	01/2013 -	-	-	0/0
632	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA , .	11/2011	909.00 -	909.00	844.10	05/2014 -	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
633	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH , .	07/1999	635.90 -	635.90	-	07/2012 -	-	-	0/0
634	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA , .	04/2011	682.00 -	682.00	34.81	10/2013 -	-	-	0/0
635	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH , .	10/2012	250.50 -	250.50	-	10/2014 -	-	-	0/0
636	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH , .	09/2013	606.00 -	606.00	-	- -	-	-	0/0
637	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA , .	04/2014	1,123.17 -	1,123.17	-	- -	-	-	0/0
638	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249]PWD,TELANGANA , .	03/2011	218.31 -	339.82	-	12/2015 -	12/2015	0(0) -	0/3
639	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , .	03/2015	298.33 -	298.33	-	- -	-	-	0/4
640	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA , .	03/2015	184.05 -	184.05	-	- -	-	-	0/4
641	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , .	03/2015	280.16 -	280.16	-	- -	-	-	0/4
642	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , .	12/2014	201.12 201.00	201.12	14.71	02/2015 -	-	-	0/4
643	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , .	03/2015	175.03 -	175.00	-	- -	-	-	0/1
644	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , .	02/2015	266.00 -	266.00	24.24	- -	-	-	0/4
645	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , .	07/2015	314.43 -	314.43	-	- -	-	-	0/0
646	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , .	10/2015	289.60 -	289.60	-	- -	-	-	0/0
647	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , .	12/2011	156.26 227.00	156.26	50.94	- -	-	-	0/0
648	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , .	03/2011	185.82 292.00	185.82	189.37	- -	-	-	0/0
649	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , .	10/2014	213.47 -	213.47	20.70	03/2015 -	03/2015	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
650	REHABILITATION AND UPGRADE OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , .	10/2014	298.34 -	298.34	5.26	03/2015 -	03/2015	-	0/0
651	REHABILITATION AND UPGRADE OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , .	11/2014	262.54 -	262.54	10.14	03/2015 -	03/2015	-	0/0
652	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , .	12/2010	169.26 -	169.26	111.73	12/2012 -	12/2012	-	0/0
653	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , .	12/2014	394.20 -	394.20	96.04	-	-	-	0/0
654	REHABILITATION AND UPGRADE OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , .	11/2015	485.44 -	485.44	-	12/2015 -	12/2015	0(0) -	0/0
655	REHABILITATION AND UPGRADE OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , .	03/2015	422.34 -	422.34	8.89	03/2015 -	03/2015	-	0/0
656	REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , .	03/2015	435.90 -	435.90	15.50	-	-	-	0/0
657	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , .	01/2015	279.68 -	279.68	29.39	-	-	-	0/0
658	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , .	11/2014	463.65 546.00	463.65	256.48	-	-	-	0/0
659	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , .	11/2014	573.96 605.00	605.00	198.10	-	-	-	0/0
660	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , .	10/2015	480.21 -	480.21	-	-	-	-	0/0
661	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , .	10/2014	269.22 -	269.22	27.00	01/2015 -	01/2015	-	0/0
662	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , .	10/2014	257.09 -	257.09	15.17	01/2015 -	01/2015	-	0/0
663	REHABILITATION AND UPGRADE TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , .	10/2013	278.87 -	278.87	-	05/2014 -	05/2014	-	0/0
664	REHABILITATION AND UPGRADE TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , .	01/1991	376.52 -	376.52	171.16	04/2014 -	04/2014	-	0/0
665	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , .	02/2015	383.40 -	383.40	131.09	03/2015 -	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
666	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM , .	08/2010	186.96 -	186.96	132.80	- -	-	-	0/0
667	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , .	11/2010	624.41 -	624.41	219.50	03/2011 -	03/2011	-	0/0
668	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , .	12/2011	156.63 276.00	276.00	140.75	02/2012 -	02/2012	-	0/0
669	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , .	08/2010	193.69 -	193.69	122.00	10/2010 -	10/2010	-	0/0
670	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , .	11/2010	305.49 -	305.49	122.11	03/2011 -	03/2011	-	0/0
671	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , .	03/2012	207.03 -	207.03	102.67	05/2012 -	05/2012	-	0/0
672	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM , .	04/2013	151.59 -	151.59	7.19	08/2013 -	08/2013	-	0/0
673	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , .	04/2013	166.27 -	166.27	7.89	08/2013 -	08/2013	-	0/0
674	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , .	01/2013	182.28 -	182.00	49.42	02/2013 -	02/2013	-	0/0
675	WIDENING OF 2(TWO) LANING OF LONGLENG- CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , .	12/2010	1,296.00 -	1,296.00	557.84	02/2011 -	02/2011	-	0/0
676	CONSTN FOR FOUR LANING OF BABATPUR- VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , .	03/2015	629.74 -	629.74	-	- -	-	-	0/0
677	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , .	01/2015	225.81 -	225.81	-	- -	-	-	0/0
678	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR , .	11/2005	240.00 -	240.00	295.50	11/2008 -	11/2008	-	0/0
679	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , .	02/2015	483.38 -	483.38	45.64	- -	-	-	0/0
680	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , .	02/2015	616.36 -	616.36	29.09	- -	-	-	0/0
681	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , .	02/2015	486.74 -	486.74	90.17	- -	-	-	0/0
682	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , .	06/2015	390.51 -	390.51	-	02/2015 -	02/2015	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
683	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , .	01/1991	675.00 -	675.00 -	-	-	-	-	0/0
684	CONST.OF 4 LANES WITH PAVED SHOULDER OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , .	03/2015	312.79 -	312.79 -	10.19	-	-	-	0/0
685	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , .	07/2014	319.80 -	319.80 -	56.97	-	-	-	0/0
686	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , .	12/2015	766.36 -	766.36 -	12.08	-	-	-	0/0
687	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , .	01/2011	264.16 -	264.16 -	323.00	-	-	-	0/0
688	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , .	11/2015	847.02 -	847.02 -	299.55	-	-	-	0/0
689	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , .	11/2015	889.24 -	889.24 -	388.43	-	-	-	0/0
690	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , .	08/2015	257.80 -	257.00 -	-	05/2015 -	05/2015	-	0/0
691	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , .	12/2015	578.38 -	578.38 -	9.18	-	-	-	0/0
692	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , .	03/2015	789.83 -	789.83 -	72.79	-	-	-	0/0
693	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18 -	-	-	-	-	0/0
694	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , .	07/2015	1,282.94 -	1,282.94 -	-	-	-	-	0/0
695	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , .	01/1991	225.02 -	225.02 -	-	-	-	-	0/0
696	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , .	01/1991	223.30 -	223.30 -	-	-	-	-	0/0
697	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , .	01/1991	520.01 -	520.01 -	-	-	-	-	0/0
698	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA , .	09/2015	414.00 -	414.00 -	-	-	-	-	0/0
699	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH , .	06/2015	583.79 -	583.79 -	-	-	-	-	0/0
700	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,WEST BENGAL , .	10/2015	531.13 -	531.13 -	-	-	-	-	0/0

Sector Wise Details

(December 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
701	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]MEGA, WEST BENGAL , .	10/2015	361.15 -	361.15 -	-	-	-	-	0/0
702	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM , .	01/1991	289.99 -	289.99 -	-	-	-	-	0/0
703	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA , PPP (BOT)	07/2015	1,885.74 -	1,885.74 -	-	-	-	-	0/0
704	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA , .	10/2015	593.26 -	593.26 -	-	-	-	-	0/0
705	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA , .	12/2015	649.50 -	649.50 -	-	-	-	-	0/0
706	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH, GOA , .	10/2015	936.40 -	936.40 -	-	-	-	-	0/0
707	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP, MADHYA PRADESH , .	11/2011	670.82 -	670.82 -	-	02/2015 -	02/2015	-	0/0
708	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72 -	-	-	-	-	0/0
709	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA , .	08/2015	505.00 -	505.00 -	-	-	-	-	0/0
710	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20 -	-	-	-	-	0/0
711	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI, MADHYA PRADESH , PPP (BOT)	06/2015	1,012.90 -	1,012.90 -	-	-	-	-	0/0
712	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA , .	06/2015	845.24 -	845.24 -	-	-	-	-	0/0
713	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI, TAMIL NADU , .	01/1991	285.00 -	285.00 -	-	01/2008 -	11/2011	-	0/0
714	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH , .	03/2015	795.76 -	795.76 -	-	-	-	-	0/0
715	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH , .	03/2015	794.30 -	794.30 -	-	-	-	-	0/0
716	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN , .	09/2012	511.00 -	511.00 -	-	10/2013 -	09/2015	-	0/0
717	NAGPUR - KONDHALI - [N24000472]MEGA, MAHARASHTRA , .	09/2005	168.00 -	168.00 -	279.92	06/2006 -	12/2008	-	0/0
718	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR , .	08/2015	556.07 -	556.07 -	-	-	-	-	0/0
719	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, ANDAMAN & NICOBAR ISLANDS , .	09/2015	273.06 -	273.06 -	-	-	-	-	0/0
720	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR , .	12/2015	1,041.10 -	1,041.10 -	-	-	-	-	0/0
721	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]MEGA, BIHAR , .	08/2015	814.04 -	814.04 -	-	-	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
722	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , .	09/2014	479.00	479.00	345.50	-	-	-	0/0
723	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA , .	12/2015	752.28	752.28	-	-	-	-	0/0
724	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,WEST BENGAL , .	12/2015	1,423.96	1,423.96	-	-	-	-	0/0
725	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00	1,393.00	-	-	-	-	0/0
726	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , .	03/2015	928.83	928.83	-	-	-	-	0/0
727	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	01/1991	1,388.00	1,388.00	-	-	-	-	0/0
728	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH , .	12/2015	596.67	596.67	-	-	-	-	0/0
729	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR , .	08/2015	322.09	322.09	-	-	-	-	0/0
730	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH , .	12/2015	509.13	509.13	-	-	-	-	0/0
731	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH , .	03/2015	810.22	810.22	-	-	-	-	0/0
732	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79	1,583.79	-	-	-	-	0/0
733	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR , .	01/1991	642.41	642.41	-	-	-	-	0/0
734	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR , .	01/1991	1,167.45	1,167.45	-	-	-	-	0/0
735	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH , .	12/2015	726.67	726.67	-	-	-	-	0/0
736	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , .	12/2014	207.88	207.88	-	-	-	-	0/0
737	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , .	12/2015	773.98	773.98	-	-	-	-	0/0
738	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00	1,665.00	-	-	-	-	0/0
739	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUJAR - [N24000516]MORTH,GOA , .	12/2015	819.95	819.95	-	-	-	-	0/0
740	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA , .	12/2015	479.20	479.20	-	-	-	-	0/0
741	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR , .	08/2015	399.54	399.54	-	-	-	-	0/0
742	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR , .	01/1991	478.35	478.35	-	-	-	-	0/0
743	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN , .	08/2015	275.90	275.90	-	-	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
744	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , .	08/2015	854.80 -	854.80 -	-	-	-	-	0/0
745	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR , .	08/2015	516.13 -	516.13 -	-	-	-	-	0/0
746	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , .	06/2015	892.17 -	892.17 -	14.70	-	-	-	0/0
747	ROHTAK - BAWAL(APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA , .	02/2010	650.00 -	650.00 -	830.97	-	-	-	0/0
748	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , .	06/2015	899.21 -	899.21 -	13.13	-	-	-	0/0
749	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00 -	761.19	07/2008 -	07/2008	-	0/0
750	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , .	12/2014	207.88 -	207.88 -	-	-	-	-	0/0
751	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , .	01/1991	154.62 -	154.62 -	-	-	-	-	0/0
752	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , .	01/1991	319.68 -	319.68 -	-	-	-	-	0/0
753	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH , .	12/2003	155.00 -	201.66 -	142.60	09/2008 -	01/2016	88(O) -	0/0
754	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN , .	12/2003	275.00 -	250.39 -	270.76	10/2008 -	01/2016	87(O) -	0/0
755	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM , .	12/2003	198.16 -	198.16 -	242.40	04/2008 01/2016	01/2016	93(O) 0(R)	0/0
756	NALBARI T BIJINI (AS-7) - [N24000048]NHAI,ASSAM , .	12/2003	208.00 230.00	208.00 -	295.20	04/2008 01/2017	01/2017	105(O) 0(R)	0/0
757	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54 -	351.23	05/2013 -	01/2016	32(O) -	0/0
758	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU , PPP (BOT)	06/2011	535.00 -	535.00 -	913.00	12/2013 -	01/2016	25(O) -	0/0
759	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT , PPP (BOT)	09/2010	805.39 -	805.39 -	543.70	03/2013 -	01/2016	34(O) -	0/0
760	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00 -	609.00	02/2014 -	01/2016	23(O) -	0/0
761	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00 -	882.72	03/2014 -	01/2016	22(O) -	0/0
762	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN , .	01/2014	177.32 -	177.32 -	86.65	01/2016 -	01/2016	0(O) -	0/0
763	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN , .	01/2014	368.15 -	368.15 -	153.02	01/2016 -	01/2016	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
764	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , .	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	0(O) -	0/0
765	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , .	10/2015	179.82 -	179.82	-	01/2019 -	01/2019	0(O) -	0/0
766	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB , .	01/2014	523.85 -	523.85	74.12	01/2016 -	01/2016	0(O) -	0/0
767	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU , .	07/2014	401.11 -	401.11	1.75	01/2017 -	01/2017	0(O) -	0/0
768	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH , .	04/2014	351.34 -	351.34	4.77	01/2016 -	01/2016	0(O) -	0/0
769	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH , .	06/2014	301.04 -	301.04	51.79	01/2016 -	01/2016	0(O) -	0/0
770	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH , .	04/2014	495.78 -	495.78	-	01/2016 -	01/2016	0(O) -	0/0
771	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , .	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
772	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , .	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	0(O) -	0/0
773	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2016 -	01/2016	0(O) -	0/0
774	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]MEGA,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	2,434.74	10/2011 -	01/2016	51(O) -	0/0
775	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH , .	11/2015	867.66 -	867.66	374.03	11/2015 -	01/2016	2(O) -	0/0
776	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]MEGA,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,055.00	374.03	11/2015 -	01/2016	2(O) -	0/0
777	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2019 -	01/2016	-36(O) -	0/0
778	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	830.19	01/2018 -	01/2018	0(O) -	0/0
779	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM , .	12/2003	264.72 -	264.72	307.92	06/2008 -	02/2016	92(O) -	0/0
780	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	468.41	05/2010 -	02/2016	69(O) -	0/0
781	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	2,821.52	09/2012 -	02/2016	41(O) -	2/3
782	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN , PPP (BOT)	06/2010	792.06 -	792.06	1,983.00	12/2012 -	02/2016	38(O) -	0/0
783	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	390.01	07/2014 -	02/2017	31(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
784	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN , PPP (ANNUITY)	03/2012	333.51 -	333.51	271.60	09/2014 -	02/2016	17(O) -	0/0
785	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , .	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	0(O) -	0/0
786	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH , .	02/2015	241.61 -	241.61	23.83	02/2017 -	02/2017	0(O) -	0/1
787	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , .	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017	0(O) -	0/0
788	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , .	07/2014	251.55 -	251.55	-	02/2015 -	02/2017	24(O) -	0/1
789	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN , .	08/2015	538.08 -	538.08	-	02/2018 -	02/2018	0(O) -	0/0
790	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA , .	08/2015	723.54 -	723.54	-	02/2018 -	02/2018	0(O) -	0/0
791	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN , .	08/2015	482.27 -	482.27	0.88	02/2018 -	02/2018	0(O) -	0/0
792	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , .	03/2013	257.80 -	257.80	-	02/2016 -	02/2016	0(O) -	0/0
793	2-LANING OF SHILLONG - NONGSTOIN SECTION OF NH 44 AND NONGSTOIN - TURA STATE ROAD UNDER PHASE 'A' OF - [N24000390]PWD,MEGHALAYA , .	12/2010	1,494.48 -	1,494.48	2,090.00	02/2011 -	02/2011	-	0/0
794	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , .	11/2010	470.20 -	470.20	165.89	02/2011 -	02/2011	-	0/0
795	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , .	05/2011	176.22 -	176.22	106.61	02/2018 -	02/2018	0(O) -	0/0
796	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , .	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
797	4 LANING OF GOMTI CHAURAH - UDAIPUR - [N24000455]MEGA,RAJASTHAN , PPP (BOT)	03/2012	914.50 -	914.50	850.53	10/2015 -	02/2016	4(O) -	0/0
798	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM , .	12/2003	280.00 -	361.00	389.31	02/2009 -	03/2016	85(O) -	0/0
799	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM , .	12/2003	199.81 -	385.13	194.33	04/2009 -	03/2016	83(O) -	0/0
800	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM , .	12/2003	167.64 -	167.64	231.27	11/2008 -	03/2016	88(O) -	0/0
801	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM , .	12/2003	155.04 -	280.13	184.97	11/2008 -	03/2016	88(O) -	0/0
802	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM , .	12/2003	200.00 -	200.00	234.99	04/2009 -	03/2016	83(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
803	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM , .	12/2003	195.00 -	195.00	276.28	06/2008 -	03/2016	93(O) -	0/0
804	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM , .	12/2003	237.80 -	237.80	369.05	06/2008 -	03/2016	93(O) -	0/0
805	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR , .	12/2003	332.94 -	332.94	488.87	09/2008 -	03/2016	90(O) -	0/0
806	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM , .	12/2003	196.00 -	331.23	298.40	07/2009 -	03/2016	80(O) -	0/0
807	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH , .	12/2003	348.16 -	348.16	322.70	09/2007 -	03/2016	102(O) -	0/0
808	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA , PPP (BOT)	03/2005	940.00 -	940.00	1,415.36	07/2012 -	03/2016	44(O) -	0/0
809	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN , PPP (BOT)	11/2009	795.00 -	795.00	1,605.89	05/2012 -	03/2016	46(O) -	0/0
810	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,182.58	04/2013 -	03/2016	35(O) -	0/0
811	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	30.00	08/2012 -	03/2017	55(O) -	0/0
812	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2016	33(O) -	0/0
813	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,474.52	08/2014 -	03/2016	19(O) -	0/0
814	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	830.97	11/2013 -	03/2016	28(O) -	0/0
815	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	282.68	08/2013 -	03/2017	43(O) -	0/0
816	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	622.74	10/2013 -	03/2016	29(O) -	0/0
817	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR , PPP (BOT)	10/2011	375.09 -	375.09	428.32	04/2014 -	03/2016	23(O) -	0/0
818	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	543.94	11/2013 -	03/2016	28(O) -	0/0
819	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA , PPP (BOT)	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26(O) -	0/0
820	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	646.75	08/2013 -	03/2016	31(O) -	0/0
821	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN , .	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37(O) -	0/0
822	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN , PPP (BOT)	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	03/2016	21(O) -	0/0
823	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,125.40	06/2014 -	03/2016	21(O) -	0/0
824	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA , PPP (BOT)	04/2012	484.19 -	484.19	455.26	10/2014 -	03/2016	17(O) -	0/0
825	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR , PPP (BOT)	07/2012	356.40 -	356.40	343.50	07/2014 -	03/2016	20(O) -	0/0
826	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE , PPP (ANNUITY)	04/2012	624.00 -	624.00	333.72	04/2014 -	03/2016	23(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
827	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE , PPP (BOT)	12/2011	942.69 -	942.69	286.80	06/2014 -	03/2016	21(O) -	0/0
828	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE , PPP (BOT)	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7(O) -	0/0
829	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU , PPP (BOT)	06/2013	1,287.95 -	1,287.95	715.50	11/2015 -	03/2017	16(O) -	0/0
830	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN , .	03/2014	240.10 -	240.10	137.69	03/2016 -	03/2016	0(O) -	0/0
831	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , .	12/2013	177.18 -	177.18	-	03/2016 -	03/2016	0(O) -	0/4
832	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA , .	12/2013	158.65 -	158.65	-	03/2016 -	03/2016	0(O) -	0/4
833	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , .	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016	0(O) -	1/4
834	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , .	01/2014	340.00 -	340.00	-	03/2016 -	03/2016	0(O) -	0/4
835	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAAGAR DAM SECT - [N24000245]PWD,TELANGANA , .	01/2014	270.00 -	270.00	50.85	03/2016 -	03/2016	0(O) -	1/4
836	FOUR LANING FROM BISWANATH CHARALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , .	03/2015	829.00 -	829.00	-	03/2018 -	03/2018	0(O) -	0/4
837	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , .	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018	0(O) -	0/4
838	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , .	01/2014	282.41 -	282.41	31.64	03/2016 -	03/2016	0(O) -	0/0
839	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN , .	09/2015	567.51 -	567.51	-	03/2018 -	03/2018	0(O) -	0/0
840	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , .	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	0(O) -	0/0
841	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , .	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017	0(O) -	0/0
842	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , .	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0
843	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL , .	01/1991	322.00 -	322.00	-	03/2018 -	03/2018	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
844	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP, UTTAR PRADESH , .	10/2013	317.76 -	317.76	-	03/2017 -	03/2017	0(O) -	0/0
845	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH , .	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	0(O) -	0/0
846	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI, UTTAR PRADESH , .	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(O) -	0/0
847	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI, UTTAR PRADESH , .	09/2015	664.53 -	664.53	-	03/2018 -	03/2018	0(O) -	0/0
848	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI, UTTAR PRADESH , .	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(O) -	0/0
849	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, HARYANA , .	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
850	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH , .	09/2015	785.78 -	785.78	-	03/2018 -	03/2018	0(O) -	0/0
851	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN , .	09/2012	511.00 -	511.00	-	10/2013 -	03/2013	-	0/0
852	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH , .	11/2015	628.45 -	628.45	-	03/2018 -	03/2018	0(O) -	0/0
853	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH , .	09/2015	934.46 -	934.46	-	03/2018 -	03/2018	0(O) -	0/0
854	FOUR LANING OF ORISSA/CHHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH , .	02/2013	1,232.00 -	1,232.00	632.63	08/2015 -	03/2016	7(O) -	0/0
855	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH , .	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016	0(O) -	0/0
856	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH , .	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7(O) -	0/0
857	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA , .	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31(O) -	0/0
858	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM , .	12/2003	245.00 -	245.00	214.17	03/2008 04/2016	04/2016	97(O) 0(R)	0/0
859	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI, ASSAM , .	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016	94(O) 0(R)	0/0
860	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE , .	12/2003	232.45 -	232.45	284.69	09/2010 -	04/2016	67(O) -	0/0
861	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,026.65	07/2013 -	04/2016	33(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
862	GHABIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32(O) -	0/0
863	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	477.26	03/2014 -	04/2017	37(O) -	0/0
864	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	777.06	04/2015 -	04/2016	12(O) -	0/0
865	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN , PPP (BOT)	10/2013	677.79 -	677.79	682.13	04/2016 -	04/2016	0(O) -	0/0
866	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , .	03/2015	297.00 -	297.00	36.02	-	04/2018	-	0/1
867	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , .	05/2014	497.89 -	497.89	49.78	04/2017 -	04/2017	0(O) -	0/3
868	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN , .	10/2014	206.12 -	206.12	0.74	04/2017 -	04/2017	0(O) -	0/0
869	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN , .	10/2014	264.72 -	264.72	-	04/2017 -	04/2017	0(O) -	0/0
870	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA , .	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
871	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , .	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12(O) -	0/0
872	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	-	04/2018 -	04/2018	0(O) -	0/0
873	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN , .	12/2003	275.00 -	281.31	148.55	02/2010 -	05/2017	87(O) -	0/0
874	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,784.75	06/2015 -	05/2016	11(O) -	0/0
875	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE , PPP (BOT)	02/2011	580.43 -	580.43	221.08	08/2013 -	05/2017	45(O) -	0/0
876	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	05/2016	20(O) -	0/0
877	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	448.14	06/2015 -	05/2017	23(O) -	0/0
878	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN , .	01/2014	158.04 -	158.04	81.84	12/2015 -	05/2016	5(O) -	0/0
879	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , .	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24(O) -	0/4
880	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , .	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018	0(O) -	0/4
881	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , .	03/2015	194.11 -	194.11	-	05/2018 -	05/2018	0(O) -	0/4
882	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN , .	11/2014	279.14 -	279.14	-	05/2017 -	05/2017	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
883	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH , .	05/2015	261.09 -	261.09	-	05/2017 -	05/2017	0(O) -	0/0
884	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , .	11/2011	704.26 -	704.26	-	05/2015 -	05/2015	-	0/0
885	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , .	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	0(O) -	0/0
886	2 LANING FROM KANUBARI TO START OF BOGIBEEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , .	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017	0(O) -	0/0
887	SHAHDL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , .	06/2015	532.49 -	532.49	-	05/2017 -	05/2017	0(O) -	0/0
888	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , .	01/1991	208.87 -	208.87	-	05/2016 -	05/2016	0(O) -	0/0
889	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , .	01/1991	229.41 -	229.41	-	05/2018 -	05/2018	0(O) -	0/0
890	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , .	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13(O) -	0/0
891	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , .	03/2015	235.08 -	235.08	28.86	05/2018 -	05/2018	0(O) -	0/4
892	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , .	02/2015	327.32 -	327.32	-	05/2017 -	05/2017	0(O) -	0/0
893	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU , PPP (BOT)	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56(O) -	0/0
894	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,570.55	11/2011 -	06/2016	55(O) -	0/0
895	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA , .	02/2010	390.56 -	390.56	-	02/2012 -	06/2013	-	0/0
896	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	862.18	03/2013 -	06/2016	39(O) -	0/0
897	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	1,472.64	07/2015 -	06/2016	11(O) -	0/0
898	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.72	07/2013 -	06/2016	35(O) -	0/0
899	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT , PPP (BOT)	12/2010	1,008.50 -	1,008.50	1,275.83	06/2013 -	06/2016	36(O) -	0/3
900	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU , .	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36(O) -	0/0
901	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	949.96	07/2013 -	06/2016	35(O) -	0/0
902	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	649.52	01/2014 -	06/2016	29(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
903	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	06/2016	25(O) -	0/0
904	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	970.44	06/2014 -	06/2016	24(O) -	0/0
905	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	875.91	03/2013 -	06/2016	39(O) -	0/0
906	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,832.80	09/2015 -	06/2016	9(O) -	0/0
907	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,467.07	12/2015 -	06/2016	6(O) -	0/3
908	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	862.73	09/2014 -	06/2016	21(O) -	0/3
909	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , .	01/2014	446.77 -	446.77	-	- -	06/2017	-	0/4
910	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , .	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24(O) -	0/4
911	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , .	10/2014	437.39 -	437.39	-	06/2018 -	06/2018	0(O) -	0/4
912	FOUR LANING OF JHANJHI UN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , .	10/2014	463.49 -	463.49	-	06/2018 -	06/2018	0(O) -	0/4
913	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , .	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/0
914	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , .	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
915	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI,TAMIL NADU , .	12/2014	451.58 -	451.58	-	06/2017 -	06/2017	0(O) -	0/0
916	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI,UTTAR PRADESH , PPP (ANNUITY)	06/2014	569.38 -	569.38	680.83	06/2016 -	06/2016	0(O) -	0/0
917	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA , .	12/2015	602.95 -	602.95	-	06/2016 -	06/2016	0(O) -	0/0
918	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]MEGA,HARYANA , PPP (BOT)	03/2013	959.25 -	959.25	523.50	06/2016 -	06/2016	0(O) -	0/0
919	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH , .	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24(O) -	0/0
920	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL , .	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018	0(O) -	0/0
921	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR , .	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
922	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , .	12/2015	927.54 -	927.54	-	06/2018 -	06/2018	0(O) -	0/0
923	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH , .	01/2016	815.28 -	815.28	-	06/2018 -	06/2018	0(O) -	0/0
924	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH , .	01/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018	0(O) -	0/0
925	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH , .	12/2015	667.00 -	667.00	-	06/2018 -	06/2018	0(O) -	0/0
926	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM , .	12/2003	175.96 -	175.96	304.17	04/2008 12/2015	07/2016	99(O) 7(R)	0/0
927	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM , .	12/2003	160.00 -	160.00	197.40	05/2008 12/2015	07/2016	98(O) 7(R)	0/0
928	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE , PPP (BOT)	02/2011	998.79 -	998.79	1,635.92	08/2013 -	07/2017	47(O) -	0/0
929	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , .	08/2014	187.79 -	187.79	-	07/2016 -	07/2016	0(O) -	0/0
930	REHABILITATION AND UPGRADATION FROM KM.425/400 TO 509/400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH , .	01/2014	361.30 -	361.30	-	07/2014 -	07/2014	-	0/1
931	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , .	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24(O) -	0/1
932	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , .	02/2015	377.83 -	377.83	-	07/2017 -	07/2017	0(O) -	0/0
933	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , .	03/2015	157.18 162.00	162.00	-	07/2015 -	07/2015	-	0/0
934	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN , .	07/2015	455.60 -	455.60	-	07/2017 -	07/2017	0(O) -	0/0
935	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA , .	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
936	4-LANING OF SOLAPUR - YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	-	07/2017 -	07/2017	0(O) -	0/0
937	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH , .	06/2016	667.00 -	667.00	-	07/2018 -	07/2018	0(O) -	0/0
938	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
939	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM , .	12/2003	217.61 309.56	309.56	370.66	04/2010 02/2016	08/2016	76(O) 6(R)	0/0
940	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	08/2016	39(O) -	0/0
941	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE , PPP (BOT)	02/2011	1,078.84 -	1,078.84	1,849.33	08/2013 -	08/2016	36(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
942	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH , .	01/2013	373.47 -	373.47	358.30	07/2014 -	08/2015	-	0/0
943	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,103.87	02/2014 -	08/2016	30(O) -	0/0
944	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , .	03/2015	309.01 -	309.01	38.55	09/2015 -	08/2017	23(O) -	0/4
945	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , .	03/2015	258.97 -	258.97	20.80	08/2015 -	08/2015	-	0/0
946	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , .	11/2015	154.14 -	154.14	2.55	08/2015 -	08/2015	-	0/0
947	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT , .	03/2014	503.16 -	503.16	52.89	08/2016 -	08/2016	0(O) -	0/0
948	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , .	01/1991	282.41 -	282.41	-	08/2016 -	08/2016	0(O) -	0/0
949	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , .	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11(O) -	0/0
950	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	227.68	08/2016 -	08/2016	0(O) -	0/0
951	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH , PPP (BOT)	02/2012	912.00 -	912.00	-	08/2016 -	08/2016	0(O) -	0/0
952	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	582.00	08/2016 -	08/2016	0(O) -	0/0
953	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA , .	04/2010	1,170.52 -	1,170.52	1,578.80	06/2012 -	08/2016	50(O) -	0/0
954	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , .	03/2015	511.83 -	511.83	-	08/2017 -	08/2017	0(O) -	0/0
955	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	453.58	05/2013 -	09/2016	40(O) -	0/0
956	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	197.31	01/2014 -	09/2016	32(O) -	0/0
957	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND , PPP (ANNUITY)	11/2011	478.00 -	478.00	275.21	10/2013 -	09/2016	35(O) -	0/0
958	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	674.20	09/2016 -	09/2016	0(O) -	0/0
959	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , .	01/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017	0(O) -	0/0
960	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA , .	05/2015	709.00 -	709.00	-	09/2017 -	09/2017	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
961	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND , .	09/2015	341.61 -	341.61 -	-	09/2017 -	09/2017 -	0(O) -	0/0
962	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN , .	09/2014	425.19 -	425.19 -	4.60	09/2016 -	09/2016 -	0(O) -	0/0
963	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH , .	09/2015	368.73 -	368.73 -	-	09/2016 -	09/2016 -	0(O) -	0/0
964	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , .	01/2012	320.48 -	320.48 -	-	08/2015 -	09/2016 -	13(O) -	0/0
965	TWO LANING OF HOJ - POTIN SECTION OF NH-229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH - [N24000419]PWD,ARUNACHAL PRADESH , .	12/2009	82.73 165.00	165.00	135.01	09/2010 -	09/2010 -	-	0/0
966	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , .	12/2009	104.00 -	201.00	109.00	09/2010 -	09/2010 -	-	0/0
967	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI,HARYANA , .	12/2012	438.75 -	438.75 -	0.63	09/2016 -	09/2016 -	0(O) -	0/0
968	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,335.12	09/2014 -	10/2016 -	25(O) -	0/0
969	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , .	03/2015	168.30 -	168.30	-	-	10/2017 -	-	0/4
970	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH , .	03/2015	271.45 -	271.45	-	10/2015 -	10/2017 -	24(O) -	0/0
971	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , .	07/2015	197.16 -	197.16	19.72	10/2018 -	10/2018 -	0(O) -	0/4
972	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , .	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016 -	0(O) -	0/0
973	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN , .	01/1991	269.26 -	269.26	-	10/2016 -	10/2016 -	0(O) -	0/0
974	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , .	01/2014	397.04 -	397.04	-	10/2016 -	10/2016 -	0(O) -	0/0
975	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , .	01/1991	218.63 -	218.63	-	10/2017 -	10/2017 -	0(O) -	0/0
976	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , .	01/1991	358.22 -	358.22	-	10/2016 -	10/2016 -	0(O) -	0/0
977	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , .	10/2013	283.45 -	283.45	-	10/2016 -	10/2016 -	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
978	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , .	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	0(O) -	0/0
979	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , .	08/2010	195.04 -	195.04	157.22	10/2010 -	10/2010	-	0/0
980	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN , .	10/2015	597.00 -	597.00	-	10/2017 -	10/2017	0(O) -	0/0
981	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	917.89	11/2016 -	11/2016	0(O) -	0/0
982	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA , .	06/2014	260.39 -	260.39	-	11/2016 -	11/2016	0(O) -	0/4
983	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , .	12/2013	220.72 -	220.72	-	11/2016 -	11/2016	0(O) -	0/4
984	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , .	01/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017	0(O) -	0/0
985	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , .	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24(O) -	0/4
986	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , .	02/2014	170.21 -	170.21	28.66	11/2014 -	11/2016	24(O) -	0/4
987	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , .	03/2015	168.39 -	168.39	-	11/2018 -	11/2018	0(O) -	0/4
988	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , .	10/2014	588.95 -	588.95	-	11/2018 -	11/2018	0(O) -	0/4
989	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , .	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24(O) -	0/0
990	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , .	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24(O) -	0/0
991	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU , .	05/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017	0(O) -	0/0
992	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU , .	11/2014	563.92 -	563.92	-	11/2016 -	11/2016	0(O) -	0/0
993	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , .	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
994	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , .	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017	0(O) -	0/0
995	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM , .	12/2003	230.00 -	230.00	202.97	06/2005 -	12/2016	138(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
996	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM , .	12/2003	212.00 -	212.00	102.85	09/2007 -	12/2016	111(O) -	0/0
997	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA , .	02/2011	193.45 -	193.45	47.41	11/2012 -	12/2016	49(O) -	0/0
998	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	39(O) -	0/0
999	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	1,699.96	03/2013 -	12/2016	45(O) -	0/0
1000	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	879.84	02/2013 -	12/2016	46(O) -	0/0
1001	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,326.02	12/2013 -	12/2016	36(O) -	0/0
1002	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	303.94	05/2013 -	12/2016	43(O) -	0/0
1003	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	604.46	07/2013 -	12/2016	41(O) -	0/0
1004	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA , PPP (BOT)	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35(O) -	0/0
1005	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2016	39(O) -	0/0
1006	BARSAAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1007	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA , PPP (BOT)	10/2013	283.25 -	283.25	176.11	10/2015 -	12/2016	14(O) -	0/0
1008	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , .	10/2014	244.30 -	244.30	-	12/2016 -	12/2016	0(O) -	0/4
1009	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH , .	07/2015	333.21 - 333.21	333.21	14.12	12/2015 -	12/2016	12(O) -	0/2
1010	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , .	12/2015	291.05 -	291.05	-	12/2015 -	12/2015	0(O) -	0/0
1011	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH , .	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12(O) -	0/0
1012	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU , .	06/2015	563.92 -	563.92	-	12/2017 -	12/2017	0(O) -	0/0
1013	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA , .	06/2015	996.37 -	996.37	-	12/2017 -	12/2017	0(O) -	0/0
1014	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , .	06/2015	641.02 -	641.02	-	12/2017 -	12/2017	0(O) -	0/0
1015	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	163.80	11/2016 -	12/2016	1(O) -	0/0
1016	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , .	12/2015	239.23 -	239.23	-	12/2017 -	12/2017	0(O) -	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1017	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , .	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
1018	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB , .	10/2015	447.29 -	447.29	-	12/2017 -	12/2017	0(O) -	0/0
	Total		248,089.13 -	250,598.57	112,808.43				16/162
	SHIPPING AND PORTS								
1019	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , .	10/2002	150.00 -	600.00	139.80	03/2006 -	01/2016	118(O) -	0/0
1020	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , .	01/2007	366.39 669.46	669.46	412.00	12/2010 -	01/2016	61(O) -	0/0
1021	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , .	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
1022	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU , .	12/2014	274.85 -	274.85	0.38	04/2017 -	04/2017	0(O) -	0/0
1023	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , .	10/2013	198.94 -	198.94	37.70	06/2017 -	06/2017	0(O) -	0/0
1024	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA , .	03/2007	245.67 373.22	409.83	360.35	04/2009 03/2010	08/2016	88(O) 77(R)	0/0
1025	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , .	02/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017	0(O) -	0/0
1026	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , .	06/2005	2,427.40 -	2,427.40	837.90	10/2008 -	-	-	0/0
	Total		4,117.75 -	5,048.81	1,788.41				0/0
	TELECOMMUNICATIONS								
1027	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , .	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20(O) -	0/0
	Total		13,334.00 -	13,334.00	1,360.00				0/0
	URBAN DEVELOPMENT								
1028	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA , .	02/2011	241.33 -	241.33	70.64	11/2014 -	-	-	0/0
1029	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB , .	02/2014	388.00 -	388.00	-	01/2015 -	-	-	0/0
1030	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU , .	12/2015	209.00 -	209.00	-	- -	-	-	0/0
1031	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU , .	04/2014	332.72 -	332.72	58.72	09/2016 01/2017	01/2017	4(O) 0(R)	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1032	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI, .	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17(O) -	0/0
1033	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA, .	02/2014	26,405.14 26,405.01	26,405.01	217.41	02/2019 -	03/2020	13(O) -	0/0
1034	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL, .	01/2009	225.81 -	225.81	138.36	06/2012 03/2016	03/2016	45(O) 0(R)	10/16
1035	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH, .	11/2012	270.83 -	270.83	-	11/2014 -	03/2016	16(O) -	0/0
1036	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD, ANDHRA PRADESH, .	06/2014	157.84 -	157.84	-	03/2017 -	03/2017	0(O) -	0/0
1037	NAGPUR METRO RAIL - [N28000085]NMRC, MAHARASHTRA, .	08/2014	8,680.00 -	8,680.00	50.91	03/2018 -	03/2018	0(O) -	0/0
1038	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI, .	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
1039	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND, .	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14(O) -	0/6
1040	BANGALORE METRO RAIL PROJECT - [N28000008]MRT, KARNATAKA, .	05/2006	6,395.00 11,609.00	13,845.01	13,427.27	06/2011 12/2015	06/2016	60(O) 6(R)	3/3
1041	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI, .	05/2009	261.85 -	261.85	-	05/2013 10/2015	06/2016	37(O) 8(R)	0/0
1042	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA, .	07/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017	-1(O) -	0/0
1043	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES (CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI, .	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
1044	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU, .	02/2009	14,600.00 14,600.00	14,600.00	11,786.98	12/2015 -	08/2016	8(O) -	1/24
1045	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI, .	06/2012	4,264.00 -	4,264.00	948.27	11/2019 -	11/2019	0(O) -	0/7
1046	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI, .	09/2011	38,585.00 -	38,585.00	19,388.91	03/2016 -	12/2016	9(O) -	0/0
1047	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH, .	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24(O) -	0/0
1048	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL, .	02/2014	156.57 -	156.57	21.12	09/2015 07/2016	12/2016	15(O) 5(R)	0/7
1049	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA, .	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(O) -	0/0
1050	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD, BIHAR, .	02/2012	171.10 -	171.10	-	09/2014 -	-	-	0/0
1051	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHA NEW DELHI - [N28000064]CPWD, DELHI, .	01/2010	162.90 -	162.90	-	07/2012 -	-	-	0/0

Sector Wise Details									
(December 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1052	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA , .	11/2012	238.43 -	238.43	-	02/2015 -	-	-	0/0
1053	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB , .	08/2005	191.24 -	191.24	-	08/2007 -	-	-	0/0
1054	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA , .	06/2010	205.00 -	205.00	-	03/2012 -	-	-	0/0
1055	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA , .	12/2012	315.00 -	315.00	3.11	06/2015 -	-	-	0/0
1056	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA , .	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
1057	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR , .	11/2006	2,727.89 -	2,727.89	-	03/2010 -	-	-	0/0
1058	REHABILITATION AND STRENGTHENING OF SEWWRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH , .	08/2007	246.90 -	246.90	-	- -	-	-	0/0
	Total		136,783.82 -	144,233.70	48,692.67				14/63
	Grand Total		1,168,413.82	1,379,878.25	589,925.05				1768/3755

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.


Summary of projects in the Flash Report for the month of December, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	787
Number of Projects completed/dropped/frozen in Current Month	17
Number of Projects elevated to the status of Major project during the current month	18
Number of Projects Added in Current Month	270
Number of Projects in Current Month	1058

Brief Analysis


Project Status with respect to Original Schedule: Out of 1058 projects, 8 projects are ahead of schedule, 261 projects are on schedule 334 projects are delayed. 425 projects do not have fixed dates of commissioning. 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

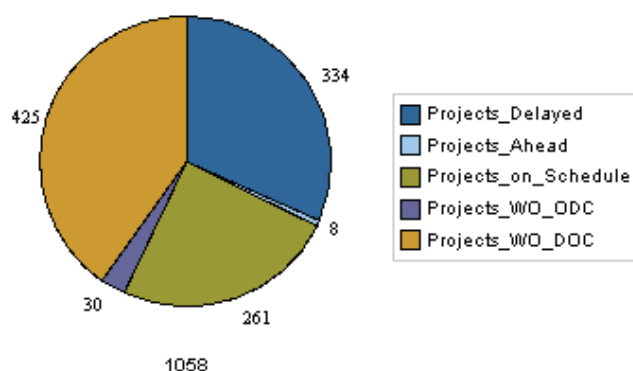

Investment Scenario

Total original cost of implementation of 1058 projects when sanctioned, was of the order of Rs. 1168413.82 crore but this was subsequently revised to Rs. 1379878.25 crore implying a cost overrun of 18.1%. The expenditure incurred on these projects till December, 2015 is Rs. 589925.05 crore, which is 42.8% of the revised cost of the projects.

Figures are in Rs. Crore

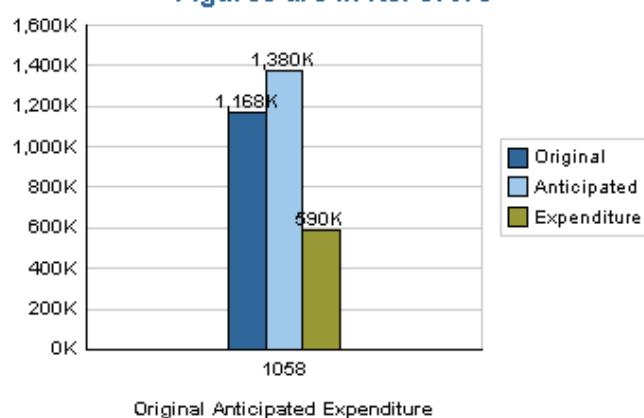

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

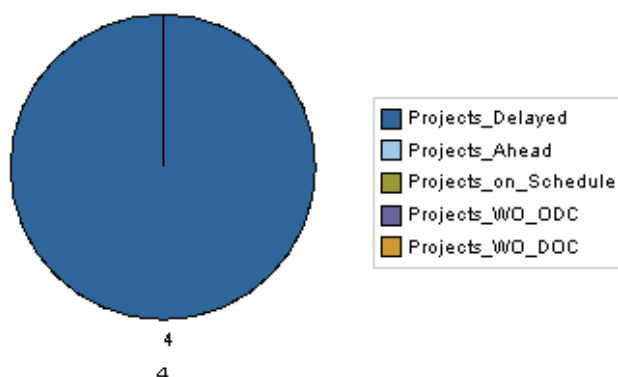

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till December, 2015 is Rs. 39268.59 crore, which is 75.6% of the revised cost of the projects.

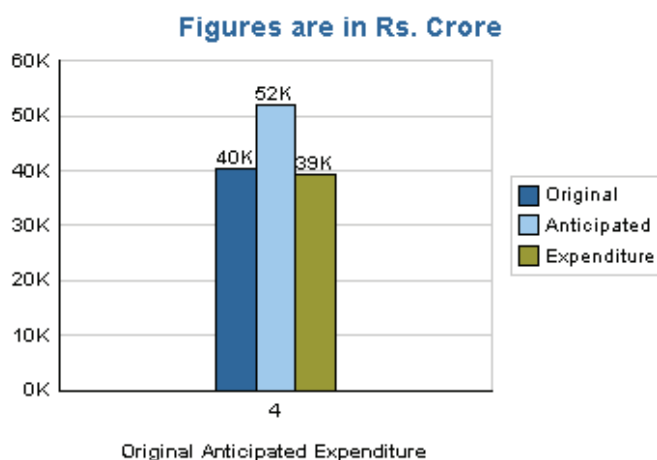

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	4
Number of Projects Delayed	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is delayed. 2 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

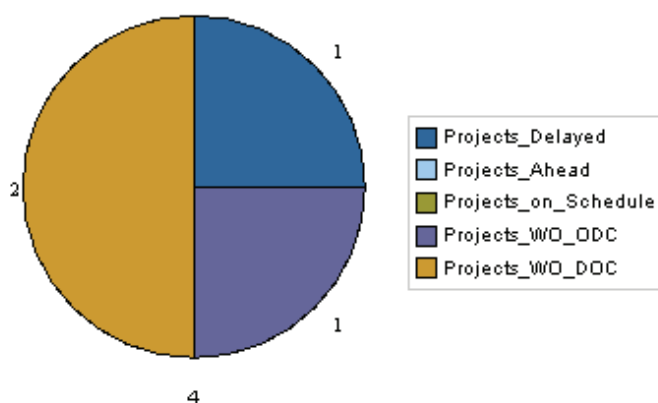

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1177.28 crore but this was subsequently anticipated to Rs. 1186.17 crore implying a cost overrun of .8%. The expenditure incurred on these projects till December, 2015 is Rs. 762.2 crore, which is 64.3% of the revised cost of the projects.

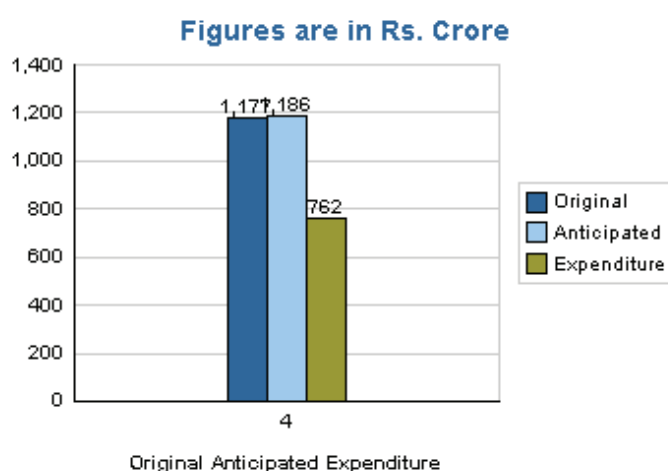

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	87
Number of Projects On Schedule	41
Number of Projects Delayed	44
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 87 projects, 1 project is ahead of schedule, 41 projects are on schedule 44 projects are delayed. 1 project does not have fixed dates of commissioning.

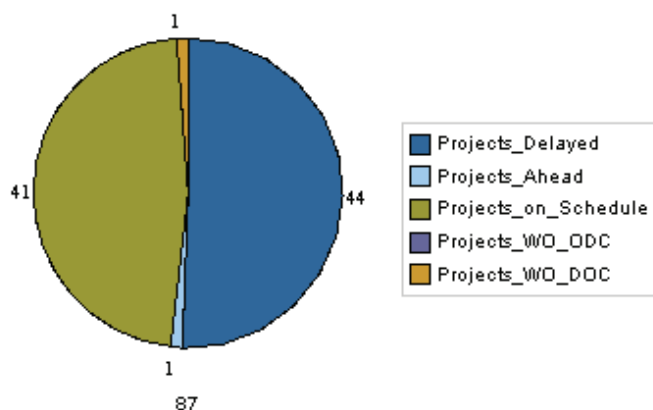

Investment Scenario

Total original cost of implementation of 87 projects when sanctioned, was of the order of Rs. 61587.45 crore but this was subsequently anticipated to Rs. 62537.14 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till December, 2015 is Rs. 15120.59 crore, which is 24.2% of the revised cost of the projects.

Figures are in Rs. Crore

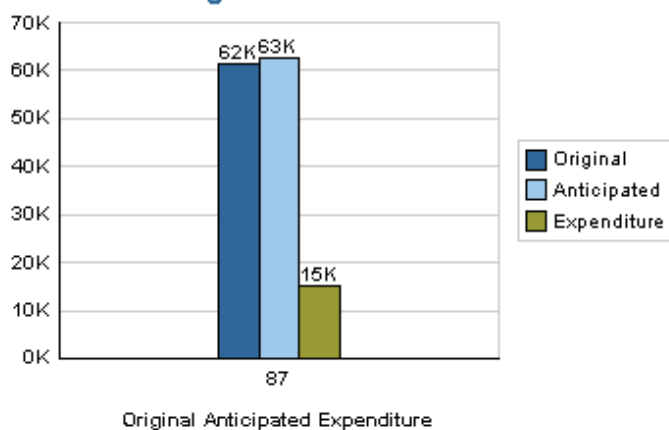

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	36
Number of Projects On Schedule	17
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning	7
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 36 projects, 17 projects are on schedule 12 projects are delayed. 7 projects do not have fixed dates of commissioning.

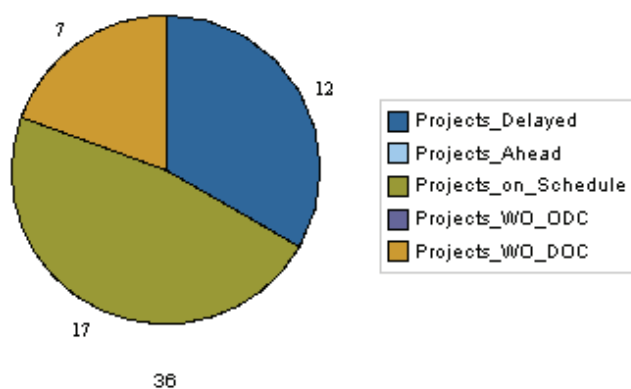

Investment Scenario

Total original cost of implementation of 36 projects when sanctioned, was of the order of Rs. 54570.11 crore but this was subsequently anticipated to Rs. 55086.01 crore implying a cost overrun of .9%. The expenditure incurred on these projects till December, 2015 is Rs. 30243.76 crore, which is 54.9% of the revised cost of the projects.

Figures are in Rs. Crore

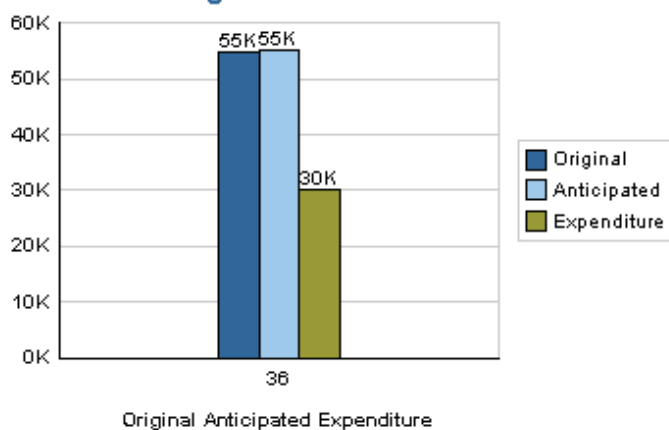

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	59
Number of Projects On Schedule	16
Number of Projects Delayed	33
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 59 projects, 3 projects are ahead of schedule, 16 projects are on schedule 33 projects are delayed. 7 projects do not have fixed dates of commissioning.

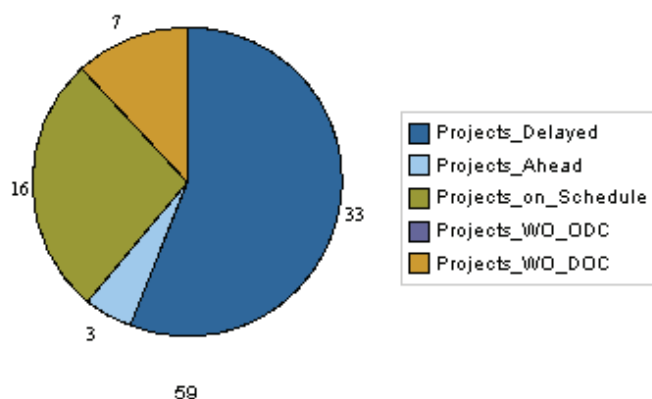

Investment Scenario

Total original cost of implementation of 59 projects when sanctioned, was of the order of Rs. 128876.79 crore but this was subsequently anticipated to Rs. 138276.44 crore implying a cost overrun of 7.3%. The expenditure incurred on these projects till December, 2015 is Rs. 65197.5 crore, which is 47.2% of the revised cost of the projects.

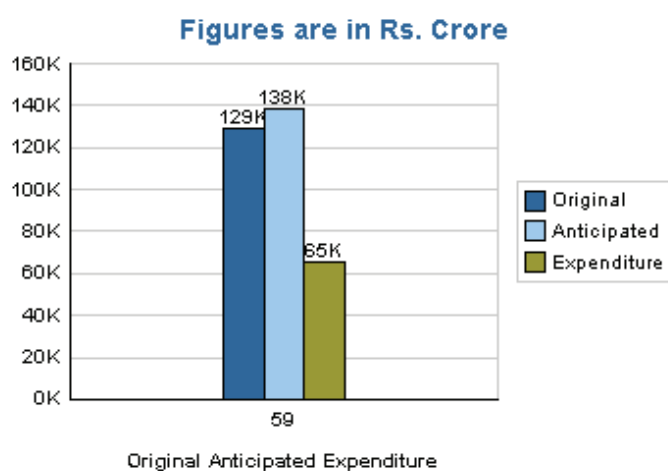

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	105
Number of Projects On Schedule	41
Number of Projects Delayed	58
Number of Projects Ahead	2

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 105 projects, 2 projects are ahead of schedule, 41 projects are on schedule 58 projects are delayed. 4 projects do not have fixed dates of commissioning.

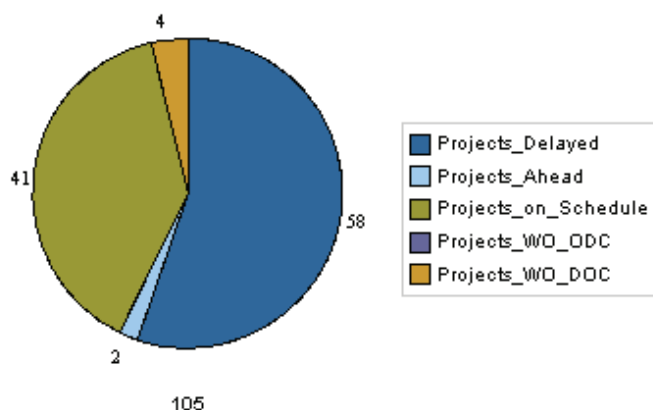

Investment Scenario

Total original cost of implementation of 105 projects when sanctioned, was of the order of Rs. 294222.64 crore but this was subsequently anticipated to Rs. 341026.11 crore implying a cost overrun of 15.9%. The expenditure incurred on these projects till December, 2015 is Rs. 171005.75 crore, which is 50.1% of the revised cost of the projects.

Figures are in Rs. Crore

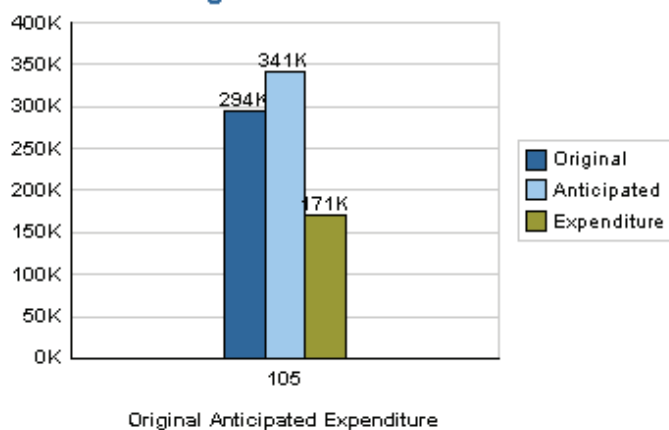

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	297
Number of Projects On Schedule	5
Number of Projects Delayed	33
Number of Projects Without Original Date of Commissioning	26
Number of Projects Without Date Of Commissioning	233


Brief Analysis

Project Status with respect to Original Schedule: Out of 297 projects, 5 projects are on schedule 33 projects are delayed. 233 projects do not have fixed dates of commissioning. 26 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

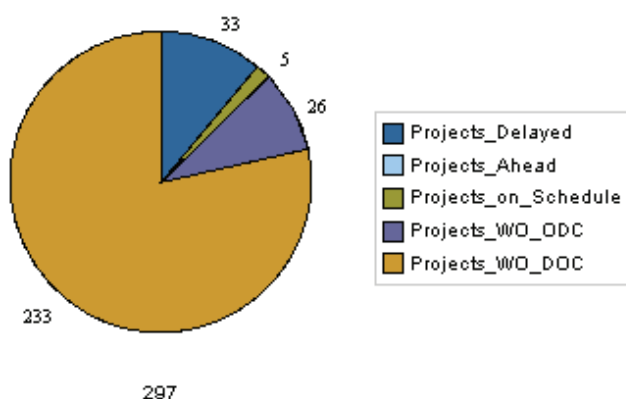

Investment Scenario

Total original cost of implementation of 297 projects when sanctioned, was of the order of Rs. 172717.67 crore but this was subsequently anticipated to Rs. 298204.43 crore implying a cost overrun of 72.7%. The expenditure incurred on these projects till December, 2015 is Rs. 93596.86 crore, which is 31.4% of the revised cost of the projects.

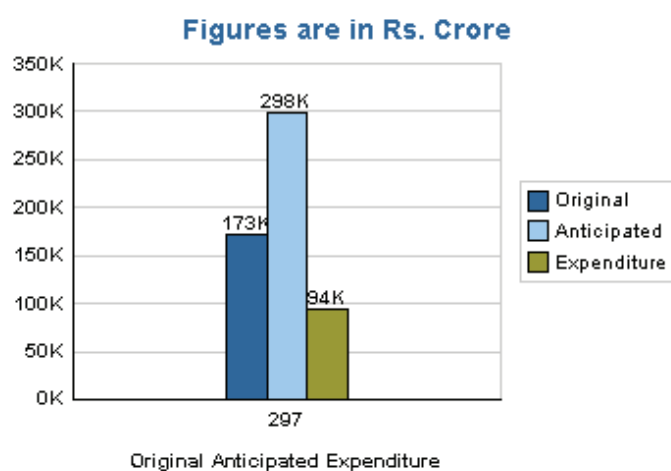

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	411
Number of Projects On Schedule	125
Number of Projects Delayed	125
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	157

Brief Analysis


Project Status with respect to Original Schedule: Out of 411 projects, 1 project is ahead of schedule, 125 projects are on schedule 125 projects are delayed. 157 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

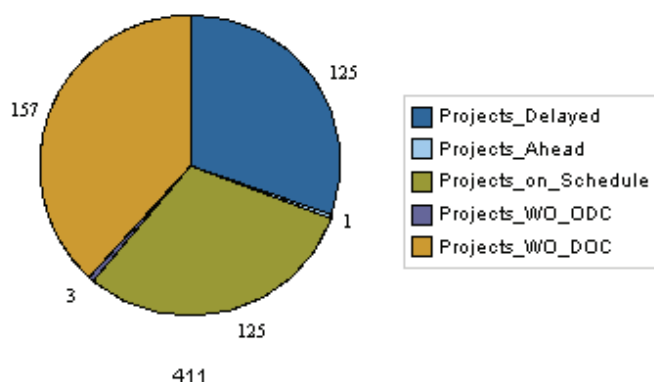

Investment Scenario

Total original cost of implementation of 411 projects when sanctioned, was of the order of Rs. 248089.13 crore but this was subsequently anticipated to Rs. 250598.57 crore implying a cost overrun of 1%. The expenditure incurred on these projects till December, 2015 is Rs. 112808.43 crore, which is 45% of the revised cost of the projects.

Figures are in Rs. Crore

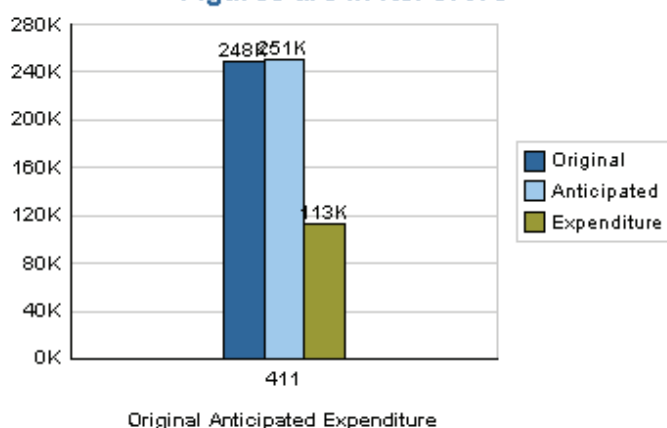

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule 3 projects are delayed. 1 project does not have fixed dates of commissioning.

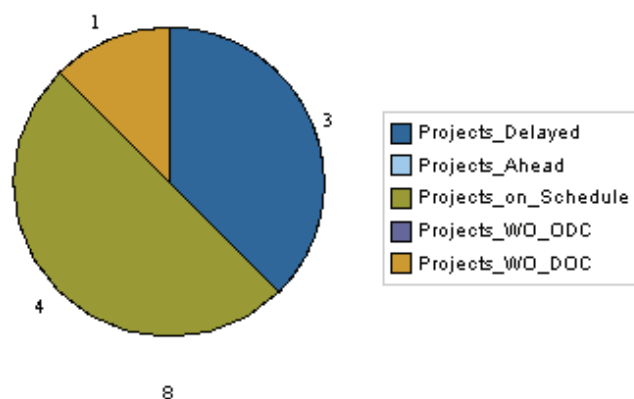

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5048.81 crore implying a cost overrun of 22.6%. The expenditure incurred on these projects till December, 2015 is Rs. 1788.41 crore, which is 35.4% of the revised cost of the projects.

Figures are in Rs. Crore

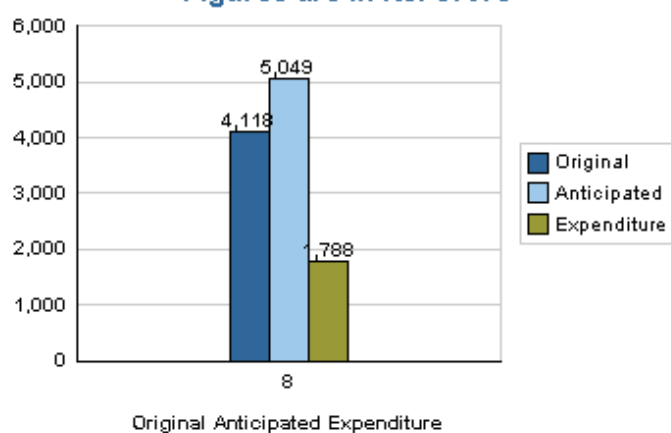

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	1
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.



Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 13334 crore but this was subsequently anticipated to Rs. 13334 crore. The expenditure incurred on these projects till December, 2015 is Rs. 1360 crore, which is 10.2% of the revised cost of the projects.

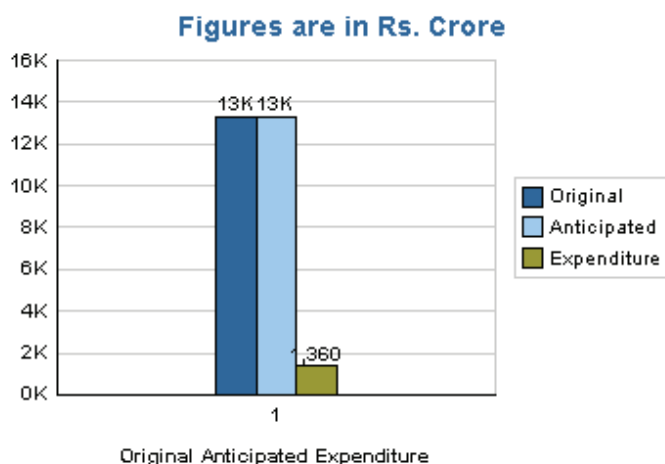

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	31
Number of Projects On Schedule	4
Number of Projects Delayed	14
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	12

Brief Analysis


Project Status with respect to Original Schedule: Out of 31 projects, 1 project is ahead of schedule, 4 projects are on schedule 14 projects are delayed. 12 projects do not have fixed dates of commissioning.

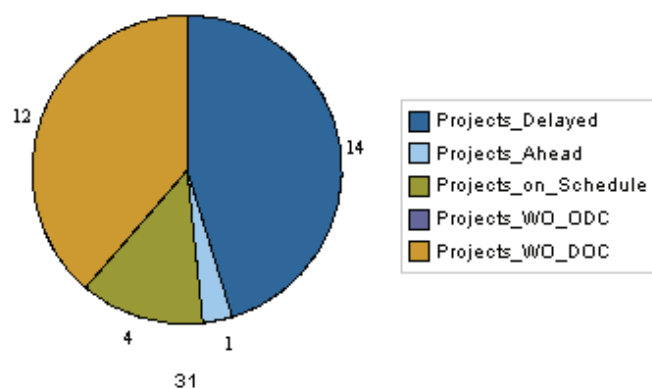

Investment Scenario

Total original cost of implementation of 31 projects when sanctioned, was of the order of Rs. 136783.82 crore but this was subsequently anticipated to Rs. 144233.7 crore implying a cost overrun of 5.4%. The expenditure incurred on these projects till December, 2015 is Rs. 48692.67 crore, which is 33.8% of the revised cost of the projects.

Figures are in Rs. Crore

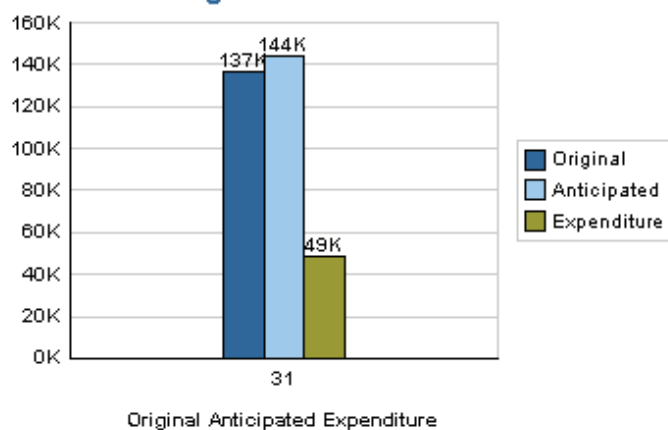

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	9
Number of Projects On Schedule	5
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 5 projects are on schedule 3 projects are delayed. 1 project does not have fixed dates of commissioning.

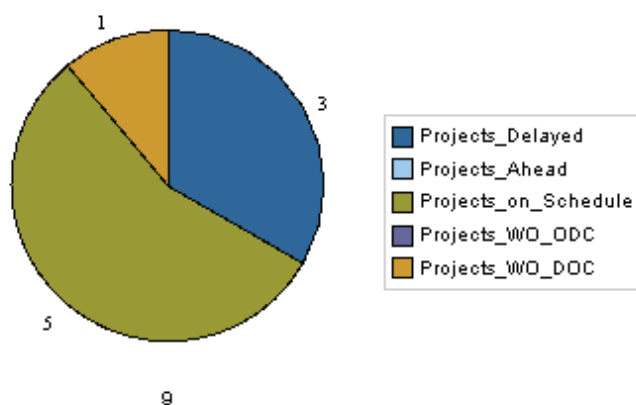

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 2563.15 crore but this was subsequently anticipated to Rs. 2563.15 crore. The expenditure incurred on these projects till December, 2015 is Rs. 929.79 crore, which is 36.3% of the revised cost of the projects.

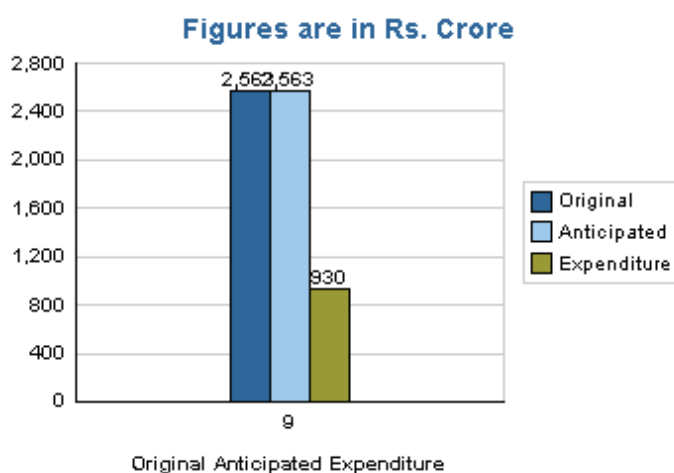

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	3
Number of Projects On Schedule	2
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are on schedule 1 project is delayed.

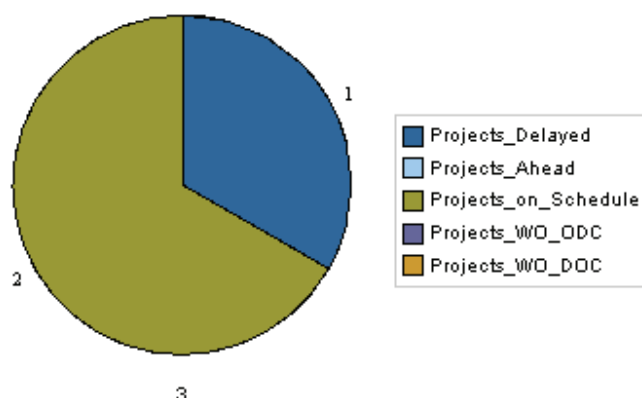

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 2555.63 crore but this was subsequently anticipated to Rs. 1875.63 cr The expenditure incurred on these projects till December, 2015 is Rs. 2.86 crore, which is .2% of the revised cost of the projects.

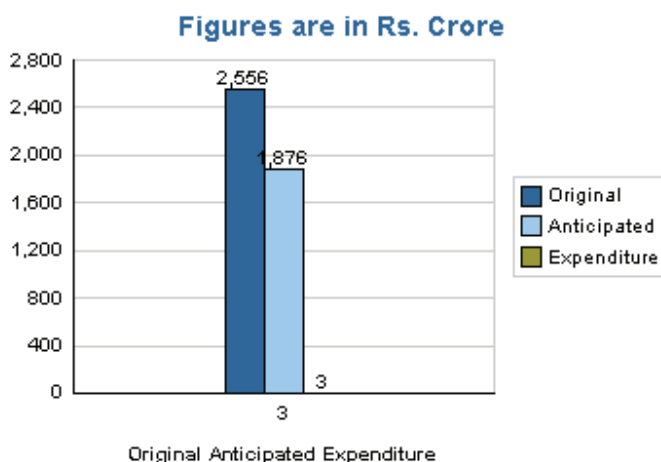

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE
 (All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	18.02
2	ANDHRA PRADESH	46	21,019.05	22,854.09	8,188.22
3	ARUNACHAL PRADESH	14	11,676.43	28,030.85	14,304.12
4	ASSAM	49	27,764.34	43,467.68	31,782.24
5	BIHAR	65	60,600.22	74,378.42	39,236.37
6	CHHATISGARH	41	88,321.18	89,633.53	48,536.93
7	D & N HAVELI	1	6,086.08	6,086.08	586.87
8	DELHI	16	49,963.05	49,963.05	21,088.49
9	GOA	8	3,925.48	3,907.87	341.03
10	GUJARAT	28	29,665.99	30,663.63	22,810.98
11	HARYANA	20	13,986.73	15,957.35	7,054.05
12	HIMACHAL PRADESH	5	8,088.55	13,907.75	6,326.34
13	JAMMU AND KASHMIR	9	25,620.25	44,540.93	23,746.74
14	JHARKHAND	44	41,826.84	44,389.67	12,460.05
15	KARNATAKA	41	71,364.99	88,854.89	32,751.03
16	KERALA	16	25,825.82	30,300.97	15,093.66
17	MADHYA PRADESH	50	44,409.65	46,089.94	10,213.37
18	MAHARASHTRA	71	1,13,214.96	1,21,960.1	35,625.98
19	MANIPUR	1	727.56	6,570.75	2,787.99
20	MEGHALAYA	6	6,970.03	8,194.91	2,752.15
21	MIZORAM	6	2,188.16	5,402.06	1,760.83
22	MULTI STATE	174	1,85,283.98	2,14,831.94	76,033.58
23	NAGALAND	3	6,420	8,757.12	568.28
24	ODISHA	49	73,735.51	83,247.71	43,993.13
25	PUNJAB	23	11,714.51	11,718.51	2,078.69
26	RAJASTHAN	57	39,614.1	40,097.55	21,653.21
27	SIKKIM	5	2,149.08	4,999.32	561.61
28	TAMIL NADU	56	68,607.63	88,218.97	57,009.18
29	TELANGANA	31	11,908.91	14,943.51	3,439.54
30	TRIPURA	9	3,776.07	7,486.36	3,351.98
31	UTTAR PRADESH	60	52,378.07	55,394.73	19,598.16
32	UTTARAKHAND	6	9,351.89	11,651.71	5,401.25
33	WEST BENGAL	46	49,641.04	62,788.63	18,770.98
TOTAL		1,058	11,68,413.82	13,79,878.25	5,89,925.05

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	21,025
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	5,129.59
3	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,367.65
4	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,934.88
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,937.7
6	VIRAMGAM-BHILDI (WR) ,GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	RAILWAYS	03/1995	2,500	3000	10,658.34
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	RAILWAYS	02/1997	295	-	1,092.98
12	KARUR-SALEM (NL) , SR	RAILWAYS	02/1997	155.55	-	800.7
13	NANDYAL-YERRAGUNTALA (NL) , SCR	RAILWAYS	03/1996	155.74	164.36	755.5
14	KANPUR KASGANJ MATHURA (GC) NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
16	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
17	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	819.19
18	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
19	KATIHAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
20	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
21	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
22	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
23	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
24	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
25	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53
26	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	301.84
27	JIND-SONEPAT (NL) , NR	RAILWAYS	01/2004	238.56	-	639.77
28	HARIDASPUR-PARADEEP (NL)	RAILWAYS	04/1996	301.64	-	577.84

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	RAJATGARH-BARANG (LD) , ECR	RAILWAYS	04/1999	166.16	-	348.66
30	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
31	KOSI BRIDGE (NL) , ECR	RAILWAYS	04/2002	322.95	-	325.36
32	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	RAILWAYS	04/2002	921	-	1,691.12
33	PATNA GANGA BRIDGE (NL) , ECR	RAILWAYS	04/2001	624.47	-	2,521.72
34	ETAWAH-MAINPURI (NL) ,NCR	RAILWAYS	04/1997	120	245.39	249.33
35	SUKINDA ROAD - ANGUL (NL) (ECOR)	RAILWAYS	04/1998	183.23	-	185.46
36	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	322.05
38	RAICHUR-GUNTAKAL (DL) (SCR)	RAILWAYS	04/2003	136.62	-	357.91
39	HARANGAJO TO MAIBANG (AS-23) , KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	389.31
40	MAIBANG TO LUMDING (AS-26) , KM.60.500 TO KM.83.400, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	167.64	-	231.27
41	MAIBANG TO LUMDING (AS-24) , KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	-	184.97
42	MAIBANG TO LUMDING (AS-27) , KM.40.000 TO KM.60.500	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	234.99

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	BIJNI TO ASSAM WB BORDER (NH-31.C) (1) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	276.28
44	BIJNI TO ASSAM /WB.BORDER (NH-31.C) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	369.05
45	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	488.87
46	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	408.55
47	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	STEEL	11/2012	313.05	-	314.87
48	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	STEEL	03/2007	149.73	173	175.89
49	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	STEEL	05/2005	768.88	1060	1,070.97
50	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	8920	9,103.96
51	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	-	160.78
52	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	4,351.15
53	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	POWER	02/2009	509.66	-	523.76
54	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	POWER	02/2010	2,144	-	2,253.9
55	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,303.03
56	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	POWER	12/2011	552.44	-	574.6

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
58	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RAILWAYS	07/2006	743	-	743.47
59	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RAILWAYS	09/2006	324.9	-	328.12
60	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	890.25
61	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
62	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
63	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
64	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
65	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
66	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
67	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
68	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
69	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
70	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
72	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.11
73	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	258.31
74	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
75	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
76	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
77	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
78	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
79	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
80	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
81	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
82	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62
83	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
84	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	RAILWAYS	04/1997	836.26	-	888.87

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	304.17
86	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	307.92
87	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
88	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	311.13
89	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	295.2
90	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.4
91	HARANGAJO TO MAIBANG, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	196	-	298.4
92	BRAHMPUTRA BRIDGE, NH NO-31	ROAD TRANSPORT AND HIGHWAYS	12/2003	217.61	309.56	370.66
93	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
94	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	284.69
95	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,415.36
96	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,821.52
97	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,605.89
98	CHENNAI-TADA (SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	365.08

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	761.4
100	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,570.55
101	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
102	INDORE-JHABUA-GUJRAT/MP	ROAD TRANSPORT AND HIGHWAYS	10/2010	1,175	-	1,182.58
103	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,055.94
104	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	862.18
105	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	1,026.65
106	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	487.9
107	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
108	INDORE-DEWAS (NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	453.58
109	NASHRI- CHANANI	ROAD TRANSPORT AND HIGHWAYS	05/2011	2,159	-	3,784.75
110	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	ROAD TRANSPORT AND HIGHWAYS	07/2010	1,813.76	-	2,393.72
111	PATNA-MUZZAFFARPUR	ROAD TRANSPORT AND HIGHWAYS	08/2010	671.3	-	879.84
112	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,275.83

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	919.56
114	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	830.97
115	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	1,911.64
116	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	ROAD TRANSPORT AND HIGHWAYS	06/2011	535	-	913
117	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,326.02
118	TIRUPATI - TIRUTHANI - CHENNAI	ROAD TRANSPORT AND HIGHWAYS	04/2011	571	-	622.74
119	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	649.52
120	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,188
121	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	882.72
122	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	428.32
123	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	604.46
124	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	543.94
125	PUNE-SHOLAPUR, PKG-II	ROAD TRANSPORT AND HIGHWAYS	09/2011	835	-	1,684
126	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	646.75

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
128	MUZAFFARNAGAR-HARIDWAR	ROAD TRANSPORT AND HIGHWAYS	09/2011	754	-	875.91
129	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,849.33
130	4-LANING OF BRAHAMPURE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,635.92
131	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	ROAD TRANSPORT AND HIGHWAYS	12/2011	1,047	-	1,125.4
132	ETAWAH CHAKERI	ROAD TRANSPORT AND HIGHWAYS	03/2013	1,573	-	1,832.8
133	AHMEDABAD TO VADODARA SECTION	ROAD TRANSPORT AND HIGHWAYS	01/2013	2,125.24	-	4,467.07
134	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	ROAD TRANSPORT AND HIGHWAYS	03/2012	828	-	862.73
135	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA	ROAD TRANSPORT AND HIGHWAYS	10/2013	677.79	-	682.13
136	KOTWA TO DEWAPUR (LMNHP-10)	ROAD TRANSPORT AND HIGHWAYS	11/2005	240	-	295.5
137	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	ROAD TRANSPORT AND HIGHWAYS	01/2011	264.16	-	323
138	2-LANING OF SHILLONG - NONGSTOIN SECTION OF NH 44 AND NONGSTOIN - TURA STATE ROAD UNDER PHASE 'A' OF	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,494.48	-	2,090
139	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	ROAD TRANSPORT AND HIGHWAYS	12/2009	104	-	109
140	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR	ROAD TRANSPORT AND HIGHWAYS	06/2014	569.38	-	680.83

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
141	NAGPUR - KONDHALI	ROAD TRANSPORT AND HIGHWAYS	09/2005	168	-	279.92
142	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	02/2008	1,673.7	-	2,434.74
143	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,170.52	-	1,578.8
144	ROHTAK - BAWAL (APPROVED LENGTH 97 KM)	ROAD TRANSPORT AND HIGHWAYS	02/2010	650	-	830.97
145	TRICHY - KARUR	ROAD TRANSPORT AND HIGHWAYS	03/2007	516	-	761.19
146	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6,395	11609	13,427.27

Annexure-III

Details of Projects Ahead of Schedule w.r.t. Original Schedule

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	2/2015	302.49 -	302.49	229.19	02/2016 -	01/2016
	Total		302.49 -	302.49	229.19		
	<u>COAL</u>						
2	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
3	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	70.80	02/2017 -	03/2016
	Total		188.75 -	188.75	70.80		
	<u>PETROLEUM</u>						
4	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	219.00	160.78	09/2016 -	03/2016
5	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	254.80	01/2017 -	06/2016
	Total		560.90 -	638.04	415.58		
	<u>URBAN DEVELOPMENT</u>						
6	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,562.95		
	<u>PETROLEUM</u>						
7	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	523.70	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	523.70		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
8	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]	3/2015	830.36	830.36	-	01/2019 -	01/2016
	Total		830.36 -	830.36	.00		
	Grand Total		13,688.61	13,765.75	3,805.74		

Annexure-IV

Details of On Schedule Projects w.r.t. Original Schedule

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
2	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.43	03/2016 -	03/2016
3	MALACHUA OPENCAS T PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
4	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	158.47	03/2021 -	03/2021
5	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	61.37	03/2025 -	03/2025
6	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
7	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	30.90	03/2018 -	03/2018
8	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	203.82	03/2017 -	03/2017
9	KHADIA EXPANSION OPENCAS T PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	140.70	03/2018 -	03/2018
10	AMGAON OPENCAS T PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	15.85	03/2020 -	03/2020
11	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
12	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	94.45	03/2021 -	03/2021
13	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	197.01	03/2018 -	03/2018
14	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
15	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	-	03/2018 -	03/2018
16	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020
17	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	131.57	03/2020 -	03/2020
18	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	784.34	03/2023 03/2023	03/2023
19	MADANNAGAR OPENCAS T PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
20	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	108.45	03/2020 -	03/2020
21	GOKUL - [N06000120]	11/2014	267.67 -	267.67	176.63	03/2018 -	03/2018
22	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	10.25	03/2019 -	03/2019
24	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
25	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
26	AMALGAMATED PAUNI-II III OC MINE - [N06000131	6/2015	483.69 -	483.69	39.36	03/2021 -	03/2021
27	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	28.78	03/2021 -	03/2021
28	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	194.04	03/2020 -	03/2020
29	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	125.13	03/2016 -	03/2016
30	DURGAPUR OPENCAST PROJECT - [N06000136	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
31	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
32	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	808.54	03/2016 -	03/2016
33	BATURA HIGHWALL PROJECT - [N06000134	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
34	NEW MAJRI UG TO OC - [N06000128	5/2015	295.56 -	295.56	79.03	03/2019 -	03/2019
35	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
36	PELMA OCP(15.00MTY) - [N06000045	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
37	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	0.29	03/2019 -	03/2019
38	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
39	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
40	BHANEGAON OC - [N06000121	2/2015	187.94 -	187.94	49.30	03/2023 -	03/2023
41	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	620.51	03/2026 -	03/2026
	Total		34,655.54 -	34,494.74	4,527.97		
	<u>FERTILISERS</u>						
42	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	197.79	43.68	11/2016 -	11/2016
	Total		197.79 -	197.79	43.68		
	<u>HEALTH AND FAMILY WELFARE</u>						
43	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005	11/2013	196.70 -	196.70	157.61	01/2016 -	01/2016

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	9.74	03/2018 -	03/2018
45	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	168.90	0.05	05/2017 -	05/2017
46	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	293.65	36.53	05/2017 -	05/2017
47	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	204.44	21.73	05/2017 -	05/2017
	Total		1,369.27 -	1,369.27	225.66		
	<u>MINES</u>						
48	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]	12/2015	355.13 -	355.13	-	11/2016 -	11/2016
49	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	-	11/2016 -	11/2016
	Total		699.63 -	699.63	.00		
	<u>PETROLEUM</u>						
50	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	502.37	05/2017 -	05/2017
51	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
52	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	34.49	11/2016 -	11/2016
53	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	68.96	07/2016 -	07/2016
54	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	59.42	10/2017 10/2017	10/2017
55	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	9,397.86	05/2016 -	05/2016
56	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	137.49	12/2016 -	12/2016
57	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	368.95	12/2018 -	12/2018
58	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	2,268.83	05/2017 05/2017	05/2017
59	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
60	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	81.45	12/2017 -	12/2017
61	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
62	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
63	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
64	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N18000179]	3/2014	3,150.00 -	3,150.00	111.66	09/2017 -	09/2017
65	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	50.18	07/2016 -	07/2016
	Total		38,132.08 -	40,075.00	13,093.33		
	<u>POWER</u>						
66	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	142.00	08/2017 -	08/2017
67	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	965.00	12/2016 -	12/2016
68	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	0.80	11/2017 -	11/2017
69	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	175.30	04/2018 -	04/2018
70	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	10.00	05/2016 -	05/2016
71	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018
72	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
73	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	115.70	04/2020 -	04/2020
74	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
75	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	53.40	02/2017 -	02/2017
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	431.09	03/2016 -	03/2016
77	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,287.00	02/2019 -	02/2019
78	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
79	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
80	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	4,822.73	01/2018 -	01/2018
81	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	2,378.00	08/2018 -	08/2018
82	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
83	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
84	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	47.20	11/2016 -	11/2016

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	623.05	05/2016 -	05/2016
86	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	295.10	05/2018 -	05/2018
87	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	-	10/2016 -	10/2016
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	116.00	06/2016 -	06/2016
89	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	4.60	03/2018 -	03/2018
90	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	113.10	10/2016 -	10/2016
91	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	67.10	04/2017 -	04/2017
92	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	2.30	03/2016 -	03/2016
93	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	939.00	03/2019 -	03/2019
94	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	22.60	03/2018 -	03/2018
95	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	4,611.00	09/2017 -	09/2017
96	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	153.00	09/2019 -	09/2019
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	101.70	06/2016 -	06/2016
98	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	3.10	10/2017 -	10/2017
99	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	45.19	04/2017 -	04/2017
100	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	19.70	07/2016 -	07/2016
101	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	430.87	04/2016 -	04/2016
102	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	16.00	07/2018 -	07/2018
103	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	5,419.00	06/2017 -	06/2017
104	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	434.29	12/2016 -	12/2016
105	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	64.00	08/2016 -	08/2016
106	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	243.10	04/2018 -	04/2018
	Total		125,312.72 -	125,312.72	25,876.10		
	RAILWAYS						

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
108	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
109	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
110	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
111	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
	Total		2,670.53 -	6,808.36	172.17		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
112	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]	3/2015	830.36 -	830.36	-	01/2016 -	01/2016
113	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
114	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
115	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	153.02	01/2016 -	01/2016
116	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	106.61	02/2018 -	02/2018
117	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	-	07/2017 -	07/2017
118	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
119	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
120	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
121	VADODARA-SURAT SECTION - [N24000361]	3/2014	503.16 -	503.16	52.89	08/2016 -	08/2016
122	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
123	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
124	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
125	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19 -	425.19	4.60	09/2016 -	09/2016
126	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]	11/2014	563.92 -	563.92	-	11/2016 -	11/2016

(December 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
127	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]	6/2014	569.38 -	569.38	680.83	06/2016 -	06/2016
128	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	-	03/2018 -	03/2018
129	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	351.34	4.77	01/2016 -	01/2016
130	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
131	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
132	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
133	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
134	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	3/2015	829.00 -	829.00	-	03/2018 -	03/2018
135	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]	6/2015	563.92 -	563.92	-	12/2017 -	12/2017
136	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
137	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79 -	677.79	682.13	04/2016 -	04/2016
138	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	830.19	01/2018 -	01/2018
139	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
140	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
141	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
142	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
143	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
144	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
145	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]	12/2013	177.18 -	177.18	-	03/2016 -	03/2016
146	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
147	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
148	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26 -	269.26	-	10/2016 -	10/2016
149	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
150	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	1/1991	282.41 -	282.41	-	08/2016 -	08/2016
151	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	-	05/2017 -	05/2017
152	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
153	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
154	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242	12/2013	158.65 -	158.65	-	03/2016 -	03/2016
155	4-LANING OF SOLAPUR - YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	-	07/2017 -	07/2017
156	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
157	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
158	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
159	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
160	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	3/2011	218.31 -	339.82	-	12/2015 -	12/2015
161	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	674.20	09/2016 -	09/2016
162	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340	12/2014	451.58 -	451.58	-	06/2017 -	06/2017
163	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
164	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377	1/2014	397.04 -	397.04	-	10/2016 -	10/2016
165	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381	3/2013	257.80 -	257.80	-	02/2016 -	02/2016
166	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
167	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017

(December 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
168	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00	667.00	-	07/2018	07/2018
169	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION) - [N24000287]	11/2015	485.44	485.44	-	12/2015	12/2015
170	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5) - [N24000320]	10/2014	463.49	463.49	-	06/2018	06/2018
171	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41	229.41	-	05/2018	05/2018
172	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD (NH-52B) (NEW NH NO.215) FROM KM 0.00 TO KM 68.30 IN THE STATE - [N24000373]	11/2010	305.49	305.49	122.11	03/2017	03/2017
173	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]	12/2012	438.75	438.75	0.63	09/2016	09/2016
174	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]	1/2014	282.41	282.41	31.64	03/2016	03/2016
175	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B (EXTN) IN ASSAM - [N24000392]	11/2010	268.08	268.08	103.22	05/2017	05/2017
176	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]	10/2013	283.45	283.45	-	10/2016	10/2016
177	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]	10/2015	447.29	447.29	-	12/2017	12/2017
178	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO) - [N24000246]	10/2014	244.30	244.30	-	12/2016	12/2016
179	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66	2,168.66	-	06/2019	06/2019
180	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01	1,655.01	582.00	08/2016	08/2016
181	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]	3/2015	511.83	511.83	-	08/2017	08/2017
182	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00	912.00	-	08/2016	08/2016
183	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10	240.10	137.69	03/2016	03/2016
184	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT) - [N24000245]	1/2014	270.00	270.00	50.85	03/2016	03/2016
185	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB" - [N24000376]	1/1991	219.40	219.40	-	01/2018	01/2018
186	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]	6/2015	1,012.90	1,012.90	-	03/2016	03/2016
187	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23	239.23	-	12/2017	12/2017
188	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53	1,027.53	-	06/2018	06/2018

(December 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
189	PADI - DAHOD - [N24000353]	11/2014	279.14 -	279.14	-	05/2017 -	05/2017
190	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
191	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	-	09/2017 -	09/2017
192	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	-	02/2018 -	02/2018
193	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	-	05/2017 -	05/2017
194	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
195	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
196	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	-	03/2017 -	03/2017
197	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
198	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017
199	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342]	5/2015	709.00 -	709.00	-	09/2017 -	09/2017
200	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]	6/2014	301.04 -	301.04	51.79	01/2016 -	01/2016
201	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018
202	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
203	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	495.78	-	01/2016 -	01/2016
204	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	445.89	-	03/2017 -	03/2017
205	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
206	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
207	FOUR LANING OF PARWANOO - SOLAN - [N24000479]	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
208	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
209	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
210	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	0.88	02/2018 -	02/2018

(December 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
211	REHABILITATION & UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]	12/2015	291.05 -	291.05	-	12/2015 -	12/2015
212	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	10/2014	437.39 -	437.39	-	06/2018 -	06/2018
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
214	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
215	JALANDHAR - AMRITSAR - [N24000351]	1/2014	523.85 -	523.85	74.12	01/2016 -	01/2016
216	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
217	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]	3/2013	959.25 -	959.25	523.50	06/2016 -	06/2016
218	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]	12/2015	602.95 -	602.95	-	06/2016 -	06/2016
219	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
220	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
221	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
222	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
223	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	-	05/2018 -	05/2018
224	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016
225	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
226	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]	9/2015	368.73 -	368.73	-	09/2016 -	09/2016
227	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	227.68	08/2016 -	08/2016
228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
229	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	0.74	04/2017 -	04/2017
230	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	917.89	11/2016 -	11/2016

						(December 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
231	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72 -	264.72	-	04/2017 -	04/2017
232	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263	2/2015	241.61 -	241.61	23.83	02/2017 -	02/2017
233	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
234	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	1.75	01/2017 -	01/2017
235	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
236	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
	Total		66,594.19 -	66,943.29	6,510.40		
	<u>SHIPPING AND PORTS</u>						
237	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	274.85	0.38	04/2017 -	04/2017
238	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	198.94	37.70	06/2017 -	06/2017
239	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
240	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 - 258.00	258.33	0.28	12/2017 -	12/2017
	Total		928.29 -	942.12	38.36		
	<u>STEEL</u>						
241	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097	2/2014	4,749.00 -	4,749.00	2.61	09/2017 -	09/2017
242	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
243	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
244	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103	4/2014	151.33 -	151.33	4.84	09/2017 -	09/2017
245	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111	2/2014	787.29 -	787.29	23.83	12/2016 -	12/2016
246	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
247	TURBO BLOWER - 5 - [N12000092	12/2009	280.00 -	280.00	19.87	09/2016 -	09/2016
248	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	79.89	05/2016 -	05/2016

(December 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
249	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	27.45	12/2017 -	12/2017
250	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 207.00	207.00	129.17	12/2016 -	12/2016
251	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]	7/2011	324.87 325.00	325.00	263.57	12/2015 -	12/2015
252	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 254.00	254.00	192.96	06/2016 -	06/2016
253	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	195.46	12/2016 -	12/2016
254	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	232.80	04/2018 -	04/2018
255	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	173.00	175.89	12/2015 -	12/2015
256	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.90	04/2018 -	04/2018
257	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	126.65	03/2018 -	03/2018
	Total		13,449.59 -	13,528.97	1,585.94		
	URBAN DEVELOPMENT						
258	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
259	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
260	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	948.27	11/2019 -	11/2019
261	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	50.91	03/2018 -	03/2018
	Total		14,321.05 -	14,321.05	999.18		
	Grand Total		298,330.68	304,692.94	53,072.79		

Annexure-V

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	06/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,471.75 -	2,889.44			
	<u>HEAVY INDUSTRY</u>						
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIPI) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
10	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00			

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	PETROLEUM						
11	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	05/2016	70.49
13	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	10/2017	17.66
14	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	4,941.49	04/2016 -	12/2017	19.81
15	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	219.00	09/2016 -	03/2016	54.38
16	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
17	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83
19	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	01/2016	16.05
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
21	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
22	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
23	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62
25	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72
	Total		63,099.10 -	74,422.00			
	POWER						
26	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48
27	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,063.89	09/2010 -	-	187.40
28	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
29	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	06/2016	51.10
30	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	01/2016	13.18
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
32	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
33	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
34	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21
35	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	01/2017	133.06
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,085.84	12/2009 06/2016	06/2016	143.74
37	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
38	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	-	31.17
39	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91
40	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	02/2016	16.63
41	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	06/2016	27.60
42	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
43	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	11/2008 -	12/2016	21.34
44	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
45	TUJRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
46	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	01/2016	139.32
	Total		60,901.26 -	107,768.34			
	RAILWAYS						
47	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
48	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
49	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
50	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
51	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
52	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
53	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
54	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
55	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
56	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
57	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
58	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
59	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
60	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
61	RAMGANJ-MUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
62	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
63	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
64	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
65	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
66	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
67	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
68	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
69	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
70	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	360.00	02/2006 -	-	37.56
71	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
72	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
73	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
74	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
75	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
76	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
77	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
78	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
79	VIRAMGAM-BHILD(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
80	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
81	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
82	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
83	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
84	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
85	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
86	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
87	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
88	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
89	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
90	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
91	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
92	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
93	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
94	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
95	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
96	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
97	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
98	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
99	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
100	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
101	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
102	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
103	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
104	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
105	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
106	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
107	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
108	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
109	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
110	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
111	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	3,500.00	05/2008 -	-	1,313.23
112	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
113	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
114	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
115	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
116	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
117	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
118	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
119	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
120	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
121	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
122	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
123	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
124	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
125	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
126	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
127	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	-	03/2018	99.75
128	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
129	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	-	03/2018	143.60
130	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
131	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
132	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
133	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
134	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	631.78	12/2012 -	-	107.82
135	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
136	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
137	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
138	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	-	03/2015	195.55
139	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
140	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
141	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
142	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
143	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
144	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	-	-	840.53
145	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N220000345]	04/1997	836.26 -	1,072.51	-	-	28.25

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
146	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [N220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
147	BANGLORE - SATYAMANGALAM (NL)(SWR) - [N220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
148	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
149	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]	09/1995	100.00 -	980.00	- -	-	880.00
150	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
151	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
152	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
153	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
154	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	-	42.11
155	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
156	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
157	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [N220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
158	AMRAVATI-NARKHER NL(CR) - [N220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
159	ANGAMALI-SABARIMALA (N.L.)(SR) - [N220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
160	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
161	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
162	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
163	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
164	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
165	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
166	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
167	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
168	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
169	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR- BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
170	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
171	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
172	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
173	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
174	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
175	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
176	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
177	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
178	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
179	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
180	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
181	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
182	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
183	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
184	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
185	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
186	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
187	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
188	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
189	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
190	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
191	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70 -	- -	03/2020	5.00
192	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45 -	- -	03/2018	110.44
193	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81 -	- -	03/2018	1.86
194	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22 -	- -	-	109.04
195	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00 -	- -	-	173.71
196	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24 -	- -	03/2015	285.12
197	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95 -	- -	-	16.29
198	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90 -	- -	03/2020	30.00
199	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57 -	- -	03/2018	180.56
200	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28 -	- -	03/2017	63.25
201	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58 -	- -	03/2018	162.68
202	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55 -	- -	03/2018	216.06
203	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10 -	- -	03/2018	45.17
204	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06 -	- -	03/2019	47.95
205	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55 -	03/2016 -	12/2017	29.06
206	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00 -	- -	-	33.02
	Total		81,779.00 -	210,420.06 -			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
207	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00 -	02/2009 -	03/2016	28.93
208	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13 -	04/2009 -	03/2016	92.75
209	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13 -	11/2008 -	03/2016	80.68
210	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23 -	07/2009 -	03/2016	68.99
211	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00 -	11/2011 -	06/2016	106.50

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
212	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
213	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
214	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	162.00	07/2015 -	07/2015	3.07
215	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	08/2016	42.25
216	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	01/2016	30.10
217	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
218	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
219	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
220	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
221	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
222	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
223	TWO LANING OF HOJ - POTIN SECTION OF NH-229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH - [N24000419	12/2009	82.73 -	165.00	09/2010 -	09/2010	99.44
224	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
	Total		4,995.43 -	7,530.59			
	SHIPPING AND PORTS						
225	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	01/2016	300.00
226	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
227	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
228	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72

(December 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		1,006.56 -	1,937.62			
	<u>STEEL</u>						
229	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2016	12.04
230	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 207.00	207.00	12/2016 -	12/2016	17.96
231	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,060.00	1,060.00	02/2014 -	-	37.86
232	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]	07/2011	324.87 325.00	325.00	12/2015 -	12/2015	0.04
233	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 254.00	254.00	06/2016 -	06/2016	0.03
234	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
235	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	173.00	12/2015 -	12/2015	15.54
	Total		2,218.50 -	2,734.40			
	<u>URBAN DEVELOPMENT</u>						
236	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	13,845.01	06/2011 -	06/2016	116.50
	Total		6,395.00 -	13,845.01			
	Grand Total		245,925.81	463,722.86			

Annexure-VI

Details of Delayed Projects w.r.t. Original Schedule

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,025.00	12/2008 10/2013	06/2016	90	70.54	Local Protests - Law & Order issues- local protest / agitation during Oct 2011 to March 2012 affected project work. After normalisation of the situation it took time to mobilize the workforce and resume the normal work.
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,129.59	09/2010 -	09/2016	72	62.57	Clearance from AERB is awaited.
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	7,711.00	12/2015 10/2016	10/2017	22	0	1.Delay in manufacturing and supply of major equipment like End-shields, Reactor Headers, Steam Generators, nuclear piping, PDHRs, etc. Late receipt of financial sanction for the projects leading to delay in first pour of concrete i.e. zero date of the project
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,403.00	12/2016 04/2017	05/2018	17	0	1.Delay in manufacturing and supply of major equipment like End-shields, Reactor Headers, Steam Generators, nuclear piping, PDHRs, etc.
	Total		40,442.00 -	51,918.00	39,268.59					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	408.55	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		309.46 -	309.46	408.55					
	<u>COAL</u>									

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
6	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,925.28	03/2014 -	03/2016	24	0	i) Delay in procurement of major HEMM & construction of CHP & In-pit Conveyor transport system.
7	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,713.30	03/2014 -	03/2016	24	0	i) Delay in procurement of major HEMM & construction of CHP including Silo.
8	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	498.75	03/2013 -	03/2016	36	-6.11	i) Delay in Environment Clearance ii) Coal evacuation problem.
9	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH	06/2011	746.04 535.10	535.10	424.18	03/2015 -	03/2016	12	-28.27	i) Delay in Environment Clearance ii) Coal evacuation problem.
10	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	866.72	03/2013 09/2012	03/2016	36	478.5	i) Delay in supply of LW equipment ii) Delay in drivage of gate roadways and installation of belt conveyors.
11	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	69.02	03/2014 -	03/2016	24	0	Delay/ non issuance of 'Patta' for land/plots allotted to PAFs shifted and being shifted in the area acquired under CBA Act.
12	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	76.28	03/2015 -	03/2016	12	0	i) Delay in acquisition of forest land.
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	67.47	03/2012 -	03/2016	48	0	Environmental Clearance
14	CHURI BENTU UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	36.08	03/2011 -	03/2016	60	0	i) Delay in handing over of forest land.
15	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	0	i) Environmental Clearance ii) Others Problems
16	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.06	04/2014 -	03/2016	23	0	i) Environmental Clearance
17	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	183.91	10/2014 -	03/2016	17	0	i) Delay in land acquisition ii) Delay in supply of equipment, iii) Delay in civil works.
18	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	99.28	05/2014 -	10/2016	29	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator.
19	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	62.95	04/2014 -	11/2016	31	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator.

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
20	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	297.62	03/2010 -	03/2017	84	0	Coal Evacuation problem
21	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL, JHARKHAND	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72	0	Authentication of land of Jhulundia, Bijain Torhad, Sidhalu, Thetangi and Lukaiya villages for 3621 acres. Authentication completed for 1600 acres. Balance pending at District Administration, Chatra.
22	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72	0	Processing of FC stage-I and stage-II was delayed by State Forest Deptt. and State Govt.
23	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 486.57	486.57	75.15	03/2012 03/2018	03/2017	60	87.58	i) Land Acquisition ii) Rehabilitations & Resettlement Problems
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	208.05	03/2013 -	03/2017	48	0	i) Environmental Clearance ii) Coal evacuation Problems
25	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	150.27	03/2010 -	03/2017	84	0	Rehabilitations & Resettlement Issues
26	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51	0	i) Land Acquisition ii) Rehabilitations & Resettlement Problems iii) Contractual Issues iv) Adverse Geomining Conditions
27	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	205.98	03/2012 -	03/2017	60	0	i) Environmental Clearance ii) Delay in forest land Diversion
28	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	175.70	03/2013 -	03/2017	48	0	Environmental Clearance
29	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	91.85	03/2012 -	03/2017	60	0	Authentication of village potanga, Court cases
30	PUKNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48	0	Verification of authenticated land
31	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	70.20	03/2014 -	03/2017	36	0	Authentication of land of village
32	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
33	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	14.18	07/2016 -	03/2017	8	0	Aquisition of non forest land and R&R
34	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	76.98	03/2012 -	03/2018	72	0	i) Adverse Geo-mining condition.
35	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	209.59	03/2014 -	03/2018	48	0	Environmental Clearance
36	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land.
37	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Law & Order problem.
38	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land.
39	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	96.39	03/2016 -	03/2018	24	0	i) Land Acquisition ii) Delay in forestry clearance.
40	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 486.27	486.27	93.51	03/2016 -	03/2018	24	12.97	i) Delay in diversion of forest land and acquisition of non forest land ii) Delay in implementation of R & R.
41	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,297.62	12/2015 04/2018	04/2018	28	0	i) Delay in civil works ii) Delay in equipment erection iii) Delay in supply of indigenous equipment by public sector.
42	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	47.76	04/2015 04/2019	04/2019	48	0	i) Land Acquisition ii) Contractual issues.
43	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	1,458.17	8.68	06/2015 -	08/2019	50	0	N.R.
44	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	Delay in Environment and forestry Clearance.

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
45	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems
46	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	i) Rehabilitation & Resettlement Problems ii) Environmental Clearance.
47	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	77.78	07/2012 -	03/2021	104	0	Law & Order
48	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	i) Delay in Environment and forestry Clearance ii) Rehabilitation & Resettlement problem
49	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	411.47	03/2012 -	03/2023	132	16.86	i) Delay in diversion of Canal -6 and acquisition of non forest land ii) Delay in implementation of R & R due to abnormal increase in cost of land.
	Total		25,908.61 -	27,019.10	10,586.25					
	<u>MINES</u>									
50	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	1,176.00	2.86	09/2017 -	04/2020	31	-36.64	Delay in grant of statutory clearances i.e. environmental clearance, clearance from standing committee of NBWL.
	Total		1,856.00 -	1,176.00	2.86					
	<u>STEEL</u>									
51	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	143.50	09/2014 01/2016	01/2016	16	0	i) Short/ delay in supply of instrumentation & control cable. ii) Non-availability of foreign expert.
52	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	229.56	08/2014 02/2016	02/2016	18	0	i) Inadequate deployment of manpower. ii) Delay in supply of structural material & equipment due to delay in ordering.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
53	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	314.87	06/2015 02/2016	02/2016	8	0	Design changes in laying of pipelines in Battery Area.
54	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	220.15	12/2014 05/2016	05/2016	17	0	Under-firing is withheld due to inadequate supply of Coke Oven Gas.
55	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	173.07	10/2013 06/2016	06/2016	32	0	i) Inadequate deployment of manpower ii) delay in submission of drawings by Reliable Hi-tech Pvt. Ltd. iii) Poor progress by HSCL.
56	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	370.73	07/2015 -	06/2016	11	0	i) Delay due to technical issues of revamping of Blast Furnace - 2 ii) The shutdown plan has been redrawn matching the production schedules. iii) Delay in ordering of Stock House Dust Extraction & Cast House Fume Extraction system.
57	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	290.11	04/2016 09/2016	09/2016	5	0	Delay in supply & erection of material.
58	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,431.95	03/2013 10/2016	10/2016	43	0	Delay by HEC in supply of EOT Cranes is affecting the progress of Universal Rail Mill and Bar & Rod Mill.
59	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	8,318.82	05/2015 12/2016	12/2016	19	0	N.R.
60	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH	07/2011	974.76 -	974.76	215.52	07/2016 -	12/2016	5	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
61	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	248.38	07/2015 -	06/2017	23	0	i) Delay due to strengthening of steel structure of BOF shop in view of the new design of equipment as per requirement. ii) Delay due to additional requirement for up-gradation of electrical system (HTMCC & LTMCC). iii) Delay due to schedule of revamping of other 2 Converters redrawing matching the production plan.
62	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	36.00	10/2016 -	06/2017	8	42.39	N.R.
	Total		37,329.16 -	37,474.56	25,992.66					
	<u>PETROCHEMICALS</u>									
63	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,965.00	9,103.96	04/2012 12/2013	12/2015	44	82.49	Initial delay in resolving the issues raised by feedstock suppliers and promoters after the project got approved by the CCEA. iii) Delay in incorporation of BCPL and in the appointment of Engineering Project Management Consultant (EPMC) iv) Delay in the award and finalization of the agreement with the process technology licensors. v) Significant changes in technology/ engineering/ operational/ utility requirements. vi) time escalation and increased prices of feedstock. vii) inadequate development of key personnel.
	Total		5,460.61 -	9,965.00	9,103.96					
	<u>PETROLEUM</u>									

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
64	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	30,818.63	11/2012 11/2013	01/2016	38	16.05	Repair of Generator by BHEL
65	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,663.75	01/2014 12/2015	01/2016	24	0	slow progress by the contractor in laying of pipelines.
66	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	186.98	12/2014 -	01/2016	13	0	Delay in erection of bullets and welding
67	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 -	01/2016	43	-20.13	Court cases, expenditure is zero because as per payment terms of the rig purchase order, payment is to be made on delivery of the rigs at Ports for shipment.
68	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,261.12	09/2012 -	03/2016	42	0	Frequent interruption by villagers and delay in getting forest clearances
69	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,366.24	08/2015 -	03/2016	7	0	Final forest clearance is awaited.
70	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	315.82	06/2011 03/2012	03/2016	57	0	Retendering
71	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	123.32	09/2012 03/2016	03/2016	42	-24.14	Slow progress in civil works
72	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	407.88	08/2015 -	03/2016	7	0	Delay in acquisition of land at Balasore by Odisha Govt for pump station construction has affected the project completion schedule.
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,029.66	10/2011 -	03/2016	53	67.62	issues faced with local elements in the RoU.
74	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	995.12	05/2013 04/2016	04/2016	35	45.83	Delay in procurement of steel
75	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,282.07	03/2015 05/2016	05/2016	14	29.42	Non-performance of contractor
76	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	830.50	05/2014 05/2016	05/2016	24	0	Retendering
77	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	Non-performance of contractor

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
78	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016	26	0	Consortium having Financial issues with their bankers
79	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	552.58	04/2015 04/2015	05/2016	13	-39.69	delay in hook-up and commissioning
80	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR, KERALA	01/2006	993.00 1,693.00	1,693.00	1,446.59	01/2012 -	05/2016	52	70.49	Progress is slow due to heavy rains during the period, RoU issue
81	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL, GUJARAT	12/2011	160.00 -	160.00	35.07	02/2016 02/2016	05/2016	3	0	Contractual problem
82	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL, BIHAR	04/2013	480.00 -	480.00	126.43	02/2016 -	07/2016	5	0	Clearances from MoEF is awaited
83	RESID UPGRADE PROJECT - [N16000184]CPCL, TAMIL NADU	02/2011	3,110.36 -	3,110.36	1,292.13	11/2015 07/2016	07/2016	8	0	Change in scope of work, limited working timing due to radioactive activities
84	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	455.47	03/2015 11/2015	08/2016	17	37.72	space constraint in few locations, obstructions, retendering, poor performance of contractor, torrential rain, delay in award
85	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	498.95	09/2011 10/2016	10/2016	61	0	Delay in preparation of drawing and additional model testing of Hull form in Austria . - Shortage of skilled manpower at contractor end. - Inadequate ancillary/sub-contractors at the location -Lack of planning to match resources to work targets. - Change in delivery location. -Delay in procurement of steel by PSL. -poor financial health of the contractor M/s Pipavav Defence and Offshore Engineering Company and because of delay in its subsequent take-over by M/s Reliance Group
86	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, KARNATAKA	02/2012	666.00 838.08	838.08	570.28	11/2015 11/2016	11/2016	12	25.84	Due to prolonged monsoon, permission was given to enter forest area in mid-December.
87	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 -	913.00	460.06	08/2015 -	12/2016	16	0	Final forest clearance is awaited

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
88	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	100.19	11/2016 -	12/2016	1	0	N.R.
89	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,789.87	03/2013 03/2016	03/2017	48	-3.5	Initially more time taken for mobilization of survey & pre-engineering teams by the contractor. •Bandhs & barricades in Assam and resistance from the local villagers for site activities. •Delay in Right of Use (ROU) clearances and resource mobilization by contractor resulted in delay in pipeline laying activities. •Finalization of major equipment vendors by the contractor took longer time leading to delay in engineering. •Lack of planning & resource mobilization by contractor as well as local issues for starting the critical activities
90	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	258.68	10/2014 03/2017	03/2017	29	49.38	Delay in getting forest clearances, RoU, delay in getting working permission from state government.
91	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25	0	expenditure is zero because of project is still under tendering.
92	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,941.49	4,941.49	521.23	04/2016 12/2017	12/2017	20	19.81	Under tendering
93	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	164.88	09/2017 03/2018	12/2017	3	0	Environment clearance is awaited
94	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	25.93	01/2013 -	12/2018	71	-10.01	Deployment of CA - Bihar.
95	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	586.87	05/2019 03/2020	03/2020	10	0	Tendering issue

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
96	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]JCL,JHARKHAND	04/2011	191.96 -	191.96	98.84	05/2015 -	12/2015	7	0	Project schedule is adversely affected due to delay in acquisition of additional land admeasuring 3.99 acre. Completion will take 8 months after possession of the land.
	Total		75,080.24 -	82,459.83	49,771.47					
	<u>POWER</u>									
97	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.57	1,007.57	953.59	07/2013 01/2016	01/2016	30	139.32	Non supply of requisite quantum of gas
98	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	757.94	11/2012 -	01/2016	38	0	Severe ROW problem in western UP.
99	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,950.24	03/2013 06/2015	01/2016	34	13.18	Severe ROW problem in Odisha.
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,444.82	04/2013 -	01/2016	33	0	Severe ROW problem in western UP.
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	360.37	02/2012 -	02/2016	48	0	Severe ROW problem in western UP.
102	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	184.20	01/2013 -	02/2016	37	0	Delay in land acquisition of Kishanganj s/stn.
103	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,307.76	08/2014 -	02/2016	18	0	Delay in land acquisition for Varansai S/stn. & ROW problem (Nexalite problem).
104	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	302.97	08/2014 06/2015	02/2016	18	16.63	Severe ROW problem.
105	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,573.17	10/2014 -	02/2016	16	0	Severe ROW problem faced.
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	282.92	05/2015 -	02/2016	9	0	Delay in land acquisition for Varansai Sub station.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
107	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,062.99	08/2012 -	03/2016	43	0	Contractual /legal issue.
108	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,570.76	11/2013 -	03/2016	28	0	Severe ROW problem & forest clearance delayed.
109	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	520.31	11/2013 -	03/2016	28	0	Delay in land acquisition for Chandwa S/stn. & Huge forest clearance awaited.
110	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	574.60	02/2014 -	03/2016	25	0	Severe ROW problem.
111	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	88.20	12/2015 -	03/2016	3	0	N.R.
112	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,125.22	01/2013 -	03/2016	38	0	N.R.
113	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	83.21	N.R.
114	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,085.84	6,085.84	4,303.08	12/2009 06/2016	06/2016	78	143.74	(1)Redesign of dam parameter (2)Geological surprise (3) realignment of HPT (4) Slope stabilization of power house area (5) Flash flood/Rain (6) Deviation in work (7) Contractual issue (8) Major deviation in encountered geology than that envisaged (9) permission for quarry operation yet to be received from Govt. of Arunachal Pradesh.
115	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,937.70	09/2009 -	06/2016	81	81.76	N.R.
116	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	577.79	09/2010 06/2013	06/2016	69	51.1	Severe ROW problem.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	523.76	11/2011 -	06/2016	55	0	Severe ROW problem in western UP.
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	541.02	07/2013 11/2015	06/2016	35	-8.45	Delay in forest clearance & Limited working periods/snow bound area.
119	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,784.85	05/2014 -	06/2016	25	0	Delay in land acquisition for Champa Sub station.
120	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,888.96	09/2014 -	06/2016	21	0	Contractual issue & severe ROW problem in Karnataka.
121	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,303.03	07/2014 -	06/2016	23	0	Severe ROW problem (grap garden) & forest clearance awaited.
122	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,475.53	08/2014 12/2015	06/2016	22	27.6	Forest clearance awaited.
123	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,373.62	01/2015 -	06/2016	17	0	Forest clearance awaited.
124	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	93.03	09/2014 -	06/2016	21	0	Severe ROW problem
125	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	5,337.19	06/2015 -	06/2016	12	0	Delay in land acquisition for Champa HVDC Station & forest clearance awaited.
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	583.62	11/2014 -	06/2016	19	0	Severe ROW problem & delayed forest clearance

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
127	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,893.07	10/2014 -	06/2016	20	0	Delay in land acquisition for Kanpur S/stn.
128	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	17.60	02/2016 -	06/2016	4	0	Completion delay due to delay in manufacturing of Reactors by M/s BHEL.
129	PARE HYDRO ELECTRIC PROJECT - [N18000045]NNEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,262.27	1,262.27	1,085.04	08/2013 07/2016	07/2016	35	119.91	N.R.
130	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	291.60	06/2015 -	08/2016	14	0	Completion matching with line.
131	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	989.03	06/2015 -	08/2016	14	0	Forest clearance awaited.
132	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NNEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	930.00	07/2006 10/2016	10/2016	123	274.73	(1) Poor approach road condition from Bhagabazar to Natachera affecting seriously transportation of man, material, equipment and POL
133	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,351.15	01/2016 -	11/2016	10	50.95	
134	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	16.00	04/2016 -	11/2016	7	0	Non-availability of PMU test lab worldwide.
135	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,903.55	11/2008 03/2012	12/2016	97	21.34	Severe ROW problem in Kerala.
136	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,204.18	10/2012 -	12/2016	50	0	Severe ROW problem & forest clearance awaited.
137	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,357.96	01/2015 -	12/2016	23	0	Wildlife sanctuary & forest clearance awaited.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
138	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,253.90	12/2012 -	12/2016	48	0	Contractual issues and forest clearance & local disturbance in NER.
139	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,228.13	11/2012 -	12/2016	49	0	Delay in sub station land acquisition & ROW problem in LILO line.
140	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,779.00	09/2016 -	12/2016	3	0	
141	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,043.56	12/2015 -	12/2016	12	0	Severe ROW problem & huge forest involvement.
142	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.00	9,606.82	1,353.36	02/2011 -	01/2017	71	133.06	N.R.
143	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,642.00	09/2011 -	03/2017	66	54.25	*Inadequate deployment of manpower & resources by M/s BHEL and its sub-agencies have affected the erection/commissioning progress of U#1
144	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	9,969.00	01/2017 -	03/2017	2	0	N.R.
145	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,749.00	11/2016 -	08/2017	9	0	N.R.
146	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,206.93	05/2014 -	09/2017	40	0	N.R.
147	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	4,382.19	12/2016 -	09/2017	9	0	N.R.
148	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	11,225.70	08/2013 12/2017	12/2017	52	23.65	Generation project delayed & ROW problem/Law & order problem in NER.
149	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	44.00	02/2014 -	02/2018	48	0	Installation of 3 rd transformer and charging of line is pending.
150	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,070.00	01/2011 10/2014	05/2018	88	73.65	*Non performance of Russian agency M/s TPE & M/s PM.
151	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,367.65	09/2009 -	12/2018	111	99.48	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
152	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,661.00	03/2013 -	12/2018	69	29.14	N.R.
153	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,545.54	02/2016 09/2019	09/2019	43	79.77	4.668 Ha. Land diversion case for dumping area at Village Chopra.
154	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	775.12	06/2013 -	12/2019	78	0	Post Award: 1. Minor hindrances by local villagers.
	Total		161,207.08 -	196,080.02	136,206.50					
	<u>HEAVY INDUSTRY</u>									
155	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	122.78	NATRIP is a temporary organization is the major hurdle of the project. NATRIP is first of its kind of project for which no train manpower was available in the country.
	Total		1,718.00 -	3,827.30	.00					
	<u>HEALTH AND FAMILY WELFARE</u>									
156	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	268.07	12/2015 -	03/2016	3	0	Fund Constraints.
157	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	118.95	11/2013 -	03/2016	28	0	Local disturbances.
158	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	106.20	12/2014 -	03/2016	15	0	i) Delay in issuance of labour licence from labour Deptt. ii) Frequent bandhs and heavy rain iii) Obstruction of work by locals. iv) Difficulty in procurement of sand and aggregates due to ban of forest produce.
	Total		779.77 -	779.77	493.22					
	<u>RAILWAYS</u>									

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
159	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
160	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	367.76	Railway bridge targeted for commissioning in October, 2015. However Road bridge would take time as there are issues in land acquisition.
161	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	259.68	N.R.
162	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defroze and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut -Saharanpur).
163	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	N.R.
164	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	N.R.
165	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	N.R.
166	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.

(December 2015)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
167	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	325.50	348.66	02/2009 02/2009	04/2016	86	95.9	Contractual issues
168	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
169	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	318.33	322.05	03/2009 03/2009	10/2016	91	138.61	Contractual issues
170	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	N.R.
171	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	N.R.
172	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	N.R.
173	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	233.08	N.R.
174	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	890.25	03/2010 -	06/2017	87	38.24	N.R.
175	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	328.12	03/2010 -	12/2017	93	18.66	contractual issue, land acquisition,non finalisation of alignment of flyover at Bilaspur
176	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	130.80	03/2016 -	12/2017	21	29.06	land acquisition & hurdle clearances like drains etc. by GHMC authorities.
177	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
178	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
179	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
180	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	NR

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
181	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	N.R.
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	N.R.
183	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	614.96	03/2016 -	12/2018	33	-28.09	Non-handing over of land of Joka Depot
184	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	N.R.
185	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
186	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Progress is going as per the allotment of budget grant.
187	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
188	TAMLUK DIGHA, LINE DOUBLING (SER) - [N220000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.
189	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
190	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	850.74	03/2016 -	12/2020	57	-20	land aquisition problem
	Total		37,532.74 -	92,383.86	40,692.09					
	ROAD TRANSPORT AND HIGHWAYS									

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
192	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	142.60	09/2008 -	01/2016	88	30.1	N.R.
193	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	270.76	10/2008 -	01/2016	87	-8.95	N.R.
194	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2016	01/2016	93	0	N.R.
195	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	01/2016	32	0	N.R.
196	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	913.00	12/2013 -	01/2016	25	0	N.R.
197	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	543.70	03/2013 -	01/2016	34	0	N.R.
198	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	609.00	02/2014 -	01/2016	23	0	N.R.
199	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	882.72	03/2014 -	01/2016	22	0	N.R.
200	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]MEGA,RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,434.74	10/2011 -	01/2016	51	0	N.R.
201	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH	11/2015	867.66 -	867.66	374.03	11/2015 -	01/2016	2	0	N.R.
202	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]MEGA,MADHYA PRADESH	05/2013	1,055.00 -	1,055.00	374.03	11/2015 -	01/2016	2	0	N.R.
203	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	307.92	06/2008 -	02/2016	92	0	N.R.
204	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	468.41	05/2010 -	02/2016	69	0	N.R.
205	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,821.52	09/2012 -	02/2016	41	0	N.R.
206	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	02/2016	38	0	N.R.
207	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	02/2016	17	0	N.R.
208	4 LANING OF GOMTI CHAURAH - UDAIPUR - [N24000455]MEGA,RAJASTHAN	03/2012	914.50 -	914.50	850.53	10/2015 -	02/2016	4	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
209	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	389.31	02/2009 -	03/2016	85	28.93	N.R.
210	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	194.33	04/2009 -	03/2016	83	92.75	N.R.
211	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	231.27	11/2008 -	03/2016	88	0	N.R.
212	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	184.97	11/2008 -	03/2016	88	80.68	N.R.
213	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	234.99	04/2009 -	03/2016	83	0	N.R.
214	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	276.28	06/2008 -	03/2016	93	0	N.R.
215	BIJUNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	369.05	06/2008 -	03/2016	93	0	N.R.
216	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	488.87	09/2008 -	03/2016	90	0	N.R.
217	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	298.40	07/2009 -	03/2016	80	68.99	N.R.
218	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	348.16	322.70	09/2007 -	03/2016	102	0	N.R.
219	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	03/2016	44	0	N.R.
220	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,605.89	05/2012 -	03/2016	46	0	N.R.
221	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	1,182.58	04/2013 -	03/2016	35	0	N.R.
222	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2016	33	0	N.R.
223	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,474.52	08/2014 -	03/2016	19	0	N.R.
224	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	830.97	11/2013 -	03/2016	28	0	N.R.
225	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.74	10/2013 -	03/2016	29	0	N.R.
226	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	428.32	04/2014 -	03/2016	23	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
227	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	543.94	11/2013 -	03/2016	28	0	N.R.
228	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26	0	N.R.
229	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	646.75	08/2013 -	03/2016	31	0	N.R.
230	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37	0	N.R.
231	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	03/2016	21	0	N.R.
232	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	1,125.40	06/2014 -	03/2016	21	0	N.R.
233	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	455.26	10/2014 -	03/2016	17	0	N.R.
234	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	343.50	07/2014 -	03/2016	20	0	N.R.
235	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	03/2016	23	0	N.R.
236	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	03/2016	21	0	N.R.
237	FOUR LANING OF ORISSA CHATTISGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7	0	N.R.
238	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	632.63	08/2015 -	03/2016	7	0	N.R.
239	WIDNG WITH PS & STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7	0	N.R.
240	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	214.17	03/2008 04/2016	04/2016	97	0	N.R.
241	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016	94	0	N.R.
242	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	284.69	09/2010 -	04/2016	67	0	N.R.
243	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,026.65	07/2013 -	04/2016	33	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
244	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32	0	N.R.
245	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	777.06	04/2015 -	04/2016	12	0	N.R.
246	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12	0	N.R.
247	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	3,784.75	06/2015 -	05/2016	11	0	N.R.
248	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	05/2016	20	0	N.R.
249	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	81.84	12/2015 -	05/2016	5	0	N.R.
250	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13	0	N.R.
251	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56	0	N.R.
252	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,570.55	11/2011 -	06/2016	55	106.5	N.R.
253	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	862.18	03/2013 -	06/2016	39	0	N.R.
254	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,472.64	07/2015 -	06/2016	11	0	N.R.
255	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,393.72	07/2013 -	06/2016	35	0	N.R.
256	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,275.83	06/2013 -	06/2016	36	0	N.R.
257	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36	0	N.R.
258	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	949.96	07/2013 -	06/2016	35	0	N.R.
259	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	649.52	01/2014 -	06/2016	29	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
260	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	06/2016	25	0	N.R.
261	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	970.44	06/2014 -	06/2016	24	0	N.R.
262	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	875.91	03/2013 -	06/2016	39	0	N.R.
263	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,832.80	09/2015 -	06/2016	9	0	N.R.
264	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,467.07	12/2015 -	06/2016	6	0	N.R.
265	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	862.73	09/2014 -	06/2016	21	0	N.R.
266	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24	0	N.R.
267	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	304.17	04/2008 12/2015	07/2016	99	0	N.R.
268	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.40	05/2008 12/2015	07/2016	98	0	N.R.
269	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	0	N.R.
270	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	370.66	04/2010 02/2016	08/2016	76	42.25	N.R.
271	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	08/2016	39	0	N.R.
272	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,849.33	08/2013 -	08/2016	36	0	N.R.
273	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,103.87	02/2014 -	08/2016	30	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
274	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11	0	N.R.
275	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	1,578.80	06/2012 -	08/2016	50	0	N.R.
276	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	453.58	05/2013 -	09/2016	40	0	N.R.
277	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	197.31	01/2014 -	09/2016	32	0	N.R.
278	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	275.21	10/2013 -	09/2016	35	0	N.R.
279	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	0	N.R.
280	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	1,335.12	09/2014 -	10/2016	25	0	N.R.
281	REHABILITATION AND UPGRADEATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	0	N.R.
282	REHABILITATION AND UPGRADEATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	28.66	11/2014 -	11/2016	24	0	N.R.
283	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	202.97	06/2005 -	12/2016	138	0	N.R.
284	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	102.85	09/2007 -	12/2016	111	0	N.R.
285	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	47.41	11/2012 -	12/2016	49	0	N.R.
286	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	39	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
287	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,699.96	03/2013 -	12/2016	45	0	N.R.
288	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	879.84	02/2013 -	12/2016	46	0	N.R.
289	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,326.02	12/2013 -	12/2016	36	0	N.R.
290	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	303.94	05/2013 -	12/2016	43	0	N.R.
291	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.46	07/2013 -	12/2016	41	0	N.R.
292	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35	0	N.R.
293	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2016	39	0	N.R.
294	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	176.11	10/2015 -	12/2016	14	0	N.R.
295	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12	0	N.R.
296	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	0	N.R.
297	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	163.80	11/2016 -	12/2016	1	0	N.R.
298	NALBARI T BIJINI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	295.20	04/2008 01/2017	01/2017	105	0	N.R.
299	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	390.01	07/2014 -	02/2017	31	0	N.R.
300	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	-	02/2015 -	02/2017	24	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
301	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	30.00	08/2012 -	03/2017	55	0	N.R.
302	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	282.68	08/2013 -	03/2017	43	0	N.R.
303	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	715.50	11/2015 -	03/2017	16	0	N.R.
304	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	477.26	03/2014 -	04/2017	37	0	N.R.
305	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	148.55	02/2010 -	05/2017	87	2.29	N.R.
306	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	221.08	08/2013 -	05/2017	45	0	N.R.
307	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	448.14	06/2015 -	05/2017	23	0	N.R.
308	REHABILITATION AND UPGRADEATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	0	N.R.
309	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,635.92	08/2013 -	07/2017	47	0	N.R.
310	REHABILITATION AND UPGRADEATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	38.55	09/2015 -	08/2017	23	0	N.R.
311	REHABILITATION AND UPGRADEATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	N.R.
312	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24	0	N.R.
313	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
314	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	N.R.
315	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31	0	N.R.
316	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	0	N.R.
	Total		90,538.15 -	92,365.10	89,807.34					
	<u>SHIPPING AND PORTS</u>									
317	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	01/2016	118	300	Encroachment, Due to flood in chennai construction work of extension of existing auction platform has not been started. It is expected that the work will start in the last week of December, 2015 and likely to be completed by Jan'16.
318	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	669.46	412.00	12/2010 -	01/2016	61	82.72	poor performance of contractor
319	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	409.83	360.35	04/2009 03/2010	08/2016	88	66.82	some initial delays pertaining to land acquisition
	Total		762.06 -	1,679.29	912.15					
	<u>TELECOMMUNICATIONS</u>									
320	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20	0	N.R.
	Total		13,334.00 -	13,334.00	1,360.00					
	<u>URBAN DEVELOPMENT</u>									
321	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
322	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17	0	N.R.
323	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	138.36	06/2012 03/2016	03/2016	45	0	N.R.
324	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	03/2016	16	0	N.R.
325	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	N.R.
326	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 11,609.00	13,845.01	13,427.27	06/2011 12/2015	06/2016	60	116.5	Difficult geological condition, slow progress to avoid damages to structure in densely populated area
327	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	-	05/2013 10/2015	06/2016	37	0	N.R.
328	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,786.98	12/2015 -	08/2016	8	0	N.R.
329	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	19,388.91	03/2016 -	12/2016	9	0	Rehabilitation & Resettlement, Land acquisition and Delay in technical approval from M/o Railways delays the project.
330	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	0	N.R.
331	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	21.12	09/2015 07/2016	12/2016	15	0	N.R.

(December 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
332	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	58.72	09/2016 01/2017	01/2017	4	0	N.R.
333	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14	0	N.R.
334	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 26,405.01	26,405.01	217.41	02/2019 -	03/2020	13	0	N.R.
	Total		112,018.96 -	119,468.84	45,056.79					
	Grand Total		604,276.84	730,240.13	449,662.43					

Annexure-VII

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00 -	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00 -	12/2008 -	06/2016	70.54	90
	Total		16,663.00 -	28,139.00 -				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39 -	03/2013 -	03/2016	478.50	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57 -	03/2012 -	03/2017	87.58	60
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62 -	03/2012 -	03/2023	16.86	132
6	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27 -	03/2016 -	03/2018	12.97	24
	Total		1,321.16 -	2,690.85 -				
	<u>HEAVY INDUSTRY</u>							
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30 -	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30 -				
	<u>PETROCHEMICALS</u>							
8	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00 -	04/2012 -	12/2015	82.49	44
	Total		5,460.61 -	9,965.00 -				
	<u>PETROLEUM</u>							
9	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79 -	10/2014 -	03/2017	49.38	29
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08 -	11/2015 -	11/2016	25.84	12

(December 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62	53
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83	35
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72	17
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	05/2016	70.49	52
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
16	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	4,941.49	04/2016 -	12/2017	19.81	20
17	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	01/2016	16.05	38
	Total		40,394.93 -	48,839.73				
	<u>POWER</u>							
18	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	02/2016	16.63	18
19	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
20	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	01/2016	139.32	30
21	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	06/2016	51.10	69
22	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91	35
23	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76	81
24	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77	43
25	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	06/2016	27.60	22
26	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	11/2008 -	12/2016	21.34	97
27	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	01/2016	13.18	34
28	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21	51
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,085.84	12/2009 06/2016	06/2016	143.74	78
30	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69

(December 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
31	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
32	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48	111
33	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	01/2017	133.06	71
34	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
35	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
36	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		54,128.44 -	89,064.99				
	<u>RAILWAYS</u>							
37	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
38	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61	91
39	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
40	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90	86
41	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
42	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
43	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
44	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
45	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
46	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66	93
47	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
48	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
49	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
50	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
51	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47

(December 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
52	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47	2,921.00	10/2007	12/2015	367.76	98
53	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68	816.55	03/2016	12/2017	29.06	21
54	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20	950.00	03/2010	06/2017	38.24	87
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56	6,570.75	03/2011	03/2019	803.12	96
56	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00	2,531.34	12/2008	03/2018	245.34	111
57	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34	2,876.00	03/2014	03/2018	253.60	48
58	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00	2,973.42	03/2015	03/2020	249.81	60
59	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00	1,242.25	03/2007	03/2016	38.80	108
60	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48	4,190.00	12/2015	03/2020	212.81	51
61	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00	4,996.19	04/2008 12/2011	06/2017	233.08	110
62	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31	5,500.00	03/2009	03/2016	228.10	84
63	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00	19,565.00	11/2002	12/2018	682.60	193
64	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00	7,986.04	03/2014	03/2019	50.68	60
	Total		22,680.85	79,140.68				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
65	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00	201.66	09/2008	01/2016	30.10	88
66	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04	280.13	11/2008	03/2016	80.68	88
67	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00	331.23	07/2009	03/2016	68.99	80
68	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81	385.13	04/2009	03/2016	92.75	83
69	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61	309.56	04/2010	08/2016	42.25	76
70	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00	281.31	02/2010	05/2017	2.29	87
71	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00	361.00	02/2009	03/2016	28.93	85

(December 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
72	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00	2,288.00	11/2011	06/2016	106.50	55
	Total		2,586.46	4,438.02				
	<u>SHIPPING AND PORTS</u>							
73	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00	600.00	03/2006	01/2016	300.00	118
74	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67	409.83	04/2009	08/2016	66.82	88
75	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39	669.46	12/2010	01/2016	82.72	61
	Total		762.06	1,679.29				
	<u>STEEL</u>							
76	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00	488.40	10/2016	06/2017	42.39	8
	Total		343.00	488.40				
	<u>URBAN DEVELOPMENT</u>							
77	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00	13,845.01	06/2011	06/2016	116.50	60
	Total		6,395.00	13,845.01				
	Grand Total		152,453.51	282,118.27				

Annexure-VIIIDetails of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015
	Total		553.21 -		
	<u>COAL</u>				
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		467.78 -		
	<u>STEEL</u>				
4	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	04/2013 09/2014	06/2015
5	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	05/2013 01/2015	08/2015
6	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	02/2014 -	-
7	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
8	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
9	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	-
10	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
	Total		3,791.36 -		
	<u>PETROLEUM</u>				
11	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	06/2015
12	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
13	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
14	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
15	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
17	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	01/2014 -	-
	Total		9,034.77 -		
	<u>POWER</u>				
18	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
19	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
20	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	06/2014 03/2016	-
21	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		7,211.60 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
22	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014
	Total		414.11 -		
	<u>RAILWAYS</u>				
23	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
24	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
25	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
26	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
27	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
28	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
29	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
30	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
31	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
32	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014
33	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
34	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015
35	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
36	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
37	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015
38	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
39	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
40	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
41	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015
42	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
43	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015
44	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015
45	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015
46	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015
47	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015
48	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	10/2015
49	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
50	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-
51	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
52	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]UTTAR PRADESH	04/1997	836.26 -	- -	-
53	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
54	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
55	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
56	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
57	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
58	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
59	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
60	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
61	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
62	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
63	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
64	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
65	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
66	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
67	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
68	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
69	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
70	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
71	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
72	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
73	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
74	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
75	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
76	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
77	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
78	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
79	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
80	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
81	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
82	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
83	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
84	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
85	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
86	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
87	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
88	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
89	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
90	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N220000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
91	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
92	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
93	TIDIVANAM-NAGARI (NL) - [N220000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
94	BARDHAMAN-KATWA (GC) - [N220000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
96	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
97	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
98	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
99	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
100	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
101	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
102	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
103	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
104	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
105	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
106	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
107	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
108	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
110	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
111	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
112	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
113	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
114	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
115	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
116	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
117	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
118	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
119	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
120	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
121	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
122	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
123	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
124	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
125	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
126	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
127	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
128	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
129	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
130	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
131	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
132	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
133	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
134	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
135	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
136	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
137	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
138	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
139	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
140	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
141	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
142	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
143	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
144	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
145	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
146	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
147	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
148	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
149	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
150	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
151	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
152	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
153	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
154	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
155	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
156	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
157	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
158	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
159	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
160	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
161	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
162	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
163	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
164	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
165	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
166	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
167	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
168	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
169	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
170	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
171	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
172	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
173	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
174	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
175	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
176	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
177	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
178	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
179	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
180	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
181	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
182	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
183	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
184	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
185	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
186	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
187	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
188	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
189	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
190	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
191	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
192	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
193	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
194	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
195	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
196	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
197	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
198	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
199	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
200	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
201	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
202	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
203	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
204	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
205	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
206	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
207	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
208	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
209	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
210	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
211	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
212	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
213	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
214	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
215	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
216	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
217	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
218	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
219	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
220	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
221	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
222	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
223	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
224	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
225	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
226	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
227	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
228	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
229	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
230	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
231	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
232	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
233	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
234	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	01/1999 -	-
235	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	01/1999 -	-
236	MM FROM BURAMARA-CHAKULIA - [N22000305]SER, MULTI STATE	04/2008	466.48 -	01/1999 -	-
237	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	285.57 -	01/1999 -	-
238	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
239	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
240	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	- -	-
241	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	-
242	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA	03/2006	201.00 -	- -	-
243	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	-
244	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
245	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR, TAMIL NADU	04/2011	190.10 -	- -	-
246	HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA	03/2015	1,900.00 -	- -	-
247	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	- -	-
248	MIRAJ-LONDA - [N22000327]SWR, MULTI STATE	03/2015	1,830.00 -	- -	-
249	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 -	- -	-
250	SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR	05/2015	380.00 -	- -	-
251	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-
252	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR, HARYANA	05/2015	400.00 -	- -	-
253	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 -	- -	-
254	HOTGI-KUDGI-GADAG - [N22000333]SWR, MULTI STATE	03/2015	1,618.00 -	- -	-
255	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	720.00 -	- -	-
	Total		114,427.23 -		
	ROAD TRANSPORT AND HIGHWAYS				

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
256	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	01/2015
257	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	01/2015
258	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	02/2011
259	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	02/2012
260	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	02/2013
261	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	02/2015 -	02/2015
262	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
263	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	03/2011
264	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	03/2011
265	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015
266	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
267	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015
268	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	03/2015 -	03/2015
269	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	04/2014
270	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	05/2012
271	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	05/2014
272	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	05/2015 -	05/2015
273	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	07/2008
274	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	08/2013
275	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	08/2013

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
276	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	09/2015
277	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	10/2010
278	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	11/2008 -	11/2008
279	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU	01/1991	285.00 -	01/2008 -	11/2011
280	NAGPUR - KONDHALI - [N24000472]MEGA,MAHARASHTRA	09/2005	168.00 -	06/2006 -	12/2008
281	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 & 352.00- 400.00 OF NH 63 (OLD NH-16 - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	12/2012
282	TWO LANING OF HOJ - POTIN SECTION OF NH-229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	82.73 165.00	09/2010 -	09/2010
283	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010
284	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010
285	2-LANING OF SHILLONG – NONGSTOIN SECTION OF NH 44 AND NONGSTOIN – TURA STATE ROAD UNDER PHASE 'A' OF - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
286	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011
287	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	03/2013
288	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
289	REHABILITATION AND UPGRADATION FROM KM.425/400 TO 509/400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	07/2014
290	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015
291	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	07/2015
292	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	08/2015
293	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	08/2015
294	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
295	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
296	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 -	-
297	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
298	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-
299	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
300	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
301	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
302	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
303	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
304	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
305	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
306	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
307	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
308	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
309	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-
310	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	- -	-
311	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-
312	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
313	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
314	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	-
315	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
316	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-
317	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	-
318	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	-
319	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
320	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-
321	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
322	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-
323	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
324	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
325	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
326	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
327	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
328	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
329	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
330	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
331	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
332	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
333	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
334	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
335	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-
336	REHABILITATION & UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
337	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
338	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
339	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
340	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
341	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293])MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
342	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
343	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-
344	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
345	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
346	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC.IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
347	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
348	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
349	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
350	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
351	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
352	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
353	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
354	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
355	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
356	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
357	WIDENING & STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISAR- - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
358	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-
359	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
360	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL, ASSAM	01/1991	225.02 -	- -	-
361	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	01/1991	223.30 -	- -	-
362	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	-
363	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.00 -	- -	-
364	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI, MADHYA PRADESH	06/2015	583.79 -	- -	-
365	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B & FROM 5.300 TO KM 7.422 (OL - [N24000435]NHAI, WEST BENGAL	10/2015	531.13 -	- -	-
366	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]MEGA, WEST BENGAL	10/2015	361.15 -	- -	-
367	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	01/1991	289.99 -	- -	-
368	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	- -	-
369	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	- -	-
370	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA	12/2015	649.50 -	- -	-
371	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH, GOA	10/2015	936.40 -	- -	-
372	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	- -	-
373	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	- -	-
374	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	- -	-
375	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	- -	-
376	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- -	-
377	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	-
378	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	-
379	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
380	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, ANDAMAN & NICOBAR ISLANDS	09/2015	273.06 -	- -	-
381	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
382	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]MEGA,BIHAR	08/2015	814.04 -	- -	-
383	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	-
384	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
385	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, WEST BENGAL	12/2015	1,423.96 -	- -	-
386	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	-
387	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
388	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	- -	-
389	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-
390	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	- -	-
391	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-
392	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
393	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-
394	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
395	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-
396	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-
397	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
398	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
399	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
400	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
401	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	-
402	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-
403	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
404	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
405	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
406	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	- -	-
407	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
408	ROHTAK - BAWAL (APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA	02/2010	650.00 -	- -	-
409	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
410	WIDENING & STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
411	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
412	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
	Total		89,214.36 -		
	<u>SHIPPING AND PORTS</u>				
413	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		2,427.40 -		
	<u>URBAN DEVELOPMENT</u>				
414	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	-
415	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	01/2015 -	-
416	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
417	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-
418	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	-
419	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	-
420	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-
421	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	-
422	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	-
423	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
424	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	-
425	REHABILITATION AND STRENGTHENING OF SEWEWRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		5,262.02 -		
	Grand Total		232,803.84		

Annexure-IX

Details of Projects Without Original Date of Commissioning

(December 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved / Total
1	2	3	4	5	6	7	8	9	10
	CIVIL AVIATION								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	18.02	-	09/2018	-	0/0
	Total		314.61	314.61	18.02				0/0
	RAILWAYS								
2	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71	744.71	576.86	-	03/2016	-	0/1
3	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17	914.98	846.18	-	03/2016	-	0/0
4	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81	155.81	18.25	-	12/2016	-	0/0
5	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92	1,225.90	257.59	-	03/2017	-	0/0
6	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79	1,101.16	194.91	-	03/2017	-	0/0
7	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00	496.24	213.72	-	03/2017	-	0/0
8	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52	394.28	233.46	-	03/2017	-	0/0
9	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20	365.00	2.52	-	12/2017	-	0/0
10	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97	1,651.54	1,621.40	-	03/2018	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92	565.13	2.80	-	03/2018	48(R3)	0/0
12	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00	886.65	-	-	03/2018	-	0/0
13	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77	441.45	85.78	-	03/2018	-	0/0
14	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55	288.81	11.74	-	03/2018	-	0/0
15	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22	679.57	40.41	-	03/2018	-	0/0
16	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82	435.58	0.56	-	03/2018	-	0/0

(December 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved / Total
1	2	3	4	5	6	7	8	9	10
17	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWAJAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
18	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
19	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
21	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
22	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
23	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
24	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
25	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
26	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
27	NEW BG LINE FROM BYRNIAH TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
	Total		18,087.17 -	29,381.05	5,817.25				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
28	REHABILITATION AND UPGRADE OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	446.77	-	- -	06/2017	-	0/4
29	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	-	- -	10/2017	-	0/4
30	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	36.02	- -	04/2018	-	0/1
	Total		912.07 -	912.07	36.02				0/9
	Grand Total		19,313.85	30,607.73	5,871.29				0/10

Annexure-X

Details of Projects Without Milestones w.r.t. Original Schedule

(December 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	09/2017	0/0
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- -	09/2018	0/0
	Total		1,177.28 -			0/0
	<u>COAL</u>					
5	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND	10/2015	359.69 -	03/2022 -	03/2022	0/0
6	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	03/2024 -	03/2024	0/0
	Total		2,235.01 -			0/0
	<u>FERTILISERS</u>					
7	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 197.79	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
8	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 -	11/2016 -	11/2016	0/0
9	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 -	11/2016 -	11/2016	0/0
10	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	04/2020	0/0
	Total		2,555.63 -			0/0
	<u>STEEL</u>					
11	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	12/2015	0/0
12	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	12/2015 -	12/2015	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
13	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 254.00	06/2016 -	06/2016	0/0
14	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2016	0/0
15	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 207.00	12/2016 -	12/2016	0/0
16	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2016	0/0
17	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	03/2017	0/0
18	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	06/2017	0/0
19	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
20	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	09/2017	0/0
21	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
22	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
23	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
24	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
25	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0
26	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
27	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	02/2014 -	-	0/0
28	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
29	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
30	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	-	0/0
	Total		15,398.80 -			0/0
	<u>PETROLEUM</u>					
31	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 -	01/2016	0/0
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	03/2016	0/0
33	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 04/2015	05/2016	0/0
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	05/2016	0/0

(December 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL, GUJARAT	12/2011	160.00 -	02/2016 02/2016	05/2016	0/0
36	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	09/2011 10/2016	10/2016	0/0
37	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 -	08/2015 -	12/2016	0/0
38	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
39	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
40	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA	03/2014	238.50 -	03/2017 -	03/2017	0/0
41	PIPELINE REPLACEMENT PROJECT - 4 - [N16000203]ONGC, MAHARASHTRA	02/2015	2,899.93 2,098.43	05/2017 -	05/2017	0/0
42	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL, ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
43	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	09/2017 03/2018	12/2017	0/0
44	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL, MAHARASHTRA	05/2015	2,443.00 -	12/2017 -	12/2017	0/0
45	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
46	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA	08/2015	2,818.88 -	03/2019 -	03/2019	0/0
47	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT	05/2015	1,671.22 1,881.22	11/2019 -	11/2019	0/0
48	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	05/2019 03/2020	03/2020	0/0
49	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	- -	-	0/0
50	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU	11/2006	171.83 -	- -	-	0/0
51	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
52	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL, MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
53	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE	02/2015	890.00 -	- -	-	0/0
	Total		39,893.59 -			0/0
	<u>POWER</u>					
54	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,139.00	12/2011 -	03/2016	0/0
55	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL, ANDHRA PRADESH	05/2015	312.94 -	05/2016 -	05/2016	0/0
56	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
57	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	11/2016	0/0
58	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.00	02/2011 -	01/2017	0/0
59	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
60	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2017	0/0
61	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
62	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
63	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
64	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
65	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		26,322.17 -			0/0
	<u>HEAVY INDUSTRY</u>					
66	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
67	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014	0/0
68	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	01/2016	0/0
69	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	03/2016	0/0
70	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 -	03/2016	0/0
71	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016	0/0
72	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	05/2017	0/0
73	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	05/2017	0/0
74	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	05/2017 -	05/2017	0/0
75	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	03/2018	0/0
	Total		2,563.15 -			0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>RAILWAYS</u>					
76	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
77	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
78	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
79	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
80	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
81	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
82	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
83	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
84	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
85	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
86	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
87	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
88	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015	0/0
89	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
90	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
91	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
92	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
93	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
94	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
95	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
96	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
97	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
98	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
99	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
100	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
101	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	03/2009 12/2012	10/2015	0/0
102	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
103	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
104	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
105	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	03/2004 -	03/2016	0/0
106	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
107	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
108	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
109	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
110	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
111	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	03/2007 -	03/2016	0/0
112	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	02/2009 02/2009	04/2016	0/0
113	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
114	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	10/2016	0/0
115	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
116	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	12/2016	0/0
117	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
118	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
119	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
120	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
121	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
122	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
123	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
124	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
125	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
126	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19	04/2008 12/2011	06/2017	0/0
127	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
128	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	12/2017	0/0
129	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
130	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
131	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
132	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
133	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
134	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
135	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
136	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
137	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	- -	03/2018	0/0
138	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
139	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
140	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0
141	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
142	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJBHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
143	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
144	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
145	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
146	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
148	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
149	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
150	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
151	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
152	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
153	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
154	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
155	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
156	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	03/1998 -	12/2019	0/0
157	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
158	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
159	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
160	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
161	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
162	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
163	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
164	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
166	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-	0/0
167	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-	0/0
168	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345], UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
169	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
170	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
171	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
172	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
173	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
174	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
175	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
176	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
177	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
178	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
179	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
180	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
181	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
182	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
183	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
184	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
185	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
186	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
187	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
188	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
189	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
190	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
191	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
192	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
193	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
194	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
195	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
196	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
197	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
198	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
199	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
200	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
201	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
202	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
203	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
204	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
205	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
206	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
207	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
208	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
209	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
210	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
211	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
212	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
213	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
214	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
215	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
216	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
217	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
218	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
219	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
220	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
221	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
222	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
223	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
224	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
225	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
226	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
227	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
228	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
229	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
230	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
231	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
232	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
233	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
234	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
235	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
236	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
237	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
238	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
239	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
240	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
241	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
242	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
243	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
244	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
245	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
246	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
247	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
248	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
249	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
250	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
251	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
252	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
253	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
254	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
255	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
256	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
257	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
258	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
259	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
260	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
261	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
262	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
263	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
264	HAJIPUR-RAMDALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
265	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
266	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0

(December 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
267	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
268	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
269	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
270	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
271	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
272	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
273	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
274	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
275	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
276	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
277	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRT, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
278	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
279	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAGAR - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
280	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
281	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
282	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
283	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
284	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
285	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
286	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR-CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
287	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
288	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
289	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
290	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
291	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
292	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
293	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
294	BARIPUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
295	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
296	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
297	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
298	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
299	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
300	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
301	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
302	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
303	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
304	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
305	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
306	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
307	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
308	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
309	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
310	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
311	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
312	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
313	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
314	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0

(December 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
316	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
317	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
318	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
319	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
320	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
321	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
322	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
323	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
324	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
325	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
326	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
327	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
328	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
329	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
330	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
331	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
332	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
333	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
334	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
335	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
336	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
337	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
338	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
339	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
340	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
341	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
342	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
343	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
344	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
345	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
346	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
347	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
348	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
349	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
350	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
351	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
352	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
353	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
354	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
355	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
356	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0
357	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
358	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-	0/0
359	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
360	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
361	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0
362	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
363	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00	-	-	0/0
364	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43	-	-	0/0
365	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00	-	-	0/0
366	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71	-	-	0/0
367	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00	-	-	0/0
368	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00	-	-	0/0
369	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00	-	-	0/0
370	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00	-	-	0/0
	Total		171,692.96			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
371	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22	01/2015	01/2015	0/0
372	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09	01/2015	01/2015	0/0
373	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00	02/2011	02/2011	0/0
374	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012	02/2012	0/0
375	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28	02/2013	02/2013	0/0
376	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51	02/2015	02/2015	0/0
377	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82	02/2015	02/2015	0/0
378	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41	03/2011	03/2011	0/0
379	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49	03/2011	03/2011	0/0
380	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47	03/2015	03/2015	0/0
381	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34	03/2015	03/2015	0/0
382	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54	03/2015	03/2015	0/0
383	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34	03/2015	03/2015	0/0
384	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52	04/2014	04/2014	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
385	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	05/2012	0/0
386	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	05/2014	0/0
387	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	05/2015 -	05/2015	0/0
388	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	07/2008	0/0
389	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	08/2013	0/0
390	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	08/2013	0/0
391	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	09/2015	0/0
392	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	10/2010	0/0
393	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	11/2008 -	11/2008	0/0
394	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU	01/1991	285.00 -	01/2008 -	11/2011	0/0
395	NAGPUR - KONDHALI - [N24000472]MEGA,MAHARASHTRA	09/2005	168.00 -	06/2006 -	12/2008	0/0
396	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 & 352.00-400.00 OF NH 63 (OLD NH-16) - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	12/2012	0/0
397	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	12/2015	0/0
398	TWO LANING OF HOJ - POTIN SECTION OF NH-229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	82.73 165.00	09/2010 -	09/2010	0/0
399	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
400	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
401	2-LANING OF SHILLONG - NONGSTOIN SECTION OF NH 44 AND NONGSTOIN - TURA STATE ROAD UNDER PHASE 'A' OF - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
402	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
403	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	03/2013	0/0
404	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
405	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015	0/0
406	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	07/2015	0/0
407	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	08/2015	0/0
408	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	08/2015	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
409	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
410	FOUR LANNING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
411	REHABILITATION & UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	12/2015 -	12/2015	0/0
412	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	01/2016	0/0
413	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	01/2016	0/0
414	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2016	01/2016	0/0
415	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	01/2016	0/0
416	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	01/2016	0/0
417	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	01/2016	0/0
418	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	01/2016	0/0
419	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	01/2016	0/0
420	2-LANNING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	01/2016	0/0
421	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	01/2016	0/0
422	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	01/2016	0/0
423	2-LANNING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	01/2016	0/0
424	2-LANNING WITH PS SITARGANJ BAREILLY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	01/2016	0/0
425	2-LANNING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	01/2016	0/0
426	FOUR LANNING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2016 -	01/2016	0/0
427	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]MEGA,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	01/2016	0/0
428	FOUR LANNING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH	11/2015	867.66 -	11/2015 -	01/2016	0/0
429	FOUR LANNING OF GWALIOR-SHIVPURI - [N24000494]MEGA,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	01/2016	0/0
430	FOUR LANNING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2019 -	01/2016	0/0
431	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	02/2016	0/0
432	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	02/2016	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
433	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	02/2016	0/0
434	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	02/2016	0/0
435	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
436	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]MEGA,RAJASTHAN	03/2012	914.50 -	10/2015 -	02/2016	0/0
437	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	03/2016	0/0
438	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	03/2016	0/0
439	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	03/2016	0/0
440	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	03/2016	0/0
441	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	03/2016	0/0
442	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	03/2016	0/0
443	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	03/2016	0/0
444	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	03/2016	0/0
445	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	03/2016	0/0
446	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	03/2016	0/0
447	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	03/2016	0/0
448	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	03/2016	0/0
449	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	03/2016	0/0
450	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2016	0/0
451	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	03/2016	0/0
452	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	03/2016	0/0
453	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	03/2016	0/0
454	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2016	0/0
455	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	03/2016	0/0
456	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	03/2016	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
457	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	08/2013 -	03/2016	0/0
458	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	03/2016	0/0
459	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	06/2014 -	03/2016	0/0
460	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	06/2014 -	03/2016	0/0
461	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	10/2014 -	03/2016	0/0
462	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	03/2016	0/0
463	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	04/2014 -	03/2016	0/0
464	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	06/2014 -	03/2016	0/0
465	FOUR LANING OF ORISSA CHATTISGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
466	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	03/2016 -	03/2016	0/0
467	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH, UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
468	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
469	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2016	0/0
470	WIDENING WITH PS & STRONG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	03/2016	0/0
471	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	03/2008 04/2016	04/2016	0/0
472	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	06/2008 04/2016	04/2016	0/0
473	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	09/2010 -	04/2016	0/0
474	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	07/2013 -	04/2016	0/0
475	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	04/2016	0/0
476	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2016	0/0
477	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN	10/2013	677.79 -	04/2016 -	04/2016	0/0
478	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHAI, MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2016	0/0
479	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	05/2016	0/0
480	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2016	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
481	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	05/2016	0/0
482	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	05/2016	0/0
483	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
484	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	06/2016	0/0
485	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	06/2016	0/0
486	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2016	0/0
487	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
488	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	06/2016	0/0
489	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	06/2016	0/0
490	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2016	0/0
491	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2016	0/0
492	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2016	0/0
493	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	06/2016	0/0
494	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	06/2016	0/0
495	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	06/2016	0/0
496	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI,UTTAR PRADESH	06/2014	569.38 -	06/2016 -	06/2016	0/0
497	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2016	0/0
498	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]MEGA,HARYANA	03/2013	959.25 -	06/2016 -	06/2016	0/0
499	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 12/2015	07/2016	0/0
500	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 12/2015	07/2016	0/0
501	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016	0/0
502	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 02/2016	08/2016	0/0
503	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	08/2016	0/0
504	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	08/2016	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
505	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	08/2016	0/0
506	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	08/2016	0/0
507	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH, BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
508	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD, MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
509	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	08/2016	0/0
510	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI, MADHYA PRADESH	02/2012	912.00 -	08/2016 -	08/2016	0/0
511	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2016	0/0
512	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	08/2016	0/0
513	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	09/2016	0/0
514	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2016	0/0
515	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	10/2013 -	09/2016	0/0
516	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
517	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2016	0/0
518	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2016	0/0
519	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD, MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
520	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI, HARYANA	12/2012	438.75 -	09/2016 -	09/2016	0/0
521	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	10/2016	0/0
522	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH, UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
523	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH, RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
524	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377]NHDP, UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
525	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH, BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
526	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP, UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
527	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD, ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
528	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
529	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	11/2016	0/0
530	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	12/2016	0/0
531	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	12/2016	0/0
532	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2016	0/0
533	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
534	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2016	0/0
535	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2016	0/0
536	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2016	0/0
537	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2016	0/0
538	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2016	0/0
539	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
540	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2016	0/0
541	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	12/2016	0/0
542	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016	0/0
543	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
544	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	12/2016	0/0
545	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	01/2017	0/0
546	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
547	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	01/2017	0/0
548	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
549	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	02/2017	0/0
550	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017	0/0
551	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
552	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2017	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
553	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	03/2017	0/0
554	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	03/2017	0/0
555	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
556	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
557	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
558	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
559	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2017	0/0
560	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN	10/2014	206.12 -	04/2017 -	04/2017	0/0
561	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017	0/0
562	CHAMBAL BRIDGE, NH-76 (R.J-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	05/2017	0/0
563	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	05/2017	0/0
564	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	05/2017	0/0
565	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	05/2017	0/0
566	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	05/2017	0/0
567	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
568	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
569	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
570	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
571	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI,TAMIL NADU	12/2014	451.58 -	06/2017 -	06/2017	0/0
572	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	07/2017	0/0
573	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
574	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
575	4-LANING OF SOLAPUR - YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	07/2017	0/0
576	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
577	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
578	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
579	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
580	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
581	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	10/2017	0/0
582	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2017	0/0
583	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
584	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
585	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
586	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
587	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
588	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
589	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2017	0/0
590	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
591	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
592	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
593	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	12/2017	0/0
594	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
595	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
596	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
597	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
598	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
599	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
600	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
601	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
602	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
603	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
604	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI, UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
605	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI, UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
606	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI, UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
607	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, HARYANA	09/2015	788.51 -	03/2018 -	03/2018	0/0
608	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
609	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
610	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
611	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
612	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA - BARWALA - PANCHKULA (PKG - 2) - [N24000358]NHAI, HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
613	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
614	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH, ODISHA	01/1991	229.41 -	05/2018 -	05/2018	0/0
615	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	06/2018	0/0
616	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
617	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
618	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
619	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
620	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
621	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
622	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
623	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
624	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	07/2018	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
625	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
626	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	11/2018	0/0
627	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
628	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	01/2019	0/0
629	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
630	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 -	-	0/0
631	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
632	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
633	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
634	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
635	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
636	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
637	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
638	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
639	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
640	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
641	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
642	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-	0/0
643	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-	0/0
644	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	-	0/0
645	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	-	0/0
646	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0
647	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-	0/0
648	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
649	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-	0/0
650	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-	0/0
651	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
652	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
653	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-	0/0
654	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
655	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
656	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
657	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
658	REHABILITATION & UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
659	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
660	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
661	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
662	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
663	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
664	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
665	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-	0/0
666	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
667	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
668	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
669	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
670	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
671	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
672	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
673	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
674	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
675	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
676	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
677	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
678	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
679	WIDENING & STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISAR - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
680	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-	0/0
681	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
682	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	01/1991	225.02 -	- -	-	0/0
683	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	01/1991	223.30 -	- -	-	0/0
684	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
685	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.00 -	- -	-	0/0
686	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH	06/2015	583.79 -	- -	-	0/0
687	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B & FROM 5.300 TO KM 7.422 (OL - [N24000435]NHAI,WEST BENGAL	10/2015	531.13 -	- -	-	0/0
688	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]MEGA,WEST BENGAL	10/2015	361.15 -	- -	-	0/0
689	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	01/1991	289.99 -	- -	-	0/0
690	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-	0/0
691	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-	0/0
692	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-	0/0
693	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
694	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-	0/0
695	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	-	0/0
696	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
697	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	- -	-	0/0
698	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-	0/0
699	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
700	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
701	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
702	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,ANDAMAN & NICOBAR ISLANDS	09/2015	273.06 -	- -	-	0/0
703	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-	0/0
704	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]MEGA,BIHAR	08/2015	814.04 -	- -	-	0/0
705	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	-	0/0
706	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
707	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,WEST BENGAL	12/2015	1,423.96 -	- -	-	0/0
708	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	-	0/0
709	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
710	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	- -	-	0/0
711	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-	0/0
712	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	- -	-	0/0
713	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-	0/0
714	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
715	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-	0/0
716	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
717	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-	0/0
718	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-	0/0
719	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
720	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
721	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
722	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH, GOA	12/2015	819.95 -	- -	-	0/0
723	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	- -	-	0/0
724	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	- -	-	0/0
725	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH, BIHAR	01/1991	478.35 -	- -	-	0/0
726	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-	0/0
727	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-	0/0
728	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	- -	-	0/0
729	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD, PUNJAB	06/2015	892.17 -	- -	-	0/0
730	ROHTAK - BAWAL (APPROVED LENGTH 97 KM) - [N24000525]NHAI, HARYANA	02/2010	650.00 -	- -	-	0/0
731	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD, PUNJAB	06/2015	899.21 -	- -	-	0/0
732	WIDENING & STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH, UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
733	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD, BIHAR	01/1991	154.62 -	- -	-	0/0
734	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD, BIHAR	01/1991	319.68 -	- -	-	0/0
	Total		225,873.34 -			0/0
	<u>SHIPPING AND PORTS</u>					
735	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	03/2006 -	01/2016	0/0
736	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	12/2010 -	01/2016	0/0
737	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	04/2009 03/2010	08/2016	0/0
738	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL, TAMIL NADU	12/2014	274.85 -	04/2017 -	04/2017	0/0
739	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL, TAMIL NADU	10/2013	198.94 -	06/2017 -	06/2017	0/0
740	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL, TAMIL NADU	02/2015	244.50 258.00	12/2017 -	12/2017	0/0
741	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL, TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
742	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0

(December 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	Total		4,117.75 -			0/0
	<u>TELECOMMUNICATIONS</u>					
743	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 -	03/2017	0/0
	Total		13,334.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
744	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
745	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	08/2014 -	01/2016	0/0
746	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	03/2016	0/0
747	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
748	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	05/2013 10/2015	06/2016	0/0
749	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
750	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	12/2014 -	12/2016	0/0
751	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	09/2016 01/2017	01/2017	0/0
752	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD, ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
753	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	07/2017 -	06/2017	0/0
754	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
755	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
756	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 26,405.01	02/2019 -	03/2020	0/0
757	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33 -	11/2014 -	-	0/0
758	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB	02/2014	388.00 -	01/2015 -	-	0/0
759	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD, TAMIL NADU	12/2015	209.00 -	- -	-	0/0
760	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD, BIHAR	02/2012	171.10 -	09/2014 -	-	0/0
761	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD, DELHI	01/2010	162.90 -	07/2012 -	-	0/0
762	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43 -	02/2015 -	-	0/0

(December 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
763	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-	0/0
764	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	-	0/0
765	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	-	0/0
766	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
767	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	-	0/0
768	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		110,970.58 -			0/0
	Grand Total		618,050.05			0/0

Annexure-XI

List of Projects Ahead of Schedule w.r.t. Latest Schedule

							(December 2015)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	75.15	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	75.15		
	<u>PETROLEUM</u>						
2	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	164.88	09/2017 03/2018	12/2017
	Total		3,076.00 -	3,076.00	164.88		
	<u>POWER</u>						
3	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	2/2015	302.49 -	302.49	229.19	02/2016 -	01/2016
	Total		302.49 -	302.49	229.19		
	<u>COAL</u>						
4	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
5	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	70.80	02/2017 -	03/2016
	Total		188.75 -	188.75	70.80		
	<u>PETROLEUM</u>						
6	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	219.00	160.78	09/2016 -	03/2016
7	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	254.80	01/2017 -	06/2016
	Total		560.90 -	638.04	415.58		
	<u>URBAN DEVELOPMENT</u>						

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
8	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,562.95		
	<u>PETROLEUM</u>						
9	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	6,068.80	523.70	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	523.70		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
10	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497	3/2015	830.36	830.36	-	01/2019 -	01/2016
	Total		830.36 -	830.36	.00		
	Grand Total		17,024.01	17,328.32	4,045.77		

Annexure-XII

List of Projects on schedule w.r.t. Latest Schedule

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
2	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.43	03/2016 -	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	203.82	03/2017 -	03/2017
4	MALACHUA OPENCASE PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
5	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	30.90	03/2018 -	03/2018
6	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	158.47	03/2021 -	03/2021
7	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	61.37	03/2025 -	03/2025
8	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	620.51	03/2026 -	03/2026
9	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	28.78	03/2021 -	03/2021
10	AMGAON OPENCASE PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	15.85	03/2020 -	03/2020
11	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
12	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	94.45	03/2021 -	03/2021
13	MOONIDH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	47.76	04/2015 04/2019	04/2019
14	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	197.01	03/2018 -	03/2018
15	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
16	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	-	03/2018 -	03/2018
17	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020
18	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	131.57	03/2020 -	03/2020
19	MADANNAGAR OPENCASE PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
20	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	108.45	03/2020 -	03/2020
21	GOKUL - [N06000120]	11/2014	267.67 -	267.67	176.63	03/2018 -	03/2018

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
22	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
23	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.25	03/2019 -	03/2019
24	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
25	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
26	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	39.36	03/2021 -	03/2021
27	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	784.34	03/2023 03/2023	03/2023
28	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	125.13	03/2016 -	03/2016
29	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
30	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
31	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	808.54	03/2016 -	03/2016
32	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
33	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	79.03	03/2019 -	03/2019
34	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
35	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
36	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.29	03/2019 -	03/2019
37	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
38	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
39	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	49.30	03/2023 -	03/2023
40	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	140.70	03/2018 -	03/2018
41	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	194.04	03/2020 -	03/2020
42	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	1,297.62	12/2015 04/2018	04/2018
43	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
	Total		41,792.92 -	41,632.12	5,873.35		
	FERTILISERS						

						(December 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	43.68	11/2016 -	11/2016
	Total		197.79 -	197.79	43.68		
	<u>HEALTH AND FAMILY WELFARE</u>						
45	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70 -	196.70	157.61	01/2016 -	01/2016
46	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	168.90	0.05	05/2017 -	05/2017
47	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	293.65	36.53	05/2017 -	05/2017
48	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	204.44	21.73	05/2017 -	05/2017
49	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	9.74	03/2018 -	03/2018
	Total		1,369.27 -	1,369.27	225.66		
	<u>MINES</u>						
50	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]	12/2015	355.13 -	355.13	-	11/2016 -	11/2016
51	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	-	11/2016 -	11/2016
	Total		699.63 -	699.63	.00		
	<u>PETROLEUM</u>						
52	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	586.87	05/2019 03/2020	03/2020
53	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	59.42	10/2017 10/2017	10/2017
54	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
55	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	9,397.86	05/2016 -	05/2016
56	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,282.07	03/2015 05/2016	05/2016
57	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	137.49	12/2016 -	12/2016
58	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	368.95	12/2018 -	12/2018
59	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	2,268.83	05/2017 05/2017	05/2017

						(December 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
60	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
61	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	736.65	498.95	09/2011 10/2016	10/2016
62	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	1,292.13	11/2015 07/2016	07/2016
63	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
64	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	111.66	09/2017 -	09/2017
65	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	570.28	11/2015 11/2016	11/2016
66	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	995.12	05/2013 04/2016	04/2016
67	CONSTRUCTION OF 6 ETSPS - [N16000117]	3/2009	317.64 -	240.95	123.32	09/2012 03/2016	03/2016
68	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	34.49	11/2016 -	11/2016
69	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	68.96	07/2016 -	07/2016
70	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,941.49	521.23	04/2016 12/2017	12/2017
71	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
72	IOR OF B-173A FIELD - [N16000140]	1/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016
73	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	830.50	05/2014 05/2016	05/2016
74	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
75	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	81.45	12/2017 -	12/2017
76	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	50.18	07/2016 -	07/2016
77	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	502.37	05/2017 -	05/2017
78	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	258.68	10/2014 03/2017	03/2017
79	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
	Total		59,633.87 -	63,643.25	20,183.67		

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
80	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	142.00	08/2017 -	08/2017
81	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	965.00	12/2016 -	12/2016
82	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	243.10	04/2018 -	04/2018
83	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	11,225.70	08/2013 12/2017	12/2017
84	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	115.70	04/2020 -	04/2020
85	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
86	TRIPURA GAS BASED POWER PROJECT - [N18000071]	7/2009	421.01 -	1,007.57	953.59	07/2013 01/2016	01/2016
87	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	53.40	02/2017 -	02/2017
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	431.09	03/2016 -	03/2016
89	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,287.00	02/2019 -	02/2019
90	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
91	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
92	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	4,822.73	01/2018 -	01/2018
93	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	2,378.00	08/2018 -	08/2018
94	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
95	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
96	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	47.20	11/2016 -	11/2016
97	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	623.05	05/2016 -	05/2016
98	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	295.10	05/2018 -	05/2018
99	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	-	10/2016 -	10/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	116.00	06/2016 -	06/2016
101	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	113.10	10/2016 -	10/2016
102	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	19.70	07/2016 -	07/2016
103	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	939.00	03/2019 -	03/2019
104	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	22.60	03/2018 -	03/2018
105	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	4,611.00	09/2017 -	09/2017
106	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	153.00	09/2019 -	09/2019
107	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	2,978.86	1,545.54	02/2016 09/2019	09/2019
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	101.70	06/2016 -	06/2016
109	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	3.10	10/2017 -	10/2017
110	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,381.71	930.00	07/2006 10/2016	10/2016
111	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	45.19	04/2017 -	04/2017
112	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	67.10	04/2017 -	04/2017
113	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	2.30	03/2016 -	03/2016
114	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,085.84	4,303.08	12/2009 06/2016	06/2016
115	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	430.87	04/2016 -	04/2016
116	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	16.00	07/2018 -	07/2018
117	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	5,419.00	06/2017 -	06/2017
118	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	434.29	12/2016 -	12/2016
119	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	1,085.04	08/2013 07/2016	07/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
120	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	64.00	08/2016 -	08/2016
121	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	0.80	11/2017 -	11/2017
122	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	10.00	05/2016 -	05/2016
123	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	4.60	03/2018 -	03/2018
124	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	175.30	04/2018 -	04/2018
125	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
126	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018
	Total		141,960.53 -	151,791.77	45,919.05		
	<u>RAILWAYS</u>						
127	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
128	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017
129	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
130	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
131	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019
132	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
133	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
134	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
	Total		9,145.53 -	19,332.36	3,046.94		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
135	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]	3/2015	830.36 -	830.36	-	01/2016 -	01/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
137	JALANDHAR - AMRITSAR - [N24000351	1/2014	523.85 -	523.85	74.12	01/2016 -	01/2016
138	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
139	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456	3/2013	959.25 -	959.25	523.50	06/2016 -	06/2016
140	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443	12/2015	602.95 -	602.95	-	06/2016 -	06/2016
141	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
142	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
143	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA- JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
144	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
145	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	3/2015	829.00 -	829.00	-	03/2018 -	03/2018
146	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350	6/2015	563.92 -	563.92	-	12/2017 -	12/2017
147	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
148	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	682.13	04/2016 -	04/2016
149	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	830.19	01/2018 -	01/2018
150	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
151	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
152	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
153	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
154	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
156	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]	12/2013	177.18 -	177.18	-	03/2016 -	03/2016
157	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
158	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017
159	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]	1/1991	269.26 -	269.26	-	10/2016 -	10/2016
160	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
161	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	282.41	-	08/2016 -	08/2016
162	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]	2/2015	327.32 -	327.32	-	05/2017 -	05/2017
163	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
164	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
165	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]	12/2013	158.65 -	158.65	-	03/2016 -	03/2016
166	4-LANING OF SOLAPUR - YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	-	07/2017 -	07/2017
167	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
168	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
169	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
170	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
171	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	3/2011	218.31 -	339.82	-	12/2015 -	12/2015
172	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	674.20	09/2016 -	09/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
173	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- [N24000340	12/2014	451.58 -	451.58	-	06/2017 -	06/2017
174	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
175	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377	1/2014	397.04 -	397.04	-	10/2016 -	10/2016
176	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381	3/2013	257.80 -	257.80	-	02/2016 -	02/2016
177	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
178	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
179	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
180	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287	11/2015	485.44 -	485.44	-	12/2015 -	12/2015
181	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5 - [N24000320	10/2014	463.49 -	463.49	-	06/2018 -	06/2018
182	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	-	05/2018 -	05/2018
183	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017
184	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461	12/2012	438.75 -	438.75	0.63	09/2016 -	09/2016
185	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	282.41	31.64	03/2016 -	03/2016
186	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017
187	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	-	10/2016 -	10/2016
188	FOUR LANING OF CHADIGARH - KHARAR - [N24000503	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
189	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	244.30	-	12/2016 -	12/2016
190	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
191	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	582.00	08/2016 -	08/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
192	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]	3/2015	511.83 -	511.83	-	08/2017 -	08/2017
193	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
194	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	137.69	03/2016 -	03/2016
195	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]	1/2014	270.00 -	270.00	50.85	03/2016 -	03/2016
196	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
197	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
198	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
199	VADODARA-SURAT SECTION - [N24000361]	3/2014	503.16 -	503.16	52.89	08/2016 -	08/2016
200	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
201	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	-	05/2017 -	05/2017
202	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
203	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	295.20	04/2008 01/2017	01/2017
204	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
205	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19 -	425.19	4.60	09/2016 -	09/2016
206	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]	11/2014	563.92 -	563.92	-	11/2016 -	11/2016
207	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
208	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]	6/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016
209	PADI - DAHOD - [N24000353]	11/2014	279.14 -	279.14	-	05/2017 -	05/2017
210	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
211	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	-	09/2017 -	09/2017

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
212	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
213	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367	4/2014	495.78 -	495.78	-	01/2016 -	01/2016
214	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	-	03/2017 -	03/2017
215	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
216	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
217	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
218	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428	6/2014	569.38 -	569.38	680.83	06/2016 -	06/2016
219	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	-	03/2018 -	03/2018
220	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	351.34	4.77	01/2016 -	01/2016
221	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
222	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
223	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
224	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
225	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
226	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018
227	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
228	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	-	02/2018 -	02/2018
229	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
230	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	-	03/2018 -	03/2018

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
231	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	-	03/2017 -	03/2017
232	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
233	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017
234	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00 -	709.00	-	09/2017 -	09/2017
235	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]	6/2014	301.04 -	301.04	51.79	01/2016 -	01/2016
236	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018
237	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
238	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	0.88	02/2018 -	02/2018
239	REHABILITATION & UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]	12/2015	291.05 -	291.05	-	12/2015 -	12/2015
240	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	214.17	03/2008 04/2016	04/2016
241	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	10/2014	437.39 -	437.39	-	06/2018 -	06/2018
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATTA - [N24000379]	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
243	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]	9/2015	368.73 -	368.73	-	09/2016 -	09/2016
244	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	227.68	08/2016 -	08/2016
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
246	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	0.74	04/2017 -	04/2017
247	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016
248	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	242.40	04/2008 01/2016	01/2016
249	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	917.89	11/2016 -	11/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
250	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72	264.72	-	04/2017	04/2017
251	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244	1/2014	340.00	340.00	-	03/2016	03/2016
252	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11	194.11	-	05/2018	05/2018
253	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTON) TO TW - [N24000243	12/2013	244.08	244.08	114.72	03/2016	03/2016
254	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60	455.60	-	07/2017	07/2017
255	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263	2/2015	241.61	241.61	23.83	02/2017	02/2017
256	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22	176.22	106.61	02/2018	02/2018
257	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34	562.34	-	04/2018	04/2018
258	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239	1/2014	368.15	368.15	153.02	01/2016	01/2016
259	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11	401.11	1.75	01/2017	01/2017
260	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00	667.00	-	06/2018	06/2018
261	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253	8/2014	187.79	187.79	-	07/2016	07/2016
262	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57	774.57	-	03/2018	03/2018
263	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90	822.90	-	04/2018	04/2018
	Total		67,470.35	67,819.45	7,573.30		
	SHIPPING AND PORTS						
264	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85	274.85	0.38	04/2017	04/2017
265	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94	198.94	37.70	06/2017	06/2017
266	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00	210.00	-	01/2018	01/2018

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
267	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017
	Total		928.29 -	942.12	38.36		
	<u>STEEL</u>						
268	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	8/2010	17,265.00 -	17,265.00	15,431.95	03/2013 10/2016	10/2016
269	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	2.61	09/2017 -	09/2017
270	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	232.80	04/2018 -	04/2018
271	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.90	04/2018 -	04/2018
272	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	173.00	175.89	12/2015 -	12/2015
273	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
274	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	19.87	09/2016 -	09/2016
275	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]	10/2012	160.48 -	160.48	143.50	09/2014 01/2016	01/2016
276	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	79.89	05/2016 -	05/2016
277	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	27.45	12/2017 -	12/2017
278	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 207.00	207.00	129.17	12/2016 -	12/2016
279	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
280	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]	12/2011	187.33 -	187.33	173.07	10/2013 06/2016	06/2016
281	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]	7/2011	324.87 325.00	325.00	263.57	12/2015 -	12/2015
282	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 254.00	254.00	192.96	06/2016 -	06/2016
283	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	237.09	220.15	12/2014 05/2016	05/2016
284	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	290.11	04/2016 09/2016	09/2016

(December 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
285	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	229.56	08/2014 02/2016	02/2016
286	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	195.46	12/2016 -	12/2016
287	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
288	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]	4/2014	151.33 -	151.33	4.84	09/2017 -	09/2017
289	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]	2/2014	787.29 -	787.29	23.83	12/2016 -	12/2016
290	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	8,318.82	05/2015 12/2016	12/2016
291	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	126.65	03/2018 -	03/2018
292	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	314.87	06/2015 02/2016	02/2016
	Total		48,179.10 -	48,258.48	26,707.97		
	<u>URBAN DEVELOPMENT</u>						
293	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]	1/2009	225.81 -	225.81	138.36	06/2012 03/2016	03/2016
294	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
295	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	50.91	03/2018 -	03/2018
296	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	948.27	11/2019 -	11/2019
297	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
298	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	58.72	09/2016 01/2017	01/2017
	Total		14,879.58 -	14,879.58	1,196.26		
	Grand Total		386,256.86	410,565.82	110,808.24		

Annexure-XIII

List of ongoing projects having cost overrun w.r.t. to revised schedule

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	09/2010	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	22,462.00	12/2008	06/2016	70.54
	Total		16,663.00	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60	244.10	03/2015	09/2015	12.18
	Total		217.60	244.10			
	<u>COAL</u>						
4	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97	489.62	03/2012	03/2023	16.86
	Total		418.97	489.62			
	<u>HEAVY INDUSTRY</u>						
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00	3,827.30	09/2011	12/2017	122.78
	Total		1,718.00	3,827.30			
	<u>PETROCHEMICALS</u>						
6	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61	9,965.00	04/2012	12/2015	82.49
	Total		5,460.61	9,965.00			
	<u>PETROLEUM</u>						
7	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56	450.55	03/2017	03/2017	27.79
8	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86	219.00	09/2016	03/2016	54.38

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00 -	05/2016 -	05/2016	16.02
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00 -	03/2015 -	08/2016	37.72
	Total		15,590.77 -	18,373.55 -			
	<u>POWER</u>						
11	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68 -	09/2009 -	12/2018	99.48
12	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,063.89 -	09/2010 -	-	187.40
13	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15 -	09/2009 -	06/2016	81.76
14	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49 -	02/2016 -	01/2016	0.00
15	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67 -	12/2011 -	03/2016	83.21
16	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82 -	02/2011 -	01/2017	133.06
17	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72 -	01/2016 -	11/2016	50.95
	Total		21,645.83 -	47,456.42 -			
	<u>RAILWAYS</u>						
18	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57 -	- -	03/2019	3,531.98
19	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37 -	- -	02/2012	141.40
20	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00 -	- -	-	414.30
21	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27 -	12/2010 -	03/2018	250.37
22	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00 -	- 05/2009	03/2015	248.16
23	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00 -	- -	-	300.71
24	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00 -	- -	-	217.27
25	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92 -	12/2006 -	-	224.37
26	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00 -	02/2011 -	-	191.48

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
27	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
28	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
29	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
30	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
31	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
32	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
33	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
34	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
35	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
36	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
37	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
38	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
39	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	360.00	02/2006 -	-	37.56
40	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
41	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
42	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
43	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
44	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
45	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
46	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
47	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
48	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
49	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
50	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55 -	03/2014 -	-	0.06
51	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25 -	03/2012 -	-	135.68
52	KATAKHAL TO BHAI RABI - [N22000126]	04/1998	227.90 -	331.40 -	12/2012 -	03/2016	45.41
53	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05 -	- -	-	400.91
54	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70 -	- -	-	0.72
55	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00 -	- -	03/2015	105.59
56	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16 -	- -	01/2015	170.55
57	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01 -	- -	-	97.26
58	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91 -	- -	-	651.97
59	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30 -	- -	-	160.97
60	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00 -	- -	-	985.42
61	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18 -	- -	-	100.76
62	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99 -	- -	-	183.41
63	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43 -	- -	-	24.09
64	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65 -	- -	-	57.65
65	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47 -	- -	-	47.93
66	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00 -	- -	-	79.63
67	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85 -	- -	-	2.29
68	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50 -	- -	-	0.00
69	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97 -	- -	-	50.10
70	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50 -	- -	-	14.14
71	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00 -	- -	-	72.07
72	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77 -	- -	-	12.38
73	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00 -	01/1999 -	-	123.46

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
74	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
75	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
76	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
77	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
79	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
80	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
81	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
82	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
83	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
84	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
85	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
86	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
87	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
88	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
89	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
90	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
91	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
92	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
93	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
94	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
95	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
96	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
97	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
98	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
99	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
100	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
101	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
102	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
103	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
104	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
105	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
106	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
107	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
108	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
109	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
110	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
111	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345	04/1997	836.26 -	1,072.51	- -	-	28.25
112	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
113	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
114	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
115	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
116	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
117	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
118	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60 -	- -	03/2018	38.35
120	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71 -	03/2015 -	-	42.11
121	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73 -	- -	-	8.10
122	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00 -	12/2016 -	12/2016	40.49
123	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30 -	- -	02/2014	643.63
124	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00 -	06/1999 -	07/2012	9.35
125	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00 -	- -	-	184.73
126	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92 -	- -	-	67.77
127	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17 -	- -	-	53.63
128	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00 -	- -	-	68.05
129	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00 -	- -	-	10.58
130	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16 -	- -	-	87.54
131	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22 -	- -	-	17.92
132	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39 -	- -	-	2.34
133	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00 -	- -	-	62.32
134	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00 -	- -	12/2019	82.25
135	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00 -	- -	-	162.39
136	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00 -	03/2015 -	12/2016	53.44
137	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00 -	12/2015 -	03/2016	88.40
138	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00 -	- -	12/2017	41.36
139	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00 -	- -	-	84.98
140	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56 -	- -	-	32.80
141	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09 -	- -	-	338.91

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
142	HAJIPUR-RAMDALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
143	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
144	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
145	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
146	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
147	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
148	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
149	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
150	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
151	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
152	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
153	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
154	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
155	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
156	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
157	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
158	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
159	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
160	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
161	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
162	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
163	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
164	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
165	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17	1,653.55	-	03/2018	216.06
166	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	312.12	453.10	-	03/2018	45.17
167	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07	364.06	-	03/2019	47.95
168	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68	816.55	03/2016	12/2017	29.06
169	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43	800.00	-	-	33.02
	Total		77,516.05	194,083.93			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
170	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00	361.00	02/2009	03/2016	28.93
171	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81	385.13	04/2009	03/2016	92.75
172	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04	280.13	11/2008	03/2016	80.68
173	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00	331.23	07/2009	03/2016	68.99
174	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00	2,288.00	11/2011	06/2016	106.50
175	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00	201.66	09/2008	01/2016	30.10
176	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00	281.31	02/2010	05/2017	2.29
177	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47	313.27	02/2017	02/2017	6.02
178	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31	339.82	12/2015	-	55.66
179	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017	09/2017	36.24
180	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017	11/2017	31.78
181	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015	-	0.00
182	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00	201.00	09/2010	09/2010	93.27
	Total		3,710.66	5,884.15			

(December 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
183	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	01/2016	300.00
184	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
185	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
	Total		640.17 -	1,268.16			
	<u>STEEL</u>						
186	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
187	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	13,845.01	06/2011 -	06/2016	116.50
	Total		6,395.00 -	13,845.01			
	Grand Total		150,319.66	324,064.64			

Annexure-XIV

List of Delayed Projects w.r.t. Latest Schedule

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,025.00	12/2008 10/2013	06/2016	90	32
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,129.59	09/2010 -	09/2016	72	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	7,711.00	12/2015 10/2016	10/2017	22	12
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,403.00	12/2016 04/2017	05/2018	17	13
	Total		40,442.00 -	51,918.00	39,268.59				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	408.55	01/2011 06/2016	09/2017	80	15
	Total		309.46 -	309.46	408.55				
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,925.28	03/2014 -	03/2016	24	-
7	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,713.30	03/2014 -	03/2016	24	-
8	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 741.62	741.62	498.75	03/2013 -	03/2016	36	-
9	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 535.10	535.10	424.18	03/2015 -	03/2016	12	-
10	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	866.72	03/2013 09/2012	03/2016	36	42
11	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	69.02	03/2014 -	03/2016	24	-
12	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	76.28	03/2015 -	03/2016	12	-
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	67.47	03/2012 -	03/2016	48	-
14	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	36.08	03/2011 -	03/2016	60	-
15	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	-
16	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.06	04/2014 -	03/2016	23	-
17	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	183.91	10/2014 -	03/2016	17	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	99.28	05/2014 -	10/2016	29	-
19	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	62.95	04/2014 -	11/2016	31	-
20	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	297.62	03/2010 -	03/2017	84	-
21	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72	-
22	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72	-
23	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	208.05	03/2013 -	03/2017	48	-
24	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	150.27	03/2010 -	03/2017	84	-
25	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51	-
26	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	205.98	03/2012 -	03/2017	60	-
27	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	175.70	03/2013 -	03/2017	48	-
28	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	91.85	03/2012 -	03/2017	60	-
29	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48	-
30	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	70.20	03/2014 -	03/2017	36	-
31	RG OC -II EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	-
32	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	14.18	07/2016 -	03/2017	8	-
33	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	76.98	03/2012 -	03/2018	72	-
34	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	209.59	03/2014 -	03/2018	48	-
35	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	-
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	-
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	-
38	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	96.39	03/2016 -	03/2018	24	-
39	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 486.27	486.27	93.51	03/2016 -	03/2018	24	-
40	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	1,458.17	8.68	06/2015 -	08/2019	50	-
41	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	-
42	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	-
43	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
44	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	77.78	07/2012 -	03/2021	104	-
45	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-
46	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	411.47	03/2012 -	03/2023	132	-
	Total		18,511.83 -	19,395.15	9,165.72				
	<u>MINES</u>								
47	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N1000007]JCL,MADHYA PRADESH	09/2011	1,856.00 -	1,176.00	2.86	09/2017 -	04/2020	31	-
	Total		1,856.00 -	1,176.00	2.86				
	<u>STEEL</u>								
48	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	370.73	07/2015 -	06/2016	11	-
49	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	215.52	07/2016 -	12/2016	5	-
50	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	248.38	07/2015 -	06/2017	23	-
51	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	36.00	10/2016 -	06/2017	8	-
	Total		2,599.65 -	2,745.05	870.63				
	<u>PETROCHEMICALS</u>								
52	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	9,965.00	9,103.96	04/2012 12/2013	12/2015	44	24
	Total		5,460.61 -	9,965.00	9,103.96				
	<u>PETROLEUM</u>								
53	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	30,818.63	11/2012 11/2013	01/2016	38	26
54	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,663.75	01/2014 12/2015	01/2016	24	1
55	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	186.98	12/2014 -	01/2016	13	-
56	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 -	01/2016	43	-
57	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,261.12	09/2012 -	03/2016	42	-
58	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,366.24	08/2015 -	03/2016	7	-
59	VKPL UPGRADEATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	315.82	06/2011 03/2012	03/2016	57	48

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
60	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	407.88	08/2015 -	03/2016	7	-
61	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,029.66	10/2011 -	03/2016	53	-
62	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	12
63	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	552.58	04/2015 04/2015	05/2016	13	13
64	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,446.59	01/2012 -	05/2016	52	-
65	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	35.07	02/2016 02/2016	05/2016	3	3
66	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	126.43	02/2016 -	07/2016	5	-
67	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	455.47	03/2015 11/2015	08/2016	17	9
68	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	460.06	08/2015 -	12/2016	16	-
69	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	100.19	11/2016 -	12/2016	1	-
70	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,789.87	03/2013 03/2016	03/2017	48	12
71	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	25.93	01/2013 -	12/2018	71	-
72	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	98.84	05/2015 -	12/2015	7	-
	Total		50,502.45 -	55,815.58	42,516.25				
	<u>POWER</u>								
73	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	757.94	11/2012 -	01/2016	38	-
74	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,950.24	03/2013 06/2015	01/2016	34	7
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,444.82	04/2013 -	01/2016	33	-
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	360.37	02/2012 -	02/2016	48	-
77	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	184.20	01/2013 -	02/2016	37	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
78	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,307.76	08/2014 -	02/2016	18	-
79	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	302.97	08/2014 06/2015	02/2016	18	8
80	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,573.17	10/2014 -	02/2016	16	-
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	282.92	05/2015 -	02/2016	9	-
82	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,062.99	08/2012 -	03/2016	43	-
83	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,570.76	11/2013 -	03/2016	28	-
84	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	520.31	11/2013 -	03/2016	28	-
85	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	574.60	02/2014 -	03/2016	25	-
86	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	88.20	12/2015 -	03/2016	3	-
87	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,125.22	01/2013 -	03/2016	38	-
88	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	-
89	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,937.70	09/2009 -	06/2016	81	-
90	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	577.79	09/2010 06/2013	06/2016	69	36
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	523.76	11/2011 -	06/2016	55	-
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	541.02	07/2013 11/2015	06/2016	35	7
93	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,784.85	05/2014 -	06/2016	25	-
94	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,888.96	09/2014 -	06/2016	21	-
95	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,303.03	07/2014 -	06/2016	23	-

(December 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
96	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,475.53	08/2014 12/2015	06/2016	22	6
97	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	1,373.62	01/2015 -	06/2016	17	-
98	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	93.03	09/2014 -	06/2016	21	-
99	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	5,337.19	06/2015 -	06/2016	12	-
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	583.62	11/2014 -	06/2016	19	-
101	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,893.07	10/2014 -	06/2016	20	-
102	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	17.60	02/2016 -	06/2016	4	-
103	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	291.60	06/2015 -	08/2016	14	-
104	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	989.03	06/2015 -	08/2016	14	-
105	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,351.15	01/2016 -	11/2016	10	-
106	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	16.00	04/2016 -	11/2016	7	-
107	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,903.55	11/2008 03/2012	12/2016	97	57
108	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,204.18	10/2012 -	12/2016	50	-
109	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,357.96	01/2015 -	12/2016	23	-
110	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,253.90	12/2012 -	12/2016	48	-
111	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,228.13	11/2012 -	12/2016	49	-
112	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,779.00	09/2016 -	12/2016	3	-
113	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,043.56	12/2015 -	12/2016	12	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
114	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.00	9,606.82	1,353.36	02/2011 -	01/2017	71	-
115	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,642.00	09/2011 -	03/2017	66	-
116	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19 -	15,166.19	9,969.00	01/2017 -	03/2017	2	-
117	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,749.00	11/2016 -	08/2017	9	-
118	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	5,353.00	5,206.93	05/2014 -	09/2017	40	-
119	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	4,382.19	12/2016 -	09/2017	9	-
120	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42 -	195.42	44.00	02/2014 -	02/2018	48	-
121	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,070.00	01/2011 10/2014	05/2018	88	43
122	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,367.65	09/2009 -	12/2018	111	-
123	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,661.00	03/2013 -	12/2018	69	-
124	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58 -	2,491.58	775.12	06/2013 -	12/2019	78	-
	Total		144,559.27 -	169,600.97	116,163.55				
	HEAVY INDUSTRY								
125	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE, MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	.00				
	HEALTH AND FAMILY WELFARE								
126	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC, DELHI	09/2013	444.70 -	444.70	268.07	12/2015 -	03/2016	3	-
127	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC, UTTAR PRADESH	10/2013	159.50 -	159.50	118.95	11/2013 -	03/2016	28	-
128	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	175.57	106.20	12/2014 -	03/2016	15	-
	Total		779.77 -	779.77	493.22				
	RAILWAYS								
129	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	-
130	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	36
131	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
132	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
133	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
134	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
135	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
136	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
137	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	325.50	348.66	02/2009 02/2009	04/2016	86	86
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	-
139	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	318.33	322.05	03/2009 03/2009	10/2016	91	91
140	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
141	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	-
142	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	66
143	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	890.25	03/2010 -	06/2017	87	-
144	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	328.12	03/2010 -	12/2017	93	-
145	MULTI MODAL TRANSPORT SYSTEM(MMST) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	130.80	03/2016 -	12/2017	21	-
146	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
147	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
148	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
149	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
150	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	-
151	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	614.96	03/2016 -	12/2018	33	-
153	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
154	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-
155	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
156	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
157	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
158	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	3,161.58	850.74	03/2016 -	12/2020	57	-
	Total		31,057.74 -	79,859.86	37,817.32				
	ROAD TRANSPORT AND HIGHWAYS								
159	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	142.60	09/2008 -	01/2016	88	-
160	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	270.76	10/2008 -	01/2016	87	-
161	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	01/2016	32	-
162	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	913.00	12/2013 -	01/2016	25	-
163	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	543.70	03/2013 -	01/2016	34	-
164	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	609.00	02/2014 -	01/2016	23	-
165	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	882.72	03/2014 -	01/2016	22	-
166	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]MEGA,RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,434.74	10/2011 -	01/2016	51	-
167	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH	11/2015	867.66 -	867.66	374.03	11/2015 -	01/2016	2	-
168	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]MEGA,MADHYA PRADESH	05/2013	1,055.00 -	1,055.00	374.03	11/2015 -	01/2016	2	-
169	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	307.92	06/2008 -	02/2016	92	-
170	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	468.41	05/2010 -	02/2016	69	-
171	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,821.52	09/2012 -	02/2016	41	-
172	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	02/2016	38	-
173	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	02/2016	17	-
174	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]MEGA,RAJASTHAN	03/2012	914.50 -	914.50	850.53	10/2015 -	02/2016	4	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
175	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	389.31	02/2009 -	03/2016	85	-
176	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	194.33	04/2009 -	03/2016	83	-
177	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	231.27	11/2008 -	03/2016	88	-
178	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	184.97	11/2008 -	03/2016	88	-
179	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	234.99	04/2009 -	03/2016	83	-
180	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	276.28	06/2008 -	03/2016	93	-
181	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	369.05	06/2008 -	03/2016	93	-
182	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	488.87	09/2008 -	03/2016	90	-
183	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	298.40	07/2009 -	03/2016	80	-
184	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	348.16	322.70	09/2007 -	03/2016	102	-
185	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	03/2016	44	-
186	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,605.89	05/2012 -	03/2016	46	-
187	INDORE-JHABUA-GUJRATMP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	1,182.58	04/2013 -	03/2016	35	-
188	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2016	33	-
189	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,474.52	08/2014 -	03/2016	19	-
190	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	830.97	11/2013 -	03/2016	28	-
191	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.74	10/2013 -	03/2016	29	-
192	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	428.32	04/2014 -	03/2016	23	-
193	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	543.94	11/2013 -	03/2016	28	-
194	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26	-
195	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	646.75	08/2013 -	03/2016	31	-
196	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37	-
197	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	03/2016	21	-
198	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	1,125.40	06/2014 -	03/2016	21	-
199	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	455.26	10/2014 -	03/2016	17	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
200	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	343.50	07/2014 -	03/2016	20	-
201	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	03/2016	23	-
202	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	03/2016	21	-
203	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7	-
204	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATISGARH	02/2013	1,232.00 -	1,232.00	632.63	08/2015 -	03/2016	7	-
205	WIDNG WITH PS & STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7	-
206	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45	284.69	09/2010 -	04/2016	67	-
207	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	1,026.65	07/2013 -	04/2016	33	-
208	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32	-
209	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	777.06	04/2015 -	04/2016	12	-
210	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12	-
211	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	3,784.75	06/2015 -	05/2016	11	-
212	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	05/2016	20	-
213	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI, RAJASTHAN	01/2014	158.04 -	158.04	81.84	12/2015 -	05/2016	5	-
214	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13	-
215	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56	-
216	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,570.55	11/2011 -	06/2016	55	-
217	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	862.18	03/2013 -	06/2016	39	-
218	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,472.64	07/2015 -	06/2016	11	-
219	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,393.72	07/2013 -	06/2016	35	-
220	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	1,275.83	06/2013 -	06/2016	36	-
221	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	949.96	07/2013 -	06/2016	35	-
223	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	649.52	01/2014 -	06/2016	29	-
224	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	06/2016	25	-
225	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	970.44	06/2014 -	06/2016	24	-
226	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	875.91	03/2013 -	06/2016	39	-
227	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,832.80	09/2015 -	06/2016	9	-
228	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,467.07	12/2015 -	06/2016	6	-
229	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	862.73	09/2014 -	06/2016	21	-
230	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24	-
231	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	304.17	04/2008 12/2015	07/2016	99	7
232	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.40	05/2008 12/2015	07/2016	98	7
233	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	-
234	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	370.66	04/2010 02/2016	08/2016	76	6
235	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	08/2016	39	-
236	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,849.33	08/2013 -	08/2016	36	-
237	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,103.87	02/2014 -	08/2016	30	-
238	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11	-
239	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	1,578.80	06/2012 -	08/2016	50	-
240	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	453.58	05/2013 -	09/2016	40	-
241	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	197.31	01/2014 -	09/2016	32	-
242	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	275.21	10/2013 -	09/2016	35	-
243	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
244	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00	1,410.00	1,335.12	09/2014	10/2016	25	-
245	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD, ANDHRA PRADESH	01/2014	195.45	195.45	-	11/2014	11/2016	24	-
246	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD, ANDHRA PRADESH	02/2014	170.21	170.21	28.66	11/2014	11/2016	24	-
247	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00	230.00	202.97	06/2005	12/2016	138	-
248	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00	212.00	102.85	09/2007	12/2016	111	-
249	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45	193.45	47.41	11/2012	12/2016	49	-
250	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00	359.00	2.74	09/2013	12/2016	39	-
251	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55	1,724.55	1,699.96	03/2013	12/2016	45	-
252	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30	671.30	879.84	02/2013	12/2016	46	-
253	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00	1,250.00	1,326.02	12/2013	12/2016	36	-
254	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00	374.00	303.94	05/2013	12/2016	43	-
255	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00	575.00	604.46	07/2013	12/2016	41	-
256	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00	586.00	160.54	01/2014	12/2016	35	-
257	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00	1,046.00	403.00	09/2013	12/2016	39	-
258	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25	283.25	176.11	10/2015	12/2016	14	-
259	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD, ANDHRA PRADESH	07/2015	333.21	333.21	14.12	12/2015	12/2016	12	-
260	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21	333.21	-	12/2015	12/2016	12	-
261	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04	923.04	163.80	11/2016	12/2016	1	-
262	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16	702.16	390.01	07/2014	02/2017	31	-
263	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55	251.55	-	02/2015	02/2017	24	-

(December 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
264	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	30.00	08/2012 -	03/2017	55	-
265	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	282.68	08/2013 -	03/2017	43	-
266	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	715.50	11/2015 -	03/2017	16	-
267	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	477.26	03/2014 -	04/2017	37	-
268	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	148.55	02/2010 -	05/2017	87	-
269	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	221.08	08/2013 -	05/2017	45	-
270	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	448.14	06/2015 -	05/2017	23	-
271	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
272	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,635.92	08/2013 -	07/2017	47	-
273	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	38.55	09/2015 -	08/2017	23	-
274	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
275	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24	-
276	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24	-
277	BARSAAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
278	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31	-
279	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	-
	Total		89,661.99 -	91,488.94	88,744.44				
	SHIPPING AND PORTS								
280	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	01/2016	118	-

(December 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
281	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	669.46	412.00	12/2010 -	01/2016	61	-
282	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	409.83	360.35	04/2009 03/2010	08/2016	88	77
	Total		762.06 -	1,679.29	912.15				
	<u>TELECOMMUNICATIONS</u>								
283	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20	-
	Total		13,334.00 -	13,334.00	1,360.00				
	<u>URBAN DEVELOPMENT</u>								
284	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	-
285	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17	-
286	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	03/2016	16	-
287	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
288	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 11,609.00	13,845.01	13,427.27	06/2011 12/2015	06/2016	60	6
289	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	-	05/2013 10/2015	06/2016	37	8
290	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,786.98	12/2015 -	08/2016	8	-
291	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	19,388.91	03/2016 -	12/2016	9	-
292	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	-
293	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	21.12	09/2015 07/2016	12/2016	15	5
294	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14	-
295	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 26,405.01	26,405.01	217.41	02/2019 -	03/2020	13	-
	Total		111,460.43 -	118,910.31	44,859.71				
	Grand Total		513,015.26	620,804.68	391,686.95				

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	05/2018	12320	17
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	06/2016	13171	90
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
9	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
10	RCE OF INDARAM OCP (1.20 MTPA)	SCCL	07/2011	03/2015	03/2018	162.76	36
11	BAROUD OC EXPANSION (RCE) - 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
12	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12
13	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
14	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
15	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
16	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2016	209.78	12
17	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
18	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
19	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24
20	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
22	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	36
23	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
24	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
25	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
26	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
27	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
28	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
29	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
30	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
31	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
32	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
33	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
34	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
35	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
36	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
37	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
38	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
39	JAGANNATHPOR OCP (3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
40	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
41	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
42	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
43	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
45	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
46	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
47	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
48	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	08/2019	1458.17	50
49	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	03/2016	364.75	17

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	LGBRIMH-TEZPUR, ASSAM	HSCC	07/2012	12/2014	03/2016	175.57	15
51	AIIMS-RAEBARELI-HOUSING	HSCC	10/2013	11/2013	03/2016	159.5	28

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718	75

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	HCL	09/2011	09/2017	04/2020	1856	31

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
54	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	12/2015	5460.61	44

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
55	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	17
56	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	29
57	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	01/2016	279	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
58	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	IOCL	08/2011	08/2015	03/2016	586	7
59	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
60	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
61	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
62	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
63	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	03/2016	317.64	42
64	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
65	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	35
66	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
67	DE-BOTTLENECKING OF SMPL	IOCL	12/2009	08/2015	03/2016	1584	7
68	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	01/2016	29777	38
69	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
70	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
71	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	05/2016	1138.5	13
72	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	10/2016	736.65	61
73	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	01/2016	2523	24
74	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	01/2016	270	43
75	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993	52
76	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
77	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
78	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	07/2016	3110.36	8
79	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
80	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2016	2592.17	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
81	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
82	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	12/2016	913	16
83	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732	53

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
84	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
85	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	12/2016	2514.88	12
86	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	06/2016	509.66	55
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	06/2016	752.64	35
89	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	02/2016	250.03	37
90	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2016	1272.8	49
91	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48
92	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
93	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
94	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
95	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313	51
96	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	01/2017	4122	71
97	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
98	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	02/2016	2422.66	18
99	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	03/2016	558.26	28
100	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
101	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	06/2016	2127.51	23
103	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	35
104	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	02/2016	297.33	18
105	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
106	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
107	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2016	477.69	69
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	PGCIL	02/2009	02/2012	02/2016	410.29	48
109	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2016	4824.12	50
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	01/2016	1677.57	33
111	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	01/2016	965.58	38
112	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	03/2016	1585.12	28
113	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	12/2016	4404.57	23
114	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	01/2016	2074.86	34
115	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
116	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
117	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	12/2016	2144	48
118	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	11/2016	374.63	7
119	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	25
120	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
121	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
122	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	06/2016	1746.65	22
123	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
124	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	97

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
125	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
126	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	06/2016	1422.85	17
127	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
128	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	01/2016	421.01	30
129	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	02/2016	1927.16	16
130	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2016	2496.9	78
131	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	03/2016	552.44	25
132	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2016	9569.76	12
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2016	723.63	19
134	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2016	3201.44	20
135	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
136	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	02/2016	524.4	9
137	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
138	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
139	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	12/2017	632.68	21
140	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
141	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
142	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	91
143	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87
144	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
145	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL	RVNL	04/2010	03/2016	12/2018	2913.51	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DINESH BAGH.						
147	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
148	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	144
149	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
150	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733	111
151	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
152	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	98
153	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
154	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2019	5300	60
155	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
156	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
157	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
158	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
159	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
160	RAJATGARH-BARANG (LD), ECOR	RVNL	04/1999	02/2009	04/2016	166.16	86
161	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
162	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
163	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
164	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
165	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	12/2015	194.07	138
166	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
167	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
168	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	03/2016	895	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
169	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA)	PWD	12/2011	08/2015	03/2018	191.08	31
170	WIDNG WITH PS & STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	03/2016	164.54	7
171	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	08/2016	1170.52	50
172	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	03/2016	1232	7
173	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	MEGA	02/2008	10/2011	01/2016	1673.7	51
174	JAIPUR-TONK-DEOLI	NHAI	06/2010	12/2012	02/2016	792.06	38
175	CHENNAI-TADA(SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
176	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
177	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2016	2159	11
178	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	06/2016	1813.76	35
179	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2016	671.3	46
180	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	01/2016	351.54	32
181	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	06/2016	1008.5	36
182	ROHTAK-BAWAL	NHAI	05/2011	11/2013	03/2016	650	28
183	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	04/2016	1141	32
184	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	12/2013	01/2016	535	25
185	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2016	1250	36
186	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	06/2016	600	36
187	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	06/2016	953.88	35
188	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2016	374	43
189	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	03/2017	485	43
190	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	03/2016	571	29
191	SAMAIKHIALI - GANDHIDHAM	NHAI	09/2010	03/2013	01/2016	805.39	34

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
192	JAIPUR-REENGUS	NHAI	08/2010	02/2013	03/2016	267.81	37
193	BEAWAR-PALI-PINDWARA	NHAI	12/2011	06/2014	03/2016	2388	21
194	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
195	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	06/2016	754	39
196	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2016	1078.84	36
197	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	07/2017	998.79	47
198	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
199	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
200	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	03/2016	356.4	20
201	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	02/2016	1509.1	41
202	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	03/2016	1175	35
203	BIJUNI TO ASSAM /WB.BORDER (NH-31.C) (NHAI)	NHAI	12/2003	06/2008	03/2016	237.8	93
204	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2016	536	29
205	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
206	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2016	1535	25
207	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	01/2016	664	23
208	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	01/2016	574	22
209	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2016	375.09	23
210	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2016	575	41
211	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	03/2016	511.54	28
212	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	06/2016	1100.7	24
213	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	03/2016	835	26
214	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
215	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	03/2016	500.29	31
216	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	10/2016	1410	25
217	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	03/2016	795	46
218	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2016	1108	55
219	DEOLI-KOTA	NHAI	01/2011	07/2013	04/2016	593	33
220	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	06/2016	828	21
221	REENGUS SIKAR	NHAI	03/2012	09/2014	02/2016	333.51	17
222	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	03/2017	1287.95	16
223	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
224	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2016	1348.2	30
225	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
226	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	02/2016	486	69
227	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	07/2012	03/2016	940	44
228	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2016	230	138
229	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	03/2016	280	85
230	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	83
231	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	03/2016	167.64	88
232	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	88
233	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	03/2016	200	83
234	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	03/2016	348.16	102
235	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	07/2016	160	98
236	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	07/2016	175.96	99
237	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	09/2008	03/2016	332.94	90

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
238	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	12/2016	212	111
239	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196	80
240	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	04/2016	232.45	67
241	MURADABAD-BAREILY	NHAI	04/2010	06/2013	03/2016	1267	33
242	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	03/2016	2498.76	19
243	PUNE-SATARA (NH-4)	NHAI	10/2010	03/2013	12/2016	1724.55	45
244	INDORE-DEWAS (NH-3)	NHAI	11/2010	05/2013	09/2016	325	40
245	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	02/2016	264.72	92
246	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	04/2016	245	97
247	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	08/2016	217.61	76
248	NALBARI T BIJUNI (AS-7)	NHAI	12/2003	04/2008	01/2017	208	105
249	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	PWD	02/2014	07/2014	07/2016	258.99	24
250	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24
251	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	PWD	07/2015	12/2015	12/2016	333.21	12
252	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	PWD	01/2014	11/2014	11/2016	195.45	24
253	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	PWD	02/2014	11/2014	11/2016	170.21	24
254	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
255	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU	PWD	03/2015	09/2015	08/2017	309.01	23
256	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
257	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	12/2016	333.21	12
258	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	PWD	02/2014	06/2014	06/2016	417.61	24
259	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	01/2016	198.16	93
260	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION (KM 240-270KM)	NHAI	02/2010	08/2012	03/2017	617	55

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
261	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM)	NHAI	02/2011	11/2012	12/2016	193.45	49
262	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2016	225	94
263	BIJNI TO ASSAM WB BORDER (NH-31.C) (1) (NHAI)	NHAI	12/2003	06/2008	03/2016	195	93
264	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	01/2016	155	88
265	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	01/2016	275	87
266	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
267	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	06/2016	852	39
268	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	08/2016	1585	39
269	4-LANING OF ROHATAK JIND (LENGTH 45 KM)	NHAI	10/2013	10/2015	12/2016	283.25	14
270	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	NHAI	11/2011	10/2013	09/2016	478	35
271	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	NHAI	04/2012	04/2014	03/2016	624	23
272	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	05/2017	1479	23
273	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2016	942.69	21
274	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	03/2016	1232	7
275	ETAWAH CHAKERI	NHAI	03/2013	09/2015	06/2016	1573	9
276	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	06/2016	2125.24	6
277	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	04/2016	1928.22	12
278	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	05/2016	1396.18	20
279	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2016	291.36	32
280	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
281	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
282	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
283	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	PWD	02/2015	04/2015	05/2016	224.83	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
284	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	04/2016	381.86	12
285	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	08/2016	871.15	11
286	SATANA-BELA SECTION OF NH-75 (4L) IN MP	PWD	01/2012	08/2015	09/2016	320.48	13
287	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
288	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
289	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	01/2016	366.39	61
290	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	88
291	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	01/2016	150	118

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
292	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	SAIL	11/2012	06/2015	02/2016	313.05	8
293	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	01/2016	160.48	16
294	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	10/2016	17265	43
295	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
296	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	06/2016	877.73	11
297	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	06/2017	404.16	23
298	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343	8
299	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	06/2016	187.33	32
300	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	05/2016	237.09	17
301	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	02/2016	332.65	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
302	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2017	13334	20

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
303	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
304	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	01/2016	884.3	17
305	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
306	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	05/2017	171.86	14
307	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	12/2016	156.57	15
308	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
309	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	06/2016	6395	60
310	BANGALORE METRO RAIL PROJECT PHASE-2	BM RCL	02/2014	02/2019	03/2020	26405.14	13
311	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	03/2016	225.81	45
312	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	03/2016	270.83	16
313	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	06/2016	261.85	37
314	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MM RCL	07/2013	01/2015	12/2015	23136	11
315	CHENNAI METRO RAIL LTD (PHASE 1)	CM RL	02/2009	12/2015	08/2016	14600	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
8	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	4941.49	817.14
9	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
14	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
16	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210
19	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7818.68	3899.09
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	18063.89	11778.56
22	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
23	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12
24	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
25	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.57	586.56
26	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
27	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
28	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68
29	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
30	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1262.27	688.28
31	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
32	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6085.84	3588.94
34	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9606.82	5484.82
35	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
36	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2159.07	379.78
38	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
40	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
41	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
42	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
43	KARUR-SALEM (NL) ,SR	SR	02/1997	N.A.	155.55	800	644.45
44	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
45	GULBARGA-BIDAR,SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
46	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
47	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
48	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
49	GADWAL - RAICHUR (NL) , SCR	SCR	04/1998	02/2011	92.63	270	177.37
50	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
51	JIND-SONEPAT (NL) ,NR	NR	01/2004	03/2012	238.56	740	501.44
52	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
53	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	921	2363	1442
54	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
55	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
56	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
57	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
58	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
59	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5
60	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
62	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
63	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	3500	3252.34
64	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
65	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
66	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
67	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
68	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
69	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
70	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
71	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
72	KANPUR KASGANJ MATHURA (GC) NER	NER	03/1997	N.A.	677.97	1651.54	973.57
73	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
74	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
75	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
76	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
77	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
78	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
79	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
80	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
81	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
82	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87
83	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
85	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA- NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
86	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
87	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
88	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
89	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
90	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
91	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
92	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
93	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
94	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
95	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
96	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
97	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
98	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
99	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
100	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
101	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
102	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
103	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
104	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
105	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
106	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
108	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
109	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
110	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
111	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
112	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
113	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
114	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
115	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
116	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
117	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
118	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
119	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
120	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	SWR	02/1997	N.A.	295	1289.92	994.92
121	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)		04/1997	N.A.	836.26	1072.51	236.25
122	HUBLI-ANKOLA (NL) , SWR	SWR	04/1997	N.A.	227	2135	1908
123	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
124	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
125	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
126	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
127	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
128	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
129	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
131	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
132	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
133	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
134	MUNEERABAD-MAHABOONAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	645	426.76
135	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
136	RAJATGARH-BARANG (LD) , ECR	RVNL	04/1999	02/2009	166.16	325.5	159.34
137	DALLI-RAJHARA - RAOGHAT (PART OF DALLI- RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
138	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
139	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	847.75	222.45
140	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	19565	17065
141	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
142	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
143	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
144	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
145	KHURDA ROAD-BOLANGIR (NL) ECR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
146	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
147	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
148	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
149	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
150	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
151	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
152	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
154	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
155	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
156	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
157	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
158	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
159	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
160	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
161	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
162	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
163	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
164	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	360	223.38
165	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	318.33	184.92
166	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
167	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
168	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
169	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
170	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
171	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
172	RAMGANJMUNDI-BHOPAL (NL) ,WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
173	MAIBANG TO LUMDING (AS-25) , KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
174	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
175	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
176	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
177	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
178	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
179	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
180	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
181	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
182	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1060	291.12
183	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
184	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	13845.01	7450.01

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	06/2016	1,3171.00	2,2462.00	9291	90
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	1228.39	1016.05	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	12/2015	5460.61	9965.00	4504.39	44

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	1200.00	328.65	17
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732.00	1227.00	495	53
9	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	4941.49	817.14	20
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993.00	1693.00	700	52
11	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	462.79	152.98	29
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	1256.72	394.93	35

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	01/2016	2,9777.00	3,4555.00	4778	38
14	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
16	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	01/2016	421.01	1007.57	586.56	30
17	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	1262.27	688.28	35
18	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
19	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
20	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313.00	4237.67	1924.67	51
21	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	01/2017	4122.00	9606.82	5484.82	71
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2016	2496.90	6085.84	3588.94	78
23	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
24	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	06/2016	1746.65	2228.71	482.06	22
25	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7818.68	3899.09	111
27	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81
28	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2016	477.69	721.81	244.12	69

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	01/2016	2074.86	2348.37	273.51	34
30	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
31	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
32	BARH STPP (3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88
33	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	2159.07	379.78	97

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
34	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
35	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138
36	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
37	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
38	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
39	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
40	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
41	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	318.33	184.92	91
42	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
43	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
44	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
46	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
47	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
49	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
50	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
51	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
52	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
53	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
54	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
55	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
56	RAJATGARH-BARANG (LD), ECR	RVNL	04/1999	02/2009	04/2016	166.16	325.50	159.34	86
57	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174
58	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
59	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2016	1108.00	2288.00	1180	55
60	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196.00	331.23	135.23	80

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
61	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	385.13	185.32	83
62	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	280.13	125.09	88

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
63	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	01/2016	366.39	669.46	303.07	61
64	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	409.83	164.16	88
65	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	01/2016	150.00	600.00	450	118

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
66	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343.00	488.40	145.4	8

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
67	BANGALORE METRO RAIL PROJECT	MRTP	05/2006	06/2011	06/2016	6395.00	1,3845.01	7450.01	60

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure-XVIII

Details of 20 Railways Projects [as identified by Ministry of Railways vide letter
no. 2011/w-1 /Genl / MoSPI dated 28/10/2015] to be monitored at MoSPI level

			(December 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	RAILWAYS					
1	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 - 2,363.00	03/2009 12/2012	10/2015	0/0
2	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 - 2,921.00	10/2007 12/2012	12/2015	0/0
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 - 5,500.00	03/2009 -	03/2016	0/0
4	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00 1,242.25	03/2007 -	03/2016	0/0
5	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 - 1,564.54	03/2010 03/2017	03/2017	0/0
6	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19 4,996.19	04/2008 12/2011	06/2017	0/0
7	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36 1,651.54	- - -	03/2018	0/0
8	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 - 1,143.60	- -	03/2018	0/0
9	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00 19,565.00	11/2002 -	12/2018	0/0
10	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54 1,544.40	03/1998 -	12/2019	0/0
11	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 3,500.00 3,500.00	05/2008 -	-	0/0
12	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 - 1,266.89	- -	-	0/0
13	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345],UTTAR PRADESH	04/1997	836.26 - 1,072.51	- -	-	0/0
14	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 - 2,957.21	07/2005 -	-	0/0

			(December 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 - 1,185.64	- 09/2009	-	0/0
16	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 - 1,202.70	02/2015 -	-	0/0
17	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR, MULTI STATE	04/2008	822.39 - 1,280.83	- -	-	0/0
18	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,054.35 - 1,054.35	- -	-	0/0
19	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]SWR, KARNATAKA	04/2010	2,127.00 - 2,127.00	- -	-	0/0
20	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 - 1,111.99	- -	-	0/0
	Total		20,808.52 -			0/0
	Grand Total		20,808.52			0/0
