

**422nd FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
December, 2020**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for December 2020 contains information on the status of the 1687 Central Sector Infrastructure Projects costing ₹150 crore and above.


2. During the reference month, out of 1687 projects, 21 projects are added. 558 projects are delayed with respect to their original schedules and 75 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 75 projects, 25 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report	Additional delayed Mega Projects
1	ROAD TRANSPORT AND HIGHWAYS	858	146	18	2
2	RAILWAYS	311	159	9	8
3	PETROLEUM	142	70	12	4
4	COAL	105	42	11	2
5	POWER	67	41	11	5
6	WATER RESOURCES	51	17	1	1
7	URBAN DEVELOPMENT	35	10	1	0
8	HEALTH AND FAMILY WELFARE	28	14	6	0
9	HUMAN RESOURCE DEVELOPMENT	21	4	1	0
10	CIVIL AVIATION	15	12	0	0
11	STEEL	9	7	3	2
12	TELECOMMUNICATIONS	8	3	1	0
13	MINES	5	3	0	0
14	ATOMIC ENERGY	4	4	0	0
15	FERTILISERS	4	4	0	0
16	RURAL DEVELOPMENT	4	3	0	0
17	COMMERCE AND INDUSTRY	3	2	0	0
18	HOME AFFAIRS	3	2	1	1
19	FINANCE	2	1	0	0
20	HEAVY INDUSTRY	1	1	0	0
21	SHIPPING AND PORTS	1	0	0	0
22	DEFENCE PRODUCTION	1	1	1	0
23	CULTURE DEVELOPMENT	1	1	0	0
Total		1687	558	75	25

3. Total original cost of implementation of the 1687 projects was ₹21,44,627.66 crore and their anticipated completion cost is likely to be ₹25,72,670.28 crore, which reflects overall cost overruns of ₹4,28,042.62 crore (19.96% of original cost). The expenditure incurred on these projects till December

2020 is ₹12,17,692.37 crore, which is 47.33% of the anticipated cost of the projects. The information can be viewed graphically as:

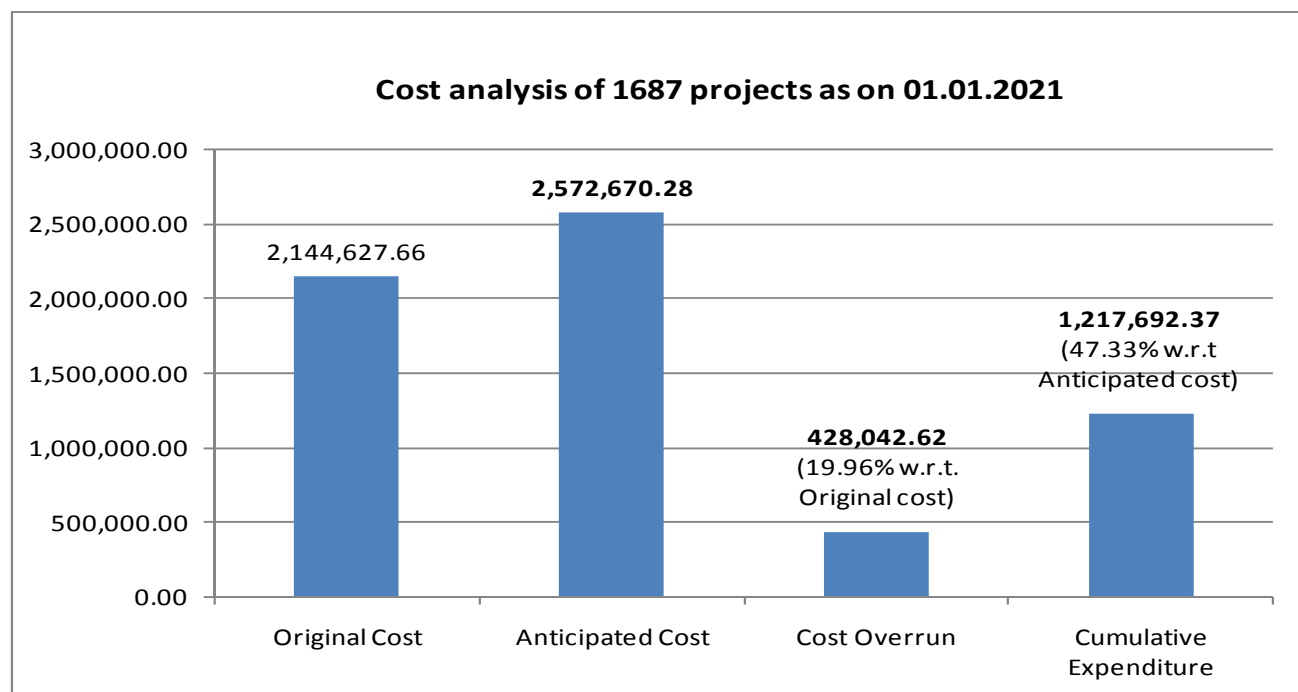


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.

5. Out of the 1687 projects, 11 projects are ahead of schedule, 195 are on schedule, 558 are delayed, 450 projects reported cost overrun and 221 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 408 if delay is calculated on the basis of latest schedule of completion. Further, for 923 projects neither the year of commissioning nor the tentative gestation period has been reported.


Status of projects (as on 01.01.2021)

(All the figures corresponds to number of project)

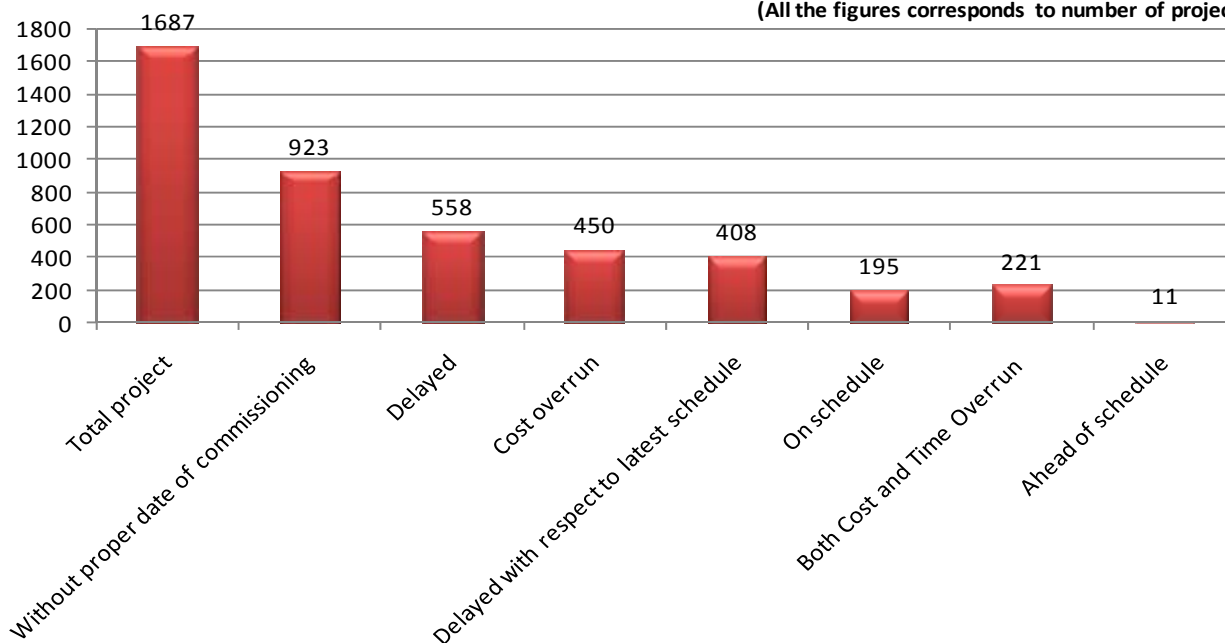


6. Out of 558 delayed projects, 111 (19.89%) projects have overall delay in the range of 1 to 12 months, 135 (24.19%) projects have delay in the range of 13 to 24 months, 187 (33.51%) projects have delay in the range of 25 to 60 months and 125 (22.40%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below.

Break up of delayed projects w.r. t magnitude of delay

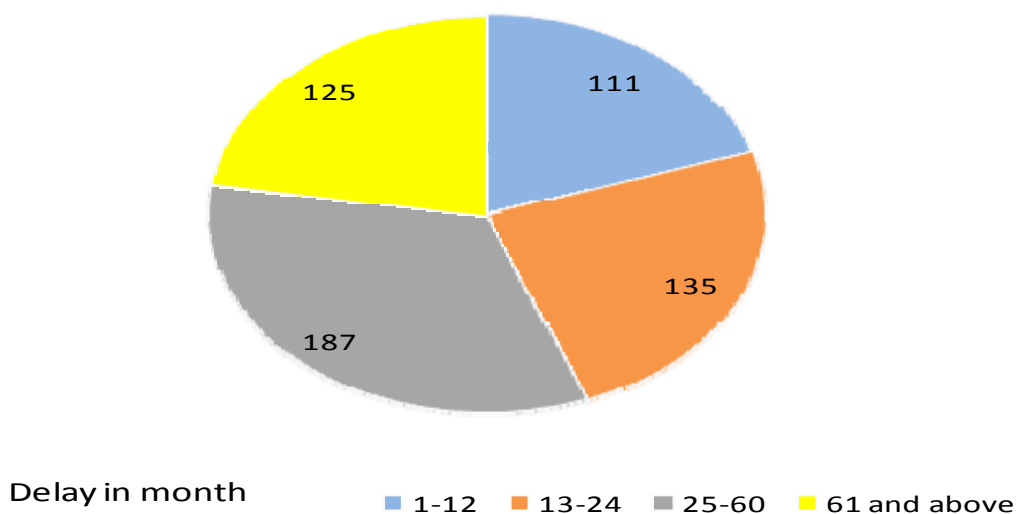

7. The status of online reporting of projects can be viewed month wise as:

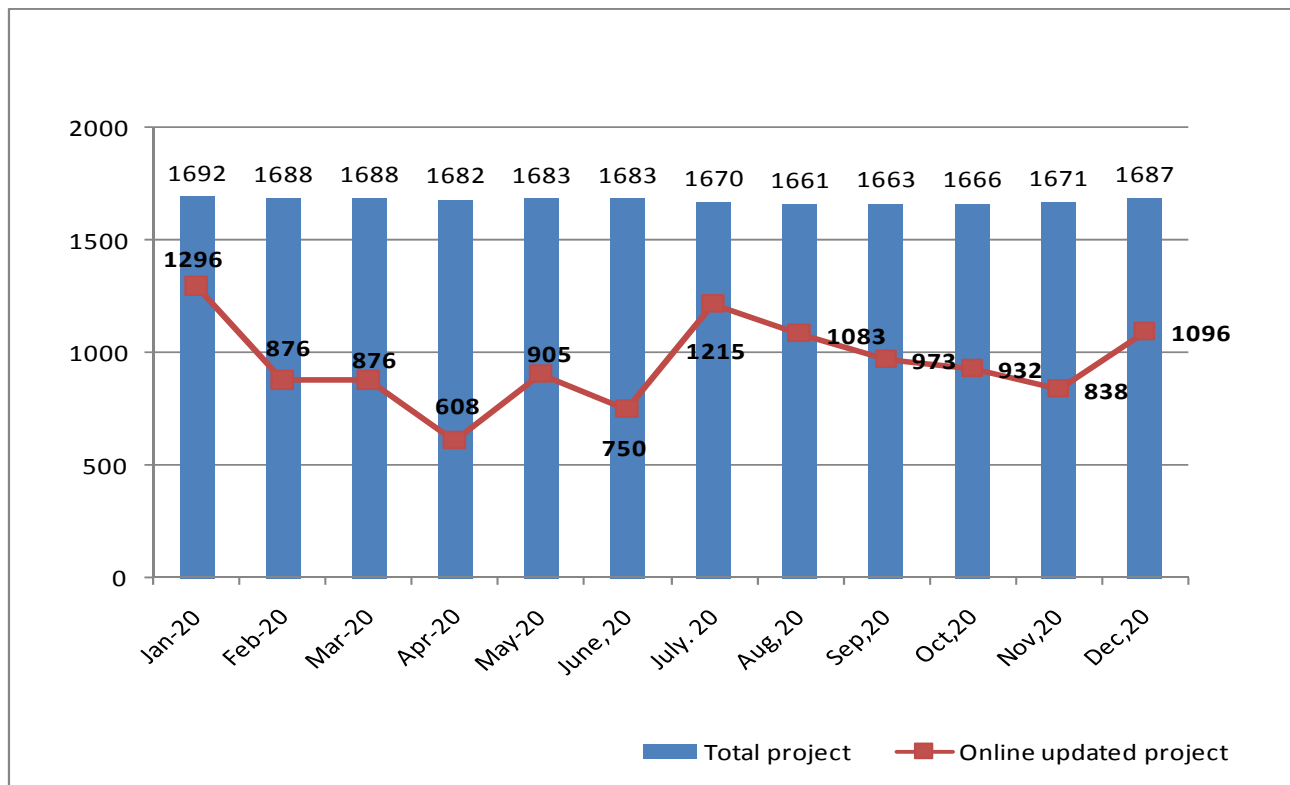

The average time overrun in these 558 delayed projects is 45 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns ('TOD') are at Table-C.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-01-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
1	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	5.78
COAL			5		

1	BALRAM EXPANSION OCP	12/2007	172.08	646.01	275.41
2	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
3	BHANEGAON OC	02/2015	187.94	409.68	117.98
4	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
5	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
COMMERCE AND INDUSTRY					
1	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80
2	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
HEALTH AND FAMILY WELFARE					
1	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	20.55
3	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
4	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
5	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	15.71
HOME AFFAIRS					
1	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
2	NSG AT KOLKATA	10/2014	162.88	179.16	10.00
HUMAN RESOURCE DEVELOPMENT					
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
2	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROHAR, PUNJAB	04/2016	294.00	350.69	19.23
3	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	10.22
4	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	1.85
5	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
PETROLEUM					
1	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1846.46	114.26
3	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52

4	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
5	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	5867.38	96.99
RAILWAYS					
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
2	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	04/2011	120.70	2172.16	1699.64
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
4	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
5	RAMGANJMUNDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
ROAD TRANSPORT AND HIGHWAYS					
1	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
2	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
3	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
4	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95
5	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	94.94
RURAL DEVELOPMENT					
1	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	3.96
2	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	2.23
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	1525.00	2940.00	4.32
2	CENTRAL DISPATCH YARD	01/2015	320.06	336.00	4.73
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
3	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
4	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	18.69
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4720.73	10.71
WATER RESOURCES					
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
2	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	01/2019	231.79	234.03	0.97

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-01-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
		7			

	ATOMIC ENERGY				
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
	CIVIL AVIATION				
1	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	24.10
	COAL				
1	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
3	BALRAM EXPANSION OCP	12/2007	172.08	646.01	473.93
4	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
5	GOPAL JI KANIHA OCP, MCL	12/2007	457.77	684.32	226.55
	COMMERCE AND INDUSTRY				
1	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
2	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
	HEALTH AND FAMILY WELFARE				
1	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00
2	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
3	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	85.12
4	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJA	09/2014	50.58	85.00	9.42
5	AIIMS - MOTHER AND CHILD BLOCK	12/2013	20.44	250.00	5.56
	HOME AFFAIRS				
1	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
2	NSG AT KOLKATA	10/2014	162.88	179.16	16.28
	HUMAN RESOURCE DEVELOPMENT				
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
2	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	350.69	56.69
3	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	19.00
4	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	10.16
5	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
	PETROLEUM				
1	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00
3	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
4	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
5	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00

	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
5	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9151.56	4397.14
	RAILWAYS				
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
5	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12264.15	7809.98
	ROAD TRANSPORT AND HIGHWAYS				
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
2	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
3	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2587.50	1199.16
4	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
5	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
	RURAL DEVELOPMENT				
1	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	5.93
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	4.51
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	1552.00	2140.00	645.00
2	CENTRAL DISPATCH YARD	03/2005	32.66	36.00	5.34
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
	URBAN DEVELOPMENT				
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
3	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
4	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4720.73	456.73
5	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	151.74
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
2	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	01/2019	231.79	234.03	2.24

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-01-2021)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
	ATOMIC ENERGY				

1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	03/2023	75
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	09/2021	69
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2021	33
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	12/2020	18
3	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	06/2021	16
4	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	06/2021	15
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	05/2021	13
COAL					
1	BALRAM EXPANSION OCP	12/2007	03/2010	03/2029	228
2	GOPAL JI KANIHA OCP, MCL	12/2007	03/2013	03/2028	180
3	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	03/2017	03/2031	168
4	MAGADH EXPANSION OC RPR	08/2008	07/2012	03/2025	152
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
COMMERCE AND INDUSTRY					
1	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	07/2021	22
2	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	07/2021	10
CULTURE DEVELOPMENT					
1	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR	04/2014	09/2017	03/2021	42
DEFENCE PRODUCTION					
1	RESIDENTIAL QUATERS FOR HAL, BANGLORE	12/2016	02/2020	06/2021	16
FERTILISERS					
1	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	03/2021	16
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	03/2021	16
3	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	02/2021	15
4	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	03/2021	11
FINANC					
1	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	04/2021	18
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	03/2021	88
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	03/2021	46
3	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	12/2021	43
4	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	12/2020	34
5	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	03/2019	03/2021	24
HEAVY INDUSTRY					

1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	12/2020	15
HOME AFFAIRS					
1	NSG AT KOLKATA	10/2014	04/2018	12/2020	32
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	09/2021	23
HUMAN RESOURCE DEVELOPMENT					
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	12/2020	75
2	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	12/2020	73
3	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	06/2021	63
4	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	09/2021	51
5	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	04/2019	01/2021	21
MINES					
1	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	12/2022	20
2	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	12/2020	18
3	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	02/2021	3
PETROLEUM					
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2008	12/2012	02/2022	110
2	CONVERSION OF REG SAG B - AMRAY TO MOBILE OFF SHORE PRODUCTION UNIT (MOPS)	03/2011	5/2013	03/2021	94
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
4	LPG TERMINAL AT KOCHI	10/2015	10/2017	03/2022	53
5	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	03/2017	03/2021	48
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	03/2022	150
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	01/2021	133
4	BARH STPP(3X660MW) NTPC	02/2005	10/2011	04/2022	126
5	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2023	126
RAILWAYS					
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
2	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
3	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2022	241
5	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
ROAD TRANSPORT AND HIGHWAYS					
1	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2020	152
2	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	10/2010	06/2021	128
3	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	03/2011	12/2020	117

4	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	06/2021	106
5	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
RURAL DEVELOPMENT					
1	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	02/2021	62
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	03/2021	51
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016	03/2021	51
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2021	74
2	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	12/2021	50
3	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	02/2021	38
4	COKE OVEN BATTERY-5	12/2011	12/2017	12/2020	36
5	FORGED WHEEL PLANT	04/2014	09/2018	02/2021	29
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	06/2021	71
2	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	03/2018	12/2020	33
3	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	11/2021	5
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	12/2015	12/2020	60
2	DELHI MRTS PHASE III	09/2011	03/2016	03/2021	60
3	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2011	02/2018	11/2022	47
4	CHENNAI METRO RAIL LTD (PHASE I EXT)	06/2016	03/2018	12/2020	33
5	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	06/2015	04/2019	06/2021	26
WATER RESOURCES					
1	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
2	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	04/2022	25
3	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	02/2017	11/2019	12/2020	13
4	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	12/2019	12/2020	12
5	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	12/2020	12

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones (as on 01-01-2021)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	291.75	09/2018	06/2021

2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	438.28	438.28	335.58	06/2019	12/2020
3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	458.00	458.00	105.12	03/2020	06/2021
4	UPGRADATION OF JABALPUR AIRPORT	06/2016	412.24	412.24	0.00	06/2021	06/2021
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT	11/2016	303.80	303.80	115.88	04/2020	05/2021
COAL							
1	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	158.25	09/2020	N.A.
2	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
3	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	173.83	09/2020	N.A.
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
5	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	16.73	04/2018	12/2021
COMMERCE AND INDUSTRY							
1	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	7305.07	09/2019	07/2021
2	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5171.00	2334.57	12/2019	07/2021
3	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	60.00	10/2020	10/2020
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	456.52	11/2013	03/2021
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	438.92	06/2020	07/2021
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	511.74	04/2020	07/2021
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
HEAVY INDUSTRY							
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	806.15	09/2019	12/2020
HOME AFFAIRS							
1	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	166.98	166.98	0.00	10/2023	10/2023

HUMAN RESOURCE DEVELOPMENT							
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	12/2020
2	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	171.72	171.72	53.94	03/2020	06/2021
3	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676.00	676.00	0.00	04/2023	04/2023
4	STUDY IN INDIA	03/2018	150.00	150.00	0.00	04/2018	N.A.
5	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	418.00	418.00	110.00	03/2019	N.A.
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	N.A.
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	16.38	02/2017	08/2022
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
5	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	07/2014	247.00	247.00	0.00	03/2021	03/2021
POWER							
1	LOKTAK D/S HEP(NHPC)	12/199	576.62	576.62	0.00	06/2006	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	12855.18	09/2010	08/2023
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3312.62	10/2017	N.A.
4	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	238.32	04/2016	03/2021
5	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1598.96	04/2020	07/2025
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2200.00	714.78	07/2012	03/2024
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.07	03/2019	N.A.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	149.30	03/2006	03/2025
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	541.83	07/2014	N.A.
ROAD TRANSPORT AND HIGHWAYS							

1	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	435.30	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	216.25	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	317.05	08/2016	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	358.22	377.64	341.81	10/2016	N.A.
SHIPPING AND PORTS							
1	JAL MARG VIKAS PROJECT	01/2018	5369.18	4633.81	1787.23	03/2023	03/2023
STEEL							
1	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATIO I OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	377.18	377.18	0.38	05/2023	05/2023
TELECOMMUNICATIONS							
1	CONVERGENT BILLING AND CRM-MTNL(DELHI)	12/2005	249.00	229.41	0.00	02/2007	N.A.
2	CONVERGENT BILLING AND CRM(MUMBAI)	01/2006	247.00	247.00	0.00	02/2007	N.A.
3	DELHI CONVERGENT BILLING AND CRM PE-5834	02/2006	229.41	229.41	0.00	03/2012	N.A.
4	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES	05/2006	1077.00	1077.00	0.00	03/2009	N.A.
5	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	15239.00	07/2015	06/2021
URBAN DEVELOPMENT							
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
2	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	N.A.
3	DELHI MRTS PHASE-III	09/2011	38585.00	38585.00	39843.96	03/2016	03/2021

4	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	884.30	884.30	812.00	12/2015	12/2020
5	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6031.09	07/2017	09/2020
WATER RESOURCES							
1	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	279.91	222.79	12/2019	12/2020
2	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	189.36	12/2019	12/2020
3	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	225.77	249.54	03/2020	12/2020
4	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	202.18	04/2020	12/2020
5	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	254.50	01/2021	01/2021

N.A.: Not Available.

Table-E

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates
(as on 01-01-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL ESTIMATE (Rs. Crore)	COST RE-EVALUATED (Rs. Crore)	CUMULATIVE EXENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	5896.72
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	16038.00
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	0.00	12799.00
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	0.00	326.69
2	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.10	0.00	586.86
3	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	362.50
4	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	0.00	491.85
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	0.00	279.54
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	456.52
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	226.54
3	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
4	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
5	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
HOME AFFAIRS					
1	NSG AT KOLKATA	10/2014	162.88	0.00	168.45
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	352.56	0.00	445.41
3	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	0.00	4808.25
4	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	0.00	2724.32
5	HALDIA LPG IMPORT FACILITY	03/2015	694.00	0.00	971.84

	POWER				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	8151.00
2	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	7998.00	8648.28
3	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	487.49	0.00	590.30
4	MUNPL-MEJA TPP - JV (2X660 MW)	04/2012	9750.89	0.00	11044.00
5	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	11846.00	0.00	13766.78
	RAILWAYS				
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	714.78
2	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	541.83
3	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	1177.09
4	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	693.14
5	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	928.36
	ROAD TRANSPORT AND HIGHWAYS				
1	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	0.00	317.05
2	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	612.58
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	325.28
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	0.00	251.39
5	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	0.00	655.17
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	0.00	15239.00
	URBAN DEVELOPMENT				
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.87
2	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39843.96
	WATER RESOURCES				
1	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2011	225.00	0.00	249.54

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-01-2021)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	COAL				
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	RANIGANJ MASTER PLAN	08/2009	08/2019	N.A.	N.A.
3	KAPURIA UG(PSLW)	08/2011	04/2017	N.A.	N.A.
4	PATHERDIH NLW WASHERY	10/2012	04/2014	N.A.	04/2020
5	DINESH OCP	11/2014	03/2020	N.A.	03/2020
	COMMERCE AND INDUSTRY				
1	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	10/2020
	HEALTH AND FAMILY WELFARE				
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
2	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020

3	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
4	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
5	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	05/2019
HUMAN RESOURCE DEVELOPMENT					
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	03/2020
2	STUDY IN INDIA	03/2018	04/2018	N.A.	N.A.
3	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	03/2019	N.A.	N.A.
4	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	02/2019	06/2020	N.A.	N.A.
5	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	03/2020	N.A.	N.A.
MINES					
1	UTKAL D AND E COAL BLOCK	05/2016	01/2020	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	01/2019	N.A.	N.A.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
4	GAIL GAS LTD BENGALURU CGD PROJECT	02/2015	02/2020	N.A.	N.A.
5	HALDIA LPG IMPORT FACILITY	03/2015	10/2018	02/2020	07/2020
POWER					
1	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
3	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	06/2014	N.A.	N.A.
4	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
5	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NEW BGRLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	03/2019	N.A.	N.A.
3	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
4	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	02/2009	N.A.	N.A.

5	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	03/1996	03/2017	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LNES- 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
STEEL					
1	CENTRAL DISPATCH YARD	08/2015	08/2018	11/2020	11/2020
TELECOMMUNICATIONS					
1	CONVERGENT BILLING AND CRM-MTNL(DELHI)	12/2005	02/2007	N.A.	N.A.
2	CONVERGENT BILLING AND CRM(MUMBAI)	01/2006	02/2007	N.A.	N.A.
3	DELHI CONVERGENT BILLING AND CRM PE- 5834	02/2006	03/2012	N.A.	N.A.
4	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES	05/2006	03/2009	N.A.	N.A.
5	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
URBAN DEVELOPMENT					
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
2	CONSTRUCTION OF ITBP ROAD TO INDO- CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	N.A.	N.A.
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
4	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	11/2019	11/2020	11/2020
5	KOCHI METRO RAIL PROJECT	07/2012	07/2017	10/2020	09/2020

	WATER RESOURCES				
1	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	03/2017	08/2019	N.A.	N.A.
2	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH	03/2017	11/2019	N.A.	N.A.
3	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	N.A.	N.A.
4	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	05/2017	05/2020	N.A.	N.A.
5	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	09/2020	N.A.	N.A.

N.A.: Not Available.

.

FLASH REPORT

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	858	18
2	RAILWAYS	311	9
3	PETROLEUM	142	12
4	COAL	105	11
5	POWER	67	11
6	WATER RESOURCES	51	1
7	URBAN DEVELOPMENT	35	1
8	HEALTH AND FAMILY WELFARE	28	6
9	HUMAN RESOURCE DEVELOPMENT	25	0
10	CIVIL AVIATION	19	0
11	STEEL	9	3
12	TELECOMMUNICATIONS	8	1
13	MINES	5	0
14	ATOMIC ENERGY	4	0
15	FERTILISERS	4	0
16	RURAL DEVELOPMENT	4	0
17	COMMERCE AND INDUSTRY	3	0
18	HOME AFFAIRS	3	1
19	FINANC	2	0
20	HEAVY INDUSTRY	1	0
21	SHIPPING AND PORTS	1	0
22	DEFENCE PRODUCTION	1	1
23	CULTURE DEVELOPMENT	1	0
	Total	1687	75

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2020			
	<u>STEEL</u>			
1	INSTALLATION OF NEW HOT STRIP MILL AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000094]	3,127.30	04/2018	3,201.42
	<u>PETROLEUM</u>			
2	INTEGRATED DEVELOPMENT OF B-127 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000131]	2,059.63	03/2015	2,011.80
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000197]	6,068.80	04/2019	4,956.05
4	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000212]	4,619.94	12/2017	4,663.66
5	INDMAX PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000243]	2,322.00	11/2019	1,718.52
6	MOTIHARI / MLEKHANJ PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000254]	324.00	06/2020	129.09
7	DEVELOPMENT OF B-147 FIELD Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000292]	546.15	11/2019	537.69
8	BS-VI PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000310]	3,380.00	09/2019	2,381.00
9	BS-VI PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000320]	1,222.00	09/2019	764.17
10	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000322]	2,934.40	09/2019	1,957.94
11	BS-VI PROJECT AT PANIPAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000325]	3,529.00	07/2019	2,095.75
12	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR (GAS AUTHORITY OF INDIA LIMITED) - [N16000330]	221.45	10/2022	63.59
13	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000366]	154.84	11/2019	128.71
	June,2020			
	<u>COAL</u>			
14	RKP OCP PHASE-I (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000079]	209.78	03/2015	104.19
15	RG OC -III EXTENSION (PHASE -II) PROJECT (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000100]	365.01	06/2015	365.01
	July,2020			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
16	KULDA OCP (MAHANADI COALFIELDS LTD) (MAHANADI COAL FIELDS LIMITED) - [060100092]	302.96	03/2010	281.80
	<u>PETROLEUM</u>			
17	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000204]	2,818.88	03/2019	2,907.03
18	BS-VI PROJECT AT MATHURA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000306]	666.64	09/2019	493.90
19	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000335]	766.37	12/2019	606.49
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
20	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000347]	723.54	02/2018	1,163.64
21	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000492]	867.66	05/2018	1,289.81
22	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000604]	320.30	01/2019	237.81
23	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALI TO AP/KARATAKA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000671]	648.32	03/2020	511.34
24	FOUR LANING OF BTDN BORDER TO NALAGAMPALI VILAGE (KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) Central Sector Projects(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000700]	648.32	06/2017	229.94
25	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000951]	382.81	01/2015	338.18
26	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000952]	179.32	11/2017	129.04
27	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000953]	155.77	09/2016	111.65
28	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000954]	378.07	01/2014	188.65
29	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000955]	511.21	10/2013	813.54
30	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000956]	501.00	09/2013	659.98
31	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000960]	621.43	10/2016	429.97
32	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000961]	163.54	07/2017	108.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>TELECOMMUNICATIONS</u>			
33	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000105]	418.26	06/2017	367.04
34	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000113]	231.80	10/2018	119.92
	<u>URBAN DEVELOPMENT</u>			
35	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000101]	768.88	02/2014	1,125.98
36	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000102]	324.87	12/2015	270.24
37	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000062]	156.57	08/2016	159.35
38	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000108]	206.58	03/2019	185.84
	August, 2021			
	<u>COAL</u>			
39	MANUGURU OC-II EXTENSION PHASE-II (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000080]	181.19	03/2012	170.60
	<u>PETROLEUM</u>			
40	RESID UPGRADEATION PROJECT (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000184]	3,110.36	11/2015	2,915.00
41	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR- 2/PSA-2/RSU (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000255]	224.00	04/2019	164.61
42	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000256]	135.00	03/2019	156.65
43	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000260]	554.00	02/2020	375.80
44	50MW WIND ENERGY POWER PROJECT (OIL INDIA LIMITED) - [N16000298]	500.00	06/2017	368.24
45	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP (INDIAN OIL CORPORATION LIMITED) - [N16000354]	204.00	09/2019	162.53
46	UPGRADEATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA- BARAUNI CRUDE OIL TRUNK PIPELINE (OIL INDIA LIMITED) - [N18000148]	871.35	03/2015	565.63
	<u>URBAN DEVELOPMENT</u>			
47	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000109]	253.92	06/2016	1,113.24

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
48	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000110]	200.00	03/2018	131.15
49	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000111]	787.29	12/2016	285.30
50	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000112]	170.00	04/2018	88.91
51	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG Central Sector Projects(HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000114]	185.37	03/2016	178.30
52	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000093]	154.00	11/2015	280.32
	September,2020			
	<u>HUMAN RESOURCE DEVELOPMENT</u>			
53	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000088]	388.00	05/2017	452.80
	October,2020			
	<u>COAL</u>			
54	PENGANGA OCP(REVISED) (WESTERN COAL FIELDS LIMITED) - [N06000066]	441.82	03/2020	259.82
55	GAURI DEEP OC (WESTERN COAL FIELDS LIMITED) - [N06000181]	164.96	03/2019	96.37
	December,2020			
56	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000114]	337.66	03/2019	258.65
	<u>PETROLEUM</u>			
57	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000277]	429.00	01/2019	373.62
58	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000284]	208.35	07/2020	170.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
59	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000505]	1,583.79	01/2019	1,648.90
60	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000669]	165.50	03/2020	117.09

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
61	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000670]	239.68	03/2020	219.75

FLASH REPORT

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	August, 2020			
	<u>COAL</u>			
1	KALYANIKHANI 6 INCLINE PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000147]	477.65	03/2020	2.11
2	RAMPURAM SHAFT BLOCK (SINGARENI COLLIERS COMPANY LIMITED) - [N06000174]	431.92	-	0.00
3	SRAVANAPALLI OPENCAST PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000175]	412.70	-	0.76
	<u>HUMAN RESOURCE DEVELOPMENT</u>			
4	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000092]	216.69	03/2015	52.00
	September, 2020			
	<u>COAL</u>			
5	KOYAGUDEM OPENCAST PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000146]	426.79	03/2018	0.72

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1671
No of Projects Completed/Dropped/Frozen in Current Month	6
No of Project Elevated in Current Month	1
No of Projects added in Current Month	21
No of Projects in Current Month	1687

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	558 (33.08%)	11 (.65%)	195 (11.56%)	129 (7.65%)	794 (47.07%)	1687
Latest Approved (Date)	408 (24.18%)	25 (1.48%)	341 (20.21%)	119 (7.05%)	794 (47.07%)	1687

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1407	17,71,732.86	19,57,878.90	8,67,519.46	44.30	1,86,146.04	10.50
Project with Revision in Cost	280	6,27,393.32	6,14,791.38	3,50,172.91	57.00	-12,601.94	-2.00
Total	1,687	23,99,126.18	25,72,670.28	12,17,692.37	47.33	1,73,544.10	7.23
Original Cost of All Projects							
Original Cost	1,687	21,44,627.66	25,72,670.28	12,17,692.37	47.33	4,28,042.62	19.96

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	558	8,82,703.66	11,74,901.33	6,83,281.06	58.20	2,92,197.67	33.10
Latest Approved (RCE)	408	7,29,363.26	8,50,340.36	4,83,719.56	56.90	1,20,977.10	16.59

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	75	1,07,602.36	1,82,411.81	1,11,990.79	61.40	74,809.45	69.50
Total	75	1,07,602.36	1,82,411.81	1,11,990.79	61.39	74,809.45	69.52

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	2	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	19	13,786.54	14,031.50	1.80	3	1,903.50	2,153.66	13.02
3	COAL	105	1,12,535.7	1,18,871.80	5.24	19	3,741.56	3,531.44	22.09
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0.00
7	STEEL	9	23,478.11	29,608.45	26.11	2	15,845.66	22,276.00	40.58
8	PETROLEUM	142	2,82,358.27	2,90,123.35	2.75	29	64,350.04	83,925.21	30.42
9	POWER	67	2,83,975.91	3,56,631.39	25.59	28	1,60,515.47	2,33,688.00	45.59
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	28	13,445.26	13,766.81	2.39	12	5,589.39	6,253.60	11.88
12	RAILWAYS	311	4,61,691.03	6,98,197.39	51.23	209	2,27,287.87	4,74,869.26	108.93
13	ROAD TRANSPORT AND HIGHWAYS	858	5,08,495.62	5,27,475.09	3.73	126	90,922.81	1,16,551.16	28.19
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	8	17,926.94	29,137.35	62.53	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	35	2,84,575.18	2,92,612.80	2.82	5	34,933.05	43,049.87	23.24
17	WATER RESOURCES	51	27,955.51	73,105.94	161.51	2	10,382.83	55,782.90	437.26
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0.00
19	COMMERCE AND INDUSTRY	3	17,654.73	19,292.94	9.28	2	17,352.09	18,990.30	9.44
20	HUMAN RESOURCE DEVELOPMENT	25	10,702.40	10,890.83	1.76	5	2,009.81	2,240.41	11.47

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
21	HOME AFFAIRS	3	1,549.07	2,346.14	51.45	2	1,382.09	2,179.16	57.67
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	2.96
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
Total		1687	21,44,627.66	25,72,670.28	19.96	450	7,04,175.51	11,65,016.75	65.44

^ - Cost Overrun = Anticipated Cost minus Original Cost

FLASH REPORT

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	74	1,19,147.53	1,66,693.54	39.91	17	47,599.98	1,04,370.99	119.27
2	ARUNACHAL PRADESH	40	21,795.08	41,308.38	89.53	6	11,263.82	30,777.12	173.24
3	ASSAM	46	41,915.67	46,133.18	10.06	19	9,251.85	14,635.71	58.19
4	BIHAR	105	1,21,115.30	1,56,495.18	29.21	35	42,074.64	78,574.34	86.75
5	GOA	11	5,629.77	5,640.26	0.19	2	529.17	539.66	1.98
6	GUJARAT	58	86,586.94	97,799.93	12.95	16	33,231.01	45,423.09	36.69
7	HARYANA	42	30,149.37	32,670.16	8.36	7	3,872.20	6,803.47	75.70
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	3	8,237.58	18,122.01	119.99
9	JAMMU AND KASHMIR	18	30,493.84	56,545.15	85.19	4	6,582.27	22,776.33	397.95
10	KARNATAKA	62	7,012.53	78,500.12	7.44	16	17,769.36	28,520.35	32.36
11	KERALA	21	37,063.23	41,659.56	12.40	12	18,147.21	22,767.58	25.46
12	MADHYA PRADESH	85	91,778.35	1,05,425.81	14.87	20	35,307.11	49,952.02	41.48
13	MAHARASHTRA	243	2,16,084.44	2,28,778.81	5.87	31	38,648.30	56,594.36	46.43
14	MANIPUR	4	5,785.67	13,535.85	133.95	1	4,454.17	12,264.15	175.34
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	2	1,390.78	4,709.28	238.61
16	MIZORAM	13	7,757.62	11,706.32	50.90	5	3,593.57	7,542.27	109.88
17	NAGALAND	26	14,842.43	19,040.81	28.29	2	2,699.59	7,298.44	170.35
18	ODISHA	91	1,16,984.91	1,22,804.57	4.97	22	29,562.19	39,699.81	34.29
19	PUNJAB	28	14,921.05	18,022.94	20.79	8	5,301.19	8,645.53	63.09
20	RAJASTHAN	56	47,334.20	55,321.42	16.87	13	19,470.60	27,458.05	41.02
21	SIKKIM	9	3,476.73	10,883.48	213.04	3	1,909.76	9,316.51	387.84
22	TAMIL NADU	68	1,13,045.04	1,31,786.39	16.58	22	38,174.33	58,588.36	53.48
23	TRIPURA	7	2,076.64	2,259.45	8.80	3	921.97	1,104.78	19.83
24	UTTAR PRADESH	132	1,75,440.76	1,82,971.92	4.29	29	54,826.89	64,532.54	17.70
25	WEST BENGAL	78	66,850.06	84,903.63	27.01	30	31,812.00	50,201.86	57.81
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	2	655.03	679.33	3.71
27	CHANDIGARH	2	349.15	570.00	63.25	2	349.15	570.00	63.25
28	DELHI	37	90,924.18	92,955.69	2.23	9	11,777.30	13,907.60	18.09
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
30	CHHATISGARH	44	78,072.89	89,205.29	14.26	12	39,499.71	50,751.46	28.49
31	JHARKHAND	44	62,432.53	68,421.43	9.59	11	23,892.14	29,881.04	25.07
32	UTTARAKHAND	32	34,539.29	46,026.02	33.26	9	24,756.17	36,269.40	46.51
33	TELANGANA	48	36,627.01	39,302.51	7.30	10	5,579.86	8,908.63	59.66

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						150	Crore and above		
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
34	MULTI STATE	131	3,71,661.49	4,85,400.65	30.60	67	1,31,034.61	2,47,830.68	89.13
Total		1687	21,44,627.66	25,72,670.28	19.96	450	7,04,175.51	11,65,016.75	65.44

^ - Cost Overrun = Anticipated Cost minus Original Cost

FLASH REPORT

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	13	10,370.13	10,484.23	5 - 33
3	COAL	105	1,12,965.37	1,18,879.80	5.24	42	26,869.08	30,076.22	12 - 228
4	FINANC	2	557.77	557.73	-0.01	1	209.00	208.96	18 - 18
5	FERTILISERS	4	1,101.28	1,101.28	0.00	4	1,101.28	1,101.28	11 - 16
6	MINES	5	7,078.62	7,075.17	-0.05	3	6,061.62	6,058.17	3 - 20
7	STEEL	9	23,478.11	29,608.45	26.11	7	22,780.27	28,895.27	8 - 74
8	PETROLEUM	142	2,82,358.27	2,90,123.35	2.75	70	1,24,228.91	1,30,628.73	3 - 110
9	POWER	67	2,83,975.91	3,56,631.39	25.59	41	2,12,493.18	2,81,578.59	7 - 155
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	15 - 15
11	HEALTH AND FAMILY WELFARE	28	13,445.26	13,766.81	2.39	14	5,215.15	5,028.49	11 - 88
12	RAILWAYS	311	4,61,691.03	6,98,197.39	51.23	159	2,02,957.83	3,31,316.06	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	653	5,33,495.62	5,27,455.00	-2.77	146	88,346.23	93,679.21	1 - 152
14	SHIPPING AND PORTS	1	5,369.18	4,613.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	8	17,926.94	29,137.35	62.53	3	14,013.36	25,343.36	5 - 71
16	URBAN DEVELOPMENT	35	2,84,575.18	2,92,612.80	2.82	10	57,007.19	58,941.99	2 - 60
17	WATER RESOURCES	51	27,955.51	73,105.94	161.51	17	15,955.05	61,103.24	1 - 72
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	1	246.31	246.31	16 - 16
19	COMMERCE AND INDUSTRY	3	17,654.73	19,292.94	9.28	2	17,352.09	18,990.30	19 - 22
20	HUMAN RESOURCE DEVELOPMENT	25	10,702.40	10,890.83	1.76	14	6,261.73	6,450.16	3 - 75
21	HOME AFFAIRS	3	1,549.07	2,346.14	51.45	2	1,382.09	2,179.16	23 - 32
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	3	527.83	538.27	51 - 62
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	1	151.33	151.33	42 - 42
Total		1687	21,44,627.66	25,72,670.28	19.96	558	8,82,703.66	11,74,901.33	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Antici pated cost	Cost overrun (%)	No.	Original Cost	Antici pated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,19,147.53	1,66,693.54	39.91	28	87,256.30	1,33,413.07	1 - 180
2	ARUNACHAL PRADESH	40	21,795.08	41,308.38	89.53	8	11,052.30	30,189.84	46 - 155
3	ASSAM	46	41,915.67	46,133.18	10.06	16	9,675.93	13,156.49	2 - 152
4	BIHAR	105	1,21,115.30	1,56,495.18	29.21	26	38,757.68	63,613.82	1 - 128
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	58	86,586.94	97,799.93	12.95	15	33,355.39	44,015.82	3 - 132
7	HARYANA	42	30,149.37	32,670.16	8.36	12	7,394.86	8,086.90	7 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	4	6,936.35	12,914.35	11 - 150
9	JAMMU AND KASHMIR	18	30,483.84	56,545.15	85.49	3	12,780.78	38,229.78	18 - 241
10	KARNATAKA	62	73,062.53	78,500.10	7.44	18	18,288.11	18,393.00	6 - 264
11	KERALA	21	37,063.23	41,659.56	12.40	8	12,453.35	13,698.06	12 - 53
12	MADHYA PRADESH	85	91,778.35	1,05,425.81	14.87	42	41,808.43	51,815.08	12 - 73
13	MAHARASHTRA	243	2,16,084.44	2,28,778.81	5.87	40	38,047.84	45,751.70	3 - 216
14	MANIPUR	4	5,785.67	13,535.85	133.95	2	4,971.74	12,721.92	36 - 144
15	MEGHALAYA	3	3,255.09	6,561.59	102.26	3	991.64	1,141.58	42 - 75
16	MIZORAM	3	7,717.62	1,17,013.32	100.90	5	3,513.57	7,542.27	75 - 128
17	NAGALAND	26	14,842.43	19,040.81	28.29	10	4,774.52	9,359.44	38 - 96
18	ODISHA	91	1,16,984.91	1,22,804.57	4.97	33	53,812.40	58,709.96	3 - 228
19	PUNJAB	28	14,921.05	18,022.94	20.79	11	4,648.87	4,544.57	6 - 34
20	RAJASTHAN	56	47,334.20	55,321.42	16.87	10	15,929.08	21,494.42	11 - 75
21	SIKKIM	9	3,476.73	10,883.48	213.04	4	1,839.62	9,187.00	87 - 94
22	TAMIL NADU	68	1,13,045.04	1,31,786.39	16.58	32	78,619.69	90,337.00	3 - 198
23	TRIPURA	7	2,076.64	2,259.45	8.80	5	1,535.74	1,718.55	18 - 62
24	UTTAR PRADESH	132	1,75,440.76	1,82,971.92	4.29	38	54,633.50	57,994.00	1 - 83
25	WEST BENGAL	78	66,850.06	84,903.63	27.01	29	29,489.47	38,507.63	5 - 324
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	1	417.23	441.33	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	37	90,924.18	92,955.69	2.23	20	53,813.34	55,050.61	2 - 88
29	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
30	CHHATISGARH	44	78,072.89	89,205.29	14.26	23	31,398.84	41,051.82	12 - 96
31	JHARKHAND	44	62,432.53	68,421.43	9.59	20	45,653.40	47,137.03	12 - 152
32	UTTARAKHAND	32	34,539.29	46,026.02	33.26	6	22,781.53	33,538.80	3 - 126
33	TELANGANA	48	36,627.01	39,302.51	7.30	16	17,935.49	18,457.69	9 - 180
34	MULTI STATE	131	3,71,661.49	4,85,400.65	30.60	69	1,37,853.67	1,92,492.80	3 - 276
Total		1687	21,44,627.66	25,72,670.28	19.96	558	8,82,703.66	11,74,901.33	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	14,010.40	14,034.50	0.17	11	9,612.42	9,636.52	5 - 33
3	COAL	105	1,36,841.92	1,18,879.80	-13.13	36	35,830.79	36,577.46	0 - 168
4	FINANC	2	557.77	557.73	-0.01	1	209.00	208.96	18 - 18
5	FERTILISERS	4	1,101.28	1,101.28	0.00	3	674.56	674.56	15 - 16
6	MINES	5	7,971.07	7,075.17	-11.24	1	355.00	355.00	3 - 3
7	STEEL	9	29,908.45	29,608.45	-1.00	2	1,417.54	1,417.54	8 - 38
8	PETROLEUM	142	2,95,873.58	2,90,123.35	-1.94	34	35,860.16	39,286.19	3 - 94
9	POWER	67	3,39,545.96	3,56,631.39	5.03	33	1,59,459.01	1,71,725.52	7 - 126
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	28	13,445.26	13,766.81	2.39	14	5,215.15	5,028.49	11 - 88
12	RAILWAYS	311	5,60,597.41	6,98,197.39	24.55	122	1,89,440.97	2,65,064.57	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	858	5,14,177.44	5,27,475.09	2.59	102	70,182.57	72,668.85	0 - 152
14	SHIPPING AND PORTS	1	5,369.18	4,333.31	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	8	17,926.78	2,137.35	-11.54	2	13,705.00	25,095.16	5 - 71
16	URBAN DEVELOPMENT	35	2,86,220.00	2,92,612.80	2.23	5	51,495.00	53,429.80	2 - 60
17	WATER RESOURCES	51	73,353.34	73,105.94	-0.34	17	61,352.88	61,103.24	1 - 72
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	-
19	COMMERCE AND INDUSTRY	3	17,654.73	19,292.94	9.28	2	17,352.09	18,990.30	19 - 22
20	HUMAN RESOURCE DEVELOPMENT	25	10,797.57	10,890.83	0.86	13	5,695.99	5,861.44	3 - 75
21	HOME AFFAIRS	3	1,549.09	2,346.14	51.45	2	1,382.09	2,179.16	23 - 32
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	3	606.71	538.27	51 - 62
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	1	151.33	151.33	42 - 42
Total		1687	23,99,126.18	25,72,670.28	7.23	408	7,29,363.26	8,50,340.36	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest cost						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	19	14,010.40	14,034.50	0.17	1	417.23	441.33	5.78
3	COAL	105	1,36,841.92	1,18,879.80	-13.13	13	23,505.04	27,085.34	15.23
4	FINANC	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0.00
7	STEEL	9	29,908.45	29,608.45	-1.00	0	0.00	0.00	0.00
8	PETROLEUM	142	2,95,873.58	2,90,123.35	-1.94	11	17,366.94	23,258.89	33.93
9	POWER	67	3,39,545.96	3,56,631.39	5.03	15	95,748.34	1,13,350.82	18.38
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	28	13,445.26	13,766.81	2.39	12	5,589.39	6,253.60	11.88
12	RAILWAYS	11	5,60,97.41	6,9,197.39	24.55	185	1,84,57.91	3,31,127.22	79.38
13	ROAD TRANSPORT AND HIGHWAYS	858	5,14,77.44	5,27,475.09	2.59	144	99,054.65	1,22,007.32	23.17
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	8	17,926.78	29,137.35	62.54	2	13,765.00	25,095.16	82.31
16	URBAN DEVELOPMENT	35	2,86,220.00	2,92,612.80	2.23	2	25,373.00	31,845.00	25.51
17	WATER RESOURCES	51	73,353.34	73,105.94	-0.34	1	231.79	234.03	0.97
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0.00
19	COMMERCE AND INDUSTRY	3	17,654.73	19,292.94	9.28	2	17,352.09	18,990.30	9.44
20	HUMAN RESOURCE DEVELOPMENT	25	10,797.57	10,890.83	0.86	4	1,473.32	1,680.94	14.09
21	HOME AFFAIRS	3	1,549.09	2,346.14	51.45	2	1,382.09	2,179.16	57.67
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0.00
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
Total		1687	23,99,126.18	25,72,670.28	7.23	397	5,15,312.79	7,44,048.11	44.39

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule & cost Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	69- 145
2	CIVIL AVIATION	19	14,010.40	14,034.50	0.17	1	417.23	441.33	33- 33
3	COAL	105	1,36,841.92	1,18,879.80	-13.13	10	3,418.37	4,291.38	12- 168
4	FINANC	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0- 0
7	STEEL	9	29,908.45	29,608.45	-1.00	0	0.00	0.00	0- 0
8	PETROLEUM	142	2,95,873.58	2,90,123.35	-1.94	6	14,220.45	18,779.20	3- 48
9	POWER	67	3,39,545.96	3,56,631.39	5.03	7	44,020.50	56,804.06	27- 126
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	8	13,452.6	1,763.81	2.3	4	1,013.69	1,199.69	24- 88
12	RAILWAYS	11	5,60,97.41	6,91,17.39	24.55	77	1,01,638.53	1,83,682.28	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	858	5,14,177.44	5,27,475.09	2.59	17	16,379.09	20,368.30	8- 152
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	8	17,926.78	29,137.35	62.54	2	13,765.00	25,095.16	5- 71
16	URBAN DEVELOPMENT	35	2,86,220.00	2,92,612.80	2.23	1	10,773.00	12,787.00	47- 47
17	WATER RESOURCES	51	73,353.34	73,105.94	-0.34	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0- 0
19	COMMERCE AND INDUSTRY	3	17,654.73	19,292.94	9.28	2	17,352.09	18,990.30	19- 22
20	HUMAN RESOURCE DEVELOPMENT	25	10,797.57	10,890.83	0.86	4	1,473.32	1,680.94	6- 75
21	HOME AFFAIRS	3	1,549.09	2,346.14	51.45	2	1,382.09	2,179.16	23- 32
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0- 0
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
Total		1687	23,99,126.18	25,72,670.28	7.23	136	2,55,599.36	3,86,797.80	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	69- 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	2	1,559.23	1,673.33	12- 33
3	COAL	105	1,12,965.37	1,18,879.80	5.24	16	10,654.89	14,737.48	12- 228
4	FINANC	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0- 0
7	STEEL	9	23,478.11	29,608.45	26.11	1	15,525.00	21,940.00	74- 74
8	PETROLEUM	142	2,82,358.27	2,90,123.35	2.75	21	52,355.37	69,279.48	3- 110
9	POWER	67	2,83,975.91	3,56,631.39	25.59	20	1,30,570.25	2,00,172.71	20- 155
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	28	13,445.26	13,766.81	2.39	4	1,042.60	1,199.69	24- 88
12	RAILWAYS	311	4,11,691.03	5,98,197.39	51.23	109	1,56,474.80	2,75,314.88	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	858	5,08,495.62	5,27,475.09	3.73	31	22,453.75	28,691.64	1- 152
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	8	17,926.94	29,137.35	62.53	1	13,334.00	24,664.00	71- 71
16	URBAN DEVELOPMENT	35	2,84,575.18	2,92,612.80	2.82	1	10,773.00	12,787.00	47- 47
17	WATER RESOURCES	51	27,955.51	73,105.94	161.51	1	10,151.04	55,548.87	25- 25
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0- 0
19	COMMERCE AND INDUSTRY	3	17,654.73	19,292.94	9.28	2	17,352.09	18,990.30	19- 22
20	HUMAN RESOURCE DEVELOPMENT	25	10,702.40	10,890.83	1.76	5	2,009.81	2,240.41	6- 75
21	HOME AFFAIRS	3	1,549.07	2,346.14	51.45	2	1,382.09	2,179.16	23- 32
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	51- 62
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
Total		1687	21,44,627.66	25,72,670.28	19.96	221	4,53,262.35	7,70,280.73	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

<u>List of projects completed/dropped/Frozen during current month</u> Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	05/2014	337.66	03/2019	337.66	03/2021	258.65
	<u>PETROLEUM</u>						
2	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	05/2016	429.00	01/2019	429.00	N.A.	373.62
3	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY Central Sector Projects	09/2016	208.35	07/2020	208.35	N.A.	170.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	FOUR LANE OF BIAORA - DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)	06/2015	1,533.79	01/2019	1,533.79	N.A.	1,648.90
5	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	03/2017	165.50	03/2020	172.16	N.A.	117.09
6	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	03/2017	239.68	03/2020	235.90	N.A.	219.75

TABLE-14

List of projects added Rs. 150 Crore and above					(December 2020)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>CIVIL AVIATION</u>					
1	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	353.61	5/2022	353.61	5/2022
2	UPGRADATION OF JABALPUR AIRPORT	6/2016	412.24	6/2021	412.24	6/2021
3	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	177.10	2/2020	177.10	6/2021
4	C/O NEW GREENFIELD AIRPORT AT HISSAR, HARYANA	1/2018	1,405.00	8/2022	1,405.00	3/2023
5	DEVELOPMENT OF TITICORNIA AIRPORT	5/2019	380.37	3/2022	380.37	3/2023
6	C/O OF NEW AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2019	611.80	3/2023	611.80	3/2023
	<u>COAL</u>					
7	NIGAH EXPANSION OCP (15 TO 25 MTPA)	11/2020	1,729.68	3/2025	1,729.68	3/2025
	<u>HUMAN RESOURCE DEVELOPMENT</u>					
8	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	392.51	6/2022	392.51	6/2022
	<u>PETROLEUM</u>					
9	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	403.00	8/2022	403.00	8/2022
10	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	1,421.46	2/2023	1,421.46	2/2023
11	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	921.00	9/2023	921.00	9/2023
12	DEVANGONTHI MARKETING TERMINAL	6/2020	200.00	6/2023	200.00	6/2023
13	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	1,378.00	12/2022	1,378.00	12/2022
	<u>POWER</u>					
14	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1,810.56	1/2026	1,810.56	1/2026
	<u>RAILWAYS</u>					

List of projects added Rs. 150 Crore and above					(December 2020)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
15	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	3,677.76	12/2023	3,677.76	12/2023
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
16	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	370.36	8/2022	370.36	8/2022
17	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	166.94	12/2020	166.94	12/2020
18	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO	3/2020	255.23	8/2020	255.23	8/2020
19	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	196.23	11/2020	196.00	11/2020
	<u>STEEL</u>					
20	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	377.18	5/2023	377.18	5/2023
	<u>URBAN DEVELOPMENT</u>					
21	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	1,828.00	9/2025	1,828.00	5/2024

TABLE-15

Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		5606	
Achieved up to month		2867	

FLASH REPORT

TABLE-16

List of projects reporting additional delayed Rs. 150 Crore and above							(December 2020)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) NLC	5,907.11	7,980.79	12/2015	12/2020	01/2021	1
2	PACHWARA SOUTH COAL BLOCK NLC	1,795.01	1,795.01	08/2022	08/2023	09/2023	1
3	KISTARAM OCP SCCL	242.29	164.04	03/2015	03/2021	03/2022	12
4	RCE OF INDARAM OCP(1.20 MTPA) SCCL	162.76	349.28	03/2015	03/2021	03/2022	12
5	JALAGAM VENGALA RAO OCP-II SCCL	447.06	473.22	03/2015	03/2021	03/2022	12
6	KALYANIKHANI OPENCAST PROJECT SCCL	417.33	384.32	07/2016	03/2021	03/2022	12
7	KAKATIYANKHANI OPENCAST-2 PROJECT SCCL	397.00	442.42	03/2019	03/2021	03/2022	12
8	SRP OCP- EXPANSION PROJECT SCCL	271.73	272.73	N.A.	01/2021	03/2022	12
9	GOPAL JI KANIHA OCP, MCL	457.77	684.32	03/2013	03/2022	03/2028	72
10	BALRAM EXPANSION OCP MCL	172.08	646.01	03/2010	03/2022	03/2029	84
11	BHUBANESWARI OCP, MCL (20.0 MTY) MCL	490.10	586.86	03/2017	09/2020	03/2031	126
	<u>STEEL</u>						
12	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT SAIL	1,154.18	1,154.18	12/2017	01/2021	02/2021	1
13	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	12/2020	02/2021	2
14	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E SAIL	263.36	263.36	09/2020	03/2021	05/2021	2
	<u>PETROLEUM</u>						
15	BS-VI PROJECTS CPCL	1,858.00	1,858.00	12/2019	12/2020	01/2021	1
16	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY IOCL	951.64	951.64	10/2019	10/2020	11/2020	1
17	PIPELINE REPLACEMENT PROJECT (PRP-VI) ONGC	763.92	733.86	12/2020	03/2021	05/2021	2

List of projects reporting additional delayed Rs. 150 Crore and above (December 2020)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
18	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	12/2020	03/2021	3
19	RE-LIQUIFIED NATURAL GAS CPCL	421.00	300.00	08/2020	06/2021	09/2021	3
20	SEA WATER DESALINATION PLANT MANGALORE REFIN Central Sector Projects	581.00	637.00	03/2020	03/2021	06/2021	3
21	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR IOCL	522.00	522.00	03/2021	09/2021	12/2021	3
22	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN OIL	224.75	222.21	08/2020	12/2020	03/2021	3
23	BSVI UPGRADATION MANGALORE REFIN	1,810.00	1,810.00	12/2019	03/2021	07/2021	4
24	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY IOCL	909.00	909.00	01/2021	08/2021	03/2022	7
25	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMA PURI AND CONST HPCL	2,677.00	3,072.00	06/2021	06/2021	08/2022	14
26	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV ONGC	3,228.80	3,978.07	03/2022	03/2022	05/2023	14
	<u>POWER</u>						
27	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	7,927.34	12/2009	12/2020	01/2021	1
28	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I NTPC	11,638.55	15,105.22	01/2018	01/2021	02/2021	1
29	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	546.36	11/2016	01/2021	02/2021	1
30	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) PGCIL	871.62	871.62	10/2017	12/2020	01/2021	1
31	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	9,583.00	07/2012	02/2021	03/2021	1
32	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	06/2021	07/2021	1
33	MUNPL-MEJA TPP - JV (2X660 MW) NTPC Joint Venture	9,750.89	12,176.28	02/2017	12/2020	01/2021	1
34	EASTERN REGION STRENGTHENING SCHEME-XV PGCIL	454.11	454.11	04/2018	12/2020	01/2021	1

List of projects reporting additional delayed Rs. 150 Crore and above (December 2020)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
35	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	02/2021	03/2021	1
36	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I PGCIL	374.63	374.63	04/2016	12/2020	03/2021	3
37	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO PGCIL	197.40	197.40	03/2018	12/2020	03/2021	3
	<u>HEALTH AND FAMILY WELFARE</u>						
38	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA HSCC Central Sector Projects	274.19	274.19	03/2019	12/2020	01/2021	1
39	SUPER SPECIALITY BLOCK PMSSY GOA HSCC Central Sector Projects	249.01	249.07	N.A.	12/2020	01/2021	1
40	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) HITES	785.00	715.06	04/2020	06/2021	07/2021	1
41	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB HITES	701.00	557.48	06/2020	07/2021	07/2021	1
42	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM HITES	875.00	747.80	05/2021	06/2022	07/2022	1
43	HOSPITAL AND TEACHING- AIIMS NAGPUR HSCC Central Sector Projects	582.99	582.99	N.A.	04/2021	06/2021	2
	<u>RAILWAYS</u>						
44	GONDIA-JABALPUR(GC),(SECR) SECR	511.86	2,005.25	04/2020	01/2021	04/2021	3
45	AGARTALA-AKHAURA NL NFR	569.63	742.00	03/2020	09/2021	03/2022	6
46	HUBLI- CHIKJAJUR SWR	1,156.94	1,140.94	03/2020	03/2021	11/2021	8
47	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) SECR	1,908.51	3,524.81	03/2023	03/2023	12/2023	9
48	JHARSUGUDA-BILASPUR 4TH LINE SECR	1,973.00	2,135.34	03/2021	03/2023	12/2023	9
49	ANUPPUR-KATNI SECR	1,370.00	1,370.94	12/2021	03/2023	12/2023	9
50	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT SECR	585.93	1,268.32	02/2019	12/2020	12/2021	12
51	WADSA-GADHCHIROLI NEW LINE (52.36 KM) SECR	229.00	1,096.00	12/2021	03/2023	12/2024	21

List of projects reporting additional delayed Rs. 150 Crore and above (December 2020)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
52	SAGALI VALMIKINAGAR DOUBLING 109.7 KM ECR	744.04	1,215.54	03/2021	03/2022	03/2024	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
53	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 MoRTH EPC	957.54	957.54	02/2020	03/2021	04/2021	1
54	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	897.03	11/2018	12/2020	01/2021	1
55	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID MoRTH	235.91	235.91	02/2018	12/2020	02/2021	2
56	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS MoRTH	184.62	184.62	02/2018	12/2020	02/2021	2
57	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS MoRTH	809.16	809.16	07/2018	03/2021	05/2021	2
58	SIX LANING FROM KM 277.400 TO KM 401.200 SECTION OF NH-3 IN THE STATE OF RAJASTHAN AND GUJARAT(AFP NHAI)	1,244.10	1,244.10	N.A.	01/2021	05/2021	3
59	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) NHAI EPC	291.53	291.53	N.A.	08/2021	11/2021	3
60	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) NHAI EPC	289.21	289.21	N.A.	06/2021	09/2021	3
61	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. MoRTH	205.05	205.05	03/2017	03/2021	06/2021	3
62	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N MoRTH	236.78	263.26	08/2019	08/2021	12/2021	4
63	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO MoRTH	254.30	254.30	10/2020	10/2020	03/2021	5
64	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN NHAI	649.50	649.50	03/2019	06/2021	12/2021	6
65	NAGPUR RING ROAD PACKAGE-1 NHAI	546.00	546.00	07/2019	06/2021	12/2021	6
66	NAGPUR RING ROAD PACKAGE-2 NHAI	591.66	591.66	07/2019	06/2021	12/2021	6
67	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS MoRTH	214.69	214.69	03/2018	03/2021	09/2021	6

List of projects reporting additional delayed Rs. 150 Crore and above (December 2020)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
68	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 MoRTH	279.70	398.52	08/2017	07/2019	02/2020	7
69	4-LANNING OF STHIYATHOPU-CHOLOPURAM NHAI Central Sector Projects	1,227.87	1,227.87	09/2017	08/2020	09/2021	13
70	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND MoRTH	160.27	213.97	08/2019	08/2021	11/2022	15
	<u>TELECOMMUNICATIONS</u>						
71	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART BSNL Central Sector Projects	431.16	431.16	06/2021	09/2021	11/2021	2
	<u>URBAN DEVELOPMENT</u>						
72	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, JALIN ROAD, NEW DELHI (SH- CONSTRUCTION OF NEW BUILDING (2) CPWD	23.50	230.50	03/2020	01/2021	02/2021	1
	<u>WATER RESOURCES</u>						
73	POLAVARAM IRRIGATION PROJECT PPA National Project	10,151.04	55,548.87	03/2020	12/2021	04/2022	4
	<u>DEFENCE PRODUCTION</u>						
74	RESIDENTIAL QUARTERS FOR HAL, BANGLORE CPWD	246.31	246.31	02/2020	03/2021	06/2021	3
	<u>HOME AFFAIRS</u>						
75	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD	1,219.21	2,000.00	10/2019	03/2021	09/2021	6

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	56,858.72
CIVIL AVIATION	19	13,786.34	140,10.40	14,034.50	2,597.30
COAL	105	1,12,965.37	1,368,41.92	1,18,879.80	45,071.37
FINANC	2	557.77	5,57.77	557.73	278.94
FERTILISERS	4	1,101.28	11,01.28	1,101.28	822.11
MINES	5	7,078.62	79,71.07	7,075.17	1,173.53
STEEL	9	23,478.11	299,08.45	29,608.45	22,856.57
PETROLEUM	142	2,82,358.27	2,958,73.58	2,90,123.35	1,03,816.81
POWER	67	2,83,975.91	3,395,45.96	3,56,631.39	2,47,060.58
HEAVY INDUSTRY	1	1,554.00	15,54.00	1,554.00	806.15
HEALTH AND FAMILY WELFARE	28	13,445.26	134,45.26	13,766.81	7,113.51
RAILWAYS	311	4,61,691.03	5,605,97.41	6,98,197.39	2,37,960.69
ROAD TRANSPORT AND HIGHWAYS	858	5,08,495.62	5,141,77.44	5,27,475.09	3,40,295.62
SHIPPING AND PORTS	1	5,369.18	53,69.18	4,633.81	1,787.23
TELECOMMUNICATIONS	8	17,921.94	1,79,26.78	19,137.05	15,571.00
URBAN DEVELOPMENT	3	2,84,571.18	2,862,20.00	2,82,612.00	99,751.53
WATER RESOURCES	51	27,955.51	733,33.34	73,105.94	20,164.30
DEFENCE PRODUCTION	1	246.31	2,46.31	246.31	115.20
COMMERCE AND INDUSTRY	3	17,654.73	176,54.73	19,292.94	9,699.64
HUMAN RESOURCE DEVELOPMENT	25	10,702.40	107,97.57	10,890.83	2,263.19
HOME AFFAIRS	3	1,549.07	15,49.09	2,346.14	1,010.33
RURAL DEVELOPMENT	4	889.43	9,68.31	899.87	472.05
CULTURE DEVELOPMENT	1	151.33	1,51.33	151.33	144.00
Grand total	1687	21,44,627.66	23,99,126.18	25,72,670.28	12,17,692.37

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,19,147.53	1,66,693.54	39.91	11	42,160.66	97,539.43	1 - 180
2	ARUNACHAL PRADESH	40	21,795.08	41,308.38	89.53	2	8,782.23	27,919.77	133 - 155
3	ASSAM	46	41,915.67	46,133.18	10.06	9	6,369.24	10,075.06	2 - 152
4	BIHAR	105	1,21,115.30	1,56,495.18	29.21	11	31,377.45	56,475.93	15 - 128
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	58	86,586.94	97,799.93	12.95	10	29,488.68	40,276.89	3 - 132
7	HARYANA	42	30,149.37	32,670.16	8.36	3	828.42	1,520.46	7 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	1	3,919.59	9,897.59	150 - 150
9	JAMMU AND KASHMIR	18	30,483.84	56,545.15	85.49	1	2,500.00	27,949.00	241 - 241
10	KARNATAKA	62	73,062.53	78,500.10	7.44	3	2,109.69	2,528.00	10 - 16
11	KERALA	21	37,063.23	41,659.56	12.40	4	7,431.46	8,700.21	29 - 53
12	MADHYA PRADESH	85	91,778.35	1,05,425.81	14.87	13	22,053.99	32,844.74	12 - 73
13	MAHARASHTRA	243	2,16,084.44	2,28,778.81	5.87	14	16,655.23	28,771.62	9 - 216
14	MANIPUR	4	5,785.67	13,535.85	133.95	1	4,454.17	12,264.15	144 - 144
15	MEGHALAYA	3	3,255.09	6,366.59	102.26	1	481.32	626.26	75 - 75
16	MIZORAM	3	7,777.62	1,170.32	0.90	5	3,513.57	7,542.27	75 - 128
17	NAGALAND	26	14,842.43	19,040.81	28.29	1	2,326.52	6,911.44	96 - 96
18	ODISHA	91	1,16,984.91	1,22,804.57	4.97	17	27,729.78	36,865.34	15 - 228
19	PUNJAB	28	14,921.05	18,022.94	20.79	3	1,201.49	1,284.88	18 - 34
20	RAJASTHAN	56	47,334.20	55,321.42	16.87	6	14,632.86	20,198.20	11 - 75
21	SIKKIM	9	3,476.73	10,883.48	213.04	2	1,521.76	8,869.14	87 - 94
22	TAMIL NADU	68	1,13,045.04	1,31,786.39	16.58	11	17,500.82	30,720.30	20 - 198
23	TRIPURA	7	2,076.64	2,259.45	8.80	3	921.97	1,104.78	24 - 62
24	UTTAR PRADESH	132	1,75,440.76	1,82,971.92	4.29	8	22,849.43	27,517.72	20 - 83
25	WEST BENGAL	78	66,850.06	84,903.63	27.01	12	19,583.70	28,616.89	28 - 324
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	1	417.23	441.33	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	37	90,924.18	92,955.69	2.23	4	6,610.76	7,927.23	19 - 88
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
30	CHHATISGARH	44	78,072.89	89,205.29	14.26	9	25,751.75	35,524.08	27 - 84
31	JHARKHAND	44	62,432.53	68,421.43	9.59	4	16,591.98	18,075.61	30 - 44
32	UTTARAKHAND	32	34,539.29	46,026.02	33.26	3	21,686.06	32,443.84	3 - 126
33	TELANGANA	48	36,627.01	39,302.51	7.30	7	2,427.32	3,602.79	9 - 144
34	MULTI STATE	131	3,71,661.49	4,85,400.65	30.60	41	89,300.22	1,45,245.78	3 - 276
Total		1687	21,44,627.66	25,72,670.28	19.96	221	4,53,262.35	7,70,280.73	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	158	8
2	ROAD TRANSPORT AND HIGHWAYS	149	2
3	PETROLEUM	58	4
4	POWER	41	5
5	URBAN DEVELOPMENT	24	0
6	COAL	21	2
7	CIVIL AVIATION	5	0
8	STEEL	5	2
9	ATOMIC ENERGY	4	0
10	HEALTH AND FAMILY WELFARE	3	0
11	TELECOMMUNICATIONS	3	0
12	COMMERCE AND INDUSTRY	2	0
13	MINES	1	0
14	HEAVY INDUSTRY	1	0
15	SHIPPING AND PORTS	1	0
16	WATER RESOURCES	1	1
17	HOME AFFAIRS	1	1
	Total	478	25

FLASH REPORT

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2020			
	<u>STEEL</u>			
1	INSTALLATION OF NEW HOT STRIP MILL AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000094]	3,127.30	04/2018	3,201.42
	<u>PETROLEUM</u>			
2	INTEGRATED DEVELOPMENT OF B-127 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000131]	2,059.63	03/2015	2,011.80
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000197]	6,068.80	04/2019	4,956.05
4	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000212]	4,619.94	12/2017	4,663.66
5	INDMAX PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000243]	2,322.00	12/2019	1,718.52
6	BS-VI PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000310]	3,380.00	09/2019	2,381.00
7	BS-VI PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000320]	1,222.00	09/2019	764.17
8	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000322]	2,934.40	09/2019	1,957.94
9	BS-VI PROJECT AT PANIPAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000325]	3,529.00	07/2019	2,095.75
	July,2020			
10	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000204]	2,818.88	03/2019	2,907.03
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000347]	723.54	02/2018	1,163.64
12	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000492]	867.66	05/2018	1,289.81
	<u>URBAN DEVELOPMENT</u>			
13	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000101]	768.88	02/2014	1,125.98
	August,2020			
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
14	RESID UPGRADATION PROJECT (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000184]	3,110.36	11/2015	2,915.00
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA- BARAUNI CRUDE OIL TRUNK PIPELINE (OIL INDIA LIMITED) - [N18000148]	871.35	03/2015	565.63
	<u>URBAN DEVELOPMENT</u>			
16	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000109]	253.92	06/2016	1,113.24
	December,2020			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000505]	1,583.79	01/2019	1,648.90

FLASH REPORT

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)

FLASH REPORT

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	471
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	7
No of Projects in Current Month	478

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	207 (43.31%)	6 (1.26%)	70 (14.64%)	45 (9.41%)	150 (31.38%)	478
Latest Approved (Date)	152 (31.80%)	12 (2.51%)	121 (25.31%)	43 (9.00%)	150 (31.38%)	478

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	392	13,51,408.99	15,25,052.46	6,56,683.11	43.10	1,73,643.47	12.80
Project with Revision in Cost	86	5,27,319.63	5,36,691.25	3,05,096.02	56.80	9,371.62	1.80
Total	478	18,78,728.62	20,61,743.71	9,61,779.13	46.65	1,83,015.09	9.74
Original Cost of All Projects							
Original Cost	478	16,47,443.83	20,61,743.71	9,61,779.13	46.65	4,14,299.88	25.15

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	207	7,30,610.41	10,22,529.92	5,99,745.82	58.70	2,91,919.51	39.96
Latest Approved (RCE)	152	6,21,301.44	7,41,006.15	4,24,697.85	57.30	1,19,704.71	19.27

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	25	84,638.39	1,59,203.32	97,795.52	61.40	74,564.93	88.10
Total	25	84,638.39	1,59,203.32	97,795.52	61.43	74,564.93	88.10

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	7,613.00	7,700.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	1	76,731.4	80,810.37	5.98	3	2,805.84	3,365.07	17.67
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	5	22,254.04	28,369.04	27.48	1	15,525.00	21,940.00	41.32
6	PETROLEUM	58	2,47,613.90	2,54,901.88	2.94	17	59,190.55	77,788.51	31.42
7	POWER	41	2,73,295.13	3,45,610.15	26.46	23	1,58,707.78	2,31,539.85	45.89
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	2	2,928.00	3,299.00	12.67
10	RAILWAYS	158	3,92,325.06	6,20,659.40	58.20	117	1,94,861.32	4,24,496.65	117.85
11	ROAD TRANSPORT AND HIGHWAYS	149	2,18,466.83	2,34,268.80	7.23	42	57,066.33	73,896.67	29.49
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	3	16,522.17	27,752.17	67.97	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	24	2,80,464.14	2,88,350.02	2.81	4	34,818.79	42,783.87	22.88
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
16	COMMERCE AND INDUSTRY	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
17	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
Total		478	16,47,443.83	20,61,743.71	25.15	218	6,19,372.95	10,49,043.79	69.37

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	20	97,962.39	1,45,333.42	48.36	10	45,532.51	1,02,125.54	124.29
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	3	10,761.23	29,956.67	178.38
3	ASSAM	6	27,224.48	30,181.21	10.86	4	4,630.48	7,587.21	63.85
4	BIHAR	27	87,426.57	1,20,831.59	38.21	15	33,512.04	66,917.06	99.68
5	GUJARAT	23	68,616.17	79,233.87	15.47	10	30,646.76	41,923.51	36.80
6	HARYANA	12	16,498.78	18,358.28	11.27	1	1,108.00	2,967.50	167.82
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	3	8,237.58	18,122.01	119.99
8	JAMMU AND KASHMIR	12	28,258.96	54,186.21	91.75	3	6,236.00	32,296.00	417.90
9	KARNATAKA	18	54,654.87	59,594.94	9.04	9	14,184.58	19,140.65	34.94
10	KERALA	10	31,871.86	35,970.00	12.86	7	15,996.96	20,119.14	25.77
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	11	31,854.48	45,006.24	41.29
12	MAHARASHTRA	48	1,33,622.87	1,54,690.02	11.50	1	3,051.57	5,705.65	48.91
13	MANIPUR	1	14,417.12	12,264.15	175.34	1	4,451.17	12,264.15	175.34
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	130.69
16	NAGALAND	3	7,896.52	12,481.44	58.06	1	2,326.52	6,911.44	197.07
17	ODISHA	34	89,072.93	97,711.91	9.70	11	26,251.24	34,890.22	32.91
18	PUNJAB	4	5,049.00	7,358.55	45.74	2	2,557.95	4,867.50	90.29
19	RAJASTHAN	12	26,941.23	33,616.69	24.78	5	16,355.72	23,031.18	40.81
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	23	92,591.84	1,10,446.24	19.28	12	35,173.23	53,422.63	51.88
22	UTTAR PRADESH	47	1,39,213.12	1,46,352.52	5.13	14	48,992.89	57,073.42	16.49
23	WEST BENGAL	25	47,182.71	64,023.25	35.69	15	26,826.10	43,697.67	62.89
24	DELHI	10	81,740.38	83,303.70	1.91	3	10,256.21	11,898.73	16.01
25	CHHATISGARH	14	65,083.62	75,721.45	16.34	8	37,748.96	48,488.81	28.45
26	JHARKHAND	15	51,718.76	57,272.09	10.74	6	22,644.99	28,198.32	24.52
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	4	23,213.06	34,244.91	47.52
28	TELANGANA	5	18,567.06	20,644.30	11.19	2	2,378.60	4,455.84	87.33
29	MULTI STATE	64	3,43,314.76	4,52,496.60	31.80	36	1,18,801.71	2,30,527.32	94.04
Total		478	16,47,443.83	20,61,743.71	25.15	218	6,19,372.95	10,49,043.79	69.37

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	4	6,397.00	6,487.00	7 - 12
3	COAL	21	76,251.14	80,810.37	5.98	6	12,915.88	14,989.56	12 - 83
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	20 - 20
5	STEEL	5	22,254.04	28,369.04	27.48	5	22,254.04	28,369.04	29 - 74
6	PETROLEUM	58	2,47,613.90	2,54,901.88	2.94	23	1,05,818.97	1,11,842.09	3 - 110
7	POWER	41	2,73,295.13	3,45,610.15	26.46	28	2,07,063.93	2,76,091.78	7 - 155
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	15 - 15
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	0	0.00	0.00	-
10	RAILWAYS	158	3,92,325.06	6,20,659.40	58.20	102	1,67,688.35	2,98,039.92	2 - 324
11	ROAD TRANSPORT AND HIGHWAYS	149	2,18,466.83	2,24,238.88	2.63	21	97,293.38	41,822.56	1 - 105
12	SHIPPING AND PORTS	1	3,369.18	4,638.81	37.50	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	16,522.17	27,732.17	67.97	1	13,334.00	24,664.00	71 - 71
14	URBAN DEVELOPMENT	24	2,80,464.14	2,88,350.02	2.81	4	54,308.00	56,242.80	2 - 60
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
16	COMMERCE AND INDUSTRY	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	19 - 22
17	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	23 - 23
Total		478	16,47,443.83	20,61,743.71	25.15	207	7,30,610.41	10,22,529.92	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	20	97,962.39	1,45,333.42	48.36	10	80,449.98	1,26,487.47	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	3	10,035.33	29,172.87	60 - 155
3	ASSAM	6	27,224.48	30,181.21	10.86	4	4,630.48	7,587.21	2 - 48
4	BIHAR	27	87,426.57	1,20,831.59	38.21	9	32,035.52	56,507.05	15 - 128
5	GUJARAT	23	68,616.17	79,233.87	15.47	10	31,026.32	41,381.90	3 - 69
6	HARYANA	12	16,498.78	18,358.28	11.27	2	3,764.72	3,764.72	20 - 29
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	2	6,405.52	12,383.52	15 - 150
8	JAMMU AND KASHMIR	12	28,258.96	54,186.21	91.75	3	12,780.78	38,229.78	18 - 241
9	KARNATAKA	18	54,654.87	59,594.94	9.04	7	11,461.46	11,602.77	8 - 264
10	KERALA	10	31,871.86	35,970.00	12.86	4	10,137.40	11,274.92	12 - 44
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	12	27,938.55	37,717.18	12 - 73
12	MAHARASHTRA	48	1,38,642.87	1,54,590.02	11.50	14	22,118.91	33,858.33	6 - 216
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	144 - 144
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	2	2,313.47	5,521.45	130.69	1	2,391.47	5,521.45	117 - 117
16	NAGALAND	3	7,816.52	11,481.44	48.06	1	2,316.52	6,911.44	96 - 96
17	ODISHA	34	89,072.93	97,711.91	9.70	18	42,553.06	50,533.21	12 - 204
18	PUNJAB	4	5,049.00	7,358.55	45.74	1	1,069.59	1,069.59	14 - 14
19	RAJASTHAN	12	26,941.23	33,616.69	24.78	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	87 - 87
21	TAMIL NADU	23	92,591.84	1,10,446.24	19.28	15	69,978.02	81,704.87	3 - 145
22	UTTAR PRADESH	47	1,39,213.12	1,46,352.52	5.13	13	45,418.09	49,069.79	9 - 47
23	WEST BENGAL	25	47,182.71	64,023.25	35.69	12	23,700.15	32,584.76	12 - 324
24	DELHI	10	81,740.38	83,303.70	1.91	6	48,705.73	49,812.32	2 - 60
25	CHHATISGARH	14	65,083.62	75,721.45	16.34	6	25,403.02	34,561.43	21 - 74
26	JHARKHAND	15	51,718.76	57,272.09	10.74	8	41,525.31	42,817.19	12 - 83
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	5	18,567.06	20,644.30	11.19	2	11,759.46	11,759.46	16 - 180
29	MULTI STATE	64	3,43,314.76	4,52,496.60	31.80	38	1,23,193.31	1,75,829.70	3 - 276
Total		478	16,47,443.83	20,61,743.71	25.15	207	7,30,610.41	10,22,529.92	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,703.90	7,703.90	0.00	4	6,487.00	6,487.00	7 - 12
3	COAL	21	78,324.82	80,810.37	3.17	6	25,575.69	25,575.69	0 - 61
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	-
5	STEEL	5	28,669.04	28,369.04	-1.05	1	1,154.18	1,154.18	38 - 38
6	PETROLEUM	58	2,60,532.84	2,54,901.88	-2.16	11	26,713.39	30,239.56	3 - 94
7	POWER	41	3,28,733.44	3,45,610.15	5.13	20	1,53,972.20	1,66,238.71	7 - 126
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	0	0.00	0.00	-
10	RAILWAYS	158	4,94,504.63	6,20,659.40	25.51	76	1,64,787.53	2,39,010.48	2 - 324
11	ROAD TRANSPORT AND HIGHWAYS	149	2,20,664.31	2,34,268.80	6.17	22	35,314.28	38,276.56	8 - 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
13	TELECOMMUNICATIONS	3	16,522.17	27,752.17	67.97	1	13,334.00	24,664.00	71 - 71
14	URBAN DEVELOPMENT	2	1,81,957.22	2,88,500.02	59.27	3	50,538.00	52,472.80	2 - 60
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
16	COMMERCE AND INDUSTRY	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	19 - 22
17	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	23 - 23
Total		478	18,78,728.62	20,61,743.71	9.74	152	6,21,301.44	7,41,006.15	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	5	7,703.90	7,703.90	0.00	0	0.00	0.00	0.00
3	COAL	21	78,324.82	80,810.37	3.17	2	19,898.73	22,384.28	12.49
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0.00
5	STEEL	5	28,669.04	28,369.04	-1.05	0	0.00	0.00	0.00
6	PETROLEUM	58	2,60,532.84	2,54,901.88	-2.16	6	14,916.29	20,427.40	36.95
7	POWER	41	3,28,733.44	3,45,610.15	5.13	13	95,057.57	1,12,451.33	18.30
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	2	2,928.00	3,299.00	12.67
10	RAILWAYS	158	4,94,504.63	6,20,659.40	25.51	99	1,54,415.24	2,84,255.11	84.08
11	ROAD TRANSPORT AND HIGHWAYS	149	2,20,664.31	2,34,268.80	6.17	42	57,507.08	73,481.14	27.78
12	SHIPPING AND PORTS	1	5,69.18	1,639.81	28.79	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	5	10,22.17	2,752.17	67.05	1	10,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	24	2,81,57.22	2,83,351.02	2.27	2	25,313.00	31,845.00	25.51
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
16	COMMERCE AND INDUSTRY	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
17	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
Total		478	18,78,728.62	20,61,743.71	9.74	173	4,31,457.21	6,34,296.56	47.01

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	69- 145
2	CIVIL AVIATION	5	7,703.90	7,703.90	0.00	0	0.00	0.00	0- 0
3	COAL	21	78,324.82	80,810.37	3.17	0	0.00	0.00	0- 0
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0- 0
5	STEEL	5	28,669.04	28,369.04	-1.05	0	0.00	0.00	0- 0
6	PETROLEUM	58	2,60,532.84	2,54,901.88	-2.16	4	13,229.29	17,636.86	3- 32
7	POWER	41	3,28,733.44	3,45,610.15	5.13	7	44,020.50	56,804.06	27- 126
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	0	0.00	0.00	0- 0
10	RAILWAYS	158	4,94,504.63	6,20,659.40	25.51	51	90,903.40	1,66,635.45	2- 324
11	ROAD TRANSPORT AND HIGHWAYS	149	2,20,664.31	2,34,268.80	6.17	8	12,135.40	15,097.68	8- 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	3	16,222.17	2,752.17	67.9	1	13,344.00	24,664.00	71- 71
14	URBAN DEVELOPMENT	24	2,81,57.22	2,28,350.02	2.27	1	10,773.00	12,787.00	47- 47
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
16	COMMERCE AND INDUSTRY	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	19- 22
17	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	23- 23
Total		478	18,78,728.62	20,61,743.71	9.74	78	2,32,422.89	3,55,114.35	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	69- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	12- 12
3	COAL	21	76,251.14	80,810.37	5.98	1	5,907.11	7,980.79	61- 61
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	5	22,254.04	28,369.04	27.48	1	15,525.00	21,940.00	74- 74
6	PETROLEUM	58	2,47,613.90	2,54,901.88	2.94	12	48,820.57	65,060.13	3- 110
7	POWER	41	2,73,295.13	3,45,610.15	26.46	18	1,29,861.79	1,99,406.69	20- 155
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	0	0.00	0.00	0- 0
10	RAILWAYS	158	3,92,325.06	6,20,659.40	58.20	75	1,21,904.44	2,53,557.00	2- 324
11	ROAD TRANSPORT AND HIGHWAYS	149	2,18,466.83	2,34,268.80	7.23	9	13,668.02	17,596.68	1- 105
12	SHIPPING AND PORTS	1	5,369.12	4,633.21	-13.70	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	3	16,522.17	27,752.17	67.97	1	13,334.00	24,664.00	71- 71
14	URBAN DEVELOPMENT	24	2,80,464.14	2,88,350.02	2.81	1	10,773.00	12,787.00	47- 47
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
16	COMMERCE AND INDUSTRY	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	19- 22
17	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	23- 23
Total		478	16,47,443.83	20,61,743.71	25.15	126	4,16,929.27	7,21,262.46	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

<u>List of projects completed/dropped/Frozen during current month</u>							
Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
1	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)	06/2015	1,583.79	01/2019	1,583.79	N.A.	1,648.90

FLASH REPORT

TABLE-32

List of projects added Rs. 1000 Crore and above					(December 2020)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>CIVIL AVIATION</u>					
1	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	1,405.00	8/2022	1,405.00	3/2023
	<u>COAL</u>					
2	NIGAH EXPANSION OCP (15 TO 25 MTPA)	11/2020	1,729.68	3/2025	1,729.68	3/2025
	<u>PETROLEUM</u>					
3	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	1,378.00	12/2022	1,378.00	12/2022
4	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB	5/2020	1,421.46	2/2023	1,421.46	2/2023
	<u>POWER</u>					
5	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1,810.56	1/2026	1,810.56	1/2026
	<u>RAILWAYS</u>					
6	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	3,677.76	12/2023	3,677.76	12/2023
	<u>URBAN DEVELOPMENT</u>					
7	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	1,828.00	9/2025	1,828.00	5/2024

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2520	
Achieved up to month	1598	

FLASH REPORT

TABLE-34

List of projects reporting additional delayed Rs. 1000 Crore and above							(December 2020)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) NLC	5,907.11	7,980.79	12/2015	12/2020	01/2021	1
2	PACHWARA SOUTH COAL BLOCK NLC	1,795.01	1,795.01	08/2022	08/2023	09/2023	1
	<u>STEEL</u>						
3	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT SAIL	1,154.18	1,154.18	12/2017	01/2021	02/2021	1
4	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	12/2020	02/2021	2
	<u>PETROL</u>						
5	BS-VI PROJECTS CPCL	1,850.00	1,850.00	12/2019	12/2020	01/2021	1
6	BSVI UPGRADATION MANGALORE REFIN	1,810.00	1,810.00	12/2019	03/2021	07/2021	4
7	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST HPCL	2,677.00	3,072.00	06/2021	06/2021	08/2022	14
8	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV ONGC	3,228.80	3,976.67	03/2022	03/2022	05/2023	14
	<u>POWER</u>						
9	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	7,927.34	12/2009	12/2020	01/2021	1
10	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I NTPC	11,638.55	15,105.22	01/2018	01/2021	02/2021	1
11	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	9,583.00	07/2012	02/2021	03/2021	1
12	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	06/2021	07/2021	1
13	MUNPL-MEJA TPP - JV (2X660 MW) NTPC Joint Venture	9,750.89	12,176.28	02/2017	12/2020	01/2021	1
	<u>RAILWAYS</u>						

List of projects reporting additional delayed Rs. 1000 Crore and above (December 2020)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	GONDIA-JABALPUR(GC),(SECR) SECR	511.86	2,005.25	04/2020	01/2021	04/2021	3
15	HUBLI- CHIKJAJUR SWR	1,156.94	1,140.94	03/2020	03/2021	11/2021	8
16	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) SECR	1,908.51	3,524.81	03/2023	03/2023	12/2023	9
17	JHARSUGUDA-BILASPUR 4TH LINE SECR	1,973.00	2,135.34	03/2021	03/2023	12/2023	9
18	ANUPPUR-KATNI SECR	1,370.00	1,370.94	12/2021	03/2023	12/2023	9
19	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT SECR	585.93	1,268.32	02/2019	12/2020	12/2021	12
20	WADSA-GADHCHIROLI NEW LINE (52.36 KM) SECR	229.00	1,096.00	12/2021	03/2023	12/2024	21
21	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM ECR	744.04	1,215.54	03/2021	03/2022	03/2024	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
22	SIX LANNING FROM KM 274.00 TO KM 101.200 SECTION OF NH-1 IN THE STATE OF RAJASTHAN AND GUJARAT(APP NHAI)	1,244.10	1,244.10	N.A.	01/2021	05/2021	3
23	4-LANNING OF STHIYATHOPU-CHOLOPURAM NHAI Central Sector Projects	1,227.87	1,227.87	09/2017	08/2020	09/2021	13
	<u>WATER RESOURCES</u>						
24	POLAVARAM IRRIGATION PROJECT PPA National Project	10,151.04	55,548.87	03/2020	12/2021	04/2022	4
	<u>HOME AFFAIRS</u>						
25	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD	1,219.21	2,000.00	10/2019	03/2021	09/2021	6

TABLE-35

Sector wise analysis of projects Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	56,858.72
CIVIL AVIATION	5	7,613.90	77,03.90	7,703.90	1,118.82
COAL	21	76,251.14	783,24.82	80,810.37	31,736.41
MINES	1	5,540.00	64,35.90	5,540.00	614.13
STEEL	5	22,254.04	286,69.04	28,369.04	22,248.56
PETROLEUM	58	2,47,613.90	2,605,32.84	2,54,901.88	90,167.79
POWER	41	2,73,295.13	3,287,33.44	3,45,610.15	2,39,736.95
HEAVY INDUSTRY	1	1,554.00	15,54.00	1,554.00	806.15
HEALTH AND FAMILY WELFARE	3	4,332.00	43,32.00	4,703.00	671.65
RAILWAYS	158	3,92,325.06	4,945,04.63	6,20,659.40	2,02,016.74
ROAD TRANSPORT AND HIGHWAYS	149	2,18,466.83	2,206,64.31	2,34,268.80	1,73,609.46
SHIPPING AND PORTS	1	5,369.18	53,69.18	4,633.81	1,787.23
TELECOMMUNICATIONS	3	16,522.17	165,22.17	27,752.17	15,492.90
URBAN DEVELOPMENT	24	2,80,464.14	2,819,57.22	2,88,350.02	97,863.97
WATER RESOURCES	1	10,151.04	155,48.87	15,548.87	16,563.13
COMMERCE AND INDUSTRY	2	17,351.09	173,52.09	8,990.10	9,630.64
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	841.88
Grand total	478	16,47,443.83	18,78,728.62	20,61,743.71	9,61,779.13


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	20	97,962.39	1,45,333.42	48.36	7	41,080.27	96,339.76	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	2	8,782.23	27,919.77	133 - 155
3	ASSAM	6	27,224.48	30,181.21	10.86	4	4,630.48	7,587.21	2 - 48
4	BIHAR	27	87,426.57	1,20,831.59	38.21	7	29,343.85	53,815.38	15 - 128
5	GUJARAT	23	68,616.17	79,233.87	15.47	8	28,618.93	38,974.51	3 - 69
6	HARYANA	12	16,498.78	18,358.28	11.27	0	0.00	0.00	-
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	1	3,919.59	9,897.59	150 - 150
8	JAMMU AND KASHMIR	12	28,258.96	54,186.21	91.75	1	2,500.00	27,949.00	241 - 241
9	KARNATAKA	18	54,654.87	59,594.94	9.04	1	950.69	1,108.00	16 - 16
10	KERALA	10	31,871.86	35,970.00	12.86	3	6,824.40	7,985.96	29 - 44
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	8	20,545.18	30,841.85	12 - 73
12	MAHARASHTRA	48	1,38,642.87	1,54,590.22	11.50	10	14,064.20	26,703.71	9 - 216
13	MANIPUR	1	12,264.15	12,264.15	0.00	1	12,264.15	12,264.15	144 - 144
14	MEGHALAYA	1	96.46	4,081.02	4150.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	117 - 117
16	NAGALAND	3	7,896.52	12,481.44	58.06	1	2,326.52	6,911.44	96 - 96
17	ODISHA	34	89,072.93	97,711.91	9.70	10	25,065.60	33,045.75	15 - 204
18	PUNJAB	4	5,049.00	7,358.55	45.74	0	0.00	0.00	-
19	RAJASTHAN	12	26,941.23	33,616.69	24.78	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	87 - 87
21	TAMIL NADU	23	92,591.84	1,10,446.24	19.28	7	16,362.78	28,484.63	27 - 145
22	UTTAR PRADESH	47	1,39,213.12	1,46,352.52	5.13	5	21,993.73	26,417.38	20 - 47
23	WEST BENGAL	25	47,182.71	64,023.25	35.69	8	18,719.64	27,619.28	30 - 324
24	DELHI	10	81,740.38	83,303.70	1.91	2	5,992.21	7,178.00	19 - 23
25	CHHATISGARH	14	65,083.62	75,721.45	16.34	5	24,001.00	33,261.43	27 - 74
26	JHARKHAND	15	51,718.76	57,272.09	10.74	2	16,090.78	17,382.66	33 - 40
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	5	18,567.06	20,644.30	11.19	0	0.00	0.00	-
29	MULTI STATE	64	3,43,314.76	4,52,496.60	31.80	27	82,023.92	1,35,930.71	3 - 276
Total		478	16,47,443.83	20,61,743.71	25.15	126	4,16,929.27	7,21,262.46	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

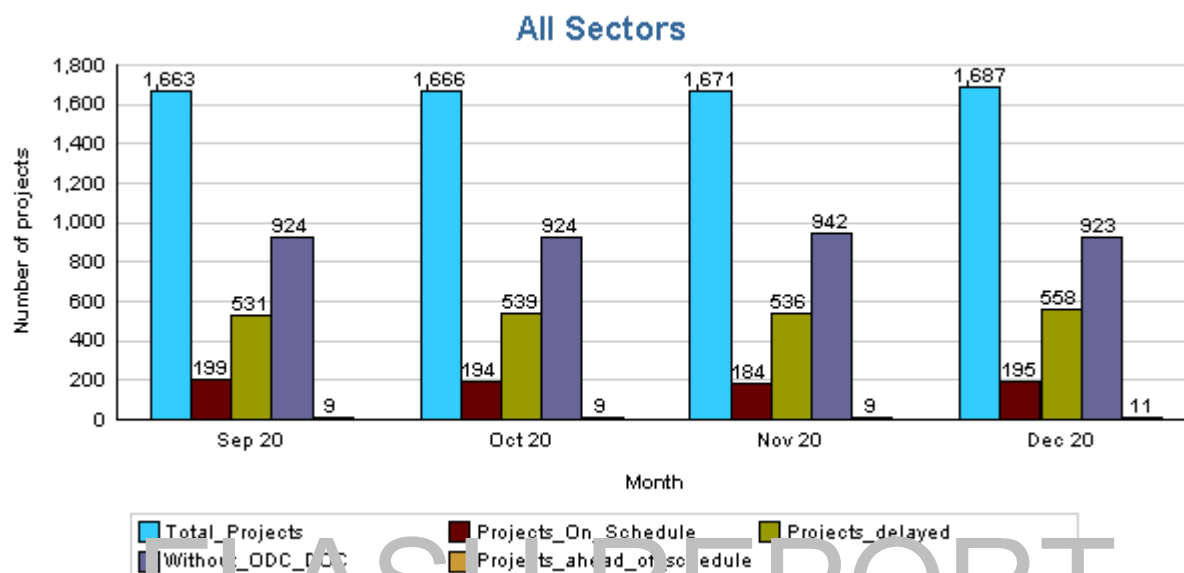


Break-up of 558 Delayed projects in December 2020

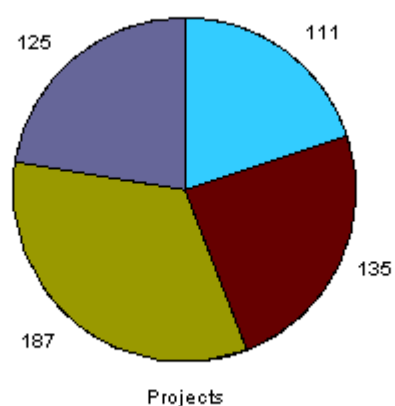


Delay in Months

Legend: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of WATER RESOURCES Sector

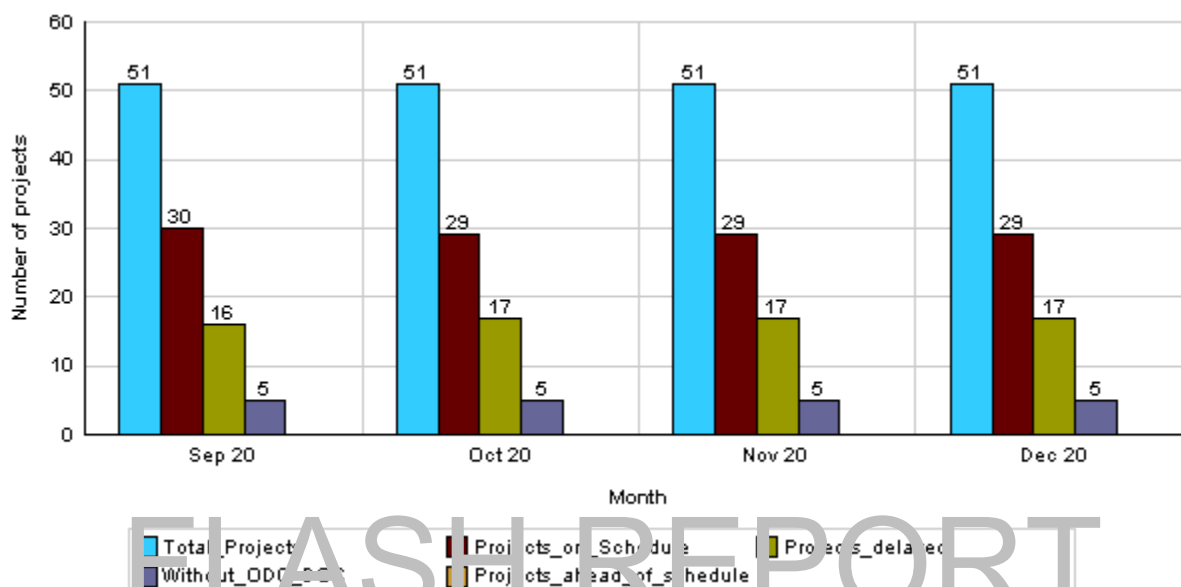


Break-up of 17 Delayed projects in December 2020

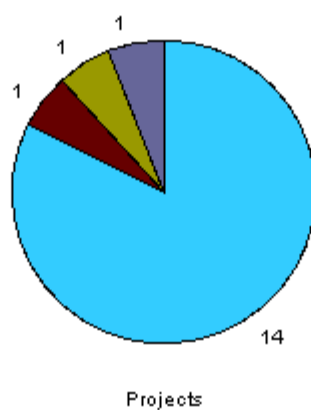


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	14	1	1	1

Graphical Presentation of URBAN DEVELOPMENT Sector

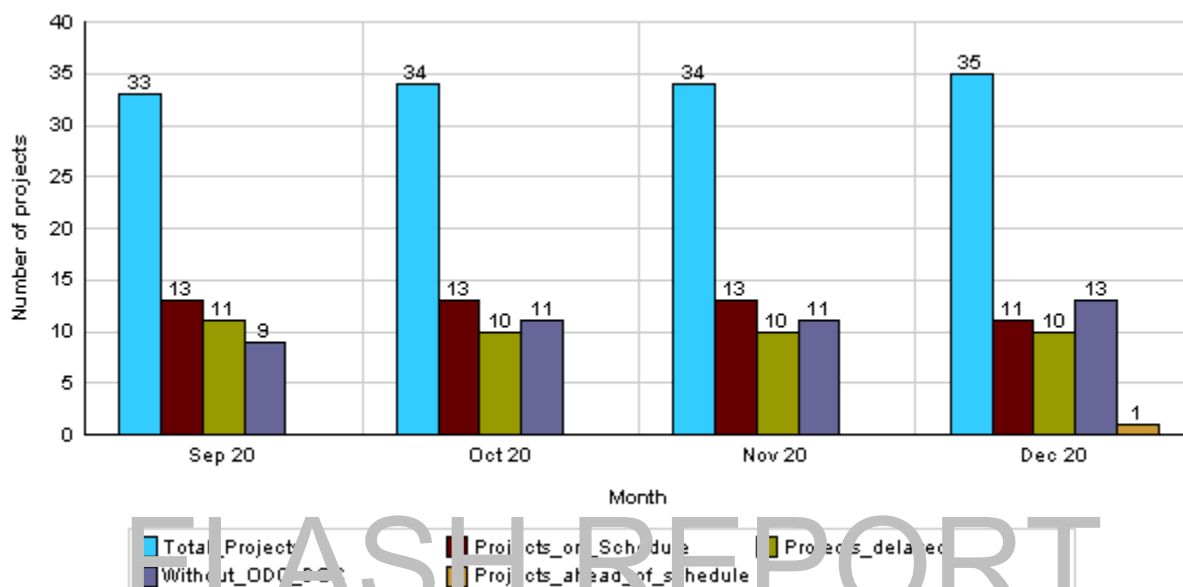


Break-up of 10 Delayed projects in December 2020

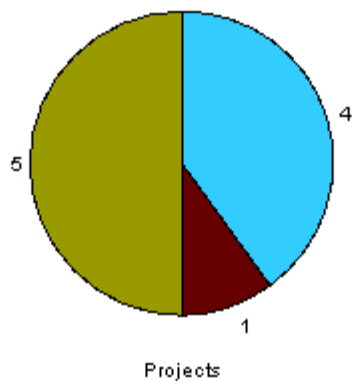


Delay in Months: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of HUMAN RESOURCE DEVELOPMENT Sector

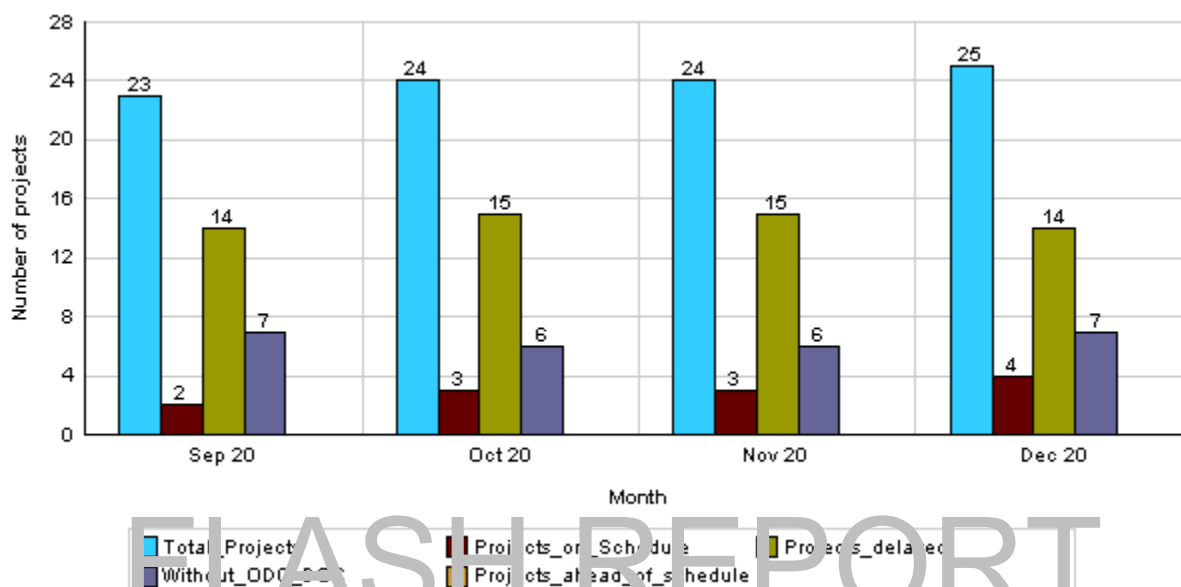


Break-up of 14 Delayed projects in December 2020

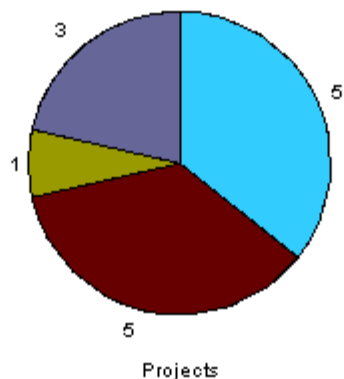


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of TELECOMMUNICATIONS Sector

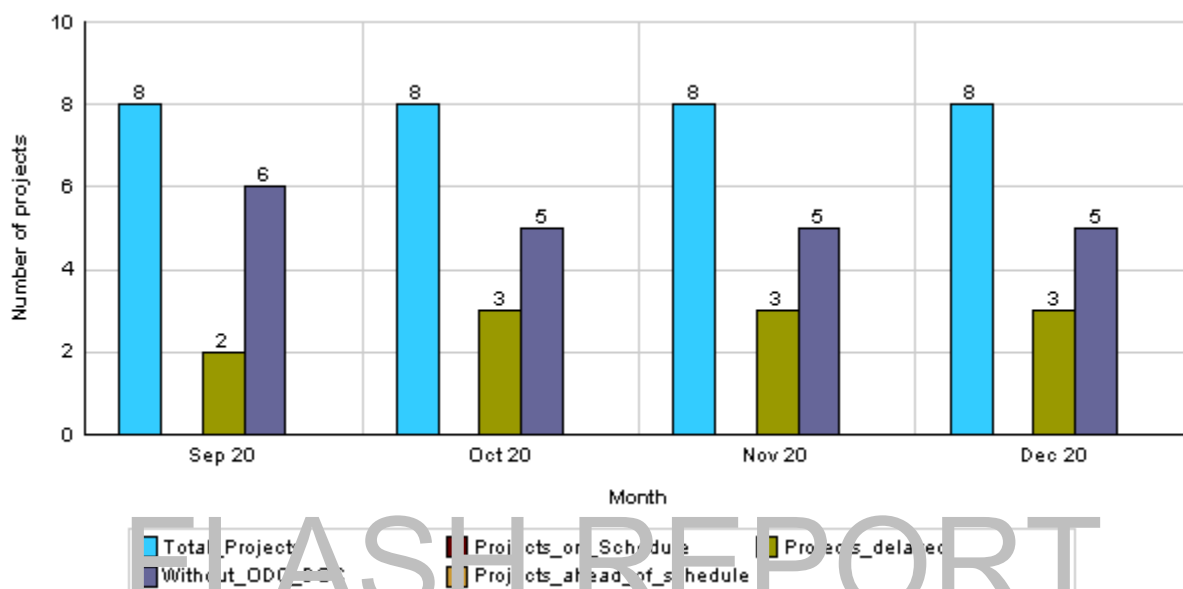


Break-up of 3 Delayed projects in December 2020

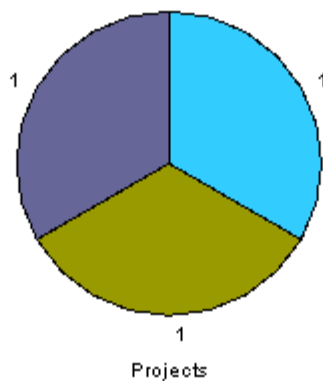


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	0	0	0
13-24	0	1	0	0
25-60	0	0	1	0
MORE THAN 60	0	0	0	1

Graphical Presentation of STEEL Sector

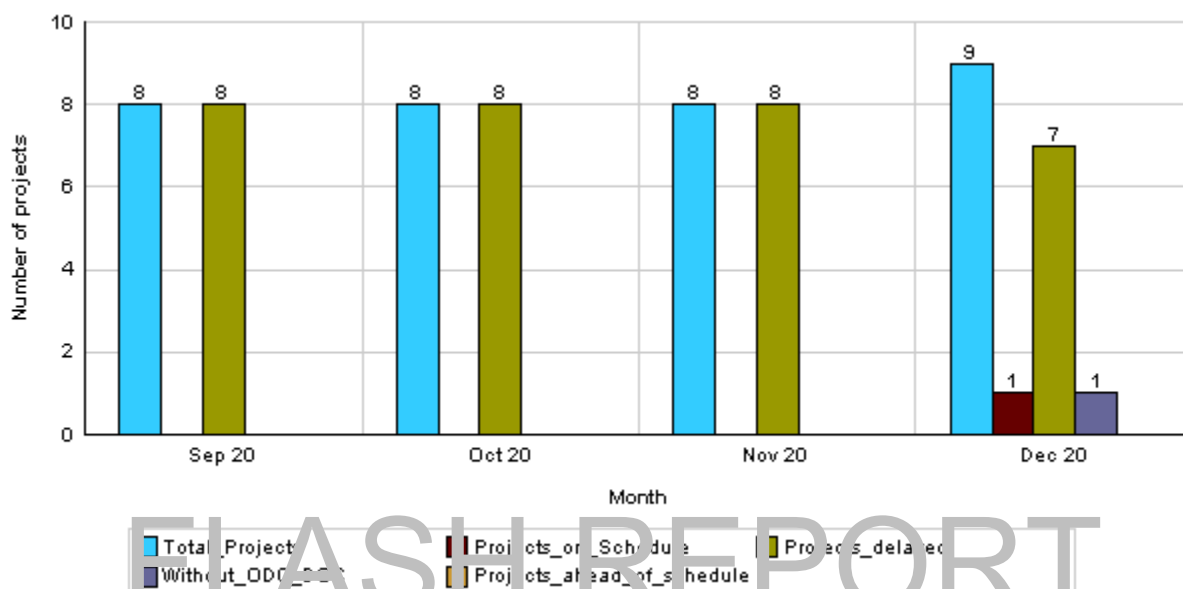


Break-up of 7 Delayed projects in December 2020

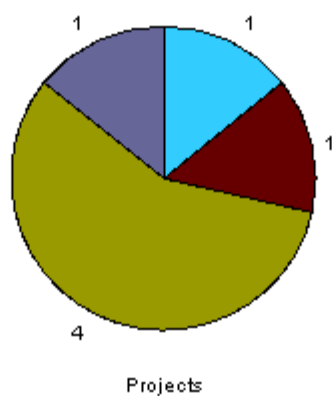

Delay in Months: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of SHIPPING AND PORTS Sector

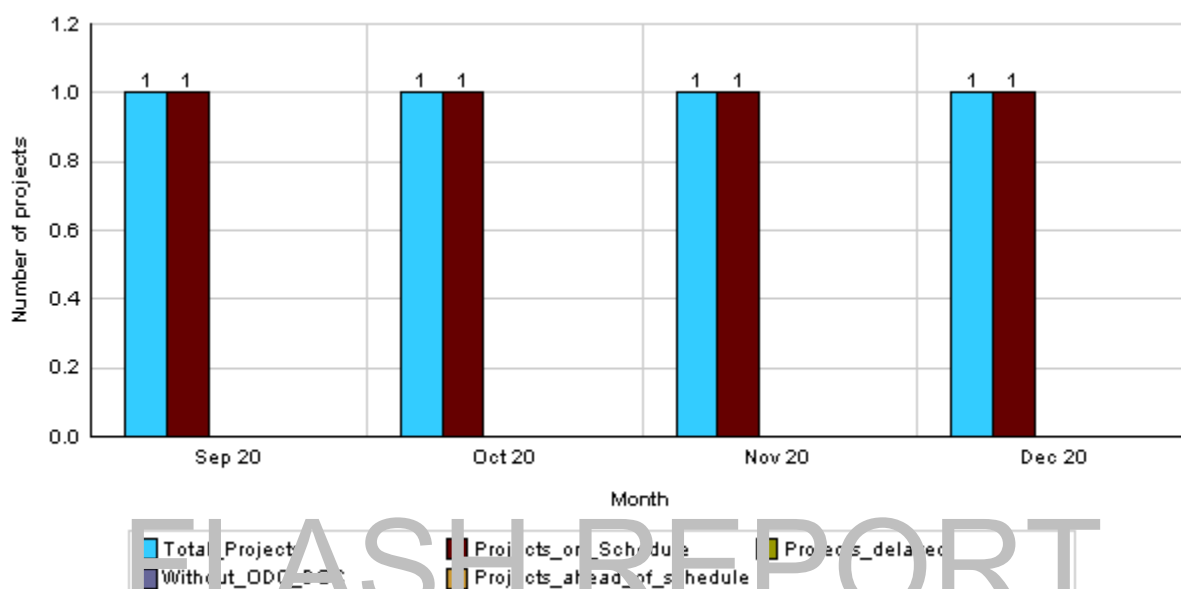


Break-up of 0 Delayed projects in December 2020


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	0	0	0	0

Graphical Presentation of RURAL DEVELOPMENT Sector

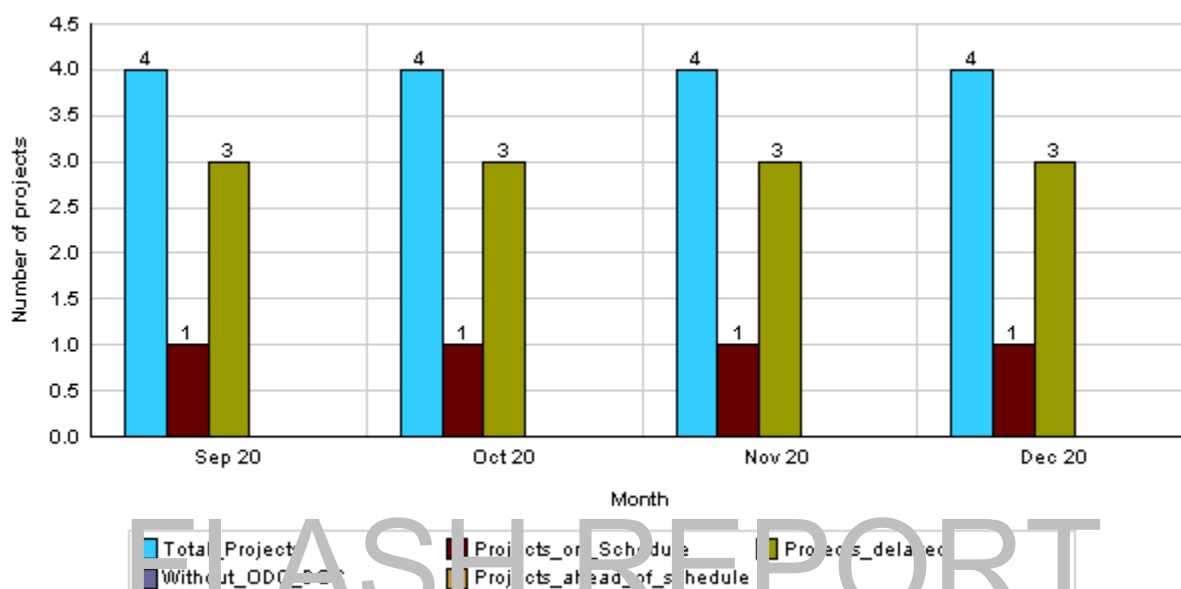


Break-up of 3 Delayed projects in December 2020

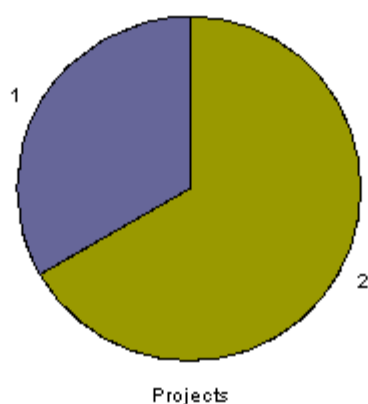


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of MINES Sector

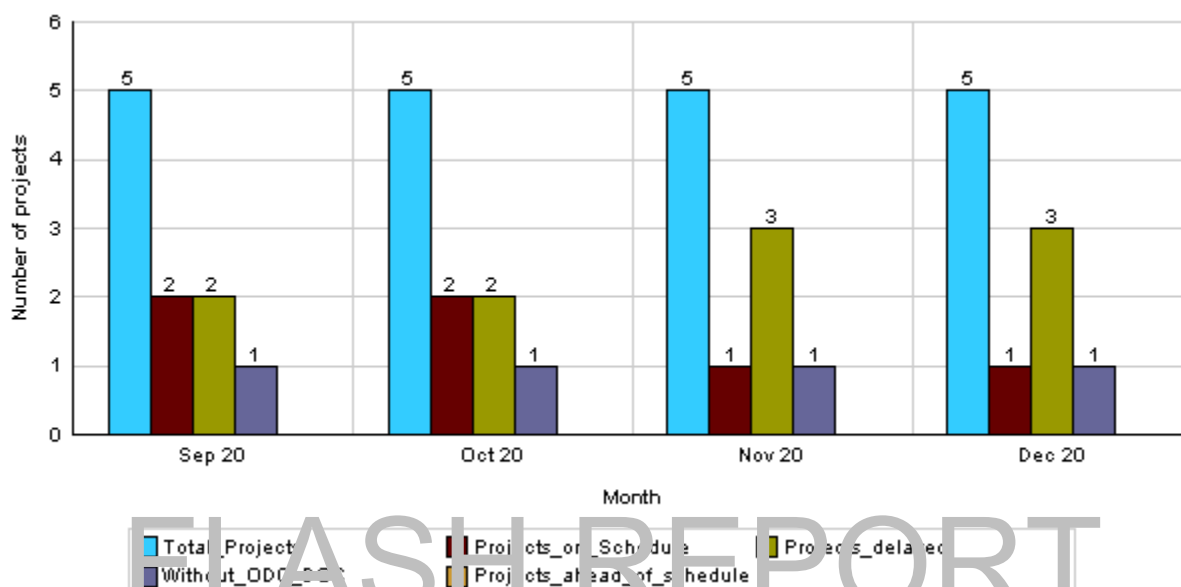


Break-up of 3 Delayed projects in December 2020

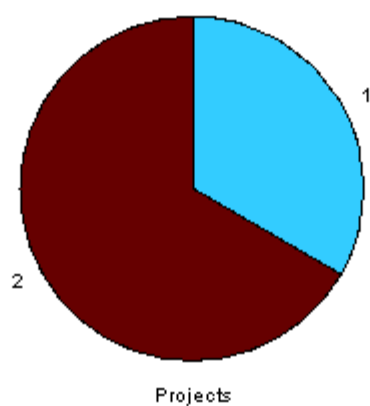


Delay in Months: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of HOME AFFAIRS Sector

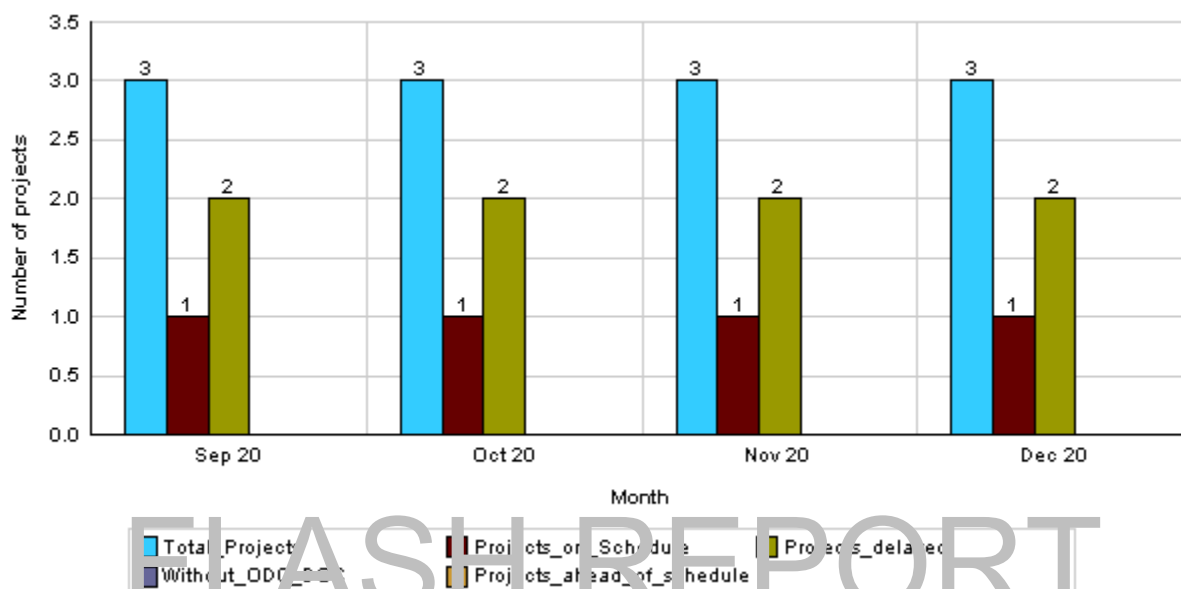


Break-up of 2 Delayed projects in December 2020

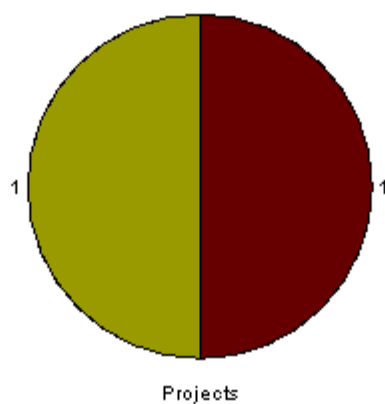


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	1	1	0	0

Graphical Presentation of HEAVY INDUSTRY Sector

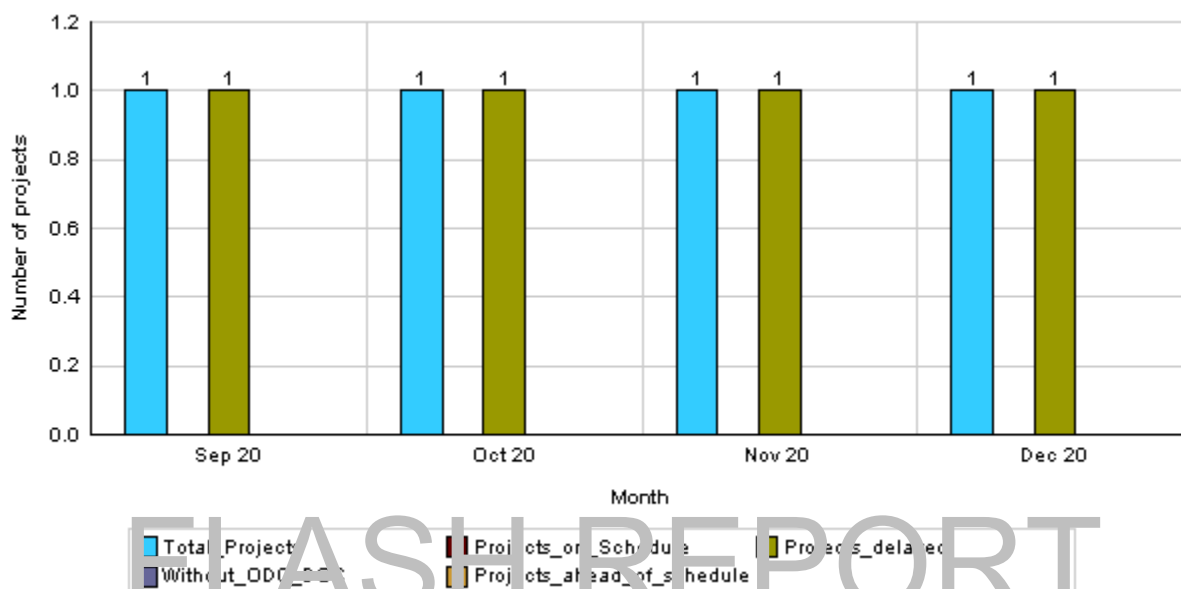


Break-up of 1 Delayed projects in December 2020

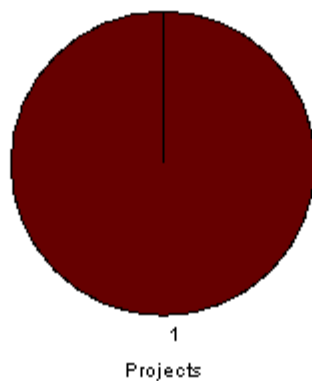

Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

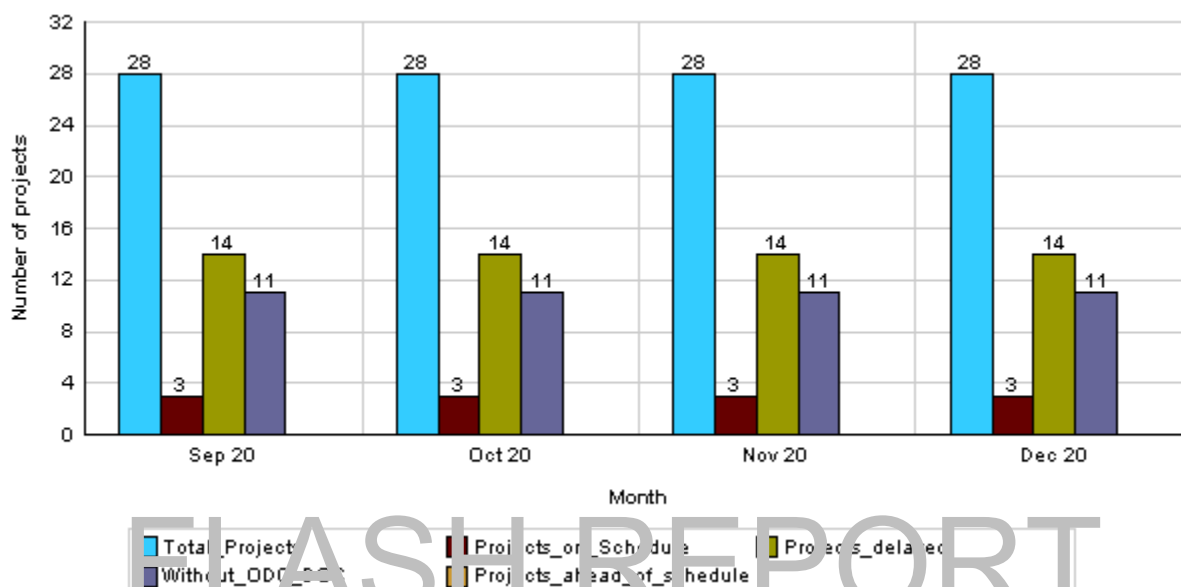


Break-up of 14 Delayed projects in December 2020




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	1	9	3	1

Graphical Presentation of FINANC Sector

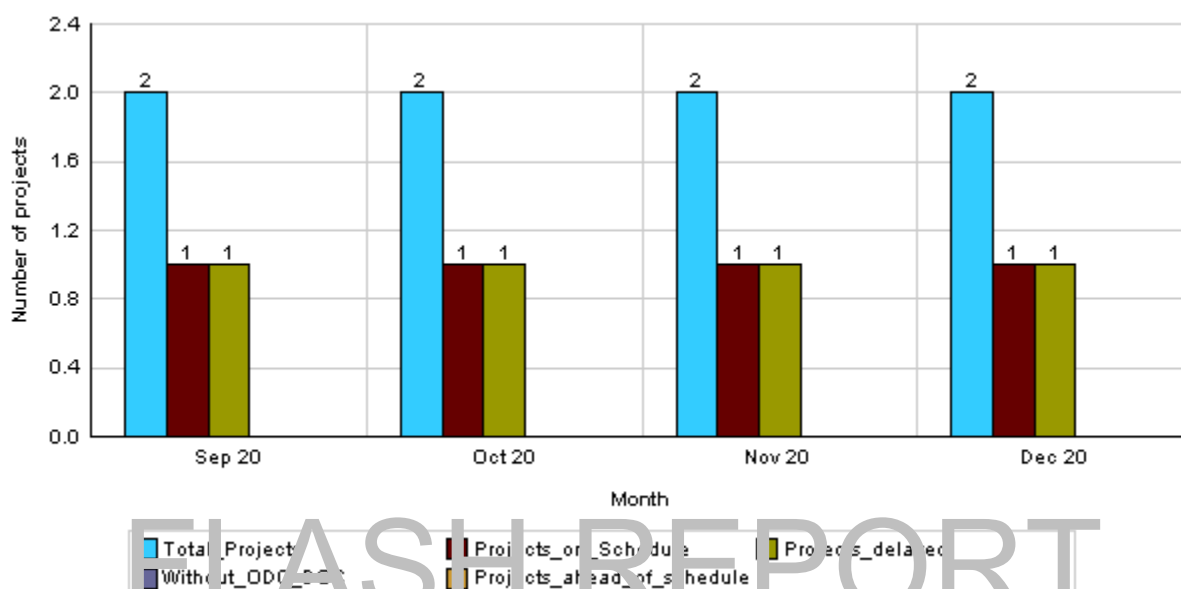


Break-up of 1 Delayed projects in December 2020

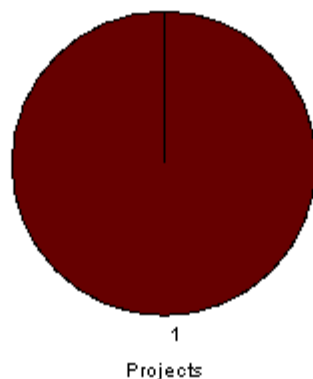


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	0	1	0	0

Graphical Presentation of FERTILISERS Sector

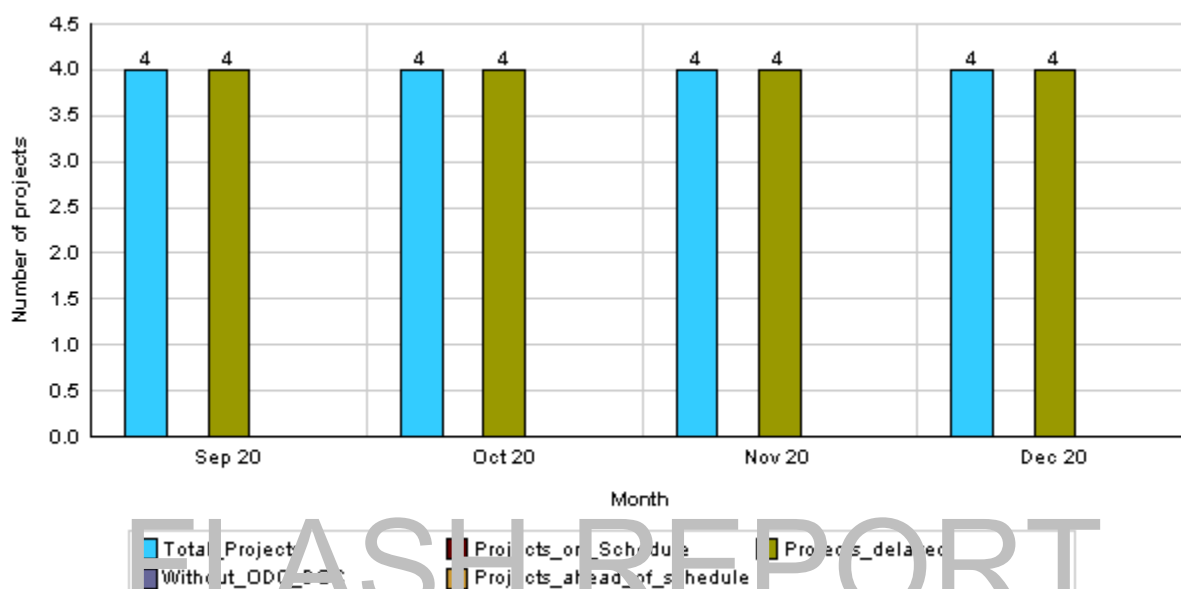


Break-up of 4 Delayed projects in December 2020

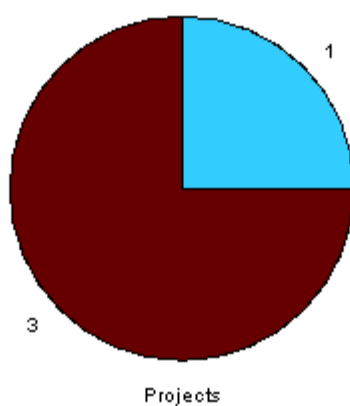


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of DEFENCE PRODUCTION Sector

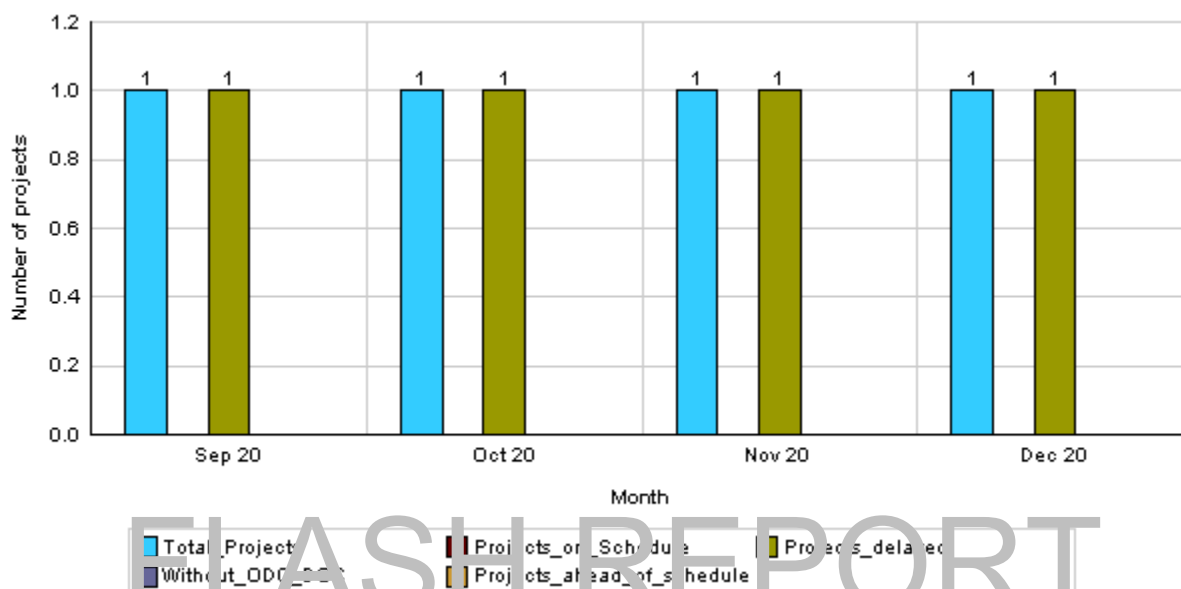


Break-up of 1 Delayed projects in December 2020

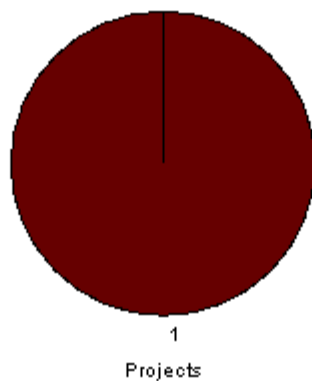

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	0	1	0	0

Graphical Presentation of CULTURE DEVELOPMENT Sector

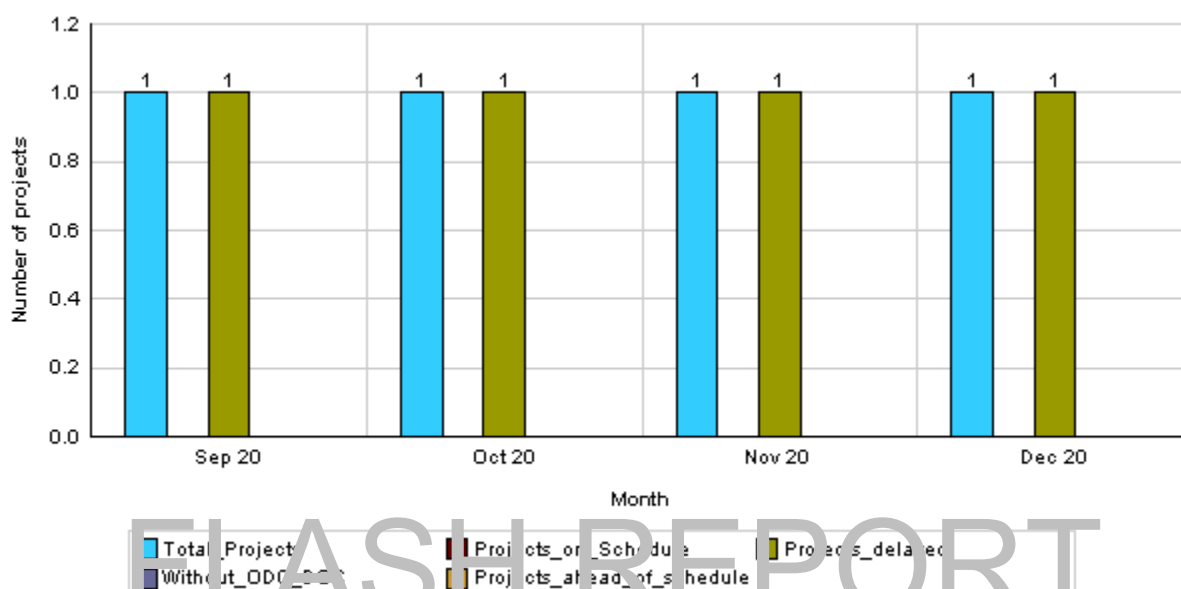


Break-up of 1 Delayed projects in December 2020




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	0	0	1	0

Graphical Presentation of COMMERCE AND INDUSTRY Sector

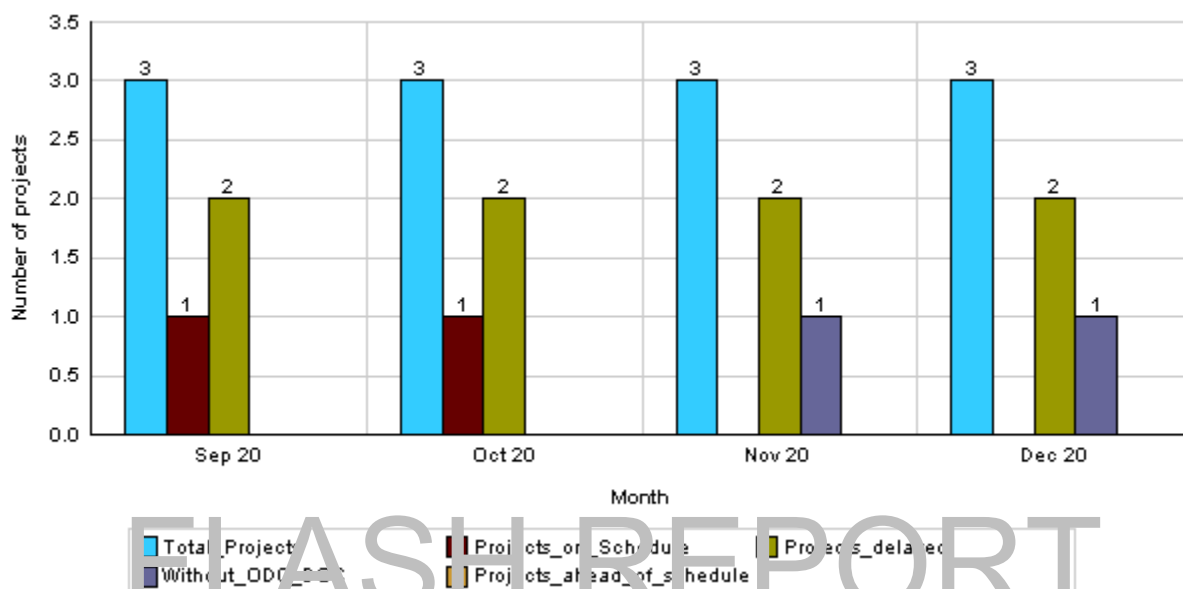


Break-up of 2 Delayed projects in December 2020

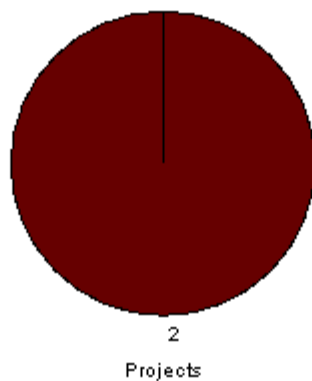


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

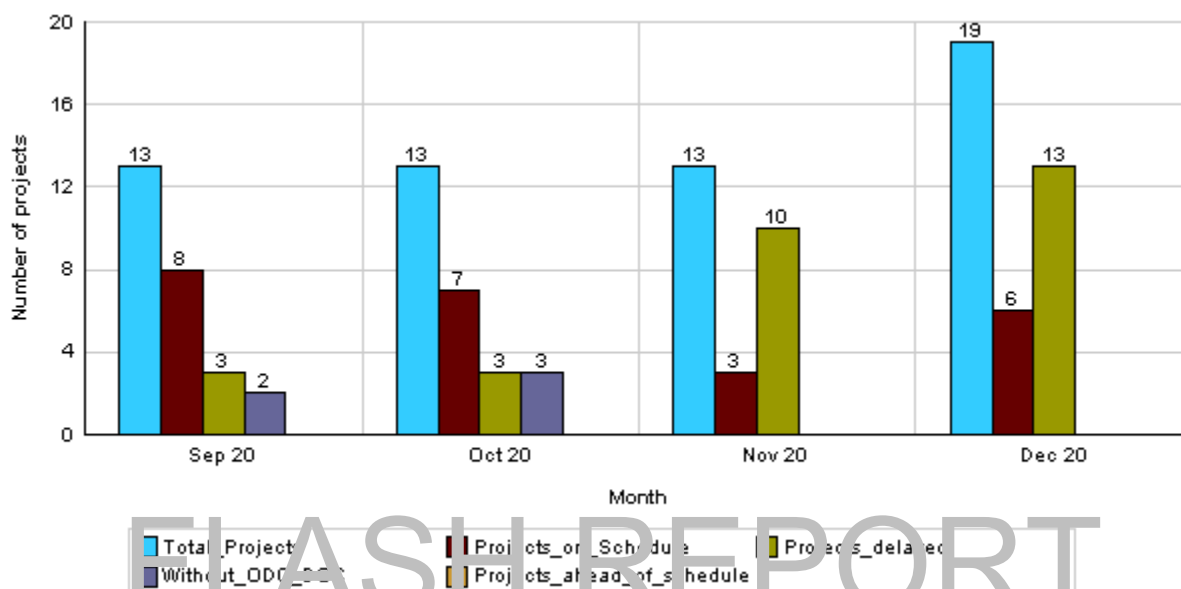


Break-up of 13 Delayed projects in December 2020

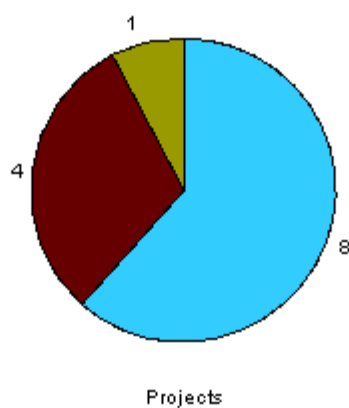


Delay in Months: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

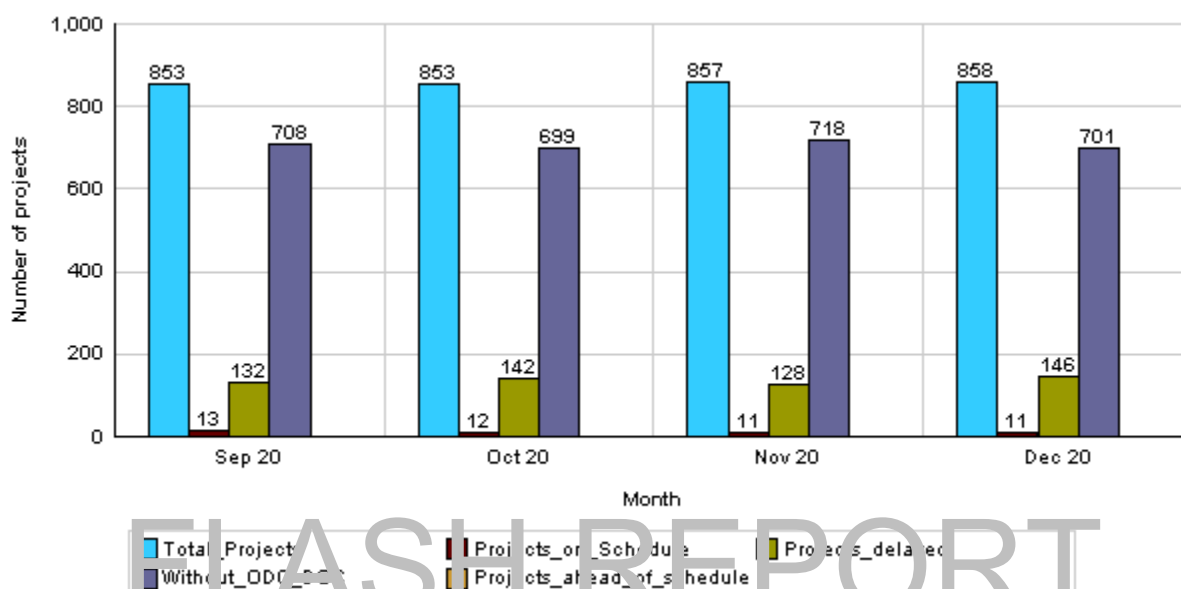


Break-up of 146 Delayed projects in December 2020

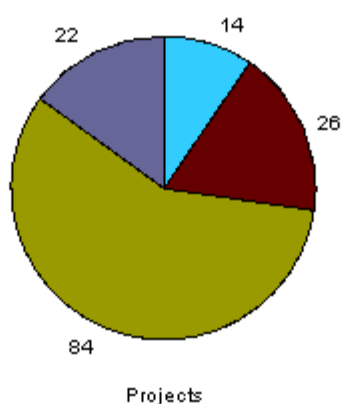


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of RAILWAYS Sector

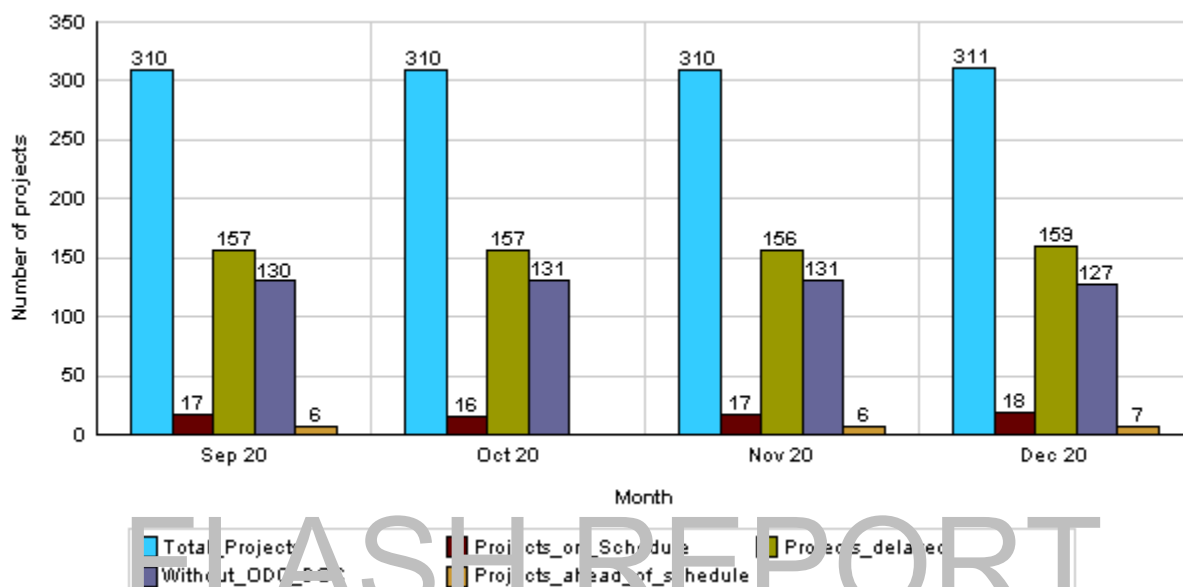


Break-up of 159 Delayed projects in December 2020

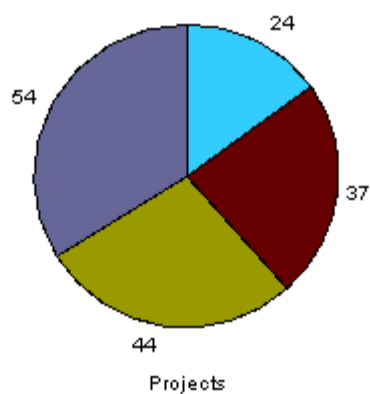


Delay in Months

Legend: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of POWER Sector

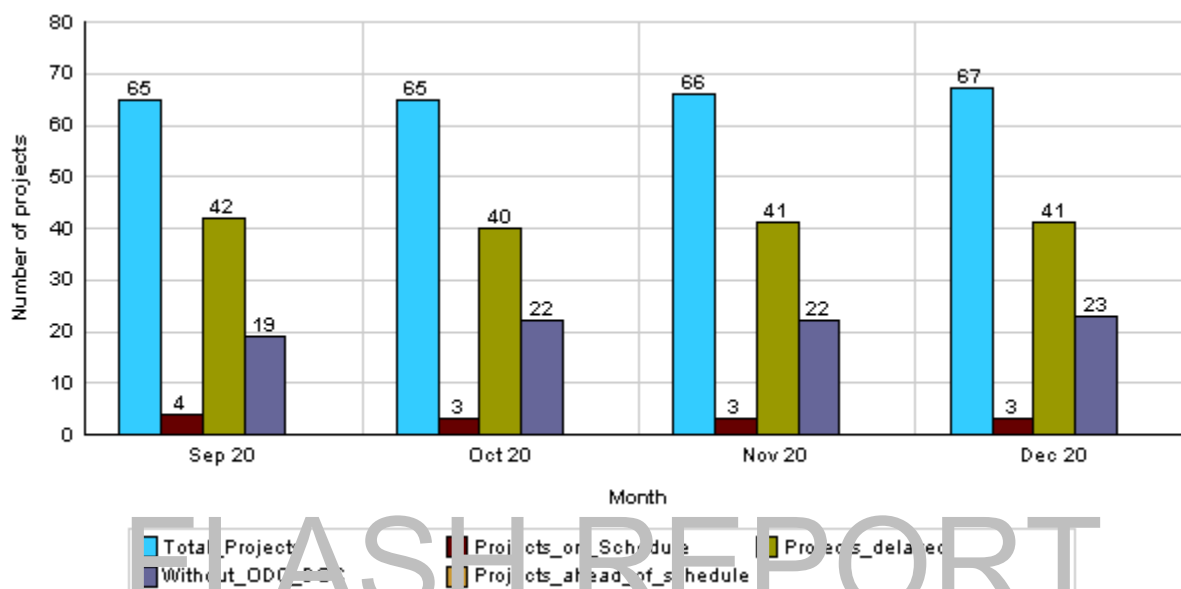


Break-up of 41 Delayed projects in December 2020

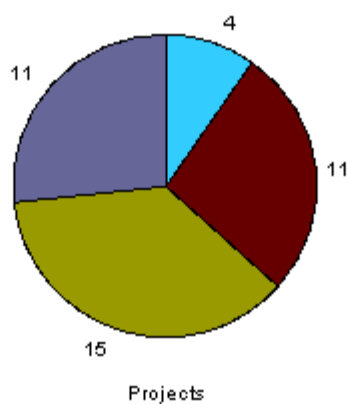


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of PETROLEUM Sector

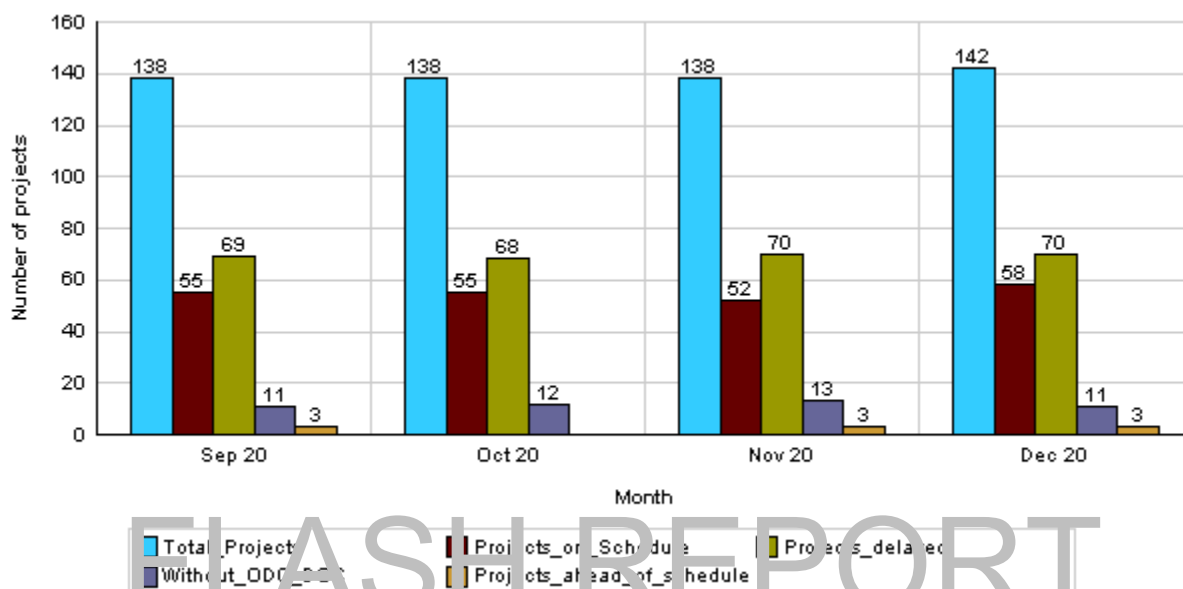


Break-up of 70 Delayed projects in December 2020

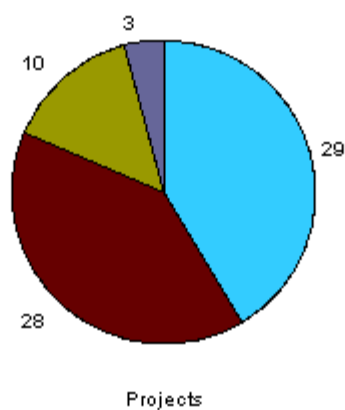


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	29	28	10	3

Graphical Presentation of COAL Sector

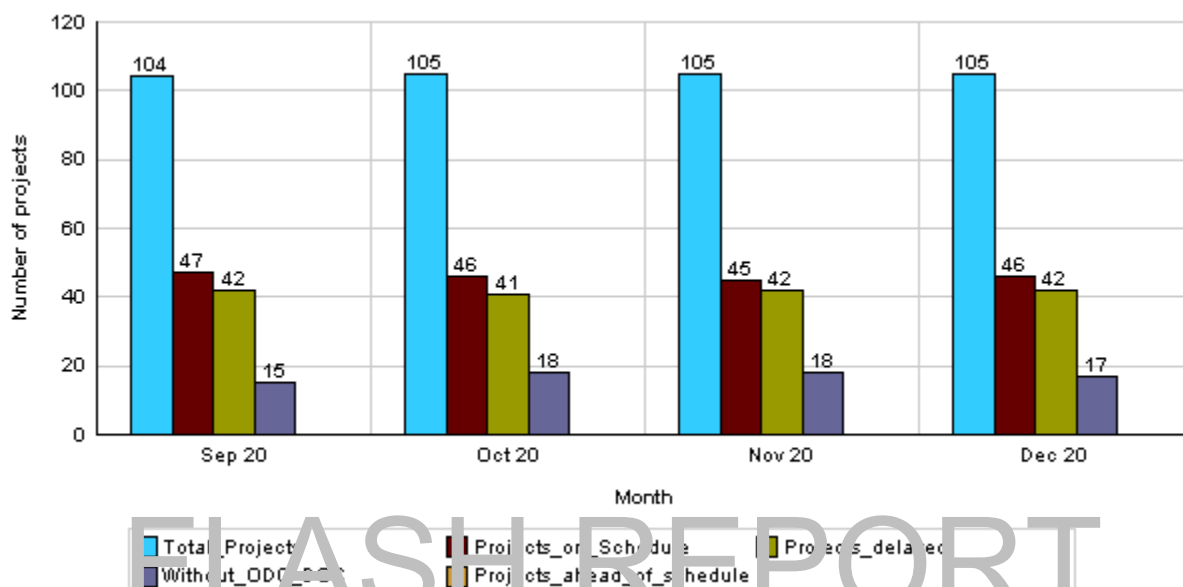


Break-up of 42 Delayed projects in December 2020

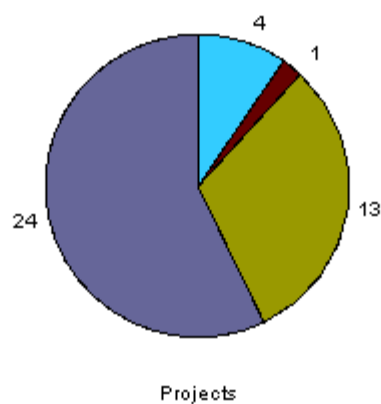


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	4	1	13	24

Graphical Presentation of ATOMIC ENERGY Sector

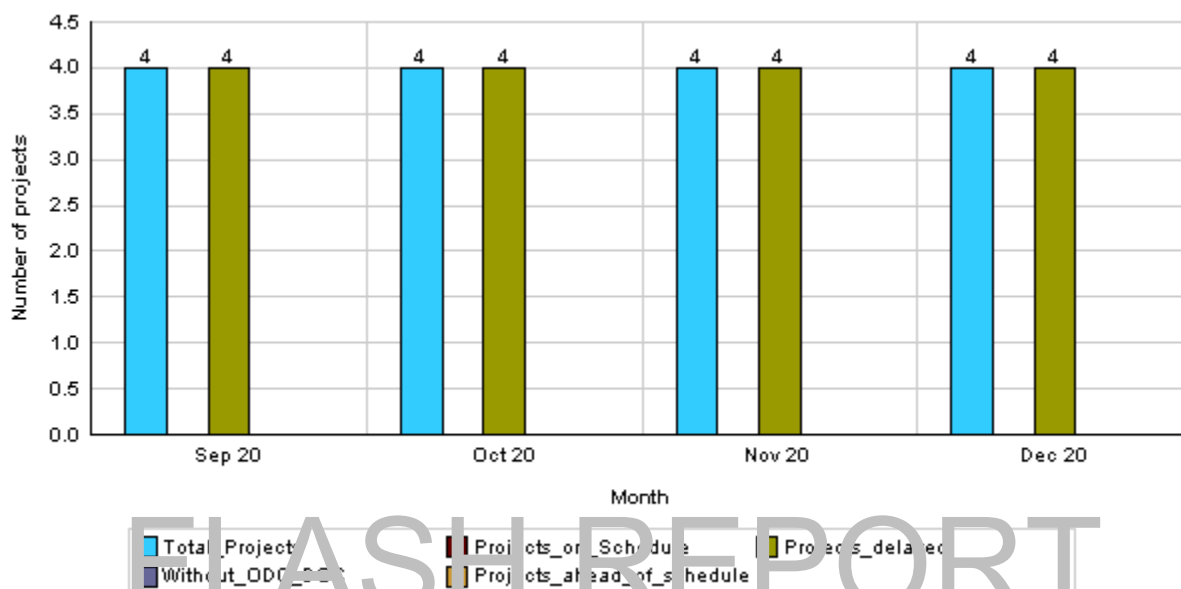

Break-up of 4 Delayed projects in December 2020

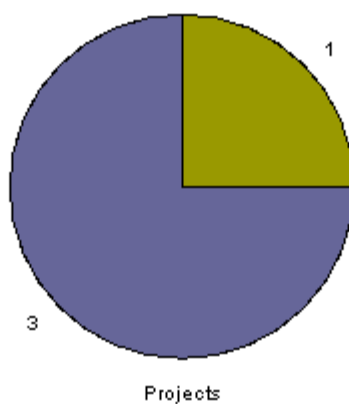

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	0	0	1	3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	16,038.00	12/2015 -	09/2021	69(O) -	57/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	17,079.00	12,799.00	12/2016 -	03/2023	75(O) -	43/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,840.00	5,896.72	09/2010 09/2016	10/2022	145(O) 0	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	22,125.00	11/2020 -	11/2023	36(O) -	28/76
	Total		67,120.00 -	80,348.00	56,858.72				211/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2011	417.23 -	41.33	291.75	09/2011 09/2020	06/2021	33(O) 0	0/0
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10 -	177.10	.00	02/2020 -	06/2021	16(O) -	0/0
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80 -	611.80	.00	03/2023 -	03/2023	0(O) -	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00 1,232.00	1,232.00	323.90	03/2021 -	03/2022	12(O) -	0/0
9	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022	0(O) -	0/0
10	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13(O) -	0/0
11	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00 -	1,405.00	.00	08/2022 -	03/2023	7(O) -	0/0
12	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	346.27 480.33	480.33	51.11	09/2021 -	09/2021	0(O) -	0/0
13	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24 -	412.24	.00	06/2021 -	06/2021	0(O) -	0/0
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39 -	475.39	88.11	04/2021 -	04/2021	0(O) -	0/0
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5(O) -	0/0
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	.00	03/2022 -	03/2023	12(O) -	0/0
18	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	.00	05/2022 -	05/2022	0(O) -	0/0
19	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	438.28 -	438.28	335.58	06/2019 -	12/2020	18(O) -	0/0
20	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	369.66	09/2021 09/2020	09/2022	12(O) 0	0/0
21	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10(O) -	0/0
22	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	105.12	03/2020 06/2021	06/2021	15(O) 0	0/0
23	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2016	389.71 -	389.71	37.25	11/2021 10/2021	10/2021	11(O) 0	0/0
	Total		13,786.34 -	14,034.50	2,597.30				0/0
	<u>COAL</u>								
24	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	3,645.58	03/2023 03/2016	03/2023	0(O) 0	15/21
25	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,446.61	03/2023 -	03/2023	0(O) -	8/22
26	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	7.31	03/2023 -	03/2023	0(O) -	1/12
27	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	180.74	03/2015 03/2020	03/2022	84(O) 0	6/11
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	4.98	03/2014 -	03/2022	96(O) -	2/9
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	208.12	03/2014 -	03/2021	84(O) -	2/6
30	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	182.04	03/2016 -	03/2021	60(O) -	4/8
31	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	129.86	03/2022 -	03/2022	0(O) -	2/11
32	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	82.60	03/2020 -	03/2021	12(O) -	7/9
33	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	49.41	03/2018 -	03/2023	60(O) -	1/7
34	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	123.22	03/2020 -	03/2023	36(O) -	2/6
35	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	8.19	03/2023 -	03/2023	0(O) -	1/11

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	2/6
37	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/2
38	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	18.19	03/2026 -	03/2026	0(O) -	0/2
39	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	2/2
40	MAGADH EXPANSION OC RPR - [N06000015]JCLL,JHARKHAND ,	08/2008	706.40 7,254.37	706.40	638.94	07/2012 03/2025	03/2025	152(O) 0	6/6
41	CHURI BENTI UG (0.81 MTY) - [N06000083]JCLL,JHARKHAND ,	08/2007	163.51 -	163.51	106.63	03/2011 -	03/2022	132(O) -	6/6
42	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCLL,JHARKHAND ,	12/2009	510.85 -	510.85	401.56	03/2016 -	03/2022	72(O) -	6/6
43	KARMA OCP (1.0MTY) - [N06000088]JCLL,JHARKHAND ,	06/2009	162.46 -	162.46	96.86	03/2014 -	03/2022	96(O) -	6/6
44	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	17.76	04/2014 04/2023	04/2023	108(O) 0	4/7
45	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	446.01	04/2015 03/2022	03/2022	83(O) 0	2/6
46	AMRAPALI OC EPR (12MTY) - [N06000103]JCLL,JHARKHAND ,	02/2011	858.11 5,136.15	58.11	24.83	03.02.03.02	03/2024	48(O) 0	7/7
47	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.54	03/2021 -	03/2021	0(O) -	0/2
48	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
49	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	277.38	05/2014 03/2020	02/2021	81(O) 0	0/8
50	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	205.37	04/2014 -	04/2020	-	0/10
51	HURA - C OC (3 MTY) - [N06000143]JCLL,JHARKHAND ,	10/2015	359.69 -	359.69	158.71	03/2022 -	03/2022	0(O) -	4/22
52	CHITRA EAST (RCE) OCP - [N06000169]JCLL,JHARKHAND ,	08/2018	513.98 -	513.98	97.01	03/2024 -	03/2024	0(O) -	0/17
53	NORTH URIMARI EXPANSION OCP - [N06000182]JCLL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	238.77	03/2023 -	03/2024	12(O) -	1/1
54	TETARIAKHAR EXPANSION OCP - [N06000186]JCLL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023	0(O) -	0/0
55	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	31.62	08/2022 -	09/2023	13(O) -	5/11
56	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 334.27	334.27	16.73	04/2018 -	12/2021	44(O) -	0/0
57	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/10
58	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	100.21	03/2021 -	03/2021	0(O) -	3/10
59	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	54.76	03/2021 -	03/2021	0(O) -	4/9
60	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.85	03/2022 -	03/2022	0(O) -	1/9
61	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	29.94	03/2023 -	03/2023	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	120.14	03/2021 -	03/2022	12(O) -	3/6
63	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	20.99	03/2022 -	03/2022	0(O) -	0/0
64	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	524.01	03/2021 -	03/2021	0(O) -	3/9
65	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	144.51	03/2022 -	03/2022	0(O) -	1/9
66	SEMARIA OPENCASST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
67	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
68	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.87	03/2026 -	03/2026	0(O) -	0/7
69	BLOCK-B EXPANSION OPENCASST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	1/7
70	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/0
71	DINESH OCP - [N06000117]WCL, MAHARASHTRA ,	11/2014	611.16 -	611.16	368.56	03/2020 -	03/2020	-	5/8
72	BHANEAGAN OC - [N06000121]WCL, MAHARASHTRA ,	02/2011	187.94 -	109.68	85.03	03/2021 -	03/2021	0(O) -	7/11
73	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	150.65	03/2019 -	-	-	10/13
74	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	131.35	03/2020 -	03/2020	-	7/10
75	AMALGAMATED PAUNI-II OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	245.47	03/2021 -	03/2021	0(O) -	3/6
76	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	277.08	03/2025 -	03/2025	0(O) -	6/13
77	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	104.95	03/2023 -	03/2024	12(O) -	3/10
78	KAMPTTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	313.34	140.64	03/2021 -	03/2024	36(O) -	5/6
79	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	178.62	03/2020 -	03/2020	-	2/6
80	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	243.41	03/2019 -	-	-	4/9
81	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	141.26	03/2019 -	-	-	5/8
82	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	327.13	03/2020 -	03/2020	-	0/0
83	SAONER I UG TO OC PHASE I - [N06000177]WCL,MAHARASHTRA ,	11/2016	162.10 -	162.10	36.94	03/2022 -	03/2022	0(O) -	0/6
84	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	204.15	03/2021 -	03/2021	0(O) -	0/4
85	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	98.99	03/2021 -	03/2021	0(O) -	0/3
86	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	226.05	03/2022 -	03/2022	0(O) -	0/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	35.65	03/2022 -	03/2022	0(O) -	2/12
88	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	260.46	03/2021 -	03/2021	0(O) -	3/6
89	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
90	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	586.86	586.86	03/2017 -	03/2031	168(O) -	11/12
91	GOPAL JI KANIHA OCP MCL - [N06000035]MCL,ODISHA ,	12/2007	457.77 8,416.19	684.32	684.32	03/2013 03/2028	03/2028	180(O) 72	8/10
92	BALRAM EXPANSION OCP - [N06000044]MCL,ODISHA ,	12/2007	172.08 3,504.21	646.01	646.01	03/2010 03/2029	03/2029	228(O) 84	3/5
93	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	362.50	362.50	03/2012 -	03/2021	108(O) -	5/7
94	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	491.85	491.85	03/2013 -	03/2022	108(O) -	6/9
95	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	274.63	03/2019 -	03/2024	60(O) -	3/9
96	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,971.87	03/2026 -	03/2026	0(O) -	7/15
97	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	285.03 -	89.03	11.36	03/2021 -	03/2024	72(O) -	5/7
98	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	494.67	03/2021 -	03/2024	36(O) -	8/10
99	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	173.89	03/2027 -	03/2027	0(O) -	3/12
100	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,217.77	03/2029 -	03/2029	0(O) -	0/9
101	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	815.93	07/2020 -	04/2020	-	18/22
102	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
103	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
104	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	158.25	09/2020 -	-	-	0/0
105	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	173.83	09/2020 -	-	-	0/0
106	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,980.79	7,980.79	7,371.83	12/2015 -	01/2021	61(O) -	34/35
107	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	479.89	06/2015 03/2025	03/2025	117(O) 0	5/7
108	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	144(O) -	36/42
109	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
110	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132(O) -	1/2
111	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	131.52	03/2015 -	03/2022	84(O) -	3/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	279.54	03/2015 -	03/2022	84(O) -	7/29
113	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2022	84(O) -	10/13
114	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	122.55	07/2016 -	03/2022	68(O) -	26/28
115	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	189.91	03/2016 -	03/2021	60(O) -	38/39
116	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	106.15	03/2019 -	03/2022	36(O) -	17/18
117	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	169.90	03/2019 03/2022	03/2022	36(O) 0	4/11
118	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	- 04/2017	03/2022	- 12	1/6
119	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	10,724.93	11/2021 -	11/2021	0(O) -	9/48
120	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	386.19	03/2022 -	03/2022	0(O) -	9/13
121	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	02/2012	1,055.05 -	1,055.05	632.85	03/2012 -	03/2021	36(O) -	12/16
122	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2000	2,661.73 -	5,464.48	510.17	08/2001 -	-	-	0/19
123	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.43	03/2026 -	03/2026	0(O) -	4/22
124	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	.87	03/2029 -	03/2029	0(O) -	1/22
125	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.40	03/2027 -	03/2027	0(O) -	0/27
126	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.00	03/2027 -	03/2027	0(O) -	0/22
127	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	.00	03/2025 -	03/2025	0(O) -	0/0
128	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 341.22	341.22	23.04	03/2017 -	10/2021	55(O) -	0/0
	Total		1,12,965.37 -	1,18,879.80	45,071.37				489/1090
	<u>FINANC</u>								
129	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	208.96	195.23	10/2019 -	04/2021	18(O) -	1/6
130	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	83.71	11/2021 -	11/2021	0(O) -	2/8
	Total		557.77 -	557.73	278.94				3/14
	<u>FERTILISERS</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	164.03	11/2019 -	03/2021	16(O) -	0/2
132	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	303.87	04/2020 03/2021	03/2021	11(O) 0	7/14
133	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	171.68	11/2019 -	02/2021	15(O) -	0/2
134	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	182.53	11/2019 -	03/2021	16(O) -	0/2
	Total		1,101.28 -	1,101.28	822.11				7/20
	<u>MINES</u>								
135	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	5,540.00	614.13	04/2021 12/2022	12/2022	20(O) 0	4/4
136	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	534.00	330.50	01/2020 -	-	-	1/3
137	CONVERSION OF FLAT BOTTOM SADDLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND 2 - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2016	355.00 -	55.00	97.16	11/2020 -	02/2021	3(O) -	2/3
138	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.74	04/2021 04/2021	04/2021	0(O) 0	2/2
139	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 06/2021	12/2020	18(O) 0	1/1
	Total		7,078.62 -	7,075.17	1,173.53				10/13
	<u>STEEL</u>								
140	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,558.00	1,762.09	12/2017 12/2020	12/2020	36(O) 0	5/6
141	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 336.00	336.00	278.28	08/2018 11/2020	11/2020	-	3/4
142	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 21,940.00	21,940.00	17,436.86	05/2015 07/2021	07/2021	74(O) 0	70/86
143	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	511.79	10/2017 12/2021	12/2021	50(O) 0	0/2
144	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	1,026.52	12/2017 10/2020	02/2021	38(O) 1	2/2
145	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	170.16	06/2019 05/2021	05/2021	23(O) 0	1/1
146	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	.38	05/2023 -	05/2023	0(O) -	0/0
147	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,511.30	09/2018 02/2021	02/2021	29(O) 2	5/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
148	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL ,	12/2018	263.36 -	263.36	159.19	09/2020 03/2021	05/2021	8(O) 2	1/4
	Total		23,478.11 -	29,608.45	22,856.57				87/110
	<u>PETROLEUM</u>								
149	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	13,324.42	07/2020 07/2022	07/2022	24(O) 0	92/111
150	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC, ANDHRA PRADESH ,	03/2016	34,012.00 -	25,090.00	9,799.00	06/2020 08/2021	08/2021	14(O) 0	15/20
151	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
152	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
153	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL, ANDHRA PRADESH ,	08/2017	384.58 -	384.58	248.45	04/2021 03/2021	03/2021	-1(O) 0	0/0
154	CONSTRUCTION OF GRA S ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH ,	08/2017	466.00 -	66.00	109.74	04/2021 07/2022	07/2022	3(O) -	0/0
155	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL, ANDHRA PRADESH ,	04/2018	355.00 -	355.00	82.31	04/2022 -	02/2023	10(O) -	0/0
156	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL, ANDHRA PRADESH ,	10/2018	316.20 -	316.20	53.36	10/2021 -	10/2021	0(O) -	0/0
157	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH ,	07/2017	580.20 -	580.20	90.13	02/2021 -	02/2021	0(O) -	0/16
158	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL, ANDHRA PRADESH ,	09/2019	196.26 -	196.26	84.06	07/2020 -	07/2021	12(O) -	1/5
159	LPG BP PROJECT CHITTOOR - [N16000381]IOCL, ANDHRA PRADESH ,	07/2019	167.00 -	167.00	8.10	07/2022 -	07/2022	0(O) -	0/0
160	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL, ASSAM ,	06/2016	423.00 -	502.00	399.01	08/2019 06/2021	06/2021	22(O) 0	6/13
161	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC, ASSAM ,	07/2016	249.85 303.75	303.75	170.85	05/2020 05/2021	05/2021	12(O) 0	4/5
162	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	-	-	0/0
163	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL, ASSAM ,	01/2018	543.91 638.60	652.10	130.10	02/2020 -	04/2021	14(O) -	1/14
164	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL, ASSAM ,	08/2018	557.00 -	557.00	467.19	02/2020 06/2021	06/2021	16(O) 0	5/5
165	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL, ASSAM ,	06/2016	224.75 -	222.21	148.44	08/2020 -	03/2021	7(O) -	0/0
166	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY - [N16000379]NRL, ASSAM ,	01/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
167	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024	0(O) -	0/0
168	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	109.56	03/2021 -	09/2021	6(O) -	18/26
169	DEVLOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	20.38	10/2020 02/2022	02/2022	16(O) 0	2/2
170	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	128.57	10/2022 -	10/2022	0(O) -	10/10
171	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	114.02	01/2021 06/2021	06/2021	5(O) 0	6/8
172	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	278.28	03/2021 12/2021	12/2021	9(O) 3	0/0
173	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR ,	06/2017	951.64 -	951.64	678.12	10/2019 11/2020	11/2020	-	9/11
174	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	632.61	04/2023 -	04/2023	0(O) -	1/2
175	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR ,	06/2020	403.00 -	403.00	.00	08/2022 -	08/2022	0(O) -	0/0
176	CAPACITY AUGMENTATION JAMNAGAR LON PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2017	327.78 -	00.00	86.50	04/2017 03/2021	03/2021	35(O) -	18/20
177	REDEVELOPMENT OF SANTHAL FIELDS [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	578.85	621.22	03/2021 -	03/2021	0(O) -	7/10
178	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,	08/2017	1,342.00 -	1,342.00	6.30	08/2020 -	-	-	1/1
179	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	234.25	02/2020 10/2021	10/2021	20(O) 0	7/8
180	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 730.20	730.20	48.20	- 05/2023	05/2023	- 0	11/17
181	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	225.54	38.70	02/2021 -	12/2021	10(O) -	5/8
182	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	52.81	12/2021 -	12/2021	0(O) -	8/11
183	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	48.16	05/2023 -	05/2023	0(O) -	3/11
184	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	.00	12/2022 -	12/2022	0(O) -	0/0
185	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 300.00	300.00	247.49	11/2020 06/2021	06/2021	7(O) 0	39/46
186	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	64.15	02/2020 08/2021	08/2021	18(O) 0	5/7
187	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	552.56	08/2020 -	04/2022	20(O) -	6/7
188	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	141.32	01/2021 03/2022	03/2022	14(O) 7	2/6

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	172.31	02/2020 02/2022	02/2022	24(O) 0	4/5
190	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.01	327.01	143.50	08/2020 05/2021	05/2021	9(O) 0	13/16
191	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	9.50	06/2021 07/2022	07/2022	13(O) 0	1/3
192	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 -	2,281.94	425.50	12/2022 -	12/2022	0(O) -	0/0
193	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	129.59	10/2021 -	10/2021	0(O) -	0/0
194	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	2.06	07/2021 -	07/2021	0(O) -	0/0
195	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	86.19	09/2026 -	09/2026	0(O) -	0/0
196	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	611.60	03/2023 03/2022	03/2022	-12(O) 0	6/10
197	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	54.07	06/2020 09/2021	09/2021	15(O) 0	3/12
198	CITY GAS DISTRIBUTION CGD NETWORK JAMSHEDI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	26.45	9.90	10/2021 -	10/2021	0(O) -	19/19
199	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	60.14	06/2022 -	06/2022	0(O) -	0/0
200	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	73.85	10/2022 -	10/2022	0(O) -	9/9
201	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
202	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	606.89	02/2020 -	-	-	0/0
203	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,501.84	12/2019 04/2021	07/2021	19(O) 4	9/10
204	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 637.00	637.00	390.06	03/2020 11/2020	06/2021	15(O) 3	2/3
205	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	79.52	03/2021 -	03/2021	0(O) -	0/15
206	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	669.37	06/2022 -	06/2022	0(O) -	10/18
207	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	121.57	12/2022 -	12/2022	0(O) -	9/19
208	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	177.00	11/2021 -	11/2021	0(O) -	10/19
209	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 -	200.00	.00	06/2023 -	06/2023	0(O) -	0/0
210	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 714.25	714.25	374.14	10/2017 02/2022	03/2022	53(O) 0	40/52
211	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 -	5,245.96	4,808.25	08/2018 11/2019	01/2021	29(O) 0	0/20

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
212	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 -	3,288.96	2,614.93	02/2020 02/2021	02/2021	12(O) 0	0/20
213	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	695.00	06/2019 -	02/2022	32(O) -	0/0
214	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	276.12	03/2023 -	03/2023	0(O) -	0/0
215	PROVISION OF 2ND SPUR FOR TWL GANTRY TWO FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 293.00	293.00	138.42	06/2020 09/2021	09/2021	15(O) 0	0/0
216	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,846.46	1,846.46	1,518.24	05/2013 12/2020	03/2021	94(O) 0	5/8
217	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,572.08	04/2018 05/2021	05/2021	37(O) 0	13/15
218	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,045.00	1,437.61	08/2021 -	02/2022	6(O) -	5/5
219	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2011	445.58 -	49.58	34.23	12/2011 02/2021	02/2021	14(O) 0	0/17
220	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	122.92	01/2021 -	04/2021	3(O) -	0/0
221	ADDITIONAL FACILITIES AT SOLAPUR FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	111.62	01/2021 -	10/2021	9(O) -	0/0
222	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	131.10	01/2021 -	04/2021	3(O) -	0/0
223	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	4,183.90	03/2020 -	-	-	114/135
224	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,475.92	3,596.00	3,442.73	05/2021 05/2021	05/2021	0(O) 0	14/15
225	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	238.43	08/2020 -	01/2021	5(O) -	0/15
226	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	110.52	06/2020 12/2021	09/2021	15(O) 0	2/12
227	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,203.71	1,303.59	05/2021 -	05/2021	0(O) -	4/6
228	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	922.04	03/2022 05/2023	05/2023	14(O) 14	4/6
229	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	1,941.83	05/2021 -	05/2021	0(O) -	4/6

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
230	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	06/2019	2,494.68 -	2,354.72	1,096.58	03/2022 -	03/2022	0(O) -	4/6
231	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	733.86	584.33	12/2020 05/2021	05/2021	5(O) 2	4/5
232	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA ,	07/2020	640.00 -	640.00	278.71	12/2021 -	12/2021	0(O) -	0/0
233	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	490.24	445.41	03/2017 -	03/2021	48(O) -	2/15
234	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	3,027.90	1,685.17	12/2020 -	08/2021	8(O) -	5/5
235	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	3,338.00	2,724.32	12/2020 -	03/2021	3(O) -	5/5
236	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	494.64	07/2018 02/2021	02/2021	31(O) 0	25/36
237	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,689.00	1,694.25	06/2020 -	10/2020	-	24/24
238	PIPELINE REHABILITATION PROJECT OF 571 KM. (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	300.00	17.37	10/2020 -	03/2021	5(O) -	6/12
239	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	450.70	12/2019 -	04/2021	16(O) -	6/22
240	LAYING OF VIJAIPIUR-AURAIYA PIPELINE SECTION OF VIJAIPIUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,542.50	12/2020 -	03/2021	3(O) -	21/24
241	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	1,925.10	12/2020 12/2021	06/2021	6(O) 0	20/24
242	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 3,048.00	3,048.00	1,659.30	12/2020 12/2021	12/2021	12(O) 0	19/24
243	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,470.70	12/2012 02/2022	02/2022	110(O) 0	26/42
244	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 3,072.00	3,072.00	1,825.04	06/2021 08/2022	08/2022	14(O) 14	18/26
245	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 3,060.00	3,060.00	1,998.30	12/2021 -	12/2021	0(O) -	15/20
246	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	71.11	11/2022 -	11/2022	0(O) -	8/20
247	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	113.30	07/2022 -	07/2022	0(O) -	6/14
248	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	2.70	11/2022 -	11/2022	0(O) -	5/12
249	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	397.60	05/2023 -	05/2023	0(O) -	0/0
250	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,174.60	12/2020 12/2021	12/2021	12(O) 0	18/24

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
251	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	45.32	12/2019 03/2022	03/2022	27(O) 0	18/26
252	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	84.25	07/2022 -	07/2022	0(O) -	10/10
253	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	180.63	12/2021 -	12/2021	0(O) -	3/3
254	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	68.12	07/2022 -	07/2022	0(O) -	9/9
255	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	2,259.24	10/2021 -	10/2021	0(O) -	5/10
256	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00 -	750.00	34.73	12/2020 -	12/2020	0(O) -	0/14
257	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	541.64	10/2021 -	10/2021	0(O) -	1/1
258	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	2.38	09/2021 -	09/2021	0(O) -	1/5
259	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	1,432.60	08/2021 -	08/2021	0(O) -	7/11
260	INSTALLATION OF STANDBY CPU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	1.80	09/2022 -	09/2022	0(O) -	0/8
261	2ND GENERATION LIGNOCELLULOSE BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	09/2019	1,607.00 -	1,607.00	168.70	03/2022 -	03/2022	0(O) -	0/21
262	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	.22	07/2022 -	07/2022	0(O) -	0/0
263	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	72.66	01/2024 -	01/2024	0(O) -	0/0
264	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL,PUNJAB ,	05/2020	1,421.46 -	1,421.46	33.86	02/2023 -	02/2023	0(O) -	0/0
265	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	79.45	- 05/2022	05/2022	- 0	16/26
266	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
267	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 1,472.00	1,472.00	16.38	02/2017 08/2022	08/2022	66(O) 0	0/0
268	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	624.35	445.60	03/2019 05/2021	05/2021	26(O) 0	4/5
269	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	6,025.00	3,275.27	12/2018 -	08/2021	32(O) -	5/5
270	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	110.61	06/2020 -	11/2021	17(O) -	5/5
271	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,498.79	12/2019 -	01/2021	13(O) -	0/0
272	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	300.00	238.43	08/2020 -	09/2021	13(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
273	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	160.41	10/2020 -	08/2021	10(O) -	0/0
274	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL,TAMIL NADU ,	10/2020	921.00 -	921.00	2.86	09/2023 -	09/2023	0(O) -	0/0
275	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	53.13	04/2022 -	08/2023	16(O) -	0/0
276	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	345.15	183.93	04/2022 -	04/2022	0(O) -	43/43
277	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	124.52	08/2021 -	11/2021	3(O) -	0/0
278	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	16.36	08/2020 11/2021	11/2021	15(O) 0	1/1
279	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000223]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	375.67	12/2021 -	08/2022	8(O) -	3/3
280	MULTI PRODUCT PIPELINE FROM INA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,24.06	57.32	12/2021 -	12/2021	0(O) -	0/21
281	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	135.22	03/2029 -	03/2029	0(O) -	0/0
282	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 -	217.92	72.40	04/2021 -	04/2021	0(O) -	0/14
283	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	78.12	02/2020 06/2021	06/2021	16(O) 0	19/26
284	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 -	1,097.54	971.84	10/2018 02/2020	07/2020	-	0/15
285	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
286	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	775.10	12/2020 12/2021	12/2021	12(O) 0	13/24
287	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	80.39	04/2020 10/2021	10/2021	18(O) 0	18/26
288	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	1,780.96	09/2022 -	03/2022	-6(O) -	3/3
289	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	13.79	03/2031 -	03/2031	0(O) -	0/0
290	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	53.20	01/2023 -	01/2023	0(O) -	0/0
	Total		2,82,358.27 -	2,90,123.35	1,03,816.81				1003/1585
	POWER								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
291	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	12,855.18	09/2010 08/2023	08/2023	155(O) 0	0/0
292	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	8,151.00	12/2009 01/2021	01/2021	133(O) 1	30/30
293	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	18,168.42	10/2011 04/2022	04/2022	126(O) 0	31/48
294	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 7,998.00	9,583.00	8,648.28	07/2012 06/2020	03/2021	104(O) 1	13/25
295	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	15,331.70	05/2018 06/2021	07/2021	38(O) 1	39/45
296	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	1,221.50	01/2024 -	01/2024	0(O) -	16/27
297	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	-	41/41
298	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	2,220.16	11/2019 -	-	-	0/0
299	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	508.31	05/2017 07/2020	06/2021	49(O) 0	4/9
300	CONSTRUCTION OF ATAL BIHARI VAJPAHEY URJA BHAVAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.00 -	271.00	172.90	11/2019 -	03/2021	16(O) -	0/0
301	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	09/2017	175.64 -	175.64	120.70	09/2019 06/2020	09/2020	-	0/0
302	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	116.91	06/2019 06/2020	09/2020	-	0/0
303	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	8,705.10	09/2009 03/2022	03/2022	150(O) 0	3/5
304	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	282.43	01/2026 -	01/2026	0(O) -	0/0
305	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,598.96	04/2020 -	07/2025	63(O) -	0/0
306	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,389.42	11,269.68	06/2019 10/2022	10/2022	40(O) 0	27/30
307	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,312.62	10/2017 -	-	-	0/0
308	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	18,668.00	3,644.04	03/2023 -	09/2024	18(O) -	2/6
309	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	443.28	02/2019 05/2020	01/2021	23(O) 0	0/0
310	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 15,105.22	15,105.22	13,473.99	01/2018 10/2020	02/2021	37(O) 1	41/43
311	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	-	41/41
312	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	454.82	09/2020 -	08/2022	23(O) -	9/16
313	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
314	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
315	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,623.08	10/2012 06/2020	01/2021	99(O) 0	8/11
316	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,864.61	08/2013 03/2022	03/2022	103(O) 0	23/26
317	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	590.30	06/2014 -	-	-	10/12
318	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,315.85	04/2016 04/2020	07/2020	-	12/12
319	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	238.32	04/2016 12/2017	03/2021	59(O) 3	0/0
320	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	477.58	11/2016 06/2020	02/2021	51(O) 1	10/12
321	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	3,269.93	03/2018 -	-	-	9/12
322	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (SP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	640.30	10/2017 12/2020	01/2021	39(O) 1	2/5
323	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	60.03	200.66	07/2015 -	-	-	3/5
324	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	89.15	03/2018 -	03/2021	36(O) -	0/0
325	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	627.32	01/2018 05/2020	03/2021	38(O) 0	0/0
326	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	-	-	0/0
327	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	11,217.10	11/2019 05/2020	03/2021	16(O) 0	0/0
328	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	196.10	11/2019 -	-	-	0/0
329	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 482.64	482.64	412.53	01/2019 04/2020	04/2020	-	0/0
330	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	425.04	04/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
331	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	195.52	02/2019 04/2020	03/2021	25(O) 0	0/0
332	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	146.71	06/2019 09/2020	03/2021	21(O) 1	0/0
333	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	210.09	12/2019 06/2020	03/2021	15(O) 0	0/0
334	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	3,989.71	04/2020 -	02/2021	10(O) -	0/0
335	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,151.56	1,893.34	12/2018 -	12/2021	36(O) -	0/0
336	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,700.00	2,430.27	12/2018 -	12/2021	36(O) -	0/0
337	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00	3,654.00	3,508.04	04/2019 -	-	-	0/0
338	EASTERN REGION STRENGTHENING SCHEME XXII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,000.00	2,721.70	07/2020 -	02/2021	7(O) -	0/0
339	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,564.64	02/2020 09/2020	03/2021	13(O) 0	0/0
340	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	140.67	09/2019 04/2020	05/2020	-	0/0
341	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	234.30	05/2020 -	02/2021	9(O) -	0/0
342	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	11,441.91	12/2018 02/2021	03/2021	27(O) 0	38/41
343	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	1,486.29	12/2018 -	-	-	0/0
344	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 219.66	219.66	156.28	07/2019 06/2020	03/2021	20(O) 0	0/0
345	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	7,998.74	11/2020 03/2022	03/2022	16(O) 0	25/28
346	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	10,016.10	7,888.03	07/2019 03/2021	03/2021	20(O) 0	38/40
347	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	11,044.00	02/2017 06/2020	01/2021	47(O) 1	39/40
348	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	1,297.85	09/2023 -	08/2024	11(O) -	0/11
349	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	250.00	09/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
350	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	125.00	11/2020 -	-	-	0/0
351	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,796.50	03/2013 12/2021	12/2022	117(O) 0	8/15
352	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	3,860.35	2,110.14	06/2013 -	12/2023	126(O) -	11/17
353	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	-	0/15
354	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	479.06	12/2021 -	12/2021	0(O) -	9/32
355	RAMMAM-III HEP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,592.34	626.32	09/2019 11/2022	12/2024	63(O) 0	6/10
356	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	341.06	04/2018 04/2020	01/2021	33(O) 1	0/0
357	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 -	529.68	294.18	11/2018 -	-	-	0/0
	Total		2,83,975.91 -	3,56,631.39	2,47,060.58				589/751
	HEAVY INDUSTRY								
358	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2011	1,554.00 -	1,554.00	806.15	09/2011 12/2020	12/2020	15(O) 0	0/0
	Total		1,554.00 -	1,554.00	806.15				0/0
	HEALTH AND FAMILY WELFARE								
359	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	245.89	03/2019 -	03/2021	24(O) -	0/0
360	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	333.61	- -	06/2021	- -	0/0
361	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0
362	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	279.76	05/2021 -	07/2022	14(O) -	0/0
363	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	499.23	456.52	11/2013 -	03/2021	88(O) -	0/0
364	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	226.54	05/2017 -	03/2021	46(O) -	2/2
365	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	3/5
366	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.64	111.58	- -	03/2021	- -	0/0
367	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	216.09	- -	01/2021	- -	0/0
368	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
369	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	577.32	09/2021 -	09/2021	0(O) -	1/4
370	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0
371	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	94.33	09/2023 -	09/2023	0(O) -	0/0
372	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
373	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	34.89	03/2020 -	12/2021	21(O) -	2/7
374	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	249.74	03/2019 -	01/2021	22(O) -	0/0
375	HOSPITAL AND TEACHING AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2019	582.00 -	582.00	424.00	-	06/2021	-	0/0
376	NEIGRIHMS SHILLONG MEGHALAYA - [N21000013]HSCC,MEGHALAYA ,	10/2017	363.99 -	62.00	227.55	03/2021 -	12/2021	43(O) -	0/0
377	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19(O) -	0/33
378	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	157.90	02/2018 -	12/2020	34(O) -	1/1
379	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	438.92	06/2020 -	07/2021	13(O) -	0/0
380	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	115.97	03/2020 -	05/2021	14(O) -	1/5
381	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	228.89	-	12/2020	-	0/0
382	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	511.74	04/2020 -	07/2021	15(O) -	0/0
383	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3
384	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
385	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	268.35	03/2019 -	03/2021	24(O) -	0/0
386	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL ,	04/2018	651.99 -	651.99	427.72	-	06/2021	-	0/0
	Total		13,445.26 -	13,766.81	7,113.51				14/62

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
387	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
388	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	746.71	03/2009 -	03/2024	180(O) -	0/0
389	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	-	-	-	0/0
390	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	-	-	-	1/1
391	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,643.25	1,191.09	03/2021 -	03/2025	48(O) -	0/1
392	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24(O) -	0/0
393	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	-	-	-	0/0
394	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	984.35	03/2022 03/2025	03/2024	24(O) 0	0/0
395	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26	3,548.68	2,224.17	12/2023 -	12/2023	0(O) -	0/0
396	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,495.71 -	2,999.71	59.79	03.02 03.02	03/2024	24(O) -24	0/0
397	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	487.13	430.52	03/2018 -	03/2021	36(O) -	0/0
398	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019 -	12/2020	21(O) -	0/0
399	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 1,105.00	1,532.00	770.73	03/2019 -	03/2023	48(O) -	0/0
400	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 -	800.00	777.27	03/2019 -	01/2021	22(O) -	0/0
401	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,950.00	1,375.36	03/2022 -	03/2023	12(O) -	0/0
402	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	1,873.21	1,007.06	03/2021 -	05/2021	2(O) -	0/0
403	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 -	1,070.00	1,061.07	03/2012 -	11/2022	128(O) -	0/0
404	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	614.45	333.16	-	03/2022	-	0/0
405	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.78	1,510.98	-	03/2023	-	0/0
406	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	431.28	03/2020 -	09/2020	-	0/0
407	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
408	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	751.55	680.95	03/2012 -	05/2021	110(O) -	0/0
409	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 -	2,145.00	967.13	03/2019 -	03/2024	60(O) -	0/0
410	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	-	03/2022	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
411	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	-	-	0/0
412	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.31	- -	-	-	0/0
413	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	- -	-	-	0/0
414	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	-	0/0
415	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 -	735.20	379.45	- -	03/2021	-	0/0
416	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	383.64	- -	03/2022	-	0/0
417	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
418	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.73	- -	-	-	0/0
419	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	- -	-	-	0/0
420	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	-	03/2024	-	0/0
421	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,005.17	2.74	-	03/2023	-	0/0
422	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	- -	-	-	0/0
423	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	- -	-	-	0/0
424	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,470.50	1,095.55	- -	03/2021	-	0/0
425	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	513.72	03/2020 -	03/2023	36(O) -	0/0
426	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	480.00	473.33	- -	01/2020	-	0/1
427	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	519.33	265.08	- -	02/2023	-	0/0
428	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	760.55	03/2020 -	03/2023	36(O) -	0/1
429	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	465.98	03/2020 -	03/2023	36(O) -	1/1
430	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	546.71	541.83	07/2014 -	-	-	0/0
431	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	299.09	03/2021 -	03/2024	36(O) -	0/0
432	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	154.70	03/2021 -	06/2022	15(O) -	0/0
433	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	726.31	535.07	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
434	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	1,483.14	1,177.09	- -	03/2022	- -	0/0
435	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	891.78	03/2020 03/2023	03/2023	36(O) 0	1/1
436	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,251.62	03/2020 -	12/2021	21(O) -	0/0
437	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
438	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,226.51	1,131.91	12/2019 10/2020	10/2020	-	0/0
439	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 2,135.34	2,135.34	351.35	03/2021 12/2023	12/2023	33(O) 9	0/1
440	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	849.31	03/2022 -	06/2024	27(O) -	0/1
441	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,386.05	09/2018 -	12/2021	39(O) -	0/1
442	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50 . KM) IN ILASPUR DIVISION OF SEC RAILW [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 06/2021	06/2021	15(O) 0	1/2
443	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 196.17	359.00	111.51	- -	03/2024	- -	0/0
444	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	112.95	- -	09/2023	- -	0/0
445	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,959.74	1,959.74	1,760.97	03/2020 12/2023	12/2023	45(O) 0	0/0
446	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 411.62	411.62	125.76	03/2012 03/2023	03/2023	132(O) 0	0/0
447	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	-	0/0
448	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,500.00	1,376.94	12/2021 -	12/2021	0(O) -	0/0
449	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	0(O) -	0/0
450	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	172.03	- 03/2024	03/2024	- 0	0/0
451	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48(O) 0	0/0
452	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,868.89	1,726.74	12/2021 -	03/2022	3(O) -	0/0
453	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,389.05	1,389.05	1,096.41	03/2021 03/2022	03/2022	12(O) 0	0/0
454	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	578.34	03/2021 12/2022	12/2022	21(O) 0	0/0
455	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
456	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
457	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
458	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
459	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 890.76	890.76	738.65	03/2019 10/2021	10/2021	31(O) 0	0/0
460	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 1,017.91	1,017.91	453.03	03/2020 12/2020	12/2020	9(O) 0	0/0
461	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	625.47	12/2011 -	06/2021	114(O) -	0/0
462	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32	346.32	315.22	03/2019	03/2021	24(O) -	0/0
463	BHANUPALI-BILASPUR BIRNI - [N22000273]RVNL,HIMACHAL PRADESH ,	04/200	2,966.99 -	6,534.2	8,37	12/202	12/202	-12(O) -	0/0
464	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1993	2,500.00 27,949.00	27,949.00	22,369.06	11/2002 -	12/2022	241(O) -	0/0
465	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 -	3,500.00	3,494.01	-	03/2022	-	0/0
466	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	1,625.87	712.11	-	03/2023	-	0/0
467	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	295.76	12/2018 12/2018	06/2021	30(O) 0	0/0
468	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	194.30	12/2016 -	08/2020	-	0/0
469	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,993.24	642.92	03/2021 03/2021	12/2023	33(O) 0	0/0
470	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	299.31	03/2021 -	12/2020	-3(O) -	0/0
471	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	3,911.65	156.88	-	12/2024	-	0/0
472	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
473	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,967.00	66.44	-	12/2023	-	0/0
474	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	307.53	03/2016 -	12/2023	93(O) -	1/1
475	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	-	12/2023	-	0/0
476	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
477	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	-	12/2023	-	0/0
478	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,000.00	2,121.59	03/2023 -	12/2022	-3(O) -	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
479	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	-	12/2023	-	0/0
480	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	273.30	12/2018 -	12/2024	72(O) -	0/0
481	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	-	12/2023	-	0/0
482	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	34.85	03/2016 -	12/2023	93(O) -	0/0
483	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,140.94	1,119.20	03/2020 -	11/2021	20(O) -	1/5
484	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	783.00	607.76	03/2020 -	01/2021	10(O) -	1/2
485	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	890.00	462.84	03/2017 -	-	-	0/0
486	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	262.68	-	-	-	0/0
487	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 - 252.96	369.55	8.50	-	-	-	0/0
488	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 - 189.24	275.21	6.73	-	-	-	0/0
489	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,311.90	1,918.81	-	-	-	0/0
490	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 - 828.00	1,246.00	.81	-	-	-	0/0
491	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
492	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	24(O) -	0/15
493	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,413.76	1,416.77	-	08/2020	-	0/0
494	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 5,912.40	5,912.40	2,118.69	03/2022 03/2024	03/2024	24(O) 0	0/0
495	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,762.94	1,032.58	03/2020 -	03/2023	36(O) -	1/1
496	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	1,450.82	12/2020 -	12/2021	12(O) -	0/0
497	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12(O) -	0/10
498	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	273.37	03/2022 -	03/2023	12(O) -	1/1
499	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	172.08	03/2019 -	-	-	0/0
500	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,268.32	941.56	02/2019 12/2021	12/2021	34(O) 12	0/1
501	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.94	1,370.94	470.49	12/2021 12/2023	12/2023	24(O) 9	0/0
502	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	232.01	06/2020 03/2023	03/2023	33(O) 0	0/0
503	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,756.68	03/2004 -	03/2022	216(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
504	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,517.49	2,637.46	03/2021 -	03/2023	24(O) -	0/0
505	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84(O) -	0/0
506	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
507	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,341.89	03/2023 -	03/2023	0(O) -	0/0
508	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	333.58	03/2021 -	03/2023	24(O) -	0/0
509	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	315.00	312.62	03/2019 03/2020	03/2020	-	0/0
510	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	248.22	03/2022 -	03/2024	24(O) -	0/0
511	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
512	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
513	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
514	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2016	1,272.19 -	1,833.09	401.70	03/2022 -	03/2023	12(O) -	0/0
515	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	321.99	03/2023 -	03/2024	12(O) -	0/0
516	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,199.46	03/2024 -	03/2023	-12(O) -	0/0
517	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	429.22	03/2023 -	03/2023	0(O) -	0/0
518	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	240.75	03/2022 -	03/2024	24(O) -	0/0
519	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	165.38	03/2023 -	03/2024	12(O) -	0/0
520	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,725.00	2,479.93	03/2020 -	03/2021	12(O) -	0/0
521	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
522	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 2,753.05	3,524.81	952.24	03/2023 12/2023	12/2023	9(O) 9	0/1
523	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	268.50	03/2019 12/2020	12/2020	21(O) 0	0/0
524	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	-	-	-	0/0
525	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	-	-	-	0/0
526	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 852.50	1,096.00	39.79	12/2021 12/2024	12/2024	36(O) 21	0/1
527	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	12,264.15	10,584.54	03/2011 -	03/2023	144(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
528	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	4,083.02	263.67	03/2021 -	03/2021	0(O) -	0/0
529	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 -	5,521.45	3,781.94	03/2014 -	12/2023	117(O) -	0/0
530	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 1,756.00	2,005.25	1,777.22	04/2020 04/2021	04/2021	12(O) 3	0/1
531	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140(O) -	0/0
532	MUNEERABAD-MAHABOBNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,472.59	1,078.84	03/2000 -	03/2023	276(O) -	0/0
533	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202(O) -	0/9
534	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 4,541.38	5,071.38	3,595.72	12/2008 -	02/2021	146(O) -	0/0
535	DEOGHAR - SULTANGANJ (NL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	133(O) -	0/0
536	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
537	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	02/2007	243.70 -	205.00	112.00	12/2021 -	12/2021	0(O) -	0/0
538	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2001	295.00 -	77.31	49.06	01/2001 -	02/2022	37(O) -	0/0
539	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	883.18	03/2022 03/2023	03/2023	12(O) 0	0/0
540	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	860.64	03/2022 03/2025	03/2025	36(O) 0	0/0
541	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	186.12	- -	-	-	0/1
542	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33(O) -	0/3
543	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
544	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
545	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.55	- -	-	-	0/0
546	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 2,047.51	2,042.51	29.84	03/2019 -	03/2023	48(O) -	0/0
547	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,300.00	2.28	- 03/2024	03/2024	- 0	0/0
548	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	439.49	- -	12/2021	- -	0/0
549	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	73.97	03/2020 -	-	-	0/0
550	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	287.09	- -	12/2021	- -	0/0
551	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	750.00	152.23	03/2020 -	03/2023	36(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
552	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]JER,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
553	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,172.16	232.66	03/2019 -	12/2027	105(O) -	0/0
554	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]JER,MULTI STATE ,	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228(O) -	0/0
555	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]JER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
556	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]JER,MULTI STATE ,	04/2010	172.03 -	260.10	11.05	- -	03/2025	- -	0/0
557	PIRPAINTI-JASIDIH - [N22000219]JER,MULTI STATE ,	04/2013	915.98 -	2,137.81	341.26	03/2022 -	03/2025	36(O) -	0/0
558	BANDEL-BOINCHI 3RD LINE - [N22000221]JER,MULTI STATE ,	04/2011	288.35 -	418.09	412.89	- -	03/2021	- -	0/0
559	PIRPAINTI-BHAGALPUR - [N22000222]JER,MULTI STATE ,	04/2011	261.38 -	516.05	535.20	- -	05/2019	-	0/0
560	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CH. PRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]JER,MULTI STATE ,	04/2005	923.52 -	95.10	636.20	03/2017 -	03/2025	108(O) -	0/0
561	CHINPAI- SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]JER,MULTI STATE ,	04/2005	595.51 -	769.40	103.51	03/2017 -	03/2025	96(O) -	0/0
562	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]JER,MULTI STATE ,	04/2010	174.56 -	174.56	71.43	- -	03/2025	- -	0/0
563	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]JER,MULTI STATE ,	04/2010	277.28 -	266.32	180.03	03/2016 -	03/2025	108(O) -	0/0
564	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]JER,MULTI STATE ,	04/2010	365.17 -	340.10	359.71	03/2017 -	03/2025	96(O) -	0/0
565	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]JER,MULTI STATE ,	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28(O) -	0/0
566	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]JER,MULTI STATE ,	04/2007	450.55 -	250.55	20.12	- -	03/2025	- -	0/0
567	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]JER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
568	HANSDIHA-GODDA NL - [N22000236]JER,MULTI STATE ,	04/2011	542.18 -	663.13	502.41	03/2020 -	03/2021	12(O) -	0/0
569	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]JER,MULTI STATE ,	04/2011	175.80 -	270.72	279.67	- -	03/2022	- -	0/0
570	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]JER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
571	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
572	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
573	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
574	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	162.75	02/2012 -	03/2025	157(O) -	0/0
575	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	105.99	03/2014 -	03/2025	132(O) -	0/0
576	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
577	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000251]SCR,MULTI STATE ,	04/2011	1,856.95	1,52.68	87.47	03/2021 03/2022	03/2024	12(O) 0	0/0
578	DEOBAND (MUZAFFARNA GAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 791.39	61.30	567.11	- -	03/2023	- -	0/0
579	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- -	12/2023	- -	0/0
580	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,432.50	1,096.12	- -	03/2025	- -	2/2
581	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 -	927.94	517.35	03/2020 03/2022	06/2021	15(O) 0	1/1
582	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	2,132.77	346.93	03/2014 -	03/2024	120(O) -	1/1
583	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	332.10	- -	03/2024	- -	0/0
584	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	780.00	155.47	03/2020 -	04/2022	25(O) -	0/0
585	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,147.00	877.08	03/2020 -	06/2021	15(O) -	0/0
586	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,870.41	1,274.19	03/2019 -	03/2021	24(O) -	0/0
587	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	678.54	708.22	03/2019 -	02/2021	23(O) -	0/38
588	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
589	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,222.16	03/2021 -	03/2024	36(O) -	0/0
590	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
591	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	9,576.52	12/2023 -	12/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
592	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	-	0/0
593	CHANDIGARH-BADDI - [N22000467]JNR,MULTI STATE ,	04/2007	328.14 1,540.13	1,540.13	241.62	03/2023 03/2025	03/2025	24(O) 0	0/0
594	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]JNR,MULTI STATE ,	03/2002	625.00 -	859.00	850.50	03/2016 -	06/2021	63(O) -	0/0
595	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 7,114.55	6,911.44	1,045.72	03/2015 -	03/2023	96(O) -	0/0
596	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
597	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,402.12	03/2009 03/2026	03/2026	204(O) 0	0/0
598	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	-	0/0
599	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88(O) -	0/0
600	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	-	1/1
601	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.70 1,928.07	1,038.07	830.77	06/2021 03/2021	03/2025	45(O) 0	0/0
602	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2001	145.90 -	30.00	54.46	03/2011 -	-	-	0/0
603	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 1,539.28	1,539.28	1,090.14	02/2019 12/2021	12/2021	34(O) 0	0/0
604	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	193.29	10/2020 03/2024	03/2024	41(O) 0	0/0
605	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 238.03	238.03	218.99	03/2020 03/2021	03/2022	24(O) 0	0/0
606	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	593.77	03/2022 03/2023	03/2023	12(O) 0	0/0
607	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	357.56	03/2022 03/2026	03/2026	48(O) 0	0/0
608	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 810.02	810.02	168.21	11/2018 03/2024	03/2024	64(O) 0	0/0
609	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	590.18	12/2018 03/2024	03/2024	63(O) 0	0/0
610	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	795.27	03/2020 03/2020	12/2021	21(O) 0	0/0
611	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	1,122.68	12/2024 -	12/2026	24(O) -	0/0
612	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	21(O) -	0/0
613	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39(O) -	0/0
614	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 962.00	962.00	54.75	03/2020 03/2024	03/2024	48(O) 0	0/0
615	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
616	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR, RAJASTHAN ,	02/1997	410.08 -	860.41	677.30	02/2019 -	11/2021	33(O) -	0/0
617	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN ,	04/2012	246.08 -	395.00	306.94	12/2019 -	02/2021	14(O) -	0/0
618	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN ,	04/2013	236.93 -	350.45	244.56	10/2018 -	-	-	0/0
619	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN ,	04/2013	822.00 -	1,099.00	.00	-	-	-	0/1
620	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN ,	04/2013	323.00 -	432.22	.00	-	-	-	0/0
621	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN ,	04/2013	420.18 -	420.18	287.94	03/2020 -	06/2021	15(O) -	0/0
622	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN ,	04/2011	213.39 -	375.00	327.89	11/2019 -	03/2021	16(O) -	0/0
623	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN ,	04/2013	242.09 -	525.00	457.31	02/2019 -	02/2020	-	0/0
624	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.60	-	-	-	0/0
625	MULTI MODAL LOGISTICS PARK AT KATHUWAS [N22000421]CCOI, RAJASTHAN ,	01/2015	493.17 -	93.17	64.53	03/2015	03/2020	-	0/0
626	JODHPUR (RAI KA BAGH) DEGAN DOUBLING (1.5 KM) - [N22000466]NWR, RAJASTHAN ,	03/2015	806.85 -	100.85	153.35	03/2021 -	03/2022	-2(O) -	0/0
627	SEVOK RANGPO NEFR - [N22000102]NFR, SIKKIM ,	04/2008	1,339.48 4,084.69	8,600.00	619.18	12/2015 12/2023	03/2023	87(O) -	0/0
628	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU ,	09/1995	303.98 -	1,720.00	693.14	03/2020 -	03/2025	60(O) -	0/0
629	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP, TAMIL NADU ,	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102(O) -	1/4
630	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU ,	09/2007	724.69 -	2,910.84	1,583.77	02/2019 -	03/2025	73(O) -	0/0
631	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU ,	09/2006	227.40 -	227.40	63.90	-	-	-	0/0
632	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU ,	09/2006	582.83 -	582.83	233.89	-	12/2025	-	0/0
633	ATTIPPATTU PUTTUR - [N22000184]SR, TAMIL NADU ,	04/2008	151.84 -	527.37	3.34	02/2019 -	-	-	0/0
634	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	-	-	-	0/0
635	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU ,	04/1999	198.68 -	559.95	319.22	-	03/2025	-	0/0
636	ERODE-PALANI - [N22000199]SR, TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	-	-	-	0/0
637	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU ,	04/2008	164.41 -	450.73	340.21	-	09/2021	-	0/0
638	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU ,	04/2007	931.98 -	961.09	873.72	- 02/2021	02/2021	- 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
639	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	332.00	239.19	04/2014 01/2021	12/2020	80(O) 0	0/0
640	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198(O) -	0/0
641	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	238.00	153.46	03/2018 -	-	-	0/0
642	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
643	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3(O) -	0/0
644	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27(O) -	0/0
645	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	466.96	03/2010 -	03/2025	180(O) -	1/1
646	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	786.37	03/2016 -	12/2021	69(O) -	0/0
647	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
648	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	02/2015	636.22 -	636.22	507.32	03/2021 -	03/2021	0(O) -	3/3
649	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	02/2015	773.94 -	668.00	705.50	12/2021 -	12/2024	0(O) -	0/0
650	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9(O) -	0/0
651	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	742.00	200.28	03/2020 03/2022	03/2022	24(O) 6	2/3
652	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
653	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
654	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
655	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
656	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	- -	0/0
657	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
658	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	778.29	03/2022 -	03/2022	0(O) -	0/0
659	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	-	4/6
660	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33(O) -	0/0
661	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,400.00	1,280.16	03/2019 -	06/2021	27(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
662	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	833.10	03/2023 -	12/2024	21(O) -	0/0
663	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24(O) -	0/0
664	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,005.54	03/2020 -	03/2021	12(O) -	0/0
665	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	194.21	03/2019 -	03/2021	24(O) -	0/0
666	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	28.80	04/2016 -	12/2021	68(O) -	0/0
667	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
668	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
669	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
670	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	475.97	04/2017 -	03/2021	47(O) -	0/0
671	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	76.90	.00	04/2017 -	04/2022	60(O) -	0/0
672	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	1,148.91	56.54	-	12/2023	-	0/0
673	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	169.83	01/2022 -	03/2022	2(O) -	0/0
674	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	80.32	12/2019 -	04/2021	16(O) -	0/0
675	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	33.37	03/2023 03/2026	03/2023	0(O) 0	0/0
676	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021	0(O) -	0/6
677	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	1,436.33	12/2023 -	12/2023	0(O) -	0/0
678	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
679	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	204.53	-	-	-	0/0
680	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	22,716.11	2,555.91	12/2024 -	03/2025	3(O) -	0/0
681	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	275.07	03/2019 -	-	-	0/0
682	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
683	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
684	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	899.24	03/2019 12/2009	03/2025	72(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
685	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	954.89	12/2010 -	03/2025	171(O) -	7/7
686	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
687	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0
688	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,629.88	03/2016 -	03/2025	108(O) -	0/0
689	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	1,002.79	03/2016 -	03/2025	108(O) -	0/0
690	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
691	BOWAICHANDI-ARAMBACH - [N22000159]SER, WEST BENGAL ,	04/2010	267.27 -	620.00	40.90	-	03/2025	-	0/0
692	NEW BG LINE FROM KALI AGANJ TO BUNIMCHUR - [N22000193]NFR, WEST BENGAL ,	04/2011	221.42 -	80.00	36.20	-	-	-	0/0
693	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	-	03/2025	-	0/0
694	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	227.07	-	03/2022	-	0/0
695	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	760.00	730.62	12/2021 -	03/2021	-9(O) -	0/0
696	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
697	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN - [N22000499]NFR, WEST BENGAL ,	02/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-	-	0/0
	Total		4,61,691.03 -	6,98,197.39	2,37,960.69				33/139
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
698	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD, ANDHRA PRADESH ,	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6(O) -	3/7
699	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD, ANDHRA PRADESH ,	02/2019	655.34 -	655.34	49.89	06/2020 -	-	-	0/110
700	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRICT - [N42000007]CPWD, ANDHRA PRADESH ,	09/2019	588.72 -	588.72	14.80	09/2022 04/2023	01/2023	4(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
701	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	185.61	06/2017 -	09/2021	51(O) -	1/6
702	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD,CHHATISGARH ,	03/2020	808.62 -	808.62	57.42	07/2022 -	07/2022	0(O) -	0/0
703	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD,GOA ,	05/2019	303.90 -	303.90	9.50	03/2020 -	-	-	0/8
704	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	226.16	11/2014 -	12/2020	73(O) -	2/8
705	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	35.88	06/2022 -	06/2022	0(O) -	0/0
706	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR ,	03/2019	329.00 -	329.00	.00	07/2022 -	07/2020	-	0/0
707	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR ,	01/2018	676.00 748.19	676.00	.00	04/2023 -	04/2023	0(O) -	0/0
708	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2011	171.86 -	171.86	11.29	03/2011 -	03/2021	63(O) -	1/6
709	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	26.10	03/2022 -	03/2022	6(O) -	0/0
710	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	03/2020	-	1/8
711	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15(O) -	0/0
712	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11(O) -	4/14
713	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	12/2020	75(O) -	0/0
714	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE ,	03/2018	150.00 -	150.00	.00	04/2018 -	-	-	0/0
715	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE ,	08/2018	418.00 -	418.00	110.00	03/2019 -	-	-	0/0
716	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BIRHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	790.79	122.02	03/2022 -	06/2022	3(O) -	0/5
717	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	350.69	258.72	04/2019 -	01/2021	21(O) -	7/8
718	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	387.83	167.01	05/2020 -	10/2021	17(O) -	2/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
719	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD,PUNJAB ,	10/2019	348.24 -	348.24	7.05	05/2022 -	05/2022	0(O) -	0/7
720	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 559.47	559.47	458.38	07/2019 12/2020	03/2021	20(O) 0	3/6
721	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 171.72	171.72	53.94	03/2020 -	06/2021	15(O) -	0/0
722	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL , EPC	03/2020	193.83 -	193.83	.45	06/2020 -	11/2020	-	0/0
	Total		10,702.40 -	10,890.83	2,263.19				24/198
	<u>HOME AFFAIRS</u>								
723	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	841.88	10/2019 -	09/2021	23(O) -	1/7
724	C/O SEPARATE FAMILY ACCOMMODATION (F.H. SE-I) WHICH INCLUDES C/O 44 - NO. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD,HARYANA , EPC	01/2020	166.98 167.00	66.98	00	10/2020 10/2020	10/2020	0(O) -	0/0
725	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	179.16	168.45	04/2018 -	12/2020	32(O) -	5/6
	Total		1,549.07 -	2,346.14	1,010.33				6/13
	<u>RURAL DEVELOPMENT</u>								
726	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI ,	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021	0(O) -	0/2
727	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2021	62(O) -	0/1
728	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	207.12	189.79	12/2016 -	03/2021	51(O) -	1/5
729	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	175.49	124.87	12/2016 -	03/2021	51(O) -	0/4
	Total		889.43 -	899.87	472.05				1/12
	<u>CULTURE DEVELOPMENT</u>								
730	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	144.00	09/2017 -	03/2021	42(O) -	12/15
	Total		151.33 -	151.33	144.00				12/15

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ROAD TRANSPORT AND HIGHWAYS								
731	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	26.44	10/2018 -	-	-	0/4
732	2 LANE WITH HARD SHOULDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	47.28	12/2017 -	-	-	0/4
733	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	172.78	04/2017 -	-	-	3/4
734	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	39.86	10/2018 -	-	-	0/4
735	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	24.96	10/2018 -	-	-	1/4
736	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 102.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2011	237.30 -	38.00	1.48	11/2011 -	-	-	0/0
737	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	-	-	0/0
738	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	164.81	07/2019 -	-	-	0/4
739	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
740	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,274.78	05/2014 -	-	-	0/0
741	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
742	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
743	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	218.26	10/2015 03/2021	-	-	3/4
744	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
745	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
746	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	1,634.05	11/2018 -	-	-	0/0
747	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
748	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	947.88	03/2020 -	-	-	0/0
749	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	234.49	-	-	-	0/0
750	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	785.33	-	07/2021	-	0/0
751	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	-	-	-	0/0
752	SIX LANING OF ANANDAPURAM PENDINGURTHI ANAKAPALLI SECTION OF NH-5 NE V NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2019	1,959.00 -	1,050.00	1,145.62	-	10/2021	-	0/0
753	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	2,499.00	1,497.61	03/2021 10/2021	04/2021	1(0) 0	2/4
754	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,290.79	-	09/2021	-	0/0
755	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	495.25	-	02/2021	-	0/0
756	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	86.83	-	04/2021	-	0/0
757	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	351.02	-	05/2018	-	0/0
758	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	355.89	315.57	12/2015 -	-	-	3/3
759	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	207.28	02/2017 06/2021	02/2019	-	2/4
760	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	315.42	01/2018 -	-	-	4/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
761	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	100.54	05/2017 07/2021	05/2019	-	2/4
762	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	141.98	08/2017 05/2021	08/2019	-	2/4
763	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	277.54	11/2017 04/2021	11/2019	-	3/4
764	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	99.57	08/2018 03/2021	03/2021	31(O) 0	2/4
765	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	136.22	08/2018 -	-	-	2/3
766	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	173.13	08/2018 06/2021	02/2021	30(O) 0	3/4
767	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	294.12	373.98	07/2018 -	-	-	4/4
768	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	403.01	11/2018 04/2021	01/2021	26(O) 0	3/4
769	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	473.71	05/2016 08/2021	04/2021	59(O) 0	2/4
770	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	268.80	08/2018 05/2021	08/2020	-	3/4
771	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	323.06	01/2017 12/2020	12/2020	47(O) 0	3/4
772	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	199.35	05/2016 01/2021	12/2020	55(O) 0	3/4
773	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021	59(O) 0	2/4
774	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	304.42	09/2016 07/2021	09/2020	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
775	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	264.97	08/2017 06/2021	08/2020	-	3/4
776	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021	44(O) 0	0/4
777	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	288.92	01/2018 11/2020	12/2020	35(O) 0	1/4
778	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/0
779	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	.00	02/2012 -	-	-	0/0
780	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
781	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	389.45	349.94	05/2012 06/2018	-	-	0/0
782	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	196.23	05/2018 -	-	-	4/4
783	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	199.53	01/2019 -	-	-	4/4
784	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 197.16	197.16	89.41	10/2018 09/2015	09/2018	-	1/4
785	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	376.15	06/2018 -	-	-	2/3
786	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	187.33	11/2016 -	-	-	4/4
787	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	160.24	- -	-	-	2/4
788	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	184.62	10/2016 -	-	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
789	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL PRADESH , [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	172.89	- -	12/2020	- -	2/4
790	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	-	2/4
791	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60(O) -	1/4
792	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	127.41	04/2017 03/2018	03/2021	47(O) 0	1/4
793	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	94.62	04/2017 -	-	-	2/4
794	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	106.52	04/2017 -	-	-	2/4
795	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	98.74	04/2017 -	-	-	2/4
796	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	43.28	04/2017 -	02/2021	46(O) -	1/4
797	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	44.85	04/2017 -	02/2021	46(O) -	0/4
798	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	26.84	04/2017 -	02/2021	46(O) -	0/4
799	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	22.06	04/2017 -	02/2021	46(O) -	1/4
800	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	98.23	04/2017 -	-	-	2/4
801	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
802	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	105.37	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
803	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	303.02	- -	-	-	0/0
804	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH ,	05/2016	259.52 -	259.52	184.51	- -	-	-	0/0
805	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	220.29	- -	-	-	0/0
806	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	88.62	- -	-	-	0/0
807	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	62.27	- -	04/2022	-	0/4
808	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 3 +050 TO KM. 44+00 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	54.56	- -	04/2022	-	0/4
809	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH ,	02/2017	199.02 -	199.02	14.21	- -	02/2021	-	0/4
810	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH ,	02/2017	184.88 -	184.88	6.85	- -	02/2021	-	0/4
811	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	135.60	- 01/2016	01/2019	-	0/4
812	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH ,	07/2015	189.91 -	189.91	160.05	- -	-	-	4/4
813	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	125.55	- -	-	-	3/4
814	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
815	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,217.25	- 03/2020	-	-	0/0
816	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	149.45	- -	09/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
817	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	520.00	612.58	02/2009 -	-	-	0/0
818	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	340.14	325.28	04/2009 -	-	-	0/0
819	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	435.78	427.96	11/2008 -	-	-	0/0
820	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	255.23	251.39	11/2008 -	-	-	0/0
821	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	231.82	03/2008 -	08/2020	-	0/0
822	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	347.28	06/2008 -	09/2019	-	0/0
823	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	355.20	04/2008 -	12/2020	152(O) -	0/0
824	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	230.89	05/2008 -	06/2019	-	0/0
825	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	655.17	655.17	07/2009 -	-	-	0/0
826	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	360.84	488.05	04/2010 -	07/2019	-	0/0
827	FOUR LANING OF NUMAL GAPH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	54.89	23.35	05/2015 -	12/2020	31(O) -	2/4
828	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	407.30	56.22	06/2018 -	12/2021	42(O) -	0/4
829	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	398.06	103.86	06/2018 -	12/2021	42(O) -	0/4
830	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	350.14	01/2019 -	-	-	2/4
831	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	114.16	11/2018 -	-	-	4/4
832	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	460.01	11/2018 -	-	-	3/4
833	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 -	268.08	267.46	05/2017 -	-	-	0/0
834	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	386.98	02/2011 -	-	-	0/0
835	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM , EPC	11/2014	218.31 -	307.47	292.55	02/2018 -	-	-	0/0
836	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	26.00	12/2018 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
837	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	111.16	06/2018 -	-	-	3/4
838	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	126.13	-	-	-	1/4
839	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	55.03	12/2018 -	-	-	1/4
840	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	170.00	01/2016 -	04/2021	63(O) -	1/4
841	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	223.50	80.88	01/2016 -	-	-	0/4
842	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	372.69	01/2016 -	-	-	2/3
843	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N2400090]NHIDCL,ASSAM ,	10/2017	818.00	887.68	178.47	-	-	-	1/4
844	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 51/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/201	160.00 -	60.00	5.16	09/202 -	09/2021	0(O) -	0/0
845	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	-	-	0/0
846	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	273.40	115.65	-	-	-	0/0
847	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM ,	03/2020	166.94 -	166.94	.00	12/2020 -	12/2020	0(O) -	0/0
848	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 671.30	671.30	1,360.63	02/2013 -	-	-	3/4
849	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
850	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
851	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	555.63	07/2013 -	-	-	2/3
852	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 585.00	591.00	575.34	11/2013 12/2020	01/2021	86(O) 0	0/0
853	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 -	675.00	239.89	-	-	-	0/0
854	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	317.05	08/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
855	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	341.81	10/2016 -	-	-	0/0
856	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	-	-	-	0/0
857	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	276.41	04/2019 -	-	-	0/0
858	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	512.04	-	10/2021	-	2/4
859	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	32(O) -	0/0
860	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	400.60	-	-	-	1/4
861	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 1,182.94	1,182.94	186.70	-	-	-	0/0
862	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	297.27	271.39	04/2019 -	-	-	3/4
863	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR ,	01/1991	478.35 -	478.35	435.30	-	-	-	0/0
864	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.50 1,036.56	1,38.50	1,16.00	-	-	-	3/4
865	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 649.27	649.27	712.15	04/2018 -	-	-	4/4
866	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR , EPC	01/1991	154.62 -	154.62	.00	-	-	-	0/0
867	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	216.25	-	-	-	0/0
868	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
869	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 -	560.70	657.38	07/2016 -	-	-	0/0
870	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
871	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	87.02	05/2016 -	-	-	0/0
872	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
873	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	289.14	05/2016 -	-	-	0/0
874	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 -	925.87	699.76	10/2016 -	-	-	0/0
875	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
876	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR ,	08/2015	288.24 -	288.24	300.58	11/2015 -	-	-	0/0
877	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	89.69	05/2017 -	-	-	0/0
878	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,399.93	12/2016 -	-	-	0/0
879	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	21.04	03/2020 -	-	-	0/0
880	CONSTRUCTION OF ROAD APPROACHES TO RAILCUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	237.77	36.00	03/2020 -	05/2021	14(O) -	0/0
881	SIX LANING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	194.95	08/2017 -	02/2022	54(O) -	0/0
882	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
883	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	22.95	- -	-	-	0/0
884	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
885	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	38.11	- -	-	-	0/0
886	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	3.72	- -	-	-	0/0
887	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR ,	11/2016	230.34 232.90	230.34	205.97	10/2019 -	-	-	0/0
888	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	39.82	- -	-	-	0/0
889	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR ,	05/2014	199.98 -	199.98	174.35	08/2016 -	12/2020	52(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
890	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	14.53	- -	-	-	0/0
891	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH ,	03/2010	179.89 271.00	271.00	.00	03/2013 -	-	-	0/0
892	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH ,	12/2010	169.26 299.00	299.00	.00	01/2019 -	-	-	0/0
893	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	200.70	- 10/2020	10/2020	-	0/0
894	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.13	12/2015 -	-	-	0/0
895	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	439.27	05/2018 -	-	-	0/0
896	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
897	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+00 TO K... 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2016	1,025.96 -	1,061.05	296.09	- 03/2021	-	-	0/0
898	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 527.66	527.66	232.36	08/2016 03/2021	03/2021	55(O) 0	0/0
899	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	245.69	06/2017 02/2021	02/2021	44(O) 0	0/0
900	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 543.73	544.00	397.32	09/2016 03/2021	03/2021	54(O) 0	0/0
901	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH ,	03/2016	491.52 512.77	491.52	474.27	09/2016 10/2020	10/2020	-	0/0
902	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 731.50	731.50	341.61	10/2016 12/2020	12/2020	50(O) 0	0/0
903	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 435.61	435.61	73.30	07/2016 03/2021	03/2021	56(O) 0	0/0
904	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	252.15	01/2018 03/2021	03/2021	38(O) 0	0/0
905	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	226.59	03/2015 03/2021	03/2021	72(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
906	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	65.21	05/2019 03/2021	03/2021	22(O) 0	0/0
907	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	235.01	11/2017 03/2021	03/2021	40(O) 0	0/0
908	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	-	-	0/0
909	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
910	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	197.75	- -	-	-	0/4
911	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	91.39	- -	-	-	2/4
912	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	219.47	- -	-	-	3/4
913	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS FIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	12/2015	936.40 -	936.40	355.10	- -	-	-	0/0
914	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	336.25	- -	-	-	0/0
915	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	205.20	- -	-	-	0/0
916	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	221.25	05/2020 -	-	-	1/4
917	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 -	852.67	138.14	12/2019 -	-	-	1/4
918	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.89	09/2012 -	-	-	2/3
919	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	11/2020	-	0/0
920	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-	-	3/3
921	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0
922	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	697.86	- -	-	-	2/2
923	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	203.40	- -	-	-	1/1
924	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	503.45	- -	-	-	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
925	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	450.54	- -	-	-	2/2
926	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	132.68	- -	-	-	0/0
927	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	392.00	353.42	- -	12/2020	-	0/0
928	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	224.34	- -	-	-	0/0
929	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	303.96	- -	-	-	0/3
930	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
931	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	8(O) -	3/3
932	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
933	SIX LANING OF SHAMLA - TO MOTACHILODA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	03/2018	1,052.21 -	1,140.00	39.36	- -	01/2021	-	0/0
934	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
935	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 -	1,437.64	584.17	- -	07/2021	-	0/0
936	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	37.17	- -	-	-	0/0
937	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN - [N24000920]MoRTH,GUJARAT ,	03/2016	223.67 -	223.67	112.81	02/2017 -	-	-	4/4
938	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]MoRTH,GUJARAT , EPC	03/2016	208.34 -	208.34	112.87	02/2016 -	-	-	0/4
939	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	392.24	11/2018 -	-	-	2/4
940	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	268.50	11/2018 -	-	-	3/4
941	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	130.53	05/2019 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
942	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	182.43	03/2018 -	-	-	1/4
943	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	84.67	06/2021 -	06/2021	0(O) -	1/4
944	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
945	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,967.50	3,994.51	11/2011 -	-	-	0/0
946	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	507.70	496.22	06/2016 -	-	-	0/0
947	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	537.16	516.32	07/2018 -	-	-	0/0
948	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29(O) -	0/0
949	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	270.65	05/2019 -	-	-	0/0
950	CONSTRUCTION OF FLY OVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT JHOKA CHOWK AT KM. 28.211 - [N2400062]NHAI,HARYANA ,	09/2017	1,004.67 -	13.45	577.11	09/2017 -	-	-	0/0
951	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	595.53	03/2020 -	-	-	0/0
952	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	356.66	- 06/2021	12/2020	- 0	0/0
953	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	169.48	- -	-	-	0/0
954	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	195.35	- -	-	-	0/0
955	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	931.21	183.69	- -	07/2021	- -	0/0
956	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	142.26	- -	07/2021	- -	0/0
957	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	117.51	- -	-	-	0/0
958	REHABILITATION AND UPGADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	128.10	- -	-	-	0/0
959	REDESIGNING REHABILITATION AND UPGADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	306.06	- -	-	-	0/0
960	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	162.62	03/2019 -	02/2021	23(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
961	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MORTH,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 -	-	-	0/0
962	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	526.09	- 02/2020	-	-	0/0
963	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	501.73	- -	-	-	0/0
964	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	690.88	- -	-	-	0/0
965	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	604.45	- -	-	-	0/0
966	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	659.79	- 01/2020	-	-	0/0
967	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	438.38	- 06/2020	-	-	0/0
968	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	468.24	- 02/2020	-	-	0/0
969	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	567.52	- -	-	-	0/0
970	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOO) ,	11/2016	1,916.70 -	1,916.70	1,960.92	11/2016 -	-	-	0/0
971	FOUR LANING OF PARWANOO -SOLAN SECTION - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2016	934.46 1,302.98	934.46	697.35	03/2016 09/2020	-	-	0/0
972	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	666.55	02/2019 -	-	-	0/0
973	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 2,173.74	1,583.18	271.06	- -	09/2020	-	0/0
974	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	650.93	- -	-	-	0/0
975	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,153.75	- -	08/2020	-	0/0
976	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	827.25	06/2020 -	09/2021	15(O) -	0/0
977	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 1,118.19	478.74	127.42	- -	05/2021	-	0/0
978	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,105.02	07/2015 -	09/2020	-	0/0
979	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,708.76	06/2015 -	-	-	0/0
980	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,650.38	07/2013 -	-	-	0/0
981	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,921.73	06/2014 -	10/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
982	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	815.94	06/2019 -	12/2020	18(O) -	0/0
983	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,602.34	12/2018 -	-	-	0/0
984	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	761.37	- -	01/2021	- -	2/3
985	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	118.87	08/2018 -	-	-	2/4
986	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	68.37	11/2018 -	-	-	1/4
987	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	16.38	07/2019 -	-	-	0/0
988	RANCHI-RARGA-JAMSHEDPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
989	4-LANNING OF MAHULIA - AHARADORA-JHARKHAND BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2011	997.15 -	97.15	72.62	03/2011 -	-	-	0/0
990	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	428.69	- -	-	-	0/0
991	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	336.60	310.12	08/2018 -	-	-	0/0
992	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	44.05	- -	-	-	0/0
993	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	327.70	- -	-	-	0/0
994	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- -	03/2021	- -	0/0
995	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND ,	03/2018	212.99 -	212.99	141.46	06/2020 -	11/2020	-	0/0
996	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	.00	09/2021 -	09/2021	0(O) -	0/0
997	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	-	-	3/3
998	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
999	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
1000	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
1001	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52(O) -	0/0
1002	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,277.00	08/2018 -	-	-	0/0
1003	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	95.50	03/2019 -	03/2022	36(O) -	0/0
1004	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	-	0/0
1005	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	936.78	04/2020 -	12/2020	8(O) -	0/0
1006	HOSPET-BELLARY-KARNATAKA BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	276.50	01/2021 -	12/2021	33(O) 0	0/0
1007	TWO/FOUR LANNING OF TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2011	950.69 -	1,080.00	1,425.26	08/2019 -	12/2020	16(O) -	0/0
1008	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	900.64	03/2020 -	-	-	0/0
1009	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,013.67	03/2020 -	-	-	0/0
1010	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	273.86	-	-	-	0/0
1011	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,080.15	-	11/2021	-	0/0
1012	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,047.35	-	-	-	0/0
1013	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
1014	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
1015	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1016	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
1017	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
1018	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0
1019	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
1020	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
1021	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 386.40	325.86	326.88	10/2018 -	-	-	0/0
1022	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.4 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	03/2018	329.51 -	29.01	13.50	02/2019 -	-	-	0/0
1023	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
1024	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
1025	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
1026	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
1027	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	-	-	0/0
1028	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
1029	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	-	-	0/0
1030	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1031	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	-	0/0
1032	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	-	0/0
1033	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	889.83	- 01/2020	01/2020	-	0/0
1034	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	520.05	06/2018 10/2020	03/2021	33(O) 0	0/0
1035	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	419.66	09/2017 -	05/2021	44(O) -	0/0
1036	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1037	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1038	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
1039	SATANA-BELA SECTION (NH-75 (4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2011	320.40 -	320.40	18.49	08/2011 -	-	-	0/0
1040	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	249.75	- 12/2020	06/2021	- 0	0/0
1041	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	728.49	05/2017 -	04/2021	47(O) -	0/0
1042	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1043	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73(O) -	0/0
1044	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71(O) -	0/0
1045	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 686.13	686.13	669.94	- -	05/2020	-	0/0
1046	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 679.94	691.38	669.35	- -	05/2020	-	0/0
1047	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	398.38	01/2020 01/2021	03/2021	14(O) 0	0/0
1048	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	713.84	02/2020 04/2021	04/2021	14(O) 1	0/0
1049	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	824.83	- -	06/2015	-	0/0
1050	FOUR LANING OF GWALIOR-SHIPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1051	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1052	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	771.23	- 06/2015	06/2015	-	0/0
1053	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	354.95	08/2017 06/2021	06/2021	46(O) 0	0/0
1054	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	195.73	01/2019 -	-	-	4/4
1055	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	447.94	10/2017 -	02/2021	40(O) -	3/4
1056	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	213.11	09/2017 -	12/2020	39(O) -	3/4
1057	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	619.77	09/2017 -	01/2021	40(O) -	3/4
1058	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	50.27	200.47	- -	03/2021	-	3/4
1059	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	738.74	- -	-	-	0/4
1060	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	280.75	- -	07/2018	-	0/0
1061	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	124.81	03/2018 02/2021	02/2021	35(O) 0	0/0
1062	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 173.41	173.41	139.19	08/2018 03/2021	03/2021	31(O) 0	0/0
1063	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	29.65	03/2018 04/2021	04/2021	37(O) -1	0/0
1064	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH ,	11/2017	235.91 -	235.91	167.93	02/2018 02/2021	02/2021	36(O) 2	0/0
1065	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	105.89	02/2018 02/2021	02/2021	36(O) 2	0/0
1066	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH ,	03/2018	191.21 -	191.21	117.80	11/2019 01/2021	01/2021	14(O) 0	0/0
1067	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	113.56	03/2017 06/2021	06/2021	51(O) 3	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1068	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	49.85	03/2018 09/2021	09/2021	42(O) 6	0/0
1069	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 226.88	226.88	160.76	08/2018 03/2021	03/2021	31(O) 0	0/0
1070	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	151.12	03/2018 01/2021	03/2021	36(O) 0	0/0
1071	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	191.67	07/2018 03/2021	03/2021	32(O) 0	0/0
1072	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	03/2021	37(O) 0	0/0
1073	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	03/2021	36(O) 0	0/0
1074	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH ,	09/2016	287.34 -	287.34	194.85	01/2019 09/2020	11/2020	-	0/0
1075	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	173.84	09/2019 06/2021	06/2021	21(O) 0	0/0
1076	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	488.46	07/2018 05/2021	05/2021	34(O) 2	0/0
1077	REHABILITATION AND UP-GRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2017	877.79 -	77.79	635.73	09/2019 03/2021	03/2021	21(O) 0	0/0
1078	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH ,	09/2016	178.23 -	178.23	122.99	09/2018 -	-	-	0/0
1079	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	246.80	06/2019 -	-	-	0/4
1080	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	305.76	03/2018 06/2021	06/2021	39(O) 0	0/0
1081	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	55.12	03/2021 -	03/2021	0(O) -	0/0
1082	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	115.40	- -	12/2021	- -	0/0
1083	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	35.00	- -	-	-	0/0
1084	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	220.12	- -	02/2022	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1085	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	31.81	- -	-	-	0/0
1086	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	302.88	12/2019 -	12/2021	24(O) -	2/3
1087	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	208.90	03/2020 -	04/2022	25(O) -	1/3
1088	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	172.62	05/2020 -	05/2022	24(O) -	1/3
1089	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	200.45	03/2020 -	-	-	1/3
1090	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,540.00	03/2013 -	03/2021	96(O) -	0/0
1091	WIDENING OF KHED-SINHAUR STRETCH OF PUNE NASHIK SECTION OF NH- 0 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	03/2011	1,348.20 -	1,48.20	1,79.90	02/2011 -	-	-	2/2
1092	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	80.00	- -	-	-	0/4
1093	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1094	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	300.50	- -	-	-	3/4
1095	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1096	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1097	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	87.11	- -	-	-	0/0
1098	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1099	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	408.40	05/2018 11/2020	11/2020	-	0/1
1100	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	730.97	614.25	05/2018 06/2021	06/2021	37(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1101	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1102	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	690.17	572.57	05/2018 06/2021	06/2021	37(O) 0	0/1
1103	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	184.90	03/2019 12/2021	12/2021	33(O) 6	0/0
1104	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	333.68	05/2018 04/2019	06/2021	37(O) 0	0/1
1105	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0
1106	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	854.98	11/2016 -	-	-	0/0
1107	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 2,754.00	1,871.34	3,443.43	01/2018 12/2018	09/2020	-	0/0
1108	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE CANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1109	BALANCE WORK OF 4-LANING FROM KM 153.00 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2011	197.69 -	97.69	151.11	07/2011 -	-	-	0/0
1110	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	298.39	07/2019 06/2021	12/2021	29(O) 6	0/0
1111	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	313.00	07/2019 06/2021	12/2021	29(O) 6	0/0
1112	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	585.85	- -	-	-	0/0
1113	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	324.00	- -	-	-	0/0
1114	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	841.64	- -	07/2021	-	2/4
1115	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	235.12	- -	07/2021	-	1/4
1116	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	89.63	03/2019 -	02/2021	23(O) -	0/0
1117	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	59.61	03/2019 -	03/2021	24(O) -	0/0
1118	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	315.00	309.40	- -	-	-	0/0
1119	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	251.87	05/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1120	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA ,	02/2017	904.16 -	904.16	855.25	02/2020 -	-	-	0/0
1121	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA ,	03/2017	247.02 -	157.49	57.96	03/2020 -	-	-	0/0
1122	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	-	-	0/0
1123	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	-	0/3
1124	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	08/2020	-	3/3
1125	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	11/2020	-	0/0
1126	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	-	-	0/0
1127	4-LANNING OF MAHAGAON-YAVATMAL SECTION (KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA ,	03/2017	1,096.06 -	1,160.64	1,066.76	03/2020 -	-	-	0/3
1128	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA ,	12/2017	404.94 -	448.18	385.69	- -	10/2020	-	0/0
1129	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA ,	01/2018	607.00 -	607.00	380.86	- -	08/2021	- -	0/1
1130	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA ,	01/2018	621.00 -	621.00	564.85	- -	04/2021	- -	2/3
1131	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI, MAHARASHTRA , EPC	03/2018	291.53 -	291.53	122.48	- 08/2021	11/2021	- 3	0/0
1132	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI, MAHARASHTRA , EPC	03/2018	289.21 -	289.21	126.45	- 06/2021	09/2021	- 3	0/0
1133	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	71.45	- -	07/2021	- -	0/0
1134	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA ,	03/2018	642.13 -	807.00	617.58	- -	12/2020	- -	0/0
1135	SARSAM TO KOTHARI - [N24001002]MoRTH, MAHARASHTRA ,	02/2016	545.64 -	545.64	125.53	07/2019 -	-	-	0/4
1136	AKOLA TO AKOT - [N24001003]MoRTH, MAHARASHTRA ,	01/2017	313.95 -	313.95	49.24	06/2019 -	-	-	0/4
1137	AKOT TO ANJANGAON - [N24001006]MoRTH, MAHARASHTRA ,	01/2017	245.77 246.00	245.77	159.98	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1138	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	173.79	05/2019 -	-	-	0/0
1139	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	266.43	05/2019 -	-	-	0/4
1140	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	229.08	05/2019 -	-	-	0/4
1141	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	353.00	06/2019 -	-	-	0/4
1142	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	173.00	06/2019 -	-	-	0/0
1143	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	233.75	06/2019 -	-	-	0/0
1144	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	192.29	06/2019 -	-	-	0/0
1145	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	289.90	06/2019 -	-	-	0/0
1146	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	152.00	06/2019 -	-	-	3/4
1147	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	264.60	06/2019 -	-	-	0/0
1148	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	241.48	06/2019 -	-	-	0/4
1149	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 397.00	396.91	264.48	06/2019 -	-	-	3/4
1150	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 364.00	363.82	26.34	09/2019 -	-	-	1/4
1151	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	224.81	06/2019 -	-	-	0/4
1152	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 -	457.52	352.94	07/2019 -	-	-	2/4
1153	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	268.87	07/2019 -	-	-	3/4
1154	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	46.03	05/2019 -	-	-	1/4
1155	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	40.42	12/2019 -	-	-	1/4
1156	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	81.57	12/2019 -	-	-	0/4
1157	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	179.58	08/2019 -	-	-	2/4
1158	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	220.44	08/2019 -	-	-	2/4
1159	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	162.30	08/2019 -	-	-	2/4
1160	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	155.78	05/2019 -	-	-	0/4
1161	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	264.50	07/2019 -	-	-	2/4
1162	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	231.39	07/2019 -	-	-	2/4
1163	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	270.13	12/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1164	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.10	07/2019 -	-	-	0/0
1165	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	221.90	07/2019 -	-	-	2/4
1166	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	8.34	05/2020 -	-	-	0/4
1167	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	80.88	-	-	-	0/4
1168	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	178.43	11/2019 -	-	-	2/4
1169	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	112.83	07/2019 -	-	-	2/4
1170	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	202.22	12/2019 -	-	-	0/4
1171	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	75.68	05/2020 -	-	-	0/4
1172	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	317.91	06/2019 -	-	-	0/4
1173	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.22	307.54	101.59	11/2019 -	-	-	0/4
1174	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2018	210.81 -	210.81	12.69	07/2019 -	-	-	0/4
1175	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	199.07	11/2019 -	-	-	0/0
1176	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	105.51	07/2019 -	-	-	0/0
1177	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	115.08	12/2019 -	-	-	0/4
1178	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	26.82	12/2019 -	-	-	0/4
1179	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	146.39	12/2019 -	-	-	0/4
1180	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	129.26	12/2019 -	-	-	0/4
1181	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	117.97	06/2019 -	-	-	0/4
1182	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	114.17	11/2019 -	-	-	0/4
1183	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	139.40	07/2019 -	-	-	0/4
1184	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	247.01	07/2019 -	-	-	0/0
1185	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	108.68	06/2019 -	-	-	0/4
1186	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	255.47	12/2019 -	-	-	0/4
1187	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	35.50	12/2019 -	-	-	0/4
1188	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	125.23	12/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1189	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	96.54	12/2019 -	-	-	0/4
1190	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	142.66	12/2019 -	-	-	0/4
1191	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	93.23	02/2020 -	-	-	0/4
1192	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	128.77	02/2020 -	-	-	0/4
1193	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	95.85	12/2019 -	-	-	0/4
1194	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	186.18	12/2019 -	-	-	0/4
1195	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	186.24	12/2019 -	-	-	0/4
1196	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	149.54	12/2019 -	-	-	1/4
1197	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	158.00	09/2019 -	-	-	1/4
1198	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	02/2018	182.62 -	182.62	132.40	12/2019 -	-	-	2/4
1199	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2017	299.92 300.00	99.92	60.25	08/2020 -	-	-	0/4
1200	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	138.50	12/2019 -	-	-	0/4
1201	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	152.42	08/2020 -	-	-	0/0
1202	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	139.20	12/2019 -	-	-	0/0
1203	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	66.18	08/2020 -	-	-	0/4
1204	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	123.76	12/2019 -	-	-	0/0
1205	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	254.75	12/2019 -	-	-	2/4
1206	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	73.50	12/2019 -	-	-	0/0
1207	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	118.97	06/2020 -	-	-	1/4
1208	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	82.00	12/2019 -	-	-	0/0
1209	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	68.30	12/2019 -	-	-	1/4
1210	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	26.42	12/2019 -	-	-	0/0
1211	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	213.97	12/2019 -	-	-	2/4
1212	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	123.23	05/2020 -	-	-	0/4
1213	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	192.26	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1214	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	124.95	07/2019 -	-	-	0/4
1215	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	113.63	11/2019 -	-	-	0/4
1216	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	-	-	0/0
1217	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	223.97	12/2019 -	-	-	0/4
1218	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	227.93	07/2019 -	-	-	0/4
1219	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 634.30	536.65	531.46	12/2019 12/2020	12/2020	12(O) 0	0/0
1220	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	240.12	07/2019 -	-	-	0/4
1221	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	181.32	12/2019 -	-	-	0/0
1222	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	104.94	03/2019 -	-	-	0/0
1223	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	88.44	87.77	-	-	-	0/0
1224	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	03/2017	264.41 264.00	264.41	70.72	03/2017 -	-	-	0/0
1225	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	22.40	05/2020 -	-	-	0/4
1226	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	103.20	12/2019 -	-	-	1/4
1227	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	213.71	07/2019 -	-	-	0/4
1228	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	409.50	08/2019 -	-	-	0/4
1229	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	180.17	07/2019 -	-	-	0/4
1230	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4
1231	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	137.63	07/2019 -	-	-	0/4
1232	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	189.91	06/2019 -	-	-	2/4
1233	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	147.72	03/2019 -	-	-	0/4
1234	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	22.09	03/2018 -	-	-	0/4
1235	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	7.03	05/2020 -	-	-	0/4
1236	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	120.05	12/2019 -	-	-	0/4
1237	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	111.00	12/2019 -	-	-	0/4
1238	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	149.29	04/2020 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1239	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	362.73	04/2019 -	-	-	0/4
1240	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	127.00	09/2019 -	-	-	2/4
1241	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	57.82	09/2018 -	04/2021	31(O) -	0/4
1242	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	648.90	12/2019 -	-	-	1/4
1243	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	858.91	11/2019 -	-	-	1/4
1244	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	250.31	06/2019 -	-	-	2/4
1245	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	34.80	07/2019 -	-	-	1/4
1246	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	54.83	06/2019 -	-	-	0/4
1247	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.60	07/2019 -	-	-	0/4
1248	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	136.85	02/2019 -	-	-	0/4
1249	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2016	285.60 -	285.60	21.10	11/2019 -	-	-	0/4
1250	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	128.89	06/2019 -	-	-	0/4
1251	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	177.79	06/2019 -	-	-	0/4
1252	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	116.75	06/2019 -	-	-	0/4
1253	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	94.22	06/2019 -	-	-	0/4
1254	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	185.74	06/2019 -	-	-	0/4
1255	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.69	06/2019 -	-	-	0/0
1256	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	188.64	07/2019 -	-	-	0/4
1257	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	137.87	06/2021 -	06/2021	0(O) -	1/4
1258	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	651.15	12/2019 -	-	-	1/4
1259	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	624.61	11/2019 -	-	-	1/4
1260	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	797.60	02/2019 -	-	-	0/0
1261	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	630.05	03/2020 -	-	-	2/4
1262	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	961.51	03/2020 -	-	-	3/5
1263	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	30.42	06/2019 -	-	-	1/4
1264	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	230.97	12/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1265	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 -	313.58	60.09	04/2020 -	-	-	0/4
1266	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	151.85	10/2018 -	10/2021	36(O) -	2/4
1267	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR ,	10/2016	235.31 -	235.31	158.59	11/2020 -	11/2020	-	0/0
1268	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 -	-	-	0/0
1269	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	88.81	- -	09/2021	- -	0/4
1270	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	83.90	05/2019 -	-	-	1/4
1271	WIDENING TO 2 LANE REALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/0 TO KM 114/618 OF NH-44A IN - [N 4000306]MoRTH,MIZORAM , ITEM RATE	11/201	624.41 -	92.67	90.74	03/201 -	02/2021	117(O) -	0/0
1272	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	295.96	10/2010 05/2016	06/2021	128(O) -	0/0
1273	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021	128(O) 0	0/0
1274	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	65.01	09/2019 -	-	-	0/0
1275	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	15.79	09/2019 -	-	-	0/0
1276	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	22.97	09/2019 -	-	-	0/0
1277	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	38.63	09/2019 -	-	-	0/0
1278	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	53.86	09/2019 -	-	-	0/0
1279	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	56.74	09/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1280	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	24.74	09/2019 10/2020	-	-	0/0
1281	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	52.08	09/2019 -	-	-	0/0
1282	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	292.10	09/2014 12/2020	12/2020	75(O) 0	0/0
1283	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	364.59	334.71	12/2009 08/2020	11/2020	-	0/0
1284	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1285	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1286	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105(O) -	0/0
1287	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	03/2011	754.00 -	34.00	2,364.00	03/2011 11/2021	-	-	0/0
1288	DELHI AGRA APPROVED LENGTH 30.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2011	1,928.22 -	2,45.00	2,467.00	04/2011 -	03/2021	71(O) -	3/4
1289	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,547.00	- -	05/2021	- -	0/0
1290	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	-	-	0/0
1291	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0
1292	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1293	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	272.09	08/2016 -	-	-	2/4
1294	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	339.55	267.34	08/2016 -	06/2020	-	2/4
1295	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	340.00	227.18	08/2016 -	-	-	2/4
1296	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	129.13	04/2017 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1297	(I) CONSTRUCTION OF FOUR/SIX LANE FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	240.72	09/2018 -	08/2020	-	1/4
1298	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 336.49	336.49	53.00	09/2018 -	-	-	0/0
1299	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	89.79	09/2018 -	07/2022	46(O) -	0/0
1300	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	58.12	09/2018 -	05/2022	44(O) -	0/4
1301	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	50.62	09/2018 -	09/2022	48(O) -	0/4
1302	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	62.00	09/2018 -	12/2021	39(O) -	0/4
1303	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.04 -	240.04	7.08	09/2018 -	12/2021	39(O) -	0/4
1304	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	79.85	09/2018 -	-	-	1/2
1305	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	92.10	09/2018 -	-	-	0/2
1306	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	192.60	92.97	09/2018 -	-	-	0/2
1307	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	68.26	09/2018 -	11/2021	38(O) -	1/4
1308	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	49.94	09/2018 -	12/2021	39(O) -	1/4
1309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	25.76	09/2018 -	10/2022	49(O) -	0/4
1310	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	28.46	09/2018 -	11/2022	50(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1311	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	98.42	12/2020 -	12/2020	0(O) -	0/0
1312	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	123.44	12/2020 -	12/2020	0(O) -	0/0
1313	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 369.96	336.25	278.10	09/2019 09/2020	-	-	0/0
1314	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	87.30	11/2020 05/2021	11/2020	-	0/0
1315	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	38.85	12/2022 -	12/2022	0(O) -	0/0
1316	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1317	SIX LANING OF CHANDIKOL-JAGTIPUR-BHUBANESWAR - [N24000199]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,47.00	1,74.43	06/2011 03/2021	03/2021	81(O) 0	0/0
1318	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1319	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1320	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1321	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	-	0/0
1322	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	181.52	- -	03/2022	-	0/1
1323	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	-	-	0/0
1324	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	-	-	0/0
1325	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	611.71	- -	01/2021	-	0/0
1326	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	525.68	08/2019 -	03/2021	19(O) -	0/0
1327	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	895.53	- -	06/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1328	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	-	0/0
1329	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1330	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1331	REHABILITATION AND UPGRADE OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1332	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	-	0/0
1333	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1334	REHABILITATION AND UPGRADE BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000647]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00 -	817.80 -	03/2020 -	06/2021 -	15(O) -	0/0
1335	REHABILITATION AND UPGRADE OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56 -	52.10 -	07/2017 -	06/2021 -	47(O) -	0/0
1336	REHABILITATION AND UPGRADE OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	227.63	- -	06/2021	- -	0/0
1337	REHABILITATION AND UPGRADE OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	127.61	- -	06/2021	- -	0/0
1338	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	332.04	- -	03/2022	- -	0/0
1339	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	276.59	- -	06/2021	- -	0/0
1340	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	63.98	- -	-	-	0/1
1341	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	191.40	- -	08/2021	- -	0/0
1342	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	221.00	- -	08/2021	- -	0/1
1343	REHABILITATION AND UPGRADE OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	260.60	- -	06/2021	- -	0/0
1344	REHABILITATION SIX LANING UPGRADE CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1345	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	102.70	- -	06/2021	- -	0/0
1346	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	25.40	- -	06/2021	- -	0/0
1347	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	145.70	- -	04/2021	- -	0/0
1348	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1349	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1350	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1351	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1352	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOLDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1353	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1354	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1355	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB , EPC	12/2015	766.36 -	766.36	685.36	- -	-	-	0/0
1356	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB , EPC	11/2015	847.02 -	847.02	795.00	- -	-	-	0/0
1357	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 -	904.82	739.41	- -	12/2020	- -	0/0
1358	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	456.80	- -	07/2021	- -	0/0
1359	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	746.43	676.33	12/2017 -	-	-	0/0
1360	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- -	-	-	0/0
1361	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	-	0/0
1362	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	2,280.00	1,282.04	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1363	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	330.92	03/2020 -	09/2021	18(O) -	0/0
1364	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	193.26	- -	01/2021	- -	0/0
1365	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	- -	-	-	0/0
1366	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	- -	-	-	0/0
1367	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB ,	03/2018	322.48 -	322.48	260.36	07/2020 -	08/2021	13(O) -	0/0
1368	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB ,	03/2018	173.24 -	173.24	106.35	06/2020 -	-	-	0/0
1369	WIDENING AND PAVED SHOULDER OF TOHANA IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	14.46	08/2020 -	08/2021	12(O) -	0/0
1370	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	663.50	10/2019 -	12/2020	14(O) -	0/0
1371	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0.000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 -	170.57	34.68	11/2020 -	05/2021	6(O) -	0/0
1372	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	-	-	0/0
1373	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	237.13	08/2020 -	-	-	0/0
1374	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1375	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1376	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1377	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1378	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH, RAJASTHAN , EPC	02/2015	383.40 -	383.40	244.68	03/2015 -	-	-	0/0
1379	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH, RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.22	06/2018 -	-	-	0/4
1380	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 -	-	-	0/0
1381	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN ,	10/2015	597.00 -	597.00	587.64	10/2017 -	11/2020	-	3/4
1382	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1383	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	1,688.16	04/2018 -	-	-	0/0
1384	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANNING WITH PAVED SHOULDER A - [N24000467]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1385	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	-	-	0/4
1386	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1387	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPA - DHOLPUR - [N24000520]NHAI, RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	-	-	-	0/0
1388	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1389	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	191.80	06/2019 -	-	-	1/1
1390	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN ,	06/2016	649.00 -	649.00	543.83	06/2019 -	-	-	0/0
1391	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN ,	07/2016	688.70 -	688.70	880.00	-	-	-	0/0
1392	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1393	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,727.66	1,672.28	-	01/2021	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1394	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,265.00	- -	02/2021	- -	0/0
1395	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	- -	0/0
1396	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	795.00	04/2020 -	03/2021	11(O) -	0/0
1397	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	704.61	10/2017 -	11/2020	-	0/0
1398	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	293.43	- -	12/2020	- -	0/0
1399	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	673.70	- -	09/2020	-	0/0
1400	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH-58 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	88.91	- -	-	-	0/0
1401	CONSTRUCTION/ UP-GRADATION OF 2 LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	03/2018	716.76 -	716.76	610.56	- -	-	-	0/0
1402	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	886.59	- -	-	-	0/0
1403	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	611.28	- -	-	-	0/0
1404	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	112.47	04/2018 -	-	-	2/4
1405	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35(O) -	3/4
1406	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	266.58	06/2018 -	04/2021	34(O) -	1/4
1407	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	192.06	05/2018 -	06/2021	37(O) -	1/4
1408	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	110.91	- -	03/2021	- -	0/0
1409	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	.00	08/2022 -	08/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1410	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	.00	08/2020 -	08/2020	-	0/0
1411	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	.00	11/2020 -	11/2020	-	0/0
1412	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM ,	04/2013	151.59 370.01	151.59	282.36	08/2013 12/2020	12/2020	88(O) 0	0/0
1413	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM , ITEM RATE	04/2013	166.27 359.92	166.27	243.59	08/2013 12/2020	12/2020	88(O) 0	0/0
1414	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM , ITEM RATE	01/2013	182.28 369.64	269.14	274.06	02/2013 12/2020	12/2020	94(O) 0	0/0
1415	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	241.07	10/2017 -	-	-	3/4
1416	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	66.63	11/2017 -	-	-	2/4
1417	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.30 -	75.80	95.44	-	-	-	1/4
1418	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	24.70	11/2017 -	-	-	1/4
1419	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1420	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,337.05	12/2013 -	-	-	0/0
1421	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	.00	06/2013 -	10/2020	-	0/0
1422	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	45.26	05/2013 -	05/2021	96(O) -	0/0
1423	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	8.56	04/2014 -	-	-	0/0
1424	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	223.10	08/2015 -	-	-	0/0
1425	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1426	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	140.64	08/2015 -	-	-	0/0
1427	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	-	-	0/0
1428	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	-	-	0/0
1429	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1430	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1431	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	415.67	08/2018 -	12/2020	28(O) -	0/0
1432	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	390.36	07/2018 -	12/2020	29(O) -	0/0
1433	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 - 932.23	848.45	209.77	03/2020 -	02/2021	11(O) -	0/0
1434	FOUR LANING OF VILLUKURI KANYAKUMARI ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2017	641.17 -	641.17	390.36	07/2018 -	11/2020	-	0/0
1435	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	425.56	08/2017 -	02/2021	42(O) -	0/0
1436	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	182.00	09/2017 -	-	-	0/0
1437	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	549.62	09/2017 -	09/2021	48(O) -	0/0
1438	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	182.58	-	-	-	0/0
1439	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	268.34	-	07/2021	-	0/0
1440	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	240.60	-	05/2021	-	0/0
1441	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	284.33	-	09/2021	-	0/0
1442	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	-	-	-	0/0
1443	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	273.52	-	07/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1444	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	-	-	0/0
1445	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU ,	03/2019	297.55 -	297.55	45.52	11/2019 -	-	-	0/0
1446	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU ,	01/2016	162.72 -	162.72	136.46	09/2016 -	-	-	0/0
1447	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]MoRTH,TAMIL NADU ,	05/2016	307.70 -	307.70	312.82	01/2017 -	-	-	0/0
1448	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 -	240.38	74.56	06/2019 -	-	-	0/0
1449	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0
1450	REHABILITATION AND UPGRADE OF NH-56 FROM KM 1.00 TO 86.057 NAKREKIL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2011	270.50 -	270.00	1.84	03/2011 -	-	-	1/4
1451	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0
1452	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	897.03	956.62	11/2018 07/2019	01/2021	26(O) 1	0/0
1453	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1454	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	272.08	- -	-	-	0/0
1455	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	461.90	- -	-	-	0/0
1456	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	11.43	- -	-	-	0/0
1457	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1458	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	112.13	02/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1459	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	112.80	03/2019 -	-	-	0/0
1460	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	146.06	05/2019 -	-	-	0/0
1461	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	103.22	10/2019 -	-	-	0/0
1462	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	187.73	12/2019 -	-	-	0/0
1463	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	288.00	05/2019 -	-	-	0/0
1464	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	148.46	05/2019 -	-	-	0/0
1465	6 LANING FROM KM 9.90 TO KM 19.948 (AP.MGAH + SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2017	283.15 -	83.15	82.57	05/2020 -	-	-	0/0
1466	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	205.96	12/2019 -	-	-	0/0
1467	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA ,	02/2018	206.13 -	206.13	168.15	06/2020 -	-	-	0/0
1468	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA ,	02/2018	294.13 -	294.13	90.20	11/2019 -	-	-	0/0
1469	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA ,	02/2018	220.28 -	220.28	103.85	11/2019 -	-	-	0/0
1470	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA ,	02/2018	426.52 -	426.52	376.33	04/2020 -	-	-	0/0
1471	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA ,	03/2018	322.81 -	322.81	77.17	09/2020 -	-	-	0/0
1472	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA ,	03/2018	626.76 -	626.76	154.52	07/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1473	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA ,	01/2017	605.08 -	605.08	389.46	10/2019 -	-	-	0/0
1474	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA ,	03/2018	192.67 -	192.67	137.66	07/2019 -	-	-	0/0
1475	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA ,	01/2019	193.19 -	193.19	41.81	- -	-	-	0/0
1476	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	357.19	03/2018 -	-	-	3/4
1477	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA ,	10/2016	171.90 -	171.90	96.21	08/2020 -	-	-	0/0
1478	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1479	2-LANING WITH PS RAIBARELI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.26 - 465.31	460.21	459.07	01/2014 - 12/2020	12/2020	83(O) 0	0/0
1480	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,573.00 -	1,730.00	2,091.25	09/2011 -	-	-	0/0
1481	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1482	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1483	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 - 417.68	417.68	433.68	01/2016 - 12/2020	12/2020	59(O) 0	0/0
1484	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	239.04	09/2016 -	-	-	0/0
1485	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 - 627.93	627.93	633.24	01/2016 - 01/2020	01/2020	-	0/0
1486	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	-	-	0/0
1487	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1488	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1489	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1490	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1491	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1492	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1493	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1494	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	128.54	08/2015 -	-	-	0/0
1495	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	987.94	867.27	- -	-	-	0/2
1496	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,057.60	542.52	06/2019 -	-	-	0/0
1497	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	977.26	04/2019 -	-	-	0/0
1498	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	- -	-	-	0/0
1499	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1500	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.30 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,082.00	276.51	04/2019 -	-	-	0/0
1501	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	641.51	04/2019 -	-	-	0/0
1502	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	08/2020	-	0/0
1503	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	-	-	0/0
1504	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	-	-	0/0
1505	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1506	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	-	-	0/0
1507	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1508	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	974.57	03/2020 -	11/2020	-	2/4
1509	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,039.23	03/2020 -	-	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1510	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	683.51	03/2020 -	12/2020	9(O) -	0/0
1511	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	-	0/0
1512	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	672.82	- -	12/2020	- -	0/0
1513	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	43.23	- -	12/2020	- -	0/0
1514	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1515	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1516	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DAGAMAPUR (PKG-I) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	70.50	09.66	- -	-	-	0/0
1517	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	469.16	- -	-	-	0/0
1518	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	951.37	- -	-	-	0/0
1519	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	- -	0/0
1520	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,344.09	- -	-	-	0/0
1521	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,072.92	- -	-	-	0/0
1522	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	431.34	- -	-	-	0/0
1523	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	541.77	- -	-	-	0/0
1524	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1525	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	65.83	- -	09/2021	- -	0/0
1526	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH ,	03/2016	208.50 -	208.50	164.97	11/2019 -	11/2020	-	0/0
1527	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	120.69	03/2020 -	-	-	0/0
1528	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	160.61	09/2019 -	-	-	0/0
1529	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	199.35	01/2020 -	03/2021	14(O) -	0/0
1530	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	141.11	10/2018 -	-	-	0/0
1531	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH ,	10/2016	445.39 653.00	53.29	469.64	07/2019 -	-	-	0/0
1532	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	139.00	08/2015 -	11/2020	-	0/0
1533	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	182.51	05/2019 -	12/2020	19(O) -	0/0
1534	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - [N24001147]MoRTH,UTTAR PRADESH ,	10/2016	239.63 -	239.63	212.53	02/2019 -	-	-	0/0
1535	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH ,	03/2016	599.34 -	599.34	492.15	01/2020 -	-	-	0/0
1536	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	1,200.52	01/2019 -	-	-	0/0
1537	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH ,	03/2016	388.83 -	388.83	304.70	12/2019 -	-	-	0/0
1538	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	112.47	03/2020 -	11/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1539	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	143.96	10/2019 -	12/2020	14(O) -	0/0
1540	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH ,	12/2016	209.10 -	209.10	195.83	10/2019 -	04/2020	-	0/0
1541	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	181.10	04/2020 -	04/2021	12(O) -	0/0
1542	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	115.87	02/2020 -	11/2020	-	0/0
1543	FOUR LANE WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	83.53	08/2020 -	03/2021	7(O) -	0/0
1544	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	141.54	09/2020 -	02/2021	5(O) -	0/0
1545	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	190.00	-	-	-	0/0
1546	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	0.00	-	-	-	0/0
1547	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	2.36	12/2020 -	12/2020	0(O) -	0/0
1548	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	12/2020	86(O) -	0/0
1549	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	348.16	-	-	-	0/0
1550	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	-	08/2020	-	0/0
1551	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 -	-	-	0/0
1552	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	48.22	05/2018 -	-	-	1/4
1553	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	112.31	06/2018 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1554	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	128.27	05/2018 -	-	-	1/4
1555	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	-	-	0/0
1556	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	-	-	0/0
1557	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	-	-	0/0
1558	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	-	-	0/0
1559	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	-	-	0/0
1560	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	-	-	0/0
1561	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	-	-	0/0
1562	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	-	-	0/0
1563	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	-	-	-	0/0
1564	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	-	-	0/0
1565	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	-	-	-	0/0
1566	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	196.35	07/2018 -	-	-	1/5
1567	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	-	-	0/0
1568	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,239.99	08/2013 -	05/2021	93(O)	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1569	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,852.94	08/2013 -	12/2021	100(O) -	3/4
1570	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	-	-	0/0
1571	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1572	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	363.93	272.98	- -	-	-	0/0
1573	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	12/2020	30(O) -	0/0
1574	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 2,360.65	2,360.65	4,472.01	- -	-	-	0/0
1575	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	130.72	11/2018 -	-	-	0/0
1576	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	604.65	08/2018 -	-	-	0/0
1577	CONSTRUCTION OF MECHHAR BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	02/2017	158.25 -	50.05	10.03	06/2018 -	-	-	0/0
1578	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
1579	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]MoRTH, WEST BENGAL ,	08/2014	600.87 720.97	720.97	682.36	11/2017 05/2019	05/2019	-	0/0
1580	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]MoRTH, WEST BENGAL ,	08/2014	823.20 937.76	937.76	807.93	11/2017 06/2019	06/2019	-	0/0
1581	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	242.95	09/2019 11/2020	05/2021	20(O) 0	0/0
1582	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH, WEST BENGAL ,	03/2017	202.69 202.69	202.69	144.43	11/2019 -	-	-	0/0
1583	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15(O) -	0/0
1584	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	90.68	11/2020 04/2020	04/2021	5(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1585	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH,WEST BENGAL ,	03/2018	254.30 254.30	254.30	78.32	10/2020 -	03/2021	5(O) -	0/0
1586	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL ,	03/2016	160.27 213.97	213.97	24.14	08/2019 -	11/2022	39(O) -	0/0
1587	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28(O) -	0/0
1588	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL ,	04/2014	279.70 398.52	398.52	330.94	08/2017 01/2020	02/2020	-	0/0
	Total		5,08,495.62 -	5,27,475.09	3,40,295.62				345/1082
	<u>SHIPPING AND PORTS</u>								
1589	JAL MARG VIKAS PROJECT - [N25000072]JWAI,MULTI STATE ,	01/2011	5,365.18 -	4,333.81	1,787.23	07/2021 03/2021	03/2021	0(O) -	0/0
	Total		5,365.18 -	4,333.81	1,787.23				0/0
	<u>TELECOMMUNICATIONS</u>								
1590	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,DELHI ,	12/2005	249.00 -	229.41	.00	02/2007 -	-	-	0/0
1591	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,DELHI ,	02/2006	229.41 -	229.41	.00	03/2012 -	-	-	0/0
1592	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	80.10	03/2018 12/2020	12/2020	33(O) 0	0/0
1593	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,MAHARASHTRA ,	01/2006	247.00 -	247.00	.00	02/2007 -	-	-	0/0
1594	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]DOT,MULTI STATE ,	05/2006	1,077.00 -	1,077.00	.00	03/2009 -	-	-	0/0
1595	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	15,239.00	07/2015 -	06/2021	71(O) -	0/0
1596	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
1597	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE , Central Sector Projects	03/2020	431.16 431.00	431.16	.00	06/2021 -	11/2021	5(O) -	0/0
	Total		17,926.94 -	29,137.35	15,573.00				0/70
	<u>URBAN DEVELOPMENT</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1598	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1599	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR ,	02/2019	13,365.77 -	13,365.77	271.17	06/2024 -	06/2024	0(O) -	0/0
1600	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5) SHOPS CO - [N28000149]CPWD,CHHATISGARH ,	05/2019	299.97 -	299.97	.29	09/2020 -	-	-	0/0
1601	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	39,843.96	03/2016 -	03/2021	60(O) -	0/0
1602	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 884.30	884.30	812.00	12/2015 12/2020	12/2020	60(O) 0	0/0
1603	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 4,720.73	4,720.73	4,683.08	11/2019 11/2020	11/2020	-	3/7
1604	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	94.18	04/2019 06/2021	06/2021	26(O) 0	1/2
1605	REDEVELOPMENT OF GPRA COLONY AT NAUQOLI NAGAR - [N28000105]NBCC,DELHI ,	01/2011	2,694.00 -	2,394.00	553.50	- -	03/2022	- -	0/9
1606	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2011	238.56 -	38.56	157.67	05/2021 02/2021	02/2021	9(O) 1	1/2
1607	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	28.26	03/2021 07/2021	07/2021	4(O) 0	0/0
1608	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	63.67	08/2020 -	12/2021	16(O) -	0/0
1609	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	126.16	11/2020 -	11/2020	-	0/2
1610	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASपुरI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 -	1,100.80	34.82	07/2021 -	09/2021	2(O) -	0/0
1611	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022	0(O) -	0/0
1612	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	965.60	03/2025 -	03/2025	0(O) -	0/0
1613	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	503.33	12/2020 -	09/2021	9(O) -	0/0
1614	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI ,	02/2020	532.00 -	532.00	102.00	11/2020 02/2021	11/2020	-	0/0
1615	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	8,276.69	12/2018 -	11/2022	47(O) -	0/0
1616	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	30.02	03/2024 -	03/2024	0(O) -	0/0
1617	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	14.89	03/2024 -	03/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1618	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	.00	09/2025 -	05/2024	-16(O) -	0/0
1619	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	-	-	0/28
1620	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 6,218.14	6,218.14	6,031.09	07/2017 09/2020	09/2020	-	0/0
1621	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	114.13	02/2023 -	02/2023	0(O) -	0/0
1622	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	112.78	02/2023 -	02/2023	0(O) -	0/0
1623	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	7,068.52	03/2018 -	-	-	0/0
1624	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	-	-	0/0
1625	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	5,234.40	11/2021 -	11/2021	0(O) -	0/0
1626	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	2,467.77	06/2025 -	06/2025	0(O) -	0/0
1627	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	03/2009	14,600.00 -	19,050.00	16,352.87	12/2015 -	-	-	12/24
1628	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2011	3,770.00 -	3,770.00	2,750.00	03/2011 12/2020	12/2020	33(O) 0	5/21
1629	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1630	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	.00	03/2024 -	03/2024	0(O) -	0/0
1631	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	.00	03/2024 -	03/2024	0(O) -	0/0
1632	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0
	Total		2,84,575.18 -	2,92,612.80	99,751.53				22/95
	<u>WATER RESOURCES</u>								
1633	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	16,568.13	03/2020 11/2021	04/2022	25(O) 4	0/19
1634	IRRIGATION WORK OF BAGMATI - [N12000108]HSLC,BIHAR ,	10/2005	956.00 -	721.37	712.37	03/2015 -	03/2021	72(O) -	5/7
1635	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	37.09	07/2021 -	07/2021	0(O) -	0/0
1636	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	254.13	.05	09/2020 -	-	-	0/0
1637	I AND D AND STP AT CHAPPRRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	12.06	12/2020 -	12/2020	0(O) -	0/0
1638	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	.00	08/2021 -	12/2021	4(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1639	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1640	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	225.77	249.54	03/2020 -	12/2020	9(O) -	0/0
1641	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR ,	04/2015	184.93 -	184.93	163.36	04/2020 -	12/2020	8(O) -	0/0
1642	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	254.50	01/2021 -	01/2021	0(O) -	0/0
1643	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	79.54	04/2021 -	04/2021	0(O) -	0/0
1644	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR ,	05/2017	184.86 -	184.86	131.43	05/2021 -	05/2021	0(O) -	0/0
1645	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	43.01	11/2020 -	12/2020	1(O) -	0/0
1646	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	111.10	05/2021 -	05/2021	0(O) -	0/0
1647	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	.29	06/2022 -	06/2022	0(O) -	0/0
1648	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	.42	06/2022 -	06/2022	0(O) -	0/0
1649	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10 MG/L - [N30000014]DJB,DELHI ,	03/2016	665.78 -	665.78	12.56	12/2021 -	12/2021	0(O) -	0/0
1650	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	50.75	12/2021 -	12/2022	12(O) -	0/0
1651	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	73.13	02/2022 -	12/2022	10(O) -	0/0
1652	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	278.37	01/2021 -	06/2021	5(O) -	0/0
1653	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1654	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	-	-	0/0
1655	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	32.47	09/2021 -	09/2021	0(O) -	0/0
1656	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH ,	03/2018	904.00 -	904.00	38.38	09/2021 -	09/2021	0(O) -	0/0
1657	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 -	213.62	.00	03/2022 -	03/2022	0(O) -	0/0
1658	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH ,	10/2016	370.40 -	370.40	323.09	08/2020 -	12/2020	4(O) -	0/0
1659	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	14.64	09/2021 -	09/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1660	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH ,	02/2017	161.31 -	161.31	50.65	11/2019 -	12/2020	13(O) -	0/0
1661	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UPJalNigam,UTTAR PRADESH ,	12/2018	857.26 -	842.25	.00	08/2021 -	06/2022	10(O) -	0/0
1662	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	0(O) -	0/0
1663	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	87.15	12/2020 -	01/2021	1(O) -	0/0
1664	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 -	279.91	222.79	12/2019 -	12/2020	12(O) -	0/0
1665	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	.00	12/2021 -	12/2021	0(O) -	0/0
1666	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	5.16	10/2021 -	10/2021	0(O) -	0/0
1667	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]UPJalNigam,UTTAR PRADESH ,	02/2019	317.19 -	17.19	.00	08/2021 -	08/2021	0(O) -	0/0
1668	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	681.78	.00	06/2022 -	06/2022	0(O) -	0/0
1669	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 -	298.12	.00	07/2021 -	06/2022	11(O) -	0/0
1670	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND ,	03/2017	273.37 -	273.37	71.53	08/2019 -	-	-	0/0
1671	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	.00	11/2019 -	-	-	0/0
1672	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(O) -	0/0
1673	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(O) -	0/0
1674	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(O) -	0/0
1675	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 -	198.43	.00	02/2022 -	02/2022	0(O) -	0/0
1676	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(O) -	0/0
1677	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1678	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 -	160.00	.00	02/2022 -	02/2022	0(O) -	0/0
1679	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	.00	12/2021 -	12/2021	0(O) -	0/0
1680	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	189.36	12/2019 -	12/2020	12(O) -	0/0
1681	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	202.18	04/2020 -	12/2020	8(O) -	0/0
1682	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	.00	12/2021 -	12/2021	0(O) -	0/0
1683	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	.00	12/2021 -	12/2021	0(O) -	0/0
	Total		27,955.51 -	73,105.94	20,164.30				5/26
	<u>DEFENCE PRODUCTION</u>								
1684	RESIDENTIAL QUARTERS FOR HALDANGLORE - [N28000103]CPWD, KARNATAKA ,	10/2010	246.31 -	46.31	115.20	02/2022 - 06/2021	06/2021	16(O) 3	6/10
	Total		246.31 -	46.31	115.20				6/10
	<u>COMMERCE AND INDUSTRY</u>								
1685	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC, DELHI ,	11/2017	4,773.00 -	5,178.00	2,334.57	12/2019 -	07/2021	19(O) -	0/0
1686	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC, DELHI ,	06/2018	302.64 -	302.64	60.00	10/2020 -	10/2020	-	0/0
1687	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC, MULTI STATE ,	09/2011	12,579.09 -	13,812.30	7,305.07	09/2019 01/2014	07/2021	22(O) 0	0/0
	Total		17,654.73 -	19,292.94	9,699.64				0/0
	Grand Total		21,44,627.66	25,72,670.28	12,17,692.37				2867/5606


Summary of projects in the Flash Report for the month of December, 2020

Project Implementation - Current Status:

Number of Projects in Previous Month	1671
Number of Projects completed/dropped/frozen in Current Month	6
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	21
Number of Projects in Current Month	1687

Brief Analysis

Project Status with respect to Original Schedule: Out of 1687 projects, 11 projects are ahead of schedule, 195 projects are on schedule, 558 projects are delayed. 794 projects do not have fixed dates of commissioning. 129 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

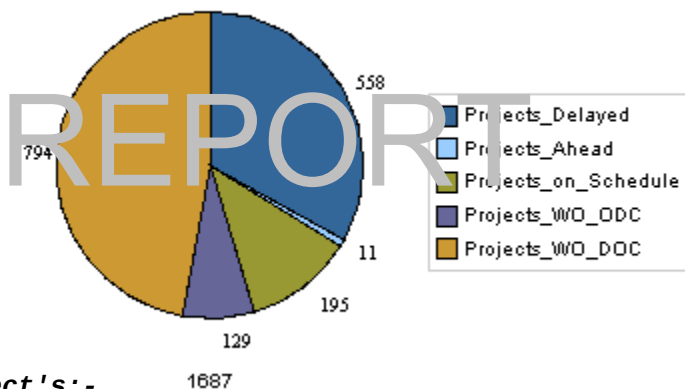


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1687 projects when sanctioned, was of the order of Rs. 2144627.66 crore but this was subsequently revised to Rs. 2572670.28 crore implying a cost overrun of 20%. The expenditure incurred on these projects till December, 2020 is Rs. 1217692.37 crore, which is 47.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

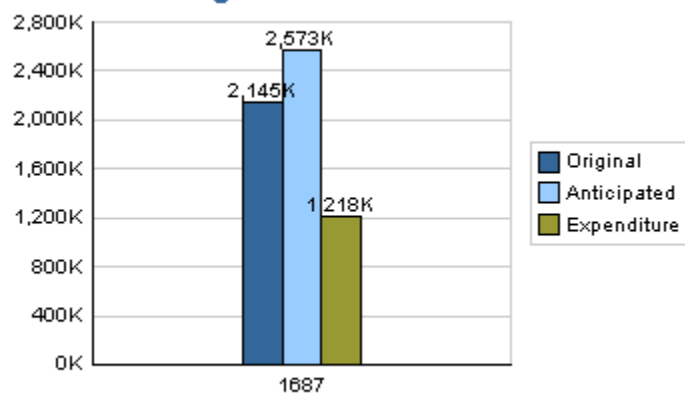

Sector wise current status of projects on the Flash Report

CULTURE DEVELOPMENT


Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

FLASH REPORT

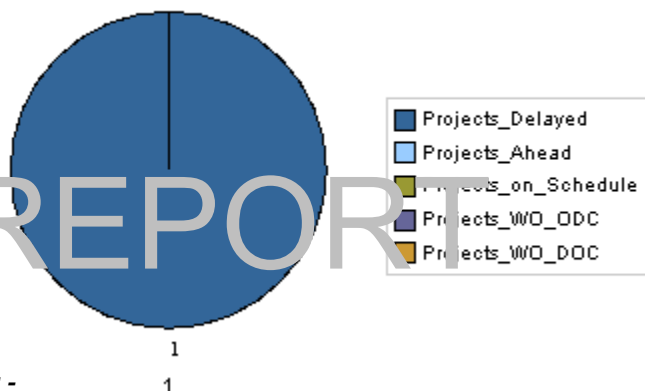


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 151.33 crore but this was subsequently anticipated to Rs. 151.33 crore. The expenditure incurred on these projects till December, 2020 is Rs. 144 crore, which is 95.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

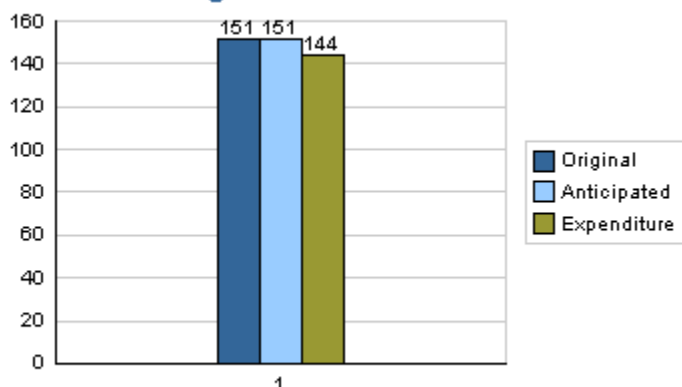

Sector wise current status of projects on the Flash Report


RURAL DEVELOPMENT

Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 3 projects are delayed.

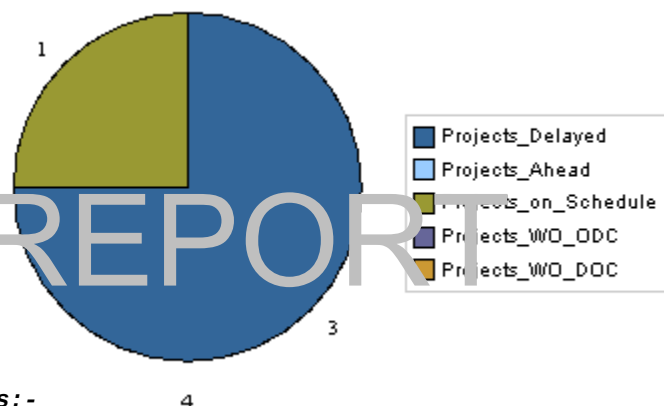


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 889.43 crore but this was subsequently anticipated to Rs. 899.87 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till December, 2020 is Rs. 472.05 crore, which is 52.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

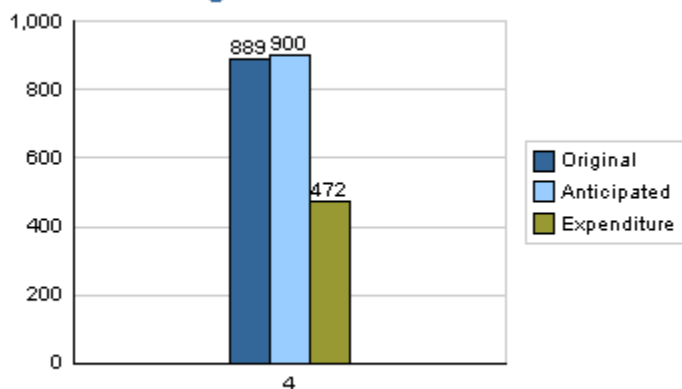

Sector wise current status of projects on the Flash Report


HOME AFFAIRS

Current Status:

Number of Projects	3
Number of Projects On Schedule	1
Number of Projects Delayed	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 1 project is on schedule 2 projects are delayed.

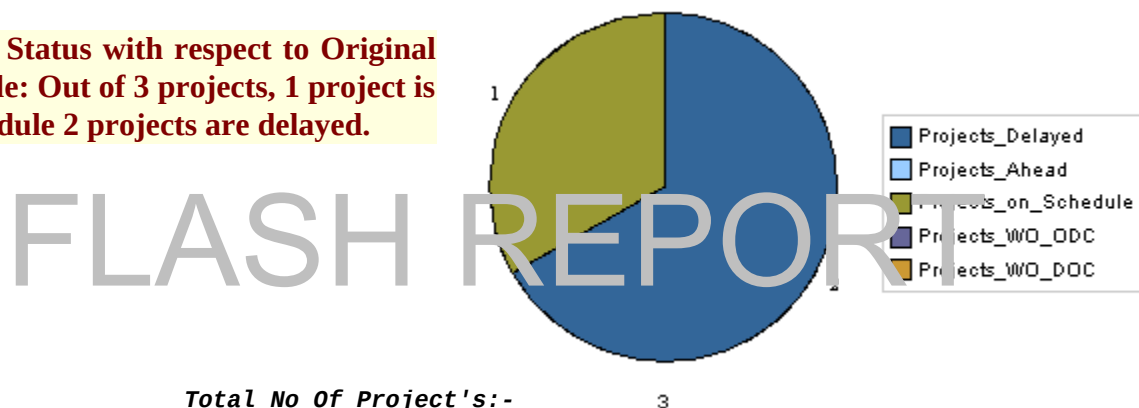

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 1549.07 crore but this was subsequently anticipated to Rs. 2346.14 crore implying a cost overrun of 51.5%. The expenditure incurred on these projects till December, 2020 is Rs. 1010.33 crore, which is 43.1% of the anticipated cost of the projects.

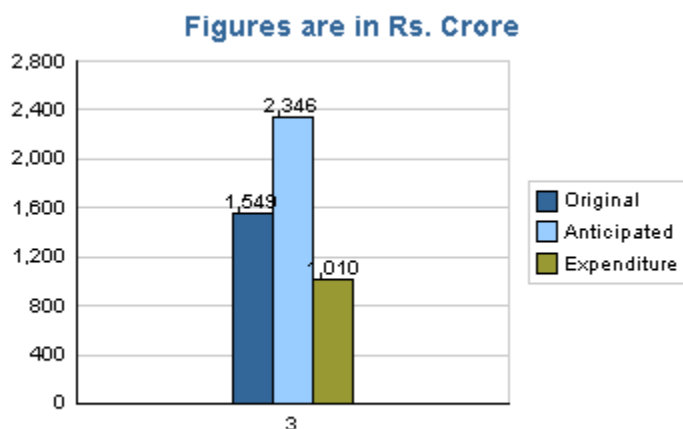

Sector wise current status of projects on the Flash Report

HUMAN RESOURCE DEVELOPMENT


Current Status:

Number of Projects	25
Number of Projects On Schedule	4
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	7
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 25 projects, 4 projects are on schedule 14 projects are delayed. 7 projects do not have fixed dates of commissioning.

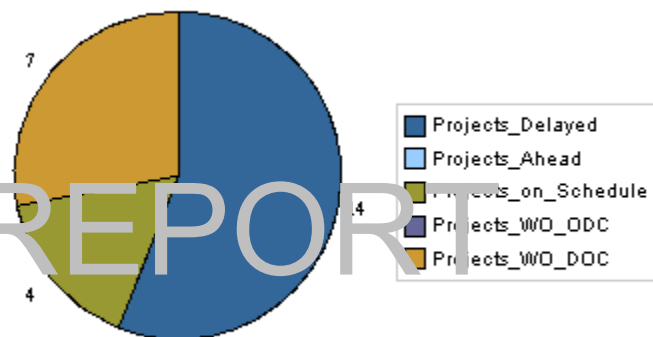


Total No Of Project's:-

25

Investment Scenario

Total original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 10702.4 crore but this was subsequently anticipated to Rs. 10890.83 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till December, 2020 is Rs. 2263.19 crore, which is 20.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

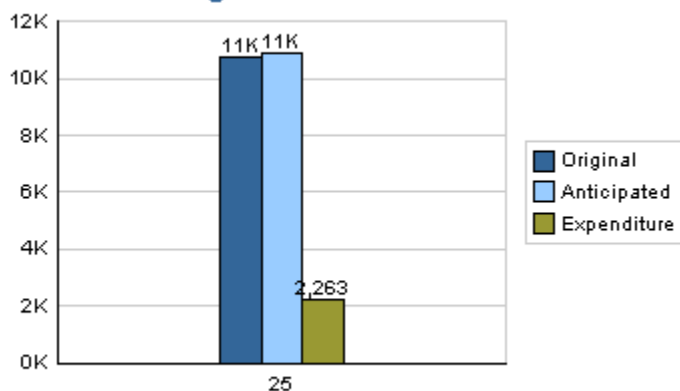

Sector wise current status of projects on the Flash Report


COMMERCE AND INDUSTRY

Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed. 1 project does not have fixed dates of commissioning.

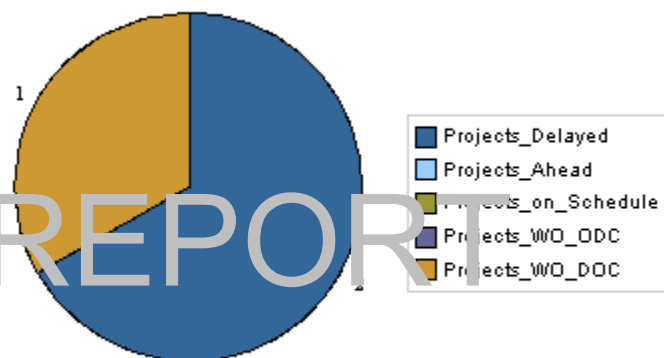


Total No Of Project's:-

3

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 17654.73 crore but this was subsequently anticipated to Rs. 19292.94 crore implying a cost overrun of 9.3%. The expenditure incurred on these projects till December, 2020 is Rs. 9699.64 crore, which is 50.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

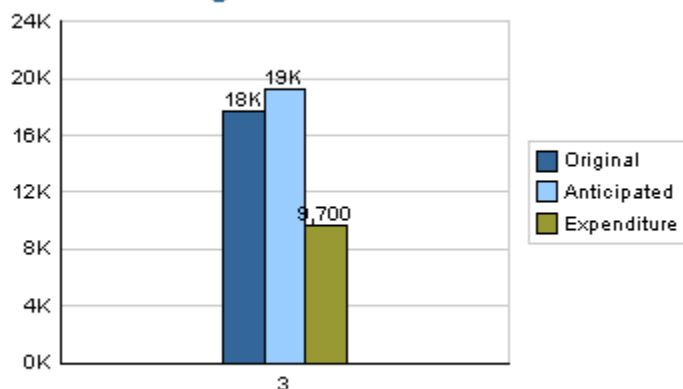

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

FLASH REPORT

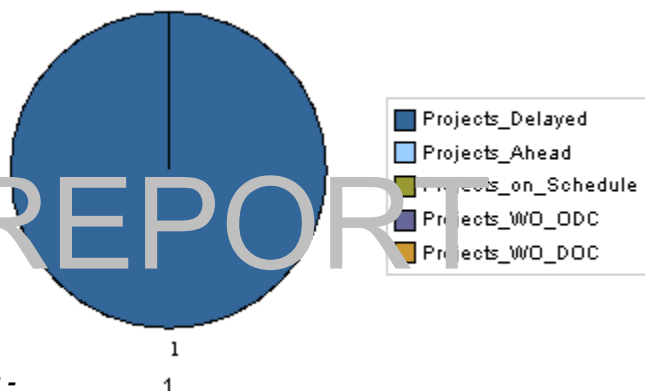


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 246.31 crore but this was subsequently anticipated to Rs. 246.31 crore. The expenditure incurred on these projects till December, 2020 is Rs. 115.2 crore, which is 46.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

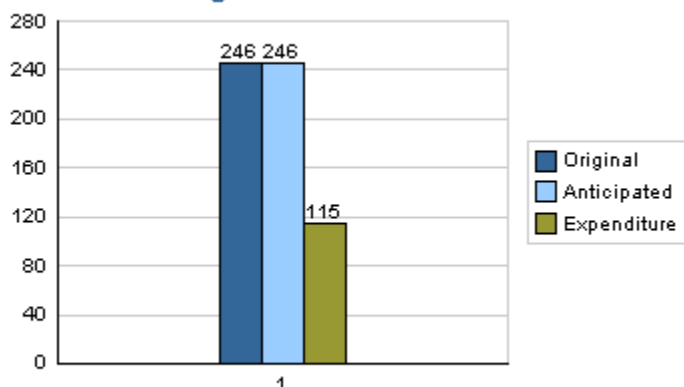

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	51
Number of Projects On Schedule	29
Number of Projects Delayed	17

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 51 projects, 29 projects are on schedule 17 projects are delayed. 5 projects do not have fixed dates of commissioning.

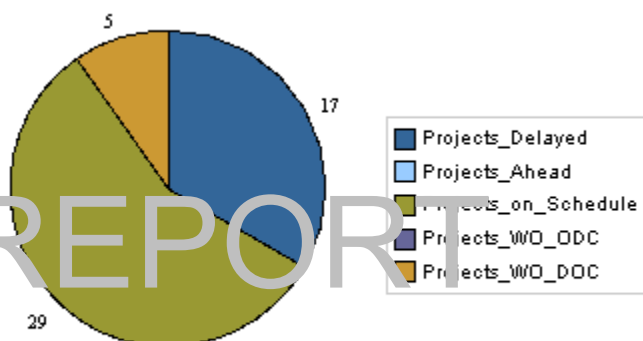


Total No Of Project's:-

51

Investment Scenario

Total original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 27955.51 crore but this was subsequently anticipated to Rs. 73105.94 crore implying a cost overrun of 161.5%. The expenditure incurred on these projects till December, 2020 is Rs. 20164.3 crore, which is 27.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

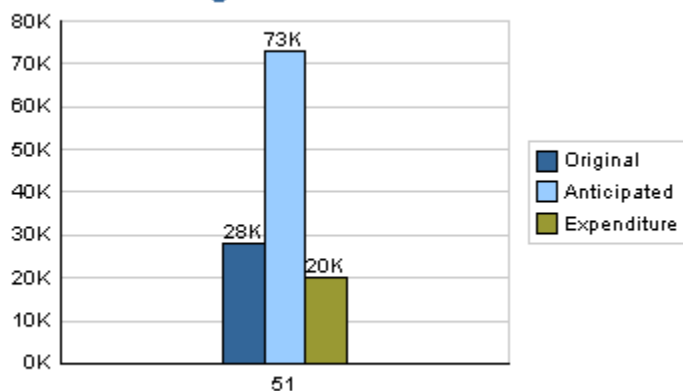

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	35
Number of Projects On Schedule	11
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	12

Brief Analysis

Project Status with respect to Original Schedule: Out of 35 projects, 1 project is ahead of schedule, 11 projects are on schedule 10 projects are delayed. 12 projects do not have fixed dates of commissioning 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

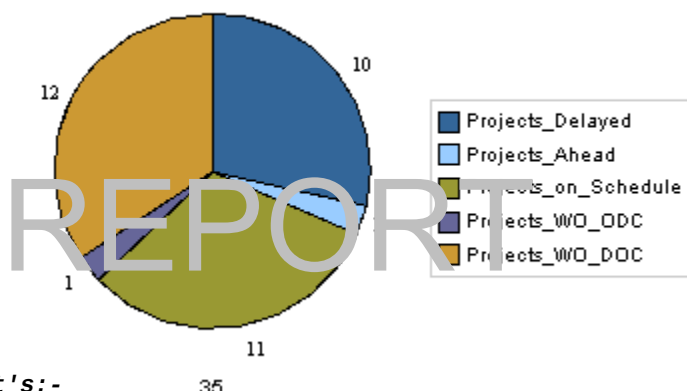


Total No Of Project's:-

35

Investment Scenario

Total original cost of implementation of 35 projects when sanctioned, was of the order of Rs. 284575.18 crore but this was subsequently anticipated to Rs. 292612.8 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till December, 2020 is Rs. 99751.53 crore, which is 34.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

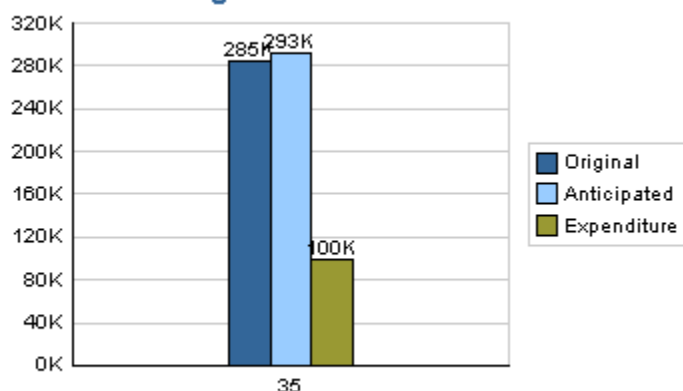

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:


Number of Projects **8**

Number of Projects Delayed **3**

Number of Projects Without Date Of Commissioning **5**

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are delayed. 5 projects do not have fixed dates of commissioning.

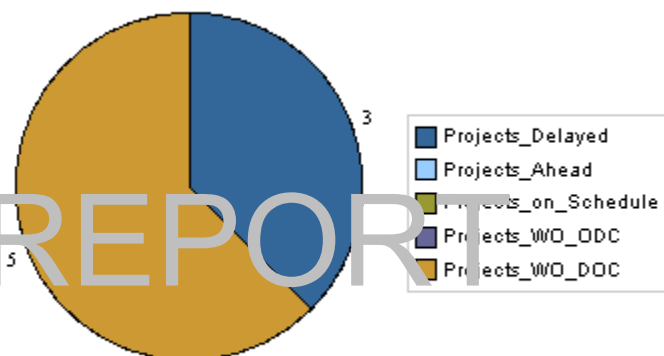


Total No Of Project's:-

8

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 17926.94 crore but this was subsequently anticipated to Rs. 29137.35 crore implying a cost overrun of 62.5%. The expenditure incurred on these projects till December, 2020 is Rs. 15573 crore, which is 53.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

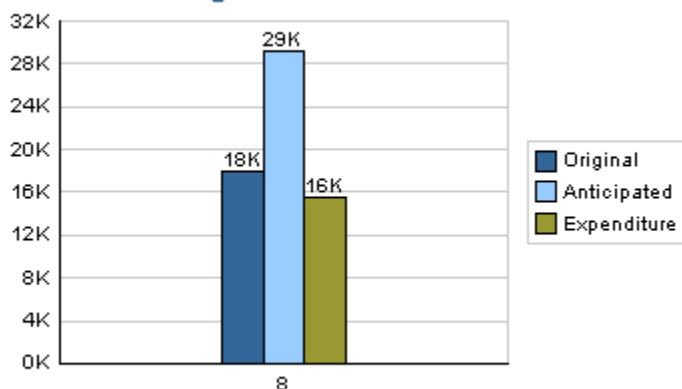

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule

FLASH REPORT




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 5369.18 crore but this was subsequently anticipated to Rs. 4633.81 cr The expenditure incurred on these projects till December, 2020 is Rs. 1787.23 crore, which is 38.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

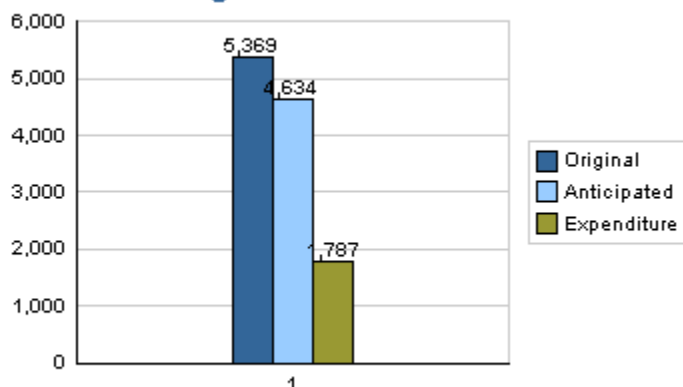

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	858
Number of Projects On Schedule	11
Number of Projects Delayed	146

Number of Projects Without Original Date of Commissioning	70
Number of Projects Without Date Of Commissioning	631

Brief Analysis

Project Status with respect to Original Schedule: Out of 858 projects, 11 projects are on schedule 146 projects are delayed. 631 projects do not have fixed dates of commissioning 70 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

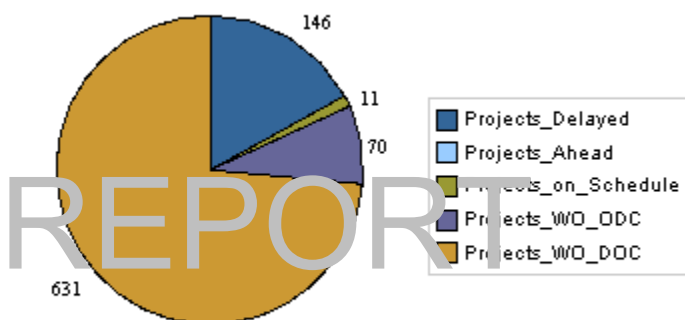


Total No Of Project's:-

858

Investment Scenario

Total original cost of implementation of 858 projects when sanctioned, was of the order of Rs. 508495.62 crore but this was subsequently anticipated to Rs. 527475.09 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till December, 2020 is Rs. 340295.62 crore, which is 64.5% of the anticipated cost of the projects.

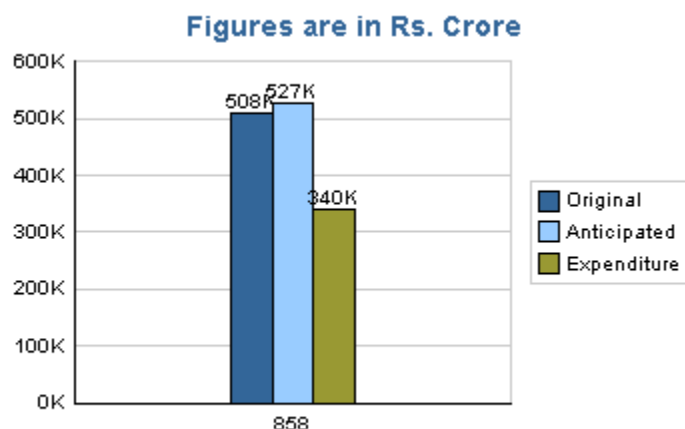

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	311
Number of Projects On Schedule	18
Number of Projects Delayed	159
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	49
Number of Projects Without Date Of Commissioning	78

Brief Analysis

Project Status with respect to Original Schedule: Out of 311 projects, 7 projects are ahead of schedule, 18 projects are on schedule 159 projects are delayed. 78 projects do not have fixed dates of commissioning 49 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

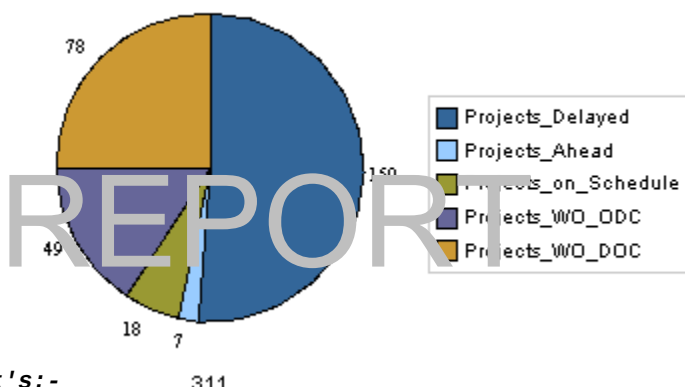


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 311 projects when sanctioned, was of the order of Rs. 461691.03 crore but this was subsequently anticipated to Rs. 698197.39 crore implying a cost overrun of 51.2%. The expenditure incurred on these projects till December, 2020 is Rs. 237960.69 crore, which is 34.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

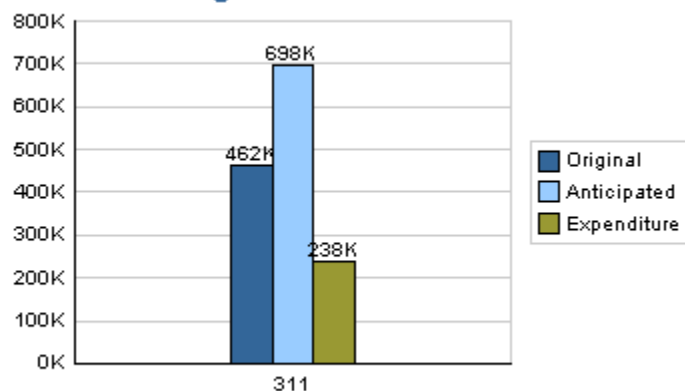

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	28
Number of Projects On Schedule	3
Number of Projects Delayed	14

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 3 projects are on schedule 14 projects are delayed. 5 projects do not have fixed dates of commissioning, 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

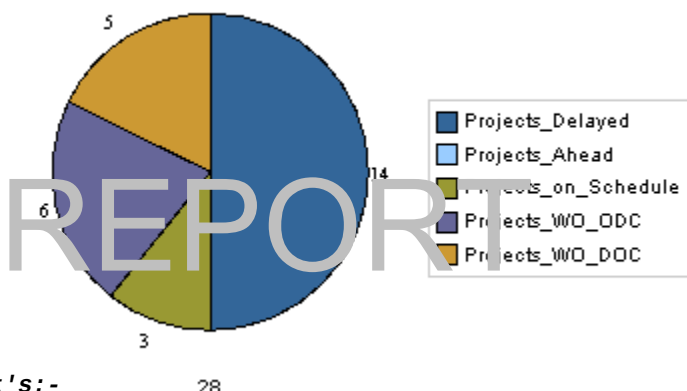


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 13445.26 crore but this was subsequently anticipated to Rs. 13766.81 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till December, 2020 is Rs. 7113.51 crore, which is 51.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

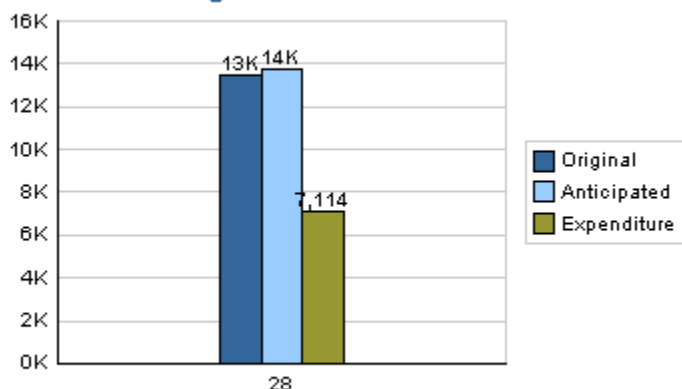

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY


Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

FLASH REPORT

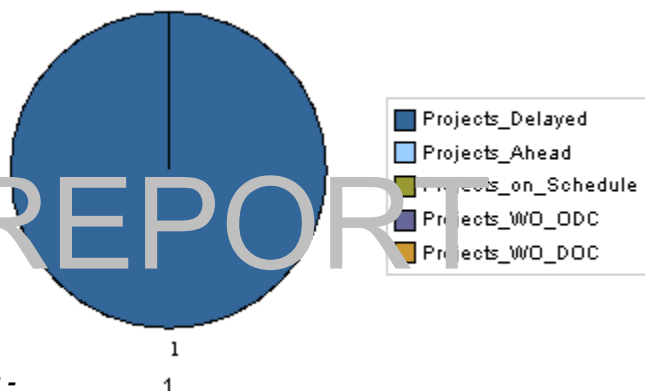


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1554 crore but this was subsequently anticipated to Rs. 1554 crore. The expenditure incurred on these projects till December, 2020 is Rs. 806.15 crore, which is 51.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

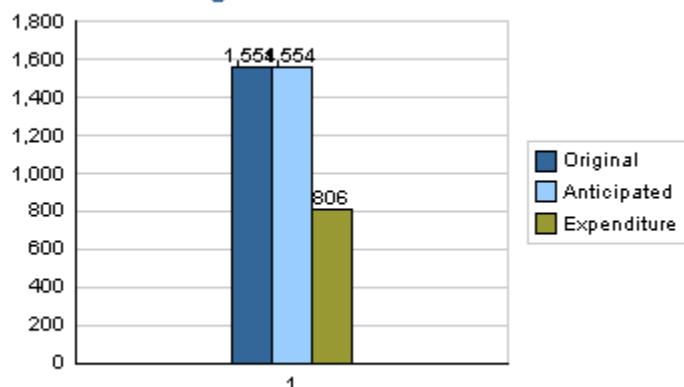

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	67
Number of Projects On Schedule	3
Number of Projects Delayed	41

Number of Projects Without Date Of Commissioning	23
--	----

Brief Analysis

Project Status with respect to Original Schedule: Out of 67 projects, 3 projects are on schedule 41 projects are delayed. 23 projects do not have fixed dates of commissioning.

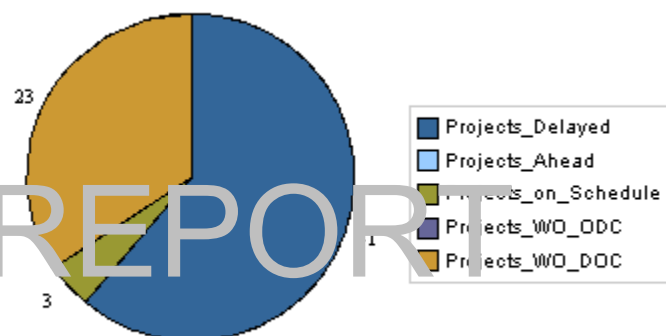


Total No Of Project's:-

67

Investment Scenario

Total original cost of implementation of 67 projects when sanctioned, was of the order of Rs. 283975.91 crore but this was subsequently anticipated to Rs. 356631.39 crore implying a cost overrun of 25.6%. The expenditure incurred on these projects till December, 2020 is Rs. 247060.58 crore, which is 69.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

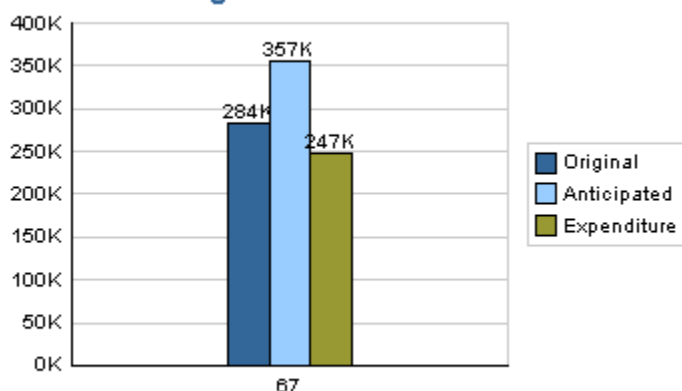

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	142
Number of Projects On Schedule	58
Number of Projects Delayed	70
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	9

Brief Analysis

Project Status with respect to Original Schedule: Out of 142 projects, 3 projects are ahead of schedule, 58 projects are on schedule 70 projects are delayed. 3 projects do not have fixed dates of commissioning 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

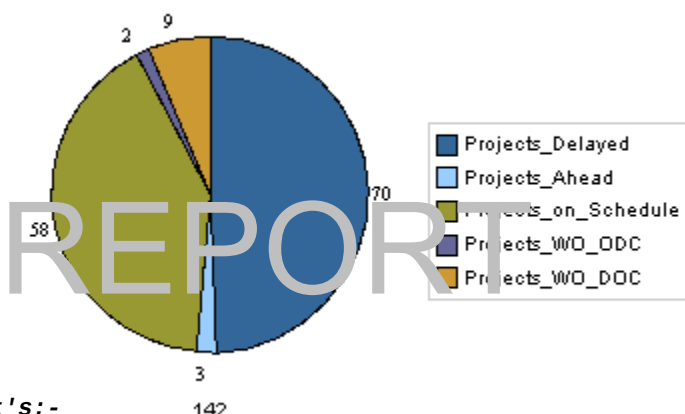


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 142 projects when sanctioned, was of the order of Rs. 282358.27 crore but this was subsequently anticipated to Rs. 290123.35 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till December, 2020 is Rs. 103816.81 crore, which is 35.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

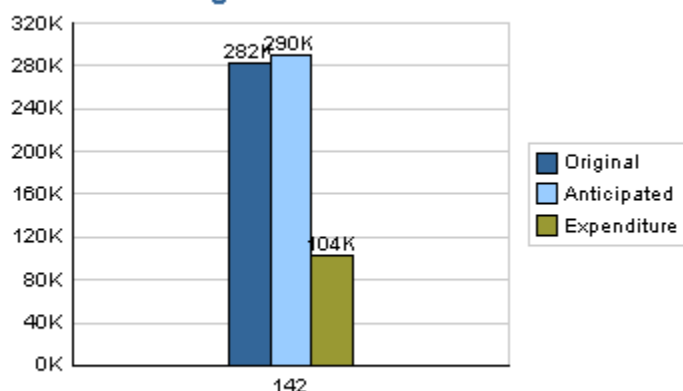

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	7

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 7 projects are delayed. 1 project does not have fixed dates of commissioning

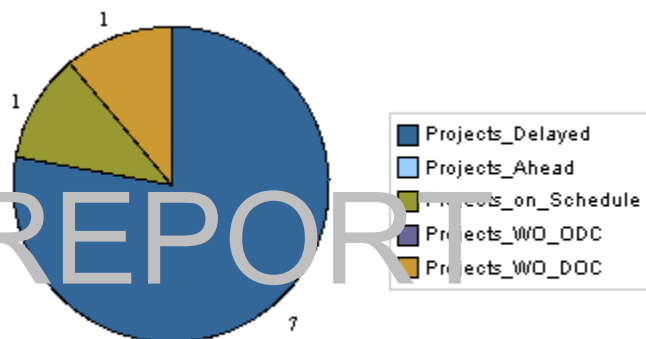


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 23478.11 crore but this was subsequently anticipated to Rs. 29608.45 crore implying a cost overrun of 26.1%. The expenditure incurred on these projects till December, 2020 is Rs. 22856.57 crore, which is 77.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

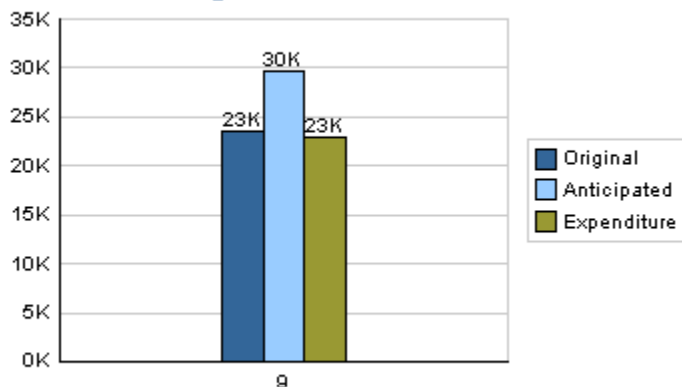

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 1 project is on schedule 3 projects are delayed. 1 project does not have fixed dates of commissioning

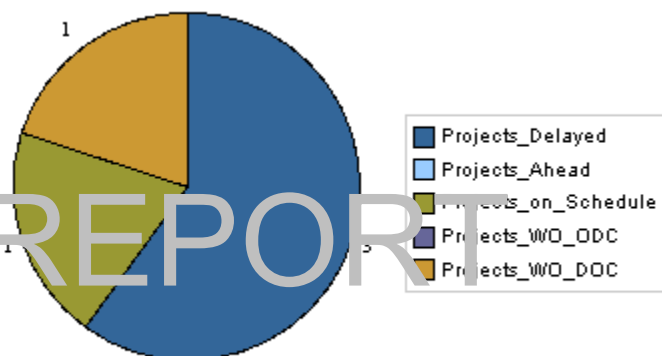


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore. The expenditure incurred on these projects till December, 2020 is Rs. 1173.53 crore, which is 16.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

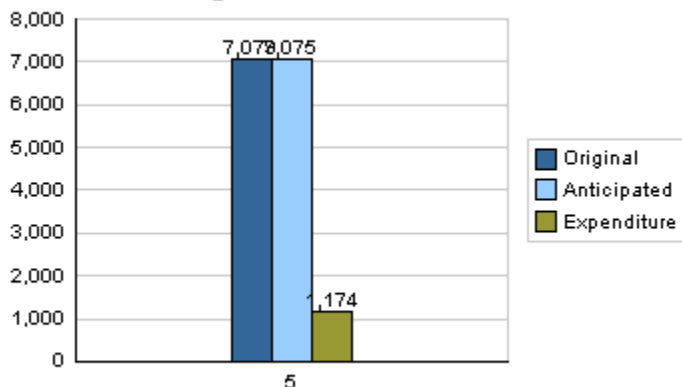

Sector wise current status of projects on the Flash Report

FERTILISERS


Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

FLASH REPORT

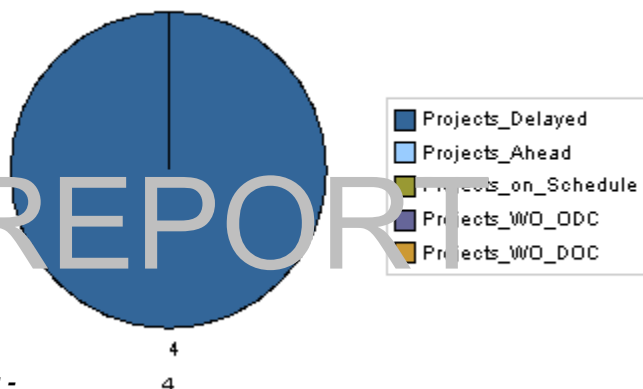


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till December, 2020 is Rs. 822.11 crore, which is 74.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

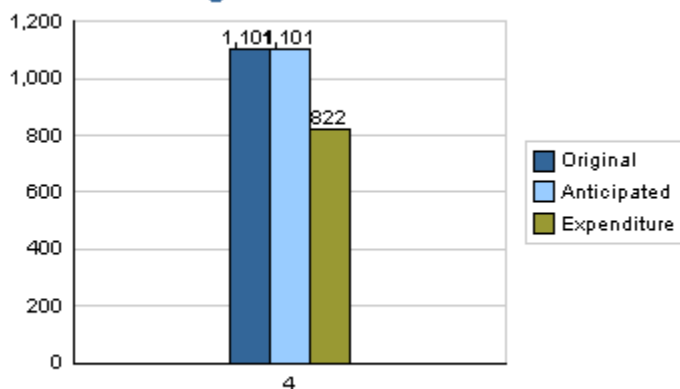

Sector wise current status of projects on the Flash Report


FINANC

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

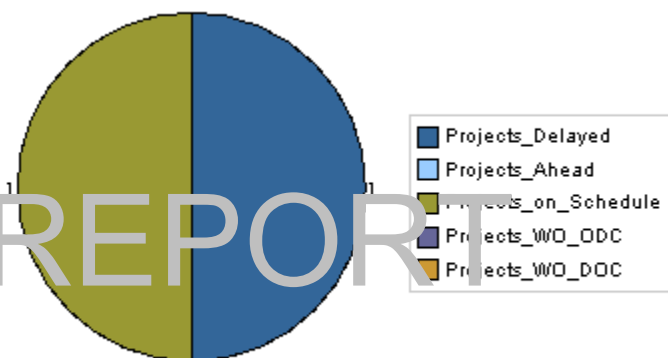


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 557.77 crore but this was subsequently anticipated to Rs. 557.73 crore. The expenditure incurred on these projects till December, 2020 is Rs. 278.94 crore, which is 50% of the anticipated cost of the projects.

Figures are in Rs. Crore

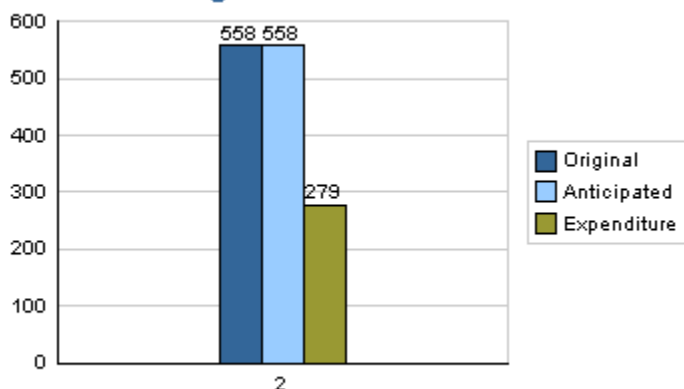

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	105
Number of Projects On Schedule	46
Number of Projects Delayed	42

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	16

Brief Analysis

Project Status with respect to Original Schedule: Out of 105 projects, 46 projects are on schedule 42 projects are delayed. 16 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

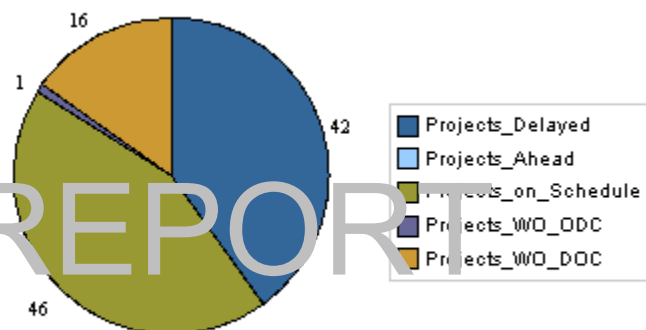


Total No Of Project's:-

105

Investment Scenario

Total original cost of implementation of 105 projects when sanctioned, was of the order of Rs. 112965.37 crore but this was subsequently anticipated to Rs. 118879.8 crore implying a cost overrun of 5.2%. The expenditure incurred on these projects till December, 2020 is Rs. 45071.37 crore, which is 37.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

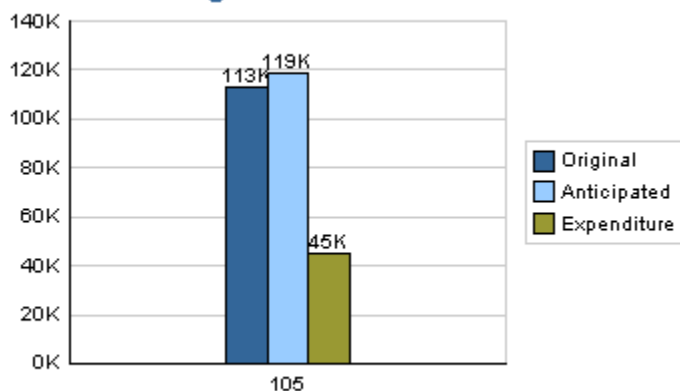

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	19
Number of Projects On Schedule	6
Number of Projects Delayed	13

Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 6 projects are on schedule 13 projects are delayed.

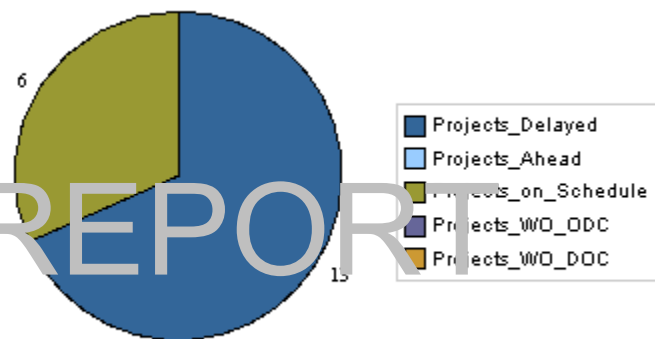


Total No Of Project's:-

19

Investment Scenario

Total original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 13786.34 crore but this was subsequently anticipated to Rs. 14034.5 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till December, 2020 is Rs. 2597.3 crore, which is 18.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

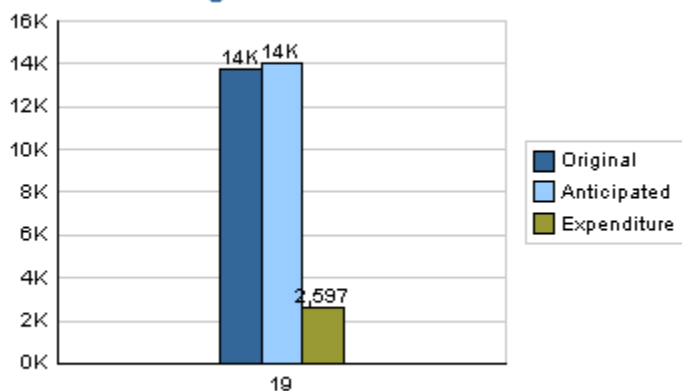

Sector wise current status of projects on the Flash Report

ATOMIC ENERGY


Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

FLASH REPORT

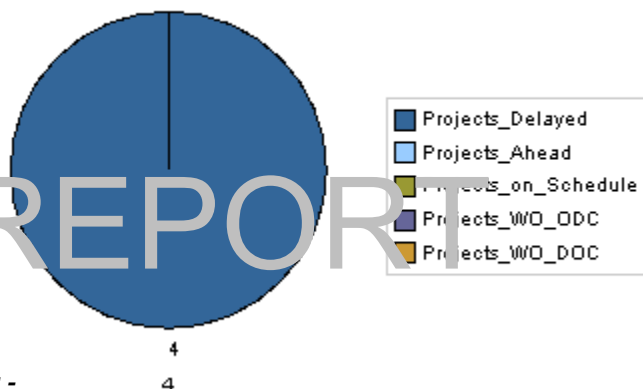


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till December, 2020 is Rs. 56858.72 crore, which is 70.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

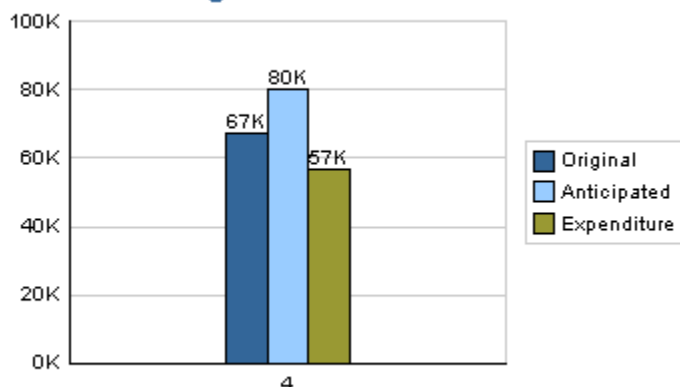

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (DECEMBER 2020)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	2,893.59	816.45
2	ANDHRA PRADESH	74	1,19,147.53	1,66,693.54	71,489.94
3	ARUNACHAL PRADESH	40	21,795.08	41,308.38	26,852.07
4	ASSAM	46	41,915.67	46,133.18	13,879.64
5	BIHAR	105	1,21,115.3	1,56,495.18	73,269.6
6	CHANDIGARH	2	349.15	570	0
7	CHHATISGARH	44	78,072.89	89,205.29	52,353.34
8	DELHI	37	90,924.18	92,955.69	54,773.28
9	GOA	11	5,629.77	5,640.26	2,280.78
10	GUJARAT	58	86,586.94	97,799.93	54,653.96
11	HARYANA	42	30,149.37	32,670.16	18,062.5
12	HIMACHAL PRADESH	15	20,365.24	30,249.67	16,991.85
13	JAMMU AND KASHMIR	18	30,483.84	56,545.15	40,882.64
14	JHARKHAND	44	62,432.53	68,421.43	32,366.74
15	KARNATAKA	62	73,062.53	78,500.1	26,940.7
16	KERALA	21	37,063.23	41,659.56	18,565.96
17	MADHYA PRADESH	85	91,778.35	1,05,425.81	52,718.48
18	MAHARASHTRA	243	2,10,084.44	2,28,773.11	1,05,046.32
19	MANIPUR	1	5,785.67	13,531.5	10,894.98
20	MEGHALAYA	7	3,245.09	6,563.59	1,520.62
21	MIZORAM	13	7,757.62	11,706.32	5,915.98
22	MULTI STATE	131	3,71,661.49	4,85,400.65	1,79,264.01
23	NAGALAND	26	14,842.43	19,040.81	3,636.24
24	ODISHA	91	1,16,984.91	1,22,804.57	53,660.42
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	28	14,921.05	18,022.94	10,540.61
27	RAJASTHAN	56	47,334.2	55,321.42	38,205
28	SIKKIM	9	3,476.73	10,883.48	1,847.03
29	TAMIL NADU	68	1,13,045.04	1,31,786.39	78,282.44
30	TELANGANA	48	36,627.01	39,302.51	18,874.05
31	TRIPURA	7	2,076.64	2,259.45	1,448.87
32	UTTAR PRADESH	132	1,75,440.76	1,82,971.92	88,771.29
33	UTTARAKHAND	32	34,539.29	46,026.02	14,542.6
34	WEST BENGAL	78	66,850.06	84,903.63	45,327.57
TOTAL		1,687	21,44,627.66	25,72,670.28	12,17,692.37

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
1	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007	9/2019	588.72 -	588.72	14.80	09/2022 04/2023	01/2023
	Total		588.72 -	588.72	14.80		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
2	25.5 MW WIND POWER PROJECT AT KANTHAR IN TAMILNADU - [N10000014	9/2017	166.22 163.7	166.22 163.7	125.00	06/2019 06/2021	12/2020
	Total		166.22 163.7	166.22 163.7	125.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
3	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273	3/2017	2,433.00 -	2,433.00	1,925.10	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
4	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315	6/2017	249.26 -	249.26	110.52	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
5	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,696.00	1,780.96	09/2022 -	03/2022
	Total		6,394.26 -	6,378.26	3,816.58		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
6	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47	3,627.47	1,199.46	03/2024 -	03/2023
	<u>East Central Railways</u>						
7	GARHWA ROAD-RAMNA - [N22000465	3/2015	348.23 -	348.23	299.31	03/2021 -	12/2020
	<u>North Central Railway</u>						
8	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495	3/2018	4,329.53 -	4,329.53	33.37	03/2023 03/2026	03/2023
	<u>North East Frontier Railway</u>						
9	SEVOK RANGPO, NEFR - [N22000102	4/2008	1,339.48 4,084.69	8,600.00	619.18	12/2015 12/2023	03/2023

Costing Rs. 150 Crore and above

(December 2020)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
10	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27	760.00	730.62	12/2021	03/2021
	<u>North Western Railway</u>						
11	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85	808.85	153.38	08/2022	06/2022
	<u>Rail Vikas Nigam Ltd.</u>						
12	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	784.37	12/2026	12/2025
13	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00	3,000.00	2,121.59	03/2023	12/2022
14	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	.19	12/2025	03/2025
	<u>South Central Railway</u>						
15	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	4/2012	1,856.95	1,952.68	487.47	03/2023 03/2025	03/2024
16	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31	927.94	517.35	03/2020 03/2022	06/2021
17	GUNTUR-GUNTAKA - [N22000368]	4/2011	3,031.50	3,187.48	184.35	03/2022 03/2025	03/2024
	<u>Southern Railway</u>						
18	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26	332.00	239.19	04/2014 01/2021	12/2020
	Total		23,253.12	36,051.38	8,169.83		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
19	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]	3/2018	289.67	289.67	173.13	08/2018 06/2021	02/2021
20	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	3/2018	504.19	504.19	403.01	11/2018 04/2021	01/2021
21	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09	995.09	473.71	05/2016 08/2021	04/2021
22	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]	1/2016	386.09	386.09	199.35	05/2016 01/2021	12/2020
	<u>National Highways Authority Of India</u>						
23	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62	2,499.00	1,497.61	03/2021 10/2021	04/2021
24	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]	3/2018	1,484.30	1,484.30	356.66	- 06/2021	12/2020
	Total		5,191.96	6,158.34	3,103.47		
	<u>URBAN DEVELOPMENT</u>						

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Central Public Works Department</u>						
25	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150	3/2019	1,828.00	1,828.00	-	09/2025	05/2024
	Total		1,828.00	1,828.00	.00		
	Grand Total		37,422.68	51,167.87	15,239.68		

FLASH REPORT

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24 -	412.24	-	06/2021 -	06/2021
2	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	-	05/2022 -	05/2022
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	51.11	09/2021 -	09/2021
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]	3/2017	475.39 -	475.39	88.11	04/2021 -	04/2021
5	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022
6	C/O OF NITB AND ASSOCIATED WORKS AT V JAYAWAL AIRPORT - [N04000091]	4/2020	611.0 -	611.8	-	03/2023 -	03/2023
	Total		3,416.21 -	3,550.27	261.41		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.54	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
8	TETARIKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
9	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	0.40	03/2027 -	03/2027
10	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	-	03/2025 -	03/2025
11	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	386.19	03/2022 -	03/2022
12	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	97.01	03/2024 -	03/2024
13	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	0.43	03/2026 -	03/2026
14	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	-	03/2027 -	03/2027
15	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	0.87	03/2029 -	03/2029
16	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	158.71	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
17	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,217.77	03/2029 -	03/2029
18	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,971.87	03/2026 -	03/2026
19	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	173.89	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
20	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	10,724.93	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
21	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
22	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
23	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	524.01	03/2021 -	03/2021
24	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	1/2020	1,729.3 -	1,729.6	-	03/2025 -	03/2025
25	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	1/2017	1,055.7 -	1,055.17	144.51	03/2022 -	03/2022
26	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
27	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	29.94	03/2023 -	03/2023
28	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.21	03/2021 -	03/2021
29	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	54.76	03/2021 -	03/2021
30	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	18.19	03/2026 -	03/2026
31	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	7.31	03/2023 -	03/2023
32	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	0.85	03/2022 -	03/2022
33	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	8.19	03/2023 -	03/2023
34	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
35	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	3,645.58	03/2023 03/2016	03/2023
36	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	129.86	03/2022 -	03/2022
37	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
38	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
39	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
40	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,446.61	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
41	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
42	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	277.08	03/2025 -	03/2025
43	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	204.15	03/2021 -	03/2021
44	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	260.46	03/2021 -	03/2021
45	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	98.99	03/2021 -	03/2021
46	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	36.94	03/2022 -	03/2022
47	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	20.99	03/2022 -	03/2022
48	BHANEGAON OC - [N06000121]	2/2016	409.61 -	409.61	85.01	03/2023 -	03/2023
49	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	245.47	03/2021 -	03/2021
50	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	226.05	03/2022 -	03/2022
51	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	0.87	03/2026 -	03/2026
52	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	35.65	03/2022 -	03/2022
	Total		71,227.42 -	71,449.96	23,518.07		
	<u>FINANC</u>						
	<u>Central Public Works Department</u>						
53	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	83.71	11/2021 -	11/2021
	Total		348.77 -	348.77	83.71		
	<u>HEALTH AND FAMILY WELFARE</u>						
54	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	94.33	09/2023 -	09/2023
55	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
56	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	577.32	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	671.65		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
57	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-- [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
	Total		166.98 -	166.98	.00		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
58	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	35.88	06/2022 -	06/2022
59	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]	10/2019	348.24 -	348.24	7.05	05/2022 -	05/2022
60	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
61	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELA BHATA DURG CHHATTISGARH, PHASE I & II. - [N30000111]	3/2020	808.2 -	808.6	57.47	07/2022 -	07/2022
	Total		2,225.37 -	2,225.37	100.35		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
62	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	0.74	04/2021 04/2021	04/2021
	Total		483.00 -	483.00	.74		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
63	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	60.14	06/2022 -	06/2022
64	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	278.71	12/2021 -	12/2021
65	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
66	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	276.12	03/2023 -	03/2023
67	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	571.32	12/2021 -	12/2021
68	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	79.52	03/2021 -	03/2021
69	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	168.73	08/2022 -	08/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
70	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20 -	580.20	90.13	02/2021 -	02/2021
	<u>Gas Authority Of India Limited</u>						
71	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	93.90	10/2022 -	10/2022
72	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	397.60	05/2023 -	05/2023
73	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]	8/2018	217.92 -	217.92	72.40	04/2021 -	04/2021
74	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	128.57	10/2022 -	10/2022
75	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	113.30	07/2022 -	07/2022
76	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	73.85	10/2022 -	10/2022
77	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	68.12	07/2022 -	07/2022
78	DHAMRA HALDWAR PIPELINE PROJECT - [N16000391]	3/2021	1,030.65 -	1,030.65	2.70	11/2022 -	11/2022
79	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	1,998.30	12/2021 -	12/2021
80	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	183.93	04/2022 -	04/2022
81	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	84.25	07/2022 -	07/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
82	SETTING UP OF PHASE II FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	177.00	11/2021 -	11/2021
83	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	669.37	06/2022 -	06/2022
84	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	33.86	02/2023 -	02/2023
85	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	135.22	03/2029 -	03/2029
86	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	13.79	03/2031 -	03/2031
87	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	71.11	11/2022 -	11/2022
88	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	86.19	09/2026 -	09/2026
89	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	121.57	12/2022 -	12/2022
	<u>Indian Oil Corporation Limited</u>						
90	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,259.24	10/2021 -	10/2021
91	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	180.63	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
92	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	1.80	09/2022 -	09/2022
93	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	48.16	05/2023 -	05/2023
94	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	-	12/2022 -	12/2022
95	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
96	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	8.10	07/2022 -	07/2022
97	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	425.50	12/2022 -	12/2022
98	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	-	08/2022 -	08/2022
99	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2018	2,031.00 -	2,031.00	1,432.00	08/2021 -	08/2021
100	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	1/2018	462.00 -	462.30	2.30	09/2021 -	09/2021
101	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	53.36	10/2021 -	10/2021
102	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	72.66	01/2024 -	01/2024
103	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	52.81	12/2021 -	12/2021
104	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	0.22	07/2022 -	07/2022
105	ADDITIONAL FACILITIES AT VIJAYAWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
106	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	53.20	01/2023 -	01/2023
107	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00 -	921.00	2.86	09/2023 -	09/2023
108	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
109	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMT/PA - [N16000386]	1/2020	14,810.00 -	14,810.00	632.61	04/2023 -	04/2023
110	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	541.64	10/2021 -	10/2021
111	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	2.06	07/2021 -	07/2021
112	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	129.59	10/2021 -	10/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
113	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	-	06/2023 -	06/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Numaligarh Refinery Limited</u>						
114	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024
115	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
116	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	621.21	03/2026 -	03/2026
117	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	1,303.59	05/2021 -	05/2021
118	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	1,941.83	05/2021 -	05/2021
119	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,096.58	03/2022 -	03/2022
120	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	3,596.00	3,442.73	05/2021 05/2021	05/2021
	Total		1,40,322.00 -	1,09,580.00	1,06,680.40		
	<u>POWER</u>						
	<u>Satluj Jal Vidyut Nigam Limited</u>						
121	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	1,221.50	01/2024 -	01/2024
122	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	282.43	01/2026 -	01/2026
123	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	479.06	12/2021 -	12/2021
	Total		12,897.98 -	12,897.98	1,982.99		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
124	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
125	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	429.22	03/2023 -	03/2023
126	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
127	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,341.89	03/2023 -	03/2023
128	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>North Central Railway</u>						
129	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021
130	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	33.37	03/2023 03/2026	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North East Frontier Railway</u>						
131	NEW BG LINE FROM BYRNHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	4,083.02	263.67	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
132	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	112.02	12/2021 -	12/2021
133	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
134	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	778.29	03/2022 -	03/2022
	<u>National High Speed Rail Corporation Limited</u>						
135	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	9,576.52	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
136	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	507.33	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
137	MATHURA-JHAJSI-3RD LANE (275.30 KM) - [N22000501]	6/2016	3,677.63 -	3,677.71	436.33	12/2023 -	12/2023
138	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	705.50	12/2024 -	12/2024
139	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
140	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,376.94	12/2021 -	12/2021
141	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021
	Total		1,47,147.85 -	1,55,917.22	20,672.35		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
142	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	137.87	06/2021 -	06/2021
143	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]	10/2016	172.63 -	172.63	123.44	12/2020 -	12/2020
144	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	57.16	09/2021 -	09/2021
145	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]	11/2018	281.45 -	281.45	2.36	12/2020 -	12/2020
146	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]	10/2016	167.62 -	167.62	98.42	12/2020 -	12/2020
147	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]	3/2018	351.00 -	351.00	84.67	06/2021 -	06/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
148	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]	12/2016	196.00 -	196.00	-	09/2021 -	09/2021
149	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]	3/2020	166.94 -	166.94	-	12/2020 -	12/2020
150	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]	3/2020	370.36 -	370.36	-	08/2022 -	08/2022
151	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	55.12	03/2021 -	03/2021
152	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH - [N24001180]	3/2019	237.51 -	237.51	38.85	12/2022 -	12/2022
	Total		3,111.22 -	3,111.22	597.89		
	<u>RURAL DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
153	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021
	Total		361.60 -	361.60	12.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
154	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	5,369.18 -	4,633.81	1,787.23	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,787.23		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (SAIL)</u>						
155	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	377.18 -	377.18	0.38	05/2023 -	05/2023
	Total		377.18 -	377.18	.38		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
156	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	14.89	03/2024 -	03/2024
157	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	30.02	03/2024 -	03/2024
	<u>Central Public Works Department</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
158	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022
	<u>Delhi Metro Rail Corporation</u>						
159	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	965.60	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
160	KANPUR METRO RAIL PROJECT - [N28000144]	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
161	AGRA METRO RAIL PROJECT - [N28000145]	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
162	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	5,234.40	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
163	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	114.13	02/2023 -	02/2023
164	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	112.78	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
165	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	2,467.77	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
166	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,365.77	271.17	06/2024 -	06/2024
	Total		1,32,439.21 -	1,32,439.21	9,232.76		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
167	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	0.42	06/2022 -	06/2022
168	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	79.54	04/2021 -	04/2021
169	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	111.10	05/2021 -	05/2021
170	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
171	SAIDPUR SEWER NETWORK PATNA - [N30000039]	4/2015	268.63 -	268.63	254.50	01/2021 -	01/2021
172	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	0.29	06/2022 -	06/2022
173	SEWERAGE SYSTEM AND STP AT CHAPRA - [N30000028]	11/2018	236.15 -	236.15	12.06	12/2020 -	12/2020
174	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	131.43	05/2021 -	05/2021
175	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	37.09	07/2021 -	07/2021
	<u>Delhi Jal Board</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
176	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78	665.78	129.56	12/2022	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
177	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22	185.22	-	12/2021	12/2021
178	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	5/2018	198.43	198.43	-	02/2022	02/2022
179	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53	287.53	-	04/2022	04/2022
180	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96	384.96	-	04/2022	04/2022
181	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12	307.12	-	09/2022	09/2022
182	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	104.03	104.03	-	12/2021	12/2021
183	INTEGRATION OF STPS WITH REHABILITATION AND HANDLING OF EXISTING ASSETS - [N30000033]	3/2018	165.16	165.16	-	06/2022	06/2022
184	INTERCEPTION AND DIVERSION WITH STP AT HUGHLI-CHINSURAH - [N30000042]	5/2018	160.00	160.00	-	02/2022	02/2022
185	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10	172.10	-	12/2021	12/2021
186	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31	234.31	-	04/2022	04/2022
	<u>Uttar Pradesh Jal Nigam</u>						
187	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]	2/2019	317.19	317.19	-	08/2021	08/2021
188	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78	681.78	-	06/2022	06/2022
189	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79	234.03	-	12/2021	12/2021
190	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62	213.62	-	03/2022	03/2022
191	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05	206.05	5.16	10/2021	10/2021
192	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39	271.39	-	08/2021	08/2021
193	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00	904.00	38.38	09/2021	09/2021
194	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59	767.59	32.47	09/2021	09/2021
195	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23	967.23	14.64	09/2021	09/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		10,736.58	10,738.82	846.64		
	Grand Total		5,35,163.42	5,42,984.46	80,449.01		

FLASH REPORT

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (December 2020)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,896.72	09/2010 09/2016	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	16,038.00	12/2015 -	09/2021	69	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	12,799.00	12/2016 -	03/2023	75	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT - 3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	50,849.00 -	50,849.00	22,250.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	56,858.72					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	438.28	335.58	06/2019 -	12/2020	18	0	
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13	0	
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	417.23 -	441.33	291.75	09/2018 09/2020	06/2021	33	5.78	
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	458.00	105.12	03/2020 06/2021	06/2021	15	0	
9	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI, ANDHRA PRADESH	08/2017	177.10 -	177.10	-	02/2020 -	06/2021	16	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10	0	
11	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5	0	
12	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 1,232.00	1,232.00	323.90	03/2021 -	03/2022	12	7.88	
13	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	85.07	12/2021 -	09/2022	7	0	
14	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.60	09/2021 09/2020	09/2022	12	0	
15	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	389.71	37.38	11/2021 10/2022	10/2022	11	0	
16	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	1,405.00	-	08/2022 -	03/2023	7	0	
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	-	03/2022 -	03/2023	12	0	
	Total		10,370.13 -	10,484.23	2,335.89					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
18	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	277.38	05/2014 03/2020	02/2021	81	0	
19	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	23.04	03/2017 -	10/2021	55	12.2	
20	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	16.73	04/2018 -	12/2021	44	37.56	
21	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	446.01	04/2015 03/2022	03/2022	83	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
22	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	17.76	04/2014 04/2023	04/2023	108	0	
	<u>Central Coal Fields Limited</u>									
23	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.63	03/2011 -	03/2022	132	0	
24	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	401.56	03/2016 -	03/2022	72	0	
25	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	96.86	03/2014 -	03/2022	96	0	
26	AMRAPALI OC EPR (12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 5,136.15	858.11	243.83	03/2020 03/2024	03/2024	48	0	
27	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND	03/2019	1,553.06 -	1,553.06	238.77	03/2023 -	03/2024	12	0	
28	MAGADH EXPANSION OCP RPR - [N06000015]CCL,JHARKHAND	08/2007	706.4 7,274.3	706.40	38.94	7/201 07/2025	03/2025	62	0	
	<u>Eastern Coal Fields Limited</u>									
29	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	632.85	03/2018 -	03/2021	36	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2.Expediting the work of tree felling for hand over of 32.65 Ha forest land.
	<u>Mahanadi Coal Fields Limited</u>									
30	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	362.50	362.50	03/2012 -	03/2021	108	74.88	
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	491.85	491.85	03/2013 -	03/2022	108	2.57	
32	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	274.63	03/2019 -	03/2024	60	0	
33	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	114.36	03/2018 -	03/2024	72	0	
34	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	494.67	03/2021 -	03/2024	36	0	
35	GOPAL JI KANIHA OCP, MCL - [N06000035]MCL,ODISHA	12/2007	457.77 8,416.19	684.32	684.32	03/2013 03/2028	03/2028	180	49.49	
36	BALRAM EXPANSION OCP - [N06000044]MCL,ODISHA	12/2007	172.08 3,504.21	646.01	646.01	03/2010 03/2029	03/2029	228	275.41	
37	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	586.86	586.86	03/2017 -	03/2031	168	19.74	
	<u>Neyveli Lignite Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
38	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	7,980.79	7,371.83	12/2015 -	01/2021	61	35.1	
39	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	31.62	08/2022 -	09/2023	13	0	
40	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	479.89	06/2015 03/2025	03/2025	117	-51.37	
	<u>Singareni Colliers Company Limited</u>									
41	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	189.91	03/2016 -	03/2021	60	-3.5	
42	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.22 -	164.04	131.55	03/2015 -	03/2022	94	32.3	
43	RCE OF INDARAM OCP (120 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	112.7 -	349.28	79.54	03/2015 -	03/2022	84	114.6	
44	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2022	84	5.85	
45	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	122.55	07/2016 -	03/2022	68	-7.91	
46	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	106.15	03/2019 -	03/2022	36	11.42	
47	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	169.90	03/2019 03/2022	03/2022	36	0	
48	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	16.86	
49	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
50	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	208.12	03/2014 -	03/2021	84	0	
51	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	182.04	03/2016 -	03/2021	60	0	
52	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	82.60	03/2020 -	03/2021	12	0	
53	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	180.74	03/2015 03/2020	03/2022	84	201.44	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
54	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	4.98	03/2014 -	03/2022	96	0	
55	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	120.14	03/2021 -	03/2022	12	0	
56	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.41	03/2018 -	03/2023	60	0	
57	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	123.22	03/2020 -	03/2023	36	0	
	<u>Western Coal Fields Limited</u>									
58	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	104.95	03/2023 -	03/2024	12	15.41	
59	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	217.6 -	313.34	40.64	03/2023 -	03/2024	6	12.85	
	Total		268.90 -	30,076.22	17,36.67					
	<u>FINANC</u>									
	<u>Central Public Works Department</u>									
60	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	208.96	195.23	10/2019 -	04/2021	18	-0.2	
	Total		209.00 -	208.96	195.23					
	<u>FERTILISERS</u>									
	<u>National Fertiliser Limited</u>									
61	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	218.83	171.68	11/2019 -	02/2021	15	0	
62	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	164.03	11/2019 -	03/2021	16	0	
63	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	239.81	182.53	11/2019 -	03/2021	16	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
64	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72	426.72	303.87	04/2020 03/2021	03/2021	11	0	
	Total		1,101.28	1,101.28	822.11					
	<u>MINES</u>									
	<u>National Aluminum Company Limited (Nalco)</u>									
65	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62	163.17	135.00	06/2019 06/2021	12/2020	18	-2.07	
66	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00	355.00	93.16	12/2020	02/2021	3	0	
67	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	5,540.00	5,540.00	614.13	04/2021 12/2022	12/2022	20	0	
	Total		6,061.62	6,058.17	842.29					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
68	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00	21,940.00	17,436.86	05/2015 07/2021	07/2021	74	41.32	
	<u>Rastriya Ispat Nigam Limited</u>									
69	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00	2,558.00	1,762.09	12/2017 12/2020	12/2020	36	-10.5	No
70	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85	1,682.85	1,511.30	09/2018 02/2021	02/2021	29	0	No
	<u>Steel Authority Of India Limited (Sail)</u>									
71	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18	1,154.18	1,026.52	12/2017 10/2020	02/2021	38	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
72	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	170.16	06/2019 05/2021	05/2021	23	0	
73	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL	12/2018	263.36 -	263.36	159.19	09/2020 03/2021	05/2021	8	0	
74	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	511.79	10/2017 12/2021	12/2021	50	0	
	Total		22,780.27 -	28,895.27	22,577.91					
	PETROLEUM									
	Bharat Petroleum Corporation Limited									
75	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	5,245.96	4,808.25	08/2018 11/2019	01/2021	29	14.33	
76	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA	08/2016	282.64 -	282.64	238.43	08/2020 -	01/2021	5	0	
77	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	449.58	342.23	12/2019 02/2021	02/2021	14	0	
78	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	3,288.96	2,614.93	02/2020 02/2021	02/2021	12	-73	
79	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	695.00	06/2019 -	02/2022	32	35.54	
80	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	16.38	02/2017 08/2022	08/2022	66	117.11	
	Chennai Petroleum Corporation Limited									
81	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	1,858.00	1,498.79	12/2019 -	01/2021	13	0	
82	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	300.00	238.43	08/2020 -	09/2021	13	-28.74	
	Gas Authority Of India Limited									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
83	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	186.50	04/2018 -	03/2021	35	-38.98	
84	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,542.50	12/2020 -	03/2021	3	-30.59	
85	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	143.50	08/2020 05/2021	05/2021	9	14.17	
86	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00 -	2,433.00	1,925.10	12/2020 12/2021	06/2021	6	0	
87	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISH	03/2017	1,933.00 -	1,933.00	1,174.60	12/2020 12/2021	12/2021	12	0	
88	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,470.00 3,038.00	3,048.00	1,593.30	12/2020 12/2021	12/2021	12	-11.32	
89	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	775.10	12/2020 12/2021	12/2021	12	0	
90	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	225.54	38.70	02/2021 -	12/2021	10	0	
91	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,470.70	12/2012 02/2022	02/2022	110	102.71	
	<u>Hindustan Petroleum Corporation Limited</u>									
92	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA	11/2017	255.00 300.00	300.00	247.49	11/2020 06/2021	06/2021	7	17.65	
93	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	84.06	07/2020 -	07/2021	12	0	
94	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	110.52	06/2020 12/2021	09/2021	15	0	
95	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	54.07	06/2020 09/2021	09/2021	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
96	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	13,324.42	07/2020 07/2022	07/2022	24	25.5	
97	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 3,072.00	3,072.00	1,825.04	06/2021 08/2022	08/2022	14	14.76	
	<u>Indian Oil Corporation Limited</u>									
98	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	494.64	07/2018 02/2021	02/2021	31	0	
99	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	3,338.00	2,724.32	12/2020 -	03/2021	3	43.82	
100	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	22.92	01/2021 -	04/2021	3	0	
101	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	131.10	01/2021 -	04/2021	3	0	
102	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	502.00	399.01	08/2019 06/2021	06/2021	22	18.68	
103	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	78.12	02/2020 06/2021	06/2021	16	0	
104	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	114.02	01/2021 06/2021	06/2021	5	0	
105	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	467.19	02/2020 06/2021	06/2021	16	0	
106	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	209.74	04/2021 -	07/2021	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
107	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	3,027.90	1,685.17	12/2020 -	08/2021	8	66.09	
108	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	6,025.00	3,275.27	12/2018 -	08/2021	32	33.98	
109	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	160.41	10/2020 -	08/2021	10	0	
110	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]IOCL,HARYANA	04/2018	206.6 -	206.63	104.13	12/2020 8/2021	08/2021	18	0	
111	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 293.00	293.00	138.42	06/2020 09/2021	09/2021	15	24.15	
112	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	109.56	03/2021 -	09/2021	6	0	
113	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	111.62	01/2021 -	10/2021	9	0	
114	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	80.39	04/2020 10/2021	10/2021	18	0	
115	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	234.25	02/2020 10/2021	10/2021	20	0	
116	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU	12/2016	228.00 -	228.00	110.61	06/2020 -	11/2021	17	0	
117	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	124.52	08/2021 -	11/2021	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
118	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	16.36	08/2020 11/2021	11/2021	15	0	
119	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	278.28	03/2021 12/2021	12/2021	9	0	
120	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 -	1,945.00	1,437.61	08/2021 -	02/2022	6	0	
121	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	20.38	10/2020 02/2022	02/2022	16	0	
122	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	172.31	02/2020 02/2022	02/2022	24	0	
123	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	374.14	10/2017 02/2022	03/2022	53	17.66	
124	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	45.32	12/2019 03/2022	03/2022	27	0	
125	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	141.32	01/2021 03/2022	03/2022	14	0	
126	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	552.56	08/2020 -	04/2022	20	0	
127	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	9.50	06/2021 07/2022	07/2022	13	0	
128	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH	03/2018	676.00 -	676.00	375.67	12/2021 -	08/2022	8	0	
129	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	82.31	04/2022 -	02/2023	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
130	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	53.13	04/2022 -	08/2023	16	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
131	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	390.06	03/2020 11/2020	06/2021	15	9.64	
132	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,501.84	12/2019 04/2021	07/2021	19	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
133	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOIS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,046.40	1,846.46	1,518.24	05/2013 12/2020	03/2021	94	114.26	
134	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,572.08	04/2018 05/2021	05/2021	37	5.8	
135	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	624.35	445.60	03/2019 05/2021	05/2021	26	-4.07	
136	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	170.85	05/2020 05/2021	05/2021	12	21.57	
137	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	584.33	12/2020 05/2021	05/2021	5	-3.93	
138	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	25,090.00	9,799.00	06/2020 08/2021	08/2021	14	-26.23	
139	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	922.04	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									
140	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	490.24	445.41	03/2017 -	03/2021	48	39.05	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
141	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	176.37	10/2020 -	03/2021	5	0	
142	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	222.21	148.44	08/2020 -	03/2021	7	-1.13	
143	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	450.70	12/2019 -	04/2021	16	0	
144	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 638.60	652.10	130.10	02/2020 -	04/2021	14	19.89	
	Total		1,24,228.9	1,30,628.73	70,63.42					
	<u>POWER</u>									
	<u>Central Public Works Department</u>									
145	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	172.99	11/2019 -	03/2021	16	0	
	<u>Chenab Valley Power Projects [P] Limited</u>									
146	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,598.96	04/2020 -	07/2025	63	0	
	<u>National Hydro-Electric Power Corporation</u>									
147	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	8,705.10	09/2009 03/2022	03/2022	150	152.52	
148	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	12,855.18	09/2010 08/2023	08/2023	155	218.08	
	<u>National Thermal Power Corporation</u>									
149	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]JNTPC,UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	11,044.00	02/2017 06/2020	01/2021	47	24.87	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
150	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 15,105.22	15,105.22	13,473.99	01/2018 10/2020	02/2021	37	29.79	
151	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	10,016.10	7,888.03	07/2019 03/2021	03/2021	20	9	- Physical possession / Acquisition of balance 8.059 Acres Abadi Land for Main Plant area (6.285 acres) and for Ash Dyke area (1.774 acres). - Readiness of Power evacuation system by M/s UPPTCL for Unit#6
152	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,332.4 -	13,740.53	11,41.91	02/2018 02/2021	03/2021	27	9.64	
153	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	9,583.00	8,648.28	07/2012 06/2020	03/2021	104	79.02	
154	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,331.70	05/2018 06/2021	07/2021	38	33.47	
155	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	7,998.74	11/2020 03/2022	03/2022	16	0	
156	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	18,168.42	10/2011 04/2022	04/2022	126	145.16	
157	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,389.42	11,269.68	06/2019 10/2022	10/2022	40	7.12	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
158	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,796.50	03/2013 12/2021	12/2022	117	96.99	Award of Srinagar to Kashipur transmission line by PTCUL for power evacuation. Support of State Govt. of Uttarakhand is required for expeditious completion of Transmission line for Power evacuation system. CEA convene meeting on 09.11.20 wherein CEO (POSOCO), COO (CTU-PGCIL), Director(P) PTCUL, HOP TVHPP and HOP THDC Pipalkoti HEP were present. PTCUL proposed to implement Khandukhal – Koteswar 400kV D/c line (approx. 35km) in place of Srinagar (Khandukhal) – Kashipur (Rampura) 400kV D/c line. Award of this line is critical as PTCUL informed that 22 months (app) will be required for completion of this line.
159	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	18,668.00	3,644.04	03/2023 -	09/2024	18	0	
160	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,592.34	626.32	09/2019 11/2022	12/2024	63	15.23	- All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSECL. State Govt is not ready to finalize power evacuation line in absence of PPA. - Shifting of balance Homesteads from Project area. (13 Nos + 01 School)
	<u>North East Electric Power Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
161	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	7,927.34	8,151.00	12/2009 01/2021	01/2021	133	217.49	
	<u>Power Grid Corporation Of India Limited</u>									
162	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,623.08	10/2012 06/2020	01/2021	99	5.14	
163	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62 -	871.62	640.30	10/2017 12/2020	01/2021	39	0	
164	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	341.06	04/2018 04/2020	01/2021	33	0	
165	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.8 -	445.8	43.28	02/2019 05/2020	01/2021	3	0	
166	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE	05/2014	522.29 546.36	546.36	477.58	11/2016 06/2020	02/2021	51	4.61	
167	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL, MULTI STATE	02/2017	5,070.13 -	5,070.13	3,989.71	04/2020 -	02/2021	10	0	
168	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 3,500.00	3,500.00	2,724.70	07/2020 -	02/2021	7	0	
169	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	358.83	234.30	05/2020 -	02/2021	9	0	
170	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	238.32	04/2016 12/2017	03/2021	59	0	
171	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	197.40	89.15	03/2018 -	03/2021	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
172	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	627.32	01/2018 05/2020	03/2021	38	0	
173	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	11,217.10	11/2019 05/2020	03/2021	16	0	
174	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	195.52	02/2019 04/2020	03/2021	25	0	
175	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	146.71	06/2019 09/2020	03/2021	11	0	
176	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	210.09	12/2019 06/2020	03/2021	15	0	
177	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	156.28	07/2019 06/2020	03/2021	20	17.99	
178	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,564.64	02/2020 09/2020	03/2021	13	0	
179	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	508.31	05/2017 07/2020	06/2021	49	0	
180	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,151.56	1,893.34	12/2018 -	12/2021	36	92.49	
181	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,700.00	2,430.27	12/2018 -	12/2021	36	31.08	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
182	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,864.61	08/2013 03/2022	03/2022	103	32.24	
	<u>Thdc India Limited</u>									
183	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 -	1,587.16	454.82	09/2020 -	08/2022	23	-24.57	1. Tenancy/Private land (337.35 Ha): Serving of notices to beneficiaries is under process by LAO which is to be expedited. 2. Govt. land for R&R (53.13 Ha): Declaration of the land as "Abadi Land" is pending at MP Govt. 3. Govt. land of Coal Block (178.13 Ha): Collector, Singrauli informed that permission under section 247 shall be accorded after grant of Mining Lease which is pending with Director (Mining), GoMP.
184	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,860.35	2,110.14	06/2013 -	12/2023	126	54.94	Environment Clearance of Gadi Quarry is still pending In the meeting of SEIAA held in Nov19 it was informedthat Environmental Clearance for Gadi Quarry shall be given to the owner THDCIL in place of HCC In thiscontext THDCIL has written letter to District Magistrate Chamoli on 13.12.19 to consider the transfer of name ofapplicant from Ms HCC to THDC India Limited in the application of EC DM.
185	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	1,297.85	09/2023 -	08/2024	11	0	• Continuous help of District administration is required for expeditious land acquisition to avoid any possible hindrance in work. • Help of District administration is required for expeditious shifting of Nagla residents from Plant Land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		2,12,493.18	2,81,578.59	1,95,293.32					
	<u>HEAVY INDUSTRY</u>									
	<u>Bharat Heavy Electricals Limited</u>									
186	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00	1,554.00	806.15	09/2019 12/2020	12/2020	15	0	
	Total		1,554.00	1,554.00	806.15					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Central Public Works Department</u>									
187	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84	209.84	15.97	03/2020	05/2021	14	0	
188	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA	09/2017	150.29	150.29	34.89	03/2020	12/2021	21	0	
189	CONST OF 152 QTRS. 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00	195.00	16.41	09/2020	04/2022	19	0	
190	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00	260.00	25.38	06/2021	05/2022	11	0	
	<u>HII Infra Tech Services Limited</u>									
191	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00	715.06	511.74	04/2020	07/2021	15	-8.91	
192	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00	557.48	438.92	06/2020	07/2021	13	-20.7	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
193	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00	747.80	279.76	05/2021	07/2022	14	-14.54	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
194	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95	177.92	157.90	02/2018	12/2020	34	16.33	
195	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19	274.19	249.74	03/2019	01/2021	22	0	
196	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11	499.23	456.52	11/2013	03/2021	88	20.55	
197	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	254.4	250.00	265.4	05/2017	03/2021	16	22.29	
198	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19	272.54	245.89	03/2019	03/2021	24	.13	
199	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15	355.15	268.35	03/2019	03/2021	24	0	
200	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99	363.99	227.35	05/2018	12/2021	43	0	
	Total		5,215.15	5,028.49	3,255.36					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
201	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50	4,517.49	2,637.46	03/2021	03/2023	24	98.88	
202	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89	1,377.48	333.58	03/2021	03/2023	24	73.73	
203	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19	1,283.49	408.70	03/2022	03/2023	12	.89	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
204	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	248.22	03/2022 -	03/2024	24	0	
205	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	321.99	03/2023 -	03/2024	12	0	
206	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	240.75	03/2022 -	03/2024	24	0	
207	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	165.38	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									
208	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	268.50	03/2019 12/2020	12/2020	21	0	
209	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.5 -	235.00	14.14	3/2019 -	12/2020	21	.21	
210	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	487.13	430.52	03/2018 -	03/2021	36	25.65	
211	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	315.22	03/2019 -	03/2021	24	0	
	<u>East Central Railways</u>									
212	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	708.22	03/2019 -	02/2021	23	0	
213	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,005.54	03/2020 -	03/2021	12	0	
214	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	194.21	03/2019 -	03/2021	24	0	
215	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	751.55	680.95	03/2012 -	05/2021	110	57.27	
216	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	154.70	03/2021 -	06/2022	15	62.06	
217	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,070.00	1,061.07	03/2012 -	11/2022	128	229.5	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
218	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	513.72	03/2020 -	03/2023	36	49.45	
219	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	760.55	03/2020 -	03/2023	36	0	
220	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	465.98	03/2020 -	03/2023	36	0	
221	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	299.09	03/2021 -	03/2024	36	63.37	
	<u>East Coast Railway</u>									
222	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.9 1,539.2	1,539.26	1,539.26	03/2019 02/202	12/2021	34	38.43	
223	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	218.99	03/2020 03/2021	03/2022	24	52.77	
224	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	891.78	03/2020 03/2023	03/2023	36	.07	
225	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	593.77	03/2022 03/2023	03/2023	12	0	
226	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	193.29	10/2020 03/2024	03/2024	41	0	
227	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	590.79	03/2022 03/2024	03/2024	24	0	
228	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 810.02	810.02	168.21	11/2018 03/2024	03/2024	64	15.45	
229	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	590.18	12/2018 03/2024	03/2024	63	0	
230	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	830.77	06/2021 03/2025	03/2025	45	137.8	
231	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,402.12	03/2009 03/2026	03/2026	204	29.71	
232	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	357.56	03/2022 03/2026	03/2026	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Eastern Railways</u>									
233	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28	0	
234	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	663.13	502.41	03/2020 -	03/2021	12	22.31	State Govt. is requested to deposit. for their balance share of cost for the project. But still deposition is awaited.
235	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	133	134.8	
236	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	899.24	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30KM between Kamarpukur and Jairambati is pending for possession to Railway. 2. Villagers of Vill- Bhabadighi, Hooghly District, are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.
237	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	954.89	12/2010 -	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 238.68 Cr. for their balance share of cost towards project Katwa-Bardhaman G.C.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
238	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects.
239	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	341.26	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
240	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2011	913.5 -	995.10	36.20	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to 41 nos. of un authorized crossings Amghata to Nabadwipghat work is dropped vide Bd's letter No. 2020/W- I/Compliance in Bd Mtg, dated 09.10.2020
241	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.51	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 km).- The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
242	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	180.03	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
243	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17	340.10	359.71	03/2017	03/2025	96	-6.87	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non availability of land.
244	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54	494.59	32.00	03/2005	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahat (9.75 Km) New line-- Work could not be started due to non availability of land
245	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96	680.68	162.75	02/2012	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Diamond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
246	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42	257.42	105.99	03/2014	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
247	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60	335.62	1.12	03/2017	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
248	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00	3,055.15	2,386.05	09/2018	12/2021	39	0	
249	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00	962.00	54.75	03/2020	03/2024	48	-81.5	
250	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00	4,970.11	849.31	03/2022	06/2024	27	117.23	
	<u>Metropolitan Rapid Transport Projects</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
251	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-82.67	
252	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
253	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102	48.06	
254	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,756.68	03/2004 -	03/2022	216	501.57	
North Central Railway										
255	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	32.02	
North East Frontier Railway										
256	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,084.69	8,600.00	619.18	12/2015 12/2023	03/2023	87	542.04	
257	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 -	800.00	777.27	03/2019 -	01/2021	22	154.78	
258	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 4,541.38	5,071.38	3,595.72	12/2008 -	02/2021	146	329.71	
259	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,007.06	03/2021 -	05/2021	2	115.07	
260	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 03/2022	03/2022	24	30.26	
261	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	10,584.54	03/2011 -	03/2023	144	175.34	
262	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,105.00	1,532.00	770.73	03/2019 -	03/2023	48	297.72	
263	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIAMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 7,114.55	6,911.44	1,045.72	03/2015 -	03/2023	96	197.07	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
264	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,047.51	2,042.51	29.84	03/2019 -	03/2023	48	13.6	
265	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	750.00	152.23	03/2020 -	03/2023	36	80.79	
266	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,375.36	03/2022 -	03/2023	12	32.15	
267	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	5,521.45	3,781.94	03/2014 -	12/2023	117	130.69	
268	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	967.13	03/2019 -	03/2024	60	302.54	
	<u>North Eastern Railway</u>									
269	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 417.0	426.74	475.97	04/2017 -	03/2021	47	-31.45	
270	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	80.32	12/2019 -	04/2021	16	-12.65	
271	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	28.80	04/2016 -	12/2021	68	.16	
272	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	497.06	01/2019 -	02/2022	37	61.8	
273	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	169.83	01/2022 -	03/2022	2	-38.88	
274	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
275	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
276	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-32.79	
	<u>North Western Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
277	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	395.00	306.94	12/2019 -	02/2021	14	60.52	
278	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	375.00	327.89	11/2019 -	03/2021	16	75.73	
279	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	287.94	03/2020 -	06/2021	15	0	
280	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	677.30	02/2019 -	11/2021	33	109.82	
281	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	780.00	155.47	03/2020 -	04/2022	25	30	
	<u>Northern Railway</u>									
282	ROHTAK-MEHAM HANSI [N22000272]NR,HARYANA	04/2011	207.00 -	893.45	25.47	02/2011 -	06/2021	14	211.31	
283	JALANDHAR-PATHANKOT - JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	605.00 -	859.00	50.50	03/2016 -	06/2021	03	37.44	
284	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	22,369.08	11/2002 -	12/2022	241	1017.96	
285	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	388.89	
286	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	1,540.13	241.62	03/2023 03/2025	03/2025	24	369.35	
	<u>Rail India Technical And Economic Service</u>									
287	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 06/2021	06/2021	15	0	
	<u>Rail Vikas Nigam Ltd.</u>									
288	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,479.93	03/2020 -	03/2021	12	281.93	
289	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,280.16	03/2019 -	06/2021	27	51.02	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
290	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	950.00	786.37	03/2016 -	12/2021	69	50.15	
291	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	21	111.91	
292	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,251.62	03/2020 -	12/2021	21	-7.28	
293	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,450.82	12/2020 -	12/2021	12	23.55	
294	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	1,868.89	1,726.74	12/2021 -	03/2022	3	20.68	
295	VIJAYWADA-GUDUGOL/NSC BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,035.07	03/2020 -	03/2022	24	124.58	
296	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	102.92	
297	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	62.89	
298	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	54.24	
299	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	5.98	
300	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	833.10	03/2023 -	12/2024	21	0	
301	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,629.88	03/2016 -	03/2025	108	7.78	
302	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,002.79	03/2016 -	03/2025	108	59.22	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
303	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00	22,716.11	2,555.91	12/2024	03/2025	3	40.08	
304	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42	2,733.86	40.46	03/2014	12/2025	141	18.95	
305	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67	3,327.72	1,122.68	12/2024	12/2026	24	42.47	
	<u>South Central Railway</u>									
306	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTISTATE	04/2010	704.31	927.94	517.35	03/2020	06/2021	15	31.75	
307	MANMAD-PARBHANI-NAIDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA	04/2007	1,197.15	449.35	7.09	03/2022	12/2022	9	275.34	
308	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTISTATE	04/1997	1,723.00	3,472.59	1,078.84	03/2000	03/2023	276	101.54	
309	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20	2,120.16	746.71	03/2009	03/2024	180	102.85	
310	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTISTATE	04/2012	1,856.95	1,952.68	487.47	03/2023	03/2025	12	5.16	
311	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTISTATE	04/2008	2,132.77	2,132.77	346.93	03/2014	03/2024	120	0	
312	KAZIPET-BALHARSHA - [N22000367]SCR, MULTISTATE	04/2015	2,063.03	2,063.03	1,222.16	03/2021	03/2024	36	0	
313	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00	3,887.48	984.35	03/2022	03/2025	24	7.06	
314	MANOHARABAD-KOTHPALLI NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48	1,160.48	466.96	03/2010	03/2025	180	0	
315	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70	2,643.25	1,191.09	03/2021	03/2025	48	15.49	
	<u>South East Central Railway</u>									
316	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTISTATE	02/1997	511.86	2,005.25	1,777.22	04/2020	04/2021	12	291.76	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
317	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93	1,268.32	941.56	02/2019 12/2021	12/2021	34	116.46	
318	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 2,753.05	3,524.81	952.24	03/2023 12/2023	12/2023	9	84.69	
319	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 2,135.34	2,135.34	351.35	03/2021 12/2023	12/2023	33	8.23	
320	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	1,370.94	470.49	12/2021 12/2023	12/2023	24	.07	
321	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2011	2,905.00 2,952.50	1,096.00	39.79	12/2021 12/2024	12/2024	6	378.6	
	<u>South Eastern Railway</u>									
322	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	295.76	12/2018 12/2018	06/2021	30	38.92	
323	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	795.27	03/2020 03/2020	12/2021	21	35.38	
324	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20	1,993.24	642.92	03/2021 03/2021	12/2023	33	15.6	
325	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00	1,009.00	7.96	03/2015	03/2025	120	54.99	
326	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003	03/2030	324	130.97	
	<u>South Western Railway</u>									
327	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00	783.00	607.76	03/2020	01/2021	10	35.47	
328	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59	1,870.41	1,274.19	03/2019	03/2021	24	15.84	
329	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43	1,147.00	877.08	03/2020	06/2021	15	33.31	
330	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94	1,140.94	1,119.20	03/2020	11/2021	20	-1.38	
331	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30	986.30	307.53	03/2016	12/2023	93	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
332	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	34.85	03/2016 -	12/2023	93	0	
333	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	
334	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
335	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	273.30	12/2018 -	12/2024	72	0	
	<u>Southern Railway</u>									
336	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	332.00	239.19	04/2014 01/2021	12/2020	80	77.29	
337	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	253.33	
338	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-23.24	
339	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	102.11	
340	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	693.14	03/2020 -	03/2025	60	465.83	
341	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,583.77	02/2019 -	03/2025	73	301.67	
342	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
343	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	232.66	03/2019 -	12/2027	105	1699.64	
	<u>West Central Railway</u>									
344	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	24	585.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
345	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93	1,762.94	1,032.58	03/2020	03/2023	36	-06	Work is suffering badly on this Critical project due to pending forest land/wildlife clearances. The track length of 118.98 Km out of 257 km is affected. The detail position is as under: 1. Niwas Road to Deoragram: Forest land 46.067 Ha from Railway Km 1261 to 1301 under DFO Singrauli in isolated patches. Application has been uploaded on Sep'2018. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 2055 Nos. trees cutting have been submitted on 18.06.2020 and 21.07.2020. However, APCCF/Bhopal vide letter dated 31.07.2020 has sought clarifications from MOEF. MOEF vide letter dated 24.09.2020 has clarified that case need to be processed further in FCA. GM/WCR vide letter dated 09.10.2020 has requested Railway Board to intervene in this matter. A meeting was held in Collector Singrauli office on 12.12.20. This meeting was chaired by Hon'ble MP/ Sidhi Smt Riti Pathak. Collector Singrauli has been requested to expedite this proposal. 2. Vijaysota to Beohari: Forest Land 66.69 Ha under DFO Shahdol from Rly Km 1162 to 1189 in isolated patches. Application has been uploaded in Feb'2019. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
346	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23	2,478.23	477.93	03/2022	03/2023	12	0	
347	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	273.37	03/2022	03/2023	12	114.32	
348	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66	8,248.50	2,131.17	05/2008	03/2025	202	3230.57	
	<u>Western Railway</u>									
349	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	1,017.91	453.03	03/2020 12/2020	12/2020	9	47.13	
350	BHILDI-VIRAMGAM GAU L CONVERSION INCLUDING GC OF MAHESANA-TARANGA HALL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	51.5 890.7	890.76	38.89	03/2019 03/2020	10/2021	31	31.51	
351	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	1,389.05	1,096.41	03/2021 03/2022	03/2022	12	33.93	
352	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	1,002.39	578.34	03/2021 12/2022	12/2022	21	0	
353	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 411.62	411.62	125.76	03/2012 03/2023	03/2023	132	29.34	
354	CHOTTADEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	1,347.26	883.18	03/2022 03/2023	03/2023	12	0	
355	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48	329.77	
356	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	232.01	06/2020 03/2023	03/2023	33	-13.76	
357	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	1,959.74	1,760.97	03/2020 12/2023	12/2023	45	136.19	
358	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	5,912.40	2,118.69	03/2022 03/2024	03/2024	24	68.75	
359	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	860.64	03/2022 03/2025	03/2025	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		2,02,957.83	3,31,316.06	1,52,743.26					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
360	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10	293.10	146.46	08/2020	08/2021	12	0	
361	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 112.00 TO KM 114/618 OF NH-4 IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41	992.67	890.74	03/2011	12/2020	117	58.98	
362	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59	151.59	282.56	08/2013	12/2020	88	0	
363	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27	166.27	243.59	08/2013	12/2020	88	0	
364	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28	269.14	274.06	02/2013	12/2020	94	47.65	
365	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59	1,069.59	663.50	10/2019	12/2020	14	0	
366	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61	350.61	323.06	01/2017	12/2020	47	0	
367	REHABILITATION AND UPGRADEATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09	386.09	199.35	05/2016	12/2020	55	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
368	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	288.92	01/2018 11/2020	12/2020	35	0	
369	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	199.98	174.35	08/2016 -	12/2020	52	0	
370	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 634.30	536.65	531.46	12/2019 12/2020	12/2020	12	0	
371	REHABILITATION AND UPGRADATION OF TULIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50	249.50	82.51	05/2019 -	12/2020	19	0	
372	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	322.24	292.10	09/2014 12/2020	12/2020	75	72.36	
373	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	143.96	10/2019 -	12/2020	14	0	
374	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	731.50	341.61	10/2016 12/2020	12/2020	50	17.04	
375	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	191.21	117.80	11/2019 01/2021	01/2021	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
376	REHABILITATION AND UPGRADE OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	403.01	11/2018 04/2021	01/2021	26	0	
377	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	124.81	03/2018 02/2021	02/2021	35	0	
378	REHABILITATION AND UPGRADE OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	235.91	167.93	02/2018 02/2021	02/2021	36	0	
379	UPGRADATION OF PACIORE, SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	105.89	02/2018 02/2021	02/2021	36	0	
380	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	162.62	03/2019 -	02/2021	23	0	
381	REHABILITATION AND UPGRADE OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	173.13	08/2018 06/2021	02/2021	30	0	
382	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	141.54	09/2020 -	02/2021	5	0	
383	REHABILITATION AND UPGRADE OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	245.69	06/2017 02/2021	02/2021	44	0	
384	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
385	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	398.38	01/2020 01/2021	03/2021	14	0	
386	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 173.41	173.41	139.19	08/2018 03/2021	03/2021	31	4.33	
387	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	254.30	78.32	10/2020 -	03/2021	5	0	
388	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 226.8	226.88	160.76	08/2018 03/2021	03/2021	31	4.45	
389	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	151.12	03/2018 01/2021	03/2021	36	0	
390	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	191.67	07/2018 03/2021	03/2021	32	0	
391	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	03/2021	37	0	
392	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	03/2021	36	0	
393	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	635.33	06/2019 03/2021	03/2021	21	0	
394	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	99.57	08/2018 03/2021	03/2021	31	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
395	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95	163.95	116.47	04/2018	03/2021	35	0	
396	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	199.35	01/2020	03/2021	14	0	
397	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30	288.30	83.53	08/2020	03/2021	7	0	
398	REHABILITATION AND UPGRADATION OF NH 40 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	477.10 527.60	527.60	32.36	08/2016	03/2021	55	6.14	
399	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	544.00	397.32	09/2016	03/2021	54	14.24	
400	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	435.61	73.30	07/2016	03/2021	56	-3.83	
401	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79	423.79	252.15	01/2018	03/2021	38	0	
402	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02	496.02	226.59	03/2015	03/2021	72	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
403	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	65.21	05/2019 03/2021	03/2021	22	0	
404	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	235.01	11/2017 03/2021	03/2021	40	0	
405	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	728.49	05/2017 -	04/2021	47	77.26	
406	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	13.84	12/2017 04/2021	04/2021	14	0	
407	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	29.65	03/2018 04/2021	04/2021	37	0	
408	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	218.70	90.68	11/2020 04/2020	04/2021	5	0	
409	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	473.71	05/2016 08/2021	04/2021	59	0	
410	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM. 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	370.30	266.58	06/2018 -	04/2021	34	0	
411	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	57.82	09/2018 -	04/2021	31	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
412	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	181.10	04/2020 -	04/2021	12	-8.28	
413	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	242.95	09/2019 11/2020	05/2021	20	0	
414	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	488.46	07/2018 05/2021	05/2021	34	0	
415	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	170.57	34.68	11/2020 -	05/2021	6	0	
416	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021	44	0	
417	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	
418	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021	128	93.8	
419	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	354.95	08/2017 06/2021	06/2021	46	0	
420	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	113.56	03/2017 06/2021	06/2021	51	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
421	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	173.84	09/2019 06/2021	06/2021	21	0	
422	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	341.79	192.06	05/2018 -	06/2021	37	0	
423	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	305.76	03/2018 06/2021	06/2021	39	9.23	
424	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	333.9 -	348.95	100.57	08/2016 07/2021	07/2021	59	0	
425	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	322.48	260.36	07/2020 -	08/2021	13	0	
426	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	49.85	03/2018 09/2021	09/2021	42	0	
427	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	24.84	
428	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
429	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28	11.18	
430	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	213.97	24.14	08/2019 -	11/2022	39	33.51	
431	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTIMOD - [N24000308]MoRTH, MIZORAM	08/2010	193.69 -	327.92	295.96	10/2010 05/2016	06/2021	128	69.3	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
432	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM	05/2015	454.89 -	454.89	239.35	05/2018 -	12/2020	31	0	
433	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 -	168.32	43.28	04/2017 -	02/2021	46	0	
434	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 -	180.57	44.85	04/2017 -	02/2021	46	0	
435	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 -	216.71	26.84	04/2017 -	02/2021	46	0	
436	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	167.28	22.06	04/2017 -	02/2021	46	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
437	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	127.41	04/2017 03/2018	03/2021	47	0	
438	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	170.00	01/2016 -	04/2021	63	0	
439	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	457.77	151.85	10/2018 -	10/2021	36	-11.55	
440	CONSTRUCTION OF TWO LANE WITH HARD SHOULDER OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL, NAGALAND	03/2013	215.1 -	215.12	68.26	09/201 -	11/2021	38	0	
441	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	407.30	56.22	06/2018 -	12/2021	42	-6.88	
442	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	398.06	103.86	06/2018 -	12/2021	42	-14.12	
443	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	315.03	62.00	09/2018 -	12/2021	39	0	
444	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	240.64	77.08	09/2018 -	12/2021	39	0	
445	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	49.94	09/2018 -	12/2021	39	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
446	CONSTRUCTION OF MEKAROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10	1,253.10	204.77	03/2017	03/2022	60	0	
447	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30	239.30	58.12	09/2018	05/2022	44	0	
448	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57	339.57	89.79	09/2018	07/2022	46	0	
449	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL, NAGALAND	03/2018	285.68	285.68	50.62	09/2018	09/2022	48	0	
450	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL, NAGALAND	03/2018	272.89	272.89	25.76	09/2018	10/2022	49	0	
451	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL, NAGALAND	03/2018	323.98	323.98	28.46	09/2018	11/2022	50	0	
	<u>National Highways Authority Of India</u>									
452	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00	1,827.15	2,082.19	06/2018	12/2020	30	68.71	
453	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00	230.00	355.20	04/2008	12/2020	152	10.58	
454	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36	469.31	459.07	01/2014	12/2020	83	61.08	
455	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51	478.00	315.11	10/2013	12/2020	86	-11	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
456	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	417.68	433.68	01/2016 12/2020	12/2020	59	18.88	
457	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	0	
458	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	815.94	06/2019 -	12/2020	18	0	
459	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	32	0	
460	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	415.67	08/2018 -	12/2020	28	0	
461	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	390.36	07/2018 -	12/2020	29	0	
462	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	1,664.20	936.78	04/2020 -	12/2020	8	0	
463	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	1,108.00	1,425.26	08/2019 -	12/2020	16	16.55	
464	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	683.51	03/2020 -	12/2020	9	0	
465	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	204.65	213.11	09/2017 -	12/2020	39	-45.34	
466	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	591.00	575.34	11/2013 12/2020	01/2021	86	15.53	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
467	FOUR LANE OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	897.03	956.62	11/2018 07/2019	01/2021	26	-37	
468	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	619.77	09/2017 -	01/2021	40	0	
469	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	89.63	03/2019 -	02/2021	23	0	-
470	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 - 322.2	848.45	209.77	03/2020	02/2021	11	0	
471	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	8	1.78	
472	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	425.56	08/2017 -	02/2021	42	0	
473	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	447.94	10/2017 -	02/2021	40	0	
474	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,540.00	03/2013 -	03/2021	96	0	
475	SIX LANE OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021	81	0	
476	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71	52.73	
477	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	520.05	06/2018 10/2020	03/2021	33	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
478	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	525.68	08/2019 -	03/2021	19	0	
479	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	59.61	03/2019 -	03/2021	24	0	
480	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	795.00	04/2020 -	03/2021	11	3.95	
481	FOUR LANING OF GUNDUGOLANU-DEVARIPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2013	1,532.61 -	1,499.00	1,976.11	03/2020 -	04/2021	1	63.05	
482	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	45.26	05/2013 -	05/2021	96	-55.37	
483	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,239.99	08/2013 -	05/2021	93	0	
484	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-3.27	
485	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	419.66	09/2017 -	05/2021	44	9.67	Additional land acquisition
486	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	730.97	614.25	05/2018 06/2021	06/2021	37	37.63	
487	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	690.17	572.57	05/2018 06/2021	06/2021	37	16.34	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
488	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	333.68	05/2018 04/2019	06/2021	37	-2	
489	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	817.80	03/2020 -	06/2021	15	10.24	
490	REHABILITATION AND UPGRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	0	
491	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	0	
492	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	714.5 -	756.27	30.92	3/2020 -	09/2021	18	.23	
493	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.25	06/2020 -	09/2021	15	0	
494	4-LANNING OF STHIYATHOPUCHOOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	549.62	09/2017 -	09/2021	48	0	
495	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,852.94	08/2013 -	12/2021	100	0	
496	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	184.90	03/2019 12/2021	12/2021	33	0	
497	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	298.39	07/2019 06/2021	12/2021	29	0	
498	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	313.00	07/2019 06/2021	12/2021	29	0	
499	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	276.50	03/2019 01/2021	12/2021	33	-25.48	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
500	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97	990.97	302.88	12/2019	12/2021	24	0	
501	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64	950.64	194.95	08/2017	02/2022	54	0	
502	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40	701.40	95.50	03/2019	03/2022	36	0	
503	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00	847.00	106.90	03/2021	04/2022	35	0	
504	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00	1,047.00	172.62	05/2020	05/2022	24	0	
505	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00	3,379.45	2,901.20	03/2014	12/2022	105	18.66	Land Acquisition issue.
	Total		88,846.23	93,679.21	58,909.91					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
506	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16	431.16	-	06/2021	11/2021	5	0	
	<u>Central Public Works Department</u>									
507	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20	248.20	80.10	03/2018	12/2020	33	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Department Of Telecommunication</u>									
508	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00	24,664.00	15,239.00	07/2015	06/2021	71	84.97	
	Total		14,013.36	25,343.36	15,319.10					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
509	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00	12,787.00	8,276.69	12/2018	11/2022	47	18.69	
	<u>Central Public Works Department</u>									
510	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAKE ADJOINING PRAGATI MALL - [N28000079]CPWD,DELHI	07/2012	884.30	884.30	812.00	12/2015	12/2020	60	0	
511	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56	238.56	157.67	05/2020	02/2021	9	0	
512	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33	197.33	94.18	04/2019	06/2021	26	0	
513	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00	422.00	28.26	03/2021	07/2021	4	0	
514	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00	1,100.80	34.82	07/2021	09/2021	2	-6.71	
515	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00	392.00	63.67	08/2020	12/2021	16	0	
	<u>Chennai Metro Rail Ltd</u>									
516	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00	3,770.00	2,750.00	03/2018	12/2020	33	0	
	<u>Delhi Metro Rail Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
517	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,843.96	03/2016 -	03/2021	60	0	
518	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	503.33	12/2020 -	09/2021	9	0	
	Total		57,007.19 -	58,941.99	52,564.58					
	<u>WATER RESOURCES</u>									
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
519	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	225.77	249.54	03/2020 -	12/2020	9	0	
520	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2017	184.93 -	184.93	63.36	04/2021 -	12/2020	3	0	
521	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	191.62	43.01	11/2020 -	12/2020	1	0	
522	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	-	08/2021 -	12/2021	4	0	
	<u>Delhi Jal Board</u>									
523	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	515.07	278.37	01/2021 -	06/2021	5	0	
524	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	50.75	12/2021 -	12/2022	12	0	
525	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	73.13	02/2022 -	12/2022	10	0	
	<u>Hindustan Steelwork Construction Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
526	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00	721.37	712.37	03/2015	03/2021	72	-24.54	The work could not start within stipulated time on Dec 2005 as MoU due to huge delay in Land acquisition, Rehabilitation & clearance of Encroachment from client side (WRD). 98.5 % of value of work completed but till date balance portion work stopped due to land acquisition problem. Maximum stretches' Work Completed and communicated to concern division for take over since 03 years.
	<u>Kolkata Metropolitan Development Authority</u>									
527	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76	274.76	89.36	12/2019	12/2020	12	0	
528	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32	272.32	202.18	04/2020	12/2020	8	0	
	<u>Polavaram Project Authority</u>									
529	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04	55,548.87	16,568.13	03/2020	04/2022	25	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									
530	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UP JalNigam, UTTAR PRADESH	10/2016	370.40	370.40	323.09	08/2020	12/2020	4	0	
531	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UP JalNigam, UTTAR PRADESH	02/2017	161.31	161.31	50.65	11/2019	12/2020	13	0	
532	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP JalNigam, UTTAR PRADESH	02/2011	279.91	279.91	222.79	12/2019	12/2020	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
533	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	460.45	87.15	12/2020 -	01/2021	1	0	
534	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UPJalNigam,UTTAR PRADESH	12/2018	857.26 -	842.25	-	08/2021 -	06/2022	10	-1.75	
535	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 -	298.12	-	07/2021 -	06/2022	11	0	
	Total		15,955.05	61,103.24	19,213.88					
	FLASH REPORT									
	DEFENCE PRODUCTION									
	Central Public Works Department									
536	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	115.20	02/2020 06/2021	06/2021	16	0	
	Total		246.31 -	246.31	115.20					
	COMMERCE AND INDUSTRY									
	Delhi Mumbai Industrial Corridor									
537	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	13,812.30	7,305.07	09/2019 01/2014	07/2021	22	9.8	
	India International Convention And Expo Centre									
538	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	5,178.00	2,334.57	12/2019 -	07/2021	19	8.49	
	Total		17,352.09 -	18,990.30	9,639.64					
	HUMAN RESOURCE DEVELOPMENT									
	Central Public Works Department									
539	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	226.16	11/2014 -	12/2020	73	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
540	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	350.69	258.72	04/2019 -	01/2021	21	19.28	
541	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	458.38	07/2019 12/2020	03/2021	20	1.85	
542	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6	10.22	
543	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	0	
544	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 171.72	171.72	53.94	03/2020 -	06/2021	15	0	
545	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	0	
546	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	185.61	06/2017 -	09/2021	51	.57	
547	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	387.83	167.01	05/2020 -	10/2021	17	-9.81	
548	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	122.02	03/2022 -	06/2022	3	0	
549	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
550	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	0	
551	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 04/2023	01/2023	4	0	
	<u>Rail India Technical And Economic Service</u>									
552	CONSTRUCTION AND DEVELOPMENT OF NATIONAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32	626.26	-	09/2014	12/2020	75	29.31	
	Total		6,261.73 -	6,450.16	1,874.48					
	<u>HOME AFFAIRS</u>									
	<u>Central Public Works Department</u>									
553	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	179.16	168.45	04/2018 -	12/2020	32	10	
554	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	841.88	10/2019 -	09/2021	23	64.04	
	Total		1,382.09 -	2,179.16	1,010.33					
	<u>RURAL DEVELOPMENT</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
555	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2021	62	3.96	
556	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	207.12	189.79	12/2016 -	03/2021	51	2.23	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
557	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	03/2021	51	0	
	Total		527.83 -	538.27	459.61					
	<u>CULTURE DEVELOPMENT</u>									
558	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	144.00	09/2017 -	03/2021	42	0	Non receipt of payment from Client
	Total		151.33	151.33	144.00					
	Grand Total		827.03.6	11,70,901.33	6,83,81.06					

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	04/2017	59(R3)	1/6
	Total		272.73	272.73	153.75				1/6
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
2	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80	229.80	79.45	-	05/2022	0(R3)	16/26
3	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.00	730.20	422.20	-	05/2023	0(R3)	12/17
	Total		818.00	960.00	127.65				28/43
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
4	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84	268.84	228.89	-	12/2020	-	0/0
5	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01	249.07	216.09	-	01/2021	-	0/0
6	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	156.64	111.58	-	03/2021	-	0/0
7	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	333.61	-	06/2021	-	0/0
8	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	424.09	-	06/2021	-	0/0
9	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	427.72	-	06/2021	-	0/0
	Total		2,510.41	2,510.55	1,741.98				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
10	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00	735.20	379.45	-	03/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
11	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	1,470.50	1,095.55	- -	03/2021	-	0/0
12	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 -	3,500.00	3,494.01	- -	03/2022	-	0/0
13	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	614.45	333.16	- -	03/2022	-	0/0
14	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,858.75	383.64	- -	03/2022	-	0/0
15	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	1,483.14	1,177.09	- -	03/2022	-	0/0
16	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	519.33	265.08	- -	02/2023	-	0/0
17	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	2,066.78	1,510.98	- -	03/2023	-	0/0
18	KODERMA-TILAINIA (NL), ECR - [220100305]ECR,JHARKHAND	04/2003	459.1 -	1,615.87	71.11	- -	03/2023	-	0/0
19	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	23.74	- -	03/2023	-	0/0
20	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	-	0/0
21	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
<u>Eastern Railways</u>									
22	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	418.09	412.89	- -	03/2021	-	0/0
23	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	270.72	279.67	- -	03/2022	-	0/0
24	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	272.20	227.07	- -	03/2022	-	0/0
25	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	332.10	- -	03/2024	-	0/0
26	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
27	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	11.05	- -	03/2025	-	0/0
28	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
29	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.12	- -	03/2025	-	0/0
30	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
31	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	- -	03/2025	-	0/0
32	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	- -	03/2025	-	0/0
33	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
34	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
35	NEW BG LINE FROM MURGHEANI TO BIRATNAGAR - [N22000201]NFR,MULTI STATE	04/2011	244.52 -	333.00	227.09	- -	03/2021	-	0/0
36	KISHANGANJ JALALGARH, NER, NER - [N22000101]NFR,BIHAR	04/2000	333.70 -	300.00	6.74	- -	03/2022	-	0/0
	<u>North Eastern Railway</u>								
37	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	714.34	56.54	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
38	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	791.39	567.14	- -	03/2023	-	0/0
39	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
40	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	112.95	- -	09/2023	-	0/0
41	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 196.17	359.00	111.51	- -	03/2024	-	0/0
42	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	<u>South Eastern Railway</u>								
43	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
44	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,967.00	66.44	- -	12/2023	-	0/0
45	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	12/2023	-	0/0
46	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	12/2023	-	0/0
47	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	- -	12/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
48	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	167.50	.34	-	12/2023	-	0/0
49	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	367.77	-	-	12/2023	-	0/0
50	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00	3,911.65	156.88	-	12/2024	-	0/0
51	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30	2,432.50	1,096.12	-	03/2025	-	2/2
	<u>Southern Railway</u>								
52	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98	961.09	873.72	-	02/2021	0(R3)	0/0
53	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41	450.73	340.21	-	09/2021	-	0/0
54	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14	457.08	439.49	-	12/2021	-	0/0
55	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2007	321.52	2,311.00	228	-	03/2024	0(R3)	0/0
56	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68	559.95	319.22	-	03/2025	-	0/0
57	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	582.83	233.89	-	12/2025	-	0/0
	<u>Western Railway</u>								
58	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10	844.10	172.03	-	03/2024	0(R3)	0/0
	Total		25,127.57	45,773.27	15,846.10				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
59	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24	904.82	739.41	-	12/2020	-	0/0
60	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13	178.13	110.91	-	03/2021	-	0/0
61	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51	390.51	249.75	-	12/2020	6(R3)	0/0
62	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	65.83	-	09/2021	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL PRADESH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06	434.06	172.89	-	12/2020	-	2/4
64	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02	199.02	14.21	-	02/2021	-	0/4
65	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88	184.88	6.85	-	02/2021	-	0/4
66	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51	553.51	88.81	-	09/2021	-	0/4
67	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06	175.06	62.27	-	04/2022	-	0/4
68	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12	176.12	54.56	-	04/2022	-	0/4
National Highways Authority Of India									
69	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21	1,087.00	672.82	-	12/2020	-	0/0
70	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00	207.00	43.23	-	12/2020	-	0/0
71	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13	807.00	617.58	-	12/2020	-	0/0
72	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56	392.00	353.42	-	12/2020	-	0/0
73	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73	1,308.73	293.43	-	12/2020	-	0/0
74	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30	1,484.30	356.66	-	06/2021	-6(R3)	0/0
75	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65	1,069.65	611.71	-	01/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
76	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,727.66	1,672.28	- -	01/2021	-	3/4
77	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
78	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	1,339.00	761.37	- -	01/2021	-	2/3
79	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	193.26	- -	01/2021	-	0/0
80	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM. 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	1,449.00	394.36	- -	01/2021	-	0/0
81	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,145.31	1,265.00	- -	02/2021	-	0/0
82	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	565.09	495.25	- -	02/2021	-	0/0
83	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	-	0/0
84	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	1,261.05	299.09	- -	03/2021	-	0/0
85	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	1,005.08	-	- -	03/2021	-	0/0
86	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	621.00	564.85	- -	04/2021	-	2/3
87	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	86.83	- -	04/2021	-	0/0
88	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	145.70	- -	04/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
89	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,547.00	- -	05/2021	-	0/0
90	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	240.60	- -	05/2021	-	0/0
91	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 1,118.19	478.74	127.42	- -	05/2021	-	0/0
92	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	895.53	- -	06/2021	-	0/0
93	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+ 00 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	227.63	- -	06/2021	-	0/0
94	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	127.61	- -	06/2021	-	0/0
95	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	276.59	- -	06/2021	-	0/0
96	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	260.60	- -	06/2021	-	0/0
97	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0
98	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	102.70	- -	06/2021	-	0/0
99	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	25.40	- -	06/2021	-	0/0
100	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
101	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	456.80	- -	07/2021	-	0/0
102	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	841.64	- -	07/2021	-	2/4

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
103	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	235.12	- -	07/2021	-	1/4
104	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0
105	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,166.26	268.34	- -	07/2021	-	0/0
106	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
107	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	273.52	- -	07/2021	-	0/0
108	CONSTRUCTION OF 5 LANE VADODARA KIM EXPRESS VAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,427.34 -	1,477.64	584.17	- -	07/2021	-	0/0
109	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	931.21	183.69	- -	07/2021	-	0/0
110	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	142.26	- -	07/2021	-	0/0
111	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	71.45	- -	07/2021	-	0/0
112	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	200.47	- -	08/2021	-	3/4
113	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	380.86	- -	08/2021	-	0/1
114	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	191.40	- -	08/2021	-	0/0
115	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	221.00	- -	08/2021	-	0/1

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
116	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
117	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,290.79	- -	09/2021	-	0/0
118	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	284.33	- -	09/2021	-	0/0
119	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	126.45	- 06/2021	09/2021	3(R3)	0/0
120	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
121	SIX LANING OF ANAKAPALLE RAM PETHI ANAKAPALLI SECTION OF NH-5 NEW NH-6 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	03/2018	1,950.00 -	1,950.00	1,145.62	- -	10/2021	-	0/0
122	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,080.15	- -	11/2021	-	0/0
123	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	122.48	- 08/2021	11/2021	3(R3)	0/0
124	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
125	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	115.40	- -	12/2021	-	0/0
126	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	220.12	- -	02/2022	-	0/0
127	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	181.52	- -	03/2022	-	0/1
128	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	332.04	- -	03/2022	-	0/0
	Total		60,615.09 -	62,385.07	30,963.51				17/53

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construction Corporation Ltd</u>								
129	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	553.56	- -	03/2022	-	0/9
	Total		2,694.00 -	2,694.00	553.56				0/9
	Grand Total		92,037.80	1,14,595.62	49,386.55				48/113

FLASH REPORT

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
2	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TA ABIRA II AND III OCP - [N06000185]NLC,ODISHA	07/2017	2,401.00 -	07/2020 -	04/2020
5	HADOLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.5 -	09/2019 -	-
6	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
9	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
	<u>Western Coal Fields Limited</u>				
10	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16 -	03/2020 -	03/2020
11	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA	06/2015	205.49 -	03/2020 -	03/2020
12	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA	11/2015	498.42 -	03/2020 -	03/2020
13	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020
14	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
15	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
16	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
	Total		14,596.14 -		
	<u>MINES</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Aluminum Company Limited (Nalco)</u>				
17	UTKAL D AND E COAL BLOCK - [N1000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		534.00 -		
	<u>STEEL</u>				
	<u>Rastriya Ispat Nigam Limited</u>				
18	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 336.00	08/2018 11/2020	11/2020
	Total		320.66 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
19	HALDIA LPG IMPORT FACILITY - [N1600023]BPCL,WEST BENGAL	03/2015	694.00 -	10/2018 02/2020	07/2020
	<u>Gas Authority of India Limited</u>				
20	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
21	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE	09/2016	1,879.00 -	06/2020 -	10/2020
22	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
23	FUEL QUALITY UPGRADEATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	10/2019 11/2020	11/2020
24	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
25	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT	08/2017	1,342.00 -	08/2020 -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Oil India Limited</u>				
27	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	-
	Total		11,868.64 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
28	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Thermal Power Corporation</u>				
29	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
30	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-
31	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
32	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-
33	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
34	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
35	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	-
36	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	-
37	ROORKEE PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,UTTAR PRADESH	05/2016	1,881.13 -	12/2018 -	-
38	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	11/2018 -	-
	<u>Power Grid Corporation Of India Limited</u>				
39	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 482.64	01/2019 04/2020	04/2020
40	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 04/2020	05/2020
41	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 04/2020	07/2020
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 06/2020	09/2020
43	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 06/2020	09/2020
44	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
45	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
46	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	-
47	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
48	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-
49	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
50	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
	Total		58,584.75 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
51	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
52	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
53	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
54	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
55	AIIMS OPD NEW - [N21000009]HSCC,DELHI	03/2014	238.65 -	07/2017 -	01/2020
	Total		1,387.70 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
56	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 03/2020	03/2020
	<u>Container Corporation Of India</u>				
57	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020
58	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
59	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
60	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
61	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
62	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
63	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	01/2020
64	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	09/2020
65	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
66	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
67	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
68	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
69	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
70	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
71	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
72	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
73	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
74	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
75	RAJGIRHIS-A TALAIYA (16KM) NCL. IMMEDIATE WARIS LAMPUR - [N22000175]ECR,BIHAR	04/1998	180.8 -	- -	-
76	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.3 -	- -	-
<u>Eastern Railways</u>					
77	PIRPAINTI-BHAGALPUR - [N22000222]ECR,MULTI STATE	04/2011	261.38 -	- -	05/2019
<u>Kolkata Metro Rail Corporation Limited</u>					
78	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
<u>Metropolitan Rapid Transport Projects</u>					
79	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
80	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
<u>North Central Railway</u>					
81	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
82	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
83	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
<u>North East Frontier Railway</u>					
84	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	-
85	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
86	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-
88	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
89	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-
	<u>North Eastern Railway</u>				
90	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
91	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
92	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
93	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
94	PANDARNA KUSHINAGAR VIA GORAKHPUR - NEW LINE [N22000460]NER,UTTAR PRADESH	04/2017	242.00 -	01/2018 -	-
	<u>North Western Railway</u>				
95	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
96	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
97	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-
98	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
99	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
100	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
101	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
102	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
103	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-
104	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
	<u>Railway Electrification</u>				
105	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
107	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
108	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
109	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
110	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
<u>South East Central Railway</u>					
111	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- 08/2020	08/2020
112	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 10/2020	10/2020
<u>South Eastern Railway</u>					
113	RAIKHARSIAN-CHANDRAPUR 3RD LINE (10 KM) JHARKHAND - [N2200032]SER,JHARKHAND	04/2012	148.7 -	12/2016 -	08/2020
114	HOWRAH-AMARA CHAMPAD,NGALNE (SLR) - [220100208]SER,WEST BENGAL	04/1974	393.40 154.30	03/2007 03/2007	-
115	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
<u>South Western Railway</u>					
116	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	-
<u>Southern Railway</u>					
117	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
118	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
119	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
120	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
121	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-
122	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
123	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-
124	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
125	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.00	- -	-
126	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
127	ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Western Railway</u>				
128	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
129	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
130	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
131	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
132	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
133	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	To all		10,295.29		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
134	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
135	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	08/2020
136	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 -	02/2017 06/2021	02/2019
137	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
138	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 07/2021	05/2019
139	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
140	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 05/2021	08/2019
141	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 -	11/2017 04/2021	11/2019
142	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
143	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	04/2020
144	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 -	08/2018 05/2021	08/2020
145	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 06/2021	08/2020
146	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 07/2021	09/2020
147	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
148	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 10/2020	10/2020
149	REHABILITATION AND UPGRADATION OF NH 201 FROM KM 177.500 TO 178.944 - ARRIGAT TO BALARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	43.52 512.7	09/2016 10/2020	10/2020
150	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
151	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	11/2020
152	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	11/2020
153	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	11/2020
154	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
155	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020
156	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	11/2020
157	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	11/2020
158	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	11/2020
159	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
160	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
161	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
162	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
163	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
164	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
165	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
166	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
167	CONST. OF MARGOA BYPASS FROM KM.68/0 (CH.00/00) TO KM 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.1 -	- -	-
168	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
169	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH.0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
170	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
171	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
172	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
173	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
174	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
175	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
176	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
177	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
178	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
179	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 03/2021	-
180	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
181	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
182	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
183	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
184	WIDENING OF 2(TWO) LANING OF LONG ENG-CHANTO GYA ROAD, MON TALU- JERANGKONG ROAD, PHU - PFUTER ROAD - [N2400031]MoRTH,NAGALAND	12/2010	296.00 -	02/2011 -	-
185	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
186	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
187	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
188	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
189	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
190	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
191	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
192	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
193	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
194	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
195	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
196	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
197	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
198	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
199	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
200	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
201	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-
202	BAMITHA-SATANA (2L P) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.8 -	- -	-
203	2 LANING OF JALMDING-DIPHULMANA ROAD (L=54.37 KM), HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.2 -	02/2011 -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
205	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
206	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
207	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
208	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM	11/2014	218.31 -	02/2018 -	-
209	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
210	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
211	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
212	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
213	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
214	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
215	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
216	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
217	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
218	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
219	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
220	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377/700 TO 471/300 (BIHARMAHUR-TA) [N24000527]MoRTH,ODISHA	12/2011	191.0 -	03/2015 -	-
221	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
222	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
223	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
224	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
225	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
226	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
227	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
228	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
229	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
230	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
231	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
232	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
233	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
234	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
235	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
236	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
237	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
238	REHABILITATION AND UPGRADING OF NH-14 FROM KM 0.0 TO KM 68.20 (PALI, HARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
239	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
240	WIDENING OF EXISTING SINGLE TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
241	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
242	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
243	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
244	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
245	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
246	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
247	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
248	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
249	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
250	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
251	REHABILITATION AND UPGRADE OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
252	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
253	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
254	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
255	REHABILITATION AND UP GRADATION OF 2 LANE WITH PAVED SHOULDER OF MUKHI-JAWAHAR SINGH VALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2020	21.24 -	03/2020 -	-
256	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-
257	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
258	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
259	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
260	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
261	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
262	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
263	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
264	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN - [N24000920]MoRTH,GUJARAT	03/2016	223.67 -	02/2017 -	-
265	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]MoRTH,GUJARAT	03/2016	208.34 -	02/2016 -	-
266	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
267	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
268	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
269	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
270	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
271	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
272	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-
273	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-
274	REHABILITATION AND UPGRADATION OF NEW NH-544D (C/O SH 30 FROM DESIGN CHAINAGE KM 0.00 TO 56.00) (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	293.12 294.00	07/2018 -	-
275	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
276	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
277	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
278	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-
279	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
280	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
281	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
282	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
283	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
284	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
285	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
286	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
287	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
288	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
289	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
290	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
291	REHABILITATION AND UPGRADATION OF HYDERABAD TO KALWAKURTHY ROAD TO METPAK SECTION OF NH- 65D FROM EXISTING - [N24000992]MoRTH,TELANGANA	02/2018	42.32 -	04/2020 -	-
292	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
293	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
294	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
295	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
296	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
297	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 232.90	10/2019 -	-
298	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
299	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
300	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
301	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
302	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
303	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
304	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
305	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
306	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
307	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
308	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
309	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
310	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
311	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
312	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.15 341.00	06/2019 -	-
313	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
314	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
315	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
316	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
317	AMDHI TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
318	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
319	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
320	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
321	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
322	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
323	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
324	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
325	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
326	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
327	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
328	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
329	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
330	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
331	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
332	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
333	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
334	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
335	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
336	JALGAON TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.99 -	11/2019 -	-
337	SHIRDI TO SHIRDI - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.31 -	07/2019 -	-
338	SALAIKHURD TO TIJORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
339	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
340	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
341	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
342	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
343	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
344	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
345	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
346	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
347	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
348	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
349	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
350	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
351	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
352	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
353	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
354	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
355	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
356	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
357	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
358	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
359	WADIGODRI TO DHANGRIIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
360	DHANGRIIMPRI TO JAIN AND AMBAD CHOWK TO MANH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.11 217.00	02/2020 -	-
361	PARBHANI TO GANGKHEDE - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.11 238.00	12/2019 -	-
362	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
363	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
364	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
365	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
366	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
367	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
368	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
369	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
370	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
371	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
372	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
373	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
374	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
375	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
376	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
377	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
378	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
379	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
380	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
381	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
382	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
383	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
384	MANGRUPUR TO MAHARASHTRA - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.19 222.00	12/2019 -	-
385	JALGAON TO NANDURBAR - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.61 177.00	12/2019 -	-
386	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
387	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
388	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
389	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
390	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
391	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
392	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
393	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
394	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
395	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
396	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
397	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
398	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
399	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
400	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
401	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
402	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
403	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
404	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
405	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
406	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
407	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
408	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.51 407.00	03/2019 -	-
409	INLAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.32 1,203.00	12/2019 -	-
410	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
411	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
412	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
413	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
414	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
415	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-
416	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
417	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
418	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
419	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
420	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
421	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
422	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
423	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
424	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
425	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
426	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
427	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
428	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
429	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
430	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
431	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 32.000 TO KM 379.555 OF NH-75 TO 2-LANE WITH P - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
432	REHABILITATION AND UPGRADATION OF KABRI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-75 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.06 215.00	03/2019 -	-
433	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-
434	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	-
435	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
436	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-
437	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
438	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
439	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-
440	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
441	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
442	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
443	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
444	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
445	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
446	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
447	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
448	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 386.40	10/2018 -	-
449	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 386.40	10/2018 -	-
450	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 118.65 TO 118.47 OF NH-15 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2017	325.01 -	02/2017 -	-
451	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
452	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
453	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
454	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
455	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
456	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
457	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
458	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	-
459	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-
460	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
461	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH, BIHAR	02/2019	2,926.42 -	- -	-
462	REHABILITATION AND UPGRADE OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH, UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
463	REHABILITATION AND UPGRADE OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH, UTTAR PRADESH	03/2018	306.59 -	- -	-
464	IMPROVEMENT AND UPGRADE OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH, UTTAR PRADESH	11/2018	281.45 -	- -	-
465	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH, CHANDIGARH	03/2010	179.89 271.00	03/2013 -	-
466	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH, CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
467	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDER WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0 - [N24001237]MoRTH, TAMIL NADU	01/2016	162.7 -	01/2016 -	-
468	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH, TAMIL NADU	05/2016	307.70 -	01/2017 -	-
469	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH, TAMIL NADU	03/2018	240.38 -	06/2019 -	-
470	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH, ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
471	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL, ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
472	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL, ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
473	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	08/2016 -	06/2020
474	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00 -	09/2018 -	08/2020
475	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL, ASSAM	06/2016	829.00 -	01/2019 -	-
476	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM	03/2015	168.39 -	11/2018 -	-
477	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM	10/2014	588.95 -	11/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
478	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	-
479	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
480	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
481	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
482	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
483	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
484	4 LANING FROM JAMULURI TO BISWANATH CHARIALI FROM KM 18 TO KM 208 OF NH 52 - [N24000431]NHIDCL,ASSAM	01/1991	520.00 -	- -	-
485	4 LANING FROM RANGAGARA TO KALIAHORTHALI FROM KM. 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.9 -	12/2018 -	-
486	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
487	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
488	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
489	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
490	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-
491	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
492	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
493	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
494	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	-
495	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
496	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
497	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
498	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
499	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
500	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
501	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
502	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.50 TO KM. 107.762 OF NH 213 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.91 -	10/2018 -	-
503	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
504	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
505	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
506	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
507	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	09/2018 -	-
508	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
509	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
510	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
511	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
512	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
513	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
514	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
515	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
516	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY- PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
517	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
518	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	-
519	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	-
520	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	-
521	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	-
522	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	-
523	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	-
524	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 10/2020	-
525	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	-
526	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
527	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
528	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
529	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
530	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
531	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
532	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
533	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-
534	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
535	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
536	BOARDSMANAMCHIN (BRIDGEHIND) JAMRAMPUR ROAD OF NH-52 (NEW NH-215) FROM KM 1.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	18.91 -	- -	-
537	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
538	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
539	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
540	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
National Highways Authority Of India					
541	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	05/2018
542	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
543	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
544	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
545	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
546	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
547	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
548	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
549	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019
550	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020
551	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
552	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
553	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
554	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
555	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020
556	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.25 OF NH-72) TO KM 17.300 - [N24000562]NHAI,UTTAR KASHMIR	03/2016	1,443.00 -	- -	08/2020
557	4-LANNING OF GAGAIHERI-SAMARANUI - YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	08/2020
558	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
559	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020
560	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
561	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 2,754.00	01/2018 12/2018	09/2020
562	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 2,173.74	- -	09/2020
563	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020
564	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
565	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
566	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020
567	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 08/2020	11/2020
568	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	11/2020
569	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2020
570	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	11/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
571	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
572	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
573	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020
574	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020
575	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	11/2020
576	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020
577	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
578	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.91 -	04/2009 -	-
579	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
580	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
581	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
582	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
583	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
584	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
585	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
586	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
587	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
588	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
589	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
590	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
591	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
592	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 671.30	02/2013 -	-
593	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
594	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
595	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
596	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
597	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
598	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
599	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
600	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
601	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
602	RAJNAGRI-RAJGA-JAMSAI-CHUPUR - [N24000215]NHAI, JHARHAND	12/2012	1,479.00 -	05/2015 -	-
603	ETAWAH CHAKERI - [N24000221]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
604	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
605	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
606	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
607	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
608	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
609	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
610	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-
611	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
612	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
613	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
614	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
615	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
616	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	-
617	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
618	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
619	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
620	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
621	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
622	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
623	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
624	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
625	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
626	GURGAON - KOTPUTLI - JALPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	672.40 -	10/2011 -	-
627	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	03/2018 09/2020	-
628	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
629	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
630	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
631	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
632	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
633	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
634	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
635	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
636	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
637	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
638	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
639	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-
640	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
641	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 1,182.94	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
642	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
643	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 2,360.65	- -	-
644	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
645	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	-
646	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
647	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 1,038.56	- -	-
648	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 649.27	04/2018 -	-
649	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00	07/2008	-
650	MEERUT-BULANDSHAHAR - [N24000539]NHAI, UTTAR PRADESH	01/2016	602.24 -	- -	-
651	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
652	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
653	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
654	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
655	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
656	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-
657	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 -	03/2019 -	-
658	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-
659	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
660	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
661	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
662	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
663	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
664	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
665	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
666	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
667	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
668	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
669	SIX LANING OF KAMRUJ CHALHAN SECTION OF NH-8 FROM KM 24.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.6 -	- -	-
670	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
671	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
672	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
673	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
674	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
675	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
676	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
677	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
678	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
679	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
680	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
681	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
682	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
683	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
684	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-
685	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA	09/2016	1,004.67 -	05/2019 -	-
686	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 -	- -	-
687	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
688	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-
689	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 231.700 OF NH-28 T [N24000637]NHAI, UTTAR PRADESH	12/2016	524.55 -	- -	-
690	4 LANNING OF KASHI-PUR-SIARCHANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.8 -	07/2018 -	-
691	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-
692	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
693	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
694	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
695	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
696	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
697	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
698	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
699	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
700	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA	03/2017	639.79 -	03/2020 -	-
701	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
702	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
703	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
704	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
705	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
706	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
707	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
708	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	270.90 -	- -	-
709	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
710	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
711	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
712	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
713	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
714	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
715	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
716	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
717	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
718	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
719	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
720	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
721	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
722	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
723	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
724	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
725	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
726	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
727	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-KAMARJHARH CHADAS R-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
728	CONSTRUCTION/UP-GRADATION OF 2 LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.7 -	- -	-
729	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
730	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
731	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
732	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
733	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
734	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
735	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
736	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
737	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
738	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
739	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
740	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
741	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-
742	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-
743	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-
744	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
745	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHJWANI - JUDAL - AND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	27.12 -	- -	-
746	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI, HARYANA	03/2018	307.79 -	- -	-
747	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-
748	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
749	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-
750	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	- -	-
751	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA	03/2018	198.05 -	- -	-
752	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA	03/2018	181.78 -	- -	-
753	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI, HARYANA	03/2018	551.58 -	- -	-
754	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
755	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI, HARYANA	01/2019	1,051.91 -	- 02/2020	-
756	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI, HARYANA	01/2019	1,120.06 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
757	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
758	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
759	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-
760	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-
761	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-
762	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
763	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-
764	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
765	PACKAGE-2 CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.07 -	03/2020 -	-
766	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
	Total		3,56,468.85 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Department Of Telecommunication</u>				
767	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]DOT,MULTI STATE	05/2006	1,077.00 -	03/2009 -	-
	<u>Indian Telephone Industry</u>				
768	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
769	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,DELHI	12/2005	249.00 -	02/2007 -	-
770	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,MAHARASHTRA	01/2006	247.00 -	02/2007 -	-
771	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,DELHI	02/2006	229.41 -	03/2012 -	-
	Total		3,913.58 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Bangalore Metro Rail Corporation Limited</u>				
772	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	-
	<u>Central Public Works Department</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
773	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	11/2020 -	11/2020
774	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 02/2021	11/2020
775	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
776	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE-VI-5), SHOPS, CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	09/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
777	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
778	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA OF SOUTH CENTRAL ZONE 2 - [N: 30000082]NNURM,ANDHRA PRADESH	08/2007	240.00 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
779	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
780	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Mumbai Metro Rail Corporation Ltd</u>				
781	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
782	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-
	<u>National Building Construcion Corporation Ltd</u>				
783	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 4,720.73	11/2019 11/2020	11/2020
	Total		90,606.78 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
784	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
785	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
	<u>Delhi Jal Board</u>				
786	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2020)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Uttarakhand Pey Jal Nigam</u>				
787	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
788	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	-
	Total		1,263.88 -		
	<u>COMMERCE AND INDUSTRY</u>				
	<u>National Building Construcion Corporation Ltd</u>				
789	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	10/2020
	Total		302.64 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
790	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	03/2020
791	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	07/2022 -	07/2020
792	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	11/2020
793	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
794	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				
795	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
796	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	Total		2,215.30 -		
	Grand Total		6,17,316.11		

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above								(December 2020)
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00	166.90	05/2013	05/2021	-55.37	96
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00	364.59	12/2009	11/2020	-39.64	131
3	2-LANING WITH FFS AT AIBAREILLY TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	91.30	469.51	01/2014	12/2020	61.08	83
4	INDORE-DIWAS(NH-3) - PPP (BOT) - [N24000139]	11/2010	25.00	475.00	06/2013	-	46.15	0
5	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00	486.00	05/2010	-	.00	0
6	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00	516.00	07/2008	-	.00	0
7	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07	530.07	08/2016	06/2020	.00	46
8	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00	571.00	10/2013	-	.00	0
9	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00	574.00	03/2014	-	.00	0
10	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00	575.00	07/2013	-	.00	0
11	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54	591.00	11/2013	01/2021	15.53	86
12	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00	617.00	08/2012	12/2019	.00	88
13	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	-	.00	0
14	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18	637.18	06/2019	09/2019	.00	3
15	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	-	.00	0
16	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	11/2020	.00	92

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	-	.00	0
18	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	-	.00	0
19	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	-	.00	0
20	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	11/2020	.00	88
21	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	-	.00	0
22	4-LANING OF BRAHMAPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.70	998.70	08/2012	12/2021	.00	100
23	SIX LANING OF CHANDIKHOL JAMSHEDPUR-BHUBANESHWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	07/2014	03/2021	.00	81
24	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	05/2021	.00	93
25	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	10/2020	.00	76
26	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	-	.00	0
27	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	-	.00	0
28	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	-	.00	0
29	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	-	.00	0
30	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	-	.00	0
31	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	-	.00	0
32	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0
33	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	-	.00	0
34	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0
35	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
36	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 (BOT) - [N24000233] - PPP	04/2014	1,266.60	1,544.00	09/2016	-	21.90	0
37	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
38	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
39	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
40	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	-	.00	0
41	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
42	SURAT-DAMODAR (SIX LANE) KM.263 TO KM.302 - PPP (BOT) - [N24000131]	02/2009	1,593.70	1,593.70	08/2011	-	.00	0
43	PUNE-SATARA (NH-4) - PPP (BOT) - [N24000130]	10/2010	1,245.55	1,724.55	03/2013	03/2021	.00	96
44	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
45	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	09/2020	.00	32
46	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
47	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	09/2020	.00	62
48	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
49	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	09/2021	.00	29
50	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,159.00	01/2019	-	.00	0
51	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	05/2019	-	.00	0
52	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	2,360.65	-	-	41.78	0
53	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0
54	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,519.00	06/2015	-	16.67	0
55	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	2,945.00	04/2015	03/2021	52.73	71
56	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,967.50	11/2011	-	167.82	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
57	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		71,749.63 -	76,998.08				
	Grand Total		71,749.63	76,998.08				

FLASH REPORT

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(December 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,896.72	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,038.00	12/2015 -	09/2021	44.69	69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00 -	17,079.00	12,799.00	12/2016 -	03/2023	38.63	75
	Total		2,27.00	4,499.0	34,733.72				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	5.78	33
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	7.88	12
	Total		1,559.23 -	1,673.33	615.65				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	16.73	04/2018 -	12/2021	37.56	44
7	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	23.04	03/2017 -	10/2021	12.20	55
	<u>Mahanadi Coal Fields Limited</u>								
8	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	08/2008	207.28 -	362.50	362.50	03/2012 -	03/2021	74.88	108
9	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	491.85	491.85	03/2013 -	03/2022	2.57	108
10	BHUBANESHWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	586.86	586.86	03/2017 -	03/2031	19.74	168
11	BALRAM EXPANSION OCP - [N06000044]	12/2007	172.08 3,504.21	646.01	646.01	03/2010 03/2029	03/2029	275.41	228
12	GOPAL JI KANIHA OCP, MCL - [N06000035]	12/2007	457.77 8,416.19	684.32	684.32	03/2013 03/2028	03/2028	49.49	180
	<u>Neyveli Lignite Corporation</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
13	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11	7,980.79	7,371.83	12/2015	01/2021	35.10	61
	<u>Singareni Colliers Company Limited</u>								
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76	349.28	279.54	03/2015	03/2022	114.60	84
15	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09	442.42	106.15	03/2019	03/2022	11.42	36
16	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	448.86	326.69	03/2012	03/2024	80.24	144
17	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06	473.22	18.60	03/2015	03/2022	5.85	84
18	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97	489.62	416.07	03/2012	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>								
19	JAGANNATHIPOR OCP(3.00MTA) - [N06000005]	09/2008	15.43	459.4	80.74	03/2015	03/2022	201.44	84
	<u>Western Coal Fields Limited</u>								
20	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65	313.34	140.64	03/2021	03/2024	12.85	36
21	ADASA UG TO OC - [N06000133]	08/2015	288.90	333.43	104.95	03/2023	03/2024	15.41	12
	Total		10,654.89	14,737.48	11,756.52				
	<u>COMMERCE AND INDUSTRY</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
22	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09	13,812.30	7,305.07	09/2019	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>								
23	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE [N40000002]	11/2017	4,773.00	5,178.00	2,334.57	12/2019	07/2021	8.49	19
	Total		17,352.09	18,990.30	9,639.64				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
24	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95	177.92	157.90	02/2018	12/2020	16.33	34
25	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44	250.00	226.54	05/2017	03/2021	22.29	46
26	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19	272.54	245.89	03/2019	03/2021	.13	24
27	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11	499.23	456.52	11/2013	03/2021	20.55	88

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		1,043.69 -	1,199.69	1,086.85				
	<u>HOME AFFAIRS</u>								
	<u>Central Public Works Department</u>								
28	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	179.16	168.45	04/2018 -	12/2020	10.00	32
29	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	841.88	10/2019 -	09/2021	64.04	23
	Total		1,382.09 -	2,179.16	1,010.33				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
30	C/O PERMANENT CAMPUS FOR IIT PATNA UNDER PHASE-1B AT TADE ALLIGUDEM, J.P. - [N28000133]	02/2019	180.00 - 190.00	205.69	30.69	09/2020 -	03/2021	10.22	6
31	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	258.72	04/2019 -	01/2021	19.28	21
32	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	185.61	06/2017 -	09/2021	.57	51
33	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	1.85	20
	<u>Rail India Technical And Economic Service</u>								
34	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	29.31	75
	Total		2,009.81 -	2,240.41	1,033.34				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
35	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	16.38	02/2017 -	08/2022	117.11	66
36	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	695.00	06/2019 -	02/2022	35.54	32
37	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,808.25	08/2018 -	01/2021	14.33	29
	<u>Gas Authority Of India Limited</u>								
38	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	143.50	08/2020 -	05/2021	14.17	9

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
39	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,470.70	12/2012 -	02/2022	102.71	110
	<u>Hindustan Petroleum Corporation Limited</u>								
40	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	247.49	11/2020 -	06/2021	17.65	7
41	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	1,825.04	06/2021 -	08/2022	14.76	14
42	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	13,324.42	07/2020 -	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								
43	PROVISION OF 2ND SUPPLY FOR WLG AND TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000001]	03/2017	230.00 -	293.00	138.42	06/2020 -	09/2021	24.15	15
44	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	399.01	06/2019 -	06/2021	18.68	22
45	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	374.14	10/2017 -	03/2022	17.66	53
46	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	1,685.17	12/2020 -	08/2021	66.09	8
47	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	2,724.32	12/2020 -	03/2021	43.82	3
48	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	3,275.27	12/2018 -	08/2021	33.98	32
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
49	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	390.06	03/2020 -	06/2021	9.64	15
	<u>Oil & Natural Gas Corporation Limited</u>								
50	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	170.85	05/2020 -	05/2021	21.57	12
51	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,846.46	1,518.24	05/2013 -	03/2021	114.26	94
52	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,375.90	2,572.08	04/2018 -	05/2021	5.80	37
53	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	922.04	03/2022 -	05/2023	23.16	14
	<u>Oil India Limited</u>								
54	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	445.41	03/2017 -	03/2021	39.05	48

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
55	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	130.10	02/2020 -	04/2021	19.89	14
	Total		52,355.37 -	69,279.48	39,275.89				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
56	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	09/2002	3,919.59 -	9,897.59	8,705.10	09/2009 -	03/2022	152.52	150
57	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,992.43	12,855.18	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								
58	RAMMAM-I HEP (3X40 MW) - [N18000113]	09/2014	1,381.34 -	9,528.31	626.72	09/2014 -	12/2024	15.23	63
59	TAPOVAN-II SHNUCAD HEP (4X150 MW) - [N18000014]	11/2006	2,974.48 -	867.38	4,966.50	03/2013 -	12/2022	96.99	117
60	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,583.00	8,648.28	07/2012 -	03/2021	79.02	104
61	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	10,016.10	7,888.03	07/2019 -	03/2021	9.00	20
62	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	11,044.00	02/2017 -	01/2021	24.87	47
63	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	11,441.91	12/2018 -	03/2021	9.64	27
64	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	15,105.22	13,473.99	01/2018 -	02/2021	29.79	37
65	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	11,269.68	06/2019 -	10/2022	7.12	40
66	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	15,331.70	05/2018 -	07/2021	33.47	38
67	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	21,312.11	18,168.42	10/2011 -	04/2022	145.16	126
	<u>North East Electric Power Corporation</u>								
68	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,927.34	8,151.00	12/2009 06/2016	01/2021	217.49	133
	<u>Power Grid Corporation Of India Limited</u>								
69	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	156.28	07/2019 -	03/2021	17.99	20
70	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	477.58	11/2016 -	02/2021	4.61	51
71	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,623.08	10/2012 -	01/2021	5.14	99

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
72	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	2,430.27	12/2018 -	12/2021	31.08	36
73	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,151.56	1,893.34	12/2018 -	12/2021	92.49	36
74	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,864.61	08/2013 -	03/2022	32.24	103
	<u>Thdc India Limited</u>								
75	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,110.14	06/2013 -	12/2023	54.94	126
	Total		1,30,570.25	2,00,172.71	156,955.41				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
76	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89	12
77	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	333.58	03/2021 -	03/2023	73.73	24
78	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,637.46	03/2021 -	03/2023	98.88	24
	<u>Container Corporation Of India</u>								
79	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	12/2020	.21	21
80	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	430.52	03/2018 -	03/2021	25.65	36
	<u>East Central Railways</u>								
81	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	680.95	03/2012 -	05/2021	57.27	110
82	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	513.72	03/2020 -	03/2023	49.45	36
83	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,070.00	1,061.07	03/2012 -	11/2022	229.50	128
84	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	154.70	03/2021 -	06/2022	62.06	15
85	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	299.09	03/2021 -	03/2024	63.37	36
	<u>East Coast Railway</u>								
86	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	218.99	03/2020 -	03/2022	52.77	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
87	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	168.21	11/2018 -	03/2024	15.45	64
88	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	891.78	03/2020 -	03/2023	.07	36
89	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,090.14	02/2019 -	12/2021	38.43	34
90	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	830.77	06/2021 -	03/2025	137.80	45
91	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,402.12	03/2009 -	03/2026	29.71	204
<u>Eastern Railways</u>									
92	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000231]	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108
93	NEW ALIPUR TO AKOLA, MM FOR LUDHIANA, PUJALI NL, PUJALI-LUBERI (BIRSAHIMPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	495.51 -	494.50	32.00	03/2009 -	03/2025	.01	240
94	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	34.08	228
95	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	502.41	03/2020 -	03/2021	22.31	12
96	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	162.75	02/2012 -	03/2025	36.15	157
97	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	103.51	03/2017 -	03/2025	29.20	96
98	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	636.20	03/2016 -	03/2025	7.75	108
99	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	134.80	133
100	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	899.24	03/2019 12/2009	03/2025	36.22	72
101	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	341.26	03/2022 -	03/2025	133.39	36
<u>Indian Railway Construction Company Limited</u>									
102	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,386.05	09/2018 -	12/2021	.00	39
103	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	849.31	03/2022 -	06/2024	117.23	27
<u>Metropolitan Rapid Transport Projects</u>									
104	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	48.06	102

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
105	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [N220100164]	03/1996	495.44 -	2,980.41	1,756.68	03/2004 -	03/2022	501.57	216
106	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>								
107	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
108	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26	24
109	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	152.23	03/2020 -	03/2023	80.79	36
110	AMBARI FAIAKATA TO NEW MAYNAGURI - [N22000200]	04/2011	314.00 -	800.00	777.27	03/2019 -	01/2021	154.78	22
111	NEW B.G. LINE FROM TETEL TO BYRNIHA, (NATIONAL PROJECT NEFR) - [N22000086]	09/2006	38.20 -	332.00	70.73	03/2019 -	03/2023	297.72	48
112	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,007.06	03/2021 -	05/2021	115.07	2
113	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,042.51	29.84	03/2019 -	03/2023	13.60	48
114	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	967.13	03/2019 -	03/2024	302.54	60
115	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,375.36	03/2022 -	03/2023	32.15	12
116	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266]	04/2000	1,180.19 -	5,071.38	3,595.72	12/2008 -	02/2021	329.71	146
117	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	3,781.94	03/2014 -	12/2023	130.69	117
118	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	6,911.44	1,045.72	03/2015 -	03/2023	197.07	96
119	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	-	542.04	87
120	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288]	04/2003	4,454.17 -	12,264.15	10,584.54	03/2011 -	03/2023	175.34	144
	<u>North Eastern Railway</u>								
121	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	28.80	04/2016 -	12/2021	.16	68
122	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	497.06	01/2019 -	02/2022	61.80	37
	<u>North Western Railway</u>								
123	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	327.89	11/2019 -	03/2021	75.73	16

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
124	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	306.94	12/2019 -	02/2021	60.52	14
125	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	780.00	155.47	03/2020 -	04/2022	30.00	25
126	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	677.30	02/2019 -	11/2021	109.82	33
	<u>Northern Railway</u>								
127	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	850.50	03/2016 -	06/2021	37.44	63
128	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	625.47	12/2011 -	06/2021	211.31	114
129	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	241.62	03/2023 -	03/2025	369.35	24
130	NANGALDAM-TALWARA(NL),NR - [220100183]	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	388.89	140
131	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	2,345.00	22,69.96	11/2002 -	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>								
132	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	786.37	03/2016 -	12/2021	50.15	69
133	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	5.98	33
134	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	1,280.16	03/2019 -	06/2021	51.02	27
135	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	62.89	39
136	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413]	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	54.24	24
137	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	1,450.82	12/2020 -	12/2021	23.55	12
138	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	1,726.74	12/2021 -	03/2022	20.68	3
139	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	111.91	21
140	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92	88
141	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,479.93	03/2020 -	03/2021	281.93	12
142	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95	141
143	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	1,122.68	12/2024 -	12/2026	42.47	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
144	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71	3,377.00	2,683.67	03/2020	03/2022	124.58	24
145	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98	4,259.48	2,629.88	03/2016	03/2025	7.78	108
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51	4,639.00	1,002.79	03/2016	03/2025	59.22	108
147	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00	22,716.11	2,555.91	12/2024	03/2025	40.08	3
	<u>South Central Railway</u>								
148	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73	449.39	7.09	03/2022	12/2022	275.34	9
149	BHADRAJI ALAM ROAD-SATTAPALLI - [N22000217]	04/2010	70.31	927.9	17.35	03/2020	06/2021	31.75	15
150	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95	1,952.68	487.47	03/2023	03/2024	5.16	12
151	KOTLAPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20	2,120.16	746.71	03/2009	03/2024	102.85	180
152	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70	2,643.25	1,191.09	03/2021	03/2025	15.49	48
153	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00	3,472.59	1,078.84	03/2000	03/2023	101.54	276
154	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00	3,887.48	984.35	03/2022	03/2024	7.06	24
	<u>South East Central Railway</u>								
155	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	1,096.00	39.79	12/2021	12/2024	378.60	36
156	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93	1,268.32	941.56	02/2019	12/2021	116.46	34
157	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00	1,370.94	470.49	12/2021	12/2023	.07	24
158	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86	2,005.25	1,777.22	04/2020	04/2021	291.76	12
159	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00	2,135.34	351.35	03/2021	12/2023	8.23	33
160	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51	3,524.81	952.24	03/2023	12/2023	84.69	9
	<u>South Eastern Railway</u>								
161	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20	358.68	295.76	12/2018	06/2021	38.92	30
162	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00	1,009.00	7.96	03/2015	03/2025	54.99	120

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
163	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	795.27	03/2020 -	12/2021	35.38	21
164	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	642.92	03/2021 -	12/2023	15.60	33
165	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>								
166	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	607.76	03/2020 -	01/2021	35.47	10
167	YELAHANKA-PENKONDA - [N22000328]	05/2015	860.43 -	1,147.00	877.08	03/2020 -	06/2021	33.31	15
168	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,274.19	03/2019 -	03/2021	15.84	24
	<u>Southern Railway</u>								
169	OMALUR-METTUR DM-DOUBLING WITH ELECTRIFICATION 28.33KM - [N22000373]	10/2013	18.26 -	332.00	39.19	04/2014 -	12/2020	77.29	80
170	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) [N22000441]	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	253.33	198
171	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11	27
172	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	693.14	03/2020 -	03/2025	465.83	60
173	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	232.66	03/2019 -	12/2027	1,699.64	105
174	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,910.84	1,583.77	02/2019 -	03/2025	301.67	73
	<u>West Central Railway</u>								
175	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	273.37	03/2022 -	03/2023	114.32	12
176	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	585.35	24
177	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
178	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	411.62	125.76	03/2012 -	03/2023	29.34	132
179	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	890.76	738.65	03/2019 -	10/2021	61.51	31
180	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494]	04/2017	691.84 -	1,017.91	453.03	03/2020 -	12/2020	47.13	9

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
181	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77	48
182	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	1,037.15 -	1,389.05	1,096.41	03/2021 -	03/2022	33.93	12
183	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,959.74	1,760.97	03/2020 -	12/2023	136.19	45
184	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	5,912.40	2,118.69	03/2022 -	03/2024	68.75	24
	Total		1,36,474.80 -	2,75,314.88	131,681.31				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
185	UPGRADATION OF FORENAROPSA ROAD TO 2L + PS - [N24000372	03/2018	160.21 -	175.41	39.19	08/2018 -	03/2021	4.33	31
186	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	24.14	08/2019 -	11/2022	33.51	39
187	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	160.76	08/2018 -	03/2021	4.45	31
188	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	12/2021	11.18	28
189	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	274.06	02/2013 -	12/2020	47.65	94
190	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	292.10	09/2014 -	12/2020	72.36	75
191	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	295.96	10/2010 -	-	69.30	128
192	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	325.42	10/2010 -	06/2021	93.80	128
193	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	305.76	03/2018 -	06/2021	9.23	39
194	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	527.66	232.36	08/2016 -	03/2021	6.14	55
195	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	397.32	09/2016 -	03/2021	14.24	54
196	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	341.61	10/2016 -	12/2020	17.04	50

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
197	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	728.49	05/2017 -	04/2021	77.26	47
198	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	58.98	117
199	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84	73
	<u>National Highways Authority Of India</u>								
200	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	355.20	04/2008 -	12/2020	10.58	152
201	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 -	417.68	433.68	01/2016 -	12/2020	18.88	59
202	2-LANING WITH PAVED SHOULDERS OF RAEBARELI TO ALLAHABAD - [N24000213]	07/2012	291.50 -	409.81	459.11	01/2016 -	12/2020	61.08	83
203	2 LANNING OF MUZAFFARPUR - SONENARSA - [N24000168]	05/2011	51.54 -	591.00	575.34	11/2013 -	01/2021	15.53	86
204	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	572.57	05/2018 -	06/2021	16.34	37
205	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	614.25	05/2018 -	06/2021	37.63	37
206	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	330.92	03/2020 -	09/2021	.23	18
207	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	795.00	04/2020 -	03/2021	3.95	11
208	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,425.26	08/2019 -	12/2020	16.55	16
209	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	419.66	09/2017 -	05/2021	9.67	44
210	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	817.80	03/2020 -	06/2021	10.24	15
211	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	68.71	30
212	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78	8
213	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	2,499.00	1,497.61	03/2021 -	04/2021	63.05	1
214	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	52.73	71

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
215	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66	105
	Total		22,453.75 -	28,691.64	21,567.04				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
216	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2021	3.96	62
217	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	207.12	189.79	12/2016 -	03/2021	2.23	51
	Total		352.34 -	362.78	334.74				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmhc)</u>								
218	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	17,436.86	05/2015 -	07/2021	41.32	74
	Total		15,525.00 -	21,940.00	17,436.86				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
219	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	15,239.00	07/2015 -	06/2021	84.97	71
	Total		13,334.00 -	24,664.00	15,239.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
220	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	8,276.69	12/2018 -	11/2022	18.69	47
	Total		10,773.00 -	12,787.00	8,276.69				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
221	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	16,568.13	03/2020 -	04/2022	447.22	25
	Total		10,151.04 -	55,548.87	16,568.13				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Grand Total		4,53,262.35	7,70,280.73	467,211.12				

FLASH REPORT

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,896.72	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,038.00	12/2015 -	09/2021	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12,799.00	12/2016 -	03/2023	38.63
	Total		27,271.00 -	30,499.00	34,733.72			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	5.78
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	51.11	09/2021 -	09/2021	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	7.88
	Total		1,905.50 -	2,153.66	666.76			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
7	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	16.73	04/2018 -	12/2021	37.56
8	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	23.04	03/2017 -	10/2021	12.20
	<u>Eastern Coal Fields Limited</u>							
9	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	516.17	08/2019 -	-	93.35
	<u>Mahanadi Coal Fields Limited</u>							
10	GOPAL JI KANIHA OCP, MCL - [N06000035]	12/2007	457.77 8,416.19	684.32	684.32	03/2013 03/2028	03/2028	49.49
11	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	586.86	586.86	03/2017 -	03/2031	19.74

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	08/2008	207.28 -	362.50	362.50	03/2012 -	03/2021	74.88
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	491.85	491.85	03/2013 -	03/2022	2.57
14	BALRAM EXPANSION OCP - [N06000044]	12/2007	172.08 3,504.21	646.01	646.01	03/2010 03/2029	03/2029	275.41
	<u>Neyveli Lignite Corporation</u>							
15	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,371.83	12/2015 -	01/2021	35.10
16	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	10,724.93	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>							
17	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.07 -	420.62	416.07	03/2012 -	03/2023	16.86
18	SHANTIKHAI LONGWALL PROJECT - [N06000017]	10/2006	249.3 -	448.8	326.6	03/2012 -	03/2024	80.24
19	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	106.15	03/2019 -	03/2022	11.42
20	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2022	5.85
21	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	279.54	03/2015 -	03/2022	114.60
	<u>South-Eastern Coal Fields Limited</u>							
22	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	180.74	03/2015 -	03/2022	201.44
	<u>Western Coal Fields Limited</u>							
23	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	140.64	03/2021 -	03/2024	12.85
24	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	85.03	03/2023 -	03/2023	117.98
25	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	104.95	03/2023 -	03/2024	15.41
	Total		30,741.56 -	37,531.44	23,082.65			
	<u>COMMERCE AND INDUSTRY</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
26	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	7,305.07	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>							
27	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,334.57	12/2019 -	07/2021	8.49
	Total		17,352.09 -	18,990.30	9,639.64			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
28	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>							
29	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	456.52	11/2013 -	03/2021	20.55
30	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	226.54	05/2017 -	03/2021	22.29
31	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68
32	CONSTRUCTION OF HOSPITAL BLOCK, IIT-KHARAGPUR - [N21000010]	12/2014	168.00 -	191.20	169.51	05/2017 -	07/2019	13.20
33	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCJ JHAJJAR - [N21000011]	09/2014	505.83 -	585.00	586.96	03/2018 -	09/2019	15.71
34	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	157.90	02/2018 -	12/2020	16.33
35	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
36	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	245.89	03/2019 -	03/2021	.13
37	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.64	111.58	-	03/2021	.05
38	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	216.09	-	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>							
39	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	577.32	09/2021 -	09/2021	8.88
	Total		5,589.39 -	6,253.60	3,272.99			
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
40	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	841.88	10/2019 -	09/2021	64.04
41	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	179.16	168.45	04/2018 -	12/2020	10.00
	Total		1,382.09 -	2,179.16	1,010.33			
	<u>HUMAN RESOURCE DEVELOPMENT</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
42	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	185.61	06/2017 -	09/2021	.57
43	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	258.72	04/2019 -	01/2021	19.28
44	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	1.85
45	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	10.22
	<u>Rail India Technical And Economic Service</u>							
46	CONSTRUCTION AND DEVELOPMENT OF NATIONAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	334.52 -	328.26		09/2014 -	12/2020	29.31
	Total		2,009.01 -	2,240.41	1,033.34			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
47	HALDIA LPG IMPORT FACILITY - [N16000223]	03/2015	694.00 -	1,097.54	971.84	10/2018 -	07/2020	58.15
48	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,808.25	08/2018 -	01/2021	14.33
49	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	16.38	02/2017 -	08/2022	117.11
50	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	695.00	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							
51	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	606.89	02/2020 -	-	12.42
52	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,470.70	12/2012 -	02/2022	102.71
53	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49 -	345.15	183.93	04/2022 -	04/2022	20.06
54	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	143.50	08/2020 -	05/2021	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
55	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	13,324.42	07/2020 -	07/2022	25.50
56	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	09/2015	4,199.00 -	5,060.00	4,183.90	03/2020 -	-	20.50

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
57	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	1,825.04	06/2021 -	08/2022	14.76
58	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	247.49	11/2020 -	06/2021	17.65
	<u>Indian Oil Corporation Limited</u>							
59	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	374.14	10/2017 -	03/2022	17.66
60	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	1,685.17	12/2020 -	08/2021	66.09
61	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	2,724.32	12/2020 -	03/2021	43.82
62	DEVELOPMENT OF FACILITIES AT HOINAIRAND (SILCHAR), TEACHAR ASSAM AS REFINEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	399.00	08/2019 -	06/2021	18.68
63	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	3,275.27	12/2018 -	08/2021	33.98
64	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	293.00	138.42	06/2020 -	09/2021	24.15
65	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	03/2018	588.20 -	730.20	48.20	-	05/2023	24.14
	<u>Indian Strategic Petroleum Reserves Ltd</u>							
66	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
67	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	390.06	03/2020 -	06/2021	9.64
	<u>Oil & Natural Gas Corporation Limited</u>							
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,846.46	1,518.24	05/2013 -	03/2021	114.26
69	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,572.08	04/2018 -	05/2021	5.80
70	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	611.60	03/2023 -	03/2022	38.20
71	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	170.85	05/2020 -	05/2021	21.57
72	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	922.04	03/2022 -	05/2023	23.16
73	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	1,941.83	05/2021 -	05/2021	2.17

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Oil India Limited</u>							
74	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	445.41	03/2017 -	03/2021	39.05
75	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	130.10	02/2020 -	04/2021	19.89
	Total		64,350.04 -	83,925.21	49,373.93			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
76	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	2,019.52 -	9,007.59	9,705.12	09/2009 -	03/2022	152.52
77	SUBANSIRI LOWER H.E.P (8X200 MW) (NHPC) - [180100221]	09/2003	6,285.31 -	9,992.41	12,855.16	09/2010 -	08/2023	218.08
	<u>National Thermal Power Corporation</u>							
78	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	15,105.22	13,473.99	01/2018 -	02/2021	29.79
79	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,796.50	03/2013 -	12/2022	96.99
80	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	10,016.10	7,888.03	07/2019 -	03/2021	9.00
81	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	11,441.91	12/2018 -	03/2021	9.64
82	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	11,269.68	06/2019 -	10/2022	7.12
83	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	626.32	09/2019 -	12/2024	15.23
84	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,583.00	8,648.28	07/2012 -	03/2021	79.02
85	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	15,331.70	05/2018 -	07/2021	33.47
86	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	11,044.00	02/2017 -	01/2021	24.87
87	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	18,168.42	10/2011 -	04/2022	145.16
88	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	7.55
89	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	17.95
90	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	12.95
91	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,312.62	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
92	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,927.34	8,151.00	12/2009 06/2016	01/2021	217.49
	<u>Power Grid Corporation Of India Limited</u>							
93	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,623.08	10/2012 -	01/2021	5.14
94	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,864.61	08/2013 -	03/2022	32.24
95	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,315.85	04/2016 -	07/2020	38.61
96	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	477.58	11/2016 -	02/2021	4.61
97	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	200.16	07/2017 -	-	27.92
98	SYSTEM STRENGTHENING XIII OF S.P. GRID - [N18000109]	10/2011	487.39 -	639.44	590.30	06/2014 -	-	31.17
99	TRANSMISSION SYSTEM OF ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	498.65 -	492.44	412.51	01/2019 -	04/2020	18.16
100	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A.P. - [N18000249]	12/2014	4,754.42 -	9,151.56	1,893.34	12/2018 -	12/2021	92.49
101	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	2,430.27	12/2018 -	12/2021	31.08
102	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	156.28	07/2019 -	03/2021	17.99
	<u>Thdc India Limited</u>							
103	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,110.14	06/2013 -	12/2023	54.94
	Total		1,60,515.47 -	2,33,688.00	186,722.17			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
104	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	333.58	03/2021 -	03/2023	73.73
105	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	315.00	312.62	03/2019 -	03/2020	71.14
106	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,637.46	03/2021 -	03/2023	98.88
107	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
108	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024	25.04

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
109	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89
110	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	429.22	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							
111	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	430.52	03/2018 -	03/2021	25.65
112	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
113	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	- -	-	143.17
114	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
115	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,500.00	3,494.01	- -	03/2022	238.80
116	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,510.98	- -	03/2023	290.95
117	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	680.95	03/2012 -	05/2021	57.27
118	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,070.00	1,061.07	03/2012 -	11/2022	229.50
119	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	333.16	- -	03/2022	277.26
120	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	431.28	03/2020 -	-	3.33
121	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	265.08	- -	02/2023	36.67
122	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	712.11	- -	03/2023	253.52
123	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	15.55	- -	-	32.26
124	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	818.15
125	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	379.45	- -	03/2021	126.22
126	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	383.64	- -	03/2022	391.01
127	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	24.73	- -	-	376.78
128	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,470.50	1,095.55	- -	03/2021	295.15

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
129	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00	819.01	513.72	03/2020	03/2023	49.45
130	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01	480.00	473.33	-	-	125.34
131	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15	546.71	541.83	07/2014	-	64.60
132	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04	1,215.54	299.09	03/2021	03/2024	63.37
133	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64	1,185.73	154.70	03/2021	06/2022	62.06
134	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82	726.31	535.07	-	-	301.68
135	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM FATHARSHARIF-BARFAGHA, DAKSHINAWAN BIHARSHARIF - [N22000476]	04/1991	329.9	1,483.1	1,177.05	-	03/2022	350.27
	<u>East Coast Railway</u>							
136	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78	1,928.07	830.77	06/2021	03/2025	137.80
137	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13	3,791.66	1,402.12	03/2009	03/2026	29.71
138	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99	1,539.28	1,090.14	02/2019	12/2021	38.43
139	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00	1,160.83	891.78	03/2020	03/2023	.07
140	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81	238.03	218.99	03/2020	03/2022	52.77
141	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61	810.02	168.21	11/2018	03/2024	15.45
	<u>Eastern Railways</u>							
142	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91	1,619.48	899.24	03/2019 12/2009	03/2025	36.22
143	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09	1,425.44	637.87	02/2013	03/2024	134.80
144	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17	527.54	1.76	-	03/2025	44.46
145	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18	663.13	502.41	03/2020	03/2021	22.31
146	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80	270.72	279.67	-	03/2022	53.99
147	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60	335.62	1.12	03/2017	03/2026	12.02
148	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54	494.59	32.00	03/2005	03/2025	.01

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
149	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	52.09	- -	03/2025	.25
150	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	162.75	02/2012 -	03/2025	36.15
151	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	332.10	- -	03/2024	23.82
152	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	227.07	- -	03/2022	6.48
153	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	34.08
154	SULTANGAN-KATURIA VIA ASARGANJ, TAPURPUR AND BELHAR - [N22000217]	04/2007	150.02 -	1,001.34	-	- -	03/2025	180.30
155	HANSNABAD HINGALGANJ NEW DOUBLING - [N22000218]	04/2010	172.3 -	260.1	11.05	- -	03/2025	51.19
156	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	341.26	03/2022 -	03/2025	133.39
157	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	418.09	412.89	- -	03/2021	44.99
158	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	516.05	535.20	- -	05/2019	97.43
159	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	636.20	03/2016 -	03/2025	7.75
160	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	103.51	03/2017 -	03/2025	29.20
Indian Railway Construction Company Limited								
161	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	849.31	03/2022 -	06/2024	117.23
162	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,386.05	09/2018 -	12/2021	.00
Metropolitan Rapid Transport Projects								
163	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37
164	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,756.68	03/2004 -	03/2022	501.57
165	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	48.06
166	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91
North Central Railway								

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
167	ETAWAH-MAINPURI (NL),NCR - [N220100318	04/1997	120.00 -	346.00	345.51	12/2008 -	-	188.33
168	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02
169	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	1.69
	<u>North East Frontier Railway</u>							
170	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	297.32 -	614.00	275.07	03/2019 -	-	106.51
171	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,521.45	3,781.94	03/2014 -	12/2023	130.69
172	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	5,071.38	3,595.72	12/2008 -	02/2021	329.71
173	JIRIBAM TO IMPHAL (JIPUR)(NL)(NEFR) - [220100288	04/2003	4,454.7 -	12,264.1	1,584.5	03/2011 -	03/2023	175.34
174	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	770.73	03/2019 -	03/2023	297.72
175	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	532.87 -	2,145.00	967.13	03/2019 -	03/2024	302.54
176	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 -	6,911.44	1,045.72	03/2015 -	03/2023	197.07
177	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	6.74	- -	03/2022	7.86
178	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	-	542.04
179	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,042.51	29.84	03/2019 -	03/2023	13.60
180	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	38.20	- -	-	71.62
181	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26
182	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	263.67	03/2021 -	03/2021	350.44
183	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	73.97	03/2020 -	-	94.45
184	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	287.09	- -	12/2021	54.80
185	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	750.00	152.23	03/2020 -	03/2023	80.79
186	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	1,082.01	- -	-	128.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
187	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	800.00	777.27	03/2019 -	01/2021	154.78
188	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,375.36	03/2022 -	03/2023	32.15
189	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,007.06	03/2021 -	05/2021	115.07
190	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	760.00	730.62	12/2021 -	03/2021	26.19
191	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-	186.55
	<u>North Eastern Railway</u>							
192	KICHHA-KHAMRIMA (NL) - NER - [220100317]	04/2003	142.50 -	228.40	0.15	-	-	60.34
193	GHAZIPUR - JALPAIGURI (40 KM) - [N22000321]	04/2014	182.20 -	197.75	-	-	-	8.10
194	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	-	-	358.99
195	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	112.02	12/2021 -	12/2021	267.13
196	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	497.06	01/2019 -	02/2022	61.80
197	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	-	.16
198	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	28.80	04/2016 -	12/2021	.16
199	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	-	01/2018 -	-	9.91
200	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	56.54	-	12/2023	18.56
	<u>North Western Railway</u>							
201	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	677.30	02/2019 -	11/2021	109.82
202	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	780.00	155.47	03/2020 -	04/2022	30.00
203	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,980.21	4.60	-	-	126.64
204	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	306.94	12/2019 -	02/2021	60.52
205	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	186.12	-	-	104.65
206	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	244.56	10/2018 -	-	47.91

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
207	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	-	-	-	33.70
208	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	-	-	33.81
209	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	327.89	11/2019 -	03/2021	75.73
210	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	457.31	02/2019 -	02/2020	116.86
	<u>Northern Railway</u>							
211	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	111.51	-	03/2024	129.17
212	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	625.47	12/2011 -	06/2021	211.31
213	DEOBAND (MUJAZFA NAGAR)-ROCKLINE NL - [N22000274]	04/2007	336.1 -	791.3	567.14	-	03/2023	134.90
214	ANAND VIHAR-TILAK BRIDGE RD AND 4 TH LINE - [N22000281]	04/2012	205.3 -	419.00	112.95	-	09/2023	41.71
215	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	204.53	-	-	57.68
216	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	103.72	-	03/2023	2.93
217	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	1.73	-	03/2024	310.24
218	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	388.89
219	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	22,369.08	11/2002 -	12/2022	1,017.96
220	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	241.62	03/2023 -	03/2025	369.35
221	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	850.50	03/2016 -	06/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>							
222	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	55.57
223	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92
224	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	196.83
225	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	1,002.79	03/2016 -	03/2025	59.22
226	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	784.37	12/2026 -	12/2025	127.62
227	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	2,121.59	03/2023 -	12/2022	41.04

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
228	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	2,629.88	03/2016 -	03/2025	7.78
229	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95
230	VIJAYAWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	124.58
231	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	1,376.94	12/2021 -	12/2021	53.75
232	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	35.42
233	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	1,726.74	12/2021 -	03/2022	20.68
234	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE II HYDERABAD - [N22000233]	04/2012	632.3 -	950.00	786.3	03/2016 -	12/2021	50.15
235	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023	9.32
236	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	5.98
237	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	705.50	12/2024 -	12/2024	9.83
238	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	1,280.16	03/2019 -	06/2021	51.02
239	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	2,555.91	12/2024 -	03/2025	40.08
240	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,479.93	03/2020 -	03/2021	281.93
241	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	1,122.68	12/2024 -	12/2026	42.47
242	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	111.91
243	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	62.89
244	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	54.24
245	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	1,450.82	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>							
246	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
247	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	746.71	03/2009 -	03/2024	102.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
248	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	- -	-	161.86
249	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	487.47	03/2023 -	03/2024	5.16
250	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,191.09	03/2021 -	03/2025	15.49
251	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	517.35	03/2020 -	06/2021	31.75
252	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	538.84
253	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,472.59	1,078.84	03/2000 -	03/2023	101.54
254	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,031.00 -	3,087.33	984.33	03/2022 -	03/2024	7.06
255	MANMAD-PARBHANI- ANDER SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.3 185.00	449.20	7.06	03/2022 -	12/2022	275.34
<u>South East Central Railway</u>								
256	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	1,416.77	- -	08/2020	268.37
257	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	291.76
258	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	952.24	03/2023 -	12/2023	84.69
259	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	116.46
260	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	378.60
261	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	1,131.91	12/2019 -	10/2020	40.65
262	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	8.23
263	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	.07
<u>South Eastern Railway</u>								
264	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
265	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	194.30	12/2016 -	08/2020	153.41
266	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	40.99	- -	03/2025	131.89
267	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
268	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
269	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	295.76	12/2018 -	06/2021	38.92
270	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	795.27	03/2020 -	12/2021	35.38
271	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	642.92	03/2021 -	12/2023	15.60
272	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>							
273	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	66.44	- -	12/2023	9.22
274	CHIKBALLA-PUR-PUTTAPARTH - RISHI TYA SAI NILAYAM NL - [N22000270]	04/2013	558.00 -	692.40	-	- -	12/2023	24.09
275	SRINIVASA-PUR-MANADALI NL - [N22000277]	04/2013	206.00 -	166.65	-	- -	12/2023	57.65
276	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	1,096.12	- -	03/2025	17.95
277	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	0.34	- -	12/2023	14.14
278	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	-	- -	12/2023	12.38
279	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	156.88	- -	12/2024	68.97
280	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	877.08	03/2020 -	06/2021	33.31
281	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	607.76	03/2020 -	01/2021	35.47
282	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,274.19	03/2019 -	03/2021	15.84
283	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	890.00	462.84	03/2017 -	-	38.03
	<u>Southern Railway</u>							
284	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,910.84	1,583.77	02/2019 -	03/2025	301.67
285	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	693.14	03/2020 -	03/2025	465.83
286	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	262.68	- -	-	79.80
287	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	3.34	02/2019 -	-	247.32
288	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	2.28	- -	03/2024	339.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
289	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	0.62	- -	-	78.78
290	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	319.22	- -	03/2025	181.84
291	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	439.49	- -	12/2021	69.20
292	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	8.50	- -	-	46.09
293	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	1.63	- -	-	295.05
294	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.73	340.21	- -	09/2021	174.15
295	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TANAPARAM- HENGALPATTU 3RD LINE G ALONWITH ELECTRIFICATION [N22000202]	04/2007	931.31 -	961.00	873.72	- -	02/2021	3.12
296	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	6.73	- -	-	45.43
297	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	232.66	03/2019 -	12/2027	1,699.64
298	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	332.00	239.19	04/2014 -	12/2020	77.29
299	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,246.00	0.81	- -	-	24.60
300	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	253.33
301	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11
<u>West Central Railway</u>								
302	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	585.35
303	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57
304	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	273.37	03/2022 -	03/2023	114.32
<u>Western Railway</u>								
305	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	5,912.40	2,118.69	03/2022 -	03/2024	68.75
306	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	72.42
307	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	411.62	125.76	03/2012 -	03/2023	29.34
308	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,959.74	1,760.97	03/2020 -	12/2023	136.19

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
309	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77
310	VIRAMGAM-SAMAKHALI (DL) - [N22000145]	04/2011	1,037.15 -	1,389.05	1,096.41	03/2021 -	03/2022	33.93
311	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	890.76	738.65	03/2019 -	10/2021	61.51
312	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	04/2017	691.84 -	1,017.91	453.03	03/2020 -	12/2020	47.13
	Total		2,27,287.87 -	4,74,869.26	197,954.51			
	ROAD TRANSPORT AND HIGHWAY							
	Ministry Of Road Transport And Highways (State Projects)							
313	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	175.00	- -	-	58.68
314	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	58.98
315	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	-	02/2012 -	-	76.21
316	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	295.96	10/2010 -	-	69.30
317	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 -	389.45	349.94	05/2012 -	-	88.11
318	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	274.06	02/2013 -	12/2020	47.65
319	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	223.10	08/2015 -	-	3.84
320	REHABILITATION AND UPGRADE OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	3.07
321	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	219.47	- -	-	3.72
322	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	36.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
323	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	-	46.51
324	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	728.49	05/2017 -	04/2021	77.26
325	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	739.41	- -	12/2020	1.75
326	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	386.98	02/2011 -	-	34.06
327	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000399]	01/1991	282.41 -	322.01	317.05	08/2016 -	-	14.02
328	SIDHI TO RUDHAULI SECTION OF NH-75E (4L) IN U.P. - [N24000401]	11/2011	954.35 -	1,191.57	235.61	09/2015 -	10/2021	24.84
329	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 -	377.64	341.81	10/2016 -	-	5.42
330	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 -	353.89	256.11	11/2015 -	-	6.21
331	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	307.47	292.55	02/2018 -	-	40.84
332	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	325.42	10/2010 -	06/2021	93.80
333	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	369.77	216.25	- -	-	15.67
334	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	.26
335	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	.02
336	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	-	- -	-	.06
337	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	-	.08
338	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]	08/2014	600.87 720.97	720.97	682.36	11/2017 -	05/2019	19.99
339	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]	08/2014	823.20 937.76	937.76	807.93	11/2017 -	06/2019	13.92

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
340	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	173.41	139.19	08/2018 -	03/2021	4.33
341	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	24.14	08/2019 -	11/2022	33.51
342	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	12/2021	11.18
343	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	330.94	08/2017 -	02/2020	42.48
344	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	160.76	08/2018 -	03/2021	4.45
345	FOUR LANE OF 5.122 KM OF NH-3 (NEW NH-35) FROM KM 269.900 (DESIGN CH 0.0) TO KM 275.622 (DESIGN CH 5.12 - [N24000892	10/2015	233.21 -	255.99	315.57	12/2015 -	-	6.81
346	BHOKAR TO SARSAH - [N24001128	02/2017	205.99 -	205.99	188.64	07/2019 -	-	.31
347	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	469.64	03/2017 -	-	46.51
348	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	305.76	03/2018 -	06/2021	9.23
349	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	292.10	09/2014 -	12/2020	72.36
350	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	1,217.25	-	-	2.93
351	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	527.66	232.36	08/2016 -	03/2021	6.14
352	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	397.32	09/2016 -	03/2021	14.24
353	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	341.61	10/2016 -	12/2020	17.04
354	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223	03/2010	179.89 271.00	271.00	-	03/2013 -	-	50.65
355	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225	12/2010	169.26 299.00	299.00	-	01/2019 -	-	76.65
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
356	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	11.57
357	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	272.09	08/2016 -	-	3.73
358	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	241.07	10/2017 -	-	15.30
359	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]	10/2017	818.00 -	887.68	178.47	- -	-	8.52
National Highways Authority Of India								
360	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	520.00	612.58	02/2009 -	-	85.71
361	MAIBANG TO LUMDING (AS-25), KM.33.400 TO KM.111.000 - [240106278]	12/2003	199.1 -	340.1	325.2	04/2009 -	-	70.23
362	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	435.78	427.96	11/2008 -	-	159.95
363	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	255.23	251.39	11/2008 -	-	64.62
364	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	230.89	05/2008 -	06/2019	4.99
365	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	655.17	07/2009 -	-	234.27
366	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,967.50	3,994.51	11/2011 -	-	167.82
367	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
368	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	488.05	04/2010 -	07/2019	65.82
369	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	355.20	04/2008 -	12/2020	10.58
370	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
371	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 -	2,519.00	4,708.76	06/2015 -	-	16.67
372	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66
373	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	575.34	11/2013 -	01/2021	15.53
374	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	459.07	01/2014 -	12/2020	61.08
375	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	52.73
376	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 -	417.68	433.68	01/2016 -	12/2020	18.88

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
377	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 -	627.93	633.24	01/2016 -	01/2020	26.66
378	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	614.25	05/2018 -	06/2021	37.63
379	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	272.98	- -	-	.77
380	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	572.57	05/2018 -	06/2021	16.34
381	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	889.83	- -	01/2020	11.33
382	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABAD (KM 0.00 TO KM . 92.785) - [N24000463]	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	68.71
383	FOUR LANING OF KOLWAR TO BHOJPUR - [N24000482]	08/2015	814.4 -	825.1	512.0	- -	10/2021	1.37
384	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
385	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	676.33	12/2017 -	-	66.88
386	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	400.60	- -	-	6.11
387	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	186.70	- -	-	1.33
388	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,472.01	- -	-	41.78
389	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,160.00	- -	-	21.50
390	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	712.15	04/2018 -	-	25.80
391	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 -	987.94	867.27	- -	-	44.60
392	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84
393	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	353.42	- -	12/2020	7.53
394	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	86.37
395	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,282.04	- -	-	94.94
396	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	310.12	08/2018 -	-	3.98

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
397	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	09/2016	1,239.82 -	1,727.66	1,672.28	- -	01/2021	39.35
398	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	1,425.26	08/2019 -	12/2020	16.55
399	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 -	1,145.31	1,265.00	- -	02/2021	4.10
400	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	309.40	- -	-	8.35
401	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	-	19.25
402	FOUR LANNING OF JHANSI-KHARAU AHOC SECTION PKG-II) OF NH-75/ 6 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.1 -	1,310.0	1,039.2	03/2020 -	-	10.58
403	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	-	03/2020 -	-	31.88
404	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	3.40
405	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	08/2020	5.56
406	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	11/2020	1.06
407	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	-	5.70
408	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	330.92	03/2020 -	09/2021	.23
409	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	21.04	03/2020 -	-	9.38
410	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	947.88	03/2020 -	-	13.97
411	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	817.80	03/2020 -	06/2021	10.24
412	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	18.50
413	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	900.64	03/2020 -	-	41.54
414	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	1,013.67	03/2020 -	-	44.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
415	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	795.00	04/2020 -	03/2021	3.95
416	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78
417	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	419.66	09/2017 -	05/2021	9.67
418	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]	12/2017	404.94 -	448.18	385.69	-	10/2020	10.68
419	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 -	276.17	44.05	-	-	.99
420	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000731]	02/2018	1,424.77 -	1,853.42	14.19	-	-	30.09
421	SIX-LANING OF PANGLORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-27 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,095.41 -	2,400.00	2,080.15	-	11/2021	20.28
422	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 -	2,450.00	2,047.35	-	-	12.50
423	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]	03/2018	1,261.98 -	1,952.20	934.06	-	07/2021	54.69
424	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 -	1,197.00	951.37	-	-	29.35
425	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 -	1,332.00	1,072.92	-	-	18.87
426	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 -	1,449.00	394.36	-	01/2021	37.71
427	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	2,499.00	1,497.61	03/2021 -	04/2021	63.05
428	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 -	537.17	38.11	-	-	8.26
429	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 -	1,261.05	299.09	-	03/2021	22.44
430	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,071.00	273.52	-	07/2021	5.32
431	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96 -	2,169.00	-	-	-	4.99

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
432	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	-	-	.12
433	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	183.69	-	07/2021	46.72
434	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	142.26	-	07/2021	.48
435	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	617.58	-	-	25.68
436	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001119	10/2019	743.88 -	743.89	115.40	-	12/2021	.00
437	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.50 -	840.00	35.00	-	-	27.86
438	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	31.81	-	-	305.58
	Total		90,922.81 -	1,16,551.16	85,220.90			
	<u>RURAL DEVELOPMENT</u>							
	<u>Hindustan Steelwork Construction Limited</u>							
439	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	207.12	189.79	12/2016 -	03/2021	2.23
440	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2021	3.96
	Total		352.34 -	362.78	334.74			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmdc)</u>							
441	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	17,436.86	05/2015 -	07/2021	41.32
	<u>Rastriya Ispat Nigam Limited</u>							
442	CENTRAL DISPATCH YARD - [N12000119	08/2015	320.66 -	336.00	278.28	08/2018 -	11/2020	4.78
	Total		15,845.66 -	22,276.00	17,715.14			
	<u>TELECOMMUNICATIONS</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Department Of Telecommunication</u>							
443	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	15,239.00	07/2015 -	06/2021	84.97
	Total		13,334.00 -	24,664.00	15,239.00			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
444	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	8,276.69	12/2018 -	11/2022	18.69
	<u>Central Public Works Department</u>							
445	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SEH TO TUDANG IN THE STATE OF UTTAR PRADESH - [N2800010	12/2008	114.26 266.00 -	266.00	-	12/2013 -	-	132.80
	<u>Chennai Metro Rail Ltd</u>							
446	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-	30.53
	<u>Kochi Metro Rail Corporation Ltd</u>							
447	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	6,218.14	6,031.09	07/2017 -	09/2020	20.00
	<u>National Building Construcion Corporation Ltd</u>							
448	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	11/2020	10.71
	Total		34,933.05 -	43,049.87	35,343.73			
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
449	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	16,568.13	03/2020 -	04/2022	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
450	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 -	234.03	-	12/2021 -	12/2021	.97
	Total		10,382.83 -	55,782.90	16,568.13			
	Grand Total		7,04,175.51	11,65,016.75	677,911.68			

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	438.28 -	06/2019 -	12/2020	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39 -	04/2021 -	04/2021	0/0
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 -	04/2020 -	05/2021	0/0
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	417.23 -	09/2018 09/2020	06/2021	0/0
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	03/2020 06/2021	06/2021	0/0
6	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	12.24 -	03/2021 -	06/2021	0/0
7	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIROPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	02/2020 -	06/2021	0/0
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	09/2020 -	07/2021	0/0
9	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR	07/2018	346.27 480.33	09/2021 -	09/2021	0/0
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	10/2021 -	03/2022	0/0
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 1,232.00	03/2021 -	03/2022	0/0
12	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]AAI,TELANGANA	05/2020	353.61 -	05/2022 -	05/2022	0/0
13	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	02/2022 -	09/2022	0/0
14	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	09/2021 09/2020	09/2022	0/0
15	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	11/2021 10/2022	10/2022	0/0
16	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	10/2022 -	10/2022	0/0
17	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	08/2022 -	03/2023	0/0
18	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	03/2022 -	03/2023	0/0
19	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH	04/2020	611.80 -	03/2023 -	03/2023	0/0
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
20	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	03/2017 -	10/2021	0/0
21	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	04/2018 -	12/2021	0/0
	<u>Central Coal Fields Limited</u>					
22	TETARIAKHAR EXPANSION OCP - [N06000186]CCL, JHARKHAND	11/2019	243.52 -	03/2023 -	03/2023	0/0
	<u>Eastern Coal Fields Limited</u>					
23	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL, WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
	<u>Neyveli Lignite Corporation</u>					
24	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
25	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
26	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.80 -	09/2020 -	-	0/0
27	BITHNOK LIGNITE MINE PROJECT(2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	02/2019 -	-	0/0
	<u>Northern Coal Fields Limited</u>					
28	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL, MADHYA PRADESH	11/2020	1,729.68 -	03/2025 -	03/2025	0/0
	<u>Western Coal Fields Limited</u>					
29	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
30	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL, MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (SAIL)</u>					
31	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL, ODISHA	11/2020	377.18 -	05/2023 -	05/2023	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
32	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	12/2021 -	12/2021	0/0
33	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
34	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
35	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	08/2022	0/0
36	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL, KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Chennai Petroleum Corporation Limited					
37	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00	12/2019	01/2021	0/0
38	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00	08/2020	09/2021	0/0
	Gas Authority Of India Limited					
39	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE	06/2020	7,844.25	05/2023	05/2023	0/0
40	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00	02/2020	-	0/0
	Hindustan Petroleum Corporation Limited					
41	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]HPCL,PUNJAB	05/2020	1,421.46	02/2023	02/2023	0/0
42	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00	09/2026	09/2026	0/0
43	CITY GAS DISTRIBUTION PROJECT IN UP AND BIHAR - [N16000377]HPCL,UTTAR PRADESH	03/2019	5,450.20	03/2029	03/2029	0/0
44	CITY GAS DISTRIBUTION PROJECT IN WEST BENGAL - [N16000359]HPCL, WEST BENGAL	03/2019	5,830.20	03/2031	03/2031	0/0
	Indian Oil Corporation Limited					
45	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL	04/2016	1,021.00	12/2020	12/2020	0/0
46	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH	01/2015	342.00	03/2021	03/2021	0/0
47	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH	07/2014	247.00	03/2021	03/2021	0/0
48	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH	08/2017	384.58	04/2021	03/2021	0/0
49	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00	01/2021	04/2021	0/0
50	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL, MAHARASHTRA	05/2016	261.00	01/2021	04/2021	0/0
51	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00	04/2021	07/2021	0/0
52	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL, HARYANA	09/2019	164.69	07/2021	07/2021	0/0
53	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43	10/2020	08/2021	0/0
54	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 293.00	06/2020 09/2021	09/2021	0/0
55	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA	05/2016	348.00	01/2021	10/2021	0/0
56	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL, ANDHRA PRADESH	10/2018	316.20	10/2021	10/2021	0/0
57	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL, HARYANA	08/2019	1,255.00	10/2021	10/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
58	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
59	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 12/2021	12/2021	0/0
60	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	07/2022	0/0
61	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	07/2022 -	07/2022	0/0
62	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0
63	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	12/2022 -	12/2022	0/0
64	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	12/2022	0/0
65	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00 -	01/2023 -	01/2023	0/0
66	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	955.00 -	04/2022 -	02/2023	0/0
67	GRASS ROOT TERMINAL AT MALAPUR - [N16000351]IOCL,TAMIL NADU	12/2018	611.00 -	04/2022 -	08/2023	0/0
68	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	09/2023	0/0
69	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	01/2024 -	01/2024	0/0
70	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
Indian Strategic Petroleum Reserves Ltd						
71	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
Mangalore Refinery And Petrochemicals Limited						
72	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA	06/2020	200.00 -	06/2023 -	06/2023	0/0
Numaligarh Refinery Limited						
73	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM	01/2019	12,366.00 -	10/2024 -	10/2024	0/0
74	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM	01/2019	10,228.00 -	10/2024 -	10/2024	0/0
Oil India Limited						
75	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	03/2021	0/0
76	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	-	0/0
POWER						
Central Public Works Department						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
77	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	03/2021	0/0
	<u>Chenab Valley Power Projects [P] Limited</u>					
78	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	07/2025	0/0
	<u>National Hydro-Electric Power Corporation</u>					
79	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
80	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
81	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
82	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-	0/0
83	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UR - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.14 -	09/2020 -	-	0/0
84	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UR - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	-	0/0
85	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	12/2018 -	-	0/0
86	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	11/2018 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
87	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 482.64	01/2019 04/2020	04/2020	0/0
88	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 04/2020	05/2020	0/0
89	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 06/2020	09/2020	0/0
90	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 06/2020	09/2020	0/0
91	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 04/2020	01/2021	0/0
92	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 05/2020	01/2021	0/0
93	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	02/2021	0/0
94	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	02/2021	0/0
95	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	02/2021	0/0
96	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	03/2021	0/0
97	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
98	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 05/2020	03/2021	0/0
99	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 05/2020	03/2021	0/0
100	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 04/2020	03/2021	0/0
101	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 09/2020	03/2021	0/0
102	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 06/2020	03/2021	0/0
103	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	07/2019 06/2020	03/2021	0/0
104	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 09/2020	03/2021	0/0
105	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2021	0/0
106	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPIP FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	02/2018 -	12/2021	0/0
107	GREEN ENERGY CORRIDORS UNDER STATE TRANSMISSION SCHEME PAPERED [N18000218]PGCIL,MULTI STATE	05/2016	2,519.59 -	05/2019 -	-	0/0
108	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-	0/0
109	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-	0/0
110	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
111	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH	11/2020	1,810.56 -	01/2026 -	01/2026	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
112	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 12/2020	12/2020	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Central Public Works Department</u>					
113	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
114	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
115	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>HII Infra Tech Services Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
116	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	07/2021	0/0
117	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	07/2021	0/0
118	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	07/2022	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
119	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
120	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
121	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	12/2020	0/0
122	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
123	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021	0/0
124	LHMC NEW DELHI RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	14.11 -	11/2013 -	03/2021	0/0
125	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
126	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
127	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2021	0/0
128	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	03/2021	0/0
129	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	06/2021	0/0
130	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	06/2021	0/0
131	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	06/2021	0/0
132	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	12/2021	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
133	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 03/2020	03/2020	0/0
134	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2023	0/0
135	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
136	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
137	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
138	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
139	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
140	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
141	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
142	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
143	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
144	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
145	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,135.6 -	03/2022 -	03/2024	0/0
146	WARDHA - NAGPUR - 4TH LINE (71 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2022 -	03/2024	0/0
<u>Container Corporation Of India</u>						
147	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020	0/0
148	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 12/2020	12/2020	0/0
149	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
150	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2021	0/0
151	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2021	0/0
152	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
153	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-	0/0
154	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-	0/0
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
155	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
156	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
<u>East Central Railways</u>						
157	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	09/2020	0/0
158	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
159	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
160	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	03/2021	0/0
161	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
162	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2021	0/0
163	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	03/2012 -	05/2021	0/0
164	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 -	- -	03/2022	0/0
165	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	03/2022	0/0
166	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
167	FATUHA-ISLAMPUR INCLUDING EXTENSION OF NEW LINE FORM BARHARSHAR BARBIGHA, DANIYAWAN-BIHARSARIF - [N22000176]ECR,BIHAR	04/1991	329.39 -	- -	03/2022	0/0
168	MUZAFFARPUR - SAGAULI DOUBLING 100.0 KM - [N220100473]ECR,BIHAR	04/2016	731.54 -	03/2021 -	06/2022	0/0
169	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	03/2012 -	11/2022	0/0
170	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	02/2023	0/0
171	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
172	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	03/2023	0/0
173	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- -	03/2023	0/0
174	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	03/2020 -	03/2023	0/0
175	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
176	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
177	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2024	0/0
178	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
179	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-	0/0
180	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
181	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-	0/0
182	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
183	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
184	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
185	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
186	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
187	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
188	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-	0/0
189	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
	<u>East Coast Railway</u>					
190	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.00 1,139.28	02/2012 02/2021	12/2021	0/0
191	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	55.31 238.03	03/2020 07/2021	03/2022	0/0
192	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
193	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2024	03/2024	0/0
194	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2024	03/2024	0/0
195	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 810.02	11/2018 03/2024	03/2024	0/0
196	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2024	03/2024	0/0
197	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 03/2025	03/2025	0/0
198	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 03/2026	03/2026	0/0
199	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
	<u>Eastern Railways</u>					
200	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
201	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021	0/0
202	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
203	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
204	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
205	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64	-	03/2022	0/0
206	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09	02/2013	03/2024	0/0
207	MONIGRAM- NIMTITA - [N22000301]ER, MULTI STATE	04/2012	250.93	-	03/2024	0/0
208	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91	03/2019 12/2009	03/2025	0/0
209	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99	03/2006	03/2025	0/0
210	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	450.00	-	03/2025	0/0
211	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03	-	03/2025	0/0
212	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98	03/2022	03/2025	0/0
213	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONG WITH KRISHNANAGAR - CHAPRA NEW LINE AND MAHATI-NAGAR 'A' 3 - [N22000224]ER, MULTI STATE	04/2001	23.92	03/2016	03/2025	0/0
214	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.51	03/2017	03/2025	0/0
215	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER, MULTI STATE	04/2010	174.56	-	03/2025	0/0
216	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28	03/2016	03/2025	0/0
217	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	365.17	03/2017	03/2025	0/0
218	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55	-	03/2025	0/0
219	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17	-	03/2025	0/0
220	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	494.54	03/2005	03/2025	0/0
221	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER, MULTI STATE	04/2000	297.47	-	03/2025	0/0
222	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER, MULTI STATE	04/2003	337.96	-	03/2025	0/0
223	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER, MULTI STATE	04/2009	499.96	02/2012	03/2025	0/0
224	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE	04/2009	257.42	03/2014	03/2025	0/0
225	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER, MULTI STATE	04/2011	166.89	-	03/2025	0/0
226	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60	03/2017	03/2026	0/0
Indian Railway Construction Company Limited						
227	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON, ODISHA	04/2016	5,200.00 962.00	03/2020 03/2024	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Kolkata Metro Rail Corporation Limited</u>					
228	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
229	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2021	0/0
230	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
231	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 -	03/2004 -	03/2022	0/0
232	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
233	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
234	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
235	JHANSI MANIKPUR AND KALAIRAR DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	1,329.63 -	03/2021 03/2026	03/2023	0/0
236	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
237	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
238	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 4,084.69	12/2015 12/2023	03/2023	0/0
239	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 -	03/2019 -	01/2021	0/0
240	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 4,541.38	12/2008 -	02/2021	0/0
241	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
242	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2021	0/0
243	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	05/2021	0/0
244	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- -	12/2021	0/0
245	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	03/2022	0/0
246	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	03/2023	0/0
247	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 1,105.00	03/2019 -	03/2023	0/0
248	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 7,114.55	03/2015 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
249	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,047.51	03/2019 -	03/2023	0/0
250	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	03/2023	0/0
251	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
252	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	03/2014 -	12/2023	0/0
253	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	03/2019 -	03/2024	0/0
254	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	03/2019 -	-	0/0
255	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
256	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
257	NEW BG LINE FROM BALURGHAT TO HALLYT - [N22000206]NFR,MULTI STATE	04/2010	42.22 -	03/2020 -	-	0/0
258	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
259	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
<u>North Eastern Railway</u>						
260	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021	0/0
261	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
262	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
263	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0
264	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0
265	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
266	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022	0/0
267	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
268	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
269	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
270	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
271	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
272	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
273	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
274	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
275	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
276	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
	<u>North Western Railway</u>					
277	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020	0/0
278	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021	0/0
279	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.30 -	11/2012 -	03/2021	0/0
280	MAVLI JUNCTION BARI SARDI, MMCT AJMER- CHITTSARGAR -UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	20.18 -	03/2020 -	06/2021	0/0
281	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	11/2021	0/0
282	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
283	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	06/2022	0/0
284	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-	0/0
285	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
286	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
287	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021	0/0
288	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	06/2021	0/0
289	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	12/2022	0/0
290	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	- -	03/2023	0/0
291	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
292	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0
293	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
294	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 196.17	- -	03/2024	0/0
295	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
296	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	03/2023 03/2025	03/2025	0/0
297	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
298	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
299	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
300	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
301	DAUND-GULBARGA - DOUBLING (24.9 KM) AND PUNE-SUNTAVAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2021	0/0
302	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	06/2021	0/0
303	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
304	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2021	0/0
305	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	12/2021	0/0
306	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	12/2021	0/0
307	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2021	0/0
308	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
309	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
310	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	06/2022	0/0
311	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
312	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
313	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
314	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76 -	12/2023 -	12/2023	0/0
315	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
316	SECUNDERABAD-MAHABUNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
317	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
318	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
319	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
320	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
321	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
322	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
323	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
324	VIZIANAGARAM - JAMABAD PUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2026	0/0
325	HARIDASPUR-PARADEEP (NL) - [N22010028]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-	0/0
<u>Railway Electrification</u>						
326	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
327	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	12/2022	0/0
328	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2023	0/0
329	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2024	0/0
330	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 03/2025	03/2024	0/0
331	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
332	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 03/2025	03/2024	0/0
333	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
334	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
335	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
336	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- 08/2020	08/2020	0/0
337	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 10/2020	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
338	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	12/2021 12/2023	12/2023	0/0
	<u>South Eastern Railway</u>					
339	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020	0/0
340	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	12/2018 12/2018	06/2021	0/0
341	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 03/2020	12/2021	0/0
342	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 03/2021	12/2023	0/0
343	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	03/2025	0/0
344	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
345	BANKURA DAMODAR VALLEY RLY LINE 96 KM CC WITH 6MIS FOR M - [N22000402]SER, WEST BENGAL	04/2009	1,027.40 1,666.70	03/2009 -	03/2030	0/0
346	HOWRAH-AMTA- HAMPAL ANGA NL - (SWR) - [22010023]SER, WEST BENGAL	04/1974	93.46 154.30	03/2007 03/2007	-	0/0
347	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
	<u>South Western Railway</u>					
348	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	03/2021	0/0
349	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	06/2021	0/0
350	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
351	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
352	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
353	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
354	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
355	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
356	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
357	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
358	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
359	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
360	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	12/2024	0/0
361	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	-	0/0
	<u>Southern Railway</u>					
362	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 01/2021	12/2020	0/0
363	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- 02/2021	02/2021	0/0
364	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	09/2021	0/0
365	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021	0/0
366	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	12/2021	0/0
367	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	06/2022	0/0
368	MADURAI - MANIYACHI - TUTICORIN (100 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	600.00 -	03/2022 -	06/2022	0/0
369	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- 03/2024	03/2024	0/0
370	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2025	0/0
371	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
372	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	03/2025	0/0
373	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
374	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
375	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0
376	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
377	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
378	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
379	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
380	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-	0/0
381	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
382	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
383	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
384	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.00	- -	-	0/0
385	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
386	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
	<u>Western Railway</u>					
387	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 12/2020	12/2020	0/0
388	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 890.76	03/2019 10/2021	10/2021	0/0
389	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	03/2021 03/2022	03/2022	0/0
390	SURENDRA NAGAR-DABHOI - [N22000392]WR,GUJARAT	04/2015	1,002.30 1,002.39	03/2021 12/2022	12/2022	0/0
391	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO MAYOF (WR) - [N22000123]WR,GUJARAT	04/2008	18.24 411.52	03/2012 03/2023	03/2023	0/0
392	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2023	03/2023	0/0
393	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	03/2019 03/2023	03/2023	0/0
394	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 03/2023	03/2023	0/0
395	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	03/2020 12/2023	12/2023	0/0
396	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	03/2022 03/2024	03/2024	0/0
397	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2024	03/2024	0/0
398	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2025	03/2025	0/0
399	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
400	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
401	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
402	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
403	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
404	PALANPUR KHOJAYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	Central Public Works Department					
405	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-	0/0
	Ministry Of Road Transport And Highways (State Pwds)					
406	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FROM - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	08/2020	0/0
407	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	08/2021	0/0
408	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
409	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0
410	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020	0/0
411	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10	10/2019	04/2020	0/0
412	4 LANING OF NH-15 FROM DESIGN CHAINAGE 29/500 TO 40/000 (ITANAGAR TO BANDARDEWA SECTION) IN THE STATE OF - [N24001195]MoRTH,UTTAR PRADESH	11/2016	43.80 -	- -	09/2020	0/0
413	REHABILITATION AND UPGRADE OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 10/2020	10/2020	0/0
414	REHABILITATION AND UPGRADE OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020	0/0
415	REHABILITATION AND UPGRADE TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34	01/2019 09/2020	11/2020	0/0
416	REHABILITATION AND UPGRADE OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	11/2020	0/0
417	REHABILITATION AND UPGRADE OF BALRAMPUR-TULSI PUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	11/2020	0/0
418	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	11/2020	0/0
419	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
420	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35	11/2020 05/2021	11/2020	0/0
421	REHABILITATION AND UPGRADE OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	11/2020	0/0
422	REHABILITATION AND UPGRADE OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	11/2020	0/0
423	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	11/2020	0/0
424	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020	0/0
425	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 12/2020	12/2020	0/0
426	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 12/2020	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
427	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 12/2020	12/2020	0/0
428	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020	0/0
429	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	12/2020	0/0
430	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020	0/0
431	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 634.30	12/2019 12/2020	12/2020	0/0
432	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	12/2020	0/0
433	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020	0/0
434	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020	0/0
435	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 138.00 TO 71.00 IN MIZORAM TO SUPPORT KILADAN TUNNEL MOD - [N24001161]MoRTH,MIZORAM	08/2010	86.96 -	09/2014 12/2020	12/2020	0/0
436	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-6 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.38 -	12/2019 -	12/2020	0/0
437	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	10/2016 12/2020	12/2020	0/0
438	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	12/2020 -	12/2020	0/0
439	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	12/2020	0/0
440	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 01/2021	01/2021	0/0
441	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 02/2021	02/2021	0/0
442	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021	0/0
443	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 02/2021	02/2021	0/0
444	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	02/2021	0/0
445	REPAIR AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	02/2021	0/0
446	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 02/2021	02/2021	0/0
447	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	03/2021	0/0
448	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 01/2021	03/2021	0/0
449	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 173.41	08/2018 03/2021	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
450	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH, WEST BENGAL	03/2018	254.30 254.30	10/2020 -	03/2021	0/0
451	UPGRADATION OF PORSABHIND ROAD TO 2L + PS - [N24000890]MoRTH, MADHYA PRADESH	03/2018	217.22 226.88	08/2018 03/2021	03/2021	0/0
452	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH, MADHYA PRADESH	03/2018	233.04 -	03/2018 01/2021	03/2021	0/0
453	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH, MADHYA PRADESH	11/2017	249.05 -	07/2018 03/2021	03/2021	0/0
454	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH, MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2021	03/2021	0/0
455	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH, MADHYA PRADESH	02/2018	279.44 -	03/2018 12/2020	03/2021	0/0
456	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH, MADHYA PRADESH	03/2016	877.79 -	06/2019 03/2021	03/2021	0/0
457	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH, UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021	0/0
458	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KALGHATA TO SARVARDEWLA ROAD - [N24001198]MoRTH, MADHYA PRADESH	01/2019	264.50 -	03/2021 -	03/2021	0/0
459	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH, RAJASTHAN	03/2019	178.13 -	- -	03/2021	0/0
460	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH, UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2021	0/0
461	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH, CHHATISGARH	01/2016	497.14 527.66	08/2016 03/2021	03/2021	0/0
462	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH, CHHATISGARH	01/2016	476.20 543.73	09/2016 03/2021	03/2021	0/0
463	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH, CHHATISGARH	03/2016	452.94 435.61	07/2016 03/2021	03/2021	0/0
464	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION - [N24001224]MoRTH, CHHATISGARH	03/2017	423.79 -	01/2018 03/2021	03/2021	0/0
465	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH, CHHATISGARH	12/2014	496.02 -	03/2015 03/2021	03/2021	0/0
466	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH, CHHATISGARH	11/2017	188.80 -	05/2019 03/2021	03/2021	0/0
467	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH, CHHATISGARH	12/2014	379.16 -	11/2017 03/2021	03/2021	0/0
468	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	04/2021	0/0
469	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH, MADHYA PRADESH	12/2015	957.54 -	02/2020 04/2021	04/2021	0/0
470	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH, MADHYA PRADESH	02/2018	169.63 -	03/2018 04/2021	04/2021	0/0
471	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2020	04/2021	0/0
472	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH, UTTAR PRADESH	03/2018	263.89 -	04/2020 -	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
473	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2020	05/2021	0/0
474	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH, MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	05/2021	0/0
475	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH, PUNJAB	03/2018	170.57 -	11/2020 -	05/2021	0/0
476	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH, KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
477	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH, MADHYA PRADESH	06/2015	390.51 -	- 12/2020	06/2021	0/0
478	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH, MIZORAM	08/2010	195.04 -	10/2010 06/2021	06/2021	0/0
479	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH, MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	06/2021	0/0
480	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH - [N24000886]MoRTH, MADHYA PRADESH	01/2017	205.05 -	03/2017 5/2021	06/2021	0/0
481	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM 182 TO 266 OF NH-59A - [N24000899]MoRTH, MADHYA PRADESH	01/2017	73.32 -	09/2019 6/2021	06/2021	0/0
482	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH, MADHYA PRADESH	11/2017	392.33 428.55	03/2018 06/2021	06/2021	0/0
483	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH, PUNJAB	03/2018	322.48 -	07/2020 -	08/2021	0/0
484	R AND U OF KHUTAR-LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH, UTTAR PRADESH	11/2016	326.99 327.00	- -	09/2021	0/0
485	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH, MADHYA PRADESH	03/2018	214.69 -	03/2018 09/2021	09/2021	0/0
486	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH, ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
487	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH, JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021	0/0
488	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH, MADHYA PRADESH	11/2011	954.43 -	09/2015 -	10/2021	0/0
489	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL	02/2018	426.18 426.18	09/2020 -	12/2021	0/0
490	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	08/2019 -	12/2021	0/0
491	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH, RAJASTHAN	03/2020	370.36 -	08/2022 -	08/2022	0/0
492	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	08/2019 -	11/2022	0/0
493	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH, NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
494	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH, TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
495	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH, KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
496	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
497	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
498	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
499	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
500	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
501	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
502	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
503	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
504	TWO LANING OF KHONSA - TISSA - LINGDING (NH 52E (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000300]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 76.00	02/2012 -	-	0/0
505	TWO LANING OF TALPUL - MANMAO - CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.19 -	03/2011 -	-	0/0
506	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-	0/0
507	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
508	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
509	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
510	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
511	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
512	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
513	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
514	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
515	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
516	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
517	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
518	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
519	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
520	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-	0/0
521	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-	0/0
522	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-	0/0
523	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
524	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
525	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
526	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANUARA-PURRI - [N24000397]MoRTH, WEST BENGAL	01/1991	222.00 -	03/2018 -	-	0/0
527	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.11 -	03/2018 -	-	0/0
528	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
529	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
530	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
531	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
532	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
533	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-	0/0
534	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
535	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
536	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-	0/0
537	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-	0/0
538	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-	0/0
539	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
540	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-	0/0
541	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
542	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-	0/0
543	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-	0/0
544	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
545	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
546	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
547	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
548	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
549	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
550	FOUR LANEING OF GAYA-BUSUA-RAJCHANDANAL-BIHARSHAF SECION (KM 0.0 TO 92.935) ON NH-62 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,108.35 -	07/2016 -	-	0/0
551	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.30 -	07/2016 -	-	0/0
552	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
553	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
554	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
555	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
556	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
557	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
558	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
559	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
560	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
561	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
562	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-	0/0
563	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
564	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-	0/0
565	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-	0/0
566	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-	0/0
567	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-	0/0
568	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-	0/0
569	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-	0/0
570	REHABILITATION AND UP GRADATION OF 2 LANE 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.500 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.55 -	-	-	0/0
571	CONSTRUCTION OF KUNDI BYPASS FROM EXISTING KM 33+100 TO KM 41+200 (EXISTING LENGTH: 8.130 Km), DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	148.00 -	05/2020 -	-	0/0
572	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	-	-	0/0
573	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-	0/0
574	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-	0/0
575	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-	0/0
576	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-	0/0
577	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-	0/0
578	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
579	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
580	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
581	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
582	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
583	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
584	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
585	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
586	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
587	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
588	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-	0/0
589	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0
590	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0
591	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
592	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
593	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
594	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANI EGUDA- AVULAPALLY SECTI - [N24000985]MoRTH,TELANGANA	01/2017	259.27 -	05/2019 -	-	0/0
595	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.25 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
596	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
597	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
598	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
599	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
600	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
601	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0
602	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
603	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
604	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
605	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
606	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
607	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 232.90	10/2019 -	-	0/0
608	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-	0/0
609	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
610	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-	0/0
611	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-	0/0
612	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
613	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
614	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
615	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-	0/0
616	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-	0/0
617	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
618	TEMBHURNI PANDHARPUR MANGALWADHARVAD UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	222.02 222.00	07/2019 -	-	0/0
619	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	03/2020 -	-	0/0
620	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-	0/0
621	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
622	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
623	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-	0/0
624	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-	0/0
625	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-	0/0
626	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-	0/0
627	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-	0/0
628	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-	0/0
629	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
630	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-	0/0
631	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
632	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-	0/0
633	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
634	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-	0/0
635	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-	0/0
636	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-	0/0
637	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	-	0/0
638	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-	0/0
639	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-	0/0
640	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-	0/0
641	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-	0/0
642	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 114.00 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001154]MoRTH,KARNATAKA	08/2016	167.14 -	01/2017 -	-	0/0
643	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.66 TO 115.00 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
644	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
645	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
646	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
647	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
648	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
649	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
650	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 386.40	10/2018 -	-	0/0
651	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 386.40	10/2018 -	-	0/0
652	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
653	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
654	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
655	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
656	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
657	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
658	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
659	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
660	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	-	0/0
661	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-	0/0
662	REHABILITATION & UPGADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-	0/0
663	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
664	REHABILITATION AND UPGADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-	0/0
665	REHABILITATION AND UPGADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0
666	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 TO - [N24001211]MoRTH,UTTAR PRADESH	11/2018	81.45 -	- -	-	0/0
667	WIDENING OF SL TO 2 L KM 107.34.80 SJKUMA TO KONTA ON NH 211 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.39 271.00	03/2013 -	-	0/0
668	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-	0/0
669	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ - [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-	0/0
670	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-	0/0
671	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-	0/0
672	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 05/2016	06/2021	0/0
673	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
674	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	07/2022	0/0
675	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	09/2018 -	-	0/0
676	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
677	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	-	0/0
678	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
679	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	-	0/0
680	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	-	0/0
681	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	-	0/0
682	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	-	0/0
683	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 10/2020	-	0/0
684	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	-	0/0
685	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHIJOF ROAD SECTION OF NH-44A FROM MANGANISH VILLAGE - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2016	53.44 -	07/2019 -	-	0/0
686	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
687	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
688	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-	0/0
689	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
690	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
691	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-	0/0
692	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0
National Highways Authority Of India						
693	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	05/2018	0/0
694	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	12/2020	0/0
695	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	12/2020	0/0
696	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	12/2020	0/0
697	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	12/2020	0/0
698	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
699	FOUR LANNING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
700	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018	0/0
701	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
702	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
703	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019	0/0
704	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
705	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019	0/0
706	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020	0/0
707	4 LANING OF KAKHAKOTI AM TO MUKHOLA SECTION OF NH-7 - [N24000459]NHAI,KERALA	06/2015	245.24 -	- 01/2020	01/2020	0/0
708	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020	0/0
709	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020	0/0
710	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
711	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
712	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	08/2020	0/0
713	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	08/2020	0/0
714	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020	0/0
715	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020	0/0
716	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 2,754.00	01/2018 12/2018	09/2020	0/0
717	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 2,173.74	- -	09/2020	0/0
718	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
719	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020	0/0
720	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020	0/0
721	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020	0/0
722	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 08/2020	11/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
723	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	11/2020	0/0
724	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2020	0/0
725	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
726	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
727	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	11/2020	0/0
728	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
729	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2020	0/0
730	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020	0/0
731	HARIDWAR DEHRA DUN A PROVED LENGTH 69 - [N24000212]NHAI,UT PRAKASH	11/2011	178.51 -	07/2013 -	12/2020	0/0
732	2-LANING WITH PAVED SHOULDER OF RAIBAREILI - BANDA SECTION OF NH-23 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020	0/0
733	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
734	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
735	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020	0/0
736	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	12/2020	0/0
737	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	12/2020	0/0
738	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	12/2020	0/0
739	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020	0/0
740	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	12/2020	0/0
741	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	12/2020	0/0
742	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2020	0/0
743	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020	0/0
744	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021	0/0
745	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 07/2019	01/2021	0/0
746	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
747	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	01/2021	0/0
748	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	01/2021	0/0
749	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021	0/0
750	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	02/2021	0/0
751	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
752	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	03/2020 -	02/2021	0/0
753	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	02/2021	0/0
754	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
755	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.35 -	03/2013 -	03/2021	0/0
756	SIX LANING OF CHANDIKHOL-RAIPUR SECTION OF NH-43 - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	03/2014 03/2021	03/2021	0/0
757	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021	0/0
758	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 10/2020	03/2021	0/0
759	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021	0/0
760	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
761	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	03/2021	0/0
762	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021	0/0
763	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	03/2021	0/0
764	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	04/2021	0/0
765	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
766	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	05/2021	0/0
767	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	05/2021	0/0
768	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
769	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	05/2021	0/0
770	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	05/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
771	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 1,118.19	- -	05/2021	0/0
772	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 06/2021	06/2021	0/0
773	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	06/2021	0/0
774	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	06/2021	0/0
775	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	06/2021	0/0
776	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	06/2021	0/0
777	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	06/2021	0/0
778	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	06/2021	0/0
779	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000730]NHAI,ODISHA	01/2018	686.35 -	- -	06/2021	0/0
780	REHABILITATION SIX LANING UPGRADATION ON BHADRAK BALESHWAR - [N24000737]NHAI,ODISHA	01/2018	999.00 -	- -	06/2021	0/0
781	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	06/2021	0/0
782	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
783	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2021	0/0
784	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	07/2021	0/0
785	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
786	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	07/2021	0/0
787	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	07/2021	0/0
788	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	07/2021	0/0
789	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
790	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	07/2021	0/0
791	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
792	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
793	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
794	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
795	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	09/2021	0/0
796	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	09/2021	0/0
797	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
798	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	09/2021	0/0
799	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
800	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	09/2021	0/0
801	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- 06/2021	09/2021	0/0
802	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
803	SIX-LANING OF BANGALORE - NIDARGUDDA SECTION, KM 18.00 TO KM 74.20 OF NH-275 IN THE STATE OF KARNATAKA - [N24000787]NHAI,KARNATAKA	02/2018	1,195.34 -	- -	11/2021	0/0
804	CONSTRUCTION OF FLYOVER AT LAKHANPUR TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.63 -	- 08/2021	11/2021	0/0
805	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 12/2021	12/2021	0/0
806	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 06/2021	12/2021	0/0
807	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 06/2021	12/2021	0/0
808	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 01/2021	12/2021	0/0
809	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
810	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	12/2021	0/0
811	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
812	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	- -	02/2022	0/0
813	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	03/2022	0/0
814	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	03/2022	0/0
815	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
816	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
817	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
818	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
819	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
820	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
821	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
822	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
823	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
824	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
825	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
826	GHAZIABAD-ALICHAH NH-1 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,411.00 -	03/2013 -	-	0/0
827	TIRUPATI - TIRUTHANI - CHENNAI - [N24000171]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
828	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
829	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
830	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
831	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
832	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
833	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
834	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
835	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
836	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
837	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
838	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
839	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-	0/0
840	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
841	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
842	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
843	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
844	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
845	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
846	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	-	0/0
847	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
848	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-	0/0
849	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
850	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	74.28 -	07/2018 -	-	0/0
851	6 LANING OF AGRA - ETAWA BY PASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	2,657.20 -	01/2019 -	-	0/0
852	4 LANING OF SOLAPUR - YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
853	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
854	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
855	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
856	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
857	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	03/2018 09/2020	-	0/0
858	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
859	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
860	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
861	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
862	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
863	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
864	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
865	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
866	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
867	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
868	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
869	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-	0/0
870	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 1,182.94	- -	-	0/0
871	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
872	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 2,360.65	- -	-	0/0
873	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
874	TWO LANING WITH PS OF JINCHANG - KANUWALA - ROOPAS - DOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	75.00 -	- -	-	0/0
875	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
876	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-	0/0
877	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
878	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
879	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
880	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-	0/0
881	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
882	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-	0/0
883	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
884	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
885	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-	0/0
886	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-	0/0
887	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
888	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
889	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
890	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-	0/0
891	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	-	0/0
892	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
893	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	-	0/0
894	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-	0/0
895	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
896	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-	0/0
897	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-	0/0
898	4/6 LANING FROM KHARA TO LUDHYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	-	0/0
899	4 LANING FROM HAWAHA TO FUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	2,169.61 -	- -	-	0/0
900	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	08/2018 -	-	0/0
901	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	05/2019 -	-	0/0
902	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
903	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-	0/0
904	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA	09/2016	1,004.67 -	05/2019 -	-	0/0
905	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
906	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
907	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
908	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	07/2018 -	-	0/0
909	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
910	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDEULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	05/2019 -	-	0/0
911	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	02/2020 -	-	0/0
912	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
913	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
914	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-	0/0
915	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	-	0/0
916	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-	0/0
917	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
918	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
919	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
920	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0
921	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
922	4-LANNING OF O TANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
923	SIX LANING OF CHENNAI-MAADA SECTION OF NH-5 FROM KM 110/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.00 -	-	-	0/0
924	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	-	-	0/0
925	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	-	-	0/0
926	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	-	-	0/0
927	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	-	-	0/0
928	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	-	-	0/0
929	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	-	-	0/0
930	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	-	-	0/0
931	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	-	-	0/0
932	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	-	-	0/0
933	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
934	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	-	-	0/0
935	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	-	-	0/0
936	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
937	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
938	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
939	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
940	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
941	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
942	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
943	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
944	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
945	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IV FOR DARGAMAGPUR-JA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
946	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.35 -	- -	-	0/0
947	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROAD - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
948	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
949	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
950	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
951	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
952	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
953	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
954	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
955	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
956	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
957	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
958	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0
959	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-	0/0
960	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
961	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
962	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
963	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-	0/0
964	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0
965	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
966	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-	0/0
967	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
968	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- 02/2020	-	0/0
969	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,200.06 -	- -	-	0/0
970	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.12 -	- -	-	0/0
971	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
972	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-	0/0
973	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-	0/0
974	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-	0/0
975	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
976	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-	0/0
977	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-	0/0
978	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Inland Waterways Authority Of India</u>					
979	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	5,369.18 -	03/2023 -	03/2023	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
980	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	06/2021 -	11/2021	0/0
	<u>Central Public Works Department</u>					
981	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	03/2018 12/2020	12/2020	0/0
	<u>Department Of Telecommunication</u>					
982	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	06/2021	0/0
983	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]DOT,MULTI STATE	05/2006	1,077.00 -	03/2009 -	-	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
984	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,DELHI	12/2005	249.00 -	02/2007 -	-	0/0
985	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,MAHARASHTRA	01/2006	247.00 -	02/2007 -	-	0/0
986	DELHI CONVERGENT BILLING AND CRM - [N26000099]MTNL,DELHI	02/2006	229.11 -	03/2011 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
987	AHMEDABAD METRO RAIL PROJECT PHASE I - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12/2018 -	11/2022	0/0
988	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT	03/2019	5,384.17 -	03/2024 -	03/2024	0/0
989	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	03/2024 -	03/2024	0/0
	<u>Central Public Works Department</u>					
990	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 02/2021	11/2020	0/0
991	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 884.30	12/2015 12/2020	12/2020	0/0
992	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	03/2021 07/2021	07/2021	0/0
993	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	07/2021 -	09/2021	0/0
994	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	08/2020 -	12/2021	0/0
995	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 -	03/2022	0/0
996	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
997	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOB LA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-	0/0
998	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112,TYPE V-68, TYPE-VI-5), SHOPS,CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	09/2020 -	-	0/0
	<u>Delhi Metro Rail Corporation</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
999	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2021	0/0
1000	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 -	09/2021	0/0
1001	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65 -	03/2025 -	03/2025	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1002	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1003	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1004	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	03/2024	0/0
1005	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	03/2024	0/0
1006	LUCKNOW METRO RAIL CORPORATION LTD - [N28000104]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1007	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 -	11/2021	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1008	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1009	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1010	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1011	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-	0/0
	<u>National Capital Region Transport Corp</u>					
1012	DELHI GHAZIABAD MEERUT RTS CORRIDOR - [N28000134]NCRTC,MULTI STATE	03/2019	30,274.00 -	06/2025 -	06/2025	0/0
	<u>Patna Metro Rail Corporation</u>					
1013	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL,BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1014	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1015	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 -	12/2020	0/0
1016	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	12/2020	0/0
1017	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	04/2020 -	12/2020	0/0
1018	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 -	12/2020	0/0
1019	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	01/2021	0/0
1020	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
1021	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021	0/0
1022	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0
1023	SEWER NETWORKS SPS AND STP BEUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
1024	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
1025	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	12/2021	0/0
1026	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0
1027	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
1028	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-	0/0
<u>Delhi Jal Board</u>						
1029	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021	0/0
1030	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
1031	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
1032	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
1033	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-	0/0
<u>Kolkata Metropolitan Development Authority</u>						
1034	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 -	12/2020	0/0
1035	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	12/2020	0/0
1036	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1037	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
1038	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
1039	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 -	02/2022 -	02/2022	0/0
1040	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 -	02/2022 -	02/2022	0/0
1041	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
1042	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
1043	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0
1044	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
1045	INTERCEPTION AND DIVERSION TREATMENT WORKS AT TULLY'S CULLAHADI GARDIGI - [N30000034]KMDA, WEST BENGAL	08/2017	107.12 -	09/2022 -	09/2022	0/0
	Uttar Pradesh Jal Nigam					
1046	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UP JalNigam, UTTAR PRADESH	10/2016	370.40 -	08/2020 -	12/2020	0/0
1047	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UP JalNigam, UTTAR PRADESH	02/2017	161.31 -	11/2019 -	12/2020	0/0
1048	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP JalNigam, UTTAR PRADESH	02/2011	279.91 -	12/2019 -	12/2020	0/0
1049	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45 -	12/2020 -	01/2021	0/0
1050	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
1051	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]UP JalNigam, UTTAR PRADESH	02/2019	317.19 -	08/2021 -	08/2021	0/0
1052	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
1053	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UP JalNigam, UTTAR PRADESH	03/2018	904.00 -	09/2021 -	09/2021	0/0
1054	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
1055	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0
1056	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam, UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
1057	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam, UTTAR PRADESH	10/2017	213.62 -	03/2022 -	03/2022	0/0
1058	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UP JalNigam, UTTAR PRADESH	12/2018	857.26 -	08/2021 -	06/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1059	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
1060	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 -	07/2021 -	06/2022	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
1061	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-	0/0
1062	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	-	0/0
	<u>COMMERCE AND INDUSTRY</u>					
	<u>Delhi Mumbai Industrial Corridor</u>					
1063	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021	0/0
	<u>India International Convention And Expo Centre</u>					
1064	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000000]IICC,DELHI	11/2017	4,730.00 -	02/2019 -	07/2021	0/0
	<u>National Building Construction Corporation Ltd</u>					
1065	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	10/2020	0/0
	<u>HUMAN RESOURCE DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
1066	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	07/2022 -	07/2020	0/0
1067	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	11/2020	0/0
1068	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 171.72	03/2020 -	06/2021	0/0
1069	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE 1A AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	03/2021 -	06/2022	0/0
1070	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH	09/2018	392.51 -	06/2022 -	06/2022	0/0
1071	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD,CHHATISGARH	03/2020	808.62 -	07/2022 -	07/2022	0/0
1072	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	03/2022 -	09/2022	0/0
1073	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	09/2022 04/2023	01/2023	0/0
1074	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 748.19	04/2023 -	04/2023	0/0
	<u>EdCIL(India) Limited</u>					
1075	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-	0/0
	<u>Indian Institute Of Technology, Kharagpur</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2020)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1076	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
1077	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	12/2020	0/0
	<u>HOME AFFAIRS</u>					
	<u>Central Public Works Department</u>					
1078	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-- [N28000147]CPWD,HARYANA	01/2020	166.98 167.00	10/2023 -	10/2023	0/0
	Total		12,79,464.75 -			0/0
	Grand Total		12,79,464.75			0/0

FLASH REPORT

List of projects original without Date of Commissioning

Costing Rs.		150 Crore and above				(December 2020)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u>								
1	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84	268.84	228.89	-	12/2020	-	0/0
2	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01	249.07	216.09	-	01/2021	-	0/0
3	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56	156.64	111.58	-	03/2021	-	0/0
4	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02	601.02	333.61	-	06/2021	-	0/0
5	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99	582.99	424.09	-	06/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.09	651.9	421.72	-	06/2021	-	0/0
	Total		2,510.41	2,510.55	1,741.98				0/0
	<u>RAILWAYS</u> <u>East Central Railways</u>								
7	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00	735.20	379.45	-	03/2021	-	0/0
8	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14	1,470.50	1,095.55	-	03/2021	-	0/0
9	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07	3,500.00	3,494.01	-	03/2022	-	0/0
10	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87	614.45	333.16	-	03/2022	-	0/0
11	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56	1,858.75	383.64	-	03/2022	-	0/0
12	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39	1,483.14	1,177.09	-	03/2022	-	0/0
13	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00	519.33	265.08	-	02/2023	-	0/0
14	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65	2,066.78	1,510.98	-	03/2023	-	0/0
15	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91	1,625.87	712.11	-	03/2023	-	0/0
16	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17	1,605.17	23.74	-	03/2023	-	0/0

Costing Rs. 150 Crore and above (December 2020)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20	2,995.01	1.94	-	03/2024	-	0/0
18	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
	<u>Eastern Railways</u>								
19	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35	418.09	412.89	-	03/2021	-	0/0
20	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80	270.72	279.67	-	03/2022	-	0/0
21	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64	272.20	227.07	-	03/2022	-	0/0
22	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93	310.70	332.10	-	03/2024	-	0/0
23	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00	1,261.34	-	-	03/2025	-	0/0
24	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	260.10	11.05	-	03/2025	-	0/0
25	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPURIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	71.43	-	03/2025	-	0/0
26	BARARIPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.35	2,200.5	20.12	-	03/2025	-	0/0
27	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17	527.54	1.76	-	03/2025	-	0/0
28	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47	298.22	52.09	-	03/2025	-	0/0
29	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96	336.96	70.20	-	03/2025	-	0/0
30	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
31	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
32	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52	373.87	287.09	-	12/2021	-	0/0
33	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76	360.00	6.74	-	03/2022	-	0/0
	<u>North Eastern Railway</u>								
34	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50	714.34	56.54	-	12/2023	-	0/0
	<u>Northern Railway</u>								

Costing Rs. 150 Crore and above (December 2020)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
35	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	791.39	567.14	- -	03/2023	-	0/0
36	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
37	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	112.95	- -	09/2023	-	0/0
38	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 196.17	359.00	111.51	- -	03/2024	-	0/0
39	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
<u>South Eastern Railway</u>									
40	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
<u>South Western Railway</u>									
41	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,967.00	66.44	- -	12/2023	-	0/0
42	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	12/2023	-	0/0
43	SRINIVASA-PURA-MADANAPALLE NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	465.6	-	- -	12/2023	-	0/0
44	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.05 -	343.8	36	- -	12/2023	-	0/0
45	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	34	- -	12/2023	-	0/0
46	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	12/2023	-	0/0
47	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	3,911.65	156.88	- -	12/2024	-	0/0
48	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,432.50	1,096.12	- -	03/2025	-	2/2
<u>Southern Railway</u>									
49	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.73	340.21	- -	09/2021	-	0/0
50	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	457.08	439.49	- -	12/2021	-	0/0
51	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	559.95	319.22	- -	03/2025	-	0/0
52	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	582.83	233.89	- -	12/2025	-	0/0
	Total		22,827.97 -	41,668.08	14,798.07				2/2
<u>ROAD TRANSPORT AND HIGHWAYS</u>									
<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
53	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	904.82	739.41	- -	12/2020	-	0/0

Costing Rs. 150 Crore and above (December 2020)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
54	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13	178.13	110.91	-	03/2021	-	0/0
55	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	65.83	-	09/2021	-	0/0
56	<u>National Highways And Infrastructure Development Corporation Ltd.</u> FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL PRADESH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06	434.06	172.89	-	12/2020	-	2/4
57	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02	199.02	14.21	-	02/2021	-	0/4
58	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 131.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88	184.88	6.85	-	02/2021	-	0/4
59	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 TO KM 100.000 (D - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51	553.51	88.81	-	09/2021	-	0/4
60	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 TO KM 32.050] (D - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06	175.06	62.27	-	04/2022	-	0/4
61	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 TO KM 44.000] (D - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12	176.12	54.56	-	04/2022	-	0/4
62	<u>National Highways Authority Of India</u> DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21	1,087.00	672.82	-	12/2020	-	0/0
63	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARNAR) - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00	207.00	43.23	-	12/2020	-	0/0
64	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13	807.00	617.58	-	12/2020	-	0/0
65	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56	392.00	353.42	-	12/2020	-	0/0

Costing Rs. 150 Crore and above (December 2020)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
66	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73	1,308.73	293.43	-	12/2020	-	0/0
67	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65	1,069.65	611.71	-	01/2021	-	0/0
68	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82	1,727.66	1,672.28	-	01/2021	-	3/4
69	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11	1,251.11	1,084.26	-	01/2021	-	0/0
70	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75	1,339.00	761.37	-	01/2021	-	2/3
71	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76	207.00	193.26	-	01/2021	-	0/0
72	SIX LANING OF SHAMLI TO MOTACHILODHA FROM KM 401.00 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21	1,119.00	394.20	-	01/2021	-	0/0
73	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19	1,145.31	1,265.00	-	02/2021	-	0/0
74	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09	565.09	495.25	-	02/2021	-	0/0
75	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94	1,282.94	468.69	-	03/2021	-	0/0
76	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96	1,261.05	299.09	-	03/2021	-	0/0
77	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08	1,005.08	-	-	03/2021	-	0/0
78	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00	621.00	564.85	-	04/2021	-	2/3
79	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43	314.43	86.83	-	04/2021	-	0/0

Costing Rs. 150 Crore and above (December 2020)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
80	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11	806.11	145.70	-	04/2021	-	0/0
81	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10	1,244.10	1,547.00	-	05/2021	-	0/0
82	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35	505.35	240.60	-	05/2021	-	0/0
83	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74	478.74	127.42	-	05/2021	-	0/0
84	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96	1,008.96	895.53	-	06/2021	-	0/0
85	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 04.00 TO - [N24000715]NHAI,ODISHA	12/2017	686.65	686.65	227.63	-	06/2021	-	0/0
86	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51	417.51	127.61	-	06/2021	-	0/0
87	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86	668.86	276.59	-	06/2021	-	0/0
88	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65	686.65	260.60	-	06/2021	-	0/0
89	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00	1,522.00	304.40	-	06/2021	-	0/0
90	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00	999.00	102.70	-	06/2021	-	0/0
91	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88	503.88	25.40	-	06/2021	-	0/0
92	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05	2,043.00	1,327.65	-	06/2021	-	0/0
93	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00	479.00	456.80	-	07/2021	-	0/0

Costing Rs. 150 Crore and above (December 2020)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
94	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61	1,048.10	841.64	-	07/2021	-	2/4
95	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88	1,021.00	235.12	-	07/2021	-	1/4
96	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15	1,323.15	785.33	-	07/2021	-	0/0
97	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26	1,166.26	268.34	-	07/2021	-	0/0
98	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98	1,952.20	934.06	-	07/2021	-	0/0
99	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000729]NHAI,TAMIL NADU	03/2018	1,016.92	1,071.00	273.52	-	07/2021	-	0/0
100	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64	1,437.64	584.17	-	07/2021	-	0/0
101	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70	931.21	183.69	-	07/2021	-	0/0
102	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50	799.30	142.26	-	07/2021	-	0/0
103	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92	1,162.92	71.45	-	07/2021	-	0/0
104	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27	950.27	200.47	-	08/2021	-	3/4
105	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00	607.00	380.86	-	08/2021	-	0/1
106	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48	614.48	191.40	-	08/2021	-	0/0

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
107	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66	564.66	221.00	-	08/2021	-	0/1
108	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95	1,031.95	374.05	-	09/2021	-	0/0
109	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98	1,550.98	1,290.79	-	09/2021	-	0/0
110	FOUR LANING OF MADURAI-CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71	628.71	284.33	-	09/2021	-	0/0
111	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04	825.17	512.04	-	10/2021	-	2/4
112	SIX LANING OF ANANDPURAM - PENDURTHI ANAKAPALI SECTION OF NH-5 NEW NH-16 FROM KM.681 TO EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00	1,959.00	1,458.00	-	10/2021	-	0/0
113	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34	2,400.00	3,080.15	-	11/2021	-	0/0
114	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84	1,117.84	-	-	12/2021	-	0/0
115	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88	743.89	115.40	-	12/2021	-	0/0
116	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97	1,094.97	220.12	-	02/2022	-	0/0
117	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28	752.28	181.52	-	03/2022	-	0/1
118	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09	953.09	332.04	-	03/2022	-	0/0
	Total		58,159.54	59,929.52	30,108.17				17/53
	URBAN DEVELOPMENT								
	National Building Construcion Corporation Ltd								

Costing Rs. 150 Crore and above (December 2020)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
119	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00	2,694.00	553.56	-	03/2022	-	0/9
	Total		2,694.00	2,694.00	553.56				0/9
	Grand Total		86,191.92	1,06,802.15	47,201.78				19/64

FLASH REPORT

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27	480.33	51.11	09/2021	09/2021
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]	3/2017	475.39	475.39	88.11	04/2021	04/2021
3	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71	389.71	37.38	11/2021	10/2022
4	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,118.90	1,216.50	122.49	11/2022	10/2022
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSBI AIRPORT KOLKATA - [N04000080]	1/2016	458.00	458.00	105.12	03/2020	06/2021
6	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61	353.61	-	05/2022	05/2022
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80	611.80	-	03/2023	03/2023
8	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24	412.24	-	06/2021	06/2021
	Total		4,263.92	4,397.98	403.91		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52	555.52	5.54	03/2021	03/2021
10	MURAI DIH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88	339.88	17.76	04/2014	04/2023
11	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27	1,230.27	446.01	04/2015	03/2022
	<u>Central Coal Fields Limited</u>						
12	MAGADH EXPANSION OC RPR - [N06000015]	8/2008	706.40	706.40	638.94	07/2012	03/2025
13	AMRAPALI OC EPR (12MTY) - [N06000103]	2/2012	858.11	858.11	243.83	03/2020	03/2024
14	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52	243.52	39.79	03/2023	03/2023
	<u>Eastern Coal Fields Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
15	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	386.19	03/2022 -	03/2022
16	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	.40	03/2027 -	03/2027
17	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	.87	03/2029 -	03/2029
18	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	158.71	03/2022 -	03/2022
19	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	-	03/2025 -	03/2025
20	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	-	03/2027 -	03/2027
21	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	.43	03/2026 -	03/2026
22	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	13.98 -	513.58	97.01	03/2024 -	03/2024
	<u>Mahanadi Coal Fields Limited</u>						
23	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,971.87	03/2026 -	03/2026
24	BALRAM EXPANSION OCP - [N06000044]	12/2007	172.08 3,504.21	646.01	646.01	03/2010 03/2029	03/2029
25	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,217.77	03/2029 -	03/2029
26	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	173.89	03/2027 -	03/2027
27	GOPAL JI KANIHA OCP, MCL - [N06000035]	12/2007	457.77 8,416.19	684.32	684.32	03/2013 03/2028	03/2028
	<u>Neyveli Lignite Corporation</u>						
28	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	479.89	06/2015 03/2025	03/2025
29	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	10,724.93	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
30	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	524.01	03/2021 -	03/2021
31	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
32	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
33	BLOCK-B EXPANSION OPENCASE PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
34	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	144.51	03/2022 -	03/2022
35	SEMARIA OPENCASE PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
	<u>Singareni Colliers Company Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	169.90	03/2019 03/2022	03/2022
	<u>South-Eastern Coal Fields Limited</u>						
37	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	7.31	03/2023 -	03/2023
38	MALACHUA OPENCASE PROJECT - [N06000139]	10/2015	488.33 -	488.33	29.94	03/2023 -	03/2023
39	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
40	JHIRIA WEST OPENCASE PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
41	MAHAMAYA OPENCASE PROJECT - [N06000164]	5/2018	410.26 -	410.26	18.19	03/2026 -	03/2026
42	VIJAY WEST OPENCASE PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
43	KUSMUNDA EXTENSION (OCF SECL)(15.00 MTY) - [N06000008]	07/2013	7,12.33 -	7,61.33	5,44.61	03/2023 -	03/2023
44	DURGAPUR OPENCASE PROJECT - [N06000136]	2/2015	916.24 -	916.24	8.19	03/2023 -	03/2023
45	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	.85	03/2022 -	03/2022
46	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	54.76	03/2021 -	03/2021
47	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.21	03/2021 -	03/2021
48	MADANNAGAR OPENCASE PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
49	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	129.86	03/2022 -	03/2022
	<u>Western Coal Fields Limited</u>						
50	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	85.03	03/2023 -	03/2023
51	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	.87	03/2026 -	03/2026
52	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	98.99	03/2021 -	03/2021
53	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	204.15	03/2021 -	03/2021
54	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
55	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	36.94	03/2022 -	03/2022
56	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	260.46	03/2021 -	03/2021
57	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	35.65	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	226.05	03/2022 -	03/2022
59	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	20.99	03/2022 -	03/2022
60	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	245.47	03/2021 -	03/2021
61	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	277.08	03/2025 -	03/2025
	Total		65,047.54 -	65,221.45	23,199.15		
	<u>DEFENCE PRODUCTION</u>						
	<u>Central Public Works Department</u>						
62	RESIDENTIAL QUARTERS FOR HAL BANGLORE - [N28000103]	12/2016	246.31 -	246.31	115.20	06/2020 01/2021	06/2021
	Total		46.31 -	246.31	115.20		
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
63	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	303.87	04/2020 03/2021	03/2021
	Total		426.72 -	426.72	303.87		
	<u>FINANC</u>						
	<u>Central Public Works Department</u>						
64	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	83.71	11/2021 -	11/2021
	Total		348.77 -	348.77	83.71		
	<u>HEALTH AND FAMILY WELFARE</u>						
65	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	94.33	09/2023 -	09/2023
66	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
67	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	577.32	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	671.65		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
68	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002	8/2016	1,554.00 -	1,554.00	806.15	09/2019 12/2020	12/2020
	Total		1,554.00 -	1,554.00	806.15		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
69	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N20000147	1/2020	166.98 167.00	166.98	-	10/2023	10/2023
	Total		166.98 -	166.98	-		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
70	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
71	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
72	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008	9/2018	392.51 -	392.51	35.88	06/2022 -	06/2022
73	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142	10/2019	348.24 -	348.24	7.05	05/2022 -	05/2022
	Total		2,225.37 -	2,225.37	100.35		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
74	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	5,540.00	614.13	04/2021 12/2022	12/2022
75	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	.74	04/2021 04/2021	04/2021
	Total		6,023.00 -	6,023.00	614.87		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
76	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	16.38	02/2017 08/2022	08/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	342.23	12/2019 02/2021	02/2021
78	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	2,614.93	02/2020 02/2021	02/2021
79	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	278.71	12/2021 -	12/2021
80	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	168.73	08/2022 -	08/2022
81	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	60.14	06/2022 -	06/2022
82	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	571.32	12/2021 -	12/2021
83	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	80.20 -	580.10	90.10	01/2021 -	02/2021
84	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	79.52	03/2021 -	03/2021
85	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	276.12	03/2023 -	03/2023
86	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
	<u>Gas Authority Of India Limited</u>						
87	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,174.60	12/2020 12/2021	12/2021
88	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,048.00	1,659.30	12/2020 12/2021	12/2021
89	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	775.10	12/2020 12/2021	12/2021
90	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	84.25	07/2022 -	07/2022
91	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	183.93	04/2022 -	04/2022
92	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	128.57	10/2022 -	10/2022
93	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	93.90	10/2022 -	10/2022
94	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	397.60	05/2023 -	05/2023
95	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	2.70	11/2022 -	11/2022
96	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]	8/2018	217.92 -	217.92	72.40	04/2021 -	04/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
97	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	73.85	10/2022 -	10/2022
98	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	113.30	07/2022 -	07/2022
99	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	327.01	143.50	08/2020 05/2021	05/2021
100	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	1,998.30	12/2021 -	12/2021
101	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	68.12	07/2022 -	07/2022
102	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,470.70	12/2012 02/2022	02/2022
<u>Hindustan Petroleum Corporation Limited</u>							
103	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,28.00	26,264.00	13,324.40	07/2020 07/2022	07/2022
104	SETTING UP OF PHASE II FACILITIES FOR HPC GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	80.00 -	380.00	177.00	11/2021 -	11/2021
105	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	86.19	09/2026 -	09/2026
106	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	33.86	02/2023 -	02/2023
107	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	13.79	03/2031 -	03/2031
108	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	135.22	03/2029 -	03/2029
109	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	71.11	11/2022 -	11/2022
110	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	121.57	12/2022 -	12/2022
111	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	247.49	11/2020 06/2021	06/2021
112	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]	6/2017	161.50 -	161.50	54.07	06/2020 09/2021	09/2021
113	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	669.37	06/2022 -	06/2022
114	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - - [N16000296]	9/2017	2,677.00 -	3,072.00	1,825.04	06/2021 08/2022	08/2022
<u>Indian Oil Corporation Limited</u>							
115	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	494.64	07/2018 02/2021	02/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
116	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	1.80	09/2022 -	09/2022
117	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	9.50	06/2021 07/2022	07/2022
118	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	1,432.60	08/2021 -	08/2021
119	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	2.38	09/2021 -	09/2021
120	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	234.25	02/2020 10/2021	10/2021
121	DEVLOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAJUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	20.38	10/2020 02/2022	02/2022
122	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	55.40 -	25.40	10.36	01/2020 11/2021	11/2021
123	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	64.15	02/2020 08/2021	08/2021
124	LPG BP PROJECT JODHPUR - [N16000318]	3/2018	229.80 -	229.80	79.45	- 05/2022	05/2022
125	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY [N16000308]	8/2017	315.00 -	315.00	180.63	12/2021 -	12/2021
126	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	293.00	138.42	06/2020 09/2021	09/2021
127	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	248.45	04/2021 03/2021	03/2021
128	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	80.39	04/2020 10/2021	10/2021
129	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	172.31	02/2020 02/2022	02/2022
130	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	141.32	01/2021 03/2022	03/2022
131	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP [N16000350]	10/2018	316.20 -	316.20	53.36	10/2021 -	10/2021
132	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	541.64	10/2021 -	10/2021
133	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	278.28	03/2021 12/2021	12/2021
134	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	467.19	02/2020 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
135	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,259.24	10/2021 -	10/2021
136	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	114.02	01/2021 06/2021	06/2021
137	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	48.20	- 05/2023	05/2023
138	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	53.20	01/2023 -	01/2023
139	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	632.61	04/2023 -	04/2023
140	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	2.06	07/2021 -	07/2021
141	ACRYLICS OF ETHANOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,031.00 -	5,251.00	10.16	07/2023 -	05/2023
142	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	67.00 -	167.00	8.10	01/2022 -	07/2022
143	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	52.81	12/2021 -	12/2021
144	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	129.59	10/2021 -	10/2021
145	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	425.50	12/2022 -	12/2022
146	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	78.12	02/2020 06/2021	06/2021
147	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00 -	921.00	2.86	09/2023 -	09/2023
148	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	-	12/2022 -	12/2022
149	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	-	08/2022 -	08/2022
150	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	72.66	01/2024 -	01/2024
151	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	.22	07/2022 -	07/2022
152	LPG BP PROJECT KORDHA - [N16000283]	12/2016	161.59 -	161.59	45.32	12/2019 03/2022	03/2022
153	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	502.00	399.01	08/2019 06/2021	06/2021
154	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
156	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
157	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	-	06/2023 -	06/2023
	<u>Numaligarh Refinery Limited</u>						
158	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINERY [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024
159	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
160	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,390.69 -	3,371.90	2,571.08	05/2018 05/2021	05/2021
161	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	611.60	03/2023 03/2022	03/2022
162	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,096.58	03/2022 -	03/2022
163	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	1,941.83	05/2021 -	05/2021
164	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	922.04	03/2022 05/2023	05/2023
165	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	1,303.59	05/2021 -	05/2021
166	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) [N16000297]	2/2017	4,006.83 -	3,596.00	3,442.73	05/2021 05/2021	05/2021
167	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	621.21	03/2026 -	03/2026
168	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	303.75	170.85	05/2020 05/2021	05/2021
169	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	25,090.00	9,799.00	06/2020 08/2021	08/2021
170	Field Development Plan of Madanam NGLP-IV Block CY-ONN-2002 - [N16000241]	11/2015	650.82 -	624.35	445.60	03/2019 05/2021	05/2021
171	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	584.33	12/2020 05/2021	05/2021
	Total		2,29,873.00 -	2,30,722.72	64,563.42		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
172	PARBATHI HEP (4X200 MW) (NHPC) II - [N180100210]	9/2002	3,919.59 -	9,897.59	8,705.10	09/2009 03/2022	03/2022
173	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	9/2003	6,285.33 -	19,992.43	12,855.18	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
174	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	10,016.10	7,888.03	07/2019 03/2021	03/2021
175	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,389.42	11,269.68	06/2019 10/2022	10/2022
176	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	7,998.74	11/2020 03/2022	03/2022
177	BARH STPP(3X660MW) NTPC - [N180100242]	2/2005	8,692.97 -	21,312.11	18,168.42	10/2011 04/2022	04/2022
	<u>North East Electric Power Corporation</u>						
178	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,96.90 -	7,27.34	3,151.00	11/2009 01/2021	01/2021
	<u>Power Grid Corporation of India Limited</u>						
179	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,864.61	08/2013 03/2022	03/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						
180	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	1,221.50	01/2024 -	01/2024
181	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	282.43	01/2026 -	01/2026
182	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	479.06	12/2021 -	12/2021
	Total		79,577.50 -	1,22,751.05	89,883.75		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
183	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,341.89	03/2023 -	03/2023
184	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
185	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
186	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
187	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	429.22	03/2023 -	03/2023
	<u>Container Corporation Of India</u>						
188	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	268.50	03/2019 12/2020	12/2020
	<u>East Coast Railway</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
189	TALCHER-BIMALAGARH(NL)(ECOR) - [N220100328	4/2005	810.78 -	1,928.07	830.77	06/2021 03/2025	03/2025
190	KHURDA ROAD-BOLANGIR(NL)ECOR - [N220100284	4/1994	2,923.13 -	3,791.66	1,402.12	03/2009 03/2026	03/2026
191	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	891.78	03/2020 03/2023	03/2023
192	BHADRAK - NERGUNDI 3RD LINE - [N22000316	3/2013	843.04 -	843.04	193.29	10/2020 03/2024	03/2024
193	SAMBALPUR-TALCHER DOUBLING - [N22000315	3/2011	1,111.99 -	1,539.28	1,090.14	02/2019 12/2021	12/2021
194	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	590.18	12/2018 03/2024	03/2024
195	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	4/2015	701.61 -	810.02	168.21	11/2018 03/2024	03/2024
196	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379	4/2015	2,611.74 -	2,361.74	257.06	01/2022 01/2026	03/2026
197	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	2,499.71	590.79	03/2022 03/2024	03/2024
198	JAGDALPUR-KORAPUT DOUBLING - [N22000376	4/2015	1,547.38 -	1,547.38	593.77	03/2022 03/2023	03/2023
	<u>Indian Railway Construction Company Limited</u>						
199	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418	4/2016	5,200.00 -	962.00	54.75	03/2020 03/2024	03/2024
	<u>North Central Railway</u>						
200	JHANSI BINA DOUBLING - [N22000496	9/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021
	<u>North East Frontier Railway</u>						
201	AGARTALA-AKHAURA NL - [N22000195	4/2012	569.63 -	742.00	200.28	03/2020 03/2022	03/2022
202	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	4/2010	906.46 -	4,083.02	263.67	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
203	HATHUA-BHATNI (N L) (NER) - [N220100319	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
204	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	3/2007	243.78 -	895.00	112.02	12/2021 -	12/2021
205	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42 -	1,295.42	778.29	03/2022 -	03/2022
	<u>Northern Railway</u>						
206	CHANDIGARH-BADDI - [N22000467	4/2007	328.14 -	1,540.13	241.62	03/2023 03/2025	03/2025
	<u>National High Speed Rail Corporation Limited</u>						
207	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463	12/2015	1,08,000.00 -	1,08,000.00	9,576.52	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Rail India Technical And Economic Service</u>						
208	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394	3/2015	636.38 -	636.38	507.33	03/2021 -	03/2021
209	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498	2/2016	393.98 -	393.98	350.81	03/2020 06/2021	06/2021
	<u>Rail Vikas Nigam Ltd.</u>						
210	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,500.00	1,376.94	12/2021 -	12/2021
211	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
212	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501	6/2016	3,677.76 -	3,677.76	1,436.33	12/2023 -	12/2023
213	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	73.94 -	350.00	705.9	12/2024 -	12/2024
214	DHASA-JETALGAR (GC) - [N22000141	4/2012	44.38 -	872.75	800.0	03/2021 -	03/2021
	<u>South East Central Railway</u>						
215	GONDIA-JABALPUR(GC),(SECR) - [220100186	2/1997	511.86 -	2,005.25	1,777.22	04/2020 04/2021	04/2021
216	ANUPPUR-KATNI - [N22000485	4/2015	1,370.00 -	1,370.94	470.49	12/2021 12/2023	12/2023
217	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	4/2015	1,973.00 -	2,135.34	351.35	03/2021 12/2023	12/2023
218	WADSA-GADHICHIROLI NEW LINE (52.36 KM) - [N22000480	6/2018	229.00 -	1,096.00	39.79	12/2021 12/2024	12/2024
219	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	4/2010	585.93 -	1,268.32	941.56	02/2019 12/2021	12/2021
220	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,908.51 -	3,524.81	952.24	03/2023 12/2023	12/2023
	<u>Southern Railway</u>						
221	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	4/2008	523.52 -	2,300.00	2.28	- 03/2024	03/2024
222	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	4/2007	931.98 -	961.09	873.72	- 02/2021	02/2021
	<u>Western Railway</u>						
223	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	4/2008	3,503.69 -	5,912.40	2,118.69	03/2022 03/2024	03/2024
224	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,959.74	1,760.97	03/2020 12/2023	12/2023
225	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494	4/2017	691.84 -	1,017.91	453.03	03/2020 12/2020	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
226	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	232.01	06/2020 03/2023	03/2023
227	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	890.76	738.65	03/2019 10/2021	10/2021
228	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	411.62	125.76	03/2012 03/2023	03/2023
229	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	578.34	03/2021 12/2022	12/2022
230	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	1,378.11	540.09	03/2019 03/2023	03/2023
231	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,389.05	1,096.41	03/2021 03/2022	03/2022
232	MIYAGAM-KATSON DATHOI-SAMLIYA (GC) - [N22000142]	4/2011	844.15 -	844.15	172.03	01/2024	03/2024
233	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000135]	4/2007	1,40.04 -	1,640.04	860.74	01/2022 01/2025	03/2025
234	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	883.18	03/2022 03/2023	03/2023
	Total		1,85,567.79 -	2,06,244.27	43,432.00		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
235	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. [N24000312]	4/2013	151.59 -	151.59	282.36	08/2013 12/2020	12/2020
236	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- [N24001180]	3/2019	237.51 -	237.51	38.85	12/2022 -	12/2022
237	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]	10/2016	172.63 -	172.63	123.44	12/2020 -	12/2020
238	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]	10/2016	167.62 -	167.62	98.42	12/2020 -	12/2020
239	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	57.16	09/2021 -	09/2021
240	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	305.76	03/2018 06/2021	06/2021
241	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	137.87	06/2021 -	06/2021
242	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	531.46	12/2019 12/2020	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
243	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021
244	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966	1/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021
245	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229	12/2014	379.16 -	379.16	235.01	11/2017 03/2021	03/2021
246	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228	11/2017	188.80 -	188.80	65.21	05/2019 03/2021	03/2021
247	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226	12/2014	496.02 -	496.02	226.59	03/2015 03/2021	03/2021
248	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO 466.974 KUNKURI TO CG. BORDER SECTION - [N24001224	3/2017	23.79 -	23.79	252.1	07/2018 07/2021	03/2021
249	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222	3/2016	452.94 -	435.61	73.30	07/2016 03/2021	03/2021
250	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	1/2016	624.98 -	731.50	341.61	10/2016 12/2020	12/2020
251	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	1/2016	476.20 544.00	544.00	397.32	09/2016 03/2021	03/2021
252	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218	11/2015	335.32 -	335.32	245.69	06/2017 02/2021	02/2021
253	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	1/2016	497.14 -	527.66	232.36	08/2016 03/2021	03/2021
254	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216	12/2016	196.00 -	196.00	-	09/2021 -	09/2021
255	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198	1/2019	264.50 -	264.50	55.12	03/2021 -	03/2021
256	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	84.67	06/2021 -	06/2021
257	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	322.24	292.10	09/2014 12/2020	12/2020
258	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964	8/2016	350.61 -	350.61	323.06	01/2017 12/2020	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
259	REHABILITATION AND UPGADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	99.57	08/2018 03/2021	03/2021
260	REHABILITATION AND UPGADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	3/2016	877.79 -	877.79	635.33	06/2019 03/2021	03/2021
261	REHABILITATION AND UPGADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898	1/2016	809.16 -	809.16	488.46	07/2018 05/2021	05/2021
262	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896	1/2017	373.82 -	373.82	173.84	09/2019 06/2021	06/2021
263	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	03/2021
264	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892	11/2017	249.05 -	249.05	191.67	07/2018 01/2021	03/2021
265	UPGRADATION OF POISA-BHINDAR ROAD TO 2L + PS - [N24000890	3/2018	17.22 -	22.88	16.76	01/2018 01/2021	03/2021
266	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243	3/2020	166.94 -	166.94	-	12/2020 -	12/2020
267	NAGOUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240	3/2020	370.36 -	370.36	-	08/2022 -	08/2022
268	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230	11/2018	281.45 -	281.45	2.36	12/2020 -	12/2020
269	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888	3/2018	214.69 -	214.69	49.85	03/2018 09/2021	09/2021
270	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886	1/2017	205.05 -	205.05	113.56	03/2017 06/2021	06/2021
271	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884	3/2018	191.21 -	191.21	117.80	11/2019 01/2021	01/2021
272	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881	11/2017	184.62 -	184.62	105.89	02/2018 02/2021	02/2021
273	REHABILITATION AND UPGADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878	11/2017	235.91 -	235.91	167.93	02/2018 02/2021	02/2021
274	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875	2/2018	169.63 -	169.63	29.65	03/2018 04/2021	04/2021
275	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	3/2018	166.21 -	173.41	139.19	08/2018 03/2021	03/2021
276	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870	3/2018	162.56 -	162.56	124.81	03/2018 02/2021	02/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
277	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 [N24000513]	3/2015	511.83 -	511.83	354.95	08/2017 06/2021	06/2021
278	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 [N24000478]	12/2015	957.54 -	957.54	713.84	02/2020 04/2021	04/2021
279	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) [N24000415]	8/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021
280	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. [N24000313]	4/2013	166.27 -	166.27	243.59	08/2013 12/2020	12/2020
281	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM [N24000314]	1/2013	182.28 -	269.14	274.06	02/2013 12/2020	12/2020
National Highways Authority Of India							
282	SIX LANEING OF CHAND KHOL-JALPAIGURI BHUBANESWAR [N24000205]	12/2011	1,47.00 -	1,04.00	1,87.43	07/2014 07/2021	03/2021
283	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	469.31	459.07	01/2014 12/2020	12/2020
284	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	572.57	05/2018 06/2021	06/2021
285	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	184.90	03/2019 12/2021	12/2021
286	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	614.25	05/2018 06/2021	06/2021
287	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 [N24000360]	4/2014	351.34 -	417.68	433.68	01/2016 12/2020	12/2020
	Total		19,232.07 -	20,418.79	13,513.64		
RURAL DEVELOPMENT							
Central Public Works Department							
288	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021
	Total		361.60 -	361.60	12.44		
SHIPPING AND PORTS							
Inland Waterways Authority Of India							
289	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	5,369.18 -	4,633.81	1,787.23	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		5,369.18	4,633.81	1,787.23		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
290	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00	21,940.00	17,436.86	05/2015 07/2021	07/2021
	<u>Rastriya Ispat Nigam Limited</u>						
291	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85	1,682.85	1,511.30	09/2018 02/2021	02/2021
292	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00	2,558.00	1,762.09	12/2017 12/2020	12/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
293	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,34.01	1,34.01	511.70	11/2017 11/2021	12/2021
294	REBUILDING OF COKE OVEN BATTERY-2 ALONG WITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	77.18	377.18	...	01/2023	05/2023
295	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87	262.87	170.16	06/2019 05/2021	05/2021
	Total		21,739.91	27,854.91	21,392.58		
	<u>TELECOMMUNICATIONS</u>						
	<u>Central Public Works Department</u>						
296	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]	10/2016	248.20	248.20	80.10	03/2018 12/2020	12/2020
	Total		248.20	248.20	80.10		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
297	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17	5,384.17	30.02	03/2024	03/2024
298	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32	12,020.32	14.89	03/2024	03/2024
	<u>Central Public Works Department</u>						
299	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33	197.33	94.18	04/2019 06/2021	06/2021
300	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]	7/2012	884.30	884.30	812.00	12/2015 12/2020	12/2020
301	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00	1,128.00	22.00	03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
302	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110	10/2016	422.00 -	422.00	28.26	03/2021 07/2021	07/2021
303	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	157.67	05/2020 02/2021	02/2021
	<u>Chennai Metro Rail Ltd</u>						
304	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097	6/2016	3,770.00 -	3,770.00	2,750.00	03/2018 12/2020	12/2020
	<u>Delhi Metro Rail Corporation</u>						
305	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS [N28000135	7/2019	24,948.65 -	24,948.65	965.60	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
306	KANPUR METRO RAIL PROJECT - [N28000144	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
307	AGRA METRO RAIL PROJECT - [N28000145	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
308	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	11,420.00	5,234.40	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
309	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	114.13	02/2023 -	02/2023
310	INDORE METRO RAIL - [N28000125	11/2018	7,500.80 -	7,500.80	112.78	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
311	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134	3/2019	30,274.00 -	30,274.00	2,467.77	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
312	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	2/2019	13,365.77 -	13,365.77	271.17	06/2024 -	06/2024
	Total		1,37,951.40 -	1,37,951.40	13,074.87		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
313	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026	3/2018	230.06 -	230.06	37.09	07/2021 -	07/2021
314	LAND AND STP AT CHAPRA - [N30000028	11/2018	236.15 -	236.15	12.06	12/2020 -	12/2020
315	SEWERAGE SCHEME AT PAHARI ZONE IV A S PATNA - [N30000041	5/2017	184.86 -	184.86	131.43	05/2021 -	05/2021
316	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050	8/2017	578.89 -	578.89	.29	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
317	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	.42	06/2022 -	06/2022
318	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	111.10	05/2021 -	05/2021
319	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	79.54	04/2021 -	04/2021
320	SAIDPUR SEWER NETWORK PATNA - [N30000039]	4/2015	268.63 -	268.63	254.50	01/2021 -	01/2021
321	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
	<u>Delhi Jal Board</u>						
322	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	129.56	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
323	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
324	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
325	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
326	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
327	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
328	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
329	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
330	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]	5/2018	160.00 -	160.00	-	02/2022 -	02/2022
331	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
332	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	5/2018	198.43 -	198.43	-	02/2022 -	02/2022
	<u>Uttar Pradesh Jal Nigam</u>						
333	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	32.47	09/2021 -	09/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
334	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007	3/2018	904.00 -	904.00	38.38	09/2021 -	09/2021
335	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022	1/2019	206.05 -	206.05	5.16	10/2021 -	10/2021
336	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	2/2019	681.78 -	681.78	-	06/2022 -	06/2022
337	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023	2/2019	317.19 -	317.19	-	08/2021 -	08/2021
338	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH [N30000021	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
339	FARRUKHABAD LAND AND STP WORKS HAM - [N30000008	10/2017	213.62 -	213.62	-	03/2022 -	03/2022
340	STP AT PANKAJA KANPUR AND INTERCEPTION WITH EXISTING STPS [N30000010	3/2018	67.23 -	96.23	1.64	09/2021 -	09/2021
341	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH [N30000013	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
	Total		10,736.58 -	10,738.82	846.64		
	Grand Total		7,75,291.84	8,47,239.15	2,74,885.53		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
1	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007	9/2019	588.72 -	588.72	14.80	09/2022 04/2023	01/2023
	Total		588.72 -	588.72	14.80		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
2	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N100 0014	9/2017	166.62 163.17	163.17	135.00	06/2019 06/2021	12/2020
	Total		166.62	63.17	135.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
3	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273	3/2017	2,433.00 -	2,433.00	1,925.10	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
4	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315	6/2017	249.26 -	249.26	110.52	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
5	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,696.00	1,780.96	09/2022 -	03/2022
	Total		6,394.26 -	6,378.26	3,816.58		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
6	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47	3,627.47	1,199.46	03/2024 -	03/2023
	<u>East Central Railways</u>						
7	GARHWA ROAD-RAMNA - [N22000465	3/2015	348.23 -	348.23	299.31	03/2021 -	12/2020
	<u>North Central Railway</u>						
8	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495	3/2018	4,329.53 -	4,329.53	33.37	03/2023 03/2026	03/2023
	<u>North East Frontier Railway</u>						

Costing Rs. 150 Crore and above

(December 2020)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
9	SEVOK RANGPO, NEFR - [N22000102	4/2008	1,339.48 4,084.69	8,600.00	619.18	12/2015 12/2023	03/2023
10	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	4/2016	602.27	760.00	730.62	12/2021	03/2021
	<u>North Western Railway</u>						
11	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466	8/2018	808.85	808.85	153.38	08/2022	06/2022
	<u>Rail Vikas Nigam Ltd.</u>						
12	BHANUPALI-BILASPUK BERI NL - [N22000273	4/2008	2,966.99	6,753.42	784.37	12/2026	12/2025
13	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00	3,000.00	2,121.59	03/2023	12/2022
14	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78	723.78	0.19	12/2025	03/2025
	<u>South Central Railway</u>						
15	KAZIPET-VIJAYAWADA ROAD LINE WITH ELECTRIFICATION - [N22000261	4/2012	1,339.48	1,952.00	187.47	03/2023 03/2025	03/2024
16	BHADRACHALAM ROAD-SATTOUPALLI - [N22000287	4/2010	704.51	927.94	517.35	03/2020 03/2022	06/2021
17	GUNTUR-GUNTAKAL - [N22000368	4/2016	3,631.00	3,887.48	984.35	03/2022 03/2025	03/2024
	<u>Southern Railway</u>						
18	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26	332.00	239.19	04/2014 01/2021	12/2020
	Total		23,253.12	36,051.38	8,169.83		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
19	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	3/2018	289.67	289.67	173.13	08/2018 06/2021	02/2021
20	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	3/2018	504.19	504.19	403.01	11/2018 04/2021	01/2021
21	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	3/2016	995.09	995.09	473.71	05/2016 08/2021	04/2021
22	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214/NH21 - [N24000965	1/2016	386.09	386.09	199.35	05/2016 01/2021	12/2020
	<u>National Highways Authority Of India</u>						
23	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	3/2018	1,532.62	2,499.00	1,497.61	03/2021 10/2021	04/2021

Costing Rs. 150 Crore and above

(December 2020)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
24	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835	3/2018	1,484.30 -	1,484.30	356.66	- 06/2021	12/2020
	Total		5,191.96 -	6,158.34	3,103.47		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
25	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150	3/2019	1,828.00	1,828.00	-	09/2025 -	05/2024
	Total		1,828.00 -	1,828.00	.00		
	Grand Total		37,422.68	51,167.87	15,239.68		

FLASH REPORT

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
2	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TALABIR II AND III OCP - [N06000139]NLC, ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
5	HADOLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
9	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	12/2012 -	-
	<u>Western Coal Fields Limited</u>				
10	DINESH OCP - [N06000118]WCL, MAHARASHTRA	11/2014	611.16 -	03/2020 -	03/2020
11	SINGHORI OC MINE - [N06000130]WCL, MAHARASHTRA	06/2015	205.49 -	03/2020 -	03/2020
12	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL, MAHARASHTRA	11/2015	498.42 -	03/2020 -	03/2020
13	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020
14	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
15	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL, MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
16	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
	Total		14,596.14 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
17	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		534.00 -		
	<u>STEEL</u>				
	<u>Rastriya Ispat Nigam Limited</u>				
18	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 336.00	08/2018 11/2020	11/2020
	Total		320.66 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
19	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	10/2018 02/2020	07/2020
	<u>Gas Authority Of India Limited</u>				
20	GAIL GAS LIFT BENGALURU CSD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	709.00 -	02/2020 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
21	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE	09/2016	1,879.00 -	06/2020 -	10/2020
22	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
23	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	10/2019 11/2020	11/2020
24	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
25	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT	08/2017	1,342.00 -	08/2020 -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Oil India Limited</u>				
27	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	-
	Total		11,868.64 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
28	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
29	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
30	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-
31	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
32	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-
33	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
34	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
35	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	-
36	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	-
37	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	12/2018 -	-
38	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC WEST BENGAL	12/2016	529.68 -	11/2018 -	-
	Power Grid Corporation of India Limited				
39	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	400.46 482.64	01/2019 04/2020	04/2020
40	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 04/2020	05/2020
41	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 04/2020	07/2020
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 06/2020	09/2020
43	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 06/2020	09/2020
44	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
45	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
46	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	-
47	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
48	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-
49	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-
50	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
	Total		58,584.75 -		

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
51	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
52	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
53	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
54	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
55	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
	Total		1,387.70 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
56	3RD LINE BETWEEN BILWAJAL-JALPAIGURI - [N2000247]CP,MAHARASHTRA	04/2011	84.06 19.12	03/2019 03/2020	03/2020
	<u>Container Corporation Of India</u>				
57	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020
58	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
59	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
60	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
61	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
62	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
63	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	01/2020
64	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	09/2020
65	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
66	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-
67	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
68	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
69	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
70	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
71	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
72	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
73	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
74	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
75	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-
76	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
	<u>Eastern Railways</u>				
77	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				
78	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAT VIA BIMANBAUNDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,507.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
79	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
80	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
81	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
82	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
83	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
	<u>North East Frontier Railway</u>				
84	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	-
85	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
86	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-
87	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-
88	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
89	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
	<u>North Eastern Railway</u>				

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
90	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
91	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
92	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
93	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
94	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
<u>North Western Railway</u>					
95	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
96	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
97	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-
98	AJMER-KOTA (NASIRABAD-JALNDRI) - [N22000140]NWR,RAJASTHAN	04/2013	821.00 -	- -	-
99	PUSHKAR-MERUT - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
100	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
<u>Northern Railway</u>					
101	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
<u>Rail India Technical And Economic Service</u>					
102	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
<u>Rail Vikas Nigam Ltd.</u>					
103	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-
104	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
<u>Railway Electrification</u>					
105	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
<u>South Central Railway</u>					
106	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
107	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
108	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
109	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
110	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
<u>South East Central Railway</u>					

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
111	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- 08/2020	08/2020
112	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 10/2020	10/2020
	<u>South Eastern Railway</u>				
113	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
114	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
115	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>South Western Railway</u>				
116	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	-
	<u>Southern Railway</u>				
117	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
118	TIRUPPATTUR - GINGEE (TIRUVANANTHAPURAM) - [220000434]SR,TAMIL NADU	09/2006	227.40 -	- -	-
119	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
120	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
121	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-
122	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
123	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-
124	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
125	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.00	- -	-
126	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
127	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
128	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
129	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
130	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
131	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
132	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
133	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		75,253.19 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
134	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
135	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	08/2020
136	REHABILITATION AND UPGRADATION OF NH214 (NEW NH42) FROM KM 24.930 TO 69.775 (MACHILIPATNAM) - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	532.68 -	02/2017 06/2021	02/2019
137	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
138	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 07/2021	05/2019
139	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
140	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 05/2021	08/2019
141	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 -	11/2017 04/2021	11/2019
142	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020
143	REHABILITATION AND UPGRADATION OF NH-31 FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	04/2020
144	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 -	08/2018 05/2021	08/2020
145	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 06/2021	08/2020
146	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 07/2021	09/2020
147	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
148	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 10/2020	10/2020
149	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020
150	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
151	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	11/2020
152	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	11/2020
153	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	11/2020
154	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM KM 211.325 TO KM 1260. - SENAPATI FROM KM 211.325 TO KM 1260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
155	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 100 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	211.35 -	11/2020 05/2021	11/2020
156	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	11/2020
157	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	11/2020
158	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	11/2020
159	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
160	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
161	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
162	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
163	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
164	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
165	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
166	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
167	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
168	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
169	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
170	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
171	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
172	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
173	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 162.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATTISGARH	11/2015	485.44 -	12/2015 -	-
174	WIDENING AND STRENGTHENING OF NH 65 TO FOUR LANES WITH PAVED SHOULDER FROM EXISTING KM 267+50.0 TO K [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
175	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
176	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
177	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
178	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
179	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 03/2021	-
180	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
181	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
182	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
183	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
184	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
185	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
186	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
187	CONSTRUCTION OF PAVED SHOULDERS INCULGING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
188	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
189	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
190	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
191	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
192	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM.106.00 TO 106.00 OF NH-218 BIJAP - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
193	RUDHAULI-BOMBARA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	44.89 -	03/2017 -	-
194	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
195	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
196	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
197	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
198	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
199	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
200	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
201	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-
202	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
203	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
205	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
206	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
207	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
208	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM	11/2014	218.31 -	02/2018 -	-
209	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
210	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
211	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-65) ON P. NJIM-MAI GALO E - [N24000444]MoRTH,GOA	10/2015	236.40 -	- -	-
212	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 18.000 TO KM 200.400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
213	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
214	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
215	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
216	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUARI - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
217	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
218	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
219	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
220	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
221	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
222	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
223	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
224	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH, BIHAR	11/2013	683.83 -	07/2016 -	-
225	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH, BIHAR	02/2014	665.50 -	07/2016 -	-
226	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH, BIHAR	02/2016	178.85 -	05/2016 -	-
227	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH, BIHAR	02/2016	369.77 -	06/2016 -	-
228	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH, BIHAR	02/2016	553.30 -	05/2016 -	-
229	FOUR LANNING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH, BIHAR	01/2014	1,408.85 -	10/2016 -	-
230	STRENGTHENING AND WIDENING WORK OF EXISTING 4-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH, BIHAR	03/2015	201.80 -	07/2016 -	-
231	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH, BIHAR	08/2015	288.24 -	11/2015 -	-
232	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH, MAHARASHTRA	03/2016	1,142.62 -	- -	-
233	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH, MAHARASHTRA	03/2016	1,101.58 -	- -	-
234	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH, BIHAR	08/2016	1,742.01 -	12/2016 -	-
235	WIDENING AND STRENGTHENING OF EXISTING SINGLE LANE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH, ODISHA	03/2014	191.50 192.00	05/2016 -	-
236	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MoRTH, ODISHA	01/2015	326.63 327.00	04/2018 -	-
237	WIDENING AND STRENGTHENING OF EXISTING SINGLE LANE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH, ODISHA	02/2015	239.91 240.00	10/2017 -	-
238	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH, ODISHA	07/2014	342.05 342.00	01/2017 -	-
239	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH, ODISHA	08/2013	171.96 172.00	06/2016 -	-
240	WIDENING OF EXISTING SINGLE LANE TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH, ODISHA	06/2016	157.30 157.00	06/2018 -	-
241	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH, UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
242	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH, UTTARAKHAND	12/2017	200.34 -	12/2019 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
243	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
244	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
245	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
246	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
247	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
248	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-
249	REHABILITATION AND UPGRADATION OF 2 LANE / 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.90 TO KM. 172.90 [N24000780]MoRTH,UTTARAKHAND	02/2018	29.68 -	- -	-
250	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
251	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
252	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
253	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
254	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
255	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-
256	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-
257	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
258	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
259	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
260	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
261	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
262	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
263	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
264	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN - [N24000920]MoRTH,GUJARAT	03/2016	223.67 -	02/2017 -	-
265	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]MoRTH,GUJARAT	03/2016	208.34 -	02/2016 -	-
266	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
267	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
268	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
269	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND REV. DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	03/2017	262.42 -	03/2018 -	-
270	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
271	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH 0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
272	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-
273	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-
274	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	-
275	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
276	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
277	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
278	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-
279	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
280	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
281	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH, TELANGANA	01/2017	244.54 -	05/2019 -	-
282	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH, TELANGANA	01/2017	196.52 -	10/2019 -	-
283	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH, TELANGANA	01/2017	283.00 -	12/2019 -	-
284	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH, TELANGANA	01/2017	359.27 -	05/2019 -	-
285	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH, TELANGANA	01/2017	300.00 -	05/2019 -	-
286	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH, TELANGANA	01/2018	283.15 -	05/2020 -	-
287	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.155/0 TO 05/4 - [N24000988]MoRTH, TELANGANA	01/2018	231.03 -	12/2019 -	-
288	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA	02/2018	206.13 -	06/2020 -	-
289	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA	02/2018	294.13 -	11/2019 -	-
290	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA	02/2018	220.28 -	11/2019 -	-
291	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA	02/2018	426.52 -	04/2020 -	-
292	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA	03/2018	322.81 -	09/2020 -	-
293	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA	03/2018	626.76 -	07/2020 -	-
294	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA	01/2017	605.08 -	10/2019 -	-
295	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA	03/2018	192.67 -	07/2019 -	-
296	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA	01/2019	193.19 -	- -	-
297	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH, BIHAR	11/2016	230.34 232.90	10/2019 -	-
298	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH, BIHAR	03/2018	153.24 -	- -	-

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
299	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
300	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
301	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
302	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
303	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
304	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
305	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
306	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
307	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 371.00	05/2019 -	-
308	MEHAKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	22.48 32.00	05/2019 -	-
309	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
310	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
311	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
312	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
313	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
314	DAHEGAON TO KUIHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
315	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
316	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
317	AMDHI TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
318	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
319	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
320	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
321	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
322	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
323	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
324	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
325	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
326	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
327	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
328	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
329	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
330	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
331	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
332	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
333	KAIJ TO KUNJALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	54.78 -	07/2019 -	-
334	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
335	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
336	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
337	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
338	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
339	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
340	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
341	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
342	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
343	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
344	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
345	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
346	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
347	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
348	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
349	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
350	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
351	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
352	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
353	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
354	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
355	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
356	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
357	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
358	DHAD BHOIRARDAN TO PARBHANI - [N24001062]MoRTH,MAHARASHTRA	03/2018	136.21 136.00	12/2019 -	-
359	WADIGODRI TO DHANGRI PIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
360	DHANGRI PIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
361	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
362	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
363	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
364	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
365	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
366	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
367	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
368	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
369	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
370	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
371	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
372	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
373	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
374	KUNDRA TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
375	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
376	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
377	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
378	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
379	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
380	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
381	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
382	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 417.00	06/2019 -	-
383	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
384	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
385	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
386	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
387	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
388	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
389	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
390	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
391	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
392	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
393	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
394	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
395	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
396	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
397	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
398	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
399	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
400	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
401	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
402	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
403	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
404	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
405	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
406	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
407	KOIHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 281.00	04/2019 -	-
408	NASRATPUR TO BAFANGGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	206.54 407.00	09/2019 -	-
409	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
410	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
411	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
412	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
413	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
414	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
415	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-
416	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
417	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
418	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
419	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
420	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
421	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
422	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
423	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
424	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
425	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
426	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
427	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
428	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
429	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
430	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
431	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
432	REHABILITATION AND UPGRADATION OF NH-76 FROM KM 17.000 TO KM 1215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-
433	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-
434	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	-
435	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
436	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-
437	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
438	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
439	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-
440	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
441	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
442	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
443	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
444	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
445	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
446	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
447	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
448	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 386.40	10/2018 -	-
449	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 386.40	10/2018 -	-
450	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 79.5 TO 111.47 OF NH-150 UNDER EPC MODE IN THE STATE OF KARN - [N24001163]MoRTH,KARNATAKA	08/2016	321.01 -	02/2017 -	-
451	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
452	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
453	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
454	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
455	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
456	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
457	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
458	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	-
459	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-
460	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
461	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH, BIHAR	02/2019	2,926.42 -	- -	-
462	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH, UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
463	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH, UTTAR PRADESH	03/2018	306.59 -	- -	-
464	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH, UTTAR PRADESH	11/2018	281.45 -	- -	-
465	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH, CHANDIGARH	03/2010	179.89 271.00	03/2013 -	-
466	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH, CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
467	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0 - [N24001237]MoRTH, TAMIL NADU	01/2016	162.72 -	02/2016 -	-
468	CONSTRUCTION OF FLYOVER FROM KM 604/25 TO 601.060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]MoRTH, TAMIL NADU	05/2016	300.70 -	01/2017 -	-
469	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH, TAMIL NADU	03/2018	240.38 -	06/2019 -	-
470	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH, ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
471	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL, ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
472	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL, ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
473	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	08/2016 -	06/2020
474	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00 -	09/2018 -	08/2020
475	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL, ASSAM	06/2016	829.00 -	01/2019 -	-
476	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM	03/2015	168.39 -	11/2018 -	-
477	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM	10/2014	588.95 -	11/2018 -	-
478	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL, ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
479	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
480	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
481	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
482	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
483	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
484	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
485	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
486	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BC JIBEL JUNCTION NEAR LAE ETAKA KM. 51.1 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
487	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	113.65 -	11/2016 -	-
488	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
489	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
490	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-
491	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
492	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
493	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
494	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	-
495	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	-
496	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
497	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
498	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
499	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
500	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
501	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
502	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
503	2 LANE WITH HARD SHOULDER, REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
504	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
505	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.00 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	39.00 -	10/2018 -	-
506	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
507	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	09/2018 -	-
508	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
509	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
510	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
511	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWAY TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
512	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
513	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
514	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
515	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
516	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
517	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
518	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	-
519	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	-
520	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	-
521	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	-
522	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	-
523	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	511.53 -	09/2019 -	-
524	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 10/2020	-
525	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	-
526	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
527	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
528	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
529	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
530	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
531	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
532	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
533	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
534	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
535	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
536	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-
537	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
538	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
539	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
540	OUR LANNING OF DOABARI TO JAMUCURI SECTION FROM KM 17.200 OF NH 37A TO KM 182.00 OF NH 52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
	National Highway Authority, Orissa				
541	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	05/2018
542	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
543	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
544	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
545	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
546	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
547	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
548	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
549	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019
550	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020
551	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
552	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
553	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
554	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
555	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020
556	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	08/2020
557	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	08/2020
558	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
559	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020
560	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
561	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 2,754.00	01/2018 12/2018	09/2020
562	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIVAJI BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 2,113.74	- -	09/2020
563	UPGRADATION TO 2 LANE WITH FIVE FOOTWIDER/4 LANE OF GAGARIA - LAORI KILAN - SEIWA - BAKIASAR SECTION - [N24000794]NHAI,RAJASTHAN	03/2018	1,103.88 -	- -	09/2020
564	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
565	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
566	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020
567	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 08/2020	11/2020
568	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	11/2020
569	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2020
570	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	11/2020
571	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
572	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
573	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020
574	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020
575	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	11/2020
576	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
577	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
578	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
579	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
580	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
581	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
582	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
583	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
584	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
585	PANIPAT-JAI ANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
586	INDORE-JHABUA-GUWAHATI MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
587	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
588	4 LANNING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
589	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
590	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
591	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
592	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 671.30	02/2013 -	-
593	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
594	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
595	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
596	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
597	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
598	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
599	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
600	6-LANNING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
601	2-LANNING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
602	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
603	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
604	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
605	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
606	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
607	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
608	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
609	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
610	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-
611	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	61.09 -	05/2017 -	-
612	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
613	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
614	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
615	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
616	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	-
617	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
618	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
619	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
620	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
621	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
622	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
623	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
624	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
625	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
626	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
627	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 1,302.98	03/2018 09/2020	-
628	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
629	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
630	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
631	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
632	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
633	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
634	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 -	-
635	FOUR LANING OF GULIA TO BIAORA SECTION OF NH-3 FROM KM 33.100 TO KM 426.00 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,112.90 -	03/2016 -	-
636	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
637	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
638	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
639	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	-
640	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
641	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 1,182.94	- -	-
642	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
643	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 2,360.65	- -	-
644	TWO LANING WITH PS OF JOWAI - MEHALAYA / ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
645	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	-
646	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
647	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 1,038.56	- -	-
648	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 649.27	04/2018 -	-
649	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
650	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
651	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
652	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
653	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
654	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
655	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
656	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
657	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-
658	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 14.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,036.74 -	- -	-
659	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
660	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-
661	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
662	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
663	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
664	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
665	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
666	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
667	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
668	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
669	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
670	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
671	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	-
672	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-
673	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	-
674	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-
675	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-
676	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-
677	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
678	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.131 (DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	-
679	4 LANNING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,199.61 -	- -	-
680	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
681	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	08/2018 -	-
682	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	05/2019 -	-
683	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
684	FOUR LANNING OF CHICHA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-
685	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA	09/2016	1,004.67 -	05/2019 -	-
686	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 -	- -	-
687	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
688	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-
689	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-
690	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
691	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
692	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
693	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
694	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
695	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
696	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
697	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
698	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000650]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
699	4-LANNING OF MAHARAJGUNJ-YAMATMAL SECTION (KM 32.580 TO 40.575) - [N2400066]NHAI,MAHARASHTRA	03/2017	1,003.06 -	03/2020 -	-
700	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	-
701	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
702	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
703	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
704	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
705	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
706	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
707	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
708	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
709	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
710	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
711	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
712	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
713	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
714	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
715	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
716	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
717	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
718	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
719	VARANASI BYPASS ROAD, PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	4,177.71 -	- -	-
720	FOUR LANING OF KHAMMAM - SHWARA PET SECTION OF NH-365 -B - [N24000751]NHAI,TELANGANA	03/2017	4,499.00 -	03/2017 -	-
721	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
722	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
723	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
724	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
725	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
726	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
727	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
728	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
729	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
730	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
731	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
732	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
733	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
734	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
735	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
736	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
737	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
738	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 98.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 13 - [N24000824]NHAI,TELANGANA	03/2018	85.62 -	- -	-
739	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
740	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
741	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
742	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
743	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
744	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
745	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
746	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
747	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
748	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-

Costing Rs. 150 Crore and above					(December 2020)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
749	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
750	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
751	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
752	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
753	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
754	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
755	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- 02/2020	-
756	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,121.06 -	- -	-
757	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
758	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
759	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-
760	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-
761	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-
762	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
763	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-
764	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
765	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
766	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
	Total		3,56,468.85 -		
	TELECOMMUNICATIONS				
	Department Of Telecommunication				

Costing Rs. 150 Crore and above					(December 2020)
					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
767	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]DOT,MULTI STATE	05/2006	1,077.00 -	03/2009 -	-
	<u>Indian Telephone Industry</u>				
768	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
769	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,DELHI	12/2005	249.00 -	02/2007 -	-
770	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,MAHARASHTRA	01/2006	247.00 -	02/2007 -	-
771	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,DELHI	02/2006	229.41 -	03/2012 -	-
	Total		3,913.58 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Bangalore Metro Rail Corporation Limited</u>				
772	BANGALORE METRO RAIL PROJECT PHASE-2 - [N: 3000058]KMRCL,KARNATAKA	02/2014	26,105.14 -	02/2019 -	-
	<u>Central Public Works Department</u>				
773	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	11/2020 -	11/2020
774	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 02/2021	11/2020
775	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
776	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	09/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
777	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
778	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
779	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
780	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Mumbai Metro Rail Corporation Ltd</u>				
781	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
782	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-
	<u>National Building Construcion Corporation Ltd</u>				
783	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 4,720.73	11/2019 11/2020	11/2020
	Total		90,606.78 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
784	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
785	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
	<u>Delhi Jal Board</u>				
786	7 NOS PRIORITIZED STP, 1 NO SPS AND PERIPHERAL SEWERS II COMMAND AREA OF MAJHAHAR DRAINAGE AREA TO - [N30000018]BJP,DELHI	05/2017	341.81 -	05/2020 -	-
	<u>Uttarakhand Pey Jal Nigam</u>				
787	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
788	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	-
	Total		1,263.88 -		
	<u>COMMERCE AND INDUSTRY</u>				
	<u>National Building Construcion Corporation Ltd</u>				
789	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	10/2020
	Total		302.64 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
790	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	03/2020
791	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	07/2022 -	07/2020
792	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	11/2020
793	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
794	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-

Costing Rs. 150 Crore and above				(December 2020)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Edcil(India) Limited</u>				
795	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
796	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	Total		2,215.30 -		
	Grand Total		6,17,316.11		

FLASH REPORT

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2020)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,896.72	09/2010 09/2016	10/2022	145	73
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	16,038.00	12/2015 -	09/2021	69	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	12,799.00	12/2016 -	03/2023	75	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	22,125.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	56,858.72				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	438.28 -	38.28	335.58	09/2019 -	12/2020	18	-
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI,DELHI	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13	-
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	417.23 -	441.33	291.75	09/2018 09/2020	06/2021	33	9
8	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	-	02/2020 -	06/2021	16	-
9	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10	-
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AIRPORT - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5	-
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 1,232.00	1,232.00	323.90	03/2021 -	03/2022	12	-
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7	-
13	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.66	09/2021 09/2020	09/2022	12	24
14	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	1,405.00	-	08/2022 -	03/2023	7	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	-	03/2022 -	03/2023	12	-
	Total		9,522.42 -	9,636.52	2,193.39				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
16	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	277.38	05/2014 03/2020	02/2021	81	11
17	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	23.04	03/2017 -	10/2021	55	-
18	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	16.73	04/2018 -	12/2021	44	-
	<u>Central Coal Fields Limited</u>								
19	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.63	03/2011 -	03/2022	132	-
20	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	401.56	03/2016 -	03/2022	72	-
21	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	96.86	03/2014 -	03/2022	96	-
22	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND	06/2019	553.06 -	1,532.06	23.77	03/2022 -	03/2024	12	-
	<u>Eastern Coal Fields Limited</u>								
23	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	632.85	03/2018 -	03/2021	36	-
	<u>Mahanadi Coal Fields Limited</u>								
24	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	362.50	362.50	03/2012 -	03/2021	108	-
25	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	491.85	491.85	03/2013 -	03/2022	108	-
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	274.63	03/2019 -	03/2024	60	-
27	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	114.36	03/2018 -	03/2024	72	-
28	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	494.67	03/2021 -	03/2024	36	-
29	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	586.86	586.86	03/2017 -	03/2031	168	-
	<u>Neyveli Lignite Corporation</u>								
30	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	7,980.79	7,371.83	12/2015 -	01/2021	61	-
31	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	31.62	08/2022 -	09/2023	13	-
	<u>Singareni Colliers Company Limited</u>								
32	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	189.91	03/2016 -	03/2021	60	-
33	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	131.52	03/2015 -	03/2022	84	-
34	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	279.54	03/2015 -	03/2022	84	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
35	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2022	84	-
36	KALYANIKHANI OPENCAS PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	122.55	07/2016 -	03/2022	68	-
37	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	106.15	03/2019 -	03/2022	36	-
38	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	153.75	- 04/2017	03/2022	-	59
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	-
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	208.12	03/2014 -	03/2021	84	-
42	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	182.04	03/2016 -	03/2021	60	-
43	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	82.60	03/2020 -	03/2021	12	-
44	JAGANNATHPOR OCP(2.00MTY) [N06000075]SECL,CHH. TISGARH	09/2008	152.43 459.45	459.40	180.74	03/2015 07/2020	03/2022	84	24
45	KARTALI (EAST) OCP (1.50 MTY) [N06000076]SECL,CHH. TISGARH	07/2009	178.44 -	78.44	198	07/2014 -	03/2022	96	-
46	AMADAND OPENCAS EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	120.14	03/2021 -	03/2022	12	-
47	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH	06/2010	11,816.40 -	11,816.40	3,645.58	03/2023 03/2016	03/2023	0	84
48	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.41	03/2018 -	03/2023	60	-
49	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	123.22	03/2020 -	03/2023	36	-
	<u>Western Coal Fields Limited</u>								
50	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	104.95	03/2023 -	03/2024	12	-
51	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	140.64	03/2021 -	03/2024	36	-
	Total		33,321.69 -	36,577.46	18,109.34				
	<u>FINANC</u>								
	<u>Central Public Works Department</u>								
52	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	208.96	195.23	10/2019 -	04/2021	18	-
	Total		209.00 -	208.96	195.23				
	<u>FERTILISERS</u>								
	<u>National Fertiliser Limited</u>								

Costing Rs. 150 Crore and above

(December 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
53	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	218.83	171.68	11/2019 -	02/2021	15	-
54	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	164.03	11/2019 -	03/2021	16	-
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	239.81	182.53	11/2019 -	03/2021	16	-
	Total		674.56 -	674.56	518.24				
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
56	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	355.00	93.16	11/2020 -	02/2021	3	-
	Total		355.00 -	355.00	93.16				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (SAIL)</u>								
57	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	1,026.52	12/2017 10/2020	02/2021	38	4
58	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL	12/2018	263.36 -	263.36	159.19	09/2020 03/2021	05/2021	8	2
	Total		1,417.54 -	1,417.54	1,185.71				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
59	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	5,245.96	4,808.25	08/2018 11/2019	01/2021	29	14
60	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA	08/2016	282.64 -	282.64	238.43	08/2020 -	01/2021	5	-
61	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	695.00	06/2019 -	02/2022	32	-
	<u>Chennai Petroleum Corporation Limited</u>								
62	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	1,858.00	1,498.79	12/2019 -	01/2021	13	-
63	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	300.00	238.43	08/2020 -	09/2021	13	-
	<u>Gas Authority Of India Limited</u>								
64	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	186.50	04/2018 -	03/2021	35	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
65	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,542.50	12/2020 -	03/2021	3	-
66	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	225.54	38.70	02/2021 -	12/2021	10	-
	<u>Hindustan Petroleum Corporation Limited</u>								
67	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	84.06	07/2020 -	07/2021	12	-
	<u>Indian Oil Corporation Limited</u>								
68	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	3,338.00	2,724.32	12/2020 -	03/2021	3	-
69	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	122.92	01/2021 -	04/2021	3	-
70	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	131.10	01/2021 -	04/2021	3	-
71	CONSTRUCTION OF GLASS ROOT PETROLEUM TOP AT ACHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2013	466.00 -	66.00	200.74	07/2021 -	07/2021	3	-
72	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	3,027.90	1,685.17	12/2020 -	08/2021	8	-
73	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	6,025.00	3,275.27	12/2018 -	08/2021	32	-
74	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	160.41	10/2020 -	08/2021	10	-
75	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	109.56	03/2021 -	09/2021	6	-
76	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	111.62	01/2021 -	10/2021	9	-
77	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU	12/2016	228.00 -	228.00	110.61	06/2020 -	11/2021	17	-
78	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	124.52	08/2021 -	11/2021	3	-
79	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 -	1,945.00	1,437.61	08/2021 -	02/2022	6	-
80	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	374.14	10/2017 02/2022	03/2022	53	1
81	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	552.56	08/2020 -	04/2022	20	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
82	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH	03/2018	676.00 -	676.00	375.67	12/2021 -	08/2022	8	-
83	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	82.31	04/2022 -	02/2023	10	-
84	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	53.13	04/2022 -	08/2023	16	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
85	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	390.06	03/2020 11/2020	06/2021	15	7
86	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,501.84	12/2019 04/2021	07/2021	19	3
	<u>Oil & Natural Gas Corporation Limited</u>								
87	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	1,846.46	1,518.24	05/2013 12/2020	03/2021	94	3
	<u>Oil India Limited</u>								
88	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000367]OIL,MULTI STATE	07/2011	352.56 -	490.24	445.41	03/2017 -	03/2021	48	-
89	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	06.00	176.27	10/2020 -	03/2021	5	-
90	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	222.21	148.44	08/2020 -	03/2021	7	-
91	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	450.70	12/2019 -	04/2021	16	-
92	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 638.60	652.10	130.10	02/2020 -	04/2021	14	-
	Total		34,222.37 -	39,286.19	25,732.48				
	<u>POWER</u>								
	<u>Central Public Works Department</u>								
93	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	172.99	11/2019 -	03/2021	16	-
	<u>Chenab Valley Power Projects [P] Limited</u>								
94	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,598.96	04/2020 -	07/2025	63	-
	<u>National Thermal Power Corporation</u>								
95	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	11,044.00	02/2017 06/2020	01/2021	47	7
96	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 15,105.22	15,105.22	13,473.99	01/2018 10/2020	02/2021	37	4

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	11,441.91	12/2018 02/2021	03/2021	27	1
98	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	9,583.00	8,648.28	07/2012 06/2020	03/2021	104	9
99	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,331.70	05/2018 06/2021	07/2021	38	1
100	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,796.50	03/2013 12/2021	12/2022	117	12
101	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	18,668.00	3,644.04	03/2023 -	09/2024	18	-
102	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	626.32	09/2019 11/2022	12/2024	63	25
	<u>Power Grid Corporation Of India Limited</u>								
103	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,623.08	10/2012 06/2020	01/2021	99	7
104	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	640.30	10/2017 12/2020	01/2021	39	1
105	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	341.06	04/2018 04/2020	01/2021	33	9
106	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	45.89	443.98	02/2019 05/2020	01/2021	23	8
107	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	477.58	11/2016 06/2020	02/2021	51	8
108	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	5,070.13	3,989.71	04/2020 -	02/2021	10	-
109	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,500.00	2,724.70	07/2020 -	02/2021	7	-
110	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	234.30	05/2020 -	02/2021	9	-
111	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	238.32	04/2016 12/2017	03/2021	59	39
112	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	89.15	03/2018 -	03/2021	36	-
113	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	627.32	01/2018 05/2020	03/2021	38	10
114	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	11,217.10	11/2019 05/2020	03/2021	16	10
115	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	195.52	02/2019 04/2020	03/2021	25	11

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	146.71	06/2019 09/2020	03/2021	21	6
117	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	210.09	12/2019 06/2020	03/2021	15	9
118	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	156.28	07/2019 06/2020	03/2021	20	9
119	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,564.64	02/2020 09/2020	03/2021	13	6
120	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	508.31	05/2017 07/2020	06/2021	49	11
121	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,151.56	1,893.34	12/2018 -	12/2021	36	-
122	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPISIP) FOR 11 (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33	6,700.00	2,430.27	12/2018 -	12/2021	36	-
	<u>Thdc India Limited</u>								
123	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 -	1,587.16	454.82	09/2020 -	08/2022	23	-
124	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,860.35	2,110.14	06/2013 -	12/2023	126	-
125	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	1,297.85	09/2023 -	08/2024	11	-
	Total		1,45,813.66 -	1,71,725.52	1,07,392.56				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Central Public Works Department</u>								
126	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	115.97	03/2020 -	05/2021	14	-
127	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	34.89	03/2020 -	12/2021	21	-
128	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
129	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>HII Infra Tech Services Limited</u>								

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
130	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	511.74	04/2020 -	07/2021	15	-
131	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	438.92	06/2020 -	07/2021	13	-
132	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	279.76	05/2021 -	07/2022	14	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
133	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	157.90	02/2018 -	12/2020	34	-
134	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	249.74	03/2019 -	01/2021	22	-
135	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	456.52	11/2013 -	03/2021	88	-
136	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	250.00	226.54	05/2017 -	03/2021	46	-
137	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	245.89	03/2019 -	03/2021	24	-
138	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	245.89	03/2019 -	03/2021	24	-
139	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	268.35	03/2019 -	03/2021	24	-
140	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	227.35	05/2018 -	12/2021	43	-
	Total		5,487.34 -	5,301.03	3,501.25				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
141	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,637.46	03/2021 -	03/2023	24	-
142	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	333.58	03/2021 -	03/2023	24	-
143	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12	-
144	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	248.22	03/2022 -	03/2024	24	-
145	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	321.99	03/2023 -	03/2024	12	-
146	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	240.75	03/2022 -	03/2024	24	-
147	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	165.38	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
148	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	14.14	03/2019 -	12/2020	21	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
149	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	487.13	430.52	03/2018 -	03/2021	36	-
150	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	315.22	03/2019 -	03/2021	24	-
	<u>East Central Railways</u>								
151	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	708.22	03/2019 -	02/2021	23	-
152	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,005.54	03/2020 -	03/2021	12	-
153	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	194.21	03/2019 -	03/2021	24	-
154	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	751.55	680.95	03/2012 -	05/2021	110	-
155	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	154.70	03/2021 -	06/2022	15	-
156	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,070.00	1,061.07	03/2012 -	11/2022	128	-
157	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	513.72	03/2020 -	03/2023	36	-
158	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,000.20	76.55	03/2020 -	03/2023	36	-
159	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	465.98	03/2020 -	03/2023	36	-
160	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	299.09	03/2021 -	03/2024	36	-
	<u>East Coast Railway</u>								
161	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	218.99	03/2020 03/2021	03/2022	24	12
	<u>Eastern Railways</u>								
162	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28	-
163	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	663.13	502.41	03/2020 -	03/2021	12	-
164	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	133	-
165	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	899.24	03/2019 12/2009	03/2025	72	183
166	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,091.59	954.89	12/2010 -	03/2025	171	-
167	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228	-
168	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	341.26	03/2022 -	03/2025	36	-
169	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	636.20	03/2016 -	03/2025	108	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
170	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51	769.40	103.51	03/2017	03/2025	96	-
171	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28	266.32	180.03	03/2016	03/2025	108	-
172	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17	340.10	359.71	03/2017	03/2025	96	-
173	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54	494.59	32.00	03/2005	03/2025	240	-
174	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96	680.68	162.75	02/2012	03/2025	157	-
175	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42	257.42	105.99	03/2014	03/2025	132	-
176	PRINCEPGHAT-MAJERA AT DOUBLING OF CIRCULAR RAILWAY - [N22000245]ER,MULTI STATE	04/2011	299.60	35.62	1.22	03/2017	03/2025	108	-
<u>Indian Railway Construction Company Limited</u>									
177	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00	3,055.15	2,386.05	09/2018	12/2021	39	-
178	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00	4,970.11	849.31	03/2022	06/2024	27	-
<u>Metropolitan Rapid Transport Projects</u>									
179	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00	918.53	284.75	03/2014	03/2021	84	-
180	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58	8,574.97	5,892.72	03/2016	06/2021	63	-
181	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74	734.01	481.29	06/2013	12/2021	102	-
182	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44	2,980.41	1,756.68	03/2004	03/2022	216	-
<u>North Central Railway</u>									
183	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96	3,845.60	148.26	03/2022	12/2024	33	-
<u>North East Frontier Railway</u>									
184	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00	800.00	777.27	03/2019	01/2021	22	-
185	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19	5,071.38	3,595.72	12/2008	02/2021	146	-
186	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96	1,873.21	1,007.06	03/2021	05/2021	2	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
187	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	10,584.54	03/2011 -	03/2023	144	-
188	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,105.00	1,532.00	770.73	03/2019 -	03/2023	48	-
189	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 7,114.55	6,911.44	1,045.72	03/2015 -	03/2023	96	-
190	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,047.51	2,042.51	29.84	03/2019 -	03/2023	48	-
191	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	750.00	152.23	03/2020 -	03/2023	36	-
192	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,375.36	03/2022 -	03/2023	12	-
193	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	5,521.45	3,781.94	03/2014 -	12/2023	117	-
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	967.13	03/2019 -	03/2024	60	-
	<u>North Eastern Railway</u>								
195	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NFR,UTTAR PRADESH	04/2017	622.50 427.00	26.74	175.37	04/2017 -	03/2021	47	-
196	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NFR,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	80.32	12/2019 -	04/2021	16	-
197	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NFR,UTTAR PRADESH	04/2016	213.00 -	213.35	28.80	04/2016 -	12/2021	68	-
198	CHHAPRA-BALLIA UP - [N22000134]NFR,MULTI STATE	03/2013	295.00 -	477.31	497.06	01/2019 -	02/2022	37	-
199	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NFR,UTTAR PRADESH	04/2016	600.00 -	366.71	169.83	01/2022 -	03/2022	2	-
200	ETAH - KASGANJ - NEW LINE - [N22000462]NFR,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
201	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NFR,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
202	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NFR,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
	<u>North Western Railway</u>								
203	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	395.00	306.94	12/2019 -	02/2021	14	-
204	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	375.00	327.89	11/2019 -	03/2021	16	-
205	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	287.94	03/2020 -	06/2021	15	-
206	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	677.30	02/2019 -	11/2021	33	-
207	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	780.00	155.47	03/2020 -	04/2022	25	-
	<u>Northern Railway</u>								

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
208	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	893.45	625.47	12/2011 -	06/2021	114	-
209	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	859.00	850.50	03/2016 -	06/2021	63	-
210	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	22,369.08	11/2002 -	12/2022	241	-
211	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	-
	<u>Rail Vikas Nigam Ltd.</u>								
212	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,479.93	03/2020 -	03/2021	12	-
213	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,280.16	03/2019 -	06/2021	27	-
214	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	786.37	03/2016 -	12/2021	69	-
215	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	21	-
216	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATTISGARH	03/2007	1,402.02 -	1,300.00	1,251.62	03/2020 -	12/2021	21	-
217	BINA - KOTA DOUBLING WITH R - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,355.85	1,451.82	11/2016 -	12/2021	12	-
218	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	1,726.74	12/2021 -	03/2022	3	-
219	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24	-
220	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	-
221	BANASPURI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	-
222	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	-
223	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	-
224	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	833.10	03/2023 -	12/2024	21	-
225	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,629.88	03/2016 -	03/2025	108	-
226	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,002.79	03/2016 -	03/2025	108	-
227	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,555.91	12/2024 -	03/2025	3	-
228	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
229	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	1,122.68	12/2024 -	12/2026	24	-
	<u>South Central Railway</u>								
230	MANMAD-PARBHANI-NANDED- SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	-
231	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,472.59	1,078.84	03/2000 -	03/2023	276	-
232	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	746.71	03/2009 -	03/2024	180	-
233	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	346.93	03/2014 -	03/2024	120	-
234	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,222.16	03/2021 -	03/2024	36	-
235	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	466.96	03/2010 -	03/2025	180	-
236	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,191.09	03/2021 -	03/2025	48	-
	<u>South Eastern Railway</u>								
237	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N2200016]SER,JHARKHAND	04/2012	258.20 358.66	358.66	29.76	12/2020 12/2020.8	06/2021	30	30
238	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	795.27	03/2020 03/2020	12/2021	21	21
239	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	642.92	03/2021 03/2021	12/2023	33	33
240	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
241	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
242	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00 -	783.00	607.76	03/2020 -	01/2021	10	-
243	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	1,274.19	03/2019 -	03/2021	24	-
244	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,147.00	877.08	03/2020 -	06/2021	15	-
245	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.94	1,119.20	03/2020 -	11/2021	20	-
246	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	307.53	03/2016 -	12/2023	93	-
247	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	34.85	03/2016 -	12/2023	93	-
248	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-
249	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
250	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	273.30	12/2018 -	12/2024	72	-
	<u>Southern Railway</u>								

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
251	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	-
252	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-
253	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	-
254	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	693.14	03/2020 -	03/2025	60	-
255	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,583.77	02/2019 -	03/2025	73	-
256	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
257	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	232.66	03/2019 -	12/2027	105	-
	<u>West Central Railway</u>								
258	RAMGANJ MUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60	2,909.99	1,132.38	03/2021	03/2023	24	-
259	KATNI - SINGRAULI DOUBLING PROJECT [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,632.04	1,033.58	03/2020 -	03/2023	36	-
260	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	-
261	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	273.37	03/2022 -	03/2023	12	-
262	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	-
	Total		1,54,788.96 -	2,65,064.57	1,28,150.73				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
263	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	293.10	146.46	08/2020 -	08/2021	12	-
264	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	117	-
265	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	663.50	10/2019 -	12/2020	14	-
266	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	288.92	01/2018 11/2020	12/2020	35	1
267	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	199.98	174.35	08/2016 -	12/2020	52	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
268	REHABILITATION AND UPGADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	182.51	05/2019 -	12/2020	19	-
269	REHABILITATION AND UPGADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	143.96	10/2019 -	12/2020	14	-
270	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	162.62	03/2019 -	02/2021	23	-
271	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	141.54	09/2020 -	02/2021	5	-
272	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71	-
273	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	398.38	01/2020 01/2021	03/2021	14	2
274	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GOSHPUR) TO KM 563.26 (BIHAR MORE, ENCL) - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	254.30	78.32	10/2020 -	03/2021	5	-
275	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	151.12	03/2018 01/2021	03/2021	36	2
276	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	03/2021	36	3
277	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35	-
278	REHABILITATION AND UPGADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	199.35	01/2020 -	03/2021	14	-
279	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	83.53	08/2020 -	03/2021	7	-
280	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	728.49	05/2017 -	04/2021	47	-
281	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	218.70	90.68	11/2020 04/2020	04/2021	5	12
282	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	370.30	266.58	06/2018 -	04/2021	34	-
283	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	57.82	09/2018 -	04/2021	31	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
284	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	181.10	04/2020 -	04/2021	12	-
285	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL	01/2017	396.86 396.86	396.86	242.95	09/2019 11/2020	05/2021	20	6
286	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	170.57	34.68	11/2020 -	05/2021	6	-
287	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
288	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	249.75	- 12/2020	06/2021	-	6
289	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA ROAD - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	341.79	192.06	05/2018 -	06/2021	37	-
290	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER OF ABHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	22.48	260.36	07/2020 -	08/2021	13	-
291	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	-
292	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15	-
293	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28	-
294	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	213.97	24.14	08/2019 -	11/2022	39	-
295	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	295.96	10/2010 05/2016	06/2021	128	61
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
296	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	239.35	05/2018 -	12/2020	31	-
297	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	168.32	43.28	04/2017 -	02/2021	46	-

Costing Rs. 150 Crore and above

(December 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
298	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 -	180.57	44.85	04/2017 -	02/2021	46	-
299	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 -	216.71	26.84	04/2017 -	02/2021	46	-
300	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	167.28	22.06	04/2017 -	02/2021	46	-
301	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	127.41	04/2017 03/2018	03/2021	47	36
302	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	170.00	01/2016 -	04/2021	63	-
303	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IN - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM 1 - [N24000869]NHIDCL, MIZORAM	08/2017	517.57 -	457.77	151.85	10/2018	10/2021	36	-
304	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL, NAGALAND	09/2018	215.12 -	215.12	68.20	09/2018 -	11/2021	38	-
305	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	407.30	56.22	06/2018 -	12/2021	42	-
306	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	398.06	103.86	06/2018 -	12/2021	42	-
307	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	315.03	62.00	09/2018 -	12/2021	39	-
308	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	240.64	77.08	09/2018 -	12/2021	39	-
309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	49.94	09/2018 -	12/2021	39	-
310	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	-
311	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	58.12	09/2018 -	05/2022	44	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
312	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	89.79	09/2018 -	07/2022	46	-
313	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	50.62	09/2018 -	09/2022	48	-
314	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	25.76	09/2018 -	10/2022	49	-
315	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	28.46	09/2018 -	11/2022	50	-
	<u>National Highways Authority Of India</u>								
316	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	12/2020	30	-
317	NALBARI T BIJNI (AS-7) [N24000048]NHAI,ASSAM	12/2013	208.00 -	30.00	355.00	04/2018 -	12/2020	152	-
318	HARIDWAR DEHRADUN APPROVED LENGTH 65 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	78.00	315.11	10/2013 -	12/2020	86	-
319	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	-
320	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	815.94	06/2019 -	12/2020	18	-
321	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	32	-
322	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	415.67	08/2018 -	12/2020	28	-
323	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	390.36	07/2018 -	12/2020	29	-
324	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	1,664.20	936.78	04/2020 -	12/2020	8	-
325	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	1,108.00	1,425.26	08/2019 -	12/2020	16	-
326	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	683.51	03/2020 -	12/2020	9	-
327	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	204.65	213.11	09/2017 -	12/2020	39	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
328	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 585.00	591.00	575.34	11/2013 12/2020	01/2021	86	1
329	FOUR LANNING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	897.03	956.62	11/2018 07/2019	01/2021	26	18
330	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI, MADHYA PRADESH	09/2017	990.61 -	990.61	619.77	09/2017 -	01/2021	40	-
331	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	400.25	89.63	03/2019 -	02/2021	23	-
332	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI, TAMIL NADU	03/2017	848.45 932.23	848.45	209.77	03/2020 -	02/2021	11	-
333	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	8	-
334	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI, TAMIL NADU	08/2017	1,176.37 -	1,176.37	425.56	08/2017 -	02/2021	42	-
335	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124 - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	639.97	447.94	10/2017 -	02/2021	40	-
336	PUNE-SATARA (NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,540.00	03/2013 -	03/2021	96	-
337	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71	-
338	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	804.97	520.05	06/2018 10/2020	03/2021	33	5
339	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	2,510.04	525.68	08/2019 -	03/2021	19	-
340	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	446.17	59.61	03/2019 -	03/2021	24	-
341	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	929.32	795.00	04/2020 -	03/2021	11	-
342	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	166.90	45.26	05/2013 -	05/2021	96	-
343	4-LANNING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,239.99	08/2013 -	05/2021	93	-
344	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-
345	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI, KERALA	09/2017	1,124.11 -	1,232.76	419.66	09/2017 -	05/2021	44	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
346	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	333.68	05/2018 04/2019	06/2021	37	26
347	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	817.80	03/2020 -	06/2021	15	-
348	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	-
349	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	-
350	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	330.92	03/2020 -	09/2021	18	-
351	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.25	06/2020 -	09/2021	15	-
352	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	549.62	09/2017 -	09/2021	48	-
353	CONSTRUCTION OF FLYOVER AT SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	89.21	26.45	- 01/2021	09/2021	-	3
354	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	122.48	- 08/2021	11/2021	-	3
355	4-LANNING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,852.94	08/2013 -	12/2021	100	-
356	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	298.39	07/2019 06/2021	12/2021	29	6
357	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	313.00	07/2019 06/2021	12/2021	29	6
358	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	276.50	03/2019 01/2021	12/2021	33	11
359	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	302.88	12/2019 -	12/2021	24	-
360	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	194.95	08/2017 -	02/2022	54	-
361	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	95.50	03/2019 -	03/2022	36	-
362	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	208.90	03/2020 -	04/2022	25	-
363	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	172.62	05/2020 -	05/2022	24	-
364	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		69,988.97	72,668.85	43,746.03				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
365	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	431.16	-	06/2021 -	11/2021	5	-
	<u>Department Of Telecommunication</u>								
366	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	15,239.00	07/2015 -	06/2021	71	-
	Total		13,765.16 -	25,095.16	15,239.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
367	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	8,276.69	12/2018 -	11/2022	47	-
	<u>Central Public Works Department</u>								
368	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIVASPUR, NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,000.80	3,82	07/2021 -	09/2021	2	-
369	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	63.67	08/2020 -	12/2021	16	-
	<u>Delhi Metro Rail Corporation</u>								
370	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,843.96	03/2016 -	03/2021	60	-
371	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	503.33	12/2020 -	09/2021	9	-
	Total		51,495.00 -	53,429.80	48,722.47				
	<u>WATER RESOURCES</u>								
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
372	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	225.77	249.54	03/2020 -	12/2020	9	-
373	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	184.93	163.36	04/2020 -	12/2020	8	-
374	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	191.62	43.01	11/2020 -	12/2020	1	-
375	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	-	08/2021 -	12/2021	4	-
	<u>Delhi Jal Board</u>								
376	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	515.07	278.37	01/2021 -	06/2021	5	-

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
377	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	50.75	12/2021 -	12/2022	12	-
378	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	73.13	02/2022 -	12/2022	10	-
	<u>Hindustan Steelwork Construction Limited</u>								
379	IRRIGATION WORK OF BAGMATI - [N12000108]HSCCL,BIHAR	10/2005	956.00 -	721.37	712.37	03/2015 -	03/2021	72	-
	<u>Kolkata Metropolitan Development Authority</u>								
380	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	274.76	189.36	12/2019 -	12/2020	12	-
381	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	272.32	202.18	04/2020 -	12/2020	8	-
	<u>Polavaram Project Authority</u>								
382	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	16,568.13	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								
383	SEWERAGE WORKS IN SEWERAGE DISTRICT OF KANPUR - [N30000009]UP Jal Nigam,UTTAR PRADESH	10/2016	370.40 -	70.40	270.99	07/2020 -	12/2020	4	-
384	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UP Jal Nigam,UTTAR PRADESH	02/2017	161.31 -	161.31	50.65	11/2019 -	12/2020	13	-
385	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP Jal Nigam,UTTAR PRADESH	02/2011	279.91 -	279.91	222.79	12/2019 -	12/2020	12	-
386	MATHURA SEWERAGE SCHEME - [N30000019]UP Jal Nigam,UTTAR PRADESH	12/2017	460.45 -	460.45	87.15	12/2020 -	01/2021	1	-
387	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UP Jal Nigam,UTTAR PRADESH	12/2018	857.26 -	842.25	-	08/2021 -	06/2022	10	-
388	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP Jal Nigam,UTTAR PRADESH	03/2019	298.12 -	298.12	-	07/2021 -	06/2022	11	-
	Total		15,955.05 -	61,103.24	19,213.88				
	<u>COMMERCE AND INDUSTRY</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
389	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	13,812.30	7,305.07	09/2019 01/2014	07/2021	22	90
	<u>India International Convention And Expo Centre</u>								
390	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	5,178.00	2,334.57	12/2019 -	07/2021	19	-
	Total		17,352.09 -	18,990.30	9,639.64				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								

Costing Rs. 150 Crore and above

(December 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Central Public Works Department</u>								
391	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	226.16	11/2014 -	12/2020	73	-
392	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	350.69	258.72	04/2019 -	01/2021	21	-
393	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	458.38	07/2019 12/2020	03/2021	20	3
394	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6	-
395	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	-
396	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 171.72	171.72	53.94	03/2020 -	06/2021	15	-
397	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	-
398	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	608.00	185.00	06/2017 -	09/2021	51	-
399	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	387.83	167.01	05/2020 -	10/2021	17	-
400	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	122.02	03/2022 -	06/2022	3	-
401	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE 1A AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	-
402	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	-
	<u>Rail India Technical And Economic Service</u>								
403	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	75	-
	Total		5,673.01 -	5,861.44	1,859.68				
	<u>HOME AFFAIRS</u>								
	<u>Central Public Works Department</u>								
404	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	179.16	168.45	04/2018 -	12/2020	32	-

Costing Rs. 150 Crore and above

(December 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
405	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	841.88	10/2019 -	09/2021	23	-
	Total		1,382.09 -	2,179.16	1,010.33				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
406	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2021	62	-
407	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	207.12	189.79	12/2016 -	03/2021	51	-
408	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	03/2021	51	-
	Total		527.83 -	538.27	459.61				
	<u>CULTURE DEVELOPMENT</u>								
409	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	144.00	09/2017 -	03/2021	42	-
	Total		151.33 -	151.33	144.00				
	Grand Total		6,29,223.07	8,50,612.90	4,83,965.45				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(December 2020)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	09/2021	44.69	69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000002]	10/2009	12,320.00 -	17,079.00	12/2016 -	03/2023	38.63	75
	Total		27,71.00	40,49.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	441.33	09/2018 -	06/2021	5.78	33
	Total		417.23 -	441.33				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
5	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	08/2019 -	-	93.35	0
	<u>Mahanadi Coal Fields Limited</u>							
6	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	08/2008	207.28 -	362.50	03/2012 -	03/2021	74.88	108
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	491.85	03/2013 -	03/2022	2.57	108
8	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	586.86	03/2017 -	03/2031	19.74	168
	<u>Neyveli Lignite Corporation</u>							
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00	0
	<u>Singareni Colliers Company Limited</u>							
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2022	114.60	84

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
11	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2022	11.42	36
12	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
13	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2022	5.85	84
14	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>Western Coal Fields Limited</u>							
15	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
16	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
17	BHANEAGAN OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98	0
	Total		23,05.04 -	21,085.64				
	<u>COMMERCE AND INDUSTRY</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
18	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>							
19	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	07/2021	8.49	19
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
20	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	09/2025 -	09/2025	15.92	0
	<u>Hospital Services Consultancy Corporation Ltd</u>							
21	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.64	- -	03/2021	.05	0
22	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	12/2020	16.33	34
23	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20	26
24	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64	8
25	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	01/2021	.02	0
26	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29	46

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
27	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13	24
28	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32
29	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	11/2013 -	03/2021	20.55	88
30	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71	18
	<u>National Building Construcion Corporation Ltd</u>							
31	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	09/2021 -	09/2021	8.88	0
	Total		5,589.39 -	6,253.60				
	<u>HOME AFFAIRS</u>							
	<u>Central Public Work Department</u>							
32	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	179.16	04/2018 -	12/2020	10.00	32
33	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	10/2019 -	09/2021	64.04	23
	Total		1,382.09 -	2,179.16				
	<u>HUMAN RESOURCE DEVELOPMENT</u>							
34	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	02/2019	186.00 199.00	205.00	09/2020 -	03/2021	10.22	6
35	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102	08/2016	294.00 -	350.69	04/2019 -	01/2021	19.28	21
36	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	09/2021	.57	51
	<u>Rail India Technical And Economic Service</u>							
37	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	09/2014 -	12/2020	29.31	75
	Total		1,460.50 -	1,680.94				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
38	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	10/2018 -	07/2020	58.15	21

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29	5,245.96	08/2018	01/2021	14.33	29
	<u>Gas Authority Of India Limited</u>							
40	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49	345.15	04/2022	04/2022	20.06	0
41	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00	842.00	02/2020	-	12.42	0
	<u>Indian Oil Corporation Limited</u>							
42	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00	502.00	08/2019	06/2021	18.68	22
43	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00	3,027.90	12/2020	08/2021	66.09	8
44	PARADIP HALDIA PIPELINE - [N16000194]	01/2015	2,211.00	3,338.00	12/2020	03/2021	43.82	3
45	ENNORE TIRUVALUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,027.00	6,025.00	12/2018	08/2021	33.98	32
	<u>Indian Strategic Petroleum Reserves Ltd</u>							
46	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00	1,693.00	01/2012	-	70.49	0
	<u>Oil India Limited</u>							
47	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56	490.24	03/2017	03/2021	39.05	48
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91	652.10	02/2020	04/2021	19.89	14
	Total		17,272.25	23,258.89				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							
49	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84	1,592.34	09/2019	12/2024	15.23	63
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00	1,801.07	08/2017	-	17.95	0
51	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96	4,552.00	10/2017	-	7.41	0
52	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00	9,583.00	07/2012	03/2021	79.02	104
53	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98	10,016.10	07/2019	03/2021	9.00	20

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
54	KHARGONE STPP STAGE I (1320 MW) - [N18000205	03/2015	9,870.51 -	11,148.86	01/2020 -	-	12.95	0
55	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	04/2012	9,750.89 -	12,176.28	02/2017 -	01/2021	24.87	47
56	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	10/2017 -	-	7.55	0
57	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 -	13,740.53	12/2018 -	03/2021	9.64	27
58	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,389.42	06/2019 -	10/2022	7.12	40
	<u>Power Grid Corporation Of India Limited</u>							
59	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	01/2015	203.28 -	260.03	07/2017 -	-	27.92	0
60	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000190	10/2011	487.49 -	639.46	06/2014 -	-	31.17	0
61	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NETIP) FOR SI, (6) STATES - [N18000250	12/2014	5,111.33 -	6,000.00	12/2018 -	12/2021	31.08	36
62	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,151.56	12/2018 -	12/2021	92.49	36
	<u>Thdc India Limited</u>							
63	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,860.35	06/2013 -	12/2023	54.94	126
	Total		93,103.30 -	1,13,350.82				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
64	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	184.06 -	315.00	03/2019 -	03/2020	71.14	12
65	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356	02/2015	1,272.19 -	1,283.49	03/2022 -	03/2023	.89	12
66	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	792.89 -	1,377.48	03/2021 -	03/2023	73.73	24
67	DAUND - MANMAD (236 KM) - [N22000360	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94	0
68	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04	0
69	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2023	.00	-12
70	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181	02/1997	2,271.50 -	4,517.49	03/2021 -	03/2023	98.88	24
71	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28	0
	<u>Container Corporation Of India</u>							

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
72	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50	235.00	03/2019	12/2020	.21	21
73	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	01/2013	387.70	487.13	03/2018	03/2021	25.65	36
	<u>East Central Railways</u>							
74	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01	480.00	-	-	125.34	0
75	KOSI BRIDGE (NL), ECR - [220100304	04/2002	499.41	516.02	03/2020	-	3.33	6
76	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00	519.33	-	02/2023	36.67	0
77	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15	546.71	07/2014	-	64.60	0
78	GAYA-CHATRA (NL) - [N22000160	04/2008	415.67	549.75	-	-	32.26	0
79	KHAGARIA-KUSHESHWAR ASHTHAN (NL)/ECR - [22010025	04/1997	62.87	11.45	-	03/2022	277.26	0
80	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	04/1996	160.82	726.31	-	-	301.68	0
81	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00	735.20	-	03/2021	126.22	0
82	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88	751.55	03/2012	05/2021	57.27	110
83	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00	819.01	03/2020	03/2023	49.45	36
84	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00	1,006.00	-	-	376.78	0
85	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	04/1997	324.73	1,070.00	03/2012	11/2022	229.50	128
86	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473	04/2016	731.64	1,185.73	03/2021	06/2022	62.06	15
87	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04	1,215.54	03/2021	03/2024	63.37	36
88	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14	1,470.50	-	03/2021	295.15	0
89	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39	1,483.14	-	03/2022	350.27	0
90	KODERMA-TILAIYA (NL), ECR - [220100305	04/2002	459.91	1,625.87	-	03/2023	253.52	0
91	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56	1,858.75	-	03/2022	391.01	0
92	HAJIPUR-SAGauli VIA VAISHALI (NL), ECR - [220100303	04/2003	528.65	2,066.78	-	03/2023	290.95	0

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
93	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15	0
94	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,500.00	- -	03/2022	238.80	0
	<u>Eastern Railways</u>							
95	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19	0
96	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	270.72	- -	03/2022	53.99	0
97	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	03/2022	6.48	0
98	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25	0
99	MONIGRAM- NIMITTA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82	0
100	PRINCEPAT-MAJURHAT DOUBLING OF CIRCULAR RAILWAY [N22000231]	04/2011	99.60 -	331.62	03/2017 -	03/2026	12.02	108
101	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	418.09	- -	03/2021	44.99	0
102	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE- PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
103	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	516.05	- -	05/2019	97.43	0
104	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46	0
105	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
106	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	03/2020 -	03/2021	22.31	12
107	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
108	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI- SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
109	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
110	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30	0
111	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
112	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
113	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
114	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	09/2018 -	12/2021	.00	39
115	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	06/2024	117.23	27
	<u>Metropolitan Rapid Transport Projects</u>							
116	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	12/2021	48.06	102
117	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2022	501.57	216
118	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSC AIRPORT(MTP) - [220100263]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37	0
119	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,745.58 -	8,574.97	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>							
120	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	-	188.33	0
121	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	-	1.69	0
122	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
123	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2022	7.86	0
124	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	- -	12/2021	54.80	0
125	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62	0
126	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
127	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	-	106.51	0
128	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	03/2020 -	03/2022	30.26	24
129	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	03/2020 -	03/2023	80.79	36
130	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	760.00	12/2021 -	03/2021	26.19	-9
131	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	800.00	03/2019 -	01/2021	154.78	22

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
132	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499	02/1999	380.60	1,090.60	04/2010	-	186.55	0
133	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20	1,532.00	03/2019	03/2023	297.72	48
134	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23	1,871.00	-	-	128.39	0
135	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96	1,873.21	03/2021	05/2021	115.07	2
136	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87	2,145.00	03/2019	03/2024	302.54	60
137	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32	2,950.00	03/2022	03/2023	32.15	12
138	NEW BG LINE FROM BYRNIHAT TO SHILONG - [N22000215	04/2010	106.46	4,083.02	03/2021	03/2021	350.44	0
139	NEW MAYT AGURI TO JOGIC HOPALIA CHANGRABANDHA (NL), NEFR - [220100266	04/2000	1,180.19	5,071.28	02/2008	02/2021	329.71	146
140	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47	5,521.45	03/2014	12/2023	130.69	117
141	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48	8,600.00	12/2015	-	542.04	87
142	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17	12,264.15	03/2011	03/2023	175.34	144
	<u>North Eastern Railway</u>							
143	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92	197.73	-	-	8.10	0
144	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00	213.35	04/2016	12/2021	.16	68
145	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45	228.40	-	-	60.34	0
146	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00	477.31	01/2019	02/2022	61.80	37
147	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136	03/2013	643.00	644.00	-	-	.16	0
148	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50	714.34	-	12/2023	18.56	0
149	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78	895.00	12/2021	12/2021	267.13	0
150	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00	1,409.09	-	-	358.99	0
151	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460	04/2017	1,343.00	1,476.15	01/2018	-	9.91	0
	<u>North Western Railway</u>							

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
152	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	10/2018 -	-	47.91	0
153	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	11/2019 -	03/2021	75.73	16
154	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	12/2019 -	02/2021	60.52	14
155	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81	0
156	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	02/2019 -	02/2020	116.86	12
157	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	780.00	03/2020 -	04/2022	30.00	25
158	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	11/2021	109.82	33
159	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	- -	-	33.70	0
160	AJMER(NASIRABAD SAWAI MADHOPUR (CHAUHAN) KA BARWARA) VISITONK NL [N22000331]	05/2015	73.71 -	1,080.21	- -	-	126.64	0
161	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	- -	-	104.65	0
	<u>Northern Railway</u>							
162	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68	0
163	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
164	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
165	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	- -	03/2024	310.24	0
166	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	03/2016 -	06/2021	37.44	63
167	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	06/2021	211.31	114
168	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	- -	03/2023	2.93	0
169	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	07/2012 -	03/2024	388.89	140
	<u>Rail Vikas Nigam Ltd.</u>							
170	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	03/2009 03/2009	-	196.83	0
171	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
172	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	03/2021	35.42	0
173	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15	69

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
174	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98	33
175	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2021	51.02	27
176	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	12/2021 -	12/2021	53.75	0
177	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	03/2019 -	06/2022	62.89	39
178	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	12/2020 -	12/2022	54.24	24
179	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	12/2020 -	12/2021	23.55	12
180	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	-	55.57	0
181	PALANPUR-SAMAKHAYALI (DL) - [N22000141]	04/2013	1,548.66 -	1,868.80	12/2021 -	02/2022	20.68	3
182	SAMBALPUR - TITLAGARH - DOUBLING - [N22000400]	03/2006	48.04 -	2,000.00	01/2020 -	12/2021	111.91	21
183	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
184	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	03/2020 -	03/2021	281.93	12
185	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
186	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04	-3
187	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
188	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58	24
189	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
190	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22	108
192	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62	-12
193	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08	3
	<u>Railway Electrification</u>							
194	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77	0

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>South Central Railway</u>							
195	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	449.39	03/2022 -	12/2022	275.34	9
196	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	704.31 -	927.94	03/2020 -	06/2021	31.75	15
197	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84	0
198	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
199	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2024	102.85	180
200	NADIKUDE-SRI KALAHASTI - [N22000286	04/2011	2,288.70 -	2,643.25	03/2021 -	03/2025	15.49	48
201	MANUGURU-DAMACUNDAM - [N22000293	04/2013	1,112.00 -	2,911.84	- -	-	161.86	0
202	MUNEERA AD-MAHABOBNICAM (NL) SCR - [220100265	04/1997	1,123.00 1,100.00	3,471.59	01/2000 -	03/2023	101.54	276
203	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>							
204	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
205	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 -	1,226.51	12/2019 -	10/2020	40.65	10
206	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	04/2010	585.93 -	1,268.32	02/2019 -	12/2021	116.46	34
207	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,413.76	- -	08/2020	268.37	0
208	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	2,005.25	04/2020 -	04/2021	291.76	12
209	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	3,524.81	03/2023 -	12/2023	84.69	9
	<u>South Eastern Railway</u>							
210	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	03/2015 -	-	53.44	0
211	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	08/2020	153.41	44
212	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	- -	03/2025	131.89	0
213	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
214	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76	0

Costing Rs. 150 Crore and above

(December
2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
215	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	03/2021 -	12/2023	15.60	33
216	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
217	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14	0
218	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38	0
219	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65	0
220	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09	0
221	ARSIKERE TUMKUR - [N22000302]	03/2015	570.00 -	783.00	03/2020 -	01/2021	35.47	10
222	KADUR CHIKMAGALUR SAKI CHIKMUR NEW LINE 93 KM) - [N22000486]	03/1996	44.78 -	890.00	01/2017 -	-	38.03	0
223	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	03/2020 -	06/2021	33.31	15
224	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84	24
225	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	- -	12/2023	9.22	0
226	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	- -	03/2025	17.95	0
227	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	- -	12/2024	68.97	0
	<u>Southern Railway</u>							
228	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	- -	-	45.43	0
229	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	332.00	04/2014 -	12/2020	77.29	80
230	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	- -	-	46.09	0
231	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.73	- -	09/2021	174.15	0
232	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	12/2021	69.20	0
233	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	02/2019 -	-	247.32	0
234	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	- -	03/2025	181.84	0
235	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	09/2021	253.33	198

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
236	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	961.09	- -	02/2021	3.12	0
237	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	- -	-	295.05	0
238	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400	02/2015	1,000.00 -	1,246.00	- -	-	24.60	0
239	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78	0
240	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451	02/2015	760.00 -	1,536.00	03/2020 -	06/2022	102.11	27
241	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	1,720.00	03/2020 -	03/2025	465.83	60
242	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000205	04/2011	120.70 -	2,172.16	03/2019 -	12/2027	1,699.64	105
243	CHENNAI-ODDALORE VIA MADURAI-PALURAI - [N22000185	04/2008	25.32 -	2,300.00	- -	03/2024	339.33	0
244	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	- -	-	79.80	0
245	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,910.84	02/2019 -	03/2025	301.67	73
<u>West Central Railway</u>								
246	RAMGANJMUDDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
247	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
<u>Western Railway</u>								
248	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	03/2011 -	-	72.42	0
Total			1,76,175.46 -	3,31,127.22				
<u>ROAD TRANSPORT AND HIGHWAYS</u>								
<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
249	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00	157.30	06/2018 -	-	.00	0
250	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	-	.00	0
251	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	-	.00	0
252	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	-	.00	0

Costing Rs. 150 Crore and above								(December 2020)
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
253	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00	203.21	05/2019 -	-	.00	0
254	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00	215.16	09/2019 -	-	.00	0
255	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00	217.14	02/2020 -	-	.00	0
256	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00	222.13	11/2019 -	-	.00	0
257	KUNDRAI TO WAZAR - [N24001077]	01/2018	225.25 225.00	225.25	12/2019 -	-	.00	0
258	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00	227.19	12/2019 -	-	.00	0
259	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000821]	11/2017	237.80 -	238.00	11/2019 -	-	.08	0
260	PARBHANI TO SANGAKHED - [N24001015]	03/2018	238.19 238.00	238.19	11/2019 -	-	.00	0
261	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00	240.30	01/2020 -	03/2021	.00	14
262	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00	244.04	03/2019 -	-	.00	0
263	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	- -	-	58.68	0
264	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00	257.38	12/2019 -	-	.00	0
265	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00	264.41	03/2019 -	-	.00	0
266	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84	0
267	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00	272.04	12/2019 -	-	.00	0
268	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	- -	-	3.72	0
269	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	03/2018	297.12 294.00	294.12	07/2018 -	-	-1.01	0
270	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	07/2019 -	-	.31	0
271	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00	301.38	08/2020 -	-	.00	0
272	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00	303.24	12/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
273	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	02/2018 -	-	40.84	0
274	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	08/2016 -	-	14.02	0
275	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	12/2020	72.36	75
276	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.00	0
277	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	-	69.30	128
278	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	-	.00	0
279	LATUR TO WANGAO - [N24001013	03/2018	336.41 336.00	336.41	12/2019 -	-	.00	0
280	MORSHI TO ACHALPUR - [N24001015	01/2017	41.16 341.00	341.16	05/2019 -	-	.00	0
281	OSMANNAGAR TO KUNDRAL - [N24001075	09/2017	344.25 344.00	344.25	08/2020 -	-	.00	0
282	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	-	.00	0
283	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	0
284	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21	0
285	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	12/2015 -	-	6.81	0
286	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67	0
287	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	-	.00	0
288	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42	0
289	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2021	93.80	128
290	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00	381.08	05/2020 -	-	.00	0
291	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	05/2012 -	-	88.11	0
292	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
293	CHIKLI TO TAKARKHED - [N24001083	03/2018	393.10 393.00	393.10	12/2019 -	-	.00	0
294	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00	404.33	05/2020 -	-	.00	0
295	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	-	.00	0
296	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00	0
297	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	06/2020 -	-	.00	0
298	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06	0
299	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASARA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	01/2021	.00	26
300	REHABILITATION AND UPGRADATION OF NH-200 FROM KM. 78.944 TO 241.55, BANARI (VILLAGE TO MASANIA KALA V - [N24001219	01/2016	70.20 44.00	54.00	01/2016 -	03/2021	14.24	54
301	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	-	.00	0
302	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06	0
303	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	-	46.51	0
304	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	03/2017 -	-	46.51	0
305	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00	743.21	06/2021 -	06/2021	.00	0
306	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	04/2021	77.26	47
307	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	12/2020	1.75	0
308	PARSHURAM GHAT TO ARAWALI - [N24001133	04/2016	983.14 983.00	983.14	12/2019 -	-	.00	0
309	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2020	58.98	117
310	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	04/2021	.00	59
311	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401	11/2011	954.43 -	1,191.51	09/2015 -	10/2021	24.84	73
312	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
313	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	-	.00	0
314	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	-	.00	0
315	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	- -	-	2.93	0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
316	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	08/2016 -	-	3.73	0
317	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30	0
318	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000602]	10/2017	818.00 -	887.68	- -	-	8.52	0
	<u>National Highways Authority of India</u>							
319	DHARAMTIL TO SONAPUR, KM 205.83 (AS-10) - [N24000049]	12/2003	168.00 -	167.90	05/2008 -	06/2019	4.99	133
320	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	12/2020	10.58	152
321	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	255.23	11/2008 -	-	64.62	0
322	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 -	276.17	- -	-	.99	0
323	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	- -	-	8.35	0
324	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]	08/2015	322.09 -	322.09	04/2018 -	12/2020	.00	32
325	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	08/2018 -	-	3.98	0
326	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	04/2009 -	-	70.23	0
327	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82	111
328	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	- -	-	.77	0
329	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	- -	12/2020	7.53	0
330	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	435.78	11/2008 -	-	159.95	0
331	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]	12/2017	404.94 -	448.18	- -	10/2020	10.68	0
332	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
333	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	520.00	02/2009 -	-	85.71	0
334	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	- -	-	8.26	0
335	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	11/2013 -	01/2021	15.53	86
336	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	07/2009 -	-	234.27	0
337	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	- -	-	6.11	0
338	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	690.17	05/2018 -	06/2021	16.34	37
339	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I [N24000461	03/2015	794.30 -	691.38	- -	05/2020	-12.96	0
340	4 LANING OF KASHI PUR-SITABGANJ SECTION KM. 175.000 TO KM. 252.000 - [N24000638	11/2012	65.04 -	72.46	01/2013 -	-	19.25	0
341	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	730.97	05/2018 -	06/2021	37.63	37
342	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	-	9.38	0
343	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	- -	12/2021	.00	0
344	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	12/2017 -	-	66.88	0
345	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	09/2021	.23	18
346	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	- -	07/2021	.48	0
347	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	- -	-	25.68	0
348	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	- -	10/2021	1.37	0
349	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	- -	-	27.86	0
350	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	- -	-	305.58	0
351	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	04/2020 -	03/2021	3.95	11

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
352	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	931.21	- -	07/2021	46.72	0
353	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	- -	01/2020	11.33	0
354	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	-	31.88	0
355	MEERUT-BULANDSHAHAAR - [N24000539]	01/2016	683.24 -	987.94	- -	-	44.60	0
356	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
357	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000655]	03/2017	1,030.44 -	1,065.51	03/2020 -	-	3.40	0
358	FOUR LANING OF KILLAGAM TO KARUPPAMPUR FROM KM.38+700 TO KM. 51+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,116.03 -	1,077.00	- -	07/2021	5.32	0
359	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
360	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	08/2019 -	12/2020	16.55	16
361	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	- -	02/2021	4.10	0
362	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	-	5.70	0
363	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	-	41.54	0
364	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	-	13.97	0
365	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 -	1,197.00	- -	-	29.35	0
366	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	09/2017 -	05/2021	9.67	44
367	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44	0
368	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 -	1,296.00	- -	-	.12	0

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
369	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	0
370	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
371	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	06/2021	10.24	15
372	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
373	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	- -	01/2021	37.71	0
374	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION C - [N2400023	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
375	FOUR LANING OF GVALIOR SHIVPURI - [N24000454	05/2013	1,555.00 -	1,601.77	11/2015 -	-	51.83	0
376	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	09/2016	1,239.82 -	1,727.66	- -	01/2021	39.35	0
377	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,827.15	06/2018 -	-	68.71	30
378	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09	0
379	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	- -	07/2021	54.69	0
380	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	06/2020 -	02/2021	1.78	8
381	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	-	4.99	0
382	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 -	2,280.00	- -	-	94.94	0
383	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28	0
384	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	-	18.50	0
385	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50	0

Costing Rs. 150 Crore and above

(December 2020)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
386	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05	1
387	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
388	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	09/2019 -	-	86.37	0
389	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	03/2021	52.73	71
390	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	11/2011 -	-	167.82	0
391	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84	0
392	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000112	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		98,01.00 -	1,02,00.32				
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
393	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00	431.16	06/2021 -	11/2021	.00	5
	<u>Department Of Telecommunication</u>							
394	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2021	84.97	71
	Total		13,765.16 -	25,095.16				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
395	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	12/2018 -	11/2022	18.69	47
	<u>Chennai Metro Rail Ltd</u>							
396	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53	0
	Total		25,373.00 -	31,845.00				
	<u>WATER RESOURCES</u>							
	<u>Uttar Pradesh Jal Nigam</u>							
397	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 -	234.03	12/2021 -	12/2021	.97	0

Costing Rs. 150 Crore and above					(December 2020)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		231.79	234.03				
	Grand Total		5,01,859.96	7,44,048.11				

FLASH REPORT

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 5,677.00	6,840.00	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	09/2021	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (1300 MW) - [N 20 0027]	10/2009	12,320.00 - 12,320.00	17,075.00	12/2016 -	03/2023	38.63
	Total		27,271.00 - 29,456.00	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 - 417.23	441.33	09/2018 -	06/2021	5.78
	Total		417.23 - 417.23	441.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
5	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	-	93.35
	<u>Mahanadi Coal Fields Limited</u>						
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 - 490.10	586.86	03/2017 -	03/2031	19.74
7	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	08/2008	207.28 - 207.28	362.50	03/2012 -	03/2021	74.88
8	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 - 479.53	491.85	03/2013 -	03/2022	2.57
	<u>Neyveli Lignite Corporation</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86
11	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 - 249.03	448.86	03/2012 -	03/2024	80.24
12	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2022	11.42
13	JALAGAM VENGALA F AO OCP-II - [N06000094]	07/2011	47.06 - 47.06	47.22	03/2015 -	03/2022	5.85
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2022	114.60
	<u>Western Coal Fields Limited</u>						
15	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 - 277.65	313.34	03/2021 -	03/2024	12.85
16	BHANEGAON OC - [N06000121]	02/2015	187.94 - 187.94	409.68	03/2023 -	03/2023	117.98
17	ADASA UG TO OC - [N06000133]	08/2015	288.90 - 288.90	333.43	03/2023 -	03/2024	15.41
	Total		23,505.04 .00 23,505.04	27,085.34			
	<u>COMMERCE AND INDUSTRY</u>						
	<u>Delhi Mumbai Industrial Corridor</u>						
18	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>						
19	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	07/2021	8.49
	Total		17,352.09 .00 17,352.09	18,990.30			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
20	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 - 1,577.00	1,828.00	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>						
21	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	11/2013 -	03/2021	20.55
22	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29
23	AIIMS - OPD (NEW) - [N21000009]	08/2014	236.65 -	321.00	05/2017 -	01/2020	10.68
24	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20
25	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71
26	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	12/2020	16.33
27	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64
28	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13
29	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.64	- -	03/2021	.05
30	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>						
31	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	09/2021 -	09/2021	8.88
	Total		5,589.39 .00 5,589.39	6,253.60			
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
32	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	09/2021	64.04
33	NSG AT KOLKATA - [N28000104	10/2014	162.88 - 162.88	179.16	04/2018 -	12/2020	10.00
	Total		1,382.09 .00 1,382.09	2,179.16			
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
34	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF T PATNA - [N28000000	02/2016	496.18 496.00 496.00	498.99	06/2017	09/2021	.60
35	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROHAR, PUNJAB - [N28000102	08/2016	294.00 - 294.00	357.69	04/2019 -	01/2021	19.28
36	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	02/2019	186.00 199.00 199.00	205.00	09/2020 -	03/2021	3.02
	<u>Rail India Technical And Economic Service</u>						
37	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 - 484.32	626.26	09/2014 -	12/2020	29.31
	Total		1,460.50 695.00 1,473.32	1,680.94			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
38	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 - 694.00	1,097.54	10/2018 -	07/2020	58.15
39	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 - 4,588.29	5,245.96	08/2018 -	01/2021	14.33
	<u>Gas Authority Of India Limited</u>						
40	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	02/2015	749.00 - 749.00	842.00	02/2020 -	-	12.42
41	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	04/2017	287.49 - 287.49	345.15	04/2022 -	04/2022	20.06
	<u>Indian Oil Corporation Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
42	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00 - 1,823.00	3,027.90	12/2020 -	08/2021	66.09
43	PARADIP HYDERABAD PIPELINE - [N16000194	01/2015	2,321.00 - 2,321.00	3,338.00	12/2020 -	03/2021	43.82
44	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 - 423.00	502.00	08/2019 -	06/2021	18.68
45	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 - 4,497.00	6,025.00	12/2018 -	08/2021	33.98
<u>Indian Strategic Petroleum Reserves Ltd</u>							
46	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	9,300.00 - 9,300.00	1,69,000.00	01/2012 -	-	70.49
<u>Oil India Limited</u>							
47	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 - 352.56	490.24	03/2017 -	03/2021	39.05
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 - 638.60	652.10	02/2020 -	04/2021	19.89
	Total		17,272.25 .00 17,366.94	23,258.89			
<u>POWER</u>							
<u>National Thermal Power Corporation</u>							
49	TANDA TPP STAGE-II (2X660 MW) - [N18000175	09/2014	9,188.98 - 9,188.98	10,016.10	07/2019 -	03/2021	9.00
50	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 - 12,532.44	13,740.53	12/2018 -	03/2021	9.64
51	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 - 14,366.58	15,389.42	06/2019 -	10/2022	7.12
52	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 - 1,381.84	1,592.34	09/2019 -	12/2024	15.23
53	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 - 7,998.00	9,583.00	07/2012 -	03/2021	79.02
54	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	04/2012	9,750.89 - 9,750.89	12,176.28	02/2017 -	01/2021	24.87

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 - 11,846.00	12,739.82	10/2017 -	-	7.55
56	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
57	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 - 9,870.51	11,148.86	01/2020 -	-	12.95
58	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
<u>Power Grid Corporation Of India Limited</u>							
59	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	2,328.00 - 2,328.00	26,003.00	07/2017 -	-	27.92
60	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 - 487.49	639.46	06/2014 -	-	31.17
61	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 - 4,754.42	9,151.56	12/2018 -	12/2021	92.49
62	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 - 5,111.33	6,700.00	12/2018 -	12/2021	31.08
<u>Thdc India Limited</u>							
63	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 - 2,491.58	3,860.35	06/2013 -	12/2023	54.94
Total			93,103.30 4,238.00 95,748.34	1,13,350.82			
<u>RAILWAYS</u>							
<u>Central Railways</u>							
64	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	1,377.48	03/2021 -	03/2023	73.73
65	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 - 199.12	315.00	03/2019 -	03/2020	71.14
66	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,517.49	03/2021 -	03/2023	98.88
67	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 - 2,425.00	5,341.68	03/2024 -	03/2024	120.28

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
68	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 - 2,750.00	3,438.51	03/2024 -	03/2024	25.04
69	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,283.49	03/2022 -	03/2023	.89
70	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
71	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2023	10.94
<u>Container Corporation Of India</u>							
72	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	3,770.00 - 3,770.00	48,130.00	03/2018 -	03/2021	25.65
73	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	12/2020	.21
<u>East Central Railways</u>							
74	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 - 1,033.07	3,500.00	- -	03/2022	238.80
75	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 - 528.65	2,066.78	- -	03/2023	290.95
76	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95 283.95	751.55	03/2012 -	05/2021	164.68
77	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 - 324.73	1,070.00	03/2012 -	11/2022	229.50
78	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 - 162.87	614.45	- -	03/2022	277.26
79	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 - 499.41	516.02	03/2020 -	-	3.33
80	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 - 380.00	519.33	- -	02/2023	36.67
81	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 - 459.91	1,625.87	- -	03/2023	253.52
82	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 - 415.67	549.75	- -	-	32.26

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
83	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 - 326.20	2,995.01	- -	03/2024	818.15
84	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 - 325.00	735.20	- -	03/2021	126.22
85	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 - 378.56	1,858.75	- -	03/2022	391.01
86	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 - 211.00	1,006.00	- -	-	376.78
87	SAKRI-NIRMAI LAND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) [N22000180]	04/2004	372.14 - 372.14	1,470.50	- -	03/2021	295.15
88	JAYNAGAR-BIJALPUR INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	538.00 - 548.00	899.01	03/2020 -	03/2023	49.45
89	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 - 213.01	480.00	- -	-	125.34
90	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 - 332.15	546.71	07/2014 -	-	64.60
91	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 - 744.04	1,215.54	03/2021 -	03/2024	63.37
92	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 - 731.64	1,185.73	03/2021 -	06/2022	62.06
93	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 - 180.82	726.31	- -	-	301.68
94	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 - 329.39	1,483.14	- -	03/2022	350.27
<u>Eastern Railways</u>							
95	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
96	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
97	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 - 542.18	663.13	03/2020 -	03/2021	22.31
99	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 - 175.80	270.72	- -	03/2022	53.99
100	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
101	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01
102	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHAT, KAPUR NL [N22000241]	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25
103	MAGRAHAT- DIAMOND HATBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 - 499.96	600.68	02/2012 -	03/2025	36.15
104	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
105	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
106	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08
107	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30
108	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
109	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
110	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 - 288.35	418.09	- -	03/2021	44.99
111	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 - 261.38	516.05	- -	05/2019	97.43
112	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
113	CHINPAI-SAINTIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTIA VIA KANDI NL [N22000225]	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Indian Railway Construction Company Limited</u>						
114	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	06/2024	117.23
115	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	12/2021	.00
	<u>Metropolitan Rapid Transport Projects</u>						
116	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37
117	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100114]	03/1996	495.44 - 4,544.00	2,980.41	03/2004 -	03/2022	501.57
118	EXTENSION OF MRTS FROM BELAPUR TO S.N. THOMAS, MTP - [N22000028]	04/2006	4,574.00 - 495.74	73,001.00	06/2013 -	12/2021	48.06
119	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
120	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 - 120.00	346.00	12/2008 -	-	188.33
121	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
122	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00 668.00	680.00	03/2020 -	-	1.80
	<u>North East Frontier Railway</u>						
123	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 - 297.32	614.00	03/2019 -	-	106.51
124	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 2,393.47	5,521.45	03/2014 -	12/2023	130.69
125	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 - 4,541.38	5,071.38	12/2008 -	02/2021	329.71
126	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 4,454.17	12,264.15	03/2011 -	03/2023	175.34
127	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 1,105.00	1,532.00	03/2019 -	03/2023	297.72

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
128	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 - 532.87	2,145.00	03/2019 -	03/2024	302.54
129	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 - 333.76	360.00	- -	03/2022	7.86
130	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 4,084.69	8,600.00	12/2015 -	-	542.04
131	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 - 221.42	380.00	- -	-	71.62
132	AGARTALA-AKHAIHARA NL - [N22000195]	04/2012	569.63 - 569.63	742.00	03/2020 -	03/2022	30.26
133	NEW BG LINE FROM BIRBHAR TO SILLONG - [N22000205]	04/2010	906.46 - 906.46	4,063.02	03/2021 -	03/2021	350.44
134	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
135	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	373.87	- -	12/2021	54.80
136	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	750.00	03/2020 -	03/2023	80.79
137	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 - 819.23	1,871.00	- -	-	128.39
138	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 - 314.00	800.00	03/2019 -	01/2021	154.78
139	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	2,950.00	03/2022 -	03/2023	32.15
140	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	1,873.21	03/2021 -	05/2021	115.07
141	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 - 602.27	760.00	12/2021 -	03/2021	26.19
142	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60 - 380.60	1,090.60	04/2010 -	-	186.55
	<u>North Eastern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
143	KICHHA-KHATIMA (NL) - NER - [N220100317]	04/2003	142.45 - 142.45	228.40	- -	-	60.34
144	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 - 182.92	197.73	- -	-	8.10
145	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
146	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 - 243.78	895.00	12/2021 -	12/2021	267.13
147	CHHAPRA-BALIA UP - [N22000134]	03/2013	295.00 - 295.00	477.31	01/2019 -	02/2022	61.80
148	KAPILVASTU BASTI VIA BANSI SIDHARTH NAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
149	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	12/2021	.16
150	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,476.15	01/2018 -	-	9.91
151	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	714.34	- -	12/2023	18.56
<u>North Western Railway</u>							
152	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	11/2021	109.82
153	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	780.00	03/2020 -	04/2022	30.00
154	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 - 873.71	1,980.21	- -	-	126.64
155	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 - 246.08	395.00	12/2019 -	02/2021	60.52
156	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
157	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 - 236.93	350.45	10/2018 -	-	47.91

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
158	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 - 822.00	1,099.00	- -	-	33.70
159	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 - 323.00	432.22	- -	-	33.81
160	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 - 213.39	375.00	11/2019 -	03/2021	75.73
161	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 - 242.09	525.00	02/2019 -	02/2020	116.86
<u>Northern Railway</u>							
162	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	136.65 - 136.17	35.00	- -	03/2024	129.17
163	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	06/2021	211.31
164	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
165	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 - 219.83	346.63	- -	-	57.68
166	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 - 1,229.00	1,265.00	- -	03/2023	2.93
167	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
168	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,200.00	07/2012 -	03/2024	388.89
169	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 625.00	859.00	03/2016 -	06/2021	37.44
<u>Rail Vikas Nigam Ltd.</u>							
170	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 - 1,185.64	1,844.47	12/2017 -	-	55.57
171	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
172	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	396.00	03/2009 03/2009	-	91.30

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22
174	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62
175	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04
176	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARA AGAR TO BARRACK MORE AND DAKSHINESHVAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
178	VIJAYWADA-GUDUR AND PUNEMAVARA - NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,257.00	03/2020 -	03/2022	124.58
179	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	12/2021 -	12/2021	53.75
180	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	03/2021	35.42
181	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68
182	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15
183	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32
184	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98
185	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83
186	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2021	51.02
187	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08
188	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	03/2020 -	03/2021	281.93

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
189	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
190	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	12/2021	111.91
191	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,536.00	03/2019 -	06/2022	62.89
192	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	1,825.00	12/2020 -	12/2022	54.24
193	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>						
194	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
195	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2024	102.85
196	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86
197	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
198	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 - 2,288.70	2,643.25	03/2021 -	03/2025	15.49
199	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 - 704.31	927.94	03/2020 -	06/2021	31.75
200	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 - 164.36	1,050.00	02/2009 -	-	538.84
201	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,472.59	03/2000 -	03/2023	3,47,159.00
202	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2024	7.06
203	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 185.00	449.39	03/2022 -	12/2022	142.91

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>South East Central Railway</u>						
204	CHHINDWARA - NAGPUR (GC)(SECR) - [N220100324	04/2005	383.79 - 383.79	1,413.76	- -	08/2020	268.37
205	GONDIA-JABALPUR(GC),(SECR) - [N220100186	02/1997	511.86 - 1,756.00	2,005.25	04/2020 -	04/2021	291.76
206	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 - 2,753.05	3,524.81	03/2023 -	12/2023	84.69
207	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438	04/2010	585.93 - 585.93	1,268.32	02/2019 -	12/2021	116.46
208	WADSA-GADACHIROLI NEW LINE (2.36 KM) - [N22000480	06/2018	239.00 - 822.50	1,090.00	12/2021 -	12/2024	378.60
209	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 - 872.00	1,226.51	12/2019 -	10/2020	40.65
	<u>South Eastern Railway</u>						
210	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [N220100208	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
211	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 - 148.77	377.00	12/2016 -	08/2020	153.41
212	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
213	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
214	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 - 149.90	230.00	03/2015 -	-	53.44
215	BONDAMUNDA RANCHI DOUBLING - [N22000396	03/2016	1,724.20 - 1,724.20	1,993.24	03/2021 -	12/2023	15.60
216	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 - 1,966.70	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
217	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	1,801.01 - 1,801.01	1,967.00	- -	12/2023	9.22

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
218	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 - 558.00	692.43	- -	12/2023	24.09
219	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	466.65	- -	12/2023	57.65
220	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,432.50	- -	03/2025	17.95
221	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 - 146.75	167.50	- -	12/2023	14.14
222	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 - 327.25	367.77	- -	12/2023	12.38
223	HUBLI-ANKOLA(NL),SIP - [220100193]	04/1997	2,315.00 - 2,315.00	3,031.65	- -	12/2024	68.97
224	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,147.00	03/2020 -	06/2021	33.31
225	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	783.00	03/2020 -	01/2021	35.47
226	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,614.59	1,870.41	03/2019 -	03/2021	15.84
227	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 - 644.78	890.00	03/2017 -	-	38.03
<u>Southern Railway</u>							
228	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -AGASTIYAMPALLI - [N22000079]	09/2007	724.69 - 724.69	2,910.84	02/2019 -	03/2025	301.67
229	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,720.00	03/2020 -	03/2025	465.83
230	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
231	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	527.37	02/2019 -	-	247.32
232	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	2,300.00	- -	03/2024	339.33

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
233	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	1,500.00	- -	-	78.78
234	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 - 198.68	559.95	- -	03/2025	181.84
235	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 270.14	457.08	- -	12/2021	69.20
236	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 252.96	369.55	- -	-	46.09
237	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	1,140.00	- -	-	295.05
238	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	450.73	- -	09/2021	174.15
239	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	961.09	- -	02/2021	3.12
240	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 189.24	275.21	- -	-	45.43
241	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,172.16	03/2019 -	12/2027	1,699.64
242	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 - 187.26	332.00	04/2014 -	12/2020	77.29
243	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 828.00	1,246.00	- -	-	24.60
244	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	950.00	03/2005 -	09/2021	253.33
245	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	06/2022	102.11
<u>West Central Railway</u>							
246	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2023	585.35
247	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
<u>Western Railway</u>							

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
248	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95 196.95	202.35	03/2011 -	-	2.74
	Total		1,76,175.46 5,323.20 1,84,597.91	3,31,127.22			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
249	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00 227.00	247.95	- - -	-	9.23
250	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/00 OF NH 44A IN - [N24000306]	11/2010	64.41 - 64.41	99.67	03/2011 -	12/2020	58.98
251	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 - 193.69	327.92	10/2010 -	-	69.30
252	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 - 207.03	389.45	05/2012 -	-	88.11
253	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 - 258.97	268.92	08/2015 -	-	3.84
254	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 - 280.16	290.59	- - -	-	3.72
255	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00 348.00	348.43	09/2017 -	-	.12
256	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 - 445.89	653.29	03/2017 -	-	46.51
257	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 - 497.05	881.05	05/2017 -	04/2021	77.26
258	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 - 889.24	904.82	- - -	12/2020	1.75
259	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 - 470.20	630.36	02/2011 -	-	34.06
260	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 - 282.41	322.01	08/2016 -	-	14.02

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
261	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 - 954.43	1,191.51	09/2015 -	10/2021	24.84
262	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 - 358.22	377.64	10/2016 -	-	5.42
263	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 - 333.21	353.89	11/2015 -	-	6.21
264	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 - 218.31	307.47	02/2018 -	-	40.84
265	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH- 4 NEAR LAUNGTLI) - [N24000415]	08/2010	195.04 - 195.04	377.99	10/2010 -	06/2021	93.80
266	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 - 319.68	369.77	- -	-	15.67
267	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]	06/2016	157.30 157.00 157.00	157.30	06/2018 -	-	.19
268	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 - 460.73	461.00	- -	-	.06
269	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 - 237.80	238.00	11/2019 -	-	.08
270	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]	10/2015	333.21 - 333.21	355.89	12/2015 -	-	6.81
271	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	03/2018	297.12 294.00 294.00	294.12	07/2018 -	-	.04
272	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	03/2018	504.19 504.00 504.00	504.19	11/2018 -	01/2021	.04
273	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00 995.00	995.09	05/2016 -	04/2021	.01
274	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00 203.00	203.21	05/2019 -	-	.10
275	SHEGAON TO DEORI PHATA - [N24001010]	02/2017	373.10 373.00 373.00	373.10	05/2019 -	-	.03
276	MEHKAR TO CHIKALI - [N24001011]	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
277	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00 548.00	548.03	06/2019 -	-	.01
278	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00 391.00	391.06	06/2019 -	-	.02
279	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
280	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	-	40.76
281	SANGOLA TO JATH - [N24001052]	01/2018	257.38 277.00 277.00	257.38	12/2019 -	-	.15
282	TEMBHURNI PANDHARIPUR MANGALVELE DHAMARVADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
283	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	-	.05
284	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	-	.08
285	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	-	.24
286	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	-	.06
287	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	-	.12
288	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	-	.06
289	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	-	.08
290	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	-	.14
291	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	-	.01
292	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	-	.13

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
293	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	-	.07
294	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	-	.11
295	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	-	.01
296	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	-	.03
297	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	-	.06
298	JALGAON TO NANDURGA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	-	.47
299	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	-	.08
300	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	-	.02
301	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	-	.16
302	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	-	.08
303	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	-	26.19
304	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	-	2.47
305	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31
306	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	06/2021	.03
307	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01
308	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
309	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	-	.01
310	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00 215.00	215.16	09/2019 -	-	.07
311	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	03/2021	.13
312	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00 653.00	653.29	03/2017 -	-	.04
313	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001131]	08/2010	186.96 - 186.96	322.24	09/2014 -	12/2020	72.36
314	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 - 1,979.00	2,056.90	- - -	-	2.93
315	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00 543.73	544.00	09/2016 -	03/2021	.00
<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
316	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 - 373.07	387.00	08/2016 -	-	3.73
317	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
318	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]	10/2017	818.00 - 818.00	887.68	- - -	-	8.52
<u>National Highways Authority Of India</u>							
319	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 - 280.00	520.00	02/2009 -	-	85.71
320	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23
321	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95
322	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
323	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 - 160.00	167.98	05/2008 -	06/2019	4.99

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
324	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 - 196.00	655.17	07/2009 -	-	234.27
325	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 - 1,108.00	2,967.50	11/2011 -	-	167.82
326	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
327	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 - 217.61	360.84	04/2010 -	07/2019	65.82
328	NALBARI T BUNJI (AS-7) - [N24000048]	12/2003	208.00 - 208.00	230.00	04/2008 -	12/2020	10.58
329	4 LANNING OF MH-KN BORDER SANGA, FDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 - 1,266.60	1,514.00	09/2016 -	-	21.90
330	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
331	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
332	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 - 585.00	591.00	11/2013 -	01/2021	15.53
333	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 - 1,928.22	2,945.00	04/2015 -	03/2021	52.73
334	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 - 531.13	730.97	05/2018 -	06/2021	37.63
335	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 - 361.15	363.93	- -	-	.77
336	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 [N24000441]	10/2015	593.26 - 593.26	690.17	05/2018 -	06/2021	16.34
337	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
338	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) [N24000463]	12/2015	1,083.00 - 1,083.00	1,827.15	06/2018 -	-	68.71
339	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]	03/2015	794.30 - 679.94	691.38	- -	05/2020	-12.96

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
340	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	10/2021	1.37
341	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
342	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]	08/2015	322.09 - 247.00	322.09	04/2018 -	12/2020	.00
343	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 - 447.29	746.43	12/2017 -	-	66.88
344	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	-	6.11
345	MEERUT-BULANDSHAHAR - [N24000539]	01/2016	633.24 - 683.24	657.94	- -	-	44.60
346	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84
347	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	12/2020	7.53
348	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	2,587.50	09/2019 -	-	86.37
349	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 - 1,169.61	2,280.00	- -	-	94.94
350	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 - 323.72	336.60	08/2018 -	-	3.98
351	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82 - 1,239.82	1,727.66	- -	01/2021	39.35
352	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 - 950.69	1,108.00	08/2019 -	12/2020	16.55
353	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 - 1,100.19	1,145.31	- -	02/2021	4.10
354	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 - 290.73	315.00	- -	-	8.35
355	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 - 605.84	722.46	07/2018 -	-	19.25

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
356	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
357	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 - 744.64	982.00	03/2020 -	-	31.88
358	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	-	3.40
359	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 - 988.34	1,043.28	03/2020 -	08/2020	5.56
360	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 20.580) - [N24000659	03/2017	1,059.73 - 1,059.73	1,071.00	03/2020 -	11/2020	1.06
361	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,030.06 - 1,098.06	1,100.64	03/2020 -	-	5.70
362	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 - 754.54	756.27	03/2020 -	09/2021	.23
363	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 - 672.89	736.01	03/2020 -	-	9.38
364	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
365	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	06/2021	10.24
366	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
367	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54
368	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
369	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	03/2021	3.95
370	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	02/2021	1.78
371	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 - 1,124.11	1,232.76	09/2017 -	05/2021	9.67

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
372	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 - 404.94	448.18	- -	10/2020	10.68
373	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 - 273.46	276.17	- -	-	.99
374	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
375	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 - 1,995.34	2,400.00	- -	11/2021	20.28
376	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.34 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
377	REHABILITATION AND UPGRADE TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,211.98 - 1,261.98	1,052.20	- -	07/2021	54.69
378	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35
379	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
380	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 - 1,052.21	1,449.00	- -	01/2021	37.71
381	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 - 1,532.62	2,499.00	03/2021 -	04/2021	63.05
382	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 - 496.20	537.17	- -	-	8.26
383	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
384	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	07/2021	5.32
385	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	-	4.99
386	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
387	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 - 634.70	931.21	- -	07/2021	46.72

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
388	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 795.50	799.30	- -	07/2021	.48
389	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	-	25.68
390	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 - 743.88	743.89	- -	12/2021	.00
391	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	-	27.86
392	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN MP BORDER TO CDW - [N2400121	12/2017	217.96 - 217.96	884.00	- -	-	305.58
	Total		98,91.66 19,154.00 99,054.65	22,07.32			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
393	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00 431.00	431.16	06/2021 -	11/2021	.04
	<u>Department Of Telecommunication</u>						
394	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 - 13,334.00	24,664.00	07/2015 -	06/2021	84.97
	Total		13,765.16 431.00 13,765.00	25,095.16			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
395	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 - 10,773.00	12,787.00	12/2018 -	11/2022	18.69
	<u>Chennai Metro Rail Ltd</u>						
396	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 - 14,600.00	19,058.00	12/2015 -	-	30.53
	Total		25,373.00 .00 25,373.00	31,845.00			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>WATER RESOURCES</u>						
	<u>Uttar Pradesh Jal Nigam</u>						
397	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH [N30000021	01/2019	231.79 - 231.79	234.03	12/2021 -	12/2021	.97
	Total		231.79 .00 231.79	234.03			
	Grand Total		5,01,859.96 29,841.20 5,15,312.79	7,44,048.11			

FLASH REPORT

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
7	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
8	NEYVELI NEW THERMAL POWER PROJECT(2X100 MW)	NLC	06/2011	2/2015	5907.11	7980.79	2073.68
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
10	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
11	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	207.28	362.5	155.22
12	BALRAM EXPANSION OCP	MCL	12/2007	03/2010	172.08	646.01	473.93
13	GOPAL JI KANIHA OCP, MCL	MCL	12/2007	03/2013	457.77	684.32	226.55

COMMERCE AND INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	12579.09	13812.3	1233.21
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
16	AIIMS BILASPUR	NBCC	04/2018	09/2021	1351	1471	120
17	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD	03/2019	09/2025	1577	1828	251

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
HOME AFFAIRS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79
HUMAN RESOURCE DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	484.32	626.26	141.94
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	352.56	490.24	137.68
21	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
22	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
23	ENNORE THIRUVALLUR BENGALURU PRODUCER RY NAGAPATTINAI MADURAI TITUT COGN GAS PIPELINE	IOCL	05/2016	2/2018	4.97	6025	1528
24	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
25	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
26	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
27	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
28	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	694	1097.54	403.54
29	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
30	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1846.46	984.67
31	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
32	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
33	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	652.1	108.19
34	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
35	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM	HPCL	09/2017	06/2021	2677	3072	395

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	VIJAYAWADA TO DHARMAPURI AND CONST						
36	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
37	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
38	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
39	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
40	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978
41	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	15105.22	3466.67
42	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
43	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
44	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	07/2012	4824.12	5071.94	247.82
45	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9151.56	4397.14
46	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
47	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
48	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
49	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
50	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
51	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
52	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
53	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
54	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
55	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
56	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
57	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	9583	4230
58	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1592.34	210.5
59	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15389.42	1022.84
60	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13740.53	1208.09
61	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	9188.98	10016.1	827.12
62	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
63	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
64	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
65	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3500	2466.93
66	KOTLIPALLI-N. RASAPUR (NL) (SECR)	SECR	12/2001	3/2009	1045.2	2120.16	1074.96
67	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
68	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
69	RAMGANJMUHDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
70	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
71	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
72	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
73	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5521.45	3127.98
74	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
75	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2910.84	2186.15
76	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
77	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	396	262.59
78	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
79	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12264.15	7809.98
80	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
81	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	5071.38	3891.19
82	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
83	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1070	745.27
84	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
85	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
86	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4517.49	2245.99
87	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
88	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1959.74	1130
89	TIRUCHIRAPPALI-NALORE-KARAIKAL(SR) (GC)	SI	09/1995	3/2020	367.98	1720	1416.02
90	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	2315	3911.65	1596.65
91	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
92	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	2005.25	1493.39
93	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3472.59	1749.59
94	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
96	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
97	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
98	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
99	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1389.05	351.9
100	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	1868.89	320.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
101	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
102	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	872.65	228.27
103	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1500	524.38
104	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	395	148.92
105	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
106	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
107	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	1825	641.75
108	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1536	593.05
109	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96
110	VIZIANAGARAM -SAMBALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
111	DAUND-GULBAGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKA - ELECTRIFICATION (641.57 KM)	RVNL	03/2009	3/2020	713.48	2725	2011.52
112	RISHIKESH - KARNATAKA NEW LINE	RVNL	04/2011	12/2024	16.16	22716.11	6500.11
113	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1400	472.99
114	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
115	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1246	246
116	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	1724.2	1993.24	269.04
117	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
118	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	12/2021	602.27	760	157.73
119	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25
120	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68
121	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
122	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
123	OMALUR-METTURDAM- DOUBLINGWITH ELECTRIFICATION 28.93KM	SR	10/2013	04/2014	187.26	332	144.74

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
124	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
125	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
126	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
127	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
128	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
129	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
130	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
131	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	516.05	254.67
132	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	418.09	129.74
133	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
134	SULTANGANJ-LATURIA VIA ASARGANJ, FARPUR AND BELHAR	EL	04/2007	N.A.	150	1261.34	811.34
135	LAKSHMIKANTPUR-NAMKANA SUBSEQUENTLY MM FOR NAMKANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	EL	04/2007	03/2006	406.99	545.7	138.71
136	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2172.16	2051.46
137	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
138	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	800	486
139	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
140	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	750	335.16
141	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
142	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
143	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
144	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450.73	286.32
145	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
146	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	742	172.37

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
147	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
148	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	369.55	116.59
149	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
150	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	559.95	361.27
151	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
152	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2300	1776.48
153	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	527.37	375.53
154	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2042.51	244.51
155	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	480	266.99
156	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
157	SAKRI-NIRMALI AND DHANJHARPUR-LAUKAHABAZAI AND SAHARSA-FARBESGANJ (CC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
158	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	11	1006	795
159	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
160	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
161	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
162	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
163	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
164	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
165	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
166	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	525	282.91
167	AJMER-BANGURGRAM	NWR	04/2011	11/2019	213.39	375	161.61
168	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
169	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099	277

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
170	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	236.93	350.45	113.52
171	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
172	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
173	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
174	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
175	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
176	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
177	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
178	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3377	1873.29
179	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	NFR	02/1999	04/2010	380.6	1090.6	710
180	DABHOI-CHANOD (11.07KM) GC WITH EXTENSION UP TO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	3/2020	691.84	1017.91	326.07
181	JALANDHAR-PATTHANKOT-SAMMU TAJI	NI	03/2002	03/2016	25	859	234
182	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
183	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	890.76	339.25
184	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	890	245.22
185	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
186	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
187	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
188	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
189	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
190	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
191	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
192	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
193	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
194	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
195	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
196	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1536	776
197	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
198	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
199	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	449.39	329.66
200	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3524.81	1616.3
201	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
202	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
203	NANGALDAM-TILWARA (NL), NR	NR	03/1981	7/2012	150	2200	1750
204	DAUSA-GANGALUR CIVIL (NL), NWR	NWR	02/2007	02/2019	410.08	860.41	450.33
205	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
206	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6911.44	4584.92
207	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
208	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
209	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
210	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
211	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	783	205
212	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
213	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
214	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1147	286.57
215	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	780	180

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
216	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
217	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
218	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
219	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
220	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35
221	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
222	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	1967	165.99
223	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	315	130.94
224	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3000	873
225	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
226	HARIDWAR-LAI SAR	NR	04/2012	N.A.	219.83	346.63	126.8
227	BHADRACHALAI ROAD SANTTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
228	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	2643.25	354.55
229	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
230	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2432.5	370.2
231	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
232	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	663.13	120.95
233	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
234	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59
235	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	5912.4	2408.71
236	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
237	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	346	226
238	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	520	240
241	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
242	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
243	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	MORTH	12/2011	02/2012	156.63	276	119.37
244	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MORTH	03/2012	05/2012	207.03	389.45	182.42
245	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
246	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
247	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KAL DAN MULTI MO	MORTH	08/2010	09/2014	186.96	322.24	135.28
248	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.87 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653.29	207.4
249	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MORTH	04/2014	08/2017	279.7	398.52	118.82
250	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	MORTH	08/2014	11/2017	823.2	937.76	114.56
251	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	MORTH	08/2014	11/2017	600.87	720.97	120.1
252	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
253	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
254	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
255	SIX LANING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
256	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	MORTH	12/2010	01/2019	169.26	299	129.74
257	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	624.98	731.5	106.52
258	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
259	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
260	4-LANNING OF BODHRE-DHULE SECTION(KM	NHAI	03/2017	03/2020	744.64	982	237.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	390.000 TO 452.800)						
261	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
262	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
263	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
264	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	NHAI	09/2016	N.A.	1239.82	1727.66	487.84
265	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
266	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2587.5	1199.16
267	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
268	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
269	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
270	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
271	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.007) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
272	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
273	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	1952.2	690.22
274	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
275	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
276	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
277	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
278	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
279	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
280	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
281	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
282	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
283	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
284	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
285	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1827.15	744.15
286	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	730.97	199.84
287	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
288	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MORTH	11/2011	09/2015	954.43	1191.51	237.08
289	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	MORTH	11/2010	02/2011	470.2	630.36	160.16
290	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
291	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
292	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
293	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65.870	MORTH	11/2013	5/2017	497.05	881.05	384
294	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	MORTH	10/2010	3/2017	445.89	653.29	207.4
295	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
296	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
297	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
298	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
299	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
300	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
301	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
302	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
303	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
304	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
305	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2020)

STEEL							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
306	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415
TELECOMMUNICATIONS							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
307	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
308	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4720.73	456.73
309	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
310	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
311	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
312	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
WATER RESOURCES							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
313	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	12320	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	09/2021	11459	69
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	03/2023	380.87	12
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	06/2021	177.1	16
7	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	AAI	01/2018	08/2022	03/2023	1405	7
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2022	1142	12
9	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	10/2022	389.71	11
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	07/2019	12/2020	438.28	18
11	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	07/2021	456.86	10
12	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	06/2021	458	15
13	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT	AAI	11/2016	04/2020	05/2021	303.8	13
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2021	417.23	33
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	09/2022	2467	7
16	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	09/2022	1383	12

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
17	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	10/2021	304.13	55
18	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	12/2021	243	44
19	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
20	NORTH URIMARI EXPANSION OCP	CCL	03/2019	03/2023	03/2024	1553.06	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	PACHWARA SOUTH COAL BLOCK	NLC	07/2013	08/2022	09/2023	1795.01	13
22	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2022	869.44	12
23	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	04/2023	339.88	108
24	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	03/2022	1230.27	83
25	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	01/2021	5907.11	61
26	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2022	447.06	84
27	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	84
28	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2021	258.56	60
29	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2022	417.33	68
30	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2021	430.45	60
31	AMRAPALI OC EXP (12 MTY)	SCCL	02/2012	03/2020	03/2024	858.11	48
32	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
33	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2022	163.51	132
34	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2022	162.46	96
35	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
36	KISTARAM OCP	SCCL	11/2010	03/2015	03/2022	242.29	84
37	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2022	178.44	96
38	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	03/2025	1458.17	117
39	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
40	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2021	1055.05	36
41	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	84
42	MAGADH EXPANSION OC RPR	CCL	08/2008	07/2012	03/2025	706.4	152
43	BIJARI OC RCE (1.50 MTY)	SECL	05/2014	03/2020	03/2021	164.49	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
45	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2024	289.03	72
46	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2024	1375.38	36
47	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
48	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	02/2021	289.45	81
49	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2022	397.09	36
50	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
51	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
52	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2022	510.85	72
53	GOPAL JI KANIHA OCP, MCL	MCL	12/2007	03/2013	03/2028	457.77	180
54	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2008	03/2014	03/2021	321.5	84
55	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2031	490.1	168
56	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
57	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2022	479.53	108
58	BALRAM EXPANSION OCP	MCL	12/2007	03/2010	03/2029	172.08	228

COMMERCE AND INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
59	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	07/2021	4773	19
60	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	12579.09	22

CULTURE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
61	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	03/2021	151.33	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
62	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	06/2021	246.31	16

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
63	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	03/2021	426.72	11
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	NFL	01/2018	11/2019	03/2021	215.92	16
65	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	NFL	01/2018	11/2019	03/2021	239.81	16
66	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	NFL	01/2018	11/2019	02/2021	218.83	15

FINANC

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
67	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD	12/2015	10/2019	04/2021	209	18

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
68	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD	03/2016	03/2020	04/2022	195	19
69	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	01/2021	274.19	22
70	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	03/2021	272.19	24
71	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	03/2021	355.15	24
72	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	03/2021	414.11	88
73	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	03/2021	204.44	46
74	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	12/2020	152.95	34
75	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	12/2021	363.99	43
76	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
77	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	CPWD	09/2017	03/2020	12/2021	150.29	21
78	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	HITES	07/2016	04/2020	07/2021	785	15
79	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	HITES	07/2016	06/2020	07/2021	703	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
80	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	HITES	05/2017	05/2021	07/2022	875	14
81	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD	12/2018	06/2021	05/2022	260	11

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
82	DEVELOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	BHEL	08/2016	09/2019	12/2020	1554	15

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
83	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	09/2021	1219.21	23
84	NSG AT KOLKATA	CPWD	10/2014	04/2018	12/2020	162.88	32

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
85	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT THERMAL IGUDEN, J.P.	CPWD	01/2019	01/2020	03/2021	186	6
86	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	03/2020	10/2021	430	17
87	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	CPWD	11/2017	03/2020	06/2021	171.72	15
88	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE 1A AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD	07/2019	03/2021	06/2022	753.63	15
89	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD	07/2019	03/2022	09/2022	851	6
90	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	12/2020	270.83	73
91	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	06/2021	171.86	63
92	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	09/2021	496.18	51
93	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	01/2021	294	21
94	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	CPWD	01/2018	07/2020	06/2021	223.37	11
95	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	12/2020	484.32	75
96	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	CPWD	12/2016	07/2019	03/2021	549.31	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
97	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	NALCO	09/2017	06/2019	12/2020	166.62	18
98	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	12/2022	5540	20

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
99	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	07/2021	196.26	12
100	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	02/2022	598	24
101	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
102	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	12/2021	522	9
103	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	10/2021	163.02	18
104	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	09/2021	421	13
105	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND	IOCL	08/2017	06/2020	09/2021	236	15
106	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	11/2020	08/2021	466.43	10
107	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	HPCL	11/2017	11/2020	06/2021	255	7
108	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
109	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15
110	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
111	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	09/2021	206.5	6
112	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	08/2021	206.63	18
113	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	11/2021	255.4	15
114	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	02/2022	199.36	16
115	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2021	906	20
116	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	04/2021	543.91	14
117	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	IOCL	03/2018	12/2021	08/2022	676	8
118	BS VI PROJECT AT GUWAHATI REFINERY	IOCL	08/2018	02/2020	06/2021	557	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
119	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	04/2022	1636	20
120	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	IOCL	06/2016	08/2019	06/2021	423	22
121	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2021	650.82	26
122	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
123	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	08/2021	02/2022	1945	6
124	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	08/2021	4497	32
125	BSVI UPGRADATION	MANGALORE REFINERY	09/2016	12/2019	07/2021	1810	19
126	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	04/2021	571.66	16
127	MMPL PIPELINE REROUTING PROJECT	BPCL	04/2013	12/2019	02/2021	449.58	14
128	MOTOR SPIRIT PROJECT (MSBP) TO PRODUCE BSVI S AT KOCHI REFINERY	BPCL	02/2010	06/2020	02/2021	3313	12
129	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	07/2018	07/2021	4588.29	29
130	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	03/2021	327.78	35
131	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
132	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
133	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
134	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1933	12
135	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2021	2433	6
136	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	3437	12
137	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1740	12
138	PIPELINE NETWORK PROJECT GELEKI, ASSAM	ONGC	07/2016	05/2020	05/2021	249.85	12
139	BS-VI PROJECTS	CPCL	09/2017	12/2019	01/2021	1858	13
140	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
141	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2021	3190.69	37
142	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	06/2021	160.1	16
143	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	03/2022	161.59	27
144	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
145	AUGMENTATION OF CTMPL	IOCL	12/2016	06/2020	11/2021	228	17
146	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	06/2021	581	15
147	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2021	352.56	48
148	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	53
149	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	08/2021	1823	8
150	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	02/2021	690	31
151	CONVERSION OF RIG S GAR SAIRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPU)	ONGC	07/2011	07/2013	03/2021	861.79	94
152	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
153	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	12/2021	225.54	10
154	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	03/2022	909	14
155	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	05/2021	286.42	9
156	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	07/2022	278.6	13
157	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	03/2021	224.75	7
158	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
159	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	09/2024	18668	18
160	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2021	808.63	38
161	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	01/2021	454.11	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
162	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	PGCIL	05/2016	11/2019	03/2021	14733.37	16
163	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	03/2021	322.3	25
164	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	03/2021	235.53	21
165	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	03/2021	379.95	15
166	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	PGCIL	02/2017	04/2020	02/2021	5070.13	10
167	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2021	4754.42	36
168	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	36
169	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	02/2021	358.83	9
170	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	CPWD	10/2017	11/2019	03/2021	271.9	16
171	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
172	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	01/2016	03/2021	374.63	59
173	EASTERN REGION STRENGTHENING SCHEME XII	PGCIL	02/2014	11/2016	07/2021	522.29	51
174	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	117
175	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
176	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	03/2021	9188.98	20
177	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	03/2021	12532.44	27
178	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	14366.58	40
179	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	63
180	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	03/2021	186.17	20
181	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	01/2021	445.89	23
182	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	03/2021	1931.39	13
183	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	07/2021	12964.6	38
184	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	01/2021	9750.89	47

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
185	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2022	3919.59	150
186	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
187	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	01/2021	4824.12	99
188	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	02/2021	11638.55	37
189	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	01/2021	871.62	39
190	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	03/2021	197.4	36
191	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2021	1394.52	49
192	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	03/2021	5353	104
193	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	126
194	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	01/2021	2496.9	133
195	BARH STPP(3X60MW) TPC	NTPC	01/2005	11/2011	04/2022	8692.97	126
196	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	03/2022	10598.98	16
197	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
198	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	02/2021	3500	7
199	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
200	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	BITES	02/2016	03/2020	06/2021	393.98	15
201	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625	63
202	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2021	3055	39
203	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
204	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	12/2020	691.84	9
205	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	06/2024	2288	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
206	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
207	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	12
208	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
209	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	03/2024	5200	48
210	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2021	528.57	24
211	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
212	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	12/2020	305	21
213	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	CCOI	01/2013	03/2018	03/2021	387.7	36
214	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2021	346.32	24
215	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
216	BONGAIGAON-GOALPARA GUWAHATI (170 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
217	SURENDRA NAGA RAJKOT	WR	01/2015	03/2021	12/2022	1002.39	21
218	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
219	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	21
220	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33
221	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
222	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
223	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2021	927.01	27
224	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
225	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
226	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
227	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
228	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
229	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	03/2023	1491.47	36
230	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2023	1763.93	36
231	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
232	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
233	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
234	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	12
235	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2025	1640.04	36
236	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	48
237	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	03/2022	1037.15	12
238	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
239	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTS RGARH UDAIPUR	NWR	04/2010	06/2020	06/2021	420.18	15
240	AJMER-BANGURGA	NWR	04/2011	12/2019	07/2021	213.39	16
241	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
242	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2021	258.2	30
243	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.2	180
244	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
245	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
246	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.6	24
247	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
248	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
249	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
250	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
251	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	117

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
252	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	05/2021	477.88	110
253	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2025	1160.48	180
254	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
255	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	24
256	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
257	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
258	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28
259	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
260	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	12
261	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
262	NEW ALIPUR TO ANDA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSA IVPUR AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
263	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
264	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
265	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
266	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
267	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
268	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287	114
269	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
270	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2025	2288.7	48
271	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	15
272	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2132.77	120
273	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
274	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
275	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
276	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	216
277	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
278	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	128
279	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	02/2021	1180.19	146
280	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	204
281	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2023	4454.17	144
282	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2021	495.74	102
283	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.2	48
284	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
285	NEW LINE FROM DIMPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2022	2326.52	96
286	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2021	5300	84
287	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2023	1339.48	87
288	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	11/2021	410.08	33
289	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140
290	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500	241
291	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
292	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
293	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
294	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	04/2021	511.86	12
295	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
296	TIRUCHIRAPPALI-NAGORE- KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
297	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2023	318.24	132
298	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	12/2023	829.74	45
299	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
300	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	34
301	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
302	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
303	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2022	155.81	24
304	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	11/2021	1156.94	20
305	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
306	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	15
307	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	01/2021	578	10
308	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
309	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	02/2021	678.54	23
310	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
311	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	06/2021	4874.58	63
312	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	02/2021	246.08	14
313	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548	36
314	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2023	1798	48
315	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	24
316	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	03/2023	414.84	36
317	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	01/2021	314	22
318	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	69
319	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
320	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
321	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
322	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631	24
323	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	12/2020	187.26	80
324	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
325	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	2499.71	24
326	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
327	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	64
328	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63
329	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -FLECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2021	713.48	12
330	VIZIANAGARAM - SAMBALPUR 3RD LINE	RVNL	01/1991	11/2004	12/2026	2335.67	24
331	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	21
332	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2021	1402.02	21
333	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
334	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
335	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	12
336	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
337	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	03/2021	622.5	47
338	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
339	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	24
340	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
341	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	36
342	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
343	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
344	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
345	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
346	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	9
347	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	34
348	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	198
349	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
350	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760	27
351	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	12/2021	213	68
352	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
353	BHILDI-VIRAMGAON GAUGE CONVERSION INCLUDING GC OF MAHESANA- VIRAMGAON HILL AS MATERIAL MODIFICATION	WR	02/1991	01/2009	10/2021	551.51	31

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
354	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE	NHAI	03/2019	05/2020	05/2022	1047	24
355	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	04/2022	847	25
356	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	12/2021	990.97	24
357	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	03/2021	188.8	22
358	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	MoRTH	03/2017	01/2018	03/2021	423.79	38
359	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	12/2020	624.98	50
360	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MoRTH	11/2015	06/2017	02/2021	335.32	44
361	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	MoRTH	01/2016	05/2016	12/2020	386.09	55
362	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MoRTH	01/2016	08/2016	07/2021	348.95	59

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
363	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	05/2021	263.45	44
364	REHABILITATION AND UPGRADE OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MoRTH	01/2017	01/2018	12/2020	576.48	35
365	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	MoRTH	05/2014	08/2016	12/2020	199.98	52
366	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	MoRTH	03/2016	12/2019	12/2020	536.65	12
367	BARASGAON TO RAHATEE	MoRTH	07/2016	09/2018	04/2021	289.11	31
368	REHABILITATION AND UPGRADE OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	MoRTH	03/2016	01/2020	03/2021	240.3	14
369	REHABILITATION AND UPGRADE OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	MoRTH	03/2016	05/2019	12/2020	249.5	19
370	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	12/2020	624.41	117
371	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	06/2021	193.69	128
372	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	MoRTH	04/2013	08/2013	12/2020	166.27	88
373	CONSTRUCTION OF 2-LANE MELI MAIPUR NAMCHI ROAD IN SOUTH SIKKIM	MoRTH	07/2013	07/2013	12/2020	182.28	94
374	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2021	195.04	128
375	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
376	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	02/2021	1176.37	42
377	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
378	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	02/2021	639.97	40
379	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	44
380	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	NHAI	09/2017	09/2017	12/2020	374.4	39
381	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	01/2021	990.61	40
382	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	09/2021	1227.87	48
383	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	12/2020	454.89	31
384	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
385	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM.	NHIDCL	06/2015	06/2018	12/2021	463.49	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	535.250(DSIGN KM 490.800 TO KM 5						
386	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	04/2021	497.05	47
387	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	03/2021	628.45	14
388	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	04/2021	957.54	14
389	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	06/2021	511.83	46
390	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	04/2021	294.17	63
391	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	73
392	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	MoRTH	01/2012	04/2015	03/2021	410.72	71
393	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	05/2021	374	96
394	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	01/2021	511.54	86
395	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	03/2021	1724.55	96
396	VARANASI-AURA SARAD KM.786 TO KM.978.40	NHAI	03/2011	01/2014	12/2022	2848	105
397	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	05/2021	1078.84	93
398	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	12/2021	998.79	100
399	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2021	1047	81
400	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2020	291.36	83
401	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	03/2021	1928.22	71
402	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	09/2021	2128.72	29
403	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
404	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	MoRTH	04/2013	08/2013	12/2020	151.59	88
405	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2020	208	152
406	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2020	478.51	86
407	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	12/2020	351.34	59
408	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073	NHAI	10/2015	05/2018	06/2021	531.13	37

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	OF NH4B AND FROM 5.300 TO KM 7.422 (						
409	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2021	593.26	37
410	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	12/2021	649.5	33
411	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	06/2021	505	37
412	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	12/2020	1083	30
413	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
414	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	01/2021	1423.96	26
415	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	12/2020	322.09	32
416	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36
417	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	12/2020	707.82	28
418	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM. 70.25 TO 96.714 OF NH- 7 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	12/2020	641.17	29
419	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2021	546	29
420	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2021	591.66	29
421	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	03/2021	804.97	33
422	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	NHAI	08/2016	04/2020	12/2020	1664.2	8
423	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	12/2021	1167.42	33
424	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	03/2021	2510.04	19
425	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16
426	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	02/2021	400.25	23
427	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	03/2021	446.17	24
428	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	02/2021	848.45	11
429	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	09/2021	754.54	18
430	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	NHAI	03/2017	03/2020	12/2020	1989	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
431	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
432	REHABILITATION AND UPGRADE BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	15
433	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
434	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
435	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	02/2021	168.32	46
436	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
437	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	02/2021	216.71	46
438	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46
439	SIX-LANING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	03/2021	894	11
440	4-LANING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
441	4-LANING OF JORDANAR DWARKA SECTION IN THE STATE OF GUJ. RAT	NHAI	06/2017	06/2020	02/2021	1958.88	8
442	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	05/2022	339.57	46
443	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
444	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
445	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	NHIDCL	03/2018	09/2018	12/2021	315.03	39
446	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	NHIDCL	03/2018	09/2018	12/2021	240.64	39
447	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	11/2021	215.12	38
448	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2021	215.79	39
449	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
450	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	NHIDCL	03/2018	09/2018	11/2022	323.98	50
451	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	03/2021	279.44	36
452	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	06/2021	373.82	21
453	REHABILITATION AND UPGRADE OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	05/2021	809.16	34

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
454	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	03/2021	877.79	21
455	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	MoRTH	01/2017	03/2019	02/2021	247.25	23
456	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	MoRTH	03/2018	07/2020	08/2021	322.48	13
457	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	MoRTH	03/2018	08/2020	08/2021	293.1	12
458	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	12/2020	1069.59	14
459	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	05/2021	170.57	6
460	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
461	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	02/2021	162.56	35
462	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2021	166.21	31
463	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	04/2021	169.63	37
464	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF NADAKUM R-ONTAICHAN	MoRTH	01/2017	06/2019	05/2021	396.86	20
465	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	MoRTH	11/2017	02/2018	02/2021	235.91	36
466	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	12/2021	426.18	15
467	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	02/2021	184.62	36
468	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	MoRTH	03/2018	11/2019	01/2021	191.21	14
469	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	11/2022	160.27	39
470	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	12/2021	236.78	28
471	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	06/2021	205.05	51
472	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	09/2021	214.69	42
473	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2021	217.22	31
474	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	03/2021	233.04	36
475	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	03/2021	249.05	32
476	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2021	254.17	37

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
477	REHABILITATION AND UPGRADE OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MoRTH	03/2018	08/2018	03/2021	228.32	31
478	REHABILITATION AND UPGRADE OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MoRTH	03/2018	08/2018	02/2021	289.67	30
479	REHABILITATION AND UPGRADE OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	MoRTH	03/2018	11/2018	01/2021	504.19	26
480	REHABILITATION AND UPGRADE OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	MoRTH	03/2016	05/2016	04/2021	995.09	59
481	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	MoRTH	11/2017	04/2018	03/2021	163.95	35
482	UPGRADE TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	06/2018	04/2021	370.3	34
483	UPGRADE TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	05/2018	06/2021	341.79	37
484	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MoRTH	08/2016	01/2017	12/2020	350.61	47
485	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	06/2021	392.33	39
486	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - ADEROLA SECTION	MoRTH	02/2017	05/2019	05/2021	157.32	24
487	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIDAM TALUK SUPPORT KALADIN MULI	MoRTH	03/2018	01/2019	12/2020	186.96	75
488	REHABILITATION AND UPGRADE OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	MoRTH	07/2016	10/2019	12/2020	208.88	14
489	REHABILITATION AND UPGRADE OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MoRTH	03/2018	04/2020	04/2021	263.89	12
490	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J	MoRTH	03/2018	08/2020	03/2021	288.3	7
491	REHABILITATION AND UPGRADE OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MoRTH	01/2016	08/2016	03/2021	497.14	55
492	REHABILITATION AND UPGRADE OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MoRTH	01/2016	09/2016	03/2021	476.2	54
493	REHABILITATION AND UPGRADE OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	03/2021	452.94	56
494	REHABILITATION AND UPGRADE OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	03/2021	496.02	72
495	UPGRADE AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	03/2021	379.16	40

RURAL DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
496	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	02/2021	149.73	62
497	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	03/2021	175.49	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
498	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSC	12/2007	12/2016	03/2021	202.61	51

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
499	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	SAIL	12/2018	09/2020	05/2021	263.36	8
500	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2021	1034.01	50
501	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2021	15525	74
502	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	02/2021	1154.18	38
503	FORGED WHEEL PLANT	RINL	04/2014	09/2018	02/2021	1682.85	29
504	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	05/2021	262.87	23
505	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	12/2020	2858	36

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
506	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD	10/2016	03/2018	12/2020	248.2	33
507	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2021	13334	71

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
508	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	DMRC	05/2017	12/2020	09/2021	565	9
509	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2021	197.33	26
510	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	12/2020	884.3	60
511	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	03/2021	38585	60
512	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	CMRL	06/2016	03/2018	12/2020	3770	33
513	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	CPWD	11/2017	05/2020	02/2021	238.56	9
514	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	11/2022	10773	47
515	REDEVELOPMENT OF GENERAL POOL	CPWD	10/2016	08/2020	12/2021	392	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N						

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
516	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	KMDA	12/2014	04/2020	12/2020	272.32	8
517	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	KMDA	02/2014	12/2019	12/2020	274.76	12
518	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	BUIDCO	04/2015	04/2020	12/2020	184.93	8
519	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	12/2020	225.77	9
520	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
521	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
522	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	06/2022	298.12	11
523	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	UPJalNigam	02/2011	12/2019	12/2020	279.91	12
524	REHABILITATION AND UPGRADATION OF KONDLI PHASE STP 45 MLD PHASE II STP 114 MLD AND PHASE III STP	DJB	05/2016	07/2022	12/2022	239.11	10
525	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12
526	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR	UPJalNigam	12/2018	08/2021	06/2022	857.26	10
527	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	UPJalNigam	02/2017	11/2019	12/2020	161.31	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2020)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	1,2320.00	1,7079.00	4759	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	09/2021	1,1459.00	1,6580.00	5121	69
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	349.28	186.52	84
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	01/2021	5907.11	7980.79	2073.68	61
6	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	459.49	307.06	84
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144
8	GOPAL JI KANIHA OCP, CL	MCL	12/2007	03/2012	03/2018	157.77	634.32	226.55	180
9	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	362.50	155.22	108
10	BALRAM EXPANSION OCP	MCL	12/2007	03/2010	03/2029	172.08	646.01	473.93	228

COMMERCE AND INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
11	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	07/2021	4773.00	5178.00	405	19
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	1,2579.09	1,3812.30	1233.21	22

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	09/2021	1219.21	2000.00	780.79	23

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

619

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2020)

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
14	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	12/2020	484.32	626.26	141.94	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14
16	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	04/2021	543.91	652.10	108.19	14
17	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
18	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677.00	3072.00	395	14
19	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	08/2021	4497.00	6025.00	1528	32
20	IRUGUR-DEVANGONM PO PIPELINE	BPCL	11/2012	07/2017	08/2022	678.00	1472.00	794	66
21	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2021	3190.69	3375.90	185.21	37
22	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	5909.00	2994	110
23	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2021	352.56	490.24	137.68	48
24	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	714.25	107.19	53
25	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	08/2021	1823.00	3027.90	1204.9	8
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2021	861.79	1846.46	984.67	94
27	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	01/2021	4588.29	5245.96	657.67	29
28	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

620

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2020)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	6700.00	1588.67	36
30	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2021	4754.42	9151.56	4397.14	36
31	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	01/2021	2496.90	7927.34	5430.44	133
32	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	1592.34	210.5	63
33	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2022	3919.59	9897.59	5978	150
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
35	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	01/2021	4824.12	5071.94	247.82	99
36	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	02/2021	1,1638.55	1,5105.22	3466.67	37
37	NORTH- EAST NORTH WESTERN INTERCONNECTOR PROJECT	PGCIL	02/2009	01/2013	03/2022	1,1139.19	1,4719.10	3588.91	103
38	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	5867.38	2888.9	117
39	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	03/2021	9188.98	1,0016.10	827.12	20
40	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	03/2021	1,2532.44	1,3740.53	1208.09	27
41	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	1,4366.58	1,5389.42	1022.84	40
42	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	07/2021	1,2964.60	1,7304.00	4339.4	38
43	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	01/2021	9750.89	1,2176.28	2425.39	47
44	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	03/2021	5353.00	9583.00	4230	104
45	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	3860.35	1368.77	126
46	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	04/2022	8692.97	2,1312.11	12619.1	126

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

621

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	12/2020	691.84	1017.91	326.07	9
48	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	06/2024	2288.00	4970.11	2682.11	27
49	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33
50	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	1185.73	454.09	15
51	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	1540.13	1211.99	24
52	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.20	1993.24	269.04	33
53	BANKURA DAMODAR VALLEY RAIL LINE 96 KM GC WITH 6 MS FOR NL	SER	04/1998	07/2003	03/2009	1077.40	2373.00	1345.6	324
54	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2021	927.01	1400.00	472.99	27
55	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2021	713.48	2725.00	2011.52	12
56	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
57	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	2009.00	1060.96	21
58	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1536.00	593.05	39
59	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	1825.00	641.75	24
60	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	1835.83	349.98	12
61	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
62	NEW WORK FOR CONSTRUCTION OF	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

622

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)								
63	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3472.59	1749.59	276
64	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	04/2021	511.86	2005.25	1493.39	12
65	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2025	303.98	1720.00	1416.02	60
66	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	12/2023	829.74	1959.74	1130	45
67	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	3377.00	1873.29	24
68	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	1539.28	427.29	34
69	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
70	NADIKUDE-SRI KAHAST	SCR	04/2011	03/2021	03/2025	2239.70	2643.25	354.55	48
71	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	927.94	223.63	15
72	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4517.49	2245.99	24
73	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	2980.41	2484.97	216
74	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
75	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	1070.00	745.27	128
76	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	02/2021	1180.19	5071.38	3891.19	146
77	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	3791.66	868.53	204
78	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2023	4454.17	1,2264.15	7809.98	144
79	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.20	2120.16	1074.96	180

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

623

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
80	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
81	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
82	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
83	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
84	TALCHER-BIMALAGARH(NL) (ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
85	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	2910.84	2186.15	73
86	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	5521.45	3127.98	117
87	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) AN ECOR	ECOR	04/1996	03/2012	05/2021	177.00	751.55	273.67	110
88	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
89	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	5912.40	2408.71	24
90	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	1377.48	584.59	24
91	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	663.13	120.95	12
92	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
93	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287.00	893.45	606.45	114
94	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2021	495.74	734.01	238.27	102
95	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.20	1532.00	1146.8	48
96	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

624

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
97	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2023	2326.52	6911.44	4584.92	96
98	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2023	1339.48	8600.00	7260.52	87
99	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	11/2021	410.08	860.41	450.33	33
100	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450.00	2200.00	1750	140
101	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500.00	2,7949.00	25449	241
102	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2021	258.20	358.68	100.48	30
103	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548.00	819.01	271.01	36
104	NEW BONGAIGAON-RANGTA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2023	1798.00	2042.51	244.51	48
105	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	369.53	742.00	172.37	24
106	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	03/2023	414.84	750.00	335.16	36
107	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	01/2021	314.00	800.00	486	22
108	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	950.00	317.32	69
109	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2172.16	2051.46	105
110	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600.00	780.00	180	25
111	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	1147.00	286.57	15
112	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	01/2021	578.00	783.00	205	10
113	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

625

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
114	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	477.31	182.31	37
115	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
116	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	02/2021	246.08	395.00	148.92	14
117	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	1378.11	1057.45	48
118	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	03/2022	1037.15	1389.05	351.9	12
119	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
120	AJMER-BANGURGRAM	NWR	04/2011	11/2019	03/2021	213.39	375.00	161.61	16
121	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KANAKPUR-BUDAKHALI AND CHANDRANAGAR	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
122	PIRAPINTI-JASIDHUR	ER	04/2013	03/2022	03/2025	935.70	2137.81	1221.83	36
123	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
124	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631.00	3887.48	256.48	24
125	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	12/2020	187.26	332.00	144.74	80
126	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	810.02	108.41	64
127	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
128	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	1312.96	343.13	21
129	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	1247.64	665.51	12
130	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3524.81	1616.3	9
131	MANMAD-PARBHANI-NANDED-	SCR	04/2017	03/2022	12/2022	119.73	449.39	329.66	9

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

626

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
132	SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	1268.32	682.39	34
133	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	950.00	681.13	198
134	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760.00	1536.00	776	27
135	SAGAUJI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	1215.54	471.5	36
136	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
137	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	890.76	339.25	31
138	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625.00	859.00	234	63

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
139	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	12/2020	624.98	731.50	106.52	50
140	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	1420.00	131.93	15
141	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2021	531.13	730.97	199.84	37
142	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	12/2020	1083.00	1827.15	744.15	30
143	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2020	291.36	469.31	177.95	83
144	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MORTH	11/2011	09/2015	10/2021	954.43	1191.51	237.08	73
145	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	12/2020	624.41	992.67	368.26	117
146	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	06/2021	193.69	327.92	134.23	128
147	CONSTRUCTION OF A NEW 2-LANE	MORTH	08/2010	10/2010	06/2021	195.04	377.99	182.95	128

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

627

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)								
148	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	1232.76	108.65	44
149	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MORTH	11/2013	05/2017	04/2021	497.05	881.05	384	47
150	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105
151	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	03/2021	1928.22	2945.00	1016.78	71
152	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	1108.00	157.31	16
153	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	12/2020	186.96	322.24	135.28	75

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
154	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	07/2015	07/2021	1,5525.00	2,1940.00	6415	74

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
155	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2021	1,3334.00	2,4664.00	11330	71

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
156	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	11/2022	1,0773.00	1,2787.00	2014	47

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
157	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

628

TOR -> Time Overrun

Details of Central Sector Projects Costing Rs.150 crore and above (as on 31.12.2020)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	ARUNACHAL PRADESH				
	Power				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (1/2021) [1/2021]	2,496.90 (7,927.34) [7,927.34]	8,151.00 (5,430.44) [133]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	12,855.18 (13,707.10) [155]
	Road Transport And Highways				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	125.55 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	376.15 (0.00) [0]
5	2 LANING FROM PASICHAH TO PAUNGU SECTION OF NH-229 FROM KM 41. TO KM 58.42 (EXISTING KM 4 TO KM 59	3/2015	5/2018 (-) [0/0]	194.21 (-) [194.11]	196.23 (0.00) [0]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	199.53 (0.00) [0]
7	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	135.60 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	187.33 (0.00) [0]
9	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	149.45 (0.00) [0]
10	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	160.05 (0.00) [0]
11	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	184.51 (0.00) [0]
12	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	105.37 (0.00) [0]
13	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	220.29 (0.00) [0]
14	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	88.62 (0.00) [0]
15	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]

16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	160.24
			(-)	(-)	(0.00)
			[0/0]	[245.79]	[0]
17	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016	198.00	184.62
			(-)	(-)	(0.00)
			[0/0]	[198.00]	[0]
18	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018	197.16	89.41
			(9/2015)	(197.16)	(0.00)
			[9/2018]	[197.16]	[0]
19	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	303.02
			(-)	(-)	(0.00)
			[0/0]	[1,718.59]	[0]
20	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017	1,253.10	204.77
			(-)	(-)	(0.00)
			[3/2022]	[1,253.10]	[60]
21	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017	167.28	22.06
			(-)	(-)	(0.00)
			[2/2021]	[167.28]	[46]
22	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017	216.71	26.84
			(-)	(-)	(0.00)
			[2/2021]	[216.71]	[46]
23	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-)	(-)	(0.00)
			[0/0]	[392.60]	[0]
24	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	172.89
			(-)	(-)	(0.00)
			[12/2020]	[434.06]	[-]
25	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	127.41
			(3/2018)	(284.09)	(0.00)
			[3/2021]	[284.09]	[47]
26	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	94.62
			(-)	(-)	(0.00)
			[0/0]	[195.23]	[0]
27	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	106.52
			(-)	(-)	(0.00)
			[0/0]	[203.36]	[0]
28	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	98.24
			(-)	(-)	(0.00)
			[0/0]	[194.66]	[0]
29	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	98.23
			(-)	(-)	(0.00)
			[0/0]	[198.22]	[0]
30	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012	207.03	349.94
			(6/2018)	(-)	(182.42)
			[0/0]	[389.45]	[0]
31	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017	180.57	44.85
			(-)	(-)	(0.00)
			[2/2021]	[180.57]	[46]
32	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017	168.32	43.28
			(-)	(-)	(0.00)
			[2/2021]	[168.32]	[46]
33	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012	156.63	0.00
			(-)	(276.00)	(119.37)
			[0/0]	[276.00]	[0]
34	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011	305.49	131.08
			(-)	(-)	(0.00)
			[0/0]	[305.49]	[0]
35	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/	256.66	24.14
			(-)	(-)	(0.00)
			[0/0]	[256.66]	[0]
36	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713)	2/2017	/	175.06	62.27

	FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0		(-) [4/2022]	(-) [175.06]	(0.00) [-]
37	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/	176.12	54.56
			(-) [4/2022]	(-) [176.12]	(0.00) [-]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/	199.02	14.21
			(-) [2/2021]	(-) [199.02]	(0.00) [-]
39	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/	184.88	6.85
			(-) [2/2021]	(-) [184.88]	(0.00) [-]
40	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/	1,979.00	1,217.25
			(3/2020) [0/0]	(-) [2,036.90]	(57.90) [0]
	ASSAM				
	Civil Aviation				
41	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021	1,142.00	323.90
			(-) [3/2022]	(1,232.00) [1,232.00]	(90.00) [12]
	Health And Family Welfare				
42	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021	875.00	279.76
			(-) [7/2022]	(-) [747.80]	(-127.20) [14]
43	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	163.37
			(-) [3/2018]	(-) [175.57]	(0.00) [0]
	Petroleum				
44	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	467.19
			(6/2021) [6/2021]	(-) [557.00]	(0.00) [16]
45	CONSTRUCTION OF 302 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGG, MADHUBAI	6/2016	8/2020	224.75	148.44
			(-) [3/2021]	(-) [222.21]	(-2.54) [7]
46	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019	350.00	2.06
			(-) [0/0]	(-) [350.00]	(0.00) [0]
47	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019	423.00	399.01
			(6/2021) [6/2021]	(-) [502.00]	(79.00) [22]
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020	543.91	130.10
			(-) [4/2021]	(638.60) [652.10]	(108.19) [14]
49	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024	12,366.00	168.82
			(-) [10/2024]	(-) [12,366.00]	(0.00) [0]
50	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024	10,228.00	117.34
			(-) [10/2024]	(-) [10,228.00]	(0.00) [0]
51	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020	249.85	170.85
			(5/2021) [5/2021]	(303.75) [303.75]	(53.90) [12]
	Railways				
52	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019	314.00	777.27
			(-) [1/2021]	(-) [800.00]	(486.00) [22]
53	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022	2,232.32	1,375.36
			(-) [3/2023]	(-) [2,950.00]	(717.68) [12]
54	DIGARU-HOJAI (102 KM)	4/2015	3/2021	870.96	1,007.06
			(-) [5/2021]	(-) [1,873.21]	(1,002.25) [2]

55	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (1,105.00) [1,532.00]	770.73 (1,146.80) [48]
Road Transport And Highways					
56	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	267.46 (0.00) [0]
57	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
58	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
59	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
60	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	126.13 (0.00) [0]
61	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	460.01 (0.00) [0]
62	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	55.03 (0.00) [0]
63	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	80.88 (-28.50) [0]
64	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.00 (DESIGN KM 433.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.50]	56.22 (-30.09) [42]
65	4 LANING OF NH- 7 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [4/2021]	294.7 (-) [294.17]	170.00 (0.00) [63]
66	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (-) [12/2020]	166.94 (-) [166.94]	0.00 (0.00) [0]
67	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	488.05 (143.23) [0]
68	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [0/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
69	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	230.89 (7.98) [0]
70	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
71	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	114.16 (0.00) [0]
72	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [887.68]	178.47 (69.68) [0]
73	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	103.86 (-65.43) [42]
74	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	372.69 (0.00) [0]

75	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	239.35 (0.00) [31]
76	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
77	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
78	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
79	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
80	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
81	NALBARI TO BIJNI (AS-7)	12/2003	4/2008 (-) [12/2020]	208.00 (-) [230.00]	355.20 (22.00) [152]
82	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	347.28 (0.00) [0]
83	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [273.40]	115.65 (-776.11) [0]
84	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	231.82 (-70.66) [0]
85	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.21 (-) [307.47]	292.55 (89.16) [0]
86	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	57.16 (0.00) [0]
MANIPUR					
Power					
87	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
Railways					
88	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2023]	4,454.17 (-) [12,264.15]	10,584.54 (7,809.98) [144]
Road Transport And Highways					
89	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	158.59 (0.00) [0]
90	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	151.85 (-59.80) [36]
MEGHALAYA					
Culture Development					
91	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	144.00 (0.00) [42]
Health And Family Welfare					
92	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	227.35 (0.00) [43]

	Human Resource Development				
93	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [12/2020]	484.32 (-) [626.26]	0.00 (141.94) [75]
	Railways				
94	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [4,083.02]	263.67 (3,176.56) [0]
	Road Transport And Highways				
95	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	83.90 (0.00) [0]
96	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
97	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	88.81 (0.00) [-]
	MIZORAM				
	Railways				
98	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [12/2023]	2,393.47 (-) [5,521.45]	3,781.94 (3,127.98) [117]
	Road Transport And Highways				
99	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2021) [6/2021]	195.04 (-) [377.99]	325.42 (182.95) [128]
100	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2020) [12/2020]	186.96 (-) [322.21]	292.10 (135.28) [75]
101	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (5/2016) [6/2021]	182.09 (-) [327.92]	295.96 (134.23) [128]
102	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	519.09 (-) [519.09]	65.01 (0.00) [0]
103	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	640.07 (-) [640.07]	15.79 (0.00) [0]
104	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	642.96 (-) [642.96]	22.97 (0.00) [0]
105	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (10/2020) [0/0]	404.29 (-) [404.29]	24.74 (0.00) [0]
106	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	428.11 (-) [428.11]	52.08 (0.00) [0]
107	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	518.53 (-) [518.53]	56.74 (0.00) [0]
108	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	537.82 (-) [537.82]	53.86 (0.00) [0]
109	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	473.18 (-) [473.18]	38.63 (0.00) [0]
110	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2020]	624.41 (-) [992.67]	890.74 (368.26) [117]
	NAGALAND				

	Railways				
111	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
112	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2023]	2,326.52 (7,114.55) [6,911.44]	1,045.72 (4,584.92) [96]
	Road Transport And Highways				
113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	58.12 (0.00) [44]
114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	50.62 (0.00) [48]
115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	92.97 (-90.38) [0]
116	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [8/2020]	387.00 (-) [387.00]	240.72 (0.00) [0]
117	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (336.49) [336.49]	53.00 (-163.60) [0]
118	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	87.30 (0.00) [0]
119	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
120	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.37 (-) [339.37]	89.79 (0.00) [46]
121	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	62.00 (0.00) [39]
122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	77.08 (0.00) [39]
123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	68.26 (0.00) [38]
124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	49.94 (0.00) [39]
125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	25.76 (0.00) [49]
126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	28.46 (0.00) [50]
127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	92.10 (0.00) [0]
128	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	79.85 (0.00) [0]
129	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [0/0]	373.07 (-) [387.00]	272.09 (13.93) [0]
130	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000	3/2016	8/2016 (-)	396.52 (-)	267.34 (-56.97)

	TO KM 1		[6/2020]	[339.55]	[0]
131	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [0/0]	429.52 (-) [340.00]	227.18 (-89.52) [0]
132	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (9/2020) [0/0]	336.25 (369.96) [336.25]	278.10 (0.00) [0]
133	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	98.42 (0.00) [0]
134	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	123.44 (0.00) [0]
135	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
136	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	38.85 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
137	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [3/2023]	1,339.48 (4,084.69) [8,600.00]	619.18 (7,260.52) [87]
	<u>Road Transport And Highways</u>				
138	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (12/2020) [12/2020]	182.28 (369.64) [269.14]	274.06 (86.86) [94]
139	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (12/2020) [12/2020]	151.59 (370.61) [151.59]	282.36 (0.00) [88]
140	CONSTRUCTION OF 2-LANE TARU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (12/2020) [12/2020]	166.7 (359.92) [166.27]	243.59 (0.00) [88]
141	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	95.44 (0.00) [0]
142	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	24.70 (0.00) [0]
143	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
144	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
145	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	241.07 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
146	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [12/2020]	438.28 (-) [438.28]	335.58 (0.00) [18]
	<u>Railways</u>				
147	AGARTALA-AKHAURA NL	4/2012	3/2020 (3/2022) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
148	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM	10/2014	3/2018 (-)	369.00 (-)	357.19 (0.00)

	55.00 IN THE S		[0/0]	[369.00]	[0]
149	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [0/0]	171.90 (-) [171.90]	96.21 (0.00) [0]
	Rural Development				
150	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [2/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [62]
151	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [3/2021]	202.61 (227.00) [207.12]	189.79 (4.51) [51]
152	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [3/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [51]
	Total			1,00,894.93 (45,933.84) [1,51,431.06]	65,995.43 (50,536.13)

FLASH REPORT

**Summary of On-going
(as on 31.12.2020)**

Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (9/2020) [6/2021]	417.23 (-) [441.33]	291.75 (24.10) [33]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	47.28 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	164.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.20 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.1 (-) [277.1]	172.78 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	26.44 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	39.86 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	24.96 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [0/0]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [3/2023]	611.80 (-) [611.80]	0.00 (0.00) [0]
11	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (-) [6/2021]	177.10 (-) [177.10]	0.00 (0.00) [16]
	<u>Health And Family Welfare</u>				
12	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [6/2021]	601.02 (-) [601.02]	333.61 (0.00) [-]
13	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI	8/2017	6/2019 (-)	272.19 (-)	245.89 (0.35)

	GUNTUR, ANDHRA PRADESH		[3/2021]	[272.54]	[24]
	<u>Human Resource Development</u>				
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-) [3/2021]	186.00 (199.00) [205.00]	130.63 (19.00) [6]
15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	9/2019	9/2022 (4/2023) [1/2023]	588.72 (-) [588.72]	14.80 (0.00) [4]
16	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [0/0]	655.34 (-) [655.34]	49.89 (0.00) [0]
	<u>Petroleum</u>				
17	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
18	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	209.74 (0.00) [3]
19	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (3/2021) [3/2021]	384.58 (-) [384.58]	248.45 (0.00) [-1]
20	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [2/2021]	580.20 (-) [580.20]	90.13 (0.00) [0]
21	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (01/2021) (08/2021)	34,012.00 (-) [25,000.00]	9,799.00 (-8,922.00) [14]
22	LPG BP PROJECT CHITTOOR	7/2017	7/2022 (-) [7/2022]	167.00 (-) [167.00]	8.10 (0.00) [0]
23	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	82.31 (0.00) [10]
24	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
25	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	53.36 (0.00) [0]
26	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [7/2021]	196.26 (-) [196.26]	84.06 (0.00) [12]
27	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	13,324.42 (5,336.00) [24]
	<u>Railways</u>				
28	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [829.00]	0.94 (0.00) [0]
29	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
30	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
31	GUNTUR-GUNTAKAL	4/2016	3/2022 (3/2025)	3,631.00 (-)	984.35 (256.48)

			[3/2024]	[3,887.48]	[24]
32	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2024]	1,045.20 (-) [2,120.16]	746.71 (1,074.96) [180]
33	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (3/2024) [3/2024]	2,499.71 (-) [2,499.71]	590.79 (0.00) [24]
34	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	14.14 (0.50) [21]
35	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [3/2021]	387.70 (-) [487.13]	430.52 (99.43) [36]
36	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2025]	2,288.70 (-) [2,643.25]	1,191.09 (354.55) [48]
37	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
38	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	2,224.17 (302.42) [0]
39	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [3,377.00]	2,683.67 (1,873.29) [24]
	Road Transport And Highways				
40	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	234.49 (0.00) [0]
41	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
42	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [5/2018]	557.30 (-) [557.30]	351.02 (0.00) [0]
43	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (5/2021) [5/2021]	263.45 (-) [263.45]	97.45 (0.00) [44]
44	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (4/2021) [11/2019]	429.43 (-) [429.43]	277.54 (0.00) [0]
45	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [4/2021]	314.43 (-) [314.43]	86.83 (0.00) [-]
46	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (12/2020) [12/2020]	350.61 (-) [350.61]	323.06 (0.00) [47]
47	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
48	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]

49	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
50	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (-) [0/0]	333.21 (-) [355.89]	315.57 (22.68) [0]
51	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (10/2021) [4/2021]	1,532.62 (-) [2,499.00]	1,497.61 (966.38) [1]
52	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	1,634.05 (0.00) [0]
53	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (11/2020) [12/2020]	576.48 (-) [576.48]	288.92 (0.00) [35]
54	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (7/2021) [7/2021]	348.95 (-) [348.95]	200.57 (0.00) [59]
55	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/430 OF NH214(NH21	1/2016	5/2016 (1/2021) [12/2020]	386.09 (-) [386.09]	199.35 (0.00) [55]
57	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (7/2021) [5/2019]	290.1 (-) [290.15]	100.54 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	495.25 (0.00) [-]
60	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (8/2021) [4/2021]	995.09 (995.00) [995.09]	473.71 (0.00) [59]
61	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (7/2021) [9/2020]	444.84 (-) [444.84]	304.42 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (6/2021) [8/2020]	376.25 (-) [376.25]	264.97 (0.00) [0]
63	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (-) [0/0]	297.12 (294.00) [294.12]	373.98 (-3.00) [0]
64	REHABILITATION AND	3/2018	8/2018	289.67	173.13

	UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG		(6/2021) [2/2021]	(290.00) [289.67]	(0.00) [30]
65	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (4/2021) [1/2021]	504.19 (504.00) [504.19]	403.01 (0.00) [26]
66	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (3/2021) [0/0]	271.45 (-) [271.45]	218.26 (0.00) [0]
67	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (5/2021) [8/2019]	319.28 (-) [319.28]	141.98 (0.00) [0]
68	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (-) [0/0]	244.95 (245.00) [244.95]	136.22 (0.00) [0]
69	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (6/2021) [2/2019]	372.68 (-) [372.68]	207.28 (0.00) [0]
70	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2021) [3/2021]	228.32 (-) [228.32]	99.57 (0.00) [31]
71	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.323 (DORIALA T JUNCTION) TO KM 420.800 (	1/2018	8/2018 (5/2021) [3/2020]	418.03 (-) [418.03]	268.80 (0.00) [0]
72	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (-) [0/0]	373.2 (-) [378.24]	315.42 (0.00) [0]
73	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [10/2021]	1,959.00 (-) [1,959.00]	1,145.62 (0.00) [-]
74	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [7/2021]	1,323.15 (-) [1,323.15]	785.33 (0.00) [-]
75	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [9/2021]	1,550.98 (-) [1,550.98]	1,290.79 (0.00) [-]
76	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,274.78 (0.00) [0]
77	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	947.88 (145.48) [0]
78	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
79	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
80	CENTRAL DISPATCH YARD	8/2015	8/2018	320.66	278.28

			(11/2020) [11/2020]	(336.00) [336.00]	(15.34) [0]
81	COKE OVEN BATTERY-5	12/2011	12/2017 (12/2020) [12/2020]	2,858.00 (-) [2,558.00]	1,762.09 (-300.00) [36]
	<u>Urban Development</u>				
82	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>Water Resources</u>				
83	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2021) [4/2022]	10,151.04 (55,548.87) [55,548.87]	16,568.13 (45,397.83) [25]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
84	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (1/2021) [1/2021]	2,496.90 (7,927.34) [7,927.34]	8,151.00 (5,430.44) [133]
85	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	12,855.18 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
86	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	125.55 (0.00) [0]
87	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	376.15 (0.00) [0]
88	2 LANING FROM PANGSIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.1 (-) [194.11]	196.23 (0.00) [0]
89	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	199.53 (0.00) [0]
90	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	135.60 (0.00) [0]
91	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	187.33 (0.00) [0]
92	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	149.45 (0.00) [0]
93	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	160.05 (0.00) [0]
94	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	184.51 (0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	105.37 (0.00) [0]

	106.200 TO KM 120.				
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	220.29 (0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	88.62 (0.00) [0]
98	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]
99	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	160.24 (0.00) [0]
100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	184.62 (0.00) [0]
101	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	89.41 (0.00) [0]
102	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	303.02 (0.00) [0]
103	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM 6 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2017]	1,253.10 (-) [1,253.10]	204.77 (0.00) [60]
104	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [2/2021]	167.28 (-) [167.28]	22.06 (0.00) [46]
105	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [2/2021]	216.71 (-) [216.71]	26.84 (0.00) [46]
106	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
107	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [12/2020]	434.06 (-) [434.06]	172.89 (0.00) [-]
108	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	127.41 (0.00) [47]
109	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	94.62 (0.00) [0]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	106.52 (0.00) [0]
111	TWO LANING OF EXISTING KHUPA	1/2017	4/2017	194.66	98.24

	HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.		(-) [0/0]	(-) [194.66]	(0.00) [0]
112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	98.23 (0.00) [0]
113	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (-) [389.45]	349.94 (182.42) [0]
114	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	44.85 (0.00) [46]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [2/2021]	168.32 (-) [168.32]	43.28 (0.00) [46]
116	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	0.00 (119.37) [0]
117	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
118	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTING	1/2017	/	256.66 (-) [256.66]	24.14 (0.00) [0]
119	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/	175.0 (-) [175.06]	62.27 (0.00) [-]
120	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/	176.12 (-) [176.12]	54.56 (0.00) [-]
121	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/	199.02 (-) [199.02]	14.21 (0.00) [-]
122	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/	184.88 (-) [184.88]	6.85 (0.00) [-]
123	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/	1,979.00 (-) [2,036.90]	1,217.25 (57.90) [0]
	ASSAM				
	Civil Aviation				
124	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2022]	1,142.00 (1,232.00) [1,232.00]	323.90 (90.00) [12]
	Health And Family Welfare				
125	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [7/2022]	875.00 (-) [747.80]	279.76 (-127.20) [14]
126	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	163.37

			(-) [3/2018]	(-) [175.57]	(0.00) [0]
	Petroleum				
127	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [6/2021]	557.00 (-) [557.00]	467.19 (0.00) [16]
128	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [3/2021]	224.75 (-) [222.21]	148.44 (-2.54) [7]
129	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [0/0]	350.00 (-) [350.00]	2.06 (0.00) [0]
130	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [6/2021]	423.00 (-) [502.00]	399.01 (79.00) [22]
131	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [4/2021]	543.91 (638.60) [652.10]	130.10 (108.19) [14]
132	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [12,366.00]	168.82 (0.00) [0]
133	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	117.34 (0.00) [0]
134	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2021) [5/2021]	249.85 (303.75) [303.75]	170.85 (53.90) [12]
	Railways				
135	AMBARI FALAKATA TO NEW MAYNAGURI	1/2011	2/2019 (-) [1/2021]	31.00 (-) [800.00]	777.27 (486.00) [22]
136	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,375.36 (717.68) [12]
137	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [5/2021]	870.96 (-) [1,873.21]	1,007.06 (1,002.25) [2]
138	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (1,105.00) [1,532.00]	770.73 (1,146.80) [48]
	Road Transport And Highways				
139	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	267.46 (0.00) [0]
140	2 LANING OF OF LUMDING-DIPHU-MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
141	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
142	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
143	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	126.13 (0.00) [0]

144	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	460.01 (0.00) [0]
145	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	55.03 (0.00) [0]
146	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	80.88 (-28.50) [0]
147	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.30]	56.22 (-30.09) [42]
148	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [4/2021]	294.17 (-) [294.17]	170.00 (0.00) [63]
149	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (-) [12/2020]	166.94 (-) [166.94]	0.00 (0.00) [0]
150	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	488.05 (143.23) [0]
151	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [3/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
152	DHARAMTUL TO SONAPUR KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	167.0 (-) [167.96]	230.89 (7.98) [0]
153	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
154	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	114.16 (0.00) [0]
155	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [887.68]	178.47 (69.68) [0]
156	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	103.86 (-65.43) [42]
157	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	372.69 (0.00) [0]
158	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	239.35 (0.00) [31]
159	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
160	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]

161	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
162	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
163	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
164	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2020]	208.00 (-) [230.00]	355.20 (22.00) [152]
165	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	347.28 (0.00) [0]
166	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [273.40]	115.65 (-776.11) [0]
167	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	231.82 (-70.66) [0]
168	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [307.47]	292.55 (89.16) [0]
169	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	57.16 (0.00) [0]
BIHAR					
Civil Aviation					
170	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	1,216.90 (-) [1,216.90]	122.19 (0.00) [0]
Human Resource Development					
171	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [9/2021]	496.18 (496.00) [498.99]	185.61 (2.81) [51]
Petroleum					
172	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [4/2023]	14,810.00 (-) [14,810.00]	632.61 (0.00) [0]
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	128.57 (0.00) [0]
174	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (12/2021) [12/2021]	522.00 (-) [522.00]	278.28 (0.00) [9]
175	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (2/2022) [2/2022]	199.36 (-) [199.36]	20.38 (0.00) [16]
176	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (11/2020) [11/2020]	951.64 (-) [951.64]	678.12 (0.00) [0]
177	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021) [6/2021]	189.00 (-) [189.00]	114.02 (0.00) [5]

178	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [9/2021]	206.50 (-) [206.50]	109.56 (0.00) [6]
179	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	0.00 (0.00) [0]
	<u>Power</u>				
180	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (4/2022) [4/2022]	8,692.97 (21,312.11) [21,312.11]	18,168.42 (12,619.14) [126]
181	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (6/2020) [3/2021]	5,353.00 (7,998.00) [9,583.00]	8,648.28 (4,230.00) [104]
182	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	1,221.50 (0.00) [0]
183	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (6/2021) [7/2021]	12,964.60 (17,304.00) [17,304.00]	15,331.70 (4,339.40) [38]
	<u>Railways</u>				
184	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]
185	ARARIA-SUPAUL (NL)	4/2008	/ (-) [3/2023]	1,605.17 (-) [1,605.17]	23.74 (0.00) [-]
186	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	1.94 (2,668.81) [-]
187	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	378.5 (-) [1,878.15]	383.64 (1,480.19) [-]
188	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
189	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [0/0]	205.00 (-) [205.00]	5.21 (0.00) [0]
190	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [3/2022]	329.39 (-) [1,483.14]	1,177.09 (1,153.75) [-]
191	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [0/0]	445.25 (-) [445.25]	1.15 (0.00) [0]
192	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (-) [1/2020]	213.01 (-) [480.00]	473.33 (266.99) [0]
193	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [3/2023]	528.65 (-) [2,066.78]	1,510.98 (1,538.13) [-]
194	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [11/2022]	324.73 (-) [1,070.00]	1,061.07 (745.27) [128]
195	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (-) [3/2023]	548.00 (-) [819.01]	513.72 (271.01) [36]
196	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [3/2022]	162.87 (-) [614.45]	333.16 (451.58) [-]
197	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.74

			(-) [3/2022]	(-) [360.00]	(26.24) [-]
198	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	760.55 (0.00) [36]
199	KOSI BRIDGE (NL), ECR	4/2002	3/2020 (-) [9/2020]	499.41 (-) [516.02]	431.28 (16.61) [0]
200	KURSELA-BIHARIGANJ (NL)	4/2008	/ (-) [0/0]	192.56 (-) [192.56]	0.39 (0.00) [0]
201	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012 (-) [5/2021]	477.88 (283.95) [751.55]	680.95 (273.67) [110]
202	MOTIHARI-SITAMARHI (NL)	4/2006	/ (-) [0/0]	211.00 (-) [1,006.00]	24.73 (795.00) [0]
203	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	4/2016	3/2021 (-) [6/2022]	731.64 (-) [1,185.73]	154.70 (454.09) [15]
204	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/ (-) [0/0]	281.30 (-) [281.30]	0.60 (0.00) [0]
205	MUZAFFARPUR-KATRA-ORAI- JANAKPUR ROAD (NL)	4/2008	/ (-) [3/2024]	228.05 (-) [228.05]	1.53 (0.00) [-]
206	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (-) [546.71]	541.83 (214.56) [0]
207	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [0/0]	320.5 (-) [620.5]	0.31 (0.00) [0]
208	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2024]	532.87 (-) [2,145.00]	967.13 (1,612.13) [60]
209	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (-) [0/0]	180.82 (-) [726.31]	535.07 (545.49) [0]
210	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [3/2023]	1,491.47 (-) [1,491.47]	465.98 (0.00) [36]
211	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [3/2024]	744.04 (-) [1,215.54]	299.09 (471.50) [36]
212	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (-) [735.20]	379.45 (410.20) [-]
213	SAKRI-NIRMALI AND JHANJHARPUR- LAUKAHABAZAR AND SAHARSA- FORBESGANJ (GC)	4/2004	/ (-) [3/2021]	372.14 (-) [1,470.50]	1,095.55 (1,098.36) [-]
214	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [2/2023]	380.00 (-) [519.33]	265.08 (139.33) [-]
215	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [678.62]	17.20 (0.00) [0]
Road Transport And Highways					
216	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (12/2020) [1/2021]	511.54 (585.00) [591.00]	575.34 (79.46) [86]
217	2-LANNING WITH PS MOTIHARI-	10/2011	4/2014	375.09	494.33

	RAXAUL		(-) [0/0]	(-) [375.09]	(0.00) [0]
218	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [0/0]	575.00 (-) [575.00]	555.63 (0.00) [0]
219	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	89.69 (0.00) [0]
220	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	14.53 (0.00) [0]
221	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	3.72 (0.00) [0]
222	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015 (-) [0/0]	288.24 (-) [288.24]	300.58 (0.00) [0]
223	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (-) [0/0]	2,598.00 (-) [2,598.00]	0.00 (0.00) [0]
224	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	36.08 (-7.71) [14]
225	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAUSATI SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [327.1]	38.11 (40.97) [0]
226	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	11/2013	7/2016 (-) [0/0]	683.8 (-) [560.70]	657.38 (-123.13) [0]
227	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [152.62]	87.02 (-26.23) [0]
228	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
229	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [478.35]	289.14 (-74.95) [0]
230	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [0/0]	1,167.45 (1,182.94) [1,182.94]	186.70 (15.49) [0]
231	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [0/0]	642.41 (-) [681.67]	400.60 (39.26) [0]
232	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [12/2020]	322.09 (247.00) [322.09]	77.53 (0.00) [32]
233	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [925.87]	699.76 (-482.98) [0]
234	FOUR LANING OF KOILWAR TO	8/2015	/	814.04	512.04

	BHOJPUR		(-) [10/2021]	(-) [825.17]	(11.13) [-]
235	FOUR LANING OF PATNA TO KOILWAR	8/2015	/	556.07	0.00
			(-) [0/0]	(-) [556.07]	(0.00) [0]
236	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019	1,041.10	276.41
			(-) [0/0]	(-) [1,041.10]	(0.00) [0]
237	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014	574.00	768.73
			(-) [0/0]	(-) [574.00]	(0.00) [0]
238	PATNA-MUZZAFFARPUR	8/2010	2/2013	671.30	1,360.63
			(-) [0/0]	(671.30) [671.30]	(0.00) [0]
239	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016	1,742.01	1,399.93
			(-) [0/0]	(-) [1,742.01]	(0.00) [0]
240	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/	573.70	22.95
			(-) [0/0]	(-) [573.70]	(0.00) [0]
241	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014	278.39	0.00
			(-) [0/0]	(-) [278.39]	(0.00) [0]
242	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/	478.35	435.30
			(-) [0/0]	(-) [478.35]	(0.00) [0]
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 4 TO KM 219.945) OF NH-104	1/1991	/	319.6	216.25
			(-) [0/0]	(-) [319.6]	(50.09) [0]
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016	665.50	0.00
			(-) [0/0]	(-) [665.50]	(0.00) [0]
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016	282.41	317.05
			(-) [0/0]	(-) [322.01]	(39.60) [0]
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016	358.22	341.81
			(-) [0/0]	(-) [377.64]	(19.42) [0]
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/	675.00	239.89
			(-) [0/0]	(-) [675.00]	(0.00) [0]
248	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/	154.62	0.00
			(-) [0/0]	(-) [154.62]	(0.00) [0]
249	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/	895.39	0.00
			(-) [0/0]	(-) [895.39]	(0.00) [0]
250	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017	950.64	194.95
			(-) [2/2022]	(-) [950.64]	(0.00) [54]
251	STRENGTHENING AND WIDENING	3/2018	/	153.24	39.82

	TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH		(-) [0/0]	(-) [153.24]	(0.00) [0]
252	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
253	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [0/0]	399.54 (-) [297.27]	271.39 (-102.27) [0]
254	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (1,038.56) [1,038.56]	1,160.00 (183.76) [0]
255	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (649.27) [649.27]	712.15 (133.14) [0]
256	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT- SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [0/0]	672.89 (-) [736.01]	21.04 (63.12) [0]
257	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	174.35 (0.00) [52]
258	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [0/0]	230.34 (232.90) [230.34]	205.97 (0.00) [0]
	<u>Urban Development</u>				
259	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [6/2024]	13,365.77 (-) [13,365.77]	271.17 (0.00) [0]
	<u>Water Resources</u>				
260	I AND D AND STP AT CHAPRA	11/2018	12/2020 (-) [12/2020]	236.15 (-) [236.15]	12.06 (0.00) [0]
261	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [0/0]	254.13 (-) [254.13]	0.05 (0.00) [0]
262	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [721.37]	712.37 (-234.63) [72]
263	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [1/2021]	268.63 (-) [268.63]	254.50 (0.00) [0]
264	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	4/2015	4/2020 (-) [12/2020]	184.93 (-) [184.93]	163.36 (0.00) [8]
265	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [7/2021]	230.06 (-) [230.06]	37.09 (0.00) [0]
266	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [12/2021]	305.19 (-) [305.19]	0.00 (0.00) [4]
267	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [10/2021]	294.02 (-) [294.02]	0.00 (0.00) [0]
268	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	5/2021 (-) [5/2021]	184.86 (-) [184.86]	131.43 (0.00) [0]
269	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [0/0]	356.37 (-) [0/0]	79.54 (0.00) [0]

			[4/2021]	[356.37]	[0]
270	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [6/2022]	824.00 (-) [824.00]	0.42 (0.00) [0]
271	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [6/2022]	578.89 (-) [578.89]	0.29 (0.00) [0]
272	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [12/2020]	225.77 (-) [225.77]	249.54 (0.00) [9]
273	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [5/2021]	277.42 (-) [277.42]	111.10 (0.00) [0]
274	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (-) [12/2020]	191.62 (-) [191.62]	43.01 (0.00) [1]
	<u>CHANDIGARH</u>				
	<u>Road Transport And Highways</u>				
275	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	3/2010	3/2013 (-) [0/0]	179.89 (271.00) [271.00]	0.00 (91.11) [0]
276	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	1/2019 (-) [0/0]	169.26 (299.00) [299.00]	0.00 (129.74) [0]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
277	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	49.41 (0.00) [60]
278	AMGAON OPENCAST PROJECT RCE	2/2015	3/2020 (-) [3/2023]	317.1 (-) [316.10]	123.22 (0.00) [36]
279	BAROUD OC EXPANSION (RCE)-3MTY	4/2012	3/2016 (-) [3/2021]	258.56 (-) [258.56]	182.04 (0.00) [60]
280	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2021]	164.49 (-) [164.49]	82.60 (0.00) [12]
281	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	129.86 (0.00) [0]
282	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	8.19 (0.00) [0]
283	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	3,645.58 (0.00) [0]
284	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2022]	152.43 (459.49) [459.49]	180.74 (307.06) [84]
285	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
286	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2022]	178.44 (-) [178.44]	4.98 (0.00) [96]
287	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,446.61 (0.00) [0]
288	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024	1,875.32	0.00

			(-) [3/2024]	(-) [1,875.32]	(0.00) [0]
289	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	18.19 (0.00) [0]
290	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	208.12 (0.00) [84]
291	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	7.31 (0.00) [0]
292	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	Human Resource Development				
293	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [7/2022]	808.62 (-) [808.62]	57.42 (0.00) [0]
	Power				
294	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (-) [0/0]	11,846.00 (-) [12,739.82]	13,766.78 (893.82) [0]
295	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [0/0]	3,004.00 (-) [3,004.00]	2,220.16 (0.00) [0]
	Railways				
296	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (10/2020) [10/2020]	872.00 (-) [1,226.51]	1,131.91 (354.51) [0]
297	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM IN BILASPUR DIVISION OF SEC RAILW	2/2015	3/2020 (6/2021) [6/2021]	303.9 (-) [303.9]	350.81 (0.00) [15]
298	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [6/2024]	2,288.00 (-) [4,970.11]	849.31 (2,682.11) [27]
299	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2023) [12/2023]	1,973.00 (2,135.34) [2,135.34]	351.35 (162.34) [33]
300	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [12/2021]	3,055.00 (-) [3,055.15]	2,386.05 (0.15) [39]
301	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2023]	1,160.00 (1,160.83) [1,160.83]	891.78 (0.83) [36]
302	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
303	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2021]	1,402.02 (-) [1,300.00]	1,251.62 (-102.02) [21]
	Road Transport And Highways				
304	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	299.09 (231.09) [-]
305	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
306	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-)	596.67 (-)	439.27 (0.00)

			[0/0]	[596.67]	[0]
307	REHABILITATION AND UPGRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI-KAWARDHA SECTION.	12/2015	/ (10/2020) [10/2020]	291.05 (-) [291.05]	200.70 (0.00) [0]
308	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (2/2021) [2/2021]	335.32 (-) [335.32]	245.69 (0.00) [44]
309	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION	3/2016	9/2016 (10/2020) [10/2020]	491.52 (512.77) [491.52]	474.27 (0.00) [0]
310	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (3/2021) [3/2021]	476.20 (543.73) [544.00]	397.32 (67.80) [54]
311	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (3/2021) [3/2021]	496.02 (-) [496.02]	226.59 (0.00) [72]
312	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (3/2021) [3/2021]	497.14 (527.66) [527.66]	232.36 (30.52) [55]
313	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (12/2020) [12/2020]	624.98 (731.50) [731.50]	341.61 (106.52) [50]
314	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATHALGAON TO KUNKURI	3/2016	7/2016 (3/2021) [3/2021]	452.94 (435.61) [435.61]	73.30 (-17.33) [56]
315	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION	3/2017	1/2018 (3/2021) [3/2021]	423.79 (-) [423.79]	252.15 (0.00) [38]
316	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	447.13 (0.00) [0]
317	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (3/2021) [3/2021]	188.80 (-) [188.80]	65.21 (0.00) [22]
318	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (3/2021) [3/2021]	379.16 (-) [379.16]	235.01 (0.00) [40]
	<u>Steel</u>				
319	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2021) [7/2021]	15,525.00 (21,940.00) [21,940.00]	17,436.86 (6,415.00) [74]
	<u>Urban Development</u>				
320	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO	5/2019	9/2020 (-) [0/0]	299.97 (-) [299.97]	0.29 (0.00) [0]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
321	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT	11/2016	4/2020 (-) [5/2021]	303.80 (-) [303.80]	115.88 (0.00) [13]

	SAFDARJUNG AIRPOR				
	<u>Commerce And Industry</u>				
322	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [10/2020]	302.64 (-) [302.64]	60.00 (0.00) [0]
323	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [7/2021]	4,773.00 (-) [5,178.00]	2,334.57 (405.00) [19]
	<u>Health And Family Welfare</u>				
324	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [3/2021]	204.44 (-) [250.00]	226.54 (45.56) [46]
325	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
326	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [3/2021]	156.56 (-) [156.64]	111.58 (0.08) [-]
327	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [3/2021]	414.11 (-) [499.23]	456.52 (85.12) [88]
	<u>Heavy Industry</u>				
328	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (12/2020) [12/2020]	1,554.00 (-) [1,554.00]	806.15 (0.00) [15]
	<u>Home Affairs</u>				
329	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [9/2021]	1,219.21 (-) [2,000.00]	841.88 (780.79) [23]
	<u>Power</u>				
330	CONSTRUCTION OF ATAL BIKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2017 (-) [3/2021]	271.9 (-) [271.90]	172.99 (0.00) [16]
331	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART- A)	3/2015	5/2017 (7/2020) [6/2021]	1,394.52 (-) [1,394.52]	508.31 (0.00) [49]
	<u>Railways</u>				
332	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	112.95 (123.32) [-]
333	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (196.17) [359.00]	111.51 (202.35) [-]
	<u>Road Transport And Highways</u>				
334	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019 (-) [0/0]	269.69 (-) [269.69]	0.00 (0.00) [0]
	<u>Rural Development</u>				
335	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [7/2021]	361.60 (-) [361.60]	12.44 (0.00) [0]
	<u>Telecommunications</u>				
336	CONVERGENT BILLING AND CRM- MTNL(DELHI)	12/2005	2/2007 (-) [0/0]	249.00 (-) [229.41]	0.00 (-19.59) [0]
337	DELHI CONVERGENT BILLING AND CRM PE-5834	2/2006	3/2012 (-) [0/0]	229.41 (-) [229.41]	0.00 (0.00) [0]

338	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	3/2018 (12/2020) [12/2020]	248.20 (-) [248.20]	80.10 (0.00) [33]
	<u>Urban Development</u>				
339	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG	2/2020	11/2020 (2/2021) [11/2020]	532.00 (-) [532.00]	102.00 (0.00) [0]
340	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2021) [6/2021]	197.33 (-) [197.33]	94.18 (0.00) [26]
341	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	11/2020 (-) [11/2020]	218.72 (-) [218.72]	126.16 (0.00) [0]
342	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (12/2020) [12/2020]	884.30 (884.30) [884.30]	812.00 (0.00) [60]
343	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	965.60 (0.00) [0]
344	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (-) [9/2021]	565.00 (-) [565.00]	503.33 (0.00) [9]
345	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [3/2021]	38,585.00 (-) [38,585.00]	39,843.96 (0.00) [60]
346	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (2/2021) [2/2021]	238.56 (-) [238.56]	157.67 (0.00) [9]
347	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (11/2020) [11/2020]	4,264.00 (4,720.73) [4,720.73]	4,683.08 (456.73) [0]
348	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [9/2021]	1,180.00 (-) [1,100.80]	34.82 (-79.20) [2]
349	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (-) [12/2021]	392.00 (-) [392.00]	63.67 (0.00) [16]
350	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [3/2022]	1,128.00 (-) [1,128.00]	22.00 (0.00) [0]
351	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (7/2021) [7/2021]	422.00 (-) [422.00]	28.26 (0.00) [4]
352	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [3/2022]	2,694.00 (-) [2,694.00]	553.56 (0.00) [-]
	<u>Water Resources</u>				
353	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
354	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT	12/2018	1/2021 (-)	515.07 (-)	278.37 (0.00)

	CORONATION PILLAR DELHI		[6/2021]	[515.07]	[5]
355	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	129.56 (0.00) [0]
356	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	50.75 (0.00) [12]
357	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	73.13 (0.00) [10]
	GOA				
	<u>Health And Family Welfare</u>				
358	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [1/2021]	249.01 (-) [249.07]	216.09 (0.06) [-]
	<u>Human Resource Development</u>				
359	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [0/0]	303.90 (-) [303.90]	9.50 (0.00) [0]
	<u>Road Transport And Highways</u>				
360	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	219.47 (10.43) [0]
361	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [124.0]	91.39 (0.00) [0]
362	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	975.4 (-) [936.40]	355.10 (0.00) [0]
363	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	197.75 (0.00) [0]
364	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHINDEAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	290.64 (0.00) [0]
365	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [0/0]	852.67 (-) [852.67]	138.14 (0.00) [0]
366	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [0/0]	634.32 (-) [634.32]	221.25 (0.00) [0]
367	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	336.25 (0.00) [0]
368	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	205.20 (0.00) [0]
	GUJARAT				
	<u>Atomic Energy</u>				
369	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [9/2021]	11,459.00 (-) [16,580.00]	16,038.00 (5,121.00) [69]

	Civil Aviation				
370	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022 (-) [3/2023]	1,405.00 (-) [1,405.00]	0.00 (0.00) [7]
	Petroleum				
371	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	48.16 (0.00) [0]
372	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (5/2023) [5/2023]	588.20 (730.20) [730.20]	48.20 (142.00) [-]
373	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [3/2021]	327.78 (-) [200.00]	186.50 (-127.78) [35]
374	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [0/0]	1,342.00 (-) [1,342.00]	6.30 (0.00) [0]
375	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2021) [10/2021]	906.00 (-) [906.00]	234.25 (0.00) [20]
376	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021 (-) [12/2021]	403.00 (-) [403.00]	52.81 (0.00) [0]
377	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [970.30]	621.21 (-192.26) [0]
378	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (-) [12/2021]	1,378.00 (-) [1,378.00]	0.00 (0.00) [0]
379	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECT	9/2018	2/2021 (-) [12/2021]	225.54 (-) [225.54]	38.70 (0.00) [10]
	Power				
380	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (6/2020) [9/2020]	193.14 (-) [193.14]	116.91 (0.00) [0]
381	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (6/2020) [9/2020]	175.64 (-) [175.64]	120.78 (0.00) [0]
	Railways				
382	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,500.00]	1,376.94 (524.38) [0]
383	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (12/2023) [12/2023]	829.74 (1,959.74) [1,959.74]	1,760.97 (1,130.00) [45]
384	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
385	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (10/2021) [10/2021]	551.51 (890.76) [890.76]	738.65 (339.25) [31]
386	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2023) [3/2023]	318.24 (411.62) [411.62]	125.76 (93.38) [132]

387	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (12/2020) [12/2020]	691.84 (1,017.91) [1,017.91]	453.03 (326.07) [9]
388	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [872.65]	800.30 (228.27) [0]
389	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
390	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2024) [3/2024]	844.10 (844.10) [844.10]	172.03 (0.00) [-]
391	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
392	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
393	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,868.89]	1,726.74 (320.23) [3]
394	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2023) [3/2023]	320.66 (1,378.11) [1,378.11]	540.09 (1,057.45) [48]
395	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,002.39) [1,002.39]	578.34 (0.00) [21]
396	VIRAMGAM-SAMAKHAYALI (DL)	4/2011	3/2021 (3/2022) [3/2022]	1,077.55 (1,379.05) [1,389.05]	1,096.41 (351.90) [12]
397	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
Road Transport And Highways					
398	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	303.96 (0.00) [0]
399	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	224.34 (0.00) [0]
400	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [2/2021]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [8]
401	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,669.71 (0.00) [0]
402	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [12/2020]	364.56 (-) [392.00]	353.42 (27.44) [-]
403	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	37.17 (0.00) [0]
404	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	584.17 (0.00) [-]

405	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [6/2021]	2,702.05 (-) [2,043.00]	1,327.65 (-659.05) [-]
406	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	130.53 (0.00) [0]
407	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (-) [962.43]	182.43 (0.00) [0]
408	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	392.24 (0.00) [0]
409	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	697.86 (0.00) [0]
410	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	503.45 (0.00) [0]
411	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	203.40 (0.00) [0]
412	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE IV) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	450.54 (0.00) [0]
413	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	5/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.89 (0.00) [0]
414	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
415	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [11/2020]	953.88 (-) [953.88]	976.79 (0.00) [0]
416	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (-) [1,449.00]	394.36 (396.79) [-]
417	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [1/2021]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [-]
418	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	132.68 (0.00) [0]
419	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	84.67 (0.00) [0]
420	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	268.50 (0.00) [0]

421	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON	3/2016	2/2016 (-) [0/0]	208.34 (-) [208.34]	112.87 (0.00) [0]
422	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
423	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE	3/2016	2/2017 (-) [0/0]	223.67 (-) [223.67]	112.81 (0.00) [0]
	<u>Urban Development</u>				
424	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [11/2022]	10,773.00 (-) [12,787.00]	8,276.69 (2,014.00) [47]
425	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	30.02 (0.00) [0]
426	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	14.89 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
427	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [3/2021]	215.92 (-) [215.92]	164.03 (0.00) [16]
	<u>Health And Family Welfare</u>				
428	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2019]	505.58 (-) [525.00]	586.96 (79.42) [0]
	<u>Home Affairs</u>				
429	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	1/2020	10/2023 (-) [10/2023]	165.9 (167.00) [166.98]	0.00 (0.00) [0]
	<u>Petroleum</u>				
430	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [3/2022]	909.00 (-) [909.00]	141.32 (0.00) [14]
431	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (8/2021) [8/2021]	206.63 (-) [206.63]	64.15 (0.00) [18]
432	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (-) [9/2026]	520.00 (-) [520.00]	86.19 (0.00) [0]
433	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (-) [7/2021]	164.69 (-) [164.69]	2.06 (0.00) [0]
434	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (6/2021) [6/2021]	255.00 (300.00) [300.00]	247.49 (45.00) [7]
435	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (2/2022) [2/2022]	598.00 (-) [598.00]	172.31 (0.00) [24]
436	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [7/2022]	278.60 (-) [278.60]	9.50 (0.00) [13]
437	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-)	1,636.00 (-)	552.56 (0.00)

			[4/2022]	[1,636.00]	[20]
438	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [10/2021]	1,255.00 (-) [1,255.00]	129.59 (0.00) [0]
439	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (-) [12/2022]	2,281.94 (-) [2,281.94]	425.50 (0.00) [0]
440	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (5/2021) [5/2021]	286.42 (327.01) [327.01]	143.50 (40.59) [9]
	<u>Railways</u>				
441	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2021]	346.32 (-) [346.32]	315.22 (0.00) [24]
442	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [6/2021]	287.00 (-) [893.45]	625.47 (606.45) [114]
	<u>Road Transport And Highways</u>				
443	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [507.70]	496.22 (-95.25) [0]
444	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	516.32 (-37.12) [0]
445	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [0/0]	639.79 (-) [552.90]	595.53 (-86.89) [0]
446	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [0/0]	2,128.72 (-) [2,128.72]	1,070.00 (0.00) [29]
447	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (-) [0/0]	275.0 (-) [276.01]	187.39 (0.00) [0]
448	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [2/2021]	247.25 (-) [247.25]	162.62 (0.00) [23]
449	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [0/0]	248.97 (-) [248.97]	270.65 (0.00) [0]
450	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (6/2021) [12/2020]	1,484.30 (-) [1,484.30]	356.66 (0.00) [-]
451	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [0/0]	1,004.67 (-) [813.45]	577.21 (-191.22) [0]
452	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]
453	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	567.52 (0.00) [0]
454	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (1/2020) [0/0]	1,243.45 (-) [1,243.45]	659.79 (0.00) [0]
455	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (6/2020) [0/0]	889.36 (-) [889.36]	438.38 (0.00) [0]

456	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (2/2020) [0/0]	1,018.79 (-) [1,018.79]	468.24 (0.00) [0]
457	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (2/2020) [0/0]	1,051.91 (-) [1,051.91]	526.09 (0.00) [0]
458	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	501.73 (0.00) [0]
459	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (-) [0/0]	1,137.42 (-) [1,137.42]	690.88 (0.00) [0]
460	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (-) [0/0]	1,033.19 (-) [1,033.19]	604.45 (0.00) [0]
461	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [0/0]	1,108.00 (-) [2,967.50]	3,994.51 (1,859.50) [0]
462	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [0/0]	551.58 (-) [551.58]	306.06 (0.00) [0]
463	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [0/0]	275.12 (-) [275.12]	169.48 (0.00) [0]
464	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING	3/2018	/ (-) [0/0]	307.79 (-) [307.79]	195.35 (0.00) [0]
465	REHABILITATION AND UPGRADATION OF HAJJALI - LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.76 (-) [181.76]	128.10 (0.00) [0]
466	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [0/0]	198.05 (-) [198.05]	117.51 (0.00) [0]
467	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [7/2021]	795.50 (-) [799.30]	142.26 (3.80) [-]
468	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [7/2021]	634.70 (-) [931.21]	183.69 (296.51) [-]
HIMACHAL PRADESH					
Health And Family Welfare					
469	AIIMS BILASPUR	4/2018	9/2021 (-) [9/2021]	1,351.00 (-) [1,471.00]	577.32 (120.00) [0]
470	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [5/2022]	260.00 (-) [260.00]	25.38 (0.00) [11]
Human Resource Development					
471	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [12/2020]	270.83 (-) [270.83]	226.16 (0.00) [73]
472	ESTABLISHMENT OF PERMANENT	9/2018	6/2022	392.51	35.88

	CAMPUS PHASE 1 OF IIM SIRMAUR		(-) [6/2022]	(-) [392.51]	(0.00) [0]
	<u>Power</u>				
473	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	282.43 (0.00) [0]
474	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (3/2022) [3/2022]	3,919.59 (9,897.59) [9,897.59]	8,705.10 (5,978.00) [150]
	<u>Railways</u>				
475	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2025]	2,966.99 (-) [6,753.42]	784.37 (3,786.43) [-12]
	<u>Road Transport And Highways</u>				
476	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [0/0]	273.20 (-) [273.20]	666.55 (0.00) [0]
477	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	827.25 (0.00) [15]
478	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,960.92 (0.00) [0]
479	FOUR LANING OF PARWANOO - SOLAN	9/2015	3/2018 (9/2020) [0/0]	934.46 (1,302.98) [934.46]	697.33 (0.00) [0]
480	FOUR LANING OF SOLAN- KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EP	3/2018	/ (-) [5/2021]	478.74 (1,118.19) [478.74]	127.42 (0.00) [-]
481	FOUR LANNING OF MERCHOWK- PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	3/2016	/ (-) [0/0]	1,233.11 (-) [1,273.71]	650.93 (0.00) [0]
482	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [8/2020]	447.75 (-) [447.75]	1,153.75 (0.00) [0]
483	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (2,173.74) [1,583.18]	271.06 (0.00) [0]
	<u>JAMMU AND KASHMIR</u>				
	<u>Civil Aviation</u>				
484	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [9/2021]	346.27 (480.33) [480.33]	51.11 (134.06) [0]
	<u>Health And Family Welfare</u>				
485	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
486	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	94.33 (0.00) [0]
	<u>Human Resource Development</u>				
487	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (748.19) [676.00]	0.00 (0.00) [0]
488	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (-) [7/2020]	329.00 (-) [329.00]	0.00 (0.00) [0]
	<u>Power</u>				
489	PAKAL DUL HYDRO ELECTRIC	10/2014	4/2020	8,112.12	1,598.96

	PROJECT (1000 MW)		(-) [7/2025]	(-) [8,112.12]	(0.00) [63]
	<u>Railways</u>				
490	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2022]	2,500.00 (27,949.00) [27,949.00]	22,369.08 (25,449.00) [241]
	<u>Road Transport And Highways</u>				
491	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	761.37 (-132.75) [-]
492	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	815.94 (0.00) [18]
493	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,602.34 (0.00) [0]
494	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,650.38 (0.00) [0]
495	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,708.76 (360.00) [0]
496	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,105.02 (0.00) [0]
497	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [10/2020]	1,100.70 (-) [1,100.70]	2,921.73 (0.00) [0]
498	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	118.87 (0.00) [0]
499	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	68.37 (0.00) [0]
500	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018			
	<u>Urban Development</u>				
501	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	0.00 (0.00) [-16]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
502	AMRAPALI OC EPR (12MTY)	2/2012	3/2020 (3/2024) [3/2024]	858.11 (5,136.15) [858.11]	243.83 (0.00) [48]
503	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	97.01 (0.00) [0]
504	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2022]	163.51 (-) [163.51]	106.63 (0.00) [132]
505	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	158.71 (0.00) [0]
506	KAPURIA UG(PSLW)	8/2011	4/2017 (-)	988.35 (-)	45.26 (0.00)

			[0/0]	[988.35]	[0]
507	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2022]	162.46 (-) [162.46]	96.86 (0.00) [96]
508	MADHUBAND NLW WASHERY	8/2010	5/2014 (3/2020) [2/2021]	289.45 (-) [289.45]	277.38 (0.00) [81]
509	MAGADH EXPANSION OC RPR	8/2008	7/2012 (3/2025) [3/2025]	706.40 (7,254.37) [706.40]	638.94 (0.00) [152]
510	MOONIDIH XV SEAM UG	8/2011	4/2015 (3/2022) [3/2022]	1,230.27 (-) [1,230.27]	446.01 (0.00) [83]
511	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (4/2023) [4/2023]	339.88 (-) [339.88]	17.76 (0.00) [108]
512	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.54 (0.00) [0]
513	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2024]	1,553.06 (-) [1,553.06]	238.77 (0.00) [12]
514	PACHWARA SOUTH COAL BLOCK	7/2013	8/2022 (-) [9/2023]	1,795.01 (-) [1,795.01]	31.62 (0.00) [13]
515	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [12/2021]	243.00 (334.27) [334.27]	16.73 (91.27) [44]
516	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2020]	269.82 (-) [269.82]	205.37 (0.00) [0]
517	RAJRAPPA RCE OCP (3.0 MTY)	12/2019	3/2016 (-) [3/2022]	510.8 (-) [510.85]	401.56 (0.00) [72]
518	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	39.79 (0.00) [0]
	<u>Human Resource Development</u>				
519	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [6/2021]	171.86 (-) [171.86]	111.29 (0.00) [63]
	<u>Petroleum</u>				
520	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (9/2021) [9/2021]	161.50 (-) [161.50]	54.07 (0.00) [15]
521	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	93.90 (0.00) [0]
522	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	73.85 (0.00) [0]
523	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	611.60 (314.52) [-12]
524	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	60.14 (0.00) [0]
	<u>Power</u>				
525	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [10/2022]	14,366.58 (-) [15,389.42]	11,269.68 (1,022.84) [40]

526	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,312.62 (314.04) [0]
527	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [9/2024]	18,668.00 (-) [18,668.00]	3,644.04 (0.00) [18]
	Railways				
528	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2023]	1,724.20 (-) [1,993.24]	642.92 (269.04) [33]
529	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	299.31 (0.00) [-3]
530	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	3/1999	/ (-) [3/2022]	1,033.07 (-) [3,500.00]	3,494.01 (2,466.93) [-]
531	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2023]	459.91 (-) [1,625.87]	712.11 (1,165.96) [-]
532	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (12/2018) [6/2021]	258.20 (358.68) [358.68]	295.76 (100.48) [30]
533	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (-) [8/2020]	148.77 (-) [377.00]	194.30 (228.23) [0]
	Road Transport And Highways				
534	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [3/2021]	1,005.08 (-) [1,005.08]	0.00 (0.00) [-]
535	4-LANNING OF MAHULIA BAHARAGORA-JH/ WB BORDER SECTION	2/2016	2/2019 (-) [0/0]	99.1 (-) [997.15]	728.62 (0.00) [0]
536	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	44.05 (2.71) [0]
537	FOUR LANING OF BARHI- HAZARIBAGH NH-33	8/2016	8/2018 (-) [0/0]	323.72 (-) [336.60]	310.12 (12.88) [0]
538	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
539	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [11/2020]	212.99 (-) [212.99]	141.46 (0.00) [0]
540	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	327.70 (0.00) [0]
541	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [458.03]	428.69 (0.00) [0]
542	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	0.00 (0.00) [0]
	Steel				
543	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (10/2020) [2/2021]	1,154.18 (-) [1,154.18]	1,026.52 (0.00) [38]

544	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [12/2021]	1,034.01 (-) [1,034.01]	511.79 (0.00) [50]
545	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (5/2021) [5/2021]	262.87 (-) [262.87]	170.16 (0.00) [23]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
546	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (6/2021) [6/2021]	246.31 (-) [246.31]	115.20 (0.00) [16]
	<u>Human Resource Development</u>				
547	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (-) [9/2022]	851.00 (851.00) [851.00]	26.10 (0.00) [6]
	<u>Petroleum</u>				
548	BSVI UPGRADATION	9/2016	12/2019 (4/2021) [7/2021]	1,810.00 (1,810.00) [1,810.00]	1,501.84 (0.00) [19]
549	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	121.57 (0.00) [0]
550	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (-) [6/2023]	200.00 (-) [200.00]	0.00 (0.00) [0]
551	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [0/0]	749.00 (-) [842.00]	606.89 (93.00) [0]
552	HASSAN CHERLAPALLE LPG PIPELINE	3/2019	6/2022 (-) [6/2022]	2,156.33 (-) [2,156.33]	669.37 (0.00) [0]
553	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	79.52 (0.00) [0]
554	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [6/2021]	581.00 (637.00) [637.00]	390.06 (56.00) [15]
555	SETTING UP OF PHASE II FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (-) [11/2021]	380.00 (-) [380.00]	177.00 (0.00) [0]
556	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
557	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (5/2020) [1/2021]	445.89 (-) [445.89]	443.28 (0.00) [23]
	<u>Railways</u>				
558	ARSIKERE-TUMKUR	3/2015	3/2020 (-) [1/2021]	578.00 (-) [783.00]	607.76 (205.00) [10]
559	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2023]	986.30 (-) [986.30]	307.53 (0.00) [93]
560	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
561	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-)	327.25 (-)	0.00 (40.52)

			[12/2023]	[367.77]	[-]
562	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/	558.00	0.00
			(-)	(-)	(134.43)
			[12/2023]	[692.43]	[-]
563	GADAG-WADI NL	4/2013	12/2018	2,841.84	273.30
			(-)	(-)	(0.00)
			[12/2024]	[2,841.84]	[72]
564	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023	2,127.00	2,121.59
			(-)	(-)	(873.00)
			[12/2022]	[3,000.00]	[-3]
565	HUBLI- CHIKJAJUR	3/2015	3/2020	1,156.94	1,119.20
			(-)	(-)	(-16.00)
			[11/2021]	[1,140.94]	[20]
566	HUBLI-ANKOLA(NL),SWR	4/1997	/	2,315.00	156.88
			(-)	(-)	(1,596.65)
			[12/2024]	[3,911.65]	[-]
567	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017	644.78	462.84
			(-)	(-)	(245.22)
			[0/0]	[890.00]	[0]
568	MARIKUPPAM - KUPPAM	4/2012	3/2016	279.54	34.85
			(-)	(-)	(0.00)
			[12/2023]	[279.54]	[93]
569	SHIMOGA-HARIHAR NL	4/2011	3/2016	832.47	0.94
			(-)	(-)	(0.00)
			[3/2024]	[832.47]	[96]
570	TORANAGALLU-RANJITPURA DL	4/2011	/	146.75	0.34
			(-)	(-)	(20.75)
			[12/2023]	[167.50]	[-]
571	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/	1,801.01	66.44
			(-)	(-)	(165.99)
			[12/2021]	[1,977.01]	[-]
572	WHITE FIELD-KOLAR NL	4/2011	/	373.8	0.36
			(-)	(-)	(0.00)
			[12/2023]	[348.85]	[-]
	<u>Road Transport And Highways</u>				
573	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019	1,167.42	276.50
			(1/2021)	(-)	(-297.42)
			[12/2021]	[870.00]	[33]
574	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/	486.78	273.86
			(-)	(-)	(0.00)
			[0/0]	[486.78]	[0]
575	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016	1,655.01	1,867.51
			(-)	(-)	(0.00)
			[12/2020]	[1,655.01]	[52]
576	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019	701.40	95.50
			(-)	(-)	(0.00)
			[3/2022]	[701.40]	[36]
577	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019	870.00	36.30
			(-)	(-)	(0.00)
			[11/2020]	[870.00]	[0]
578	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019	157.32	0.00
			(-)	(188.00)	(0.00)
			[5/2021]	[157.32]	[24]
579	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018	171.60	0.86
			(-)	(-)	(0.00)
			[0/0]	[171.60]	[0]
580	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018	1,388.00	1,277.00
			(-)	(-)	(0.00)

			[0/0]	[1,388.00]	[0]
581	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [12/2020]	1,664.20 (-) [1,664.20]	936.78 (0.00) [8]
582	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [0/0]	946.00 (-) [946.00]	818.53 (0.00) [0]
583	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (386.40) [325.86]	326.88 (0.00) [0]
584	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
585	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
586	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
587	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
588	SIX LANING OF CHITRADURGA- DAVANGERE INCLUDING CHITRADURGA BYPASS (KM 189+000 TO KM 260+000 OF NH-48(C	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,134.00]	1,013.67 (440.84) [0]
589	SIX LANING OF DAVANGERE-HAVE RI FROM KM 260+000 TO KM 336+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.5 (-) [1,177.00]	900.64 (345.42) [0]
590	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,047.35 (272.20) [0]
591	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,080.15 (404.66) [-]
592	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
593	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
594	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [12/2020]	950.69 (-) [1,108.00]	1,425.26 (157.31) [16]
595	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
596	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO	11/2016	3/2017 (-)	314.90 (-)	104.40 (0.00)

	70.900 OF NH-150 UNDER EPC MODE IN THE STAT		[0/0]	[314.90]	[0]
597	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
598	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
599	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [0/0]	191.60 (-) [191.60]	26.24 (0.00) [0]
600	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	130.00 (0.00) [0]
601	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
602	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
603	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
604	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
605	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
606	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	<u>Urban Development</u>				
607	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [0/0]	26,405.14 (-) [26,405.14]	499.85 (0.00) [0]
	<u>KERALA</u>				
	<u>Health And Family Welfare</u>				
608	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	34.89 (0.00) [21]
	<u>Human Resource Development</u>				
609	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [6/2022]	753.63 (-) [753.63]	58.47 (0.00) [15]
610	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	118.52 (0.00) [0]
	<u>Petroleum</u>				

611	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	695.00 (395.24) [32]
612	LPG TERMINAL AT KOCHI	10/2015	10/2017 (2/2022) [3/2022]	607.06 (714.25) [714.25]	374.14 (107.19) [53]
613	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (2/2021) [2/2021]	3,313.00 (-) [3,288.96]	2,614.93 (-24.04) [12]
614	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [1/2021]	4,588.29 (-) [5,245.96]	4,808.25 (657.67) [29]
615	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	276.12 (0.00) [0]
Railways					
616	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (-) [2,815.62]	262.68 (1,249.62) [0]
617	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (189.24) [275.21]	6.73 (85.97) [0]
618	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (252.96) [369.55]	8.50 (116.59) [0]
619	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
620	TRIVANDRUM-KANAKKURU RAIL DOUBLING	2/2015	/ (-) [0/0]	1,131.50 (-) [1,411.00]	198.81 (0.00) [0]
621	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (828.00) [1,246.00]	0.81 (246.00) [0]
Road Transport And Highways					
622	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (1/2020) [1/2020]	845.24 (-) [941.00]	889.83 (95.76) [0]
623	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (10/2020) [3/2021]	804.97 (-) [804.97]	520.05 (0.00) [33]
624	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [5/2021]	1,124.11 (-) [1,232.76]	419.66 (108.65) [44]
625	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
626	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [0/0]	255.75 (348.00) [348.43]	290.12 (92.68) [0]
627	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [0]
Urban Development					
628	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (9/2020) [9/2020]	5,181.79 (6,218.14) [6,218.14]	6,031.09 (1,036.35) [0]

	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
629	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021 (-) [6/2021]	412.24 (-) [412.24]	0.00 (0.00) [0]
	<u>Coal</u>				
630	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2022]	869.44 (-) [869.44]	120.14 (0.00) [12]
631	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
632	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.85 (0.00) [0]
633	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	0.00 (0.00) [0]
634	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	20.99 (0.00) [0]
635	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	144.51 (0.00) [0]
636	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	0.87 (0.00) [0]
637	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	524.01 (0.00) [0]
638	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	54.76 (0.00) [0]
639	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	29.94 (0.00) [0]
640	NIGAHI EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
641	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	100.21 (0.00) [0]
642	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
643	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
644	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND	8/2017	6/2020 (9/2021) [9/2021]	236.00 (293.00) [293.00]	138.42 (57.00) [15]
	<u>Power</u>				
645	AMELIA COAL MINE	1/2017	9/2020 (-) [8/2022]	2,104.21 (-) [1,587.16]	454.82 (-517.05) [23]
646	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (10/2020) [2/2021]	11,638.55 (15,105.22) [15,105.22]	13,473.99 (3,466.67) [37]
647	KHARGONE STPP STAGE I (1320	3/2015	1/2020	9,870.51	10,019.31

	MW)		(-) [0/0]	(-) [11,148.86]	(1,278.35) [0]
	Railways				
648	ANUPPUR-KATNI	4/2015	12/2021 (12/2023) [12/2023]	1,370.00 (1,370.94) [1,370.94]	470.49 (0.94) [24]
649	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2021]	1,485.85 (-) [1,835.83]	1,450.82 (349.98) [12]
650	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (8/2020) [8/2020]	383.79 (-) [1,413.76]	1,416.77 (1,029.97) [0]
651	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (12/2021) [12/2021]	585.93 (-) [1,268.32]	941.56 (682.39) [34]
652	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [603.69]	232.01 (-96.31) [33]
653	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,763.93 (-) [1,762.94]	1,032.58 (-0.99) [36]
654	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2023]	582.13 (1,247.64) [1,247.64]	273.37 (665.51) [12]
655	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2023]	2,478.23 (-) [2,478.23]	477.93 (0.00) [12]
656	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [0/0]	174.00 (-) [174.00]	172.08 (0.00) [0]
657	RAMGANJMUNDI-BHOPAL (NL),WCF	1/2001	2/2021 (-) [3/2023]	42.6 (-) [2,909.99]	1,132.38 (2,485.39) [24]
658	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2024) [3/2024]	3,503.69 (5,912.40) [5,912.40]	2,118.69 (2,408.71) [24]
	Road Transport And Highways				
659	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (1/2021) [1/2021]	191.21 (-) [191.21]	117.80 (0.00) [14]
660	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (3/2021) [3/2021]	249.05 (-) [249.05]	191.67 (0.00) [32]
661	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	246.80 (0.00) [0]
662	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [8/2021]	950.27 (-) [950.27]	200.47 (0.00) [-]
663	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [6/2021]	392.33 (428.55) [428.55]	305.76 (36.22) [39]
664	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL- SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	195.73 (0.00) [0]
665	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-	9/2017	9/2017 (-)	374.40 (-)	213.11 (-169.75)

	12		[12/2020]	[204.65]	[39]
666	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	619.77 (0.00) [40]
667	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
668	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (12/2020) [6/2021]	390.51 (-) [390.51]	249.75 (0.00) [-]
669	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [0/0]	656.98 (-) [840.00]	35.00 (183.02) [0]
670	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [12/2021]	743.88 (-) [743.89]	115.40 (0.01) [-]
671	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [2/2022]	1,094.97 (-) [1,094.97]	220.12 (0.00) [-]
672	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [0/0]	217.96 (-) [884.00]	31.81 (666.04) [0]
673	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (6/2021) [6/2021]	205.05 (-) [205.05]	113.56 (0.00) [51]
674	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (-) [3/2021]	264.5 (-) [264.5]	55.12 (0.00) [0]
675	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [0/0]	960.24 (-) [960.24]	738.74 (0.00) [0]
676	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
677	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
678	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [6/2015]	928.83 (-) [928.83]	824.83 (0.00) [0]
679	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [5/2020]	794.30 (679.94) [691.38]	669.35 (-102.92) [0]
680	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [5/2020]	795.76 (686.13) [686.13]	669.94 (-109.63) [0]
681	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	771.23 (0.00) [0]
682	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [2/2021]	639.97 (-) [639.97]	447.94 (0.00) [40]
683	FOUR LANNING WORK FROM HIRAN	1/2018	/	770.73	280.75

	RIVER TO SINDOOR RIVER		(-) [7/2018]	(-) [770.73]	(0.00) [0]
684	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (4/2021) [4/2021]	957.54 (-) [957.54]	713.84 (0.00) [14]
685	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [4/2021]	497.05 (-) [881.05]	728.49 (384.00) [47]
686	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
687	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
688	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (1/2021) [3/2021]	628.45 (-) [628.45]	398.38 (0.00) [14]
689	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [3/2021]	410.72 (-) [410.72]	390.00 (0.00) [71]
690	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [12/2021]	990.97 (-) [990.97]	302.88 (0.00) [24]
691	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [5/2022]	1,047.00 (-) [1,047.00]	172.62 (0.00) [24]
692	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [4/2022]	847.00 (-) [847.00]	208.90 (0.00) [25]
693	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [0/0]	996.27 (-) [996.27]	200.45 (0.00) [0]
694	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (4/2021) [4/2021]	169.63 (-) [169.63]	29.65 (0.00) [37]
695	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [0/0]	178.23 (-) [178.23]	122.99 (0.00) [0]
696	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (9/2020) [11/2020]	287.34 (-) [287.34]	194.85 (0.00) [0]
697	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (3/2021) [3/2021]	877.79 (-) [877.79]	635.33 (0.00) [21]
698	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (2/2021) [2/2021]	235.91 (-) [235.91]	167.93 (0.00) [36]
699	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (5/2021) [5/2021]	809.16 (-) [809.16]	488.46 (0.00) [34]
700	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]

701	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [10/2021]	954.43 (-) [1,191.51]	235.61 (237.08) [73]
702	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (6/2021) [6/2021]	511.83 (-) [511.83]	354.95 (0.00) [46]
703	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (3/2021) [3/2021]	254.17 (-) [254.17]	164.68 (0.00) [37]
704	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (1/2021) [3/2021]	233.04 (-) [233.04]	151.12 (0.00) [36]
705	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (12/2020) [3/2021]	279.44 (-) [279.44]	156.14 (0.00) [36]
706	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (3/2021) [3/2021]	166.21 (173.41) [173.41]	139.19 (7.20) [31]
707	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (2/2021) [2/2021]	184.62 (-) [184.62]	105.89 (0.00) [36]
708	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (9/2021) [9/2021]	214.69 (-) [214.69]	49.85 (0.00) [42]
709	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (3/2021) [3/2021]	217.22 (226.88) [226.88]	160.76 (9.66) [31]
710	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (2/2021) [2/2021]	162.56 (-) [162.56]	124.81 (0.00) [35]
711	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 162 TO 266 OF NH-59A	11/2017	9/2019 (6/2021) [6/2021]	373.8 (-) [373.82]	173.84 (0.00) [21]
Urban Development					
712	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	114.13 (0.00) [0]
713	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	112.78 (0.00) [0]
MAHARASHTRA					
Civil Aviation					
714	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	475.39 (-) [475.39]	88.11 (0.00) [0]
Coal					
715	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	104.95 (44.53) [12]
716	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	243.41 (0.00) [0]
717	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	245.47 (0.00) [0]
718	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	277.08 (0.00) [0]
719	BELLORA-NAIGAON DEEP OC	11/2018	3/2021	252.71	98.99

			(-) [3/2021]	(-) [252.71]	(0.00) [0]
720	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	85.03 (221.74) [0]
721	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [0/0]	304.52 (-) [304.52]	141.26 (0.00) [0]
722	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	368.56 (0.00) [0]
723	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2024]	277.65 (-) [313.34]	140.64 (35.69) [36]
724	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	327.13 (0.00) [0]
725	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	178.62 (0.00) [0]
726	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [0/0]	295.56 (-) [295.56]	150.65 (0.00) [0]
727	SAONER I UG TO OC PHASE I	11/2016	3/2022 (-) [3/2022]	162.10 (-) [162.10]	36.94 (0.00) [0]
728	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	131.35 (0.00) [0]
729	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	218.1 (-) [313.1]	204.15 (0.00) [0]
	Fertilisers				
730	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (3/2021) [3/2021]	426.72 (-) [426.72]	303.87 (0.00) [11]
	Health And Family Welfare				
731	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [6/2021]	582.99 (-) [582.99]	424.09 (0.00) [-]
732	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	249.74 (0.00) [22]
	Human Resource Development				
733	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [6/2021]	223.37 (-) [223.37]	61.35 (0.00) [11]
	Petroleum				
734	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (12/2021) [9/2021]	249.26 (-) [249.26]	110.52 (0.00) [15]
735	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	261.00 (-) [261.00]	131.10 (0.00) [3]
736	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	122.92 (0.00) [3]
737	ADDITIONAL FACILITIES AT	5/2016	1/2021	348.00	111.62

	SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE		(-) [10/2021]	(-) [348.00]	(0.00) [9]
738	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2020) [3/2021]	861.79 (1,846.46) [1,846.46]	1,518.24 (984.67) [94]
739	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,203.71]	1,303.59 (-88.75) [0]
740	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,475.92) [3,596.00]	3,442.73 (-410.83) [0]
741	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-) [12/2021]	640.00 (-) [640.00]	278.71 (0.00) [0]
742	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2022]	2,494.68 (-) [2,354.72]	1,096.58 (-139.96) [0]
743	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [2/2022]	1,945.00 (-) [1,945.00]	1,437.61 (0.00) [6]
744	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2021) [5/2021]	3,190.69 (3,375.90) [3,375.90]	2,572.08 (185.21) [37]
745	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (2/2021) [2/2021]	449.58 (-) [449.58]	342.23 (0.00) [14]
746	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-I	4/2019	3/2022 (3/2022) [5/2022]	3,228.80 (3,376.47) [3,966.71]	922.04 (747.87) [14]
747	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (-) [5/2021]	3,670.11 (3,740.05) [3,740.05]	1,941.83 (79.34) [0]
748	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [0/0]	4,199.00 (5,060.00) [5,060.00]	4,183.90 (861.00) [0]
749	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (5/2021) [5/2021]	763.92 (-) [733.86]	584.33 (-30.06) [5]
750	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [1/2021]	282.64 (-) [282.64]	238.43 (0.00) [5]
	Power				
751	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
	Railways				
752	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (3/2020) [3/2020]	184.06 (199.12) [315.00]	312.62 (130.94) [0]
753	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2023]	2,271.50 (-) [4,517.49]	2,637.46 (2,245.99) [24]
754	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2022]	495.44 (-) [2,980.41]	1,756.68 (2,484.97) [216]
755	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	429.22 (205.27) [0]
756	DAUND-GULBARGA - DOUBLING	3/2009	3/2020	713.48	2,479.93

	(224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)		(-) [3/2021]	(-) [2,725.00]	(2,011.52) [12]
757	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
758	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
759	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	321.99 (0.00) [12]
760	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [1,377.48]	333.58 (584.59) [24]
761	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	240.75 (0.00) [24]
762	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (12/2020) [12/2020]	305.00 (-) [305.00]	268.50 (0.00) [21]
763	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
764	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2021]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [84]
765	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	1,199.46 (0.00) [-12]
766	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,125.00 (-) [5,311.13]	0.00 (2,916.68) [0]
767	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (2,753.05) [3,524.81]	952.24 (1,616.30) [9]
768	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
769	VAIBHAVWADI-KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
770	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
771	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (12/2024) [12/2024]	229.00 (852.50) [1,096.00]	39.79 (867.00) [36]
772	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	165.38 (0.00) [12]
773	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	408.70 (11.30) [12]
774	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,341.89 (0.00) [0]
775	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	248.22 (0.00) [24]
	<u>Road Transport And Highways</u>				

776	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
777	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
778	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
779	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	380.86 (0.00) [-]
780	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [4/2021]	621.00 (-) [621.00]	564.85 (0.00) [-]
781	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	854.98 (0.00) [0]
782	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [0/0]	744.64 (-) [982.00]	0.00 (237.36) [0]
783	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,048.10]	841.64 (-23.51) [-]
784	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	59.61 (0.00) [24]
785	4-LANNING OF MAHAGAON-YAVATMAL SECTION (KM 320.580 TO 400.575)	3/2017	3/2020 (-) [0/0]	1,098.06 (-) [1,100.41]	1,068.76 (62.58) [0]
786	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,112.22 (-) [1,142.62]	585.85 (0.00) [0]
787	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	324.00 (0.00) [0]
788	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [2/2021]	400.25 (-) [400.25]	89.63 (0.00) [23]
789	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [7/2021]	1,064.88 (-) [1,021.00]	235.12 (-43.88) [-]
790	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [11/2020]	1,059.73 (-) [1,071.00]	610.87 (11.27) [0]
791	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [0/0]	1,030.44 (-) [1,065.51]	1,015.76 (35.07) [0]
792	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (-) [1,043.28]	1,035.00 (54.94) [0]
793	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [6/2021]	505.00 (-) [504.00]	333.68 (-1.00) [37]
794	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [0/0]	422.38 (-) [422.38]	179.58 (0.00) [0]
795	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-)	955.40 (-)	409.50 (0.00)

			[0/0]	[955.40]	[0]
796	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [0/0]	211.42 (-) [211.42]	136.85 (0.00) [0]
797	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	49.24 (0.00) [0]
798	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	159.98 (0.00) [0]
799	AMDNI TO SAONER	1/2017	6/2019 (-) [0/0]	396.91 (397.00) [396.91]	264.48 (0.00) [0]
800	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [0/0]	426.06 (426.00) [426.06]	118.97 (0.00) [0]
801	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [0/0]	309.94 (310.00) [309.94]	181.32 (0.00) [0]
802	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	116.75 (0.00) [0]
803	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS- 62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	151.11 (0.00) [0]
804	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [0/0]	241.69 (242.00) [241.69]	149.29 (0.00) [0]
805	BARASGAON TO RANATEE	7/2016	9/2018 (-) [4/2021]	239.1 (291.0) [239.1]	57.82 (0.00) [31]
806	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [0/0]	259.55 (260.00) [259.55]	199.07 (0.00) [0]
807	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	264.60 (0.00) [0]
808	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2021]	743.21 (743.00) [743.21]	137.87 (0.00) [0]
809	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	188.64 (0.90) [0]
810	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	124.95 (0.00) [0]
811	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [0/0]	206.97 (207.00) [206.97]	120.05 (0.00) [0]
812	CHIKALI TO DHAD	3/2018	12/2019 (-) [0/0]	189.46 (189.00) [189.46]	96.54 (0.00) [0]
813	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [0/0]	548.03 (548.00) [548.03]	353.00 (0.00) [0]
814	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [0/0]	393.10 (393.00) [393.10]	213.97 (0.00) [0]
815	CHIMUR TO WARORA	11/2016	3/2019 (-)	467.70 (-)	147.72 (0.00)

			[0/0]	[467.70]	[0]
816	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	71.45 (0.00) [-]
817	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2021) [12/2021]	649.50 (-) [649.50]	184.90 (0.00) [33]
818	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (8/2021) [11/2021]	291.53 (-) [291.53]	122.48 (0.00) [-]
819	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [0/0]	244.90 (-) [244.90]	251.87 (0.00) [0]
820	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (6/2021) [9/2021]	289.21 (-) [289.21]	126.45 (0.00) [-]
821	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2021) [6/2021]	593.26 (-) [690.17]	572.57 (96.91) [37]
822	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
823	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (6/2021) [6/2021]	531.13 (-) [730.97]	614.25 (199.84) [37]
824	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	80.00 (0.00) [0]
825	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
826	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	57.96 (-89.53) [0]
827	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (-) [414.00]	408.40 (-0.51) [0]
828	DAHEGAON TO KUHI	1/2017	6/2019 (-) [0/0]	228.89 (229.00) [228.89]	152.00 (0.00) [0]
829	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [0/0]	182.63 (-) [182.63]	132.40 (0.00) [0]
830	DEORI TO AMGAON	1/2017	5/2019 (-) [0/0]	409.62 (410.00) [409.62]	155.78 (0.00) [0]
831	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [0/0]	219.91 (-) [219.91]	123.76 (0.00) [0]
832	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200	3/2017	3/2020 (-) [0/0]	296.19 (-) [254.00]	254.85 (-42.19) [0]

	TO KM 723.000)				
833	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [0/0]	336.21 (336.00) [336.21]	142.66 (0.00) [0]
834	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [0/0]	217.14 (217.00) [217.14]	128.77 (0.00) [0]
835	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [0/0]	391.06 (391.00) [391.06]	173.00 (0.00) [0]
836	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	185.74 (0.00) [0]
837	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
838	FOUR LANING OF AKKALKOT- SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [807.00]	617.58 (164.87) [-]
839	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (12/2018) [9/2020]	1,871.34 (2,754.00) [1,871.34]	3,443.43 (0.00) [0]
840	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [0/0]	904.16 (-) [904.16]	855.25 (0.00) [0]
841	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [524.15]	250.31 (0.00) [0]
842	HELWAK TO KARAI	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	139.40 (0.00) [0]
843	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [0/0]	294.87 (295.00) [294.87]	68.30 (0.00) [0]
844	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [0/0]	355.17 (-) [355.17]	268.87 (0.00) [0]
845	INDAPUR TO VADPALE	1/2017	12/2019 (-) [0/0]	1,202.52 (1,203.00) [1,202.52]	648.90 (0.00) [0]
846	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [0/0]	461.96 (-) [461.96]	178.43 (0.00) [0]
847	JALGAON TO BHADGAON	1/2018	11/2019 (-) [0/0]	307.54 (308.00) [307.54]	101.59 (0.00) [0]
848	JALGAON TO NANDURA	3/2018	12/2019 (-) [0/0]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
849	JALKOT TO TOGRI	7/2018	8/2020 (-) [0/0]	299.92 (300.00) [299.92]	66.25 (0.00) [0]
850	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (-) [356.66]	80.88 (0.00) [0]
851	KAIJ TO KUSALAM	1/2017	7/2019 (-) [0/0]	554.78 (-) [554.78]	221.90 (0.00) [0]
852	KALMAB TO RALEGAON	1/2017	6/2019	467.78	317.91

			(-) [0/0]	(-) [467.78]	(0.00) [0]
853	KALMATH TO ZARAP	9/2016	3/2020 (-) [0/0]	1,338.13 (1,338.00) [1,338.13]	961.51 (0.00) [0]
854	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	624.61 (0.00) [0]
855	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [0/0]	407.19 (407.00) [407.19]	108.68 (0.00) [0]
856	KARAD TO TAGAON	1/2017	6/2019 (-) [0/0]	537.81 (538.00) [537.81]	117.97 (0.00) [0]
857	KARAD TO VITA	1/2018	12/2019 (-) [0/0]	344.85 (245.00) [344.85]	115.08 (0.00) [0]
858	KARWANDI TO RAJURI	3/2018	12/2019 (-) [0/0]	276.95 (277.00) [276.95]	255.47 (0.00) [0]
859	KATOL TO WARUD	1/2017	6/2019 (-) [0/0]	463.62 (664.00) [463.62]	247.48 (0.00) [0]
860	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [0/0]	249.29 (-) [249.29]	139.20 (0.00) [0]
861	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [0/0]	203.21 (203.00) [203.21]	173.79 (0.00) [0]
862	KHERDA TO NAGZARI	3/2018	12/2019 (-) [0/0]	121.3 (-) [121.3]	138.50 (0.00) [0]
863	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	227.93 (0.00) [0]
864	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [0/0]	281.78 (282.00) [281.78]	362.73 (0.00) [0]
865	KOTHARI TO DHANORA	9/2018	8/2020 (-) [0/0]	301.38 (301.00) [301.38]	152.42 (0.00) [0]
866	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	290.69 (0.00) [0]
867	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [0/0]	225.25 (225.00) [225.25]	254.75 (0.00) [0]
868	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	180.17 (0.00) [0]
869	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [0/0]	243.45 (244.00) [243.45]	111.00 (0.00) [0]
870	LATUR TO PANGAON	3/2018	12/2019 (-) [0/0]	336.47 (336.00) [336.47]	186.18 (0.00) [0]
871	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [0/0]	237.40 (-) [237.40]	8.34 (0.00) [0]
872	MAJALGAON TO KAIJ	1/2017	7/2019 (-)	413.99 (-)	299.10 (0.00)

			[0/0]	[413.99]	[0]
873	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [0/0]	256.15 (-) [256.15]	82.00 (0.00) [0]
874	MALEGAON TO RISOD	2/2018	12/2019 (-) [0/0]	303.24 (303.00) [303.24]	223.97 (0.00) [0]
875	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [0/0]	322.55 (-) [322.55]	189.91 (0.00) [0]
876	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [0/0]	457.52 (-) [457.52]	352.94 (0.00) [0]
877	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [0/0]	222.13 (222.00) [222.13]	113.63 (0.00) [0]
878	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [0/0]	228.54 (-) [228.54]	162.30 (0.00) [0]
879	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [0/0]	418.36 (-) [418.36]	270.13 (0.00) [0]
880	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [0/0]	486.19 (-) [486.19]	264.50 (0.00) [0]
881	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	105.51 (0.00) [0]
882	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	229.08 (0.00) [0]
883	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	483.6 (-) [488.60]	213.71 (0.00) [0]
884	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	192.29 (0.00) [0]
885	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	289.90 (0.00) [0]
886	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [0/0]	162.34 (-) [162.34]	34.80 (0.00) [0]
887	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [0/0]	376.72 (377.00) [376.72]	224.81 (0.00) [0]
888	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	222.60 (0.00) [0]
889	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (6/2021) [12/2021]	546.00 (-) [546.00]	298.39 (0.00) [29]
890	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (6/2021) [12/2021]	591.66 (-) [591.66]	313.00 (0.00) [29]
891	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [0/0]	244.04 (244.00) [244.04]	104.94 (0.00) [0]
892	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [0/0]	274.50 (275.00) [274.50]	146.39 (0.00) [0]

893	NANDED TO JALKOT	12/2017	9/2019 (-) [0/0]	456.93 (457.00) [456.93]	158.00 (0.00) [0]
894	NANDGAON TO MORSHI	1/2017	6/2019 (-) [0/0]	385.87 (386.00) [385.87]	233.75 (0.00) [0]
895	NASHIK TO PETH	12/2015	11/2018 (-) [0/0]	289.60 (-) [289.60]	213.10 (0.00) [0]
896	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [0/0]	406.54 (407.00) [406.54]	127.00 (0.00) [0]
897	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [0/0]	420.63 (421.00) [420.63]	75.68 (0.00) [0]
898	OMREGA TO AUSA	3/2018	12/2019 (-) [0/0]	272.04 (272.00) [272.04]	186.24 (0.00) [0]
899	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [0/0]	344.25 (344.00) [344.25]	66.18 (0.00) [0]
900	PAHUR TO BODHWAD	1/2017	5/2020 (-) [0/0]	244.93 (-) [244.93]	123.23 (0.00) [0]
901	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	128.89 (0.00) [0]
902	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [0/0]	227.19 (227.00) [227.19]	125.23 (0.00) [0]
903	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [0/0]	381.03 (382.00) [381.03]	7.03 (0.00) [0]
904	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
905	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [0/0]	238.19 (238.00) [238.19]	95.85 (0.00) [0]
906	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [0/0]	205.72 (206.00) [205.72]	30.42 (0.00) [0]
907	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	651.15 (0.00) [0]
908	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [0/0]	420.57 (-) [420.57]	231.39 (0.00) [0]
909	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [0/0]	170.00 (-) [170.00]	81.57 (0.00) [0]
910	PEN TO KHOPOLI	3/2018	3/2018 (-) [0/0]	301.39 (302.00) [301.39]	22.09 (0.00) [0]
911	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [0/0]	595.77 (-) [595.77]	220.44 (0.00) [0]
912	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [0/0]	223.46 (-) [223.46]	26.42 (0.00) [0]
913	PUNE TO MALE VILLAGE	3/2018	12/2019	228.31	73.50

			(-) [0/0]	(-) [228.31]	(0.00) [0]
914	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [3/2021]	1,724.55 (-) [1,724.55]	2,540.00 (0.00) [96]
915	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	125.69 (0.00) [0]
916	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	300.50 (0.00) [0]
917	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	87.11 (0.00) [0]
918	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (12/2020) [12/2020]	536.65 (634.30) [536.65]	531.46 (0.00) [12]
919	RISOD TO HINGOLI	2/2018	12/2019 (-) [0/0]	355.99 (-) [355.99]	230.97 (0.00) [0]
920	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [0/0]	362.96 (-) [362.96]	54.83 (0.00) [0]
921	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [0/0]	415.25 (415.25) [415.25]	202.22 (0.00) [0]
922	SANGOLA TO JATH	1/2018	12/2019 (-) [0/0]	257.3 (257.3) [257.3]	129.26 (0.00) [0]
923	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	137.63 (0.00) [0]
924	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	125.53 (0.00) [0]
925	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	187.77 (0.00) [0]
926	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	240.12 (0.00) [0]
927	SELDOH TO PANVAR	7/2018	5/2020 (-) [0/0]	404.33 (404.00) [404.33]	22.40 (0.00) [0]
928	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [0/0]	150.79 (-) [150.79]	40.42 (0.00) [0]
929	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [0/0]	373.10 (373.00) [373.10]	266.43 (0.00) [0]
930	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [0/0]	211.34 (-) [211.34]	112.83 (0.00) [0]
931	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	177.79 (0.00) [0]
932	SHIVUR TO YEOLA	3/2018	12/2019 (-)	181.08 (-)	35.50 (0.00)

			[0/0]	[181.08]	[0]
933	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	94.22 (0.00) [0]
934	SIX LANING OF PIMPALGAON- NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (-) [448.18]	385.69 (43.24) [0]
935	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [0/0]	290.73 (-) [315.00]	309.40 (24.27) [0]
936	TAKARKHED TO JALNA	9/2017	6/2019 (-) [0/0]	417.90 (418.00) [417.90]	192.26 (0.00) [0]
937	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [0/0]	264.41 (264.00) [264.41]	70.71 (0.00) [0]
938	TALGAON TO KALMATH	10/2016	3/2020 (-) [0/0]	904.70 (905.00) [904.70]	630.05 (0.00) [0]
939	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [0/0]	195.64 (196.00) [195.64]	114.17 (0.00) [0]
940	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	247.01 (0.00) [0]
941	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [0/0]	1,598.47 (1,560.00) [1,598.47]	858.91 (0.00) [0]
942	VITA TO NAGAJ	3/2018	12/2019 (-) [0/0]	30.5 (305.0) [304.58]	26.82 (0.00) [0]
943	WADI TO ASOLA	1/2017	9/2019 (-) [0/0]	363.82 (364.00) [363.82]	26.34 (0.00) [0]
944	WADIGODRI TO DHANGRI PIMPRI	3/2018	2/2020 (-) [0/0]	194.23 (194.00) [194.23]	93.23 (0.00) [0]
945	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [0/0]	376.19 (-) [376.19]	46.03 (0.00) [0]
946	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	797.60 (0.00) [0]
947	WARDHA TO ARVI	2/2018	4/2020 (-) [0/0]	313.58 (-) [313.58]	60.09 (0.00) [0]
948	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [0/0]	216.90 (217.00) [216.90]	103.20 (0.00) [0]
949	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [0/0]	165.51 (-) [165.51]	149.54 (0.00) [0]
950	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
951	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Telecommunications</u>				

952	CONVERGENT BILLING AND CRM(MUMBAI)	1/2006	2/2007 (-) [0/0]	247.00 (-) [247.00]	0.00 (0.00) [0]
	<u>Urban Development</u>				
953	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [0/0]	23,136.00 (-) [23,136.00]	0.00 (0.00) [0]
954	NAGPUR METRO RAIL	8/2014	3/2018 (-) [0/0]	8,680.00 (-) [8,680.00]	7,068.52 (0.00) [0]
955	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (-) [11,420.00]	5,234.40 (0.00) [0]
	<u>Water Resources</u>				
956	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [0/0]	233.57 (-) [233.57]	32.20 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
957	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
958	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2023]	4,454.17 (-) [12,264.15]	10,584.54 (7,809.98) [144]
	<u>Road Transport And Highways</u>				
959	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2021]	235.31 (-) [235.31]	158.59 (0.00) [0]
960	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2021 (-) [10/2021]	577.5 (-) [457.77]	151.85 (-59.80) [36]
	<u>MEGHALAYA</u>				
	<u>Culture Development</u>				
961	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	144.00 (0.00) [42]
	<u>Health And Family Welfare</u>				
962	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	227.35 (0.00) [43]
	<u>Human Resource Development</u>				
963	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [12/2020]	484.32 (-) [626.26]	0.00 (141.94) [75]
	<u>Railways</u>				
964	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [4,083.02]	263.67 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
965	IMPROVEMENT/WIDENING TO 2- LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	83.90 (0.00) [0]
966	TWO LANING WITH PS OF JOWAI -	12/2015	5/2018	479.20	712.89

	MEHALAYA /ASSAM BORDER SECTION OF NH-44		(-) [0/0]	(-) [479.20]	(0.00) [0]
967	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	88.81 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
968	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [12/2023]	2,393.47 (-) [5,521.45]	3,781.94 (3,127.98) [117]
	<u>Road Transport And Highways</u>				
969	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2021) [6/2021]	195.04 (-) [377.99]	325.42 (182.95) [128]
970	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2020) [12/2020]	186.96 (-) [322.24]	292.10 (135.28) [75]
971	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (5/2016) [6/2021]	193.69 (-) [327.92]	295.96 (134.23) [128]
972	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	519.09 (-) [519.09]	65.01 (0.00) [0]
973	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	642.96 (-) [642.96]	22.97 (0.00) [0]
974	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	473.1 (-) [473.18]	38.63 (0.00) [0]
975	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	640.07 (-) [640.07]	15.79 (0.00) [0]
976	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	537.82 (-) [537.82]	53.86 (0.00) [0]
977	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (10/2020) [0/0]	404.29 (-) [404.29]	24.74 (0.00) [0]
978	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	428.11 (-) [428.11]	52.08 (0.00) [0]
979	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [0/0]	518.53 (-) [518.53]	56.74 (0.00) [0]
980	WIDENING TO 2 LANE, RE- ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2020]	624.41 (-) [992.67]	890.74 (368.26) [117]
	<u>MULTI STATE</u>				
	<u>Coal</u>				

981	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
982	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	35.65 (0.00) [0]
983	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	260.46 (0.00) [0]
984	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	226.05 (0.00) [0]
	<u>Commerce And Industry</u>				
985	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (1/2014) [7/2021]	12,579.09 (-) [13,812.30]	7,305.07 (1,233.21) [22]
	<u>Human Resource Development</u>				
986	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	8/2018	3/2019 (-) [0/0]	418.00 (-) [418.00]	110.00 (0.00) [0]
987	STUDY IN INDIA	3/2018	4/2018 (-) [0/0]	150.00 (-) [150.00]	0.00 (0.00) [0]
	<u>Petroleum</u>				
988	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [8/2021]	1,823.00 (-) [3,027.90]	1,685.17 (1,204.90) [8]
989	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTION PHASE II	9/2016	12/2019 (-) [4/2021]	571.66 (-) [571.66]	450.70 (0.00) [16]
990	BARAUNI-GUWAHATI PIPELINE	6/2013	12/2021 (-) [12/2021]	3,378.00 (3,060.00) [3,060.00]	1,998.30 (-248.00) [0]
991	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	71.11 (0.00) [0]
992	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	3,437.00 (3,048.00) [3,048.00]	1,659.30 (-389.00) [12]
993	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	2.70 (0.00) [0]
994	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2021]	2,433.00 (-) [2,433.00]	1,925.10 (0.00) [6]
995	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (8/2022) [8/2022]	2,677.00 (3,072.00) [3,072.00]	1,825.04 (395.00) [14]
996	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (5,909.00) [5,909.00]	3,470.70 (2,994.00) [110]
997	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [3/2021]	2,881.40 (-) [2,000.00]	1,542.50 (-881.40) [3]
998	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [10/2020]	1,879.00 (-) [1,689.00]	1,694.25 (-190.00) [0]

999	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	397.60 (0.00) [0]
1000	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [3/2021]	2,321.00 (-) [3,338.00]	2,724.32 (1,017.00) [3]
1001	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (2/2021) [2/2021]	690.00 (-) [690.00]	494.64 (0.00) [31]
1002	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2021]	406.00 (-) [406.00]	176.37 (0.00) [5]
1003	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [3/2021]	352.56 (-) [490.24]	445.41 (137.68) [48]
1004	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	113.30 (0.00) [0]
	<u>Power</u>				
1005	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (4/2020) [5/2020]	198.49 (-) [198.49]	140.67 (0.00) [0]
1006	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2021]	4,754.42 (-) [9,151.56]	1,893.34 (4,397.14) [36]
1007	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [2/2021]	358.83 (-) [358.83]	234.30 (0.00) [9]
1008	EASTERN REGION STRENGTHENING SCHEME-V	12/2013	4/2016 (4/2020) [7/2020]	1,344.2 (1,811.1) [1,891.41]	1,315.85 (526.89) [0]
1009	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2020) [2/2021]	522.29 (546.36) [546.36]	477.58 (24.07) [51]
1010	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [2/2021]	3,500.00 (3,500.00) [3,500.00]	2,724.70 (0.00) [7]
1011	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (9/2020) [3/2021]	235.53 (-) [235.53]	146.71 (0.00) [21]
1012	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (4/2020) [3/2021]	322.30 (-) [322.30]	195.52 (0.00) [25]
1013	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [3/2021]	197.40 (-) [197.40]	89.15 (0.00) [36]
1014	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [0/0]	3,519.59 (-) [3,519.59]	2,562.41 (0.00) [0]
1015	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [2/2021]	5,070.13 (-) [5,070.13]	3,989.71 (0.00) [10]
1016	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALAR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (5/2020) [3/2021]	14,733.37 (-) [14,733.37]	11,217.10 (0.00) [16]

1017	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (9/2020) [3/2021]	1,931.39 (-) [1,931.39]	1,564.64 (0.00) [13]
1018	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2021]	5,111.33 (-) [6,700.00]	2,430.27 (1,588.67) [36]
1019	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (14,719.10) [14,719.10]	12,864.61 (3,588.91) [103]
1020	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [0/0]	283.72 (-) [283.72]	196.10 (0.00) [0]
1021	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [0/0]	3,654.00 (-) [3,654.00]	3,508.04 (0.00) [0]
1022	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [0/0]	608.24 (-) [608.24]	425.04 (0.00) [0]
1023	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [0/0]	203.28 (-) [260.03]	200.16 (56.75) [0]
1024	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (6/2020) [3/2021]	379.95 (-) [379.95]	210.09 (0.00) [15]
1025	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [0/0]	487.49 (-) [339.41]	590.30 (151.97) [0]
1026	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2011 (6/2020) [1/2021]	4,844.72 (5,011.14) [5,071.94]	4,623.08 (247.82) [99]
1027	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (12/2020) [1/2021]	871.62 (-) [871.62]	640.30 (0.00) [39]
1028	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (4/2020) [4/2020]	408.46 (482.64) [482.64]	412.53 (74.18) [0]
1029	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [0/0]	5,151.37 (-) [5,151.37]	3,269.93 (0.00) [0]
1030	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (5/2020) [3/2021]	808.63 (-) [808.63]	627.32 (0.00) [38]
1031	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [3/2021]	374.63 (-) [374.63]	238.32 (0.00) [59]
Railways					
1032	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	9,576.52 (0.00) [0]
1033	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2021]	288.35 (-) [418.09]	412.89 (129.74) [-]
1034	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.12 (-200.00) [-]

1035	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2022) [6/2021]	704.31 (-) [927.94]	517.35 (223.63) [15]
1036	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2022]	175.80 (-) [270.72]	279.67 (94.92) [-]
1037	CHANDIGARH-BADDI	4/2007	3/2023 (3/2025) [3/2025]	328.14 (1,540.13) [1,540.13]	241.62 (1,211.99) [24]
1038	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON- PORAMAHESTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1039	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (3/2024) [3/2024]	523.52 (-) [2,300.00]	2.28 (1,776.48) [-]
1040	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2022]	295.00 (-) [477.31]	497.06 (182.31) [37]
1041	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	112.02 (651.22) [0]
1042	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA- SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	103.51 (173.89) [96]
1043	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2023) [3/2023]	1,347.26 (1,347.26) [1,347.26]	883.18 (0.00) [12]
1044	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAF (NL)	4/2007	3/2022 (3/2025) [3/2025]	1,640.04 (1,640.04) [1,640.04]	860.64 (0.00) [36]
1045	DANKUNI-CHANDA PUR 4TH LINE 1ST PHASE OF DANKUNI- SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2011	3/2017 (-) [3/2025]	365.1 (-) [340.10]	359.71 (-25.07) [96]
1046	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2023]	336.91 (791.39) [791.39]	567.14 (454.48) [-]
1047	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	637.87 (818.35) [133]
1048	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1049	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1050	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1051	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.55 (134.08) [0]
1052	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (4/2021) [4/2021]	511.86 (1,756.00) [2,005.25]	1,777.22 (1,493.39) [12]
1053	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1054	GWALIOR-SEOPURKALA WITH	4/2011	3/2022	2,912.96	148.26

	EXTENSION TO KOTA (GC)		(-) [12/2024]	(-) [3,845.60]	(932.64) [33]
1055	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [2/2021]	678.54 (678.54) [678.54]	708.22 (0.00) [23]
1056	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [663.13]	502.41 (120.95) [12]
1057	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	11.05 (88.07) [-]
1058	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1059	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2021]	1,614.59 (-) [1,870.41]	1,274.19 (255.82) [24]
1060	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.74 (0.00) [28]
1061	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [3/2025]	166.89 (-) [166.89]	0.02 (0.00) [-]
1062	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [6/2021]	625.00 (-) [859.00]	850.50 (234.00) [63]
1063	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2024]	2,132.77 (-) [2,132.77]	346.93 (0.00) [120]
1064	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONG WITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	92.5 (-) [995.10]	636.20 (71.58) [108]
1065	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [3/2025]	174.56 (-) [174.56]	71.43 (0.00) [-]
1066	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,222.16 (0.00) [36]
1067	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (3/2025) [3/2024]	1,856.95 (-) [1,952.68]	487.47 (95.73) [12]
1068	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [12/2021]	270.14 (-) [457.08]	439.49 (186.94) [-]
1069	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	149.30 (138.71) [228]
1070	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,131.17 (8,000.84) [202]
1071	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	105.99 (0.00) [132]
1072	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2027]	120.70 (-) [2,172.16]	232.66 (2,051.46) [105]
1073	MAGRAHAT-DIAMOND HARBOUR	4/2009	2/2012	499.96	162.75

	WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL		(-) [3/2025]	(-) [680.68]	(180.72) [157]
1074	MONIGRAM- NIMTITA	4/2012	/	250.93	332.10
			(-) [3/2024]	(-) [310.70]	(59.77) [-]
1075	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000	1,723.00	1,078.84
			(-) [3/2023]	(1.00) [3,472.59]	(1,749.59) [276]
1076	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020	414.84	152.23
			(-) [3/2023]	(-) [750.00]	(335.16) [36]
1077	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012	450.00	714.78
			(-) [3/2024]	(-) [2,200.00]	(1,750.00) [140]
1078	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005	494.54	32.00
			(-) [3/2025]	(-) [494.59]	(0.05) [240]
1079	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020	242.22	73.97
			(-) [0/0]	(-) [471.00]	(228.78) [0]
1080	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/	241.52	287.09
			(-) [12/2021]	(-) [373.87]	(132.35) [-]
1081	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019	1,798.00	29.84
			(-) [3/2023]	(2,047.51) [2,042.51]	(244.51) [48]
1082	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING R LINE AND MM CHALSA MAYAL RAJABHATKHOWA PAINTI	4/1999	/	819.23	1,082.01
			(-) [0/0]	(-) [1,811.00]	(1,051.77) [0]
1083	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008	1,180.19	3,595.72
			(-) [2/2021]	(4,541.38) [5,071.38]	(3,891.19) [146]
1084	PHULERA - DIGANA DOUBLING	5/2015	3/2020	600.00	155.47
			(-) [4/2022]	(-) [780.00]	(180.00) [25]
1085	PIRPAINTI-BHAGALPUR	4/2011	/	261.38	535.20
			(-) [5/2019]	(-) [516.05]	(254.67) [0]
1086	PIRPAINTI-JASIDIH	4/2013	3/2022	915.98	341.26
			(-) [3/2025]	(-) [2,137.81]	(1,221.83) [36]
1087	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017	299.60	1.12
			(-) [3/2026]	(-) [335.62]	(36.02) [108]
1088	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/	2,082.75	186.12
			(-) [0/0]	(-) [4,262.36]	(2,179.61) [0]
1089	RAYADURGA-TUMKUR NL	4/2007	/	2,062.30	1,096.12
			(-) [3/2025]	(-) [2,432.50]	(370.20) [-]
1090	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/	297.47	52.09
			(-) [3/2025]	(-) [298.22]	(0.75) [-]
1091	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016	277.28	180.03
			(-) [3/2025]	(-) [266.32]	(-10.96) [108]
1092	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/	296.00	0.00
			(-)	(-)	(170.65)

			[12/2023]	[466.65]	[-]
1093	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	0.00 (811.34) [-]
1094	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1095	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [0/0]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1096	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [6/2021]	860.43 (-) [1,147.00]	877.08 (286.57) [15]
	Road Transport And Highways				
1097	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1098	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [3/2021]	1,928.22 (-) [2,945.00]	2,467.00 (1,016.78) [71]
1099	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1100	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [962.00]	0.00 (-36.70) [0]
1101	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [11/2021]	604.00 (-) [361.51]	334.71 (-239.41) [0]
1102	MUZAFFARNAGAR HARIDWAR	9/2011	3/2013 (-) [11/2020]	754.0 (-) [754.00]	1,364.18 (0.00) [0]
1103	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [5/2021]	1,244.10 (-) [1,244.10]	1,547.00 (0.00) [-]
1104	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,848.49 (0.00) [0]
1105	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	2,901.20 (531.45) [105]
	Shipping And Ports				
1106	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	5,369.18 (-) [4,633.81]	1,787.23 (-735.37) [0]
	Telecommunications				
1107	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES	5/2006	3/2009 (-) [0/0]	1,077.00 (-) [1,077.00]	0.00 (0.00) [0]
1108	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [6/2021]	13,334.00 (-) [24,664.00]	15,239.00 (11,330.00) [71]
1109	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
1110	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE	3/2020	6/2021 (-) [11/2021]	431.16 (431.00) [431.16]	0.00 (0.00) [5]

	OF THE ART				
	<u>Urban Development</u>				
1111	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	2,467.77 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1112	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1113	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2023]	2,326.52 (7,114.55) [6,911.44]	1,045.72 (4,584.92) [96]
	<u>Road Transport And Highways</u>				
1114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	58.12 (0.00) [44]
1115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	50.62 (0.00) [48]
1116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	92.97 (-90.38) [0]
1117	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [8/2020]	387.00 (-) [387.00]	240.72 (0.00) [0]
1118	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	50.00 (375.4) [336.49]	53.00 (-163.60) [0]
1119	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	87.30 (0.00) [0]
1120	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
1121	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	89.79 (0.00) [46]
1122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	62.00 (0.00) [39]
1123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	77.08 (0.00) [39]
1124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	68.26 (0.00) [38]
1125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	49.94 (0.00) [39]

	FROM EXISTING KM 20.456 TO				
1126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	25.76 (0.00) [49]
1127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	28.46 (0.00) [50]
1128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	92.10 (0.00) [0]
1129	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	79.85 (0.00) [0]
1130	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [0/0]	373.07 (-) [387.00]	272.09 (13.93) [0]
1131	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (-) [339.55]	267.34 (-56.97) [0]
1132	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [0/0]	429.52 (-) [340.00]	227.18 (-89.52) [0]
1133	IMPROVEMENT OF INFRASTRUCTURE OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2020]	336.2 (36.9) [336.2]	278.10 (0.00) [0]
1134	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	98.42 (0.00) [0]
1135	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	123.44 (0.00) [0]
1136	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1137	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	38.85 (0.00) [0]
	ODISHA				
	Coal				
1138	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [362.50]	362.50 (155.22) [108]
1139	BALRAM EXPANSION OCP	12/2007	3/2010 (3/2029) [3/2029]	172.08 (3,504.21) [646.01]	646.01 (473.93) [228]
1140	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	274.63 (0.00) [60]
1141	BHUBANESWARI OCP, MCL (20.0	12/2007	3/2017	490.10	586.86

	MTY)		(-) [3/2031]	(-) [586.86]	(96.76) [168]
1142	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2024]	1,375.38 (-) [1,375.38]	494.67 (0.00) [36]
1143	GOPAL JI KANIHA OCP, MCL	12/2007	3/2013 (3/2028) [3/2028]	457.77 (8,416.19) [684.32]	684.32 (226.55) [180]
1144	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2022]	479.53 (-) [491.85]	491.85 (12.32) [108]
1145	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	173.89 (0.00) [0]
1146	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2024]	289.03 (-) [289.03]	114.36 (0.00) [72]
1147	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,217.77 (0.00) [0]
1148	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,971.87 (0.00) [0]
1149	TALABIRA II AND III OCP	7/2017	7/2020 (-) [4/2020]	2,401.07 (-) [2,401.07]	815.93 (0.00) [0]
	Human Resource Development				
1150	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [0/2022]	790.79 (-) [790.79]	122.02 (0.00) [3]
	Mines				
1151	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (12/2022) [12/2022]	5,540.00 (6,435.90) [5,540.00]	614.13 (0.00) [20]
1152	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [2/2021]	355.00 (-) [355.00]	93.16 (0.00) [3]
1153	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.74 (0.00) [0]
1154	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [0/0]	534.00 (-) [534.00]	330.50 (0.00) [0]
	Petroleum				
1155	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	34.73 (0.00) [0]
1156	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [8/2022]	1,607.00 (-) [1,607.00]	168.73 (0.00) [0]
1157	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	2.38 (0.00) [0]
1158	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	180.63 (0.00) [0]
1159	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	84.25 (0.00) [0]

1160	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	68.12 (0.00) [0]
1161	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,933.00 (-) [1,933.00]	1,174.60 (0.00) [12]
1162	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	2,259.24 (0.00) [0]
1163	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	1,432.60 (0.00) [0]
1164	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	0.22 (0.00) [0]
1165	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (-) [9/2022]	371.00 (-) [371.00]	1.80 (0.00) [0]
1166	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	72.66 (0.00) [0]
1167	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [3/2022]	161.59 (-) [161.59]	45.32 (0.00) [27]
1168	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	541.64 (0.00) [0]
Power					
1169	DARLIPALLI STPP STAGE-II 2X800 MW)	2/2014	12/2021 (2/2021) [3/2021]	12,532.14 (-) [13,740.53]	11,441.91 (1,208.09) [27]
1170	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [0/0]	1,885.13 (-) [1,885.13]	1,486.29 (0.00) [0]
Railways					
1171	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,536.00]	1,089.84 (593.05) [39]
1172	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2024) [3/2024]	843.04 (843.04) [843.04]	193.29 (0.00) [41]
1173	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2024) [3/2024]	1,172.92 (1,172.92) [1,172.92]	590.18 (0.00) [63]
1174	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1175	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (3/2024) [3/2024]	5,200.00 (962.00) [962.00]	54.75 (-4,238.00) [48]
1176	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [0/0]	1,185.64 (-) [1,844.47]	1,883.44 (658.83) [0]
1177	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2023]	1,547.38 (1,547.38) [1,547.38]	593.77 (0.00) [12]
1178	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND	4/2015	11/2018 (3/2024)	701.61 (810.02)	168.21 (108.41)

	4TH LINE		[3/2024]	[810.02]	[64]
1179	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [0/0]	133.41 (207.00) [396.00]	388.21 (262.59) [0]
1180	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (3/2026) [3/2026]	2,923.13 (3,791.66) [3,791.66]	1,402.12 (868.53) [204]
1181	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	357.56 (0.00) [48]
1182	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [12/2021]	969.83 (1,312.96) [1,312.96]	795.27 (343.13) [21]
1183	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (3/2021) [3/2022]	155.81 (238.03) [238.03]	218.99 (82.22) [24]
1184	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [12/2021]	948.04 (-) [2,009.00]	1,764.93 (1,060.96) [21]
1185	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (12/2021) [12/2021]	1,111.99 (1,539.28) [1,539.28]	1,090.14 (427.29) [34]
1186	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,337.54 (1,237.83) [88]
1187	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (3/2025) [3/2025]	810.78 (1,928.07) [1,928.07]	830.77 (1,117.29) [45]
1188	VIZIANAGARAM -SAMBALPUR 3RD LINE	1/1991	12/2024 (-) [12/2021]	2,335.67 (-) [3,377.21]	1,122.68 (992.05) [24]
	Road Transport And Highways				
1189	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [3/2021]	1,282.94 (-) [1,282.94]	468.69 (0.00) [-]
1190	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [3/2021]	2,510.04 (-) [2,510.04]	525.68 (0.00) [19]
1191	FOUR LANING WITH PS TALEBANI - SMBALPUR	12/2015	/ (-) [3/2022]	752.28 (-) [752.28]	181.52 (0.00) [-]
1192	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [1/2021]	1,069.65 (-) [1,069.65]	611.71 (0.00) [-]
1193	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,935.14 (0.00) [0]
1194	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [6/2021]	1,008.96 (-) [1,008.96]	895.53 (0.00) [-]
1195	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	221.00 (0.00) [-]
1196	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [6/2021]	476.56 (-) [476.56]	52.19 (0.00) [47]
1197	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO	1/2018	/ (-)	633.68 (-)	63.98 (0.00)

	4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (		[0/0]	[633.68]	[0]
1198	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [3/2022]	953.09 (-) [953.09]	332.04 (0.00) [-]
1199	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [6/2021]	668.86 (-) [668.86]	276.59 (0.00) [-]
1200	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	191.40 (0.00) [-]
1201	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	258.91 (0.00) [0]
1202	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	25.40 (0.00) [-]
1203	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [6/2021]	1,288.07 (-) [1,420.00]	817.80 (131.93) [15]
1204	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [6/2021]	686.65 (-) [686.65]	227.63 (0.00) [-]
1205	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [6/2021]	686.65 (-) [686.65]	260.60 (0.00) [-]
1206	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [6/2021]	417.51 (-) [417.51]	127.61 (0.00) [-]
1207	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	258.91 (-0.05) [0]
1208	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [6/2021]	999.00 (-) [999.00]	102.70 (0.00) [-]
1209	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	88.30 (0.04) [0]
1210	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1212	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (-) [6/2021]	1,522.00 (-) [1,522.00]	304.40 (0.00) [-]

1213	SIX LANNING OF CHANDIKHOL- JAGATPUR-BHUBANESWAR	12/2011	6/2014 (3/2021) [3/2021]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [81]
1214	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	145.70 (0.00) [-]
1215	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	136.19 (0.50) [0]
1216	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1217	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1218	WIDENING OF EXISTING IL DL TO 2- LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1219	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	210.29 (0.00) [0]
1220	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471- 900 (BERHMAPUR-APPA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	99.98 (0.00) [0]
1221	WIDENING TO 2LPS FROM 170/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	3/2016	2/2017 (-) [0/0]	287.7 (-) [287.70]	153.90 (0.00) [0]
1222	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1223	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1224	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1225	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1226	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1227	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	Steel				
1228	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023 (-) [5/2023]	377.18 (-) [377.18]	0.38 (0.00) [0]
	PONDICHERRY				
	Health And Family Welfare				
1229	CONST OF 152 QTRS 240 BOYS 240	3/2018	9/2020	195.00	16.41

	GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT		(-) [4/2022]	(-) [195.00]	(0.00) [19]
	PUNJAB				
	Fertilisers				
1230	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [2/2021]	218.83 (-) [218.83]	171.68 (0.00) [15]
1231	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [3/2021]	239.81 (-) [239.81]	182.53 (0.00) [16]
	Health And Family Welfare				
1232	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [7/2021]	703.00 (-) [557.48]	438.92 (-145.52) [13]
1233	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [12/2020]	152.95 (-) [177.92]	157.90 (24.97) [34]
	Human Resource Development				
1234	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022 (-) [5/2022]	348.24 (-) [348.24]	7.05 (0.00) [0]
1235	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [10/2021]	430.00 (-) [387.83]	167.01 (-42.17) [17]
1236	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [1/2021]	294.00 (-) [350.69]	258.72 (56.69) [21]
	Petroleum				
1237	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	3/2020	2/2023 (-) [2/2023]	1,411.66 (-) [1,421.46]	33.86 (0.00) [0]
	Railways				
1238	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	Road Transport And Highways				
1239	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (-) [2,280.00]	1,282.04 (1,110.39) [0]
1240	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	795.00 (0.00) [0]
1241	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [12/2020]	889.24 (-) [904.82]	739.41 (15.58) [-]
1242	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [0/0]	1,388.34 (-) [2,587.50]	1,569.38 (1,199.16) [0]
1243	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [9/2021]	754.54 (-) [756.27]	330.92 (1.73) [18]
1244	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (-) [0/0]	766.36 (-) [766.36]	685.36 (0.00) [0]
1245	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-)	447.29 (-)	676.33 (299.14)

			[0/0]	[746.43]	[0]
1246	FOUR LANNING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [1/2021]	261.76 (-) [207.00]	193.26 (-54.76) [-]
1247	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION	9/2014	/ (-) [7/2021]	479.00 (-) [479.00]	456.80 (0.00) [-]
1248	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [12/2020]	1,069.59 (-) [1,069.59]	663.50 (0.00) [14]
1249	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [0/0]	196.05 (-) [196.05]	143.03 (0.00) [0]
1250	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (-) [199.90]	124.52 (0.00) [0]
1251	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0.000	3/2018	11/2020 (-) [5/2021]	170.57 (-) [170.57]	34.68 (0.00) [6]
1252	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020 (-) [0/0]	173.24 (-) [173.24]	106.35 (0.00) [0]
1253	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABCHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020 (-) [8/2021]	322.48 (-) [322.48]	260.36 (0.00) [13]
1254	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [0/0]	293.64 (-) [293.64]	28.24 (0.00) [0]
1255	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [0/0]	293.64 (-) [293.64]	237.13 (0.00) [0]
1256	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [8/2021]	293.10 (-) [293.10]	146.46 (0.00) [12]
1257	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	648.44 (0.00) [0]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1258	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [3/2023]	12,320.00 (-) [17,079.00]	12,799.00 (4,759.00) [75]
	<u>Coal</u>				
1259	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020 (-) [0/0]	2,112.60 (-) [2,112.60]	158.25 (0.00) [0]
1260	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]
1261	BITHNOK LIGNITE THERMAL POWER	3/2015	9/2020	2,196.30	173.83

	STATION		(-) [0/0]	(-) [2,196.30]	(0.00) [0]
1262	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Human Resource Development</u>				
1263	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (12/2020) [3/2021]	549.31 (559.47) [559.47]	458.38 (10.16) [20]
	<u>Petroleum</u>				
1264	LPG BP PROJECT JODHPUR	3/2018	/ (5/2022) [5/2022]	229.80 (-) [229.80]	79.45 (0.00) [-]
	<u>Railways</u>				
1265	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,980.21]	4.60 (1,106.50) [0]
1266	AJMER-BANGURGRAM	4/2011	11/2019 (-) [3/2021]	213.39 (-) [375.00]	327.89 (161.61) [16]
1267	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.00]	0.00 (277.00) [0]
1268	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [2/2020]	242.09 (-) [525.00]	457.31 (282.91) [0]
1269	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [2/2021]	246.08 (-) [375.00]	306.94 (148.92) [14]
1270	DAUSA-GANGAPUR CITY(N.),NWR	2/2017	2/2019 (-) [11/2021]	411.00 (-) [860.41]	677.30 (450.33) [33]
1271	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [6/2022]	808.85 (-) [808.85]	153.38 (0.00) [-2]
1272	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH- UDAIPUR	4/2013	3/2020 (-) [6/2021]	420.18 (-) [420.18]	287.94 (0.00) [15]
1273	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	464.53 (0.00) [0]
1274	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1275	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [0/0]	236.93 (-) [350.45]	244.56 (113.52) [0]
	<u>Road Transport And Highways</u>				
1276	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [8/2022]	370.36 (-) [370.36]	0.00 (0.00) [0]
1277	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [11/2020]	597.00 (-) [597.00]	587.64 (0.00) [0]
1278	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [0]
1279	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-	7/2016	/ (-)	688.70 (-)	880.00 (0.00)

	11A		[0/0]	[688.70]	[0]
1280	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [9/2021]	1,031.95 (-) [1,031.95]	374.05 (0.00) [-]
1281	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [3/2021]	178.13 (-) [178.13]	110.91 (0.00) [-]
1282	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [0/0]	822.90 (-) [822.90]	1,688.16 (0.00) [0]
1283	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)- TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	611.28 (0.00) [0]
1284	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [3/2021]	163.95 (-) [163.95]	116.47 (0.00) [35]
1285	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	610.56 (0.00) [0]
1286	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT- RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	88.91 (0.00) [0]
1287	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) - JAL (KM 283.500 OF NH 65 NAGAJUR ROAD) SECTIO	12/2017	/ (-) [12/2021]	1,308.73 (-) [1,308.73]	293.43 (0.00) [-]
1288	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [0/0]	763.23 (-) [763.23]	191.80 (0.00) [0]
1289	FOUR LANNING OF BAR-BILARA- JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [0/0]	649.00 (-) [649.00]	543.83 (0.00) [0]
1290	FOUR LANNING OF DARAH- JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [11/2020]	964.17 (-) [964.17]	704.61 (0.00) [0]
1291	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1292	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	492.00 (0.00) [0]
1293	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	2,323.04 (0.00) [0]
1294	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR- ASIND SECTION (K	8/2020	11/2020 (-) [11/2020]	196.23 (-) [196.00]	0.00 (-0.23) [0]
1295	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1296	REHABILITATION AND UPGRADING	1/1991	4/2014	376.52	0.00

	TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O		(-) [0/0]	(-) [376.52]	(0.00) [0]
1297	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/(-) [2/2021]	1,100.19(-) [1,145.31]	1,265.00(45.12) [-]
1298	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/(-) [1/2021]	1,239.82(-) [1,727.66]	1,672.28(487.84) [-]
1299	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020(-) [3/2021]	894.00(-) [929.32]	795.00(35.32) [11]
1300	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016(-) [0/0]	425.19(-) [425.19]	276.40(0.00) [0]
1301	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR	8/2015	/(-) [0/0]	275.90(-) [275.90]	289.13(0.00) [0]
1302	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018(-) [0/0]	331.46(-) [331.46]	267.94(0.00) [0]
1303	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	6/2019(-) [9/2019]	637.18(-) [637.18]	550.35(0.00) [0]
1304	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK F	3/2020	8/2020(-) [0/2020]	255.23(-) [255.23]	0.00(0.00) [0]
1305	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA	3/2013	/(-) [0/0]	874.2(-) [874.25]	886.59(0.00) [0]
1306	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018(-) [4/2021]	370.30(-) [370.30]	266.58(0.00) [34]
1307	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/(-) [9/2020]	1,103.88(-) [1,103.88]	673.70(0.00) [0]
1308	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018(-) [6/2021]	341.79(-) [341.79]	192.06(0.00) [37]
1309	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015(-) [0/0]	257.09(-) [257.09]	14.18(0.00) [0]
1310	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015(-) [0/0]	383.40(-) [383.40]	244.68(0.00) [0]
1311	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015(-) [0/0]	269.22(-) [269.22]	33.24(0.00) [0]
1312	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON	12/2015	6/2018(-) [0/0]	621.43(-) [621.43]	387.22(0.00) [0]

	KOTA-DARAH				
1313	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR)	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	112.47 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1314	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [3/2023]	1,339.48 (4,084.69) [8,600.00]	619.18 (7,260.52) [87]
	<u>Road Transport And Highways</u>				
1315	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (12/2020) [12/2020]	182.28 (369.64) [269.14]	274.06 (86.86) [94]
1316	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (12/2020) [12/2020]	151.59 (370.01) [151.59]	282.36 (0.00) [88]
1317	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (12/2020) [12/2020]	166.27 (359.92) [166.27]	243.59 (0.00) [88]
1318	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	95.44 (0.00) [0]
1319	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	24.70 (0.00) [0]
1320	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWAY TO GANGTOK IN SIKKIM VIA B/GRAKO - CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
1321	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1322	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	241.07 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1323	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	22,125.00 (0.00) [36]
1324	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [10/2022]	3,492.00 (5,677.00) [6,840.00]	5,896.72 (3,348.00) [145]
	<u>Civil Aviation</u>				
1325	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (-) [3/2023]	380.87 (-) [380.87]	0.00 (0.00) [12]
1326	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [9/2022]	2,467.00 (-) [2,467.00]	303.07 (0.00) [7]
1327	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AIRPORT	8/2018	10/2021 (-) [3/2022]	951.28 (-) [951.28]	249.79 (0.00) [5]
	<u>Coal</u>				
1328	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0	4/2013	6/2015 (3/2025)	1,458.17 (709.06)	479.89 (-749.11)

	MPA)		[3/2025]	[709.06]	[117]
1329	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [1/2021]	5,907.11 (7,980.79) [7,980.79]	7,371.83 (2,073.68) [61]
	<u>Financ</u>				
1330	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [4/2021]	209.00 (-) [208.96]	195.23 (-0.04) [18]
1331	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	83.71 (0.00) [0]
	<u>Mines</u>				
1332	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (6/2021) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [18]
	<u>Petroleum</u>				
1333	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [11/2021]	228.00 (-) [228.00]	110.61 (0.00) [17]
1334	BS-VI PROJECTS	9/2017	12/2019 (-) [1/2021]	1,858.00 (-) [1,858.00]	1,498.79 (0.00) [13]
1335	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [9/2023]	921.00 (-) [921.00]	2.86 (0.00) [0]
1336	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	160.41 (0.00) [10]
1337	ENNORE THIRUVALUR BEINGALUR PUDUCHERRY NAGAPATTINAM MADURAITUTICOR V GAS PIPELINE	5/2013	12/2019 (-) [8/2021]	4,497.00 (-) [6,025.00]	3,275.27 (1,528.00) [32]
1338	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1339	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2021) [5/2021]	650.82 (-) [624.35]	445.60 (-26.47) [26]
1340	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [8/2022]	678.00 (1,472.00) [1,472.00]	16.38 (794.00) [66]
1341	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [9/2021]	421.00 (-) [300.00]	238.43 (-121.00) [13]
	<u>Power</u>				
1342	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (6/2020) [3/2021]	186.17 (219.66) [219.66]	156.28 (33.49) [20]
	<u>Railways</u>				
1343	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [238.00]	153.46 (-19.00) [0]
1344	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [527.37]	3.34 (375.53) [0]
1345	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (2/2021) [2/2021]	931.98 (-) [961.09]	873.72 (29.11) [-]
1346	CUDDALORE-SALEM VIA	4/1999	/	198.68	319.22

	VRIDDHACHALAM GC		(-) [3/2025]	(-) [559.95]	(361.27) [-]
1347	ERODE-PALANI	4/2008	/	288.57	1.63
			(-) [0/0]	(-) [1,140.00]	(851.43) [0]
1348	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [12/2021]	495.74 (-) [734.01]	481.29 (238.27) [102]
1349	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2022]	760.00 (-) [1,536.00]	1,233.08 (776.00) [27]
1350	MADURAI-BODINAYAKKANUR	4/2008	/	164.41	340.21
			(-) [9/2021]	(-) [450.73]	(286.32) [-]
1351	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [6/2022]	1,700.00 (-) [1,305.00]	756.45 (-395.00) [3]
1352	MAYLADUTHURAI-THIRUVARUR- KARAIKUDI-THIRU 'POND'- AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [2,910.84]	1,583.77 (2,186.15) [73]
1353	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (1/2021) [12/2020]	187.26 (-) [332.00]	239.19 (144.74) [80]
1354	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI- AVADI-SRIPERUMBUDUR	4/2013	/	839.00	0.62
			(-) [0/0]	(-) [1,500.00]	(661.00) [0]
1355	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [9/2021]	268.87 (-) [950.00]	928.36 (681.13) [198]
1356	TIDIVANAM-NAGAR (NL)	9/2006	/	322.8	233.89
			(-) [12/2021]	(-) [582.8]	(0.00) [-]
1357	TINDIVANAM-GINGEE- TIRUVANNAMALAI (NL)	9/2006	/	227.40	63.90
			(-) [0/0]	(-) [227.40]	(0.00) [0]
1358	TIRUCHIRAPPALI-NAGORE- KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2025]	303.98 (-) [1,720.00]	693.14 (1,416.02) [60]
1359	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
Road Transport And Highways					
1360	2-LANING OF KRISHNAGIRI- TINDIVANAM (APPROVED LENHTH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	8.56 (0.00) [0]
1361	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	182.00 (0.00) [0]
1362	4-LANNING OF STHIYATHOPU- CHOLOPURAM	9/2017	9/2017 (-) [9/2021]	1,227.87 (-) [1,227.87]	549.62 (0.00) [48]
1363	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/	5/2016	1/2017 (-) [0/0]	307.70 (-) [307.70]	312.82 (0.00) [0]
1364	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	223.10 (9.95) [0]
1365	CONSTRUCTION OF PAVED SHOULDERS INCULDING	11/2015	8/2015 (-)	154.14 (-)	140.64 (0.00)

	STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-		[0/0]	[154.14]	[0]
1366	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [10/2020]	600.00 (-) [600.00]	0.00 (0.00) [0]
1367	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [7/2021]	1,016.92 (-) [1,071.00]	273.52 (54.08) [-]
1368	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [0/0]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1369	FOUR LANING OF MADURAI-CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300)	3/2018	/ (-) [9/2021]	628.71 (-) [628.71]	284.33 (0.00) [-]
1370	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1371	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [7/2021]	1,166.26 (-) [1,166.26]	268.34 (0.00) [-]
1372	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [11/2020]	641.17 (-) [641.17]	390.36 (0.00) [0]
1373	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [5/2021]	305.3 (-) [505.3]	240.60 (0.00) [-]
1374	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [2/2021]	1,176.37 (-) [1,176.37]	425.56 (0.00) [42]
1375	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [12/2020]	707.82 (-) [707.82]	415.67 (0.00) [28]
1376	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [2/2021]	848.45 (932.23) [848.45]	209.77 (0.00) [11]
1377	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [12/2020]	641.17 (-) [641.17]	390.36 (0.00) [29]
1378	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	146.79 (4.82) [0]
1379	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [0/0]	379.90 (-) [379.90]	182.58 (0.00) [0]
1380	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,337.05 (0.00) [0]
1381	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-)	401.11 (-)	273.89 (0.00)

			[0/0]	[401.11]	[0]
1382	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1383	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [5/2021]	374.00 (-) [166.90]	45.26 (-207.10) [96]
1384	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1385	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	93.53 (0.00) [0]
1386	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (-) [240.38]	74.56 (0.00) [0]
1387	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	45.52 (0.00) [0]
1388	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/	1/2016	9/2016 (-) [0/0]	162.72 (-) [162.72]	136.46 (0.00) [0]
	Urban Development				
1389	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (12/2020) [12/2021]	3,770.00 (-) [3,770.00]	2,750.00 (0.00) [33]
1390	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2011 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.87 (4,458.00) [0]
	TELANGANA				
	Civil Aviation				
1391	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (-) [5/2022]	353.61 (-) [353.61]	0.00 (0.00) [0]
	Coal				
1392	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2022]	447.06 (-) [473.22]	18.60 (26.16) [84]
1393	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1394	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (3/2022) [3/2022]	413.84 (-) [413.84]	169.90 (0.00) [36]
1395	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2022]	397.09 (-) [442.42]	106.15 (45.33) [36]
1396	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2022]	417.33 (-) [384.32]	122.55 (-33.01) [68]
1397	KISTARAM OCP	11/2010	3/2015 (-) [3/2022]	242.29 (-) [164.04]	131.52 (-78.25) [84]
1398	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	416.07 (70.65) [132]
1399	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015	162.76	279.54

			(-) [3/2022]	(-) [349.28]	(186.52) [84]
1400	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2021]	430.45 (-) [415.37]	189.91 (-15.08) [60]
1401	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2024]	249.03 (-) [448.86]	326.69 (199.83) [144]
1402	SRP OC-II EXPANSION PROJECT	11/2016	/ (4/2017) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [-]
	<u>Health And Family Welfare</u>				
1403	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	115.97 (0.00) [14]
	<u>Petroleum</u>				
1404	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	53.13 (0.00) [16]
	<u>Power</u>				
1405	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (3/2022) [3/2022]	10,598.98 (-) [10,598.98]	7,998.74 (0.00) [16]
	<u>Railways</u>				
1406	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2021]	632.68 (-) [950.00]	786.37 (317.32) [69]
1407	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	507.33 (0.00) [0]
1408	MANMAD-PARBHATINAND-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [12/2022]	173.7 (185.00) [449.39]	7.09 (329.66) [9]
1409	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2025]	1,160.48 (-) [1,160.48]	466.96 (0.00) [180]
1410	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1411	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [850.00]	705.50 (76.06) [0]
	<u>Road Transport And Highways</u>				
1412	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [0/0]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [0]
1413	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [0/0]	283.15 (-) [283.15]	82.67 (0.00) [0]
1414	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [0/0]	626.76 (-) [626.76]	154.52 (0.00) [0]
1415	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.95 (0.00) [0]
1416	FOUR LANING OF KHAMMAM-	3/2017	3/2017	4,429.00	0.00

	ASHWARAOPET SECTION OF NH 365BB		(-) [0/0]	(-) [4,429.00]	(0.00) [0]
1417	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	11.43 (0.00) [0]
1418	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	272.08 (0.00) [0]
1419	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	461.90 (0.00) [0]
1420	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (-) [0/0]	828.29 (-) [828.29]	0.00 (0.00) [0]
1421	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [1/2021]	1,423.96 (-) [897.03]	956.62 (-526.93) [26]
1422	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [0/0]	192.67 (-) [192.67]	137.66 (0.00) [0]
1423	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [0/0]	605.08 (-) [605.08]	389.46 (0.00) [0]
1424	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEERAK SECTION OF NH-763D FROM EXISTIN	1/2018	4/2020 (-) [0/0]	426.5 (-) [426.5]	376.33 (0.00) [0]
1425	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1426	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [0/0]	294.13 (-) [294.13]	90.20 (0.00) [0]
1427	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	103.85 (0.00) [0]
1428	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [0/0]	322.81 (-) [322.81]	77.17 (0.00) [0]
1429	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [0/0]	248.83 (-) [248.83]	112.80 (0.00) [0]
1430	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [0/0]	298.32 (-) [298.32]	112.13 (0.00) [0]
1431	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [0/0]	230.03 (-) [230.03]	205.96 (0.00) [0]

1432	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [0/0]	206.13 (-) [206.13]	168.15 (0.00) [0]
1433	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	41.81 (0.00) [0]
1434	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	103.22 (0.00) [0]
1435	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	187.73 (0.00) [0]
1436	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	146.06 (0.00) [0]
1437	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	288.00 (0.00) [0]
1438	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	148.46 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1439	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	3/2015	6/2019 (-) [12/2020]	43.2 (-) [438.26]	335.58 (0.00) [18]
	<u>Railways</u>				
1440	AGARTALA-AKHAURA NL	4/2012	3/2020 (3/2022) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
1441	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	357.19 (0.00) [0]
1442	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [0/0]	171.90 (-) [171.90]	96.21 (0.00) [0]
	<u>Rural Development</u>				
1443	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [2/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [62]
1444	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [3/2021]	202.61 (227.00) [207.12]	189.79 (4.51) [51]
1445	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [3/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [51]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1446	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (9/2020)	1,383.00 (-)	369.66 (0.00)

			[9/2022]	[1,383.00]	[12]
	<u>Coal</u>				
1447	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	10,724.93 (0.80) [0]
	<u>Health And Family Welfare</u>				
1448	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [7/2021]	785.00 (-) [715.06]	511.74 (-69.94) [15]
1449	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [12/2020]	268.84 (-) [268.84]	228.89 (0.00) [-]
	<u>Human Resource Development</u>				
1450	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [6/2021]	171.72 (171.72) [171.72]	53.94 (0.00) [15]
	<u>Petroleum</u>				
1451	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [8/2022]	676.00 (-) [676.00]	375.67 (0.00) [8]
1452	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [345.15]	183.93 (57.66) [0]
1453	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (-) [3/2029]	3,450.20 (-) [3,450.20]	135.22 (0.00) [0]
1454	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (-) [4/2021]	217.92 (-) [217.92]	72.40 (0.00) [0]
1455	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [11/2021]	257.4 (-) [255.40]	16.36 (0.00) [15]
1456	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	571.32 (0.00) [0]
1457	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	124.52 (0.00) [3]
	<u>Power</u>				
1458	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-) [0/0]	587.44 (-) [587.44]	250.00 (0.00) [0]
1459	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (-) [0/0]	349.00 (-) [349.00]	125.00 (0.00) [0]
1460	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	1,297.85 (0.00) [11]
1461	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [1/2021]	9,750.89 (-) [12,176.28]	11,044.00 (2,425.39) [47]
1462	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (3/2021) [3/2021]	9,188.98 (-) [10,016.10]	7,888.03 (827.12) [20]
	<u>Railways</u>				
1463	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]

1464	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	169.83 (-233.29) [2]
1465	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1466	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,825.00]	1,411.49 (641.75) [24]
1467	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [12/2023]	602.50 (-) [714.34]	56.54 (111.84) [-]
1468	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1469	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1470	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1471	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1472	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	28.80 (0.35) [68]
1473	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	809.66 (0.00) [0]
1474	JHANSI MANIKPUR AND KHARAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	33.37 (0.00) [0]
1475	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1476	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2021]	528.57 (-) [528.57]	194.21 (0.00) [24]
1477	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [6/2021]	927.01 (-) [1,400.00]	1,280.16 (472.99) [27]
1478	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	1,436.33 (0.00) [0]
1479	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [0/0]	668.70 (668.00) [680.00]	330.00 (11.30) [0]
1480	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	833.10 (0.00) [21]
1481	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1482	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1483	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [3/2021]	622.50 (427.00) [426.74]	475.97 (-195.76) [47]
1484	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020	2,436.21	1,005.54

			(-) [3/2021]	(-) [2,436.21]	(0.00) [12]
1485	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,295.42]	778.29 (0.00) [0]
1486	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	80.32 (-149.01) [16]
1487	UNCHAHAH-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,265.00]	103.72 (36.00) [-]
1488	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [1,000.00]	688.03 (56.40) [33]
	Road Transport And Highways				
1489	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	239.04 (0.00) [0]
1490	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1491	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (12/2020) [12/2020]	351.34 (417.68) [417.68]	433.68 (66.34) [59]
1492	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	4/2014	1/2016 (1/2020) [1/2020]	495.78 (627.93) [627.93]	633.24 (132.15) [0]
1493	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (12/2020) [12/2020]	291.36 (469.31) [469.31]	459.07 (177.95) [83]
1494	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2015	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1495	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,072.92 (211.43) [0]
1496	4-LANING OF GAGALHERI-SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [8/2020]	1,668.00 (-) [1,668.00]	946.08 (0.00) [0]
1497	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1498	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [0/0]	1,408.00 (-) [1,408.00]	442.70 (0.00) [0]
1499	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [0/0]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [0]
1500	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	2,977.58 (0.00) [0]
1501	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1502	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29	3/2016	/ (-)	1,396.74 (-)	227.26 (0.00)

	FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR		[0/0]	[1,396.74]	[0]
1503	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [0/0]	1,657.20 (-) [1,657.20]	2,345.00 (0.00) [0]
1504	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,357.84 (382.01) [0]
1505	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [12/2020]	207.00 (-) [207.00]	43.23 (0.00) [-]
1506	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	977.26 (0.00) [0]
1507	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1508	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1509	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1510	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BHATA ROAD AND TERMINATING AT STAPUR RO	3/2018	/ (-) [12/2020]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1511	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1512	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1513	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [0/0]	1,081.57 (-) [1,057.60]	542.52 (-23.97) [0]
1514	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [12/2020]	1,232.21 (-) [1,087.00]	672.82 (-145.21) [-]
1515	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [12/2020]	1,989.00 (-) [1,989.00]	683.51 (0.00) [9]
1516	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]
1517	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	209.66 (0.00) [0]
1518	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	469.16 (0.00) [0]
1519	FOUR LANING OF ALIGARH -	3/2018	/	925.40	951.37

	KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.		(-) [0/0]	(-) [1,197.00]	(271.60) [0]
1520	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	549.07 (0.00) [0]
1521	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	464.05 (0.00) [0]
1522	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1523	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1524	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1525	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	3/2018	8/2020 (-) [3/2021]	288.30 (-) [288.30]	83.53 (0.00) [7]
1526	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [11/2020]	1,373.28 (-) [1,373.28]	974.57 (0.00) [0]
1527	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [0/0]	1,184.71 (-) [1,310.00]	1,039.23 (125.29) [0]
1528	FOUR LANNING OF KANPUR - KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM 119.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [0/0]	839.0 (-) [839.0]	641.51 (0.00) [0]
1529	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1530	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [0/0]	281.45 (-) [281.45]	0.00 (0.00) [0]
1531	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	11/2018	12/2020 (-) [12/2020]	281.45 (-) [281.45]	2.36 (0.00) [0]
1532	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [987.94]	867.27 (304.70) [0]
1533	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019 (-) [4/2020]	209.10 (-) [209.10]	195.83 (0.00) [0]
1534	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [9/2021]	326.99 (327.00) [326.99]	65.83 (0.00) [-]
1535	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [2/2021]	296.50 (-) [296.50]	141.54 (0.00) [5]
1536	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	431.34 (-348.73) [0]

1537	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	541.77 (-345.24) [0]
1538	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	2/2019 (-) [0/0]	239.63 (-) [239.63]	212.53 (0.00) [0]
1539	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [0/0]	388.83 (-) [388.83]	304.70 (0.00) [0]
1540	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2021]	263.89 (-) [242.05]	181.10 (-21.84) [12]
1541	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [11/2020]	208.50 (-) [208.50]	164.97 (0.00) [0]
1542	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [0/0]	445.89 (653.00) [653.29]	469.64 (207.40) [0]
1543	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [0/0]	599.34 (-) [599.34]	492.15 (0.00) [0]
1544	REHABILITATION AND UPGRADATION OF KUNJNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.200 OF NH-76 TO 2-LANE	3/2018	2/2020 (-) [11/2021]	185.18 (-) [185.11]	115.87 (0.00) [0]
1545	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [12/2020]	249.50 (-) [249.50]	182.51 (0.00) [19]
1546	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [11/2020]	218.90 (-) [218.90]	112.47 (0.00) [0]
1547	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1548	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [0/0]	215.16 (215.00) [215.16]	160.61 (0.00) [0]
1549	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [3/2021]	240.30 (240.00) [240.30]	199.35 (0.00) [14]
1550	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [0/0]	218.94 (219.00) [218.94]	120.69 (0.00) [0]
1551	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [0/0]	176.94 (177.00) [176.94]	141.11 (0.00) [0]

1552	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [12/2020]	208.88 (-) [208.88]	143.96 (0.00) [14]
1553	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [653.29]	464.05 (207.40) [0]
1554	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	1,200.52 (0.00) [0]
1555	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,344.09 (0.00) [0]
1556	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1557	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [11/2020]	164.54 (165.00) [164.54]	139.00 (0.00) [0]
1558	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	128.54 (0.00) [0]
	<u>Steel</u>				
1559	FORGED WHEEL PLANT	4/2014	9/2018 (2/2021) [2/2021]	1,682.85 (-) [1,682.85]	1,511.30 (0.00) [29]
	<u>Urban Development</u>				
1560	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	8,379.62 (-) [8,379.62]	0.00 (0.00) [0]
1561	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	11,076.48 (-) [11,076.48]	0.00 (0.00) [0]
1562	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>Water Resources</u>				
1563	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [3/2022]	213.62 (-) [213.62]	0.00 (0.00) [0]
1564	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS	3/2018	9/2021 (-) [9/2021]	904.00 (-) [904.00]	38.38 (0.00) [0]
1565	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	5.16 (0.00) [0]
1566	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [234.03]	0.00 (2.24) [0]
1567	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1568	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [6/2022]	298.12 (-) [298.12]	0.00 (0.00) [11]
1569	INTERCEPTION, DIVERSION AND	5/2017	9/2021	767.59	32.47

	TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA		(-) [9/2021]	(-) [767.59]	(0.00) [0]
1570	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [1/2021]	460.45 (-) [460.45]	87.15 (0.00) [1]
1571	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR	12/2018	8/2021 (-) [6/2022]	857.26 (-) [842.25]	0.00 (-15.01) [10]
1572	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	2/2017	11/2019 (-) [12/2020]	161.31 (-) [161.31]	50.65 (0.00) [13]
1573	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [681.78]	0.00 (0.00) [0]
1574	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA	2/2019	8/2021 (-) [8/2021]	317.19 (-) [317.19]	0.00 (0.00) [0]
1575	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [12/2020]	279.91 (-) [279.91]	222.79 (0.00) [12]
1576	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	8/2020 (-) [12/2020]	370.40 (-) [370.40]	323.09 (0.00) [4]
1577	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2021]	967.23 (-) [967.23]	14.64 (0.00) [0]
UTTARAKHAND					
Civil Aviation					
1578	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2013	9/2020 (-) [7/2021]	455.8 (-) [456.86]	203.76 (0.00) [10]
Petroleum					
1579	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [6/2021]	160.10 (-) [160.10]	78.12 (0.00) [16]
Power					
1580	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.21 (274.07) [0]
1581	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	479.06 (0.00) [0]
1582	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [12/2022]	2,978.48 (5,867.38) [5,867.38]	4,796.50 (2,888.90) [117]
1583	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2023]	2,491.58 (-) [3,860.35]	2,110.14 (1,368.77) [126]
Railways					
1584	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	204.53 (126.80) [0]
1585	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1586	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-)	16,216.00 (-)	2,555.91 (6,500.11)

			[3/2025]	[22,716.11]	[3]
	Road Transport And Highways				
1587	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	112.31 (0.00) [0]
1588	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	128.27 (0.00) [0]
1589	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [0/0]	605.84 (-) [722.46]	722.46 (116.62) [0]
1590	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [8/2020]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [0]
1591	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	48.22 (0.00) [0]
1592	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	196.35 (0.00) [0]
1593	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [0/0]	248.00 (-) [248.00]	0.00 (0.00) [0]
1594	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 83	3/2016	/ (-) [0/0]	720.00 (-) [720.00]	348.16 (0.00) [0]
1595	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [12/2020]	478.51 (-) [478.00]	315.11 (-0.51) [86]
1596	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	59.44 (0.00) [0]
1597	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [0/0]	283.51 (-) [283.51]	126.38 (0.00) [0]
1598	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	257.34 (-) [257.34]	62.79 (0.00) [0]
1599	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	200.34 (-) [200.34]	31.00 (0.00) [0]
1600	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [0/0]	282.08 (-) [282.08]	77.05 (0.00) [0]
1601	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [0/0]	418.88 (-) [418.88]	88.00 (0.00) [0]
1602	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF	11/2017	11/2019 (-)	266.52 (-)	144.27 (0.00)

	EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S		[0/0]	[266.52]	[0]
1603	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [0/0]	234.88 (-) [208.89]	118.26 (-25.99) [0]
1604	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1605	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1606	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [0/0]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1607	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]
	<u>Water Resources</u>				
1608	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH	3/2017	11/2019 (-) [0/0]	158.00 (-) [158.00]	0.00 (0.00) [0]
1609	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	3/2017	8/2019 (-) [0/0]	273.37 (-) [273.37]	71.53 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1610	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (10/2022) [10/2022]	389.71 (-) [389.71]	37.38 (0.00) [11]
1611	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (6/2021) [6/2021]	458.00 (-) [458.00]	105.12 (0.00) [15]
	<u>Coal</u>				
1612	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [10/2021]	304.13 (341.22) [341.22]	23.04 (37.09) [55]
1613	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	386.19 (0.00) [0]
1614	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.87 (0.00) [0]
1615	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	0.00 (0.00) [0]
1616	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [0/0]	2,661.73 (-) [5,146.48]	516.17 (2,484.75) [0]
1617	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	0.00 (0.00) [0]
1618	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.43 (0.00) [0]
1619	SONEPUR BAZARI (COMB) OCP (8.0	8/2012	3/2018	1,055.05	632.85

	MTY)		(-) [3/2021]	(-) [1,055.05]	(0.00) [36]
1620	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.40 (0.00) [0]
	<u>Health And Family Welfare</u>				
1621	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1622	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1623	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [6/2021]	651.99 (-) [651.99]	427.72 (0.00) [-]
1624	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2021]	355.15 (-) [355.15]	268.35 (0.00) [24]
	<u>Home Affairs</u>				
1625	NSG AT KOLKATA	10/2014	4/2018 (-) [12/2020]	162.88 (-) [179.16]	168.45 (16.28) [32]
	<u>Human Resource Development</u>				
1626	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [11/2020]	193.83 (-) [193.83]	0.45 (0.00) [0]
	<u>Petroleum</u>				
1627	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH PIPELINE	3/2018	9/2022 (-) [3/2022]	3,712.00 (-) [3,636.02]	1,780.96 (-16.00) [-6]
1628	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (-) [3/2031]	5,830.20 (-) [5,830.20]	13.79 (0.00) [0]
1629	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,740.00 (-) [1,740.00]	775.10 (0.00) [12]
1630	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1631	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (2/2020) [7/2020]	694.00 (-) [1,097.54]	971.84 (403.54) [0]
1632	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	53.20 (0.00) [0]
1633	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [10/2021]	163.02 (-) [163.02]	80.39 (0.00) [18]
	<u>Power</u>				
1634	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [0/0]	529.68 (-) [529.68]	294.18 (0.00) [0]
1635	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (4/2020) [1/2021]	454.11 (-) [454.11]	341.06 (0.00) [33]
1636	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (11/2022) [12/2024]	1,381.84 (-) [1,592.34]	626.32 (210.50) [63]
	<u>Railways</u>				

1637	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (1,966.70) [2,373.00]	485.04 (1,345.60) [324]
1638	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [3/2025]	1,106.62 (-) [1,091.59]	954.89 (-15.03) [171]
1639	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	227.07 (16.56) [-]
1640	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1641	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1642	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1643	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1644	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [0/0]	221.42 (-) [380.00]	38.20 (158.58) [0]
1645	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [0/0]	297.32 (-) [614.00]	275.07 (316.68) [0]
1646	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAL AND RAJABHATKHAWA -AIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,290.00]	1,087.60 (710.00) [0]
1647	NEW MAYNAGURI-UMANIAT- DOUBLING OF REMAINING PORTION (51.65 KM)	4/2010	12/202 (-) [3/2021]	602.2 (-) [760.00]	730.62 (157.73) [-9]
1648	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1649	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	1,002.79 (1,725.49) [108]
1650	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1651	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,629.88 (307.50) [108]
1652	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	899.24 (430.57) [72]
1653	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
Road Transport And Highways					
1654	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [12/2020]	1,083.00 (-) [1,827.15]	2,082.19 (744.15) [30]
1655	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-)	998.79 (-)	1,852.94 (0.00)

			[12/2021]	[998.79]	[100]
1656	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [5/2021]	1,078.84 (-) [1,078.84]	2,239.99 (0.00) [93]
1657	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [0]
1658	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [0/0]	361.15 (-) [363.93]	272.98 (2.78) [0]
1659	CONSTRUCTION OF MECHE BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	107.03 (0.00) [0]
1660	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [11/2022]	160.27 (213.97) [213.97]	24.14 (53.70) [39]
1661	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [0/0]	229.37 (-) [229.37]	130.72 (0.00) [0]
1662	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [12/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [28]
1663	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [3/2021]	254.30 (254.30) [254.30]	78.32 (0.00) [5]
1664	FOUR LANNING OF CHIRCH A-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 184.400 INCLUDING REHABILITA	3/2016	8/2018 (-) [0/0]	767.0 (-) [767.0]	604.65 (0.00) [0]
1665	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	682.36 (120.10) [0]
1666	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	807.93 (114.56) [0]
1667	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [7/2021]	1,261.98 (-) [1,952.20]	934.06 (690.22) [-]
1668	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (1/2020) [2/2020]	279.70 (398.52) [398.52]	330.94 (118.82) [0]
1669	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (11/2020) [5/2021]	396.86 (396.86) [396.86]	242.95 (0.00) [20]
1670	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1671	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (2,360.65) [2,360.65]	4,472.01 (695.65) [0]
1672	UPGRADATION OF NH-31C WITH A	3/2017	11/2019	202.69	144.43

	MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10		(-) [0/0]	(202.69) [202.69]	(0.00) [0]
1673	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (4/2020) [4/2021]	218.70 (218.70) [218.70]	90.68 (0.00) [5]
1674	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [12/2021]	426.18 (426.18) [426.18]	242.25 (0.00) [15]
	<u>Steel</u>				
1675	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (3/2021) [5/2021]	263.36 (-) [263.36]	159.19 (0.00) [8]
	<u>Water Resources</u>				
1676	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (-) [12/2020]	274.76 (-) [274.76]	189.36 (0.00) [12]
1677	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1678	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1679	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]
1680	INTERCEPTION AND DIVERSION WITH STP AT HUGLI-CHIL SURAH	2/2018	2/2022 (-) [2/2022]	160.00 (-) [160.00]	0.00 (0.00) [0]
1681	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1682	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	0.00 (0.00) [0]
1683	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [2/2022]	198.43 (-) [198.43]	0.00 (0.00) [0]
1684	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1685	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	0.00 (0.00) [0]
1686	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [12/2021]	185.22 (-) [185.22]	0.00 (0.00) [0]
1687	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [12/2020]	272.32 (-) [272.32]	202.18 (0.00) [8]
	Total			21,44,627.66 (6,27,393.32) [25,72,670.28]	12,17,692.37 (4,28,042.62)
