

**434th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
December, 2021**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for December 2021 contains information on the status of the 1673 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, out of 1673 projects, 2 projects are added and 8 projects (6 projects of Petroleum and 1 project each of Steel and Road sector) are completed. 557 projects are delayed with respect to their original schedules and 118 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 118 projects, 20 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

S.No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report
1	ROAD TRANSPORT AND HIGHWAYS	888	115	31
2	RAILWAYS	285	145	12
3	PETROLEUM	147	84	14
4	COAL	106	55	2
5	POWER	62	45	14
6	WATER RESOURCES	43	38	30
7	HEALTH AND FAMILY WELFARE	29	5	2
8	URBAN DEVELOPMENT	29	14	0
9	DEPARTMENT OF HIGHER EDUCATION	22	16	1
10	CIVIL AVIATION	20	18	3
11	STEEL	7	3	1
12	MINES	6	4	1
13	ATOMIC ENERGY	5	4	1
14	HOME AFFAIRS	5	4	2
15	FERTILISERS	4	2	2
16	TELECOMMUNICATIONS	3	3	1
17	FINANCE	2	0	0
18	HEAVY INDUSTRY	2	0	0
19	DPIIT	2	1	0
20	SHIPPING AND PORTS	1	0	0
21	SOCIAL JUSTICE	1	0	0
22	DEFENCE PRODUCTION	1	1	1
23	COMMERCE	1	0	0
24	DONER	1	0	0
25	RENEWABLE ENERGY	1	0	0
		1673	557	118

3. Total original cost of implementation of the 1673 projects was ₹22,23,791.78 crore and their anticipated completion cost is likely to be ₹26,64,649.18 crore, which reflects overall cost overruns of ₹4,40,857.40 crore (19.82% of original cost). The expenditure incurred on these projects till December 2021 is ₹13,08,766.65 crore, which is 49.12% of the anticipated cost of the projects. The information can be viewed graphically as:

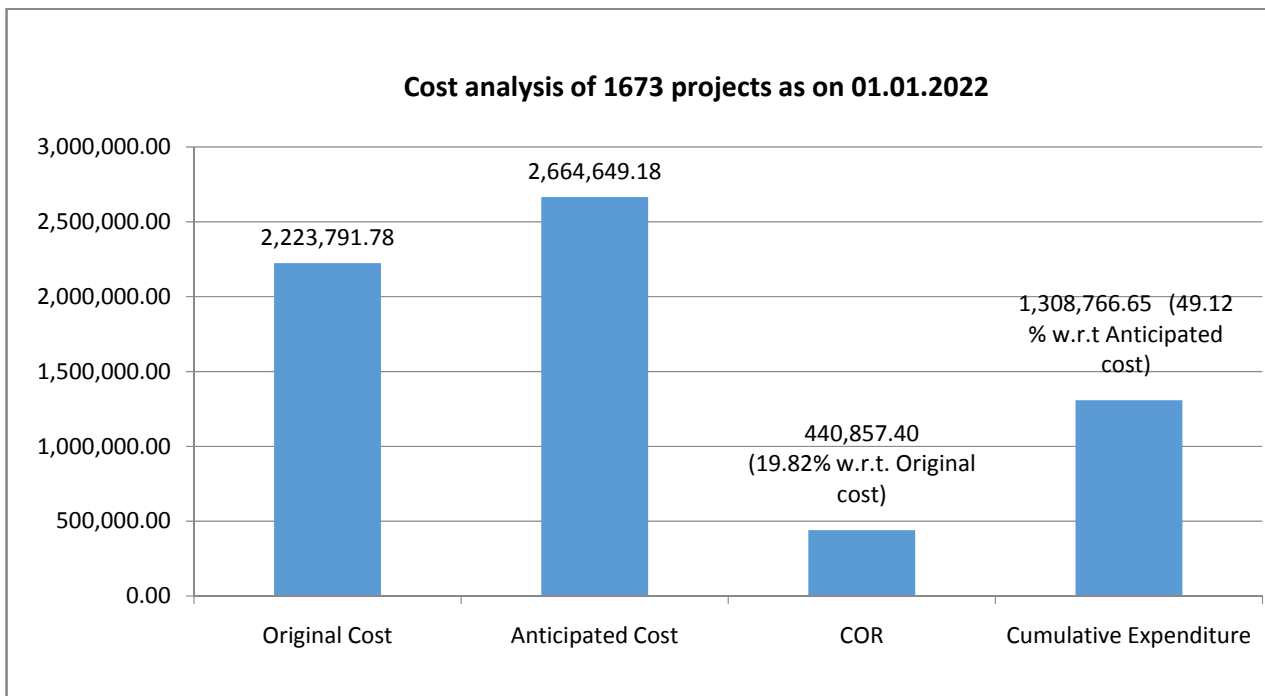


4.


The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.


5. Out of the 1673 projects, 9 projects are ahead of schedule, 269 are on schedule, 557 are delayed, 445 projects reported cost overrun and 219 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 420 if delay is calculated on the basis of latest schedule of completion. Further, for 838 projects neither the year of commissioning nor the tentative gestation period has been reported.

7. The status of online reporting of projects can be viewed month wise as:

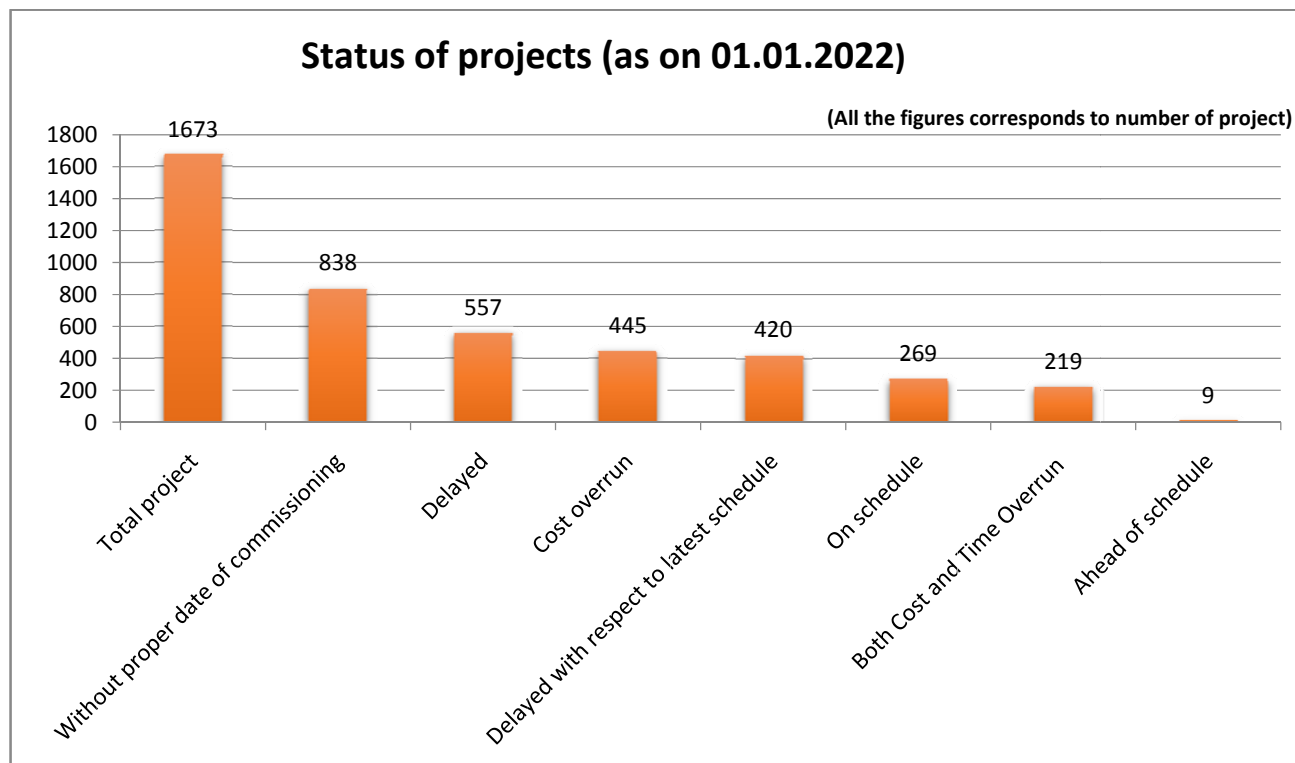

6. Out of 557 delayed projects, 97 (17.41%) projects have overall delay in the range of 1 to 12 months, 127 (22.80%) projects have delay in the range of 13 to 24 months, 217 (38.96%) projects have delay in the range of 25 to 60 months and 116 (20.82%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

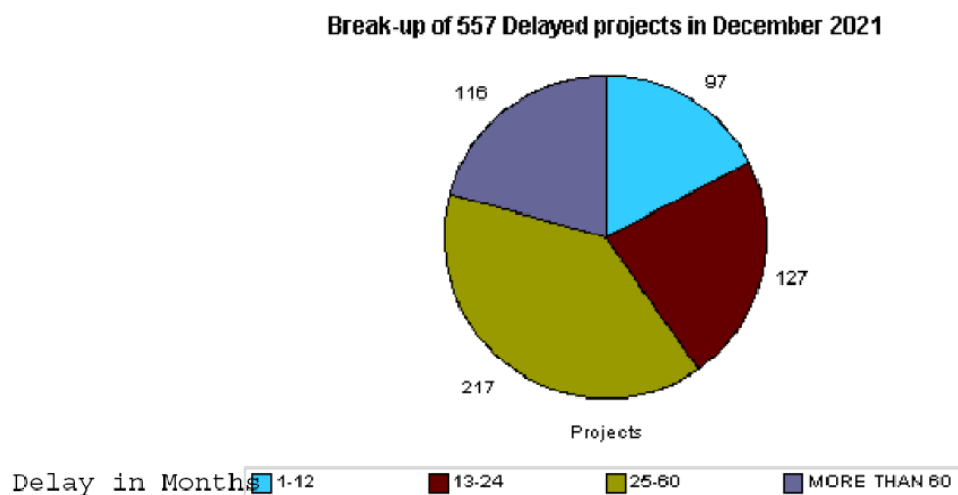

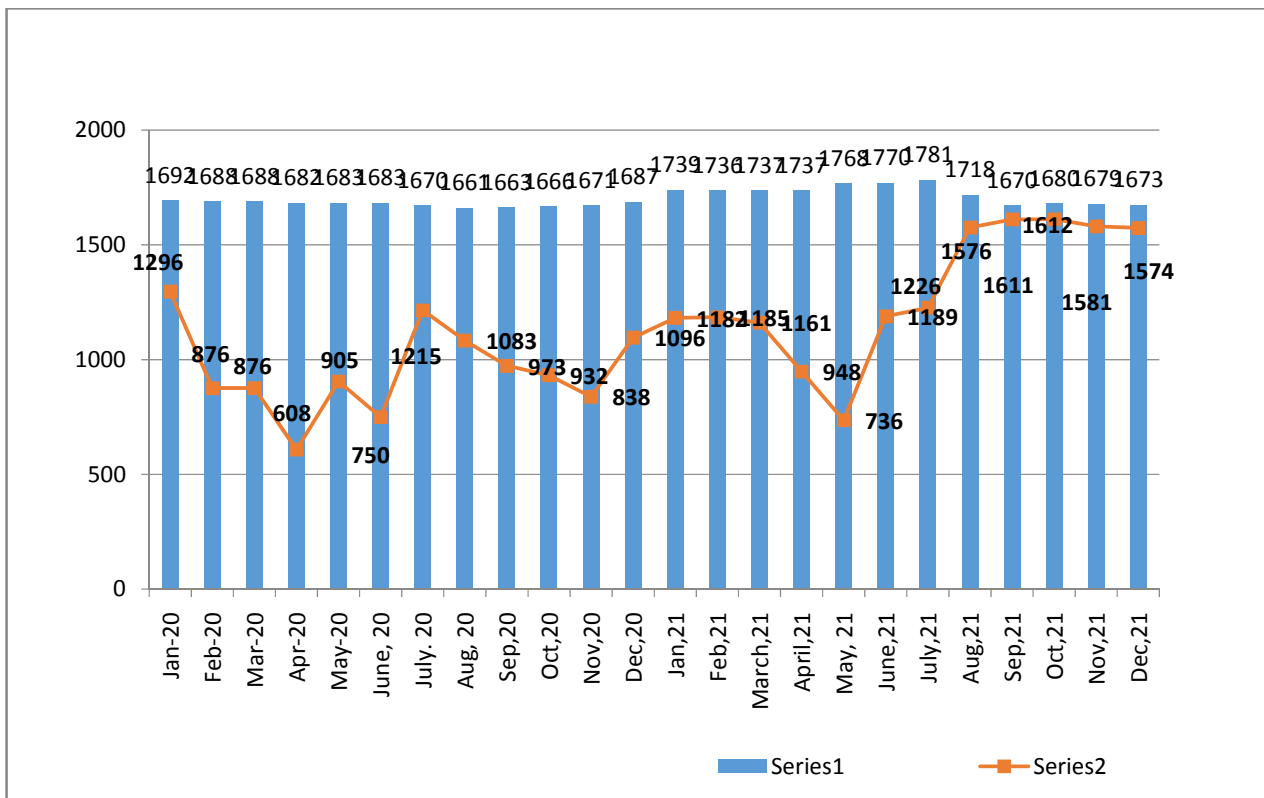

The average time overrun in these 557 delayed projects is 45.69 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

FLASH REPORT

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-01-2022)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	69.63
5	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1383.00	1938.00	40.13
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
COAL					
8	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
9	BHANEGAON OC	02/2015	187.94	409.68	117.98
10	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
11	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
12	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	808.97	68.70
DEPARTMENT OF HIGHER EDUCATION					
13	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	10.22
14	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	1.85
15	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
DPIIT					
16	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80
17	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
HEALTH AND FAMILY WELFARE					
18	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	41.63
19	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
20	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	190.34	21.58
21	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
22	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
HEAVY INDUSTRY					
23	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3727.30	116.96
HOME AFFAIRS					
24	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
25	NSG AT KOLKATA	10/2014	162.88	238.00	46.12
26	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	4.68
PETROLEUM					
27	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	2001.34	132.23

28	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
29	LPG TERMINAL AT KOCHI	10/2015	607.06	1236.00	103.60
30	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
31	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
POWER					
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
33	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4825.60	191.23
34	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52
35	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
36	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	126.58
RAILWAYS					
37	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
38	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	2172.16	1699.64
39	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
40	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
41	RAMGANJMUNDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
ROAD TRANSPORT AND HIGHWAYS					
42	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
43	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
44	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95
45	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	03/2018	478.74	1135.08	137.10
46	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	612.58	118.78
STEEL					
47	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	41.32
48	FORGED WHEEL PLANT	04/2014	1682.85	2100.00	24.79
TELECOMMUNICATIONS					
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	44.39
51	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	25.89
52	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
53	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	18.69
54	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	16.25
WATER RESOURCES					
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
56	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	76.68
57	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	62.63
58	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	22.24
59	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	17.91

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-01-2022)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1383.00	1938.00	555.00
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	290.50
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
COAL					
8	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
9	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
10	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	808.97	329.44
11	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
12	MAGADH EXPANSION OC(51 MTY)	08/2008	6964.33	7254.37	290.04
DEPARTMENT OF HIGHER EDUCATION					
13	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	19.00
14	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	10.16
15	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
DPIIT					
16	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
17	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
HEALTH AND FAMILY WELFARE					
18	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00
19	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	172.39
20	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
21	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
22	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	45.56
HEAVY INDUSTRY					
23	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3727.30	2009.30
HOME AFFAIRS					
24	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
25	NSG AT KOLKATA	10/2014	162.88	238.00	75.12
26	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	12.98
PETROLEUM					
27	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	01/2019	12366.00	18968.00	6602.00
28	VISAKH REFINERY MODERNISATION PROJECT	07/2006	20928.00	26264.00	5336.00

29	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00
30	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
31	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
POWER					
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
33	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
34	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
35	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	5213.00
36	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9129.32	4374.90
RAILWAYS					
37	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
38	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
39	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
40	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	14322.00	9867.83
41	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
ROAD TRANSPORT AND HIGHWAYS					
42	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
43	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
44	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
45	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	03/2018	1532.62	2499.00	966.38
46	4 LANING OF NH-31D FROM GHOSHPUKUR -SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	1083.00	1827.15	744.15
STEEL					
47	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	6415.00
48	FORGED WHEEL PLANT	04/2014	1682.85	2100.00	417.15
TELECOMMUNICATIONS					
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
URBAN DEVELOPMENT					
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	10270.00
51	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	4289.98
52	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	3780.00
53	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
54	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
WATER RESOURCES					
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
56	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	173.13
57	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	159.16
58	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	50.14
59	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	47.50

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-01-2022)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	12/2022	84
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2023	84
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2022	45
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	12/2022	34
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	01/2022	31
8	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	06/2024	28
9	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	09/2021	12/2023	27
COAL					
10	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY)	12/2007	03/2010	03/2029	228
11	MAGADH EXPANSION OC(51 MTY)	08/2008	07/2012	03/2028	188
12	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY)	12/2007	03/2013	03/2028	180
13	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	03/2017	03/2031	168
14	KARTALI (EAST) OCP (2.50 MTY)	07/2008	03/2014	03/2026	144
DEFENCE PRODUCTION					
15	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	02/2020	03/2022	25
DEPARTMENT OF HIGHER EDUCATION					
16	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	06/2022	93
17	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	03/2022	57
18	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	03/2020	02/2023	35
19	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	02/2019	06/2020	11/2022	29
20	PERMANENT CAMPUS FOR IIM BODH GAYA	09/2018	09/2020	11/2022	26
DPIIT					
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	05/2022	29
FERTILISERS					
22	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	12/2021	25
23	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	01/2022	21
HEALTH AND FAMILY WELFARE					
24	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	03/2022	46
25	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY10 (SCTIMST	09/2017	03/2020	12/2021	21

26	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	03/2018	09/2020	04/2022	19
27	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	06/2021	05/2022	11
28	AIIMS BILASPUR	04/2018	09/2021	06/2022	9
	HOME AFFAIRS				
29	NSG AT KOLKATA	10/2014	04/2018	08/2022	52
30	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	05/2022	31
31	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	10/2023	04/2024	6
32	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	07/2022	12/2022	5
	MINES				
33	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	12/2023	37
34	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	01/2024	33
35	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	04/2021	12/2023	32
36	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	04/2019	04/2022	12/2024	32
	PETROLEUM				
37	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	08/2024	140
38	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	05/2022	108
39	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
40	LPG TERMINAL AT KOCHI	10/2015	10/2017	09/2022	59
41	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	04/2016	04/2018	06/2022	50
	POWER				
42	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	03/2023	162
43	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
44	BARH STPP(3X660MW) NTPC	02/2005	10/2011	07/2023	141
45	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	03/2013	09/2024	138
46	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2024	138
	RAILWAYS				
47	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
48	MUNEERABAD-MAHABOONNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
49	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
50	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2022	241
51	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
	ROAD TRANSPORT AND HIGHWAYS				
52	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	06/2023	118
53	PUNE-SATARA(NH-4)	10/2010	03/2013	03/2022	108
54	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	05/2010	05/2013	02/2022	105
55	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
56	4-LANING OF FARAKA-RAIGANJ	02/2011	08/2013	01/2022	101
	STEEL				
57	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	03/2022	82
58	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	11/2022	61
59	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	06/2019	02/2022	32
	TELECOMMUNICATIONS				
60	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2022	80

61	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	03/2018	01/2022	46
62	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	03/2022	9
URBAN DEVELOPMENT					
63	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2019	03/2025	73
64	NAGPUR METRO RAIL	08/2014	03/2018	12/2021	45
65	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	08/2022	44
66	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	03/2020	03/2023	36
67	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	06/2015	04/2019	02/2022	34
WATER RESOURCES					
68	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	09/2020	03/2024	42
69	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	03/2019	07/2021	03/2024	32
70	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	03/2019	08/2021	03/2024	31
71	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	03/2017	11/2019	03/2022	28
72	SEWER NETWORKS, SPS AND STP, MUNGER	03/2018	10/2021	12/2023	26

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-01-2022)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	303.80	303.80	189.25	04/2020	06/2022
2	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	02/2019	645.63	645.63	0.00	08/2022	11/2022
COAL							
3	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	93.05	09/2020	N.A.
4	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
5	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	143.95	09/2020	N.A.
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
7	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	24.86	04/2018	10/2022
COMMERCE							
8	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	30.00	10/2020	N.A.

	DEPARTMENT OF HIGHER EDUCATION						
9	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	N.A.
10	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	171.72	171.72	110.13	03/2020	12/2021
11	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676.00	676.00	213.47	04/2023	04/2023
12	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	09/2018	392.51	392.51	57.47	06/2022	06/2022
13	PERMANENT CAMPUS FOR IIM BODH GAYA	09/2018	375.00	375.00	110.13	09/2020	11/2022
	DPIIT						
14	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9574.07	09/2019	07/2021
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	3013.69	12/2019	05/2022
	HEALTH AND FAMILY WELFARE						
16	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
17	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	573.94	11/2013	09/2021
18	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	538.20	06/2020	N.A.
19	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	591.61	04/2020	N.A.
20	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
	HEAVY INDUSTRY						
21	DEVELOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	900.00	815.00	09/2019	N.A.
	HOME AFFAIRS						
22	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	N.A.
23	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI	05/2019	199.31	199.31	20.53	01/2022	01/2020
24	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	27.25	07/2022	10/2022
25	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	166.98	166.98	0.00	10/2023	10/2023
	MINES						

26	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	04/2019	255.37	255.37	0.86	04/2022	04/2022
PETROLEUM							
27	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	19.44	02/2017	08/2022
28	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
29	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1112.00	1507.24	769.00	06/2019	02/2022
30	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	05/2016	261.00	261.00	183.60	01/2021	09/2021
31	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	212.00	212.00	172.42	01/2021	09/2021
POWER							
32	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	156.99	06/2006	N.A.
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	14458.38	09/2010	08/2023
34	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3824.26	10/2017	N.A.
35	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	252.99	04/2016	12/2021
36	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	2083.10	04/2020	07/2025
RAILWAYS							
37	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
38	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2017.96	878.49	07/2012	11/2024
39	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.06	03/2019	N.A.
40	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	149.31	03/2006	03/2025
41	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	560.09	07/2014	N.A.
RENEWABLE ENERGY							
42	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	271.90	271.90	90.99	11/2019	N.A.
ROAD TRANSPORT AND HIGHWAYS							
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40	01/1991	319.68	369.77	319.07	N.A.	N.A.

	TO KM 219.945) OF NH-104						
44	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	675.00	675.00	379.73	N.A.	N.A.
45	GWALIOR-JHANSI, NH-75	12/2003	604.00	364.59	360.15	12/2009	09/2020
46	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	612.58	612.58	02/2009	N.A.
47	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	655.17	07/2009	N.A.
STEEL							
48	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	70.05	12/2023	12/2023
TELECOMMUNICATIONS							
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	20545.00	07/2015	03/2022
50	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	422.87	46.37	06/2021	11/2021
URBAN DEVELOPMENT							
51	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6059.17	07/2017	09/2020
52	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	19493.96	03/2020	03/2023
53	NAGPUR METRO RAIL	08/2014	8680.00	8680.00	8427.24	03/2018	12/2021
54	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	6928.00	6928.00	6928.00	03/2019	03/2019
55	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	1128.00	1128.00	30.00	03/2022	06/2023
WATER RESOURCES							
56	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	260.12	12/2019	01/2021
57	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	220.08	12/2019	N.A.
58	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	291.32	03/2020	03/2021
59	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	248.86	04/2020	03/2021
60	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	326.75	01/2021	N.A.

N.A.: Not Available.

Table-E

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-01-2022)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	17298.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	0.00	13709.00
COAL					
3	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	0.00	729.73
4	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	0.00	293.69
HEALTH AND FAMILY WELFARE					
5	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	573.94
6	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	249.24
7	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
8	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
9	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
PETROLEUM					
10	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	06/2016	423.00	0.00	444.35
11	PIPELINE REPLACEMENT PROJECT (PRP-VI)	05/2019	763.92	0.00	791.49
POWER					
12	NAITWAR MORI HEP	10/2017	648.33	0.00	704.97
RAILWAYS					
13	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	560.09
14	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	803.11	1218.49
15	TIRUCHIRAPPALI-NAGORE-KARAICKAL(SR)(GC)	09/1995	303.98	0.00	705.52
16	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	920.91
17	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	495.44	0.00	1866.85
ROAD TRANSPORT AND HIGHWAYS					
18	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	612.58
19	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	0.00	655.17
20	TRICHY - KARUR	03/2007	516.00	0.00	886.96
21	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	02/2008	1673.70	0.00	3326.93
22	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2848.49
STEEL					
23	FORGED WHEEL PLANT	04/2014	1682.85	0.00	1736.92
URBAN DEVELOPMENT					
24	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39486.58
WATER RESOURCES					
25	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	0.00	291.32
26	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	0.00	326.75

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-01-2022)**

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	03/2012	N.A.	03/2021
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	12/2015	N.A.	02/2021
3	PATHERDIH NLW WASHERY	10/2012	04/2014	N.A.	04/2020
4	RFR OF MANUGURU OC PROJECT	11/2012	03/2016	N.A.	09/2021
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
COMMERCE					
6	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	N.A.
DEPARTMENT OF HIGHER EDUCATION					
7	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
8	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	N.A.	N.A.
9	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	N.A.	N.A.
10	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	07/2019	N.A.	N.A.
11	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	02/2019	06/2020	N.A.	N.A.
DONER					
12	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	04/2014	09/2017	N.A.	08/2021
DPIIT					
13	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	01/2014	07/2021
FERTILISERS					
14	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	17 05/2021	N.A.

15	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	05/2021	N.A.
FINANCE					
16	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	N.A.	07/2021
HEALTH AND FAMILY WELFARE					
17	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
18	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	09/2021
19	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	N.A.	03/2021
20	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
21	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
HEAVY INDUSTRY					
22	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	03/2021	03/2021
23	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	N.A.	N.A.
HOME AFFAIRS					
24	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	N.A.	N.A.
MINES					
25	UTKAL D AND E COAL BLOCK	05/2016	01/2020	N.A.	N.A.
PETROLEUM					
26	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
27	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	03/2019	09/2021	09/2021
28	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	05/2016	01/2021	N.A.	09/2021
29	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	01/2021	N.A.	09/2021
30	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	06/2016	08/2019	06/2021	05/2021
POWER					
31	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
32	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.

33	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
34	TALAIPALLI COAL MINING PROJECT	09/2015	11/2019	N.A.	N.A.
35	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	03/2016	01/2018	07/2021	06/2021
RAILWAYS					
36	HOWRAH-AMTA- CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
37	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL),NEFR	04/1983	03/2019	N.A.	N.A.
38	MUZAFFARPUR- SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
39	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	09/2021
40	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	04/1996	03/2012	09/2021	09/2021
RENEWABLE ENERGY					
41	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	N.A.	N.A.	N.A.
44	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	N.A.	N.A.	N.A.
45	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	N.A.	N.A.
46	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008	N.A.	N.A.
RURAL DEVELOPMENT					
47	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	07/2021	N.A.	N.A.
48	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	02/2019	02/2019
49	DELHI MRTS PHASE-III	09/2011	03/2016	08/2021	N.A.
50	KOCHI METRO RAIL PROJECT	07/2012	07/2017	09/2020	09/2020
51	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	03/2019	N.A.	03/2019
WATER RESOURCES					
52	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	N.A.	N.A.
53	SEWERAGE SYSTEM AND STP WORKS PHASE I AT	02/2011	12/2019	N.A. ¹⁹	01/2021

	MORADABAD RAMGANGA				
54	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	05/2021	N.A.
55	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	03/2020	N.A.	03/2021
56	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	04/2020	N.A.	03/2021

N.A.: Not Available.

FLASH REPORT

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	888	31
2	RAILWAYS	285	12
3	PETROLEUM	147	14
4	COAL	106	2
5	POWER	62	14
6	WATER RESOURCES	43	30
7	HEALTH AND FAMILY WELFARE	29	2
8	URBAN DEVELOPMENT	29	0
9	DEPARTMENT OF HIGHER EDUCATION	22	1
10	CIVIL AVIATION	20	3
11	STEEL	7	1
12	MINES	6	1
13	ATOMIC ENERGY	5	1
14	HOME AFFAIRS	5	2
15	FERTILISERS	4	2
16	TELECOMMUNICATIONS	3	1
17	FINANCE	2	0
18	HEAVY INDUSTRY	2	0
19	DPIIT	2	0
20	SHIPPING AND PORTS	1	0
21	SOCIAL JUSTICE	1	0
22	DEFENCE PRODUCTION	1	1
23	COMMERCE	1	0
24	DONER	1	0
25	RENEWABLE ENERGY	1	0
	Total	1673	118

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2021			
	<u>PETROLEUM</u>			
1	MMPL PIPELINE REROUTING PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000261]	449.58	12/2019	396.13
2	PUNE POL STORAGE DEPOT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000313]	282.64	08/2020	194.26
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
3	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000664]	639.79	03/2020	597.77
4	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000930]	378.24	01/2018	315.42
5	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001183]	251.55	02/2015	7.74
	June,2021			
	<u>PETROLEUM</u>			
6	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
7	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	<u>WATER RESOURCES</u>			
8	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI (Uttarakhand Pey Jal Nigam) - [N30000003]	273.37	08/2019	84.55
9	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR (Bihar Urban Infrastructure Development Corporation Ltd) - [N300000038]	184.93	04/2020	163.36
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000287]	485.44	12/2015	447.13

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000617]	198.00	10/2016	184.62
12	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001220]	491.52	09/2016	474.76
	August,2021			
	<u>PETROLEUM</u>			
13	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN (OIL INDIA LIMITED) - [N16000167]	352.56	03/2017	455.00
14	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
15	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000312]	255.00	11/2020	275.68
	<u>POWER</u>			
16	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
17	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
18	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
19	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
20	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
21	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
22	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
23	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000273]	587.44	09/2020	463.48
24	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000274]	349.00	11/2020	313.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
25	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000251]	297.00	04/2018	290.64
26	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000276]	156.26	-	141.35

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
27	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000294]	269.22	01/2015	33.24
28	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000295]	257.09	01/2015	14.18
29	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000297]	376.52	04/2014	171.16
30	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000298]	383.40	03/2015	244.68
31	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000311]	207.03	05/2012	308.09
32	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000317]	157.18	07/2015	148.24
33	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000318]	154.14	08/2015	142.06
34	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000333]	621.43	06/2018	387.22
35	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000371]	445.89	03/2017	464.05
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000376]	219.40	01/2018	0.10
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000379]	218.63	10/2017	29.27
38	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000385]	766.36	-	685.36
39	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000388]	497.05	05/2017	754.27
40	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000389]	847.02	-	795.00
41	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000397]	322.00	03/2018	56.41

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000402]	358.22	10/2016	339.86
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000414]	229.41	05/2018	6.65
44	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000417]	342.05	01/2017	258.91
45	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000467]	511.00	10/2013	2,323.04
46	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000470]	511.00	10/2013	492.00
47	FOUR LANING OF CHANDIGARH - KHARAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000503]	447.29	12/2017	346.39
48	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000523]	159.39	11/2017	210.29
49	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000524]	892.17	-	648.44
50	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000537]	278.39	08/2014	22.18
51	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08
52	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000580]	206.80	07/2016	74.04
53	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000581]	288.24	11/2015	287.37
54	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000608]	248.97	05/2019	270.65
55	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000625]	1,004.67	05/2019	577.21
56	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000640]	326.63	04/2018	249.26
57	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000641]	239.91	10/2017	147.25
58	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000644]	342.05	01/2017	258.91

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
59	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000646]	157.30	06/2018	97.29
60	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000727]	960.24	-	738.74
61	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000871]	600.87	11/2017	682.36
62	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000873]	823.20	11/2017	807.99
63	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000878]	235.91	02/2018	176.23
64	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000879]	202.69	11/2019	148.21
65	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000884]	191.21	11/2019	127.13
66	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000895]	287.34	01/2019	194.85
67	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000905]	322.48	07/2020	291.93
68	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000906]	173.24	06/2020	56.66
69	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000908]	276.01	03/2019	187.39
70	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000911]	165.06	12/2016	92.59
71	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000936]	244.95	08/2018	136.22
72	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 ((MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000938]	297.12	07/2018	373.98
73	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000942]	208.50	11/2019	165.82
74	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000962]	178.23	09/2018	122.99
75	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000999]	230.34	10/2019	201.82

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
76	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001001]	199.98	08/2016	163.16
77	MAJALGAON TO KAIJ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001036]	413.99	07/2019	299.72
78	AKKALKOT TO DHUDHNI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001120]	211.42	02/2019	131.85
79	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001131]	212.99	06/2020	156.72
80	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001139]	218.94	03/2020	120.69
81	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001143]	176.94	10/2018	141.11
82	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001147]	239.63	02/2019	212.53
83	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001148]	599.34	01/2020	492.15
84	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001153]	197.37	02/2014	89.36
85	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001155]	175.20	01/2017	142.48
86	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001184]	269.69	09/2019	0.01
87	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001202]	388.83	12/2019	304.70
88	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001205]	209.10	10/2019	201.70
89	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001223]	179.89	03/2013	242.23
90	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001225]	169.26	01/2019	270.11
91	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001237]	162.72	09/2016	136.59
92	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001238]	307.70	01/2017	313.06
	URBAN DEVELOPMENT			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
93	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000079]	884.30	12/2015	874.29
94	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000123]	218.72	11/2020	175.63
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
95	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000102]	294.00	04/2019	289.13
	September,2021			
	<u>STEEL</u>			
96	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000121]	263.36	09/2020	253.46
	<u>POWER</u>			
97	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000061]	4,824.12	10/2012	4,612.66
98	SYSTEM STRENGTHENING XIII OF SR GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000109]	487.49	06/2014	590.30
99	EASTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000155]	1,364.52	04/2016	1,290.03
100	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000168]	5,151.37	03/2018	3,269.93
101	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000181]	871.62	10/2017	628.13
102	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000182]	203.28	07/2017	200.16
103	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000218]	3,519.59	05/2019	2,562.41
104	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000238]	283.72	11/2019	196.10
105	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000239]	408.46	01/2019	369.27
106	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000240]	608.24	04/2019	425.04
107	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI Central Sector Projects(Power Grid Corporation of India Limited) - [N18000257]	3,654.00	04/2019	3,508.04

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
108	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT Central Sector Projects(Power Grid Corporation of India Limited) - [N18000261]	175.64	09/2018	115.43
109	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) Central Sector Projects(Power Grid Corporation of India Limited) - [N18000263]	445.89	02/2019	372.58
110	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) (Power Grid Corporation of India Limited) - [N18000267]	198.49	09/2019	132.15
111	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT (Power Grid Corporation of India Limited) - [N18000269]	193.14	06/2019	108.80
	<u>RAILWAYS</u>			
112	GONDIA-JABALPUR(GC),(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100186]	511.86	04/2020	1,867.16
113	NANDYAL-YERRAGUNTLA(NL),SCR (SOUTH CENTRAL RAILWAY) - [220100192]	164.36	02/2009	1,148.67
114	HARIDASPUR-PARADEEP(NL) (RAIL VIKAS NIGAM LTD.) - [220100285]	1,185.64	12/2017	2,129.37
115	ETAWAH-MAINPURI (NL),NCR (NORTH CENTRAL RAILWAY) - [220100318]	120.00	12/2008	345.51
116	CHHINDWARA - NAGPUR (GC)(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100324]	383.79	-	1,448.56
117	BARDHAMAN-KATWA (GC) (EASTERN RAILWAYS) - [N22000091]	1,106.62	12/2010	1,003.78
118	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) (WESTERN RAILWAY) - [N22000125]	117.36	03/2011	809.40
119	BANGURGRAM-GURIYA PATCH DOUBLING (NORTH WESTERN RAILWAY) - [N22000137]	246.08	12/2019	366.92
120	THIYAT HAMIRA-SANU (NORTH WESTERN RAILWAY) - [N22000149]	236.93	10/2018	287.42
121	AJMER-BANGURGRAM (NORTH WESTERN RAILWAY) - [N22000155]	213.39	11/2019	361.83
122	ALWAR-BANDIKUI DOUBLING (NORTH WESTERN RAILWAY) - [N22000157]	242.09	02/2019	476.34
123	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000165]	258.20	12/2018	318.44
124	HAJIPUR-RAMDAYALUNAGAR DOUBLING (EAST CENTRAL RAILWAYS) - [N22000182]	213.01	-	498.44
125	CUDDALORE-SALEM VIA VRIDDHACHALAM GC (SOUTHERN RAILWAY) - [N22000187]	198.68	-	273.57
126	AMBARI FALAKATA TO NEW MAYNAGURI (NORTH EAST FRONTIER RAILWAY) - [N22000210]	314.00	03/2019	831.65
127	PIRPAINTI-BHAGALPUR (EASTERN RAILWAYS) - [N22000222]	261.38	-	553.59
128	HANSDIHA-GODDA NL (EASTERN RAILWAYS) - [N22000236]	542.18	03/2020	545.97
129	HARIDWAR-LAKSAR (NORTHERN RAILWAY) - [N22000289]	219.83	-	204.53
130	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND (SOUTH EASTERN RAILWAY) - [N22000323]	148.77	12/2016	206.49

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
131	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM (SOUTHERN RAILWAY) - [N22000373]	187.26	04/2014	276.82
132	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO (WESTERN RAILWAY) - [N22000433]	243.60	-	423.00
133	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000444]	257.00	03/2018	153.84
134	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION (NORTH EASTERN RAILWAY) - [N22000461]	622.50	04/2017	521.88
135	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR (EAST CENTRAL RAILWAYS) - [N22000475]	180.82	-	546.29
136	CHAMPA-JHARSUGUDA 3RD LINE (SOUTH EAST CENTRAL RAILWAY) - [N22000483]	872.00	12/2019	1,156.06
137	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION (WESTERN RAILWAY) - [N22000487]	551.51	03/2019	773.12
138	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM (WESTERN RAILWAY) - [N22000494]	691.84	03/2020	812.08
	ROAD TRANSPORT AND HIGHWAYS			
139	SONAPUR TO GUWAHTI (AS-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000044]	245.00	03/2008	240.36
140	NALBARI TO BIJNI (AS-6) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000047]	225.00	06/2008	390.72
141	NALBARI T BIJNI (AS-7) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000048]	208.00	04/2008	370.56
142	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000049]	160.00	05/2008	270.97
143	BRAHMPUTRA BRIDGE,NH NO-31 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000063]	217.61	04/2010	489.84
144	VADODARA-SURAT SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000361]	503.16	08/2016	389.50
145	FOUR LANING OF AURANGABAD - YEDISHI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000508]	1,871.34	01/2018	3,443.43
146	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000518]	399.54	04/2019	259.67
147	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000541]	1,081.57	06/2019	480.25
148	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000542]	197.69	07/2018	151.11
149	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000545]	1,134.97	11/2018	809.71
150	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ((NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000621]	1,239.82	-	1,691.00
151	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROMEXISTI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000837]	307.79	-	197.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
152	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000850]	551.58	-	305.46
153	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000978]	172.75	-	134.38
154	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001174]	235.31	11/2020	195.72
155	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24001257]	159.85	10/2022	2.80
	<u>URBAN DEVELOPMENT</u>			
156	REDEVELOPMENT OF EAST KIDWAI NAGAR (NATIONAL BUILDING CONSTRUCTION CORPORATION LTD) - [N28000080]	4,264.00	11/2019	4,683.08
	<u>WATER RESOURCES</u>			
157	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS (Uttar Pradesh Jal Nigam) - [N30000007]	904.00	09/2021	148.55
158	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR (Uttar Pradesh Jal Nigam) - [N30000009]	370.40	08/2020	396.14
159	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA (Uttar Pradesh Jal Nigam) - [N30000011]	161.31	11/2019	91.38
160	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA (Bihar Urban Infrastructure Development Corporation Ltd) - [N30000041]	184.86	05/2021	168.85
	October,2021			
	<u>CIVIL AVIATION</u>			
161	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNAI AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000040]	535.00	06/2010	0.01
	<u>COAL</u>			
162	SINGHORI OC MINE (WESTERN COAL FIELDS LIMITED) - [N06000130]	205.49	03/2020	138.58
163	AMALGAMATED PAUNI-II III OC MINE (WESTERN COAL FIELDS LIMITED) - [N06000131]	483.69	03/2021	253.70
164	AMALGAMATED GONDEGAON GHATROHAN OC (WESTERN COAL FIELDS LIMITED) - [N06000149]	198.68	03/2019	272.90
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
165	GAIL GAS LTD BENGALURU CGD PROJECT Central Sector Projects(GAS AUTHORITY OF INDIA LIMITED) - [N16000210]	749.00	02/2020	1,043.56
166	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000227]	4,588.29	08/2018	5,376.50
167	BS-VI PROJECTS (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000295]	1,858.00	12/2019	1,528.75
	<u>RAILWAYS</u>			
168	GHAZIPUR - AUNRIHAR (40 KM) (NORTH EASTERN RAILWAY) - [N22000321]	182.92	-	0.01
	<u>URBAN DEVELOPMENT</u>			
169	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000143]	532.00	11/2020	541.00
	November,2021			
	<u>COAL</u>			
170	KOLAR PIMPRI EXTENSION OC (WESTERN COAL FIELDS LIMITED) - [N06000160]	362.73	03/2020	336.00
	December,2021			
	<u>STEEL</u>			
171	COKE OVEN BATTERY-5 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000117]	2,858.00	12/2017	2,018.72
	<u>PETROLEUM</u>			
172	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT (INDIAN OIL CORPORATION LIMITED) - [N16000236]	423.00	08/2019	447.89
173	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000267]	212.00	01/2021	177.58
174	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI (INDIAN OIL CORPORATION LIMITED) - [N16000276]	261.00	01/2021	195.22
175	PIPELINE NETWORK PROJECT GELEKI, ASSAM (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000278]	249.85	05/2020	229.85
176	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP (INDIAN OIL CORPORATION LIMITED) - [N16000302]	384.58	04/2021	302.10
177	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000365]	1,524.06	12/2021	1,037.45
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
178	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000553]	229.37	11/2018	152.85

FLASH REPORT

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000321]	829.00	01/2019	350.14
2	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000430]	223.30	06/2018	111.16
3	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000618]	434.06	-	306.05
4	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000676]	138.93	01/2017	124.76
5	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
6	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000681]	194.66	04/2017	117.61
7	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000689]	507.68	04/2017	129.13
8	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000766]	318.42	11/2017	66.63
	August,2021			
9	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
10	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000274]	333.21	12/2015	256.11
11	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000296]	278.87	05/2014	0.00
12	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000302]	333.21	12/2015	256.11

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000307]	156.63	02/2012	0.00
14	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000309]	305.49	03/2011	131.08
15	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
16	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000335]	159.12	11/2015	0.00
17	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000373]	305.49	03/2017	0.00
18	SATANA-BELA SECTION OF NH-75(4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000375]	320.48	08/2015	189.49
19	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000395]	257.80	-	12.38
20	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000396]	470.20	02/2011	569.40
21	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD- AURANG(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000398]	282.41	08/2016	327.21
22	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
23	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000407]	333.21	11/2015	256.11
24	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
25	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00
26	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000519]	478.35	-	516.69
27	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000530]	154.62	-	0.00
28	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000575]	665.50	07/2016	0.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
29	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000577]	369.77	06/2016	0.00
30	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000927]	293.64	08/2020	28.24
31	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001144]	445.89	03/2017	469.64
32	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001145]	164.54	08/2015	141.33
33	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001154]	367.44	01/2017	61.95
34	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001167]	165.67	01/2016	87.63
35	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001170]	471.16	08/2014	201.64
36	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001230]	281.45	12/2020	112.70
	September, 2021			
	<u>RAILWAYS</u>			
37	DANIAWAN-BIHARSARIF (NL), ECR (EAST CENTRAL RAILWAYS) - [220100311]	406.92	-	200.00
38	GOOTY-DHARMAVARAM-BANGLORE (RAIL INDIA TECHNICAL AND ECONOMIC SERVICE) - [N22000370]	636.38	-	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
39	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000253]	187.79	07/2016	82.95
40	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000275]	289.60	-	160.70
41	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000439]	1,885.74	05/2019	1,636.02
42	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000650]	244.90	05/2019	251.87

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	<u>RURAL DEVELOPMENT</u>			
43	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V (HSCL FOR RURAL) - [N12000098]	149.73	12/2015	144.95
44	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI (HSCL FOR RURAL) - [N12000099]	202.61	12/2016	190.22
45	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII (HSCL FOR RURAL) - [N12000100]	175.49	12/2016	124.87
	October,2021			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
46	STUDY IN INDIA (EDCIL(India) Limited) - [N42000003]	150.00	04/2018	0.00
47	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION (Indian Institute of Technology, Kharagpur) - [N42000004]	418.00	03/2019	110.00
48	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES(CPWD OF HIGHER EDUCATION) - [N44000001]	127.26	10/2023	12.73
	<u>HOME AFFAIRS</u>			
49	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 (CPWD FOR MHA) - [N45000001]	166.98	05/2022	0.29
	November,2021			
50	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA(CPWD FOR MHA) - [N28000101]	114.26	12/2013	0.00
	<u>RURAL DEVELOPMENT</u>			
51	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT(CPWD FOR RURAL) - [N28000132]	361.60	07/2021	12.44

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1679
No of Projects Completed/Dropped/Frozen in Current Month	14
No of Projects Fell down in Current Month	6
No of Projects added in Current Month	2
No of Projects in Current Month	1673

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	557 (33.29%)	9 (.54%)	269 (16.08%)	101 (6.04%)	737 (44.05%)	1673
Latest Approved (Date)	420 (25.10%)	11 (.66%)	429 (25.64%)	72 (4.30%)	741 (44.29%)	1673

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1344	17,03,334.34	18,44,963.66	8,16,520.02	44.30	1,41,629.32	8.30
Project with Revision in Cost	329	8,03,337.38	8,19,685.52	4,92,246.63	60.10	16,348.14	2.00
Total	1,673	25,06,671.72	26,64,649.18	13,08,766.65	49.12	1,57,977.46	6.30
Original Cost of All Projects							
Original Cost	1,673	22,23,791.78	26,64,649.18	13,08,766.65	49.12	4,40,857.40	19.82

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	557	8,88,221.90	11,86,144.64	6,93,894.38	58.50	2,97,922.74	33.54
Latest Approved (RCE)	420	6,87,279.76	7,77,729.89	4,51,806.71	58.10	90,450.13	13.16

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	118	1,20,072.71	1,47,023.69	1,12,569.42	76.60	26,950.98	22.40
Total	118	1,20,072.71	1,47,023.69	1,12,569.42	76.57	26,950.98	22.45

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	20	14,431.97	15,465.25	7.16	4	3,288.50	4,358.06	32.52
3	COAL	106	1,49,328.98	1,53,992.98	3.12	19	37,788.39	44,126.90	16.77
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	6	7,333.99	7,330.54	-0.05	0	0.00	0.00	0.00
7	STEEL	7	22,331.15	29,163.30	30.59	2	17,207.85	24,040.00	39.70
8	PETROLEUM	147	3,39,274.49	3,50,723.52	3.37	27	65,726.53	90,012.48	36.95
9	POWER	62	2,07,257.24	2,70,968.33	30.74	28	1,08,986.44	1,74,215.58	59.85
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	1	1,718.00	3,727.30	116.96
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	12	5,589.39	6,374.57	14.05
12	RAILWAYS	285	4,43,040.10	6,84,768.60	54.56	204	2,35,664.70	4,84,630.20	105.64
13	ROAD TRANSPORT AND HIGHWAYS	888	5,37,828.12	5,53,848.05	2.98	121	89,491.73	1,11,873.62	25.01
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	29	2,91,275.10	3,13,165.63	7.52	7	93,659.03	1,15,628.76	23.46
17	WATER RESOURCES	43	24,702.19	70,243.27	184.36	8	12,236.47	58,101.66	374.82
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
19	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0.00
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
21	DEPARTMENT OF HIGHER EDUCATION	22	10,139.61	10,047.96	-0.90	3	1,231.49	1,263.46	2.60

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	HOME AFFAIRS	5	2,025.73	2,894.62	42.89	3	1,659.44	2,528.33	52.36
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0.00
Total		1673	22,23,791.78	26,64,649.18	19.82	445	7,32,205.05	12,05,034.22	64.58

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	67	1,12,107.24	1,58,677.58	41.54	13	44,493.05	99,985.39	124.72
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	5	8,861.14	22,797.48	157.27
3	ASSAM	48	48,689.00	57,952.53	19.03	12	18,806.96	29,394.44	56.30
4	BIHAR	98	1,23,227.91	1,59,169.38	29.17	34	54,885.85	92,412.45	68.37
5	GOA	10	5,332.77	5,343.26	0.20	2	529.17	539.66	1.98
6	GUJARAT	59	1,08,152.96	1,19,380.30	10.38	20	35,705.48	47,911.91	34.19
7	HARYANA	36	61,492.56	63,819.18	3.78	7	3,823.83	6,282.82	64.31
8	HIMACHAL PRADESH	20	22,264.08	33,301.38	49.57	5	9,650.78	20,714.91	114.64
9	JAMMU AND KASHMIR	30	48,180.49	74,107.74	53.81	3	6,236.00	32,296.00	417.90
10	KARNATAKA	56	85,354.49	97,051.69	13.70	20	46,634.93	58,665.86	25.80
11	KERALA	22	30,240.60	35,398.30	17.06	11	13,558.92	18,716.64	38.04
12	MADHYA PRADESH	78	68,627.95	77,288.11	12.62	18	17,082.73	26,768.36	56.70
13	MAHARASHTRA	229	2,06,831.47	2,29,792.00	11.10	38	63,804.94	92,041.96	44.26
14	MANIPUR	26	12,108.58	22,615.20	86.77	2	5,032.79	15,633.05	210.62
15	MEGHALAYA	13	5,269.68	8,391.62	59.24	1	906.46	4,083.02	350.44
16	MIZORAM	24	11,957.35	16,911.60	41.43	5	3,593.57	8,547.82	137.86

Extent of cost overrun in projects with respect to original cost (State Wise) Rs. 150 Crore and above
(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
17	NAGALAND	35	15,989.03	20,373.15	27.42	3	3,035.84	7,419.96	144.41
18	ODISHA	78	1,09,287.57	1,17,479.30	7.50	18	16,773.01	24,964.74	48.84
19	PUNJAB	28	18,344.99	20,091.84	9.52	6	4,559.90	6,549.20	43.63
20	RAJASTHAN	55	51,403.28	58,096.28	13.02	7	16,567.47	23,268.78	40.45
21	SIKKIM	18	7,278.84	14,598.73	100.56	2	1,727.48	9,047.37	423.73
22	TAMIL NADU	68	1,70,613.20	1,90,104.32	11.42	21	39,380.30	60,510.10	53.66
23	TRIPURA	19	5,084.45	5,259.05	3.43	2	767.30	978.18	27.48
24	UTTAR PRADESH	113	1,51,519.42	1,55,425.03	2.58	35	43,023.73	50,809.10	18.10
25	WEST BENGAL	71	62,900.10	81,252.31	29.18	32	31,194.23	49,872.97	59.88
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	2	655.03	945.73	44.38
27	DELHI	30	84,192.81	85,286.80	1.30	10	7,987.98	9,815.17	22.87
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
29	CHHATISGARH	46	78,726.75	89,025.67	13.08	11	27,508.38	37,926.65	37.87
30	JHARKHAND	41	69,363.87	75,272.33	8.52	13	30,350.60	38,034.32	25.32
31	UTTARAKHAND	30	35,588.83	50,291.17	41.31	9	26,727.41	41,430.26	55.01
32	TELANGANA	51	38,003.46	41,083.48	8.10	12	17,492.19	21,066.43	20.43
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	38.72
34	MULTI STATE	113	3,46,034.59	4,57,844.63	32.31	65	1,30,501.33	2,45,123.16	87.83
Total		1673	22,23,791.78	26,64,649.18	19.82	445	7,32,205.05	12,05,034.22	64.58

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	20	14,431.97	15,465.25	7.16	18	13,439.30	14,472.58	3 - 45
3	COAL	106	1,49,328.98	1,53,992.98	3.12	55	75,193.53	78,249.01	12 - 228
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	4	1,101.28	1,101.28	0.00	2	642.64	642.64	21 - 25
6	MINES	6	7,333.99	7,330.54	-0.05	4	6,633.37	6,633.37	32 - 37
7	STEEL	7	22,331.15	29,163.30	30.59	3	16,821.88	23,236.88	32 - 82
8	PETROLEUM	147	3,39,274.49	3,50,723.52	3.37	84	1,49,775.64	1,56,064.01	1 - 140
9	POWER	62	2,07,257.24	2,70,968.33	30.74	45	1,51,049.12	2,08,226.67	1 - 162
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	5	2,320.28	2,440.28	9 - 46
12	RAILWAYS	285	4,43,040.10	6,84,768.60	54.56	145	1,88,052.74	3,23,144.80	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	888	5,37,828.12	5,53,848.05	2.98	115	62,284.90	63,092.57	5 - 118
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	3	14,013.36	25,335.07	9 - 80
16	URBAN DEVELOPMENT	29	2,91,275.10	3,13,165.63	7.52	14	1,03,728.10	1,20,242.55	12 - 73
17	WATER RESOURCES	43	24,702.19	70,243.27	184.36	38	22,180.93	67,906.50	3 - 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
19	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	1	246.31	210.00	25 - 25
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
21	DEPARTMENT OF HIGHER EDUCATION	22	10,139.61	10,047.96	-0.90	16	8,120.38	8,026.40	3 - 93
22	HOME AFFAIRS	5	2,025.73	2,894.62	42.89	4	1,826.42	2,695.31	5 - 52
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	-
Total		1673	22,23,791.78	26,64,649.18	19.82	557	8,88,221.90	11,86,144.64	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	67	1,12,107.24	1,58,677.58	41.54	21	78,438.62	1,23,455.18	5 - 180
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	6	7,811.86	21,690.30	3 - 155
3	ASSAM	48	48,689.00	57,952.53	19.03	16	9,437.10	12,095.42	5 - 74
4	BIHAR	98	1,23,227.91	1,59,169.38	29.17	29	35,428.35	56,285.99	6 - 141
5	GOA	10	5,332.77	5,343.26	0.20	1	303.90	303.90	35 - 35
6	GUJARAT	59	1,08,152.96	1,19,380.30	10.38	16	32,593.86	43,094.53	1 - 139
7	HARYANA	36	61,492.56	63,819.18	3.78	12	8,519.18	8,693.90	5 - 29
8	HIMACHAL PRADESH	20	22,264.08	33,301.38	49.57	4	5,923.10	12,021.10	4 - 162
9	JAMMU AND KASHMIR	30	48,180.49	74,107.74	53.81	3	11,037.05	36,486.05	3 - 241
10	KARNATAKA	56	85,354.49	97,051.69	13.70	18	41,251.18	46,978.82	4 - 264
11	KERALA	22	30,240.60	35,398.30	17.06	6	3,831.57	4,855.75	13 - 59
12	MADHYA PRADESH	78	68,627.95	77,288.11	12.62	45	33,986.62	41,483.24	12 - 64
13	MAHARASHTRA	229	2,06,831.47	2,29,792.00	11.10	42	81,158.58	1,03,870.66	6 - 219
14	MANIPUR	26	12,108.58	22,615.20	86.77	1	4,454.17	14,322.00	153 - 153
15	MEGHALAYA	13	5,269.68	8,391.62	59.24	3	1,154.59	1,099.97	34 - 93
16	MIZORAM	24	11,957.35	16,911.60	41.43	9	6,557.52	10,691.05	43 - 117
17	NAGALAND	35	15,989.03	20,373.15	27.42	10	5,122.51	9,458.99	39 - 132
18	ODISHA	78	1,09,287.57	1,17,479.30	7.50	34	59,643.81	67,286.77	1 - 228
19	PUNJAB	28	18,344.99	20,091.84	9.52	4	1,936.78	1,896.34	5 - 108
20	RAJASTHAN	55	51,403.28	58,096.28	13.02	12	23,216.07	28,460.72	1 - 84
21	SIKKIM	18	7,278.84	14,598.73	100.56	2	1,629.53	8,890.05	49 - 96
22	TAMIL NADU	68	1,70,613.20	1,90,104.32	11.42	31	71,106.16	81,107.32	1 - 201
23	TRIPURA	19	5,084.45	5,259.05	3.43	2	1,007.91	1,144.00	27 - 31
24	UTTAR PRADESH	113	1,51,519.42	1,55,425.03	2.58	40	80,955.60	82,214.10	2 - 73
25	WEST BENGAL	71	62,900.10	81,252.31	29.18	36	32,547.77	40,135.98	5 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	5	1,715.32	2,005.82	39 - 51
27	DELHI	30	84,192.81	85,286.80	1.30	15	12,739.94	13,879.18	5 - 59
28	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
29	CHHATISGARH	46	78,726.75	89,025.67	13.08	24	34,481.96	44,179.94	3 - 144
30	JHARKHAND	41	69,363.87	75,272.33	8.52	21	54,870.84	57,098.55	3 - 188
31	UTTARAKHAND	30	35,588.83	50,291.17	41.31	14	27,775.12	42,001.06	3 - 138
32	TELANGANA	51	38,003.46	41,083.48	8.10	14	17,681.95	18,501.20	9 - 168
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	21 - 21
34	MULTI STATE	113	3,46,034.59	4,57,844.63	32.31	59	99,362.11	1,49,781.43	7 - 276
Total		1673	22,23,791.78	26,64,649.18	19.82	557	8,88,221.90	11,86,144.64	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	20	15,324.88	15,465.25	0.92	15	12,776.77	12,917.14	3 - 34
3	COAL	106	1,51,749.92	1,53,992.98	1.48	40	40,477.27	43,508.86	0 - 168
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	4	1,101.28	1,101.28	0.00	1	215.92	215.92	25 - 25
6	MINES	6	8,226.44	7,330.54	-10.89	1	355.00	355.00	37 - 37
7	STEEL	7	28,746.15	29,163.30	1.45	3	23,236.88	23,236.88	32 - 82
8	PETROLEUM	147	3,62,601.27	3,50,723.52	-3.28	52	47,818.57	46,573.96	0 - 140
9	POWER	62	2,67,295.21	2,70,968.33	1.37	28	1,23,531.95	1,25,705.80	0 - 138
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	5	2,320.28	2,440.28	9 - 46
12	RAILWAYS	285	5,56,878.65	6,84,768.60	22.97	116	1,83,284.30	2,53,363.23	0 - 324
13	ROAD TRANSPORT AND HIGHWAYS	888	5,45,726.59	5,53,848.05	1.49	97	54,762.99	54,585.92	0 - 118
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	3	25,335.07	25,335.07	9 - 80
16	URBAN DEVELOPMENT	29	3,00,321.90	3,13,165.63	4.28	4	31,357.10	33,371.10	12 - 44
17	WATER RESOURCES	43	70,134.44	70,243.27	0.16	38	67,563.04	67,906.50	3 - 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
19	DEFENCE PRODUCTION	1	210.00	210.00	0.00	1	210.00	210.00	25 - 25
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
21	DEPARTMENT OF HIGHER EDUCATION	22	10,170.00	10,047.96	-1.20	11	5,695.41	5,656.23	3 - 57
22	HOME AFFAIRS	5	2,113.83	2,894.62	36.94	1	1,219.21	2,000.00	31 - 31
23	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	-
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	-
Total		1673	25,06,671.72	26,64,649.18	6.30	420	6,87,279.76	7,77,729.89	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest cost						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	20	15,324.88	15,465.25	0.92	2	1,488.27	1,712.33	15.06
3	COAL	106	1,51,749.92	1,53,992.98	1.48	8	22,093.43	25,237.09	14.23
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	6	8,226.44	7,330.54	-10.89	0	0.00	0.00	0.00
7	STEEL	7	28,746.15	29,163.30	1.45	1	1,682.85	2,100.00	24.79
8	PETROLEUM	147	3,62,601.27	3,50,723.52	-3.28	2	4,523.46	5,073.34	12.16
9	POWER	62	2,67,295.21	2,70,968.33	1.37	12	40,344.82	45,018.94	11.59
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	12	5,589.39	6,374.57	14.05
12	RAILWAYS	285	5,56,878.65	6,84,768.60	22.97	173	2,04,872.30	3,42,235.05	67.05
13	ROAD TRANSPORT AND HIGHWAYS	888	5,45,726.59	5,53,848.05	1.49	144	95,321.57	1,12,468.39	17.99
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	29	3,00,321.90	3,13,165.63	4.28	3	47,274.77	60,118.50	27.17
17	WATER RESOURCES	43	70,134.44	70,243.27	0.16	4	1,393.47	1,736.93	24.65
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
19	DEFENCE PRODUCTION	1	210.00	210.00	0.00	0	0.00	0.00	0.00
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
21	DEPARTMENT OF HIGHER EDUCATION	22	10,170.00	10,047.96	-1.20	3	1,244.31	1,263.46	1.54
22	HOME AFFAIRS	5	2,113.83	2,894.62	36.94	1	1,219.21	2,000.00	64.04
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0.00
Total		1673	25,06,671.72	26,64,649.18	6.30	370	4,71,670.94	6,64,827.90	40.95

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	84- 145
2	CIVIL AVIATION	20	15,324.88	15,465.25	0.92	2	1,488.27	1,712.33	21- 24
3	COAL	106	1,51,749.92	1,53,992.98	1.48	6	4,567.14	7,709.99	36- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	6	8,226.44	7,330.54	-10.89	0	0.00	0.00	0- 0
7	STEEL	7	28,746.15	29,163.30	1.45	0	0.00	0.00	0- 0
8	PETROLEUM	147	3,62,601.27	3,50,723.52	-3.28	0	0.00	0.00	0- 0
9	POWER	62	2,67,295.21	2,70,968.33	1.37	4	29,266.18	32,441.03	9- 51
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	1	1,351.00	1,471.00	9- 9
12	RAILWAYS	285	5,56,878.65	6,84,768.60	22.97	77	1,07,000.17	1,77,541.01	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	888	5,45,726.59	5,53,848.05	1.49	8	5,598.87	6,383.43	19- 105
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	29	3,00,321.90	3,13,165.63	4.28	1	10,773.00	12,787.00	44- 44
17	WATER RESOURCES	43	70,134.44	70,243.27	0.16	4	1,393.47	1,736.93	12- 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
19	DEFENCE PRODUCTION	1	210.00	210.00	0.00	0	0.00	0.00	0- 0
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
21	DEPARTMENT OF HIGHER EDUCATION	22	10,170.00	10,047.96	-1.20	1	496.00	498.99	57- 57
22	HOME AFFAIRS	5	2,113.83	2,894.62	36.94	1	1,219.21	2,000.00	31- 31
23	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	0- 0
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0- 0
Total		1673	25,06,671.72	26,64,649.18	6.30	108	1,90,424.31	2,84,780.71	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	84- 145
2	CIVIL AVIATION	20	14,431.97	15,465.25	7.16	4	3,288.50	4,358.06	21- 45
3	COAL	106	1,49,328.98	1,53,992.98	3.12	15	30,646.30	34,586.95	12- 188
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	6	7,333.99	7,330.54	-0.05	0	0.00	0.00	0- 0
7	STEEL	7	22,331.15	29,163.30	30.59	1	15,525.00	21,940.00	82- 82
8	PETROLEUM	147	3,39,274.49	3,50,723.52	3.37	23	51,661.57	68,831.34	6- 140
9	POWER	62	2,07,257.24	2,70,968.33	30.74	24	97,289.86	1,55,985.46	6- 162
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	1	1,351.00	1,471.00	9- 9
12	RAILWAYS	285	4,43,040.10	6,84,768.60	54.56	110	1,39,575.93	2,76,128.51	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	888	5,37,828.12	5,53,848.05	2.98	21	10,976.62	12,725.67	19- 105
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	1	13,334.00	24,664.00	80- 80
16	URBAN DEVELOPMENT	29	2,91,275.10	3,13,165.63	7.52	4	60,511.47	77,105.12	34- 73
17	WATER RESOURCES	43	24,702.19	70,243.27	184.36	7	11,956.56	57,771.61	12- 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
19	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0- 0
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
21	DEPARTMENT OF HIGHER EDUCATION	22	10,139.61	10,047.96	-0.90	1	496.18	498.99	57- 57
22	HOME AFFAIRS	5	2,025.73	2,894.62	42.89	3	1,659.44	2,528.33	5- 52
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0- 0
Total		1673	22,23,791.78	26,64,649.18	19.82	219	4,70,316.43	7,84,272.04	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

<u>List of projects completed/dropped/Frozen during current month</u>							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Project	DOA	Original		Now anticipated		Final Expenditure
			Cost	DOC	Cost	DOC	
	<u>PETROLEUM</u>						
1	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	06/2016	423.00	08/2019	502.00	05/2021	447.89
2	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	212.00	01/2021	212.00	09/2021	177.58
3	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	05/2016	261.00	01/2021	261.00	09/2021	195.22
4	PIPELINE NETWORK PROJECT GELEKI, ASSAM	07/2016	249.85	05/2020	303.75	11/2021	229.85
5	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	08/2017	384.58	04/2021	384.58	03/2021	302.10
6	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	1,524.06	12/2021	1,524.06	11/2021	1,037.45
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
7	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	03/2016	229.37	11/2018	229.37	N.A.	152.85
8	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	01/2017	256.66	N.A.	256.66	03/2021	16.42
	<u>STEEL</u>						
9	COKE OVEN BATTERY-5	12/2011	2,858.00	12/2017	2,858.00	09/2022	2,018.72

TABLE-14

List of projects added Rs. 150 Crore and above					(December 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON EPC	8/2021	218.38	2/2023	218.38	2/2023
	<u>SOCIAL JUSTICE</u>					
2	CENTRE FOR DISABILITY SPORTS EPC	2/2019	170.99	3/2024	170.99	3/2024

FLASH REPORT

TABLE-15

Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		6105	
Achieved up to month		3051	

TABLE-16

List of projects reporting additional delayed Rs. 150 Crore and above							(December 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 NPCIL	11,459.00	16,580.00	12/2015	02/2022	12/2022	10
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT AAI	438.28	402.00	06/2019	12/2021	01/2022	1
3	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA AAI	389.71	389.71	11/2021	01/2023	04/2023	3
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT AAI	346.27	480.33	09/2021	12/2022	06/2023	6
	<u>COAL</u>						
5	MADHUBAND NLW WASHERY BCCL	289.45	289.45	05/2014	01/2022	03/2022	2
6	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) BCCL	555.52	555.52	03/2021	03/2022	03/2023	12
	<u>FERTILISERS</u>						
7	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY RCF	426.72	426.72	04/2020	12/2021	01/2022	1

List of projects reporting additional delayed Rs. 150 Crore and above (December 2021)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
8	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT NFL	215.92	215.92	11/2019	10/2021	12/2021	2
	<u>MINES</u>						
9	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA CPWD EPC	255.37	255.37	04/2022	04/2022	12/2024	32
	<u>STEEL</u>						
10	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	21,940.00	05/2015	01/2022	03/2022	2
	<u>PETROLEUM</u>						
11	BSVI UPGRADATION MANGALORE REFIN	1,810.00	1,810.00	12/2019	02/2022	03/2022	1
12	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	12/2021	01/2022	1
13	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI IOCL EPC	1,398.00	1,398.00	12/2023	12/2023	01/2024	1
14	DOBHI-DURGAPUR PIPELINE PROJECT GAIL	2,433.00	2,433.00	12/2020	01/2022	03/2022	2
15	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU IOCL	466.43	466.43	10/2020	01/2022	03/2022	2
16	LPG BP PROJECT MOTIHARI IOCL	206.50	206.50	03/2021	01/2022	03/2022	2
17	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT GAIL	286.42	327.01	08/2020	01/2022	03/2022	2
18	PIPELINE REPLACEMENT PROJECT (PRP-VI) ONGC	763.92	733.86	12/2020	12/2021	02/2022	2
19	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	03/2022	06/2022	3
20	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR IOCL	522.00	522.00	03/2021	12/2021	03/2022	3
21	DURGAPUR-HALDIA PIPELINE PROJECT GAIL	1,740.00	1,740.00	12/2020	12/2022	06/2023	6
22	BARAUNI-GUWAHATI PIPELINE GAIL	3,308.00	3,060.00	12/2021	12/2022	06/2023	6
23	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH IOCL	466.00	466.00	04/2021	03/2022	09/2022	6

List of projects reporting additional delayed Rs. 150 Crore and above (December 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
24	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II GAIL Central Sector Projects	2,915.00	5,909.00	12/2012	02/2022	08/2024	30
	<u>POWER</u>						
25	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	546.36	11/2016	01/2022	02/2022	1
26	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	03/2022	04/2022	1
27	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	02/2022	03/2022	1
28	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII PGCIL	379.95	379.95	12/2019	12/2021	01/2022	1
29	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	2,311.89	12/2018	12/2021	01/2022	1
30	DURGAPUR PP-III (2X20 MW) - NSPCL NTPC	529.68	633.80	11/2018	02/2022	03/2022	1
31	JETSAR SOLAR 160 MW NTPC EPC	702.28	702.28	03/2021	12/2021	01/2022	1
32	CHHATTARGARH 150 MW NTPC EPC	599.99	599.99	07/2022	07/2022	08/2022	1
33	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ PGCIL	322.30	322.30	02/2019	02/2022	04/2022	2
34	ANTA SOLAR 90 MW NTPC EPC	382.22	382.22	03/2022	03/2022	05/2022	2
35	GUJARAT 200 MW (GUVNL TENDER) NTPC EPC	842.27	842.27	07/2022	06/2022	08/2022	2
36	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO PGCIL	197.40	197.40	03/2018	12/2021	03/2022	3
37	BHENSARA 320 MW NTPC EPC	1,221.73	1,221.73	07/2022	05/2022	08/2022	3
38	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	14,719.10	08/2013	08/2022	05/2023	9
	<u>HEALTH AND FAMILY WELFARE</u>						
39	HOSPITAL AND TEACHING- AIIMS NAGPUR HSCC Central Sector Projects	582.99	582.99	N.A.	10/2021	12/2021	2
40	HOSPITAL AND TEACHING- AIIMS GUNTUR HSCC Central Sector Projects	601.02	601.02	N.A.	12/2021	03/2022	3
	<u>RAILWAYS</u>						

List of projects reporting additional delayed Rs. 150 Crore and above (December 2021)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
41	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	11/2021	12/2021	1
42	ARSIKERE-TUMKUR SWR	578.00	760.00	03/2020	12/2021	01/2022	1
43	MATHURA-PLWAL 4TH LINE (80KM) NCR	668.70	680.00	03/2020	12/2021	01/2022	1
44	KURUPPANTHARA-CHINGAVANAM SR	270.14	749.40	N.A.	01/2022	03/2022	2
45	NEW BG LINE FROM JAGBANI TO BIRATNAGAR NFR	241.52	373.87	N.A.	03/2022	06/2022	3
46	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) SER	390.39	511.75	12/2021	12/2021	06/2022	6
47	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) SER	1,866.31	1,866.31	05/2023	05/2023	12/2023	7
48	ANAND GODHRA DOUBLING PROJECT 79 KMS WR	692.25	742.88	03/2020	03/2023	03/2024	12
49	PURULIA TO KOTSHILA DOUBLING (39.1 KM) SER	338.00	393.83	06/2022	06/2022	06/2023	12
50	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) SER	428.65	472.50	06/2022	06/2022	12/2025	42
51	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR NCR	2,030.50	2,030.50	N.A.	12/2021	12/2027	72
52	CHENNAI-CUDDALORE VIA MAMALLAPURAM SR	523.52	1,205.00	N.A.	03/2024	03/2030	72
ROAD TRANSPORT AND HIGHWAYS							
53	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	12/2021	01/2022	1
54	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI-KAWARDHA SECTION. MoRTH EPC	291.05	291.05	N.A.	12/2021	01/2022	1
55	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 MoRTH EPC	628.45	628.45	01/2020	12/2021	01/2022	1
56	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 MoRTH EPC	957.54	927.73	02/2020	12/2021	01/2022	1
57	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	12/2021	01/2022	1
58	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS MoRTH	279.44	279.44	03/2018	12/2021	01/2022	1

List of projects reporting additional delayed Rs. 150 Crore and above (December 2021)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
59	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIST MoRTH	809.16	809.16	07/2018	12/2021	01/2022	1
60	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM MoRTH	877.79	949.54	06/2019	12/2021	01/2022	1
61	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 MoRTH	306.59	306.59	N.A.	12/2021	01/2022	1
62	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION MoRTH	423.79	423.79	01/2018	12/2021	01/2022	1
63	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 MoRTH	379.16	379.16	11/2017	12/2021	01/2022	1
64	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T NHA	804.97	804.97	06/2018	10/2021	12/2021	2
65	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS MoRTH	162.56	162.56	03/2018	12/2021	02/2022	2
66	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS MoRTH	166.21	174.90	08/2018	12/2021	02/2022	2
67	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS MoRTH	184.62	184.62	02/2018	12/2021	02/2022	2
68	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. MoRTH	205.05	205.05	03/2017	12/2021	02/2022	2
69	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS MoRTH	217.22	226.88	08/2018	12/2021	02/2022	2
70	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS MoRTH	233.04	233.04	03/2018	12/2021	02/2022	2
71	2L+PS OF THIKRI ANJAD SECTION OF NH-347B MoRTH	249.05	249.05	07/2018	12/2021	02/2022	2
72	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA MoRTH	536.65	536.65	12/2019	12/2021	02/2022	2
73	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. MoRTH	392.33	428.55	03/2018	12/2021	02/2022	2
74	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 NHA	593.26	717.24	05/2018	03/2022	06/2022	3

List of projects reporting additional delayed Rs. 150 Crore and above (December 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
75	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB NHAI	261.76	207.00	N.A.	11/2021	02/2022	3
76	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS MoRTH	326.99	326.99	N.A.	12/2021	03/2022	3
77	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J MoRTH	288.30	323.36	08/2020	12/2021	03/2022	3
78	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION MoRTH	335.32	335.32	06/2017	12/2021	03/2022	3
79	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V MoRTH	476.20	544.00	09/2016	12/2021	03/2022	3
80	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A MoRTH	188.80	188.80	05/2019	12/2021	03/2022	3
81	HOSPET-BELLARY-KARNATAKA AP BORDER NHAI	1,167.42	870.00	03/2019	12/2022	06/2023	6
82	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION MoRTH	624.98	731.50	10/2016	12/2021	06/2022	6
83	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE NHAI	379.90	379.90	N.A.	03/2021	12/2021	9
	<u>TELECOMMUNICATIONS</u>						
84	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT CPWD FOR TELECO	248.20	248.20	03/2018	12/2021	01/2022	1
	<u>WATER RESOURCES</u>						
85	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS UPJalNigam	967.23	967.23	09/2021	09/2021	12/2021	3
86	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH UPJalNigam	206.05	206.05	10/2021	10/2021	03/2022	5
87	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA UPJalNigam	767.59	767.59	09/2021	09/2021	03/2022	6
88	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI DJB	515.07	515.07	01/2021	06/2021	12/2021	6

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (December 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
89	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA BUIDCO	578.89	578.89	06/2022	06/2022	12/2022	6
90	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA BUIDCO	824.00	824.00	06/2022	06/2022	12/2022	6
91	MATHURA SEWERAGE SCHEME UPJalNigam	460.45	460.45	12/2020	05/2021	12/2021	7
92	SEWER NETWORK SPS AND STP BEGUSARAI BUIDCO	230.06	230.06	07/2021	07/2021	04/2022	9
93	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA UPJalNigam	279.91	330.05	12/2019	01/2021	11/2021	10
94	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR BUIDCO	225.77	398.90	03/2020	03/2021	02/2022	11
95	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH UPJalNigam	231.79	234.03	12/2021	12/2021	12/2022	12
96	SEWERAGE SCHEME AT PAHARI ZONE V PATNA BUIDCO	356.37	356.37	04/2021	04/2021	04/2022	12
97	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE KMDA	272.32	272.32	04/2020	03/2021	03/2022	12
98	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK BUIDCO	277.42	277.42	05/2021	05/2021	06/2022	13
99	SEWER NETWORKS SPS AND STP HAJIPUR BUIDCO	305.19	305.19	08/2021	12/2021	04/2023	16
100	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH KMDA	160.00	154.73	02/2022	10/2022	03/2024	17
101	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA KMDA	307.12	307.12	09/2022	09/2022	04/2024	19
102	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH UPJalNigam	298.12	213.91	07/2021	06/2022	03/2024	21
103	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA KMDA	198.43	224.69	02/2022	06/2022	03/2024	21
104	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS KMDA	165.16	165.16	06/2022	06/2022	03/2024	21

List of projects reporting additional delayed Rs. 150 Crore and above (December 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
105	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH KMDA	185.22	185.22	12/2021	12/2021	09/2023	21
106	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI KMDA	172.10	172.10	12/2021	12/2021	09/2023	21
107	INTERCEPTION AND DIVERSION WITH STP AT BALLY KMDA	164.93	164.93	12/2021	12/2021	09/2023	21
108	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH UPJalNigam	681.78	690.71	06/2022	06/2022	04/2024	22
109	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS KMDA	384.96	384.96	04/2022	04/2022	04/2024	24
110	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL KMDA	287.53	287.53	04/2022	04/2022	04/2024	24
111	I AND D AND STP WORKS AT BURDWAN WEST BENGAL KMDA	234.31	234.31	04/2022	04/2022	04/2024	24
112	FARRUKHABAD I AND D AND STP WORKS HAM UPJalNigam	213.62	261.12	03/2022	03/2022	04/2024	25
113	SEWER NETWORKS, SPS AND STP, MUNGER BUIDCO	294.02	294.02	10/2021	10/2021	12/2023	26
114	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH UPJalNigam	271.39	271.39	08/2021	08/2021	03/2024	31
	<u>DEFENCE PRODUCTION</u>						
115	RESIDENTIAL QUARTERS FOR HAL, BANGLORE CPWD FOR DEFENCE	246.31	210.00	02/2020	12/2021	03/2022	3
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
116	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT CPWD EDUCATION	588.72	588.72	09/2022	04/2023	06/2023	2
	<u>HOME AFFAIRS</u>						
117	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- CPWD FOR MHA EPC	166.98	166.98	10/2023	10/2023	04/2024	6
118	NSG AT KOLKATA CPWD FOR MHA Central Sector Projects	162.88	238.00	04/2018	12/2021	08/2022	8

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (December 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)

FLASH REPORT

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,167,41.00	1,29,969.00	70,005.37
CIVIL AVIATION	20	14,431.97	153,24.88	15,465.25	5,714.71
COAL	106	1,49,328.98	1,517,49.92	1,53,992.98	55,306.02
FINANCE	2	557.77	5,57.77	557.73	412.93
FERTILISERS	4	1,101.28	11,01.28	1,101.28	914.82
MINES	6	7,333.99	82,26.44	7,330.54	1,819.26
STEEL	7	22,331.15	287,46.15	29,163.30	22,761.70
PETROLEUM	147	3,39,274.49	3,626,01.27	3,50,723.52	1,25,031.63
POWER	62	2,07,257.24	2,672,95.21	2,70,968.33	1,80,166.07
HEAVY INDUSTRY	2	3,272.00	52,81.30	4,627.30	4,341.63
HEALTH AND FAMILY WELFARE	29	15,273.26	152,73.26	15,715.78	9,278.31
RAILWAYS	285	4,43,040.10	5,568,78.65	6,84,768.60	2,77,511.94
ROAD TRANSPORT AND HIGHWAYS	888	5,37,828.12	5,457,26.59	5,53,848.05	3,35,150.64
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,967.38
TELECOMMUNICATIONS	3	14,013.36	253,35.07	25,335.07	20,771.22
URBAN DEVELOPMENT	29	2,91,275.10	3,003,21.90	3,13,165.63	1,56,187.13
WATER RESOURCES	43	24,702.19	701,34.44	70,243.27	22,941.81
SOCIAL JUSTICE	1	170.99	1,70.99	170.99	34.00
DEFENCE PRODUCTION	1	246.31	2,10.00	210.00	158.92
COMMERCE	1	302.64	3,02.64	302.64	30.00
DEPARTMENT OF HIGHER EDUCATION	22	10,139.61	101,70.00	10,047.96	4,113.00
HOME AFFAIRS	5	2,025.73	21,13.83	2,894.62	1,289.36
DPIIT	2	17,352.09	173,52.09	18,990.30	12,618.48
DONER	1	151.33	1,51.33	151.33	149.33
RENEWABLE ENERGY	1	271.90	2,71.90	271.90	90.99
Grand total	1673	22,23,791.78	25,06,671.72	26,64,649.18	13,08,766.65

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns
(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	67	1,12,107.24	1,58,677.58	41.54	5	37,258.95	91,197.51	24 - 180
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	4	6,882.14	20,760.58	59 - 155
3	ASSAM	48	48,689.00	57,952.53	19.03	6	5,442.47	8,127.54	12 - 60
4	BIHAR	98	1,23,227.91	1,59,169.38	29.17	10	25,514.93	46,372.57	23 - 141
5	GOA	10	5,332.77	5,343.26	0.20	0	0.00	0.00	-
6	GUJARAT	59	1,08,152.96	1,19,380.30	10.38	12	29,112.81	39,741.26	3 - 139
7	HARYANA	36	61,492.56	63,819.18	3.78	2	493.05	667.77	19 - 29
8	HIMACHAL PRADESH	20	22,264.08	33,301.38	49.57	2	5,270.59	11,368.59	9 - 162
9	JAMMU AND KASHMIR	30	48,180.49	74,107.74	53.81	1	2,500.00	27,949.00	241 - 241
10	KARNATAKA	56	85,354.49	97,051.69	13.70	8	31,934.94	37,996.31	7 - 264
11	KERALA	22	30,240.60	35,398.30	17.06	2	1,719.06	2,743.24	32 - 59
12	MADHYA PRADESH	78	68,627.95	77,288.11	12.62	13	14,083.91	22,223.70	12 - 48
13	MAHARASHTRA	229	2,06,831.47	2,29,792.00	11.10	18	44,122.37	66,978.06	8 - 219
14	MANIPUR	26	12,108.58	22,615.20	86.77	1	4,454.17	14,322.00	153 - 153
15	MEGHALAYA	13	5,269.68	8,391.62	59.24	0	0.00	0.00	-
16	MIZORAM	24	11,957.35	16,911.60	41.43	1	2,393.47	6,527.00	117 - 117
17	NAGALAND	35	15,989.03	20,373.15	27.42	1	2,326.52	6,663.00	132 - 132
18	ODISHA	78	1,09,287.57	1,17,479.30	7.50	13	14,838.17	22,481.13	6 - 189
19	PUNJAB	28	18,344.99	20,091.84	9.52	1	754.54	756.27	30 - 30
20	RAJASTHAN	55	51,403.28	58,096.28	13.02	3	13,624.08	18,868.73	23 - 84
21	SIKKIM	18	7,278.84	14,598.73	100.56	1	1,339.48	8,600.00	96 - 96
22	TAMIL NADU	68	1,70,613.20	1,90,104.32	11.42	10	11,558.29	23,016.66	27 - 201
23	TRIPURA	19	5,084.45	5,259.05	3.43	1	569.63	742.00	27 - 27
24	UTTAR PRADESH	113	1,51,519.42	1,55,425.03	2.58	16	27,425.13	29,645.91	11 - 73
25	WEST BENGAL	71	62,900.10	81,252.31	29.18	16	17,788.15	25,381.63	12 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	1	417.23	707.73	45 - 45
27	DELHI	30	84,192.81	85,286.80	1.30	4	6,466.89	7,685.33	5 - 34
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATISGARH	46	78,726.75	89,025.67	13.08	9	25,751.75	35,569.08	18 - 84
30	JHARKHAND	41	69,363.87	75,272.33	8.52	6	22,741.18	25,969.89	6 - 188
31	UTTARAKHAND	30	35,588.83	50,291.17	41.31	5	23,991.39	38,217.33	3 - 138
32	TELANGANA	51	38,003.46	41,083.48	8.10	8	14,219.92	15,518.31	9 - 168
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	21 - 21
34	MULTI STATE	113	3,46,034.59	4,57,844.63	32.31	38	74,974.95	1,26,993.58	12 - 276
Total		1673	22,23,791.78	26,64,649.18	19.82	219	4,70,316.43	7,84,272.04	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	153	2
2	RAILWAYS	150	4
3	PETROLEUM	58	7
4	POWER	37	5
5	COAL	31	0
6	URBAN DEVELOPMENT	23	0
7	ATOMIC ENERGY	5	1
8	CIVIL AVIATION	5	0
9	STEEL	4	1
10	HEALTH AND FAMILY WELFARE	4	0
11	DPIIT	2	0
12	MINES	1	0
13	HEAVY INDUSTRY	1	0
14	SHIPPING AND PORTS	1	0
15	TELECOMMUNICATIONS	1	0
16	WATER RESOURCES	1	0
17	HOME AFFAIRS	1	0
	Total	478	20

FLASH REPORT

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	June,2021			
	<u>PETROLEUM</u>			
1	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	August,2021			
	<u>PETROLEUM</u>			
3	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
	<u>POWER</u>			
4	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
5	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
6	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
7	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
8	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
9	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
10	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08
	September,2021			
	<u>POWER</u>			
12	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000061]	4,824.12	10/2012	4,612.66

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	EASTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000155]	1,364.52	04/2016	1,290.03
14	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000168]	5,151.37	03/2018	3,269.93
15	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000218]	3,519.59	05/2019	2,562.41
16	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000257]	3,654.00	04/2019	3,508.04
	<u>RAILWAYS</u>			
17	GONDIA-JABALPUR(GC),(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100186]	511.86	04/2020	1,867.16
18	NANDYAL-YERRAGUNTALA(NL),SCR (SOUTH CENTRAL RAILWAY) - [220100192]	164.36	02/2009	1,148.67
19	HARIDASPUR-PARADEEP(NL) (RAIL VIKAS NIGAM LTD.) - [220100285]	1,185.64	12/2017	2,129.37
20	CHHINDWARA - NAGPUR (GC)(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100324]	383.79	-	1,448.56
21	BARDHAMAN-KATWA (GC) (EASTERN RAILWAYS) - [N22000091]	1,106.62	12/2010	1,003.78
22	CHAMPA-JHARSUGUDA 3RD LINE (SOUTH EAST CENTRAL RAILWAY) - [N22000483]	872.00	12/2019	1,156.06
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
23	FOUR LANING OF AURANGABAD - YEDISHI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000508]	1,871.34	01/2018	3,443.43
24	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000541]	1,081.57	06/2019	480.25
25	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000545]	1,134.97	11/2018	809.71
26	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ((NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000621]	1,239.82	-	1,691.00
	<u>URBAN DEVELOPMENT</u>			
27	REDEVELOPMENT OF EAST KIDWAI NAGAR (NATIONAL BUILDING CONSTRUCTION CORPORATION LTD) - [N28000080]	4,264.00	11/2019	4,683.08
	October,2021			
	<u>PETROLEUM</u>			
28	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000227]	4,588.29	08/2018	5,376.50

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
29	BS-VI PROJECTS (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000295]	1,858.00	12/2019	1,528.75
	December,2021			
	<u>STEEL</u>			
30	COKE OVEN BATTERY-5 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000117]	2,858.00	12/2017	2,018.72
	<u>PETROLEUM</u>			
31	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000365]	1,524.06	12/2021	1,037.45

FLASH REPORT

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
	August,2021			
2	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
3	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
4	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
5	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
6	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00
	September,2021			
7	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000439]	1,885.74	05/2019	1,636.02

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	480
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	0
No of Projects in Current Month	478

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	209 (43.72%)	7 (1.46%)	65 (13.60%)	30 (6.28%)	167 (34.94%)	478
Latest Approved (Date)	144 (30.13%)	7 (1.46%)	141 (29.50%)	19 (3.97%)	167 (34.94%)	478

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	359	12,85,744.78	14,18,962.50	6,08,629.28	42.90	1,33,217.72	10.40
Project with Revision in Cost	119	7,16,235.73	7,31,713.09	4,40,183.04	60.20	15,477.36	2.20
Total	478	20,01,980.51	21,50,675.59	10,48,812.32	48.77	1,48,695.08	7.43
Original Cost of All Projects							
Original Cost	478	17,24,352.80	21,50,675.59	10,48,812.32	48.77	4,26,322.79	24.72

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	209	7,42,581.67	10,32,888.21	6,14,907.74	59.50	2,90,306.54	39.09
Latest Approved (RCE)	144	5,71,753.35	6,57,397.73	3,90,246.94	59.40	85,644.38	14.98

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	20	80,168.89	1,05,599.35	90,252.70	85.50	25,430.46	31.70
Total	20	80,168.89	1,05,599.35	90,252.70	85.47	25,430.46	31.72

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 1000 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	2	2,525.00	3,170.00	25.54
3	COAL	31	1,15,154.25	1,20,003.52	4.21	4	32,770.17	37,619.44	14.80
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	4	21,148.86	27,981.01	32.31	2	17,207.85	24,040.00	39.70
6	PETROLEUM	58	3,02,359.61	3,13,455.24	3.67	15	61,689.32	85,050.89	37.87
7	POWER	37	1,95,373.11	2,58,473.40	32.30	20	1,05,136.74	1,69,755.08	61.46
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	1	1,718.00	3,727.30	116.96
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
10	RAILWAYS	150	3,83,038.30	6,14,312.12	60.38	119	2,03,852.23	4,36,395.02	114.07
11	ROAD TRANSPORT AND HIGHWAYS	153	2,32,920.01	2,45,556.02	5.43	44	57,501.10	72,680.38	26.40
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	23	2,89,160.24	3,11,031.10	7.56	6	93,461.70	1,15,411.76	23.49
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		478	17,24,352.80	21,50,675.59	24.72	223	6,48,117.45	10,92,851.04	68.62

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						1000	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	18	93,351.27	1,39,782.11	49.74	8	43,079.45	98,432.29	128.49
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	2	8,264.33	22,029.33	166.56
3	ASSAM	8	33,271.03	41,170.76	23.74	5	16,996.48	26,066.21	53.36
4	BIHAR	29	91,524.56	1,25,846.81	37.50	16	46,877.81	81,835.56	74.57
5	GUJARAT	23	87,132.33	97,893.85	12.35	11	32,208.42	43,628.99	35.46
6	HARYANA	13	51,125.78	52,305.78	2.31	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	10	18,720.95	29,785.08	59.10	5	9,650.78	20,714.91	114.64
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	3	6,236.00	32,296.00	417.90
9	KARNATAKA	19	69,436.27	80,780.61	16.34	12	43,122.74	54,467.08	26.31
10	KERALA	9	24,577.63	28,831.32	17.31	7	12,015.73	16,269.42	35.40
11	MADHYA PRADESH	20	40,080.22	48,039.80	19.86	9	13,249.36	21,725.99	63.98
12	MAHARASHTRA	45	1,30,458.47	1,56,360.61	19.85	20	56,156.86	82,765.93	47.38
13	MANIPUR	2	5,032.79	15,633.05	210.62	2	5,032.79	15,633.05	210.62
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	6,527.00	172.70	1	2,393.47	6,527.00	172.70
16	NAGALAND	2	6,600.52	10,937.00	65.70	1	2,326.52	6,663.00	186.39
17	ODISHA	35	90,420.70	97,619.52	7.96	10	14,418.29	21,617.11	49.93
18	PUNJAB	7	8,647.82	9,958.16	15.15	2	2,557.95	3,868.29	51.23
19	RAJASTHAN	14	31,155.16	37,300.84	19.73	3	14,293.90	20,439.58	43.00
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	28	1,51,184.30	1,69,740.01	12.27	13	36,726.73	55,677.44	51.60
22	UTTAR PRADESH	42	1,17,043.81	1,21,833.81	4.09	15	34,907.43	41,150.08	17.88
23	WEST BENGAL	24	46,173.48	63,400.90	37.31	15	26,734.37	43,977.79	64.50
24	DELHI	8	75,922.38	77,028.97	1.46	2	5,992.21	7,178.00	19.79
25	CHHATISGARH	17	65,860.61	75,619.96	14.82	7	25,757.63	35,619.00	38.29
26	JHARKHAND	14	59,480.43	65,821.34	10.66	6	27,885.12	35,227.03	26.33
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	5	24,870.06	39,070.51	57.10
28	TELANGANA	6	19,991.02	22,312.66	11.61	4	14,138.06	16,827.58	19.02
29	MULTI STATE	57	3,22,806.44	4,29,854.50	33.16	36	1,18,871.02	2,28,172.85	91.95
Total		478	17,24,352.80	21,50,675.59	24.72	223	6,48,117.45	10,92,851.04	68.62

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	5	7,613.90	8,258.90	7 - 28
3	COAL	31	1,15,154.25	1,20,003.52	4.21	16	59,652.75	62,428.34	12 - 228
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	33 - 33
5	STEEL	4	21,148.86	27,981.01	32.31	2	16,559.01	22,974.01	61 - 82
6	PETROLEUM	58	3,02,359.61	3,13,455.24	3.67	32	1,30,117.75	1,36,033.65	1 - 140
7	POWER	37	1,95,373.11	2,58,473.40	32.30	26	1,42,400.40	1,98,967.15	1 - 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	150	3,83,038.30	6,14,312.12	60.38	99	1,65,359.50	2,95,427.83	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	153	2,32,920.01	2,45,556.02	5.43	10	15,211.87	15,375.44	21 - 108
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	23	2,89,160.24	3,11,031.10	7.56	9	1,02,178.24	1,18,673.02	12 - 73
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	31 - 31
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
Total		478	17,24,352.80	21,50,675.59	24.72	209	7,42,581.67	10,32,888.21	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	93,351.27	1,39,782.11	49.74	7	73,770.66	1,18,787.22	24 - 180
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	41,170.76	23.74	4	4,630.48	7,098.21	12 - 48
4	BIHAR	29	91,524.56	1,25,846.81	37.50	9	27,899.42	48,150.95	14 - 141
5	GUJARAT	23	87,132.33	97,893.85	12.35	8	28,375.60	38,668.18	3 - 84
6	HARYANA	13	51,125.78	52,305.78	2.31	3	5,172.94	5,172.94	7 - 20
7	HIMACHAL PRADESH	10	18,720.95	29,785.08	59.10	2	5,270.59	11,368.59	9 - 162
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	2	10,612.12	36,061.12	63 - 241
9	KARNATAKA	19	69,436.27	80,780.61	16.34	6	34,583.00	40,214.26	27 - 264
10	KERALA	9	24,577.63	28,831.32	17.31	2	1,719.06	2,743.24	32 - 59
11	MADHYA PRADESH	20	40,080.22	48,039.80	19.86	13	19,570.47	26,983.28	12 - 48
12	MAHARASHTRA	45	1,30,458.47	1,56,360.61	19.85	19	70,547.41	92,816.24	7 - 219
13	MANIPUR	2	5,032.79	15,633.05	210.62	1	4,454.17	14,322.00	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	6,527.00	172.70	1	2,393.47	6,527.00	117 - 117
16	NAGALAND	2	6,600.52	10,937.00	65.70	1	2,326.52	6,663.00	132 - 132
17	ODISHA	35	90,420.70	97,619.52	7.96	22	54,045.99	61,112.88	5 - 228
18	PUNJAB	7	8,647.82	9,958.16	15.15	0	0.00	0.00	-
19	RAJASTHAN	14	31,155.16	37,300.84	19.73	5	18,595.75	23,354.75	1 - 84
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	28	1,51,184.30	1,69,740.01	12.27	14	61,157.13	70,809.75	1 - 145
22	UTTAR PRADESH	42	1,17,043.81	1,21,833.81	4.09	16	71,197.66	72,382.71	5 - 48
23	WEST BENGAL	24	46,173.48	63,400.90	37.31	11	25,127.88	32,278.39	5 - 324
24	DELHI	8	75,922.38	77,028.97	1.46	5	9,694.73	10,801.32	15 - 59
25	CHHATISGARH	17	65,860.61	75,619.96	14.82	7	27,278.34	36,436.75	18 - 82
26	JHARKHAND	14	59,480.43	65,821.34	10.66	8	50,765.98	52,695.44	13 - 188
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	5	24,726.84	38,653.22	3 - 138
28	TELANGANA	6	19,991.02	22,312.66	11.61	3	13,183.42	13,427.82	23 - 168
29	MULTI STATE	57	3,22,806.44	4,29,854.50	33.16	33	87,857.23	1,36,766.52	7 - 276
Total		478	17,24,352.80	21,50,675.59	24.72	209	7,42,581.67	10,32,888.21	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

Extent of time overrun in projects with respect to latest schedule Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	8,168.90	8,258.90	1.10	5	8,168.90	8,258.90	7 - 28
3	COAL	31	1,17,517.97	1,20,003.52	2.12	11	29,179.51	31,664.26	0 - 168
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	-
5	STEEL	4	27,563.86	27,981.01	1.51	2	22,974.01	22,974.01	61 - 82
6	PETROLEUM	58	3,24,751.05	3,13,455.24	-3.48	14	32,888.04	32,006.64	1 - 140
7	POWER	37	2,55,249.40	2,58,473.40	1.26	14	1,17,253.51	1,19,387.23	0 - 138
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	150	4,94,823.15	6,14,312.12	24.15	75	1,64,054.12	2,29,632.46	0 - 324
11	ROAD TRANSPORT AND HIGHWAYS	153	2,39,236.63	2,45,556.02	2.64	11	15,975.08	16,071.26	0 - 108
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	1	24,664.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	23	2,98,187.37	3,11,031.10	4.31	4	31,357.10	33,371.10	12 - 44
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	31 - 31
17	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	-
Total		478	20,01,980.51	21,50,675.59	7.43	144	5,71,753.35	6,57,397.73	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	8,168.90	8,258.90	1.10	1	1,142.00	1,232.00	7.88
3	COAL	31	1,17,517.97	1,20,003.52	2.12	2	19,898.73	22,384.28	12.49
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0.00
5	STEEL	4	27,563.86	27,981.01	1.51	1	1,682.85	2,100.00	24.79
6	PETROLEUM	58	3,24,751.05	3,13,455.24	-3.48	2	4,523.46	5,073.34	12.16
7	POWER	37	2,55,249.40	2,58,473.40	1.26	7	37,733.26	41,958.26	11.20
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
10	RAILWAYS	150	4,94,823.15	6,14,312.12	24.15	100	1,77,291.25	3,00,225.19	69.34
11	ROAD TRANSPORT AND HIGHWAYS	153	2,39,236.63	2,45,556.02	2.64	39	54,031.84	64,621.23	19.60
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	0	0.00	0.00	0.00
14	URBAN DEVELOPMENT	23	2,98,187.37	3,11,031.10	4.31	3	47,274.77	60,118.50	27.17
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		478	20,01,980.51	21,50,675.59	7.43	163	3,92,348.46	5,62,501.10	43.37

[^] - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	84- 145
2	CIVIL AVIATION	5	8,168.90	8,258.90	1.10	1	1,142.00	1,232.00	24- 24
3	COAL	31	1,17,517.97	1,20,003.52	2.12	1	2,661.73	5,146.48	60- 60
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0- 0
5	STEEL	4	27,563.86	27,981.01	1.51	0	0.00	0.00	0- 0
6	PETROLEUM	58	3,24,751.05	3,13,455.24	-3.48	0	0.00	0.00	0- 0
7	POWER	37	2,55,249.40	2,58,473.40	1.26	3	28,864.28	31,999.00	19- 51
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	150	4,94,823.15	6,14,312.12	24.15	54	96,626.15	1,63,134.43	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	153	2,39,236.63	2,45,556.02	2.64	1	2,848.00	3,379.45	105- 105
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	0	0.00	0.00	0- 0
14	URBAN DEVELOPMENT	23	2,98,187.37	3,11,031.10	4.31	1	10,773.00	12,787.00	44- 44
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	31- 31
17	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	0- 0
Total		478	20,01,980.51	21,50,675.59	7.43	66	1,72,756.37	2,61,648.36	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,29,969.00	11.33	3	27,271.00	40,499.00	84- 145
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	2	2,525.00	3,170.00	24- 27
3	COAL	31	1,15,154.25	1,20,003.52	4.21	3	26,863.06	29,638.65	12- 188
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	4	21,148.86	27,981.01	32.31	1	15,525.00	21,940.00	82- 82
6	PETROLEUM	58	3,02,359.61	3,13,455.24	3.67	13	48,500.05	64,945.10	8- 140
7	POWER	37	1,95,373.11	2,58,473.40	32.30	16	93,440.16	1,51,524.96	13- 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	150	3,83,038.30	6,14,312.12	60.38	78	1,24,363.91	2,55,552.20	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	153	2,32,920.01	2,45,556.02	5.43	1	2,848.00	3,379.45	105- 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80- 80
14	URBAN DEVELOPMENT	23	2,89,160.24	3,11,031.10	7.56	3	60,314.14	76,888.12	36- 73
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	31- 31
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
Total		478	17,24,352.80	21,50,675.59	24.72	125	4,32,478.57	7,36,399.35	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

List of projects completed/dropped/Frozen during current month					Rs. 1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	1,524.06	12/2021	1,524.06	11/2021	1,037.45
	<u>STEEL</u>						
2	COKE OVEN BATTERY-5	12/2011	2,858.00	12/2017	2,858.00	09/2022	2,018.72

TABLE-32

List of projects added				Rs. 1000		Crore and above		(December 2021)
			Original		Anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC		

TABLE-33

Milestones (Cumulative due & achieved) Rs. 1000 Crore and above

Total 2676

Achieved up to month 1663

TABLE-34

List of projects reporting additional delayed Rs. 1000 Crore and above							(December 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 NPCIL	11,459.00	16,580.00	12/2015	02/2022	12/2022	10
	<u>STEEL</u>						
2	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	21,940.00	05/2015	01/2022	03/2022	2
	<u>PETROLEUM</u>						
3	BSVI UPGRADATION MANGALORE REFIN	1,810.00	1,810.00	12/2019	02/2022	03/2022	1
4	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	12/2021	01/2022	1
5	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI IOCL EPC	1,398.00	1,398.00	12/2023	12/2023	01/2024	1
6	DOBHI-DURGAPUR PIPELINE PROJECT GAIL	2,433.00	2,433.00	12/2020	01/2022	03/2022	2
7	DURGAPUR-HALDIA PIPELINE PROJECT GAIL	1,740.00	1,740.00	12/2020	12/2022	06/2023	6
8	BARAUNI-GUWAHATI PIPELINE GAIL	3,308.00	3,060.00	12/2021	12/2022	06/2023	6
9	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II GAIL Central Sector Projects	2,915.00	5,909.00	12/2012	02/2022	08/2024	30
	<u>POWER</u>						
10	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	03/2022	04/2022	1
11	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	02/2022	03/2022	1

List of projects reporting additional delayed Rs. 1000 Crore and above (December 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
12	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	2,311.89	12/2018	12/2021	01/2022	1
13	BHENSARA 320 MW NTPC EPC	1,221.73	1,221.73	07/2022	05/2022	08/2022	3
14	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	14,719.10	08/2013	08/2022	05/2023	9
	<u>RAILWAYS</u>						
15	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	11/2021	12/2021	1
16	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) SER	1,866.31	1,866.31	05/2023	05/2023	12/2023	7
17	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR NCR	2,030.50	2,030.50	N.A.	12/2021	12/2027	72
18	CHENNAI-CUDDALORE VIA MAMALLAPURAM SR	523.52	1,205.00	N.A.	03/2024	03/2030	72
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
19	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	12/2021	01/2022	1
20	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	12/2021	01/2022	1

TABLE-35

Sector wise analysis of projects Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,16,741.00	1,29,969.00	70,005.37
CIVIL AVIATION	5	7,613.90	81,68.90	8,258.90	2,374.77
COAL	31	1,15,154.25	1,175,17.97	1,20,003.52	44,734.71
MINES	1	5,540.00	64,35.90	5,540.00	1,182.87
STEEL	4	21,148.86	275,63.86	27,981.01	22,419.84
PETROLEUM	58	3,02,359.61	3,247,51.05	3,13,455.24	1,06,880.25
POWER	37	1,95,373.11	2,552,49.40	2,58,473.40	1,73,421.47
HEAVY INDUSTRY	1	1,718.00	37,27.30	3,727.30	3,526.63
HEALTH AND FAMILY WELFARE	4	6,160.00	61,60.00	6,531.00	1,484.52
RAILWAYS	150	3,83,038.30	4,948,23.15	6,14,312.12	2,45,475.47
ROAD TRANSPORT AND HIGHWAYS	153	2,32,920.01	2,392,36.63	2,45,556.02	1,67,843.02
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,967.38
TELECOMMUNICATIONS	1	13,334.00	246,64.00	24,664.00	20,545.00
URBAN DEVELOPMENT	23	2,89,160.24	2,981,87.37	3,11,031.10	1,54,947.14
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	18,335.60
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	1,049.80
DPIIT	2	17,352.09	173,52.09	18,990.30	12,618.48
Grand total	478	17,24,352.80	20,01,980.51	21,50,675.59	10,48,812.32


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	93,351.27	1,39,782.11	49.74	5	37,258.95	91,197.51	24 - 180
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	41,170.76	23.74	4	4,630.48	7,098.21	12 - 48
4	BIHAR	29	91,524.56	1,25,846.81	37.50	6	23,990.85	44,242.38	36 - 141
5	GUJARAT	23	87,132.33	97,893.85	12.35	7	26,970.60	37,263.18	3 - 84
6	HARYANA	13	51,125.78	52,305.78	2.31	0	0.00	0.00	-
7	HIMACHAL PRADESH	10	18,720.95	29,785.08	59.10	2	5,270.59	11,368.59	9 - 162
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	1	2,500.00	27,949.00	241 - 241
9	KARNATAKA	19	69,436.27	80,780.61	16.34	4	29,931.16	35,562.42	36 - 264
10	KERALA	9	24,577.63	28,831.32	17.31	2	1,719.06	2,743.24	32 - 59
11	MADHYA PRADESH	20	40,080.22	48,039.80	19.86	8	12,194.36	20,124.22	12 - 48
12	MAHARASHTRA	45	1,30,458.47	1,56,360.61	19.85	12	41,761.00	64,118.58	8 - 219
13	MANIPUR	2	5,032.79	15,633.05	210.62	1	4,454.17	14,322.00	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	6,527.00	172.70	1	2,393.47	6,527.00	117 - 117
16	NAGALAND	2	6,600.52	10,937.00	65.70	1	2,326.52	6,663.00	132 - 132
17	ODISHA	35	90,420.70	97,619.52	7.96	9	13,130.22	20,197.11	21 - 189
18	PUNJAB	7	8,647.82	9,958.16	15.15	0	0.00	0.00	-
19	RAJASTHAN	14	31,155.16	37,300.84	19.73	1	12,320.00	17,079.00	84 - 84
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	28	1,51,184.30	1,69,740.01	12.27	6	10,455.67	20,503.29	27 - 145
22	UTTAR PRADESH	42	1,17,043.81	1,21,833.81	4.09	6	23,396.00	25,203.99	12 - 39
23	WEST BENGAL	24	46,173.48	63,400.90	37.31	7	15,423.79	22,574.30	60 - 324
24	DELHI	8	75,922.38	77,028.97	1.46	2	5,992.21	7,178.00	29 - 31
25	CHHATISGARH	17	65,860.61	75,619.96	14.82	5	24,001.00	33,261.43	18 - 82
26	JHARKHAND	14	59,480.43	65,821.34	10.66	2	21,330.91	24,261.37	51 - 188
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	4	23,343.06	37,269.44	3 - 138
28	TELANGANA	6	19,991.02	22,312.66	11.61	2	11,759.46	12,371.74	23 - 168
29	MULTI STATE	57	3,22,806.44	4,29,854.50	33.16	25	68,300.23	1,18,727.92	12 - 276
Total		478	17,24,352.80	21,50,675.59	24.72	125	4,32,478.57	7,36,399.35	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

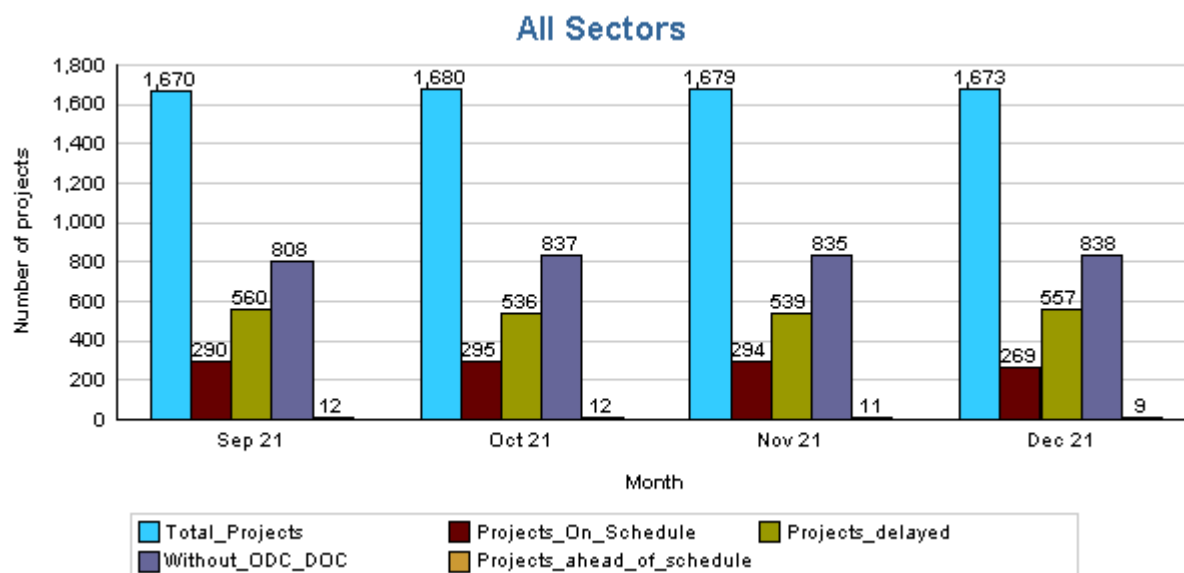

Break-up of 557 Delayed projects in December 2021

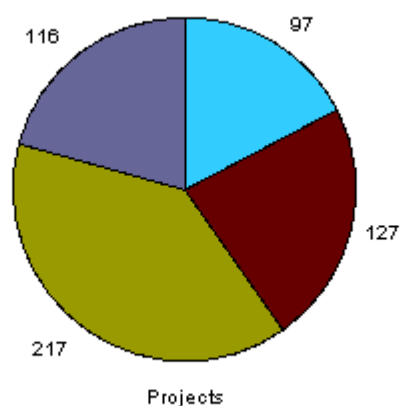


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of HOME AFFAIRS Sector

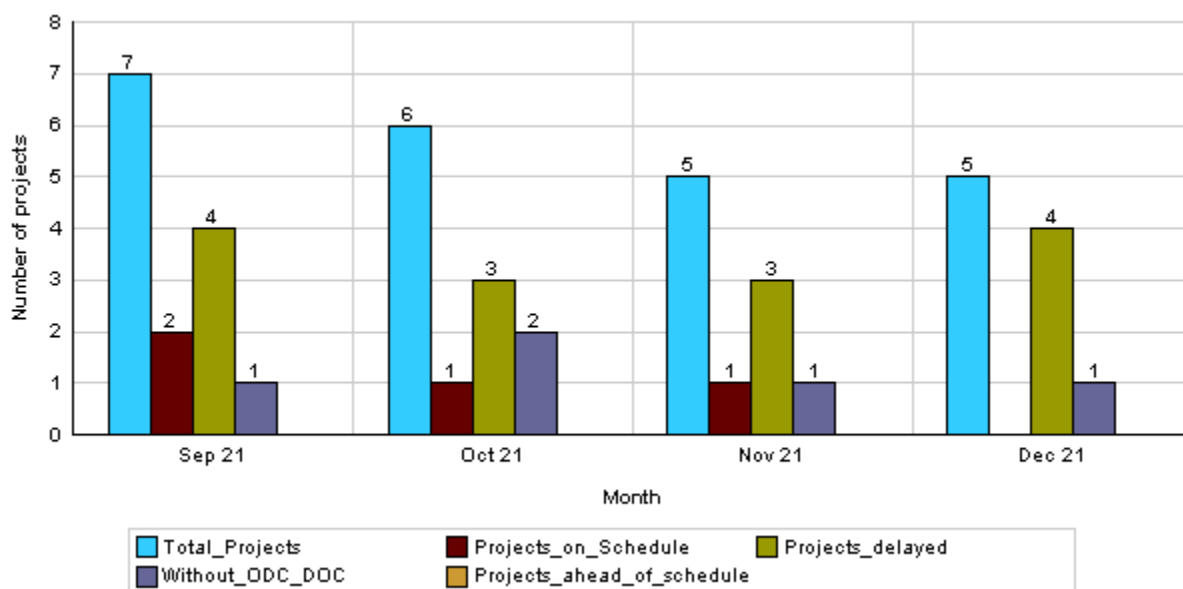


Break-up of 4 Delayed projects in December 2021

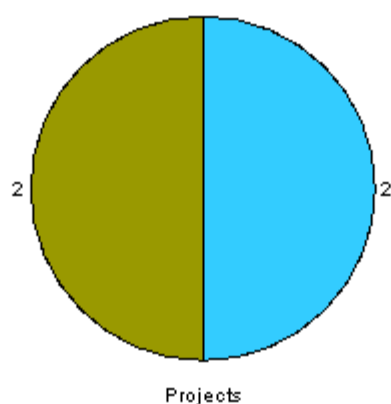


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of DEPARTMENT OF HIGHER EDUCATION Sector

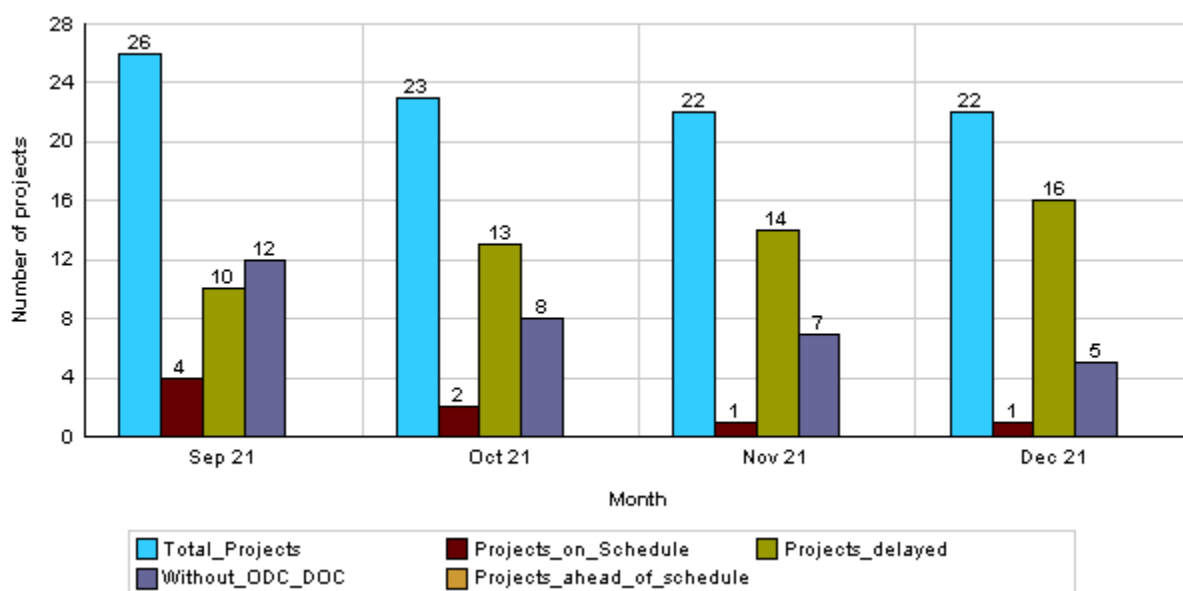


Break-up of 16 Delayed projects in December 2021

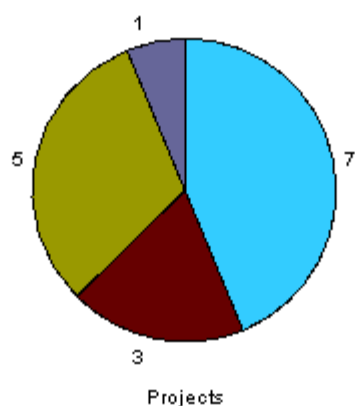


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of WATER RESOURCES Sector

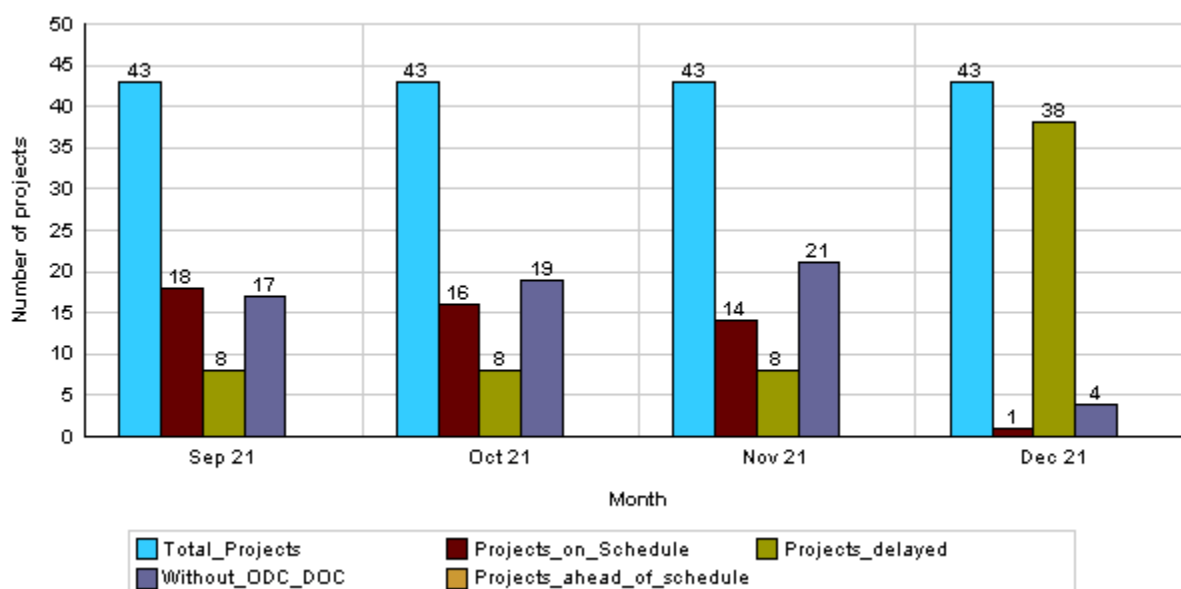


Break-up of 38 Delayed projects in December 2021

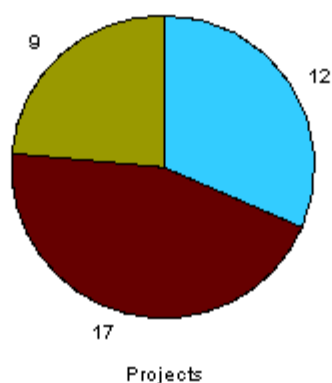


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

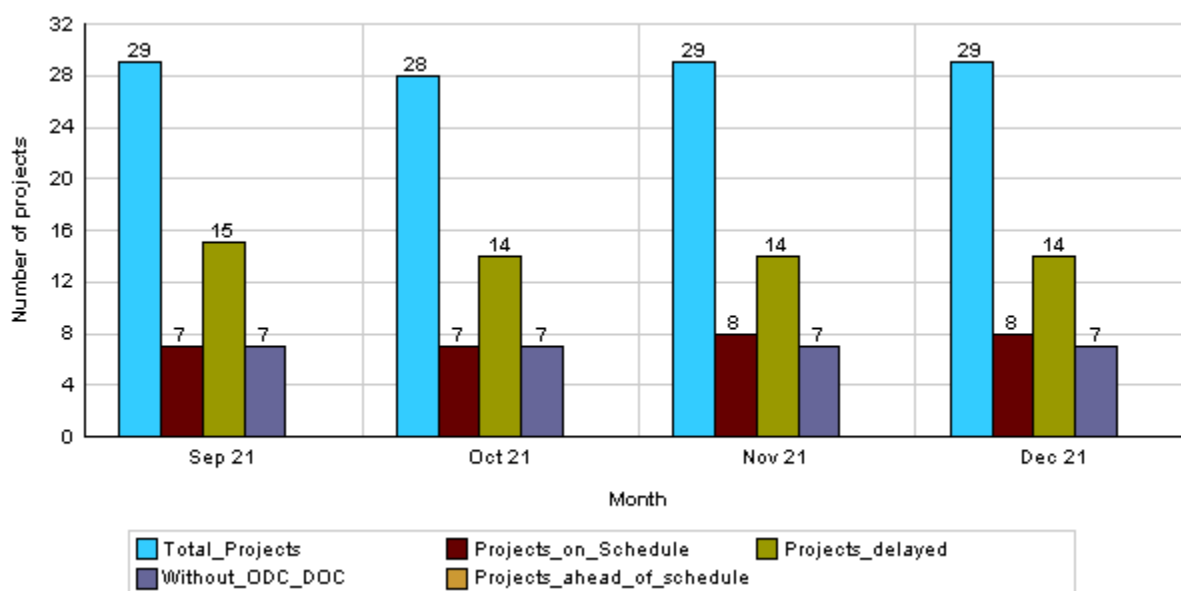


Break-up of 14 Delayed projects in December 2021

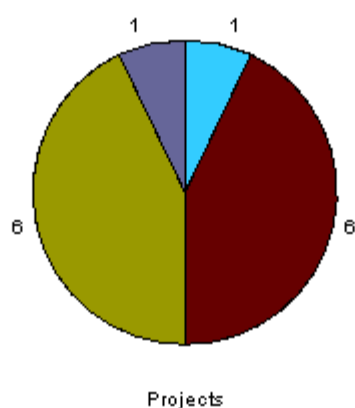


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	6	6	1

Graphical Presentation of TELECOMMUNICATIONS Sector

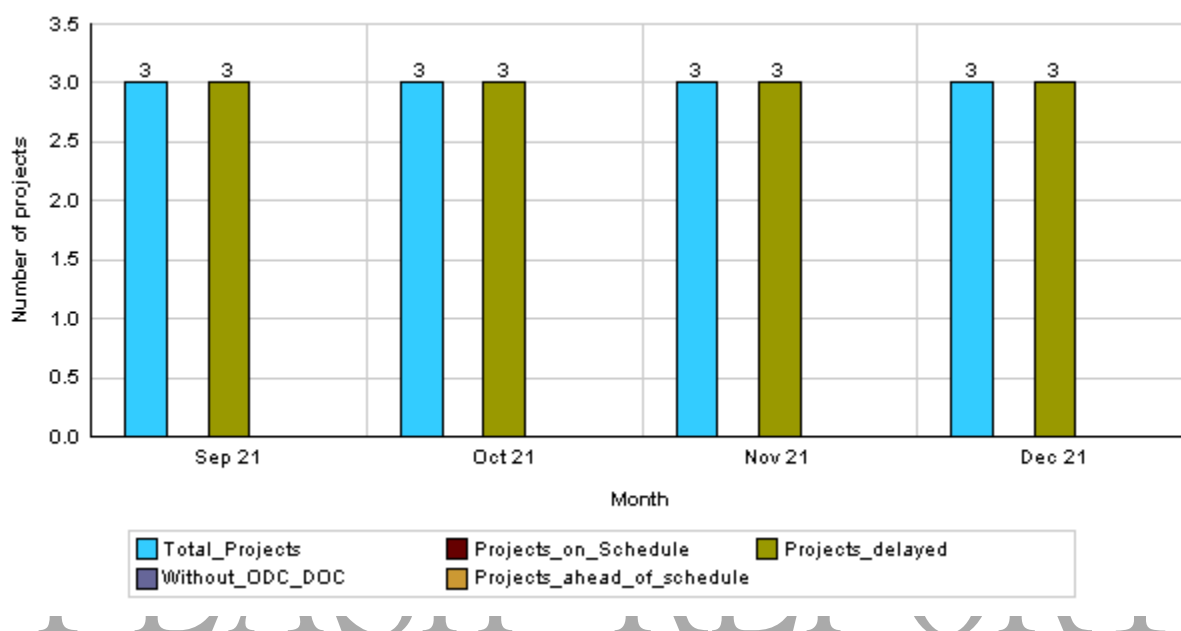

Break-up of 3 Delayed projects in December 2021

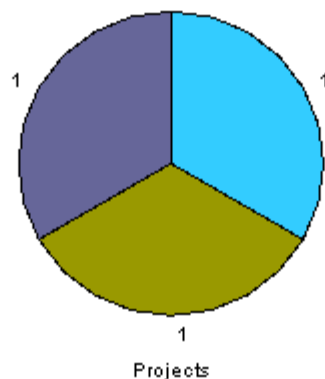


Delay in Months


Legend:

- 1-12 (Blue)
- 13-24 (Dark Red)
- 25-60 (Olive)
- MORE THAN 60 (Purple)

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

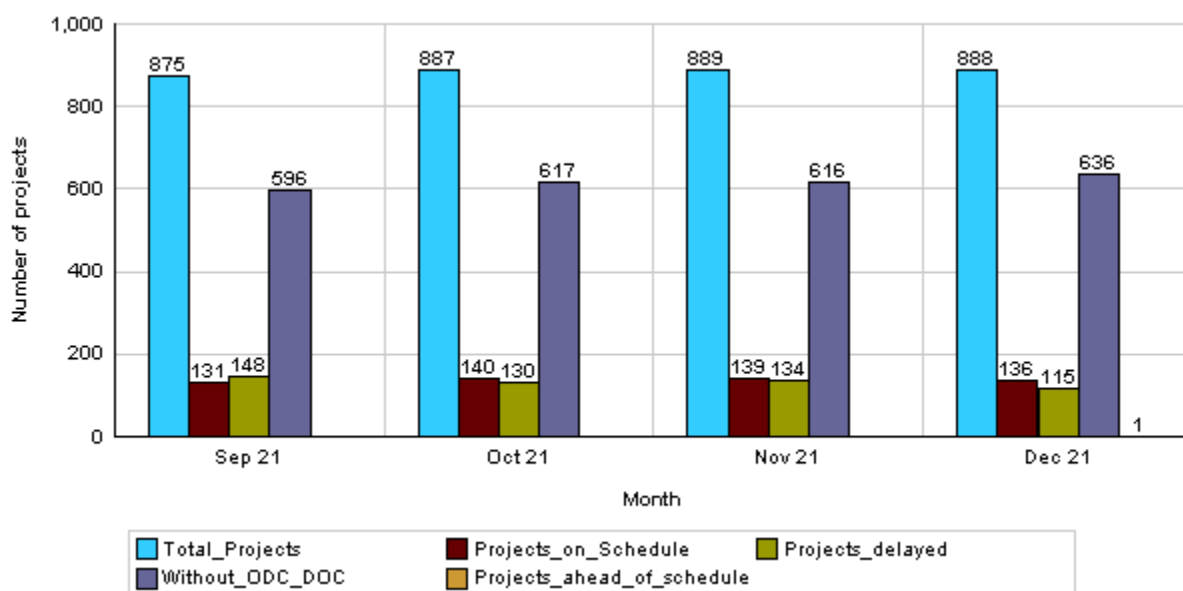


Break-up of 115 Delayed projects in December 2021

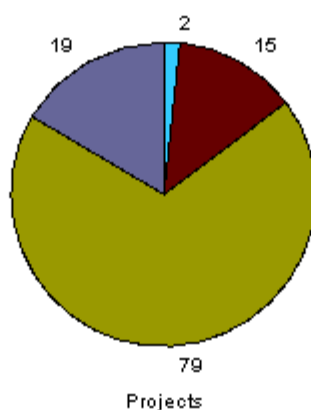


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

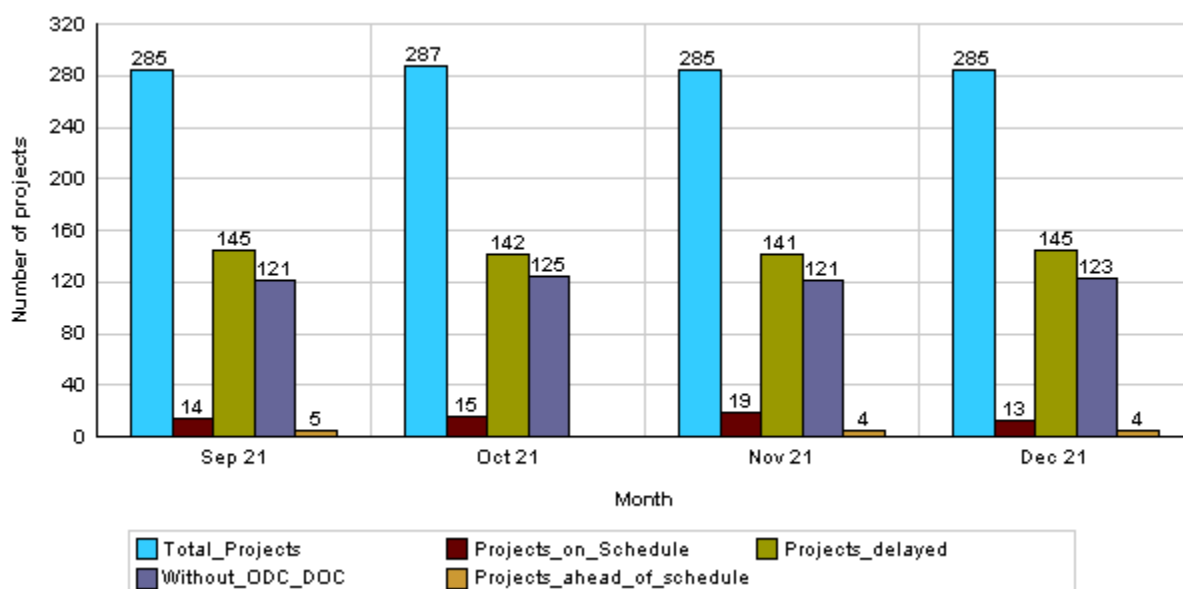


Break-up of 145 Delayed projects in December 2021

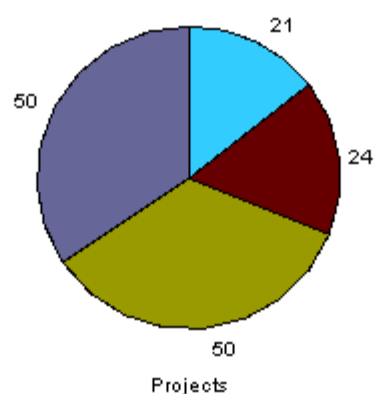


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

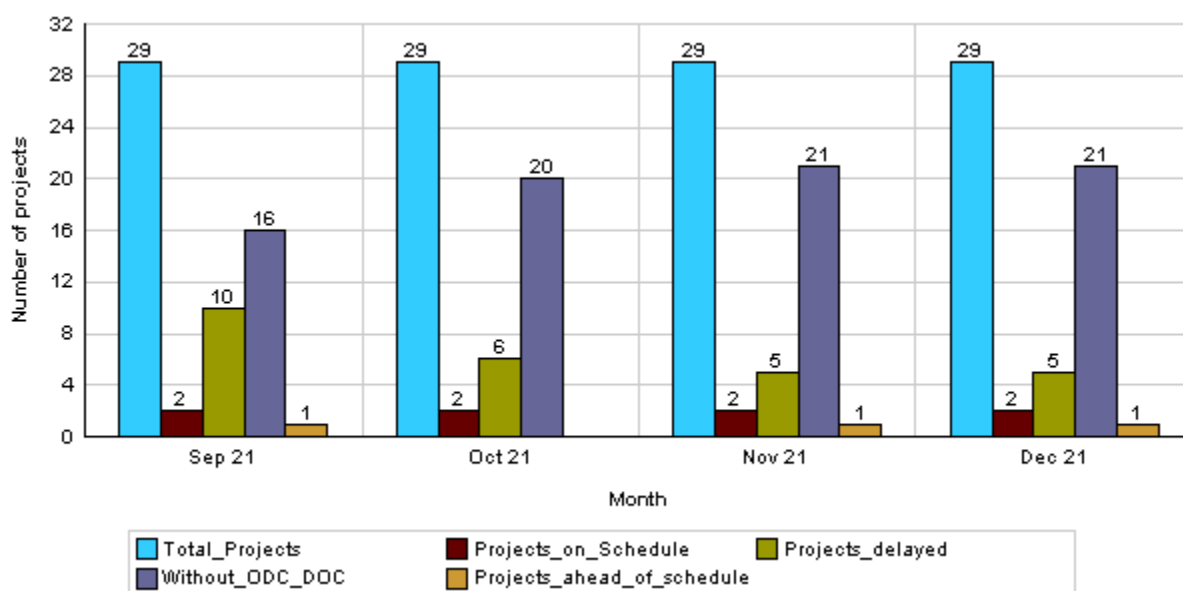


Break-up of 5 Delayed projects in December 2021

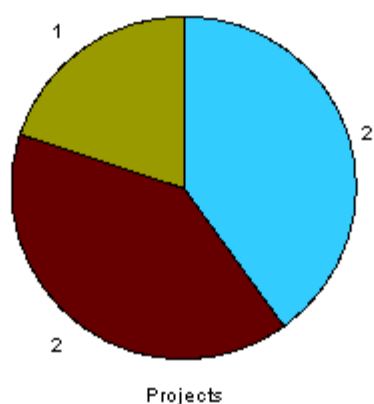


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

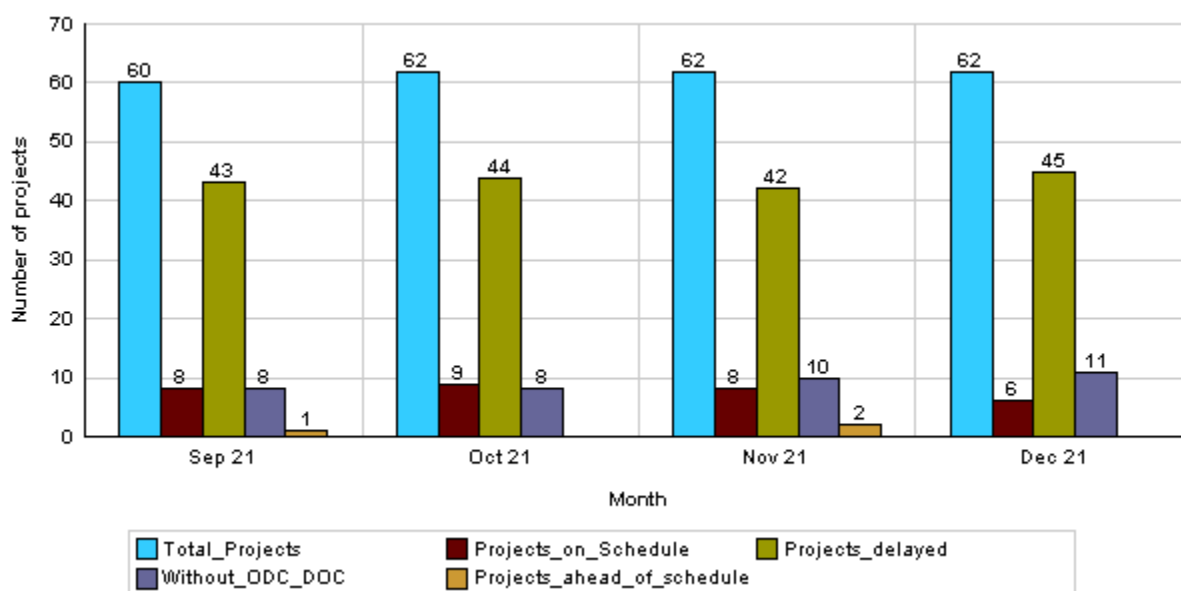


Break-up of 45 Delayed projects in December 2021

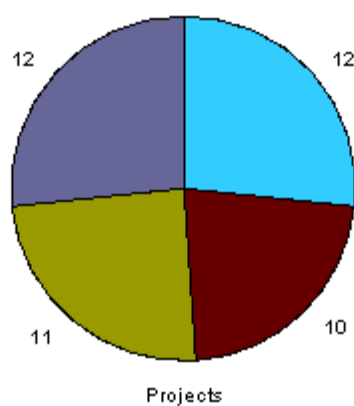


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

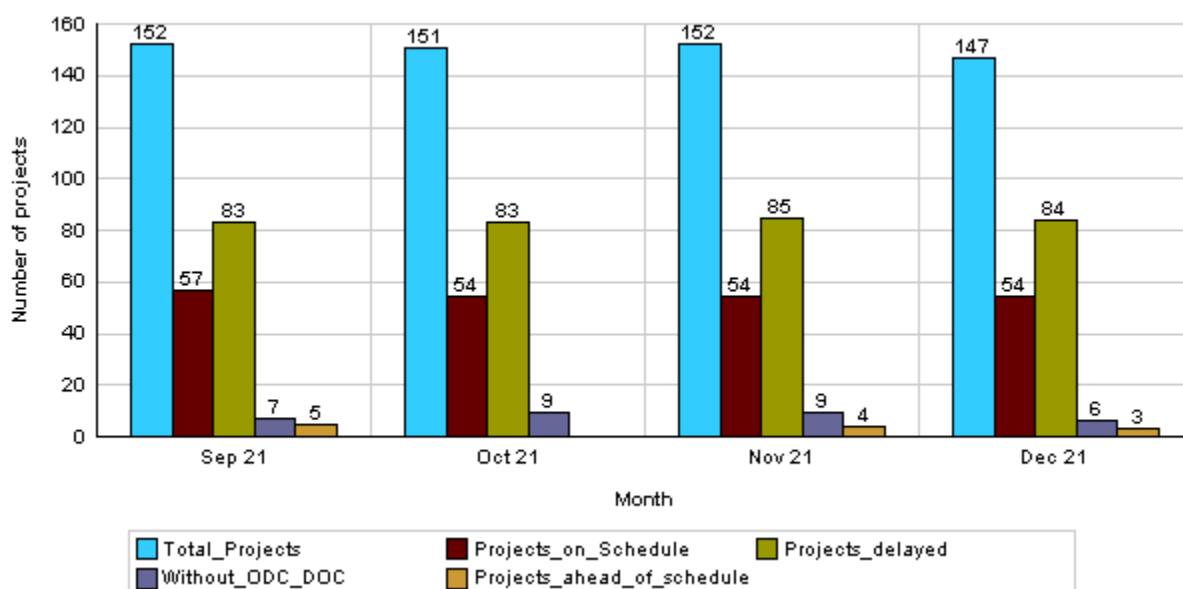


Break-up of 84 Delayed projects in December 2021

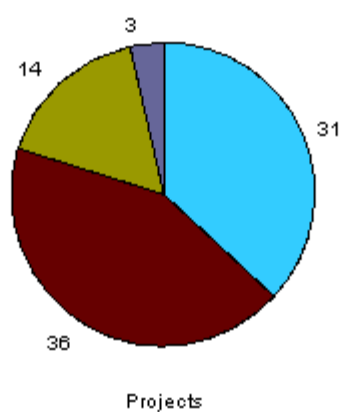


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of STEEL Sector

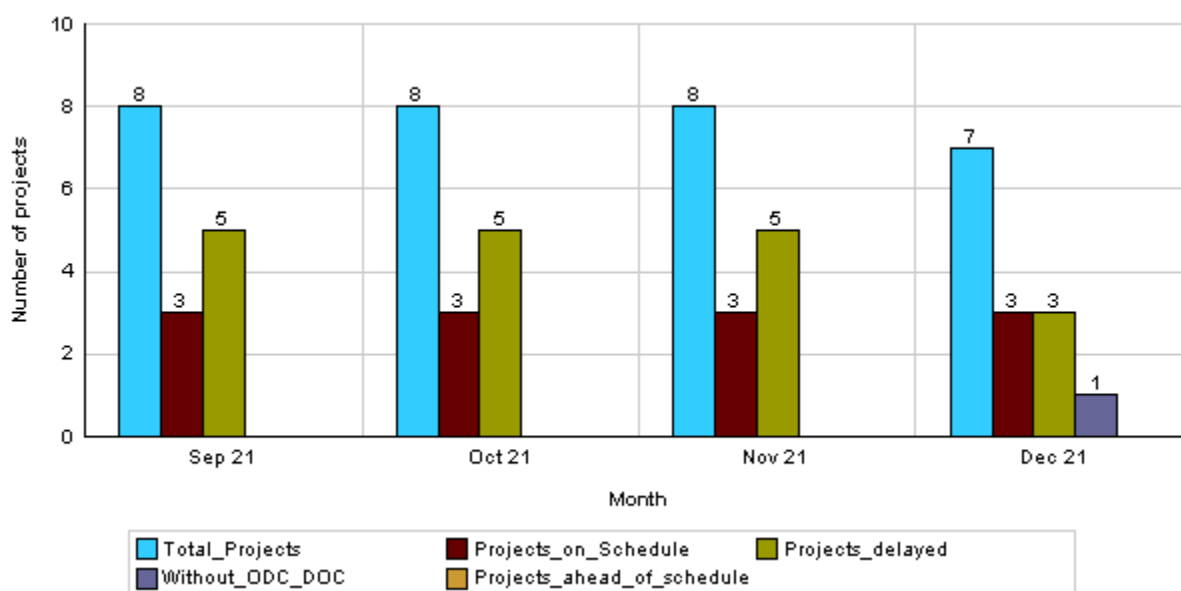


Break-up of 3 Delayed projects in December 2021

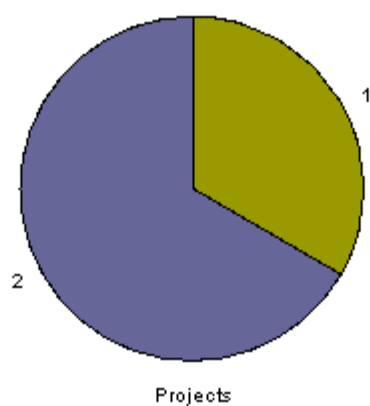

Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of MINES Sector

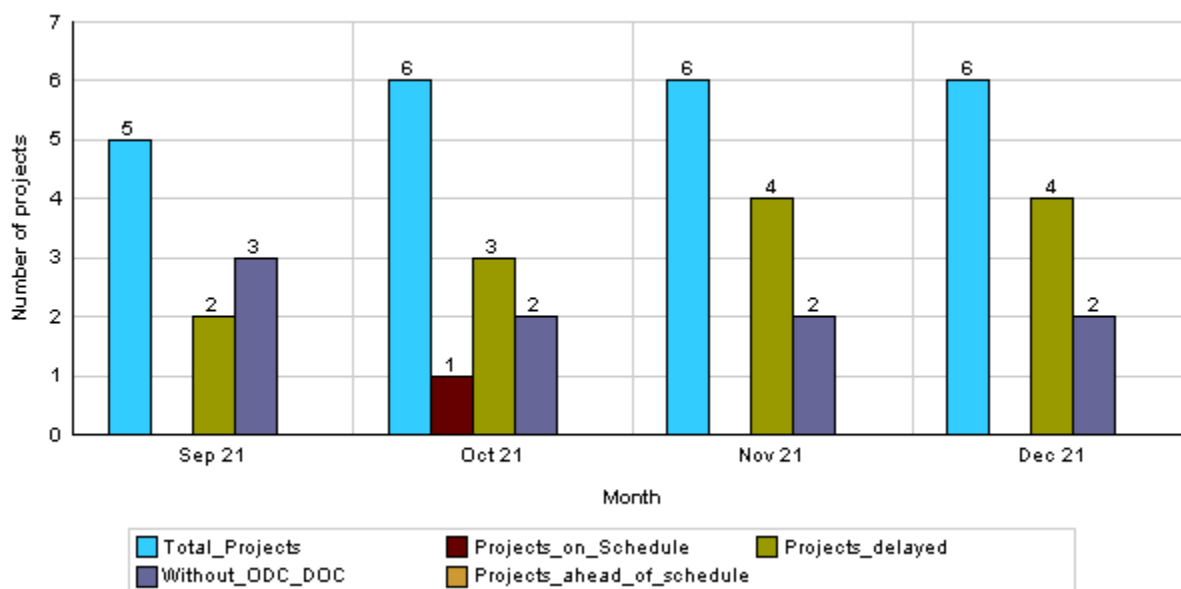


Break-up of 4 Delayed projects in December 2021




Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of COAL Sector

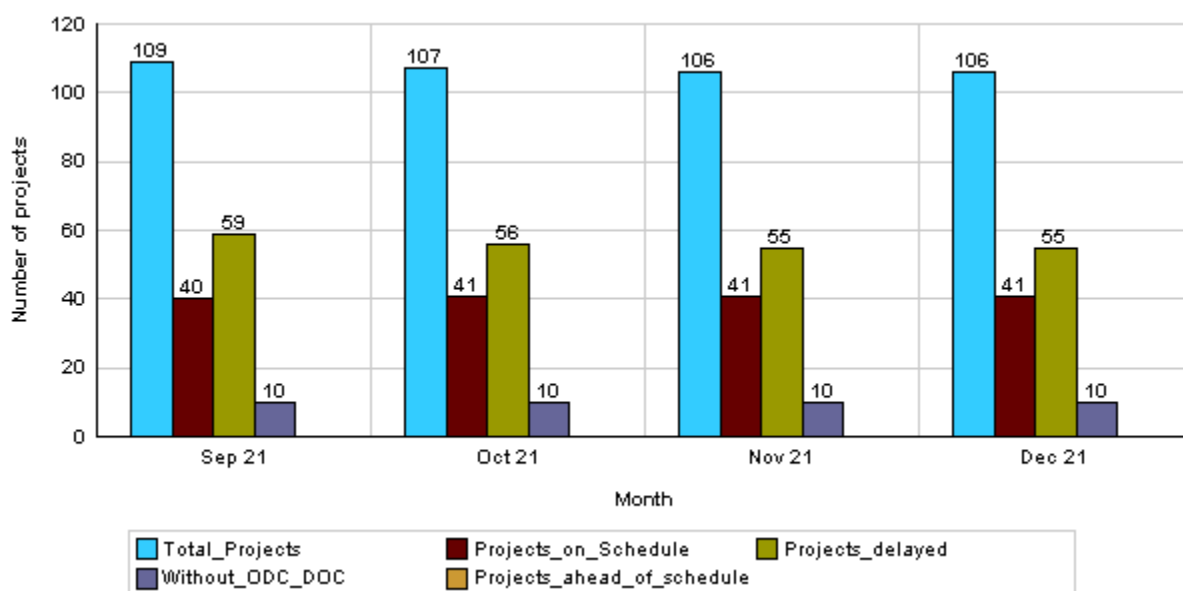


Break-up of 55 Delayed projects in December 2021

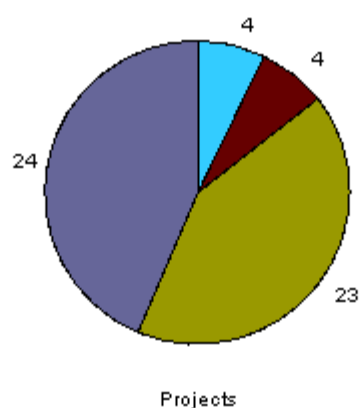

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

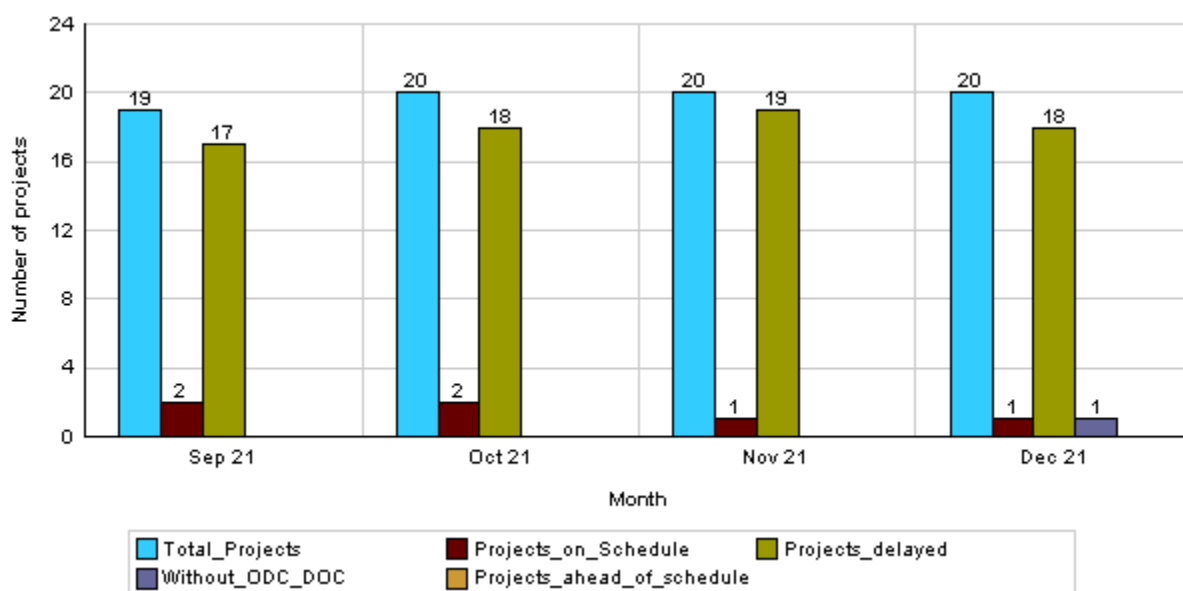


Break-up of 18 Delayed projects in December 2021




Delay in Months

1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

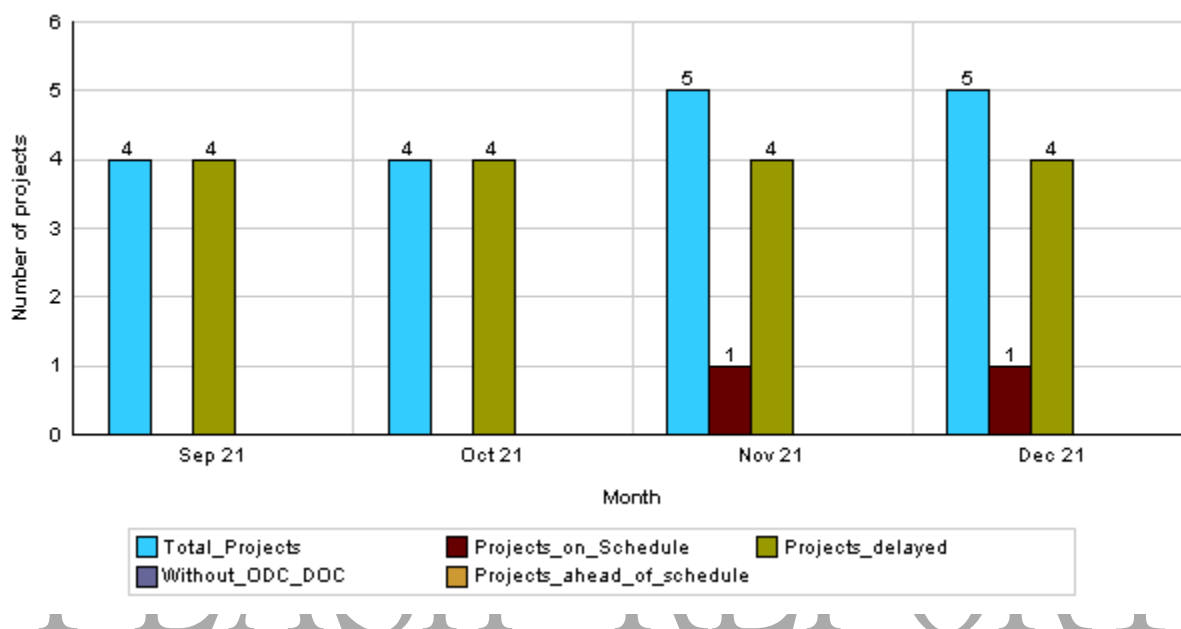

Break-up of 4 Delayed projects in December 2021

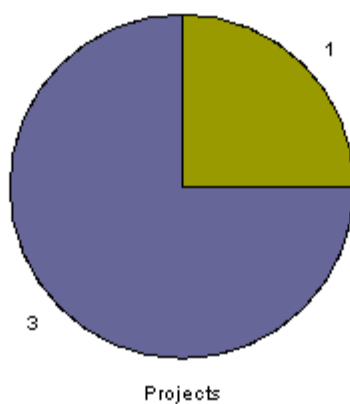

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	1	0
MORE THAN 60	0	0	0	3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	17,427.00	12/2015 -	12/2022	84(O) -	63/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	17,079.00	13,945.00	12/2016 -	12/2023	84(O) -	53/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	6,054.37	09/2010 -	10/2022	145(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	27,505.00	11/2020 -	11/2023	36(O) -	29/76
5	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]NPCIL,TAMIL NADU ,	06/2017	49,621.00 -	49,621.00	5,074.00	09/2027 -	09/2027	0(O) -	0/0
	Total		1,16,741.00 -	1,29,969.00	70,005.37				228/301
	CIVIL AVIATION								
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	417.23 707.73	707.73	494.81	09/2018 06/2022	06/2022	45(O) 0	0/6
7	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10 -	177.10	108.20	02/2020 12/2021	12/2022	34(O) 0	1/4
8	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80 -	611.80	67.47	03/2023 -	03/2023	0(O) -	4/14
9	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH ,	02/2019	645.63 -	645.63	186.02	08/2022 -	11/2022	3(O) -	0/3
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00 -	1,232.00	397.52	03/2021 03/2022	03/2023	24(O) 0	0/1
11	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90 -	1,216.90	249.46	10/2022 -	12/2023	14(O) -	0/3
12	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	303.80 351.21	303.80	203.38	04/2020 -	06/2022	26(O) -	0/0
13	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00 -	1,405.00	396.18	08/2022 -	03/2023	7(O) -	1/15
14	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH ,	07/2018	346.27 -	480.33	140.13	09/2021 12/2022	06/2023	21(O) 6	2/4
15	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24 -	412.24	224.31	06/2021 -	12/2022	18(O) -	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39 -	475.39	184.10	04/2021 -	08/2022	16(O) -	3/10
17	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	763.60	02/2022 -	06/2024	28(O) -	0/12
18	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	513.93	10/2021 -	12/2022	14(O) -	3/14
19	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	16.17	03/2022 12/2023	-	-	3/18
20	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	95.77	05/2022 -	12/2023	19(O) -	0/4
21	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	438.28 -	402.00	397.85	06/2019 12/2021	01/2022	31(O) 1	0/1
22	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 1,938.00	1,938.00	568.01	09/2021 -	12/2023	27(O) -	0/2
23	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	329.56	09/2020 -	09/2022	24(O) -	1/1
24	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	161.87	03/2020 06/2022	04/2022	25(O) 0	0/2
25	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	389.71 -	389.71	216.37	11/2021 04/2023	04/2023	17(O) 3	0/2
	Total		14,431.97 -	15,465.25	5,714.71				18/117
	<u>COAL</u>								
26	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	4,645.12	03/2023 03/2016	03/2023	0(O) 0	15/21
27	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	3,162.39	03/2023 -	03/2023	0(O) -	13/22
28	PELMA OCP(15.00MTY) - [N060000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023	0(O) -	1/12
29	JAGANNATHPOR OCP(3.00MTY) - [N060000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	200.47	03/2015 03/2020	03/2022	84(O) 0	9/11
30	KARTALI (EAST) OCP (2.50 MTY) - [N060000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.95	03/2014 -	03/2026	144(O) -	3/9
31	MANIKPUR OC EXPANSION (3.5 MTY) - [N060000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	232.34	03/2014 -	03/2023	108(O) -	5/6
32	CHHAL OC SEAM -III (6.00 MTY) - [N060000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	169.69	03/2022 -	03/2022	0(O) -	4/11
33	AMERA OC RCE - [N060000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60(O) -	1/7
34	AMGAON OPENCAST PROJECT RCE - [N060000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	149.09	03/2020 -	03/2023	36(O) -	3/6
35	DURGAPUR OPENCAST PROJECT - [N060000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36(O) -	2/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2027	36(O) -	2/6
37	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	76.12	03/2026 -	03/2026	0(O) -	2/2
38	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	46.75	03/2026 -	03/2026	0(O) -	2/4
39	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	3/5
40	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH ,	08/2020	2,309.80 -	2,309.80	322.85	03/2029 -	03/2029	0(O) -	0/0
41	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH ,	05/2020	278.64 -	278.64	187.07	03/2024 -	03/2024	0(O) -	0/0
42	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH ,	12/2020	2,310.12 -	2,310.12	.00	03/2029 -	03/2029	0(O) -	0/0
43	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH ,	12/2020	5,241.40 -	5,241.40	2,031.19	03/2029 -	03/2029	0(O) -	0/0
44	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND ,	08/2008	6,964.33 7,254.37	7,254.37	814.20	07/2012 03/2028	03/2028	188(O) 0	7/7
45	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	124.85	03/2011 -	03/2022	132(O) -	7/7
46	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	500.91	03/2016 -	03/2022	72(O) -	7/7
47	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	93.13	03/2014 -	03/2022	96(O) -	7/7
48	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	89.42	04/2014 -	04/2023	108(O) -	4/7
49	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	508.61	03/2019 -	02/2023	47(O) -	2/6
50	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND ,	02/2012	4,983.58 4,983.58	4,983.58	370.76	03/2020 03/2028	03/2028	96(O) 0	8/8
51	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2023	24(O) -	0/2
52	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	285.81	05/2014 -	03/2022	94(O) -	0/8
53	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	213.80	04/2014 -	04/2020	-	0/10
54	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	260.37	03/2022 -	03/2022	0(O) -	4/22
55	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	165.05	03/2024 -	03/2024	0(O) -	0/17
56	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	778.80	406.92	03/2023 -	03/2023	0(O) -	2/2
57	TETARIAKHAR EXPANSION OCP - [N06000186]CCL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	37.28	03/2023 -	03/2023	0(O) -	1/1
58	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	37.83	08/2022 -	09/2023	13(O) -	5/11
59	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 334.27	334.27	28.43	04/2018 -	10/2022	54(O) -	0/0
60	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	1,186.64	243.93	03/2023 -	03/2026	36(O) -	6/11
61	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2027	48(O) -	3/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	100.68	03/2021 04/2024	04/2024	37(O) 0	4/10
63	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	68.86	03/2021 -	03/2024	36(O) -	5/9
64	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	1.82	03/2022 -	03/2025	36(O) -	1/10
65	AMADAND OPENCASL EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	129.53	03/2021 -	03/2025	48(O) -	4/6
66	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	281.25 -	281.25	23.52	03/2022 03/2026	03/2026	48(O) 0	0/4
67	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	902.52	03/2021 -	03/2022	12(O) -	4/9
68	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	481.57	03/2022 -	03/2023	12(O) -	4/9
69	SEMARIA OPENCASL PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
70	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
71	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	2.65	03/2026 -	03/2026	0(O) -	1/7
72	BLOCK-B EXPANSION OPENCASL PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	1.03	03/2023 -	03/2023	0(O) -	1/7
73	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/8
74	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]SECL,MADHYA PRADESH ,	03/2021	496.28 -	496.28	.00	03/2028 -	03/2028	0(O) -	0/0
75	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA ,	11/2014	1,184.33 -	1,184.33	393.29	03/2020 03/2027	03/2027	84(O) 0	6/13
76	BHANEAGON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	87.35	03/2023 -	03/2023	0(O) -	7/11
77	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 299.67	299.67	213.92	03/2019 03/2022	03/2022	36(O) 0	12/13
78	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 745.03	745.03	423.42	03/2025 -	03/2025	0(O) -	9/13
79	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 333.43	333.43	145.94	03/2023 -	03/2024	12(O) -	5/10
80	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA ,	11/2015	313.34 -	313.34	159.36	03/2021 03/2024	03/2024	36(O) 0	5/6
81	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA ,	11/2015	851.60 826.80	826.80	283.28	03/2020 03/2026	03/2026	72(O) 0	2/6
82	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 327.41	327.41	162.29	03/2019 -	03/2022	36(O) -	6/8
83	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	223.12	03/2021 09/2022	09/2022	18(O) 0	1/4
84	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	107.27	03/2021 09/2022	09/2022	18(O) 0	0/3
85	GHONSA EXPANSION DEEP OC - [N06000205]WCL,MAHARASHTRA ,	03/2021	241.72 -	241.72	57.00	03/2028 -	03/2028	0(O) -	0/7
86	SASTI EXPANSION OC - [N06000206]WCL,MAHARASHTRA ,	08/2020	371.59 -	371.59	52.55	03/2026 -	03/2026	0(O) -	1/7

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	DHUPTALA OC(SASTI UG TO OC) - [N06000209]WCL,MAHARASHTRA ,	02/2019	720.87 -	720.87	84.05	03/2028 -	03/2028	0(O) -	0/6
88	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 404.45	404.45	248.72	03/2022 -	03/2022	0(O) -	0/3
89	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	289.29 -	289.30	37.55	03/2022 03/2025	03/2025	36(O) 0	2/12
90	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	298.78	03/2021 09/2023	09/2023	30(O) 0	5/6
91	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
92	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	3,145.45 -	3,145.45	661.05	03/2017 -	03/2031	168(O) -	12/12
93	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY) - [N06000035]MCL,ODISHA ,	12/2007	8,416.19 8,416.19	8,416.19	1,166.07	03/2013 03/2028	03/2028	180(O) 0	8/10
94	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY) - [N06000044]MCL,ODISHA ,	12/2007	3,504.21 3,504.21	3,504.21	606.54	03/2010 03/2029	03/2029	228(O) 0	3/5
95	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	206.89	03/2012 -	-	-	5/7
96	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	808.97	808.97	03/2013 -	03/2024	132(O) -	6/9
97	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	254.06	03/2019 -	03/2024	60(O) -	3/9
98	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	2,697.74	03/2026 -	03/2026	0(O) -	9/15
99	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	683.47	03/2021 -	09/2025	54(O) -	9/10
100	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	773.61	03/2027 -	03/2027	0(O) -	3/12
101	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,318.06	03/2029 -	03/2029	0(O) -	1/9
102	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	918.03	07/2020 -	04/2020	-	19/22
103	NAINI COAL MINE - [N06000203]SCCL,ODISHA ,	03/2020	494.30 -	494.30	111.78	03/2024 -	03/2024	0(O) -	1/7
104	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
105	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
106	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	93.05	09/2020 -	-	-	0/0
107	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	143.95	09/2020 -	-	-	0/0
108	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,980.79	7,980.79	7,421.14	12/2015 -	02/2021	-	35/35
109	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	496.19	06/2015 03/2025	03/2025	117(O) 0	5/7
110	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132(O) -	1/2
111	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84(O) -	4/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	306.52	03/2015 -	03/2022	84(O) -	16/29
113	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	204.84	03/2015 -	03/2023	96(O) -	10/13
114	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	144.15	07/2016 -	03/2022	68(O) -	26/28
115	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	213.44	03/2016 -	09/2021	-	38/39
116	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	123.72	03/2019 -	03/2022	36(O) -	17/18
117	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	256.54	03/2019 -	03/2022	36(O) -	6/11
118	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	-	03/2022	-	2/6
119	GODAVARIKHANI COAL MINE - [N06000202]SCCL,TELANGANA ,	07/2019	438.98 -	438.98	88.95	03/2023 -	03/2023	0(O) -	1/11
120	VENKATESH KHANI COAL MINE - [N06000204]SCCL,TELANGANA ,	10/2020	484.51 -	484.51	25.43	03/2023 -	03/2023	0(O) -	0/8
121	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NCL,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	12,939.55	11/2021 11/2022	11/2022	12(O) 0	18/48
122	KHADIA EXPANSION OCP - [N06000208]NCL,UTTAR PRADESH ,	06/2021	491.67 -	491.67	.00	03/2025 -	03/2025	0(O) -	0/5
123	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY - [N06000020]ECL,WEST BENGAL ,	11/2015	1,210.12 -	1,210.12	49.12	03/2029 03/2029	03/2029	0(O) 0	9/13
124	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	714.63	03/2018 -	03/2029	132(O) -	12/16
125	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	625.36	08/2019 -	08/2024	60(O) -	1/19
126	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	1.75	03/2026 -	03/2026	0(O) -	4/22
127	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	22.79	03/2029 -	03/2029	0(O) -	2/22
128	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	3.78	03/2027 -	03/2027	0(O) -	2/27
129	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.18	03/2027 -	03/2027	0(O) -	0/22
130	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	7.95	03/2025 -	03/2025	0(O) -	0/0
131	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 341.22	341.22	79.48	03/2017 -	10/2022	67(O) -	0/0
	Total		1,49,328.98 -	1,53,992.98	55,306.02				502/1035
	<u>FINANCE</u>								
132	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU ,	12/2015	209.00 -	208.96	208.93	10/2019 -	07/2021	-	1/6
133	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU ,	11/2017	348.77 -	348.77	204.00	11/2021 -	11/2021	-	3/8

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		557.77 -	557.73	412.93				4/14
	<u>FERTILISERS</u>								
134	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	184.57	11/2019 06/2021	12/2021	25(O) 2	0/2
135	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	324.01	04/2020 01/2022	01/2022	21(O) 1	14/14
136	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	200.30	11/2019 05/2021	-	-	1/2
137	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	205.94	11/2019 05/2021	-	-	1/2
	Total		1,101.28 -	1,101.28	914.82				16/20
	<u>MINES</u>								
138	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	5,540.00	1,182.87	04/2021 01/2024	01/2024	33(O) 0	4/4
139	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	394.68	01/2020 -	-	-	3/3
140	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	95.45	11/2020 -	12/2023	37(O) -	3/3
141	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	10.40	04/2021 12/2023	12/2023	32(O) 0	2/2
142	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2022	12/2020	-	1/1
143	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART DG GSI AT SECTOR-V SA - [N10000015]CPWD,WEST BENGAL , EPC	04/2019	255.37 255.37	255.37	.86	04/2022 12/2024	12/2024	32(O) 32	0/1
	Total		7,333.99 -	7,330.54	1,819.26				13/14
	<u>STEEL</u>								
144	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 21,940.00	21,940.00	19,538.23	05/2015 01/2022	03/2022	82(O) 2	74/86
145	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH ,	11/2020	542.24 -	542.24	81.14	12/2023 -	12/2023	0(O) -	0/0
146	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH , Central Sector Projects	11/2015	2,907.00 -	2,907.00	547.05	06/2023 -	06/2023	0(O) -	2/8
147	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	566.58	10/2017 12/2021	11/2022	61(O) 0	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
148	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	209.03	06/2019 12/2021	02/2022	32(O) 0	1/1
149	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	51.69	05/2023 -	05/2023	0(O) -	0/1
150	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	2,100.00	1,767.98	09/2018 09/2021	09/2021	-	5/5
	Total		22,331.15 -	29,163.30	22,761.70				82/103
	<u>PETROLEUM</u>								
151	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	17,704.50	07/2020 07/2022	07/2022	24(O) 0	95/111
152	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	25,090.00	15,071.32	06/2020 06/2022	06/2022	24(O) 0	15/20
153	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	301.65	04/2021 12/2021	09/2022	17(O) 6	0/0
154	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	128.30	04/2022 -	02/2023	10(O) -	0/0
155	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	142.62	10/2021 03/2022	03/2022	5(O) 0	0/0
156	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	260.89	02/2021 -	03/2023	25(O) -	0/16
157	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	105.40	07/2020 -	01/2022	18(O) -	1/5
158	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	16.06	07/2022 -	01/2023	6(O) -	0/0
159	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH , EPC	10/2020	332.61 -	332.61	30.88	11/2022 -	11/2022	0(O) -	0/0
160	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH , EPC	10/2020	303.40 -	303.40	224.20	03/2021 -	12/2021	9(O) -	0/0
161	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH , EPC	10/2020	210.94 -	210.94	128.96	08/2021 -	03/2022	7(O) -	0/0
162	CGD PROJECT AT SRIKAKULAM VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH ,	06/2019	2,880.00 -	2,880.00	113.40	08/2027 -	08/2027	0(O) -	0/0
163	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]HPCL,ANDHRA PRADESH , EPC	09/2021	160.00 -	160.00	.00	06/2024 -	06/2024	0(O) -	1/12
164	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 652.10	638.60	399.74	02/2020 -	12/2021	22(O) -	1/14
165	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	559.57	02/2020 06/2021	11/2021	-	5/5
166	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 222.21	198.00	184.60	08/2020 09/2021	12/2021	16(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
167	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM ,	01/2019	12,366.00 18,968.00	18,968.00	767.97	10/2024 -	10/2024	0(O) -	0/0
168	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 9,058.00	9,058.00	959.30	10/2024 -	10/2024	0(O) -	0/0
169	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]IOCL,ASSAM ,	05/2021	412.00 -	412.00	26.64	10/2023 -	10/2023	0(O) -	0/0
170	GAS ASSISTED GRAVITY DRAINAGE SCHEME KASOMARIGAON - [N16000433]ONGC,ASSAM , EPC	08/2021	218.38 -	218.38	.00	02/2023 -	02/2023	0(O) -	0/0
171	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	167.51	03/2021 09/2021	03/2022	12(O) 2	21/26
172	DEVLOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	90.83	10/2020 08/2022	08/2022	22(O) 0	2/2
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	197.09	10/2022 -	10/2022	0(O) -	10/10
174	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	178.65	01/2021 06/2021	01/2022	12(O) 0	7/8
175	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	399.21	03/2021 12/2021	03/2022	12(O) 3	0/0
176	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	2,089.45	04/2023 -	04/2023	0(O) -	2/2
177	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR ,	06/2020	403.00 -	403.00	111.34	08/2022 -	08/2022	0(O) -	0/0
178	CGD PROJECT AT AURANGABAD KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR ,	10/2018	176.00 -	176.00	79.72	08/2027 -	08/2027	0(O) -	0/0
179	CGD PROJECT AT ARARIA PURNIA KATI HAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR ,	06/2019	988.00 -	988.00	45.10	12/2029 -	12/2029	0(O) -	0/0
180	CGD PROJECT AT ARWAL JEHANABAD BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR ,	06/2019	439.00 -	439.00	127.63	02/2028 -	02/2028	0(O) -	0/0
181	CGD PROJECT AT KHAGARIA SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR ,	06/2019	163.00 -	163.00	26.31	12/2029 -	12/2029	0(O) -	0/0
182	CGD PROJECT AT LAKHISARAI MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR ,	06/2019	347.00 -	347.00	105.90	02/2028 -	02/2028	0(O) -	0/0
183	CGD PROJECT AT MUZAFFARPUR VAISHALI SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR ,	06/2019	2,996.00 -	2,996.00	309.12	02/2028 -	02/2028	0(O) -	0/0
184	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]HPCL,CHHATISGARH , EPC	03/2021	456.00 -	456.00	13.36	03/2024 -	03/2024	0(O) -	6/64
185	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	198.90	04/2018 -	06/2022	50(O) -	19/20
186	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	970.30	947.93	03/2026 -	03/2026	0(O) -	9/10
187	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	360.74	02/2020 10/2021	03/2022	25(O) 0	7/8
188	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 730.20	730.20	206.83	- 05/2023	05/2023	- 0	12/17

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 247.90	247.90	75.63	02/2021 -	10/2022	20(O) -	6/8
190	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	206.62	04/2022 -	04/2022	0(O) -	10/11
191	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	687.88	05/2023 -	05/2023	0(O) -	6/11
192	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	182.84	12/2022 -	12/2022	0(O) -	0/0
193	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT ,	02/2020	444.87 -	444.87	141.98	08/2022 -	08/2022	0(O) -	5/6
194	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT , Central Sector Projects	09/2020	18,936.00 -	18,936.00	829.33	09/2024 -	08/2024	-1(O) -	0/0
195	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT ,	10/2020	1,614.00 -	1,614.00	1.12	08/2023 -	08/2023	0(O) -	0/0
196	REDEVELOPMENT OF LINCH FIELD - [N16000428]ONGC,GUJARAT , EPC	04/2021	631.03 -	631.03	227.33	03/2025 -	03/2025	0(O) -	0/2
197	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]ONGC,GUJARAT , EPC	08/2021	885.63 -	885.63	183.01	02/2026 -	02/2026	0(O) -	0/2
198	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 340.76	340.76	164.11	02/2020 07/2022	07/2022	29(O) 0	6/7
199	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	954.75	08/2020 04/2022	04/2022	20(O) 0	6/7
200	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	504.26	01/2021 03/2022	03/2022	14(O) 0	3/6
201	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	470.06	02/2020 02/2022	02/2022	24(O) 0	4/5
202	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.01	327.01	234.40	08/2020 12/2021	03/2022	19(O) 2	14/16
203	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	101.96	06/2021 07/2022	07/2022	13(O) 0	3/3
204	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 3,199.60	2,281.94	673.16	12/2022 07/2023	07/2023	7(O) 0	0/0
205	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	373.81	12/2021 01/2023	01/2023	13(O) 0	0/0
206	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	30.12	07/2021 03/2022	03/2022	8(O) 0	0/0
207	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	193.31	09/2026 02/2027	02/2027	5(O) 0	38/52
208	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]IOCL,HARYANA ,	02/2021	34,627.00 -	34,627.00	505.01	09/2024 -	09/2024	0(O) -	0/0
209	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	773.03	03/2023 03/2022	03/2022	-12(O) 0	9/10
210	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	127.30	06/2020 -	03/2022	21(O) -	6/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
211	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	149.60	10/2022 -	10/2022	0(O) -	19/19
212	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	142.91	06/2022 -	09/2022	3(O) -	0/0
213	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	111.42	10/2022 -	10/2022	0(O) -	9/9
214	CGD PROJECT AT BOKARO HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND ,	10/2018	613.00 -	613.00	161.96	12/2029 -	12/2029	0(O) -	0/0
215	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,789.68	12/2019 04/2021	03/2022	27(O) 1	10/12
216	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 637.00	637.00	543.02	03/2020 11/2020	12/2021	21(O) 0	3/3
217	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	163.25	03/2021 -	12/2021	9(O) -	0/15
218	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	1,461.90	06/2022 -	06/2022	0(O) -	13/18
219	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	175.31	12/2022 -	12/2022	0(O) -	15/19
220	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	339.20	11/2021 03/2022	03/2022	4(O) 0	16/19
221	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 304.00	304.00	2.58	06/2023 01/2024	01/2024	7(O) 0	3/6
222	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 1,236.00	1,236.00	553.03	10/2017 03/2022	09/2022	59(O) 0	44/52
223	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	793.01	06/2019 -	02/2022	32(O) -	0/0
224	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023	0(O) -	0/0
225	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 319.61	319.61	226.65	06/2020 12/2021	12/2021	18(O) 0	0/0
226	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH ,	10/2018	177.00 -	177.00	66.77	02/2027 -	02/2027	0(O) -	0/0
227	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,846.46	2,001.34	1,604.42	05/2013 05/2022	05/2022	108(O) 0	5/8
228	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,888.99	04/2018 05/2022	05/2022	49(O) 0	13/15
229	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,605.89	02/2022 -	02/2022	0(O) -	5/5
230	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 437.00	437.00	209.30	01/2021 -	08/2022	19(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
231	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,475.92	3,596.00	3,526.55	05/2021 05/2021	05/2021	-	15/15
232	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	194.72	06/2020 -	03/2022	21(O) -	5/12
233	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,203.71	2,222.54	05/2021 12/2021	12/2021	7(O) 0	5/6
234	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	1,640.35	03/2022 05/2023	05/2023	14(O) 0	4/6
235	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	3,119.98	05/2021 01/2022	01/2022	8(O) 0	4/6
236	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	06/2019	2,494.68 -	2,354.72	1,800.96	03/2022 -	03/2022	0(O) -	4/6
237	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	733.86	829.58	12/2020 05/2021	02/2022	14(O) 2	4/5
238	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA ,	07/2020	640.00 -	640.00	368.06	12/2021 -	06/2022	6(O) -	0/0
239	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA ,	08/2020	697.00 -	697.00	299.02	03/2023 -	03/2023	0(O) -	0/0
240	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]GAIL,MAHARASHTRA ,	05/2019	8,797.00 -	8,797.00	178.78	04/2025 -	04/2025	0(O) -	12/20
241	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	2,225.58	03/2021 12/2021	03/2022	12(O) 0	5/5
242	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	3,124.58	12/2020 03/2022	03/2022	15(O) 0	5/5
243	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	606.58	07/2018 05/2021	03/2022	44(O) 0	27/36
244	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	283.17	10/2020 -	03/2022	17(O) -	6/12
245	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	510.00	486.90	12/2019 -	12/2021	24(O) -	6/22
246	LAYING OF VIJAIPIUR-AURAIYA PIPELINE SECTION OF VIJAIPIUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,653.50	12/2020 -	01/2022	13(O) -	22/24
247	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	2,213.00	12/2020 12/2021	03/2022	15(O) 2	21/24
248	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 3,048.00	3,048.00	2,230.20	12/2020 12/2021	03/2022	15(O) 0	21/24
249	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,778.50	12/2012 02/2022	08/2024	140(O) 30	26/42

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
250	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VV SPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	3,072.00	2,673.55	06/2021 08/2022	07/2022	13(O) 0	18/26
251	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 3,060.00	3,060.00	2,705.00	12/2021 -	06/2023	18(O) -	17/20
252	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	438.32	11/2022 -	11/2022	0(O) -	14/20
253	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	553.20	07/2022 -	07/2022	0(O) -	11/14
254	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	355.80	11/2022 -	11/2022	0(O) -	9/12
255	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	1,789.70	05/2023 -	05/2023	0(O) -	14/29
256	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE ,	06/2019	169.00 -	169.00	40.12	12/2029 -	12/2029	0(O) -	0/0
257	CGD PROJECT AT SHEIKHPURA JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE ,	06/2019	303.00 -	303.00	130.22	02/2028 -	02/2028	0(O) -	0/0
258	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,584.90	12/2020 12/2021	03/2022	15(O) 0	20/24
259	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	64.47	12/2019 03/2022	10/2022	34(O) 0	18/26
260	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	166.06	07/2022 -	07/2022	0(O) -	10/10
261	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	228.42	12/2021 08/2021	01/2022	1(O) 0	3/3
262	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	99.81	07/2022 -	07/2022	0(O) -	9/9
263	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	3,566.10	10/2021 07/2022	07/2022	9(O) 0	9/10
264	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	883.78	10/2021 -	03/2022	5(O) -	1/1
265	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	140.65	09/2021 06/2022	06/2022	9(O) 0	4/5
266	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	2,099.36	08/2021 09/2022	09/2022	13(O) 0	7/11
267	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 427.00	427.00	35.56	09/2022 03/2023	03/2023	6(O) 0	4/8
268	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	08/2019	1,607.00 -	1,607.00	304.87	08/2022 -	06/2023	10(O) -	0/21
269	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	61.04	07/2022 -	07/2022	0(O) -	0/0
270	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	579.94	01/2024 -	01/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
271	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL,PUNJAB ,	05/2020	1,421.46 -	1,421.46	229.78	02/2023 -	02/2023	0(O) -	11/22
272	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	96.11	- 05/2022	12/2022	- 0	17/26
273	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
274	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66(O) 0	0/0
275	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	624.35	455.96	03/2019 09/2021	09/2021	-	4/5
276	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	4,159.59	12/2018 02/2022	02/2022	38(O) 0	5/5
277	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	160.74	11/2021 -	12/2021	1(O) -	5/5
278	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	315.00	295.84	08/2020 -	12/2021	16(O) -	0/0
279	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	279.29	10/2020 01/2022	03/2022	17(O) 2	0/0
280	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL,TAMIL NADU ,	10/2020	921.00 -	921.00	5.59	09/2023 -	02/2024	5(O) -	0/0
281	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU , EPC	10/2020	1,398.00 -	1,398.00	134.42	12/2023 -	01/2024	1(O) -	0/0
282	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU ,	10/2018	2,998.00 -	2,998.00	202.71	03/2030 -	03/2030	0(O) -	0/0
283	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU ,	10/2018	1,304.00 -	1,304.00	42.90	03/2030 -	03/2030	0(O) -	0/0
284	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	109.24	04/2022 -	08/2023	16(O) -	0/0
285	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 345.15	345.15	255.92	04/2022 -	04/2022	0(O) -	44/53
286	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	179.06	08/2021 -	11/2022	15(O) -	0/0
287	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	136.20	08/2020 03/2022	03/2022	19(O) 0	1/1
288	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	516.61	08/2022 -	08/2022	0(O) -	3/3
289	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	515.69	03/2029 08/2029	08/2029	5(O) 0	28/64
290	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 217.92	217.92	105.90	04/2021 03/2022	03/2022	11(O) 0	12/14

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
291	60 KTA POLYPROPYLENE PROJECT - [N16000429]GAIL,UTTAR PRADESH ,	03/2019	910.56 -	910.56	117.31	04/2024 -	04/2024	0(O) -	10/17
292	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	105.42	02/2020 06/2021	06/2022	28(O) 0	19/26
293	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	1,008.20	12/2020 12/2021	06/2023	30(O) 6	13/24
294	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 207.36	207.36	129.75	04/2020 10/2021	07/2022	27(O) 0	19/26
295	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	2,360.01	09/2022 03/2022	03/2022	-6(O) 0	3/3
296	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	146.12	03/2031 08/2031	08/2031	5(O) 0	24/50
297	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	132.46	01/2023 -	01/2023	0(O) -	2/6
	Total		3,39,274.49 -	3,50,723.52	1,25,031.63				1064/1577
	POWER								
298	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	14,738.05	09/2010 08/2023	08/2023	155(O) 0	0/0
299	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	19,466.00	10/2011 07/2023	07/2023	141(O) 0	34/48
300	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 10,566.00	10,566.00	9,014.00	07/2012 06/2020	11/2021	-	25/25
301	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	16,604.00	05/2018 -	03/2022	46(O) -	43/45
302	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	4,611.25	01/2024 -	01/2024	0(O) -	16/27
303	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,395.48	11/2019 -	-	-	0/0
304	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	578.99	05/2017 12/2021	04/2022	59(O) 1	4/9
305	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT , EPC	08/2020	261.80 -	293.03	130.88	10/2021 10/2022	10/2022	12(O) 0	0/0
306	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT , EPC	01/2021	842.27 -	842.27	92.08	07/2022 -	08/2022	1(O) -	0/0
307	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI MESANKA AND RADHANPUR) - [N18000296]NTPC,GUJARAT , EPC	05/2021	674.92 -	674.92	76.91	09/2022 -	09/2022	0(O) -	0/0
308	SHIYAL SOLAR POWER PROJECT - [N18000297]SJVN,GUJARAT ,	05/2021	296.20 -	296.20	.21	10/2022 -	10/2022	0(O) -	0/5
309	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	9,357.83	09/2009 03/2023	03/2023	162(O) 0	5/5
310	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	585.06	01/2026 -	01/2026	0(O) -	0/0
311	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]SJVN,HIMACHAL PRADESH ,	10/2020	687.97 -	687.97	207.51	11/2025 -	11/2025	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
312	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	2,056.81	04/2020 07/2025	07/2025	63(O) 0	0/0
313	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR ,	03/2019	4,287.59 -	4,287.59	617.83	- 08/2024	07/2025	- 0	0/0
314	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	17,007.00	12,556.00	06/2019 10/2022	09/2023	51(O) 0	29/41
315	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,684.86	10/2017 -	-	-	0/0
316	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	17,667.00	4,771.00	03/2023 -	02/2025	23(O) -	3/16
317	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA , EPC	09/2019	403.62 -	403.62	122.49	06/2021 12/2021	07/2022	13(O) 0	0/0
318	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 1,587.16	1,587.16	648.84	09/2020 08/2022	08/2022	23(O) 0	15/25
319	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 1,311.05	1,311.05	199.40	06/2006 -	-	-	0/0
320	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	13,038.20	08/2013 11/2022	05/2023	117(O) 9	23/26
321	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	259.30	04/2016 12/2017	12/2021	68(O) 0	0/0
322	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	480.89	11/2016 12/2021	02/2022	63(O) 1	10/12
323	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	90.75	03/2018 -	03/2022	48(O) -	0/0
324	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	690.59	01/2018 07/2021	06/2021	-	0/0
325	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	11,773.07	11/2019 07/2021	10/2021	-	0/0
326	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	205.25	02/2019 04/2022	04/2022	38(O) 2	0/0
327	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	157.92	06/2019 11/2021	02/2022	32(O) 0	0/0
328	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	236.27	12/2019 09/2021	01/2022	25(O) 1	0/0
329	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	4,231.07	04/2020 09/2021	06/2021	-	0/0
330	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 9,129.32	9,129.32	2,911.97	12/2018 03/2024	03/2024	63(O) 0	0/0
331	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 6,700.00	6,700.00	3,326.92	12/2018 12/2021	03/2022	39(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
332	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 12/2020	02/2022	19(O) 0	0/0
333	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,825.25	02/2020 09/2021	10/2021	-	0/0
334	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	262.19	05/2020 08/2021	01/2022	20(O) 0	0/0
335	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 2,311.89	2,311.89	2,094.59	12/2018 -	01/2022	37(O) -	0/0
336	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN , EPC	01/2020	1,522.71 -	1,522.71	1,009.07	09/2021 08/2022	08/2022	11(O) 0	0/0
337	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN , EPC	03/2020	1,782.00 -	1,782.00	836.25	09/2021 10/2022	10/2022	13(O) 0	0/0
338	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN , EPC	12/2019	702.28 -	702.28	586.88	03/2021 11/2021	01/2022	10(O) 1	0/0
339	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN , EPC	03/2020	1,749.31 -	1,749.31	1,339.51	09/2021 10/2022	10/2022	13(O) 0	0/0
340	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN , EPC	01/2021	382.22 -	382.22	4.15	03/2022 03/2022	05/2022	2(O) 2	0/0
341	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN , EPC	01/2021	1,221.73 -	1,221.73	140.11	07/2022 05/2022	08/2022	1(O) 3	0/0
342	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN , EPC	02/2021	599.99 -	599.99	62.06	07/2022 -	08/2022	1(O) -	0/0
343	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 219.66	219.66	168.20	07/2019 07/2021	03/2022	32(O) 0	0/0
344	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU , EPC	03/2020	1,316.22 -	1,316.22	888.48	09/2021 08/2022	08/2022	11(O) 0	0/0
345	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 10,997.70	10,998.00	9,124.00	11/2020 07/2022	10/2022	23(O) 0	30/33
346	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA , EPC	06/2019	401.90 -	442.03	225.90	04/2021 10/2021	01/2022	9(O) 0	0/0
347	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	3,395.52	09/2023 -	08/2024	11(O) -	1/13
348	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH , EPC	03/2020	501.29 -	524.83	368.49	09/2021 10/2022	10/2022	13(O) 0	0/0
349	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH , EPC	01/2020	798.24 -	852.90	541.97	09/2021 08/2022	08/2022	11(O) 0	0/0
350	NOKHRA - [N18000282]NTPC,UTTAR PRADESH , EPC	03/2020	1,722.14 -	1,803.19	552.18	09/2021 10/2022	10/2022	13(O) 0	0/0
351	PARASAN SOLAR POWER PROJECT - [N18000298]SJVN,UTTAR PRADESH ,	08/2021	313.58 -	313.58	112.91	12/2022 -	12/2022	0(O) -	0/5
352	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 4,825.60	4,825.60	4,374.66	02/2016 -	06/2023	88(O) -	23/34
353	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	5,326.00	03/2013 12/2021	09/2024	138(O) 0	8/15
354	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 3,860.35	3,860.35	2,356.86	06/2013 12/2024	12/2024	138(O) 0	10/25

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
355	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.93	08/2017 -	-	-	0/15
356	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	947.89	785.06	12/2021 06/2022	06/2022	6(O) 0	11/32
357	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,803.00	743.00	09/2019 12/2024	12/2024	63(O) 0	6/10
358	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	345.21	04/2018 06/2021	06/2021	-	0/0
359	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 633.80	633.80	530.53	11/2018 -	03/2022	40(O) -	0/0
	Total		2,07,257.24 -	2,70,968.33	1,80,166.07				296/466
	<u>HEAVY INDUSTRY</u>								
360	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	900.00	815.00	09/2019 -	-	-	0/0
361	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 3,727.30	3,727.30	3,526.63	09/2011 03/2021	03/2021	-	24/25
	Total		3,272.00 -	4,627.30	4,341.63				24/25
	<u>HEALTH AND FAMILY WELFARE</u>								
362	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	273.41	03/2019 -	03/2021	-	0/0
363	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	515.47	- -	03/2022	- -	0/0
364	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0
365	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	446.44	05/2021 -	-	-	0/0
366	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	586.50	581.44	11/2013 -	09/2021	-	0/0
367	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021	-	2/2
368	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	5/5
369	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	190.34	183.36	- -	12/2021	- -	0/0
370	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	231.05	- -	01/2021	-	0/0
371	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	2/2
372	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	9(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
373	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0
374	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	394.73	09/2023 -	09/2023	0(O) -	0/0
375	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
376	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	218.99	09/2025 -	05/2024	-16(O) -	0/0
377	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD FOR HEALTH,KERALA ,	09/2017	150.29 -	150.29	70.91	03/2020 -	12/2021	21(O) -	2/7
378	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	259.46	03/2019 -	01/2021	-	0/0
379	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	546.71	-	12/2021	-	0/0
380	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	262.64	05/2018 -	03/2022	46(O) -	0/0
381	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19(O) -	0/33
382	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	-	1/1
383	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	553.85	06/2020 -	-	-	0/0
384	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA ,	10/2016	209.84 -	209.84	190.46	03/2020 -	05/2021	-	1/5
385	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	243.92	-	03/2021	-	0/0
386	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	604.15	04/2020 -	-	-	0/0
387	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3
388	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
389	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	321.31	03/2019 -	10/2021	-	0/0
390	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL ,	04/2018	651.99 -	651.99	609.49	-	10/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		15,273.26 -	15,715.78	9,278.31				18/62
	<u>RAILWAYS</u>								
391	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	1,042.28	03/2009 -	03/2024	180(O) -	0/0
392	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	3,377.00	3,753.96	03/2020 -	03/2022	24(O) -	0/0
393	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	1,388.38	03/2022 -	03/2024	24(O) -	0/0
394	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.68	3,515.82	12/2023 -	12/2023	0(O) -	0/0
395	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	769.95	03/2022 03/2024	03/2026	48(O) 0	0/0
396	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	487.13	434.63	03/2018 -	-	-	0/0
397	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019 -	-	-	0/0
398	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,043.00	919.48	03/2019 -	03/2023	48(O) -	0/0
399	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,950.00	1,939.39	03/2022 -	03/2023	12(O) -	0/0
400	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	1,873.21	1,586.23	03/2021 -	03/2022	12(O) -	0/0
401	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 898.53	1,080.00	1,086.41	03/2012 11/2022	11/2022	128(O) 0	0/0
402	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 614.45	614.45	352.68	- -	12/2023	- -	0/0
403	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,597.10	- 03/2023	03/2023	- 0	0/0
404	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 516.02	516.02	459.31	03/2020 -	-	-	0/0
405	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 751.55	751.55	722.71	03/2012 09/2021	09/2021	-	0/0
406	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,132.03	2,145.00	1,029.65	03/2019 -	03/2024	60(O) -	0/0
407	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	- -	-	-	0/0
408	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	-	-	0/0
409	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.31	- -	-	-	0/0
410	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	- -	-	-	0/0
411	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	2.55	- -	03/2024	-	0/0
412	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 735.20	735.20	390.81	- -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
413	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	- -	0/0
414	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
415	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	4.99	- -	-	-	0/0
416	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	3.20	- -	-	-	0/0
417	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
418	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	153.43	- 03/2023	03/2023	- 0	0/0
419	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	- -	-	-	0/0
420	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.59	- -	-	-	0/0
421	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	1,467.70	- -	03/2023	- -	0/0
422	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	540.73	03/2020 03/2023	12/2024	57(O) 0	0/0
423	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	519.33	316.22	- -	03/2025	-	0/0
424	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	1,051.33	03/2020 -	03/2023	36(O) -	0/1
425	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	572.94	03/2020 03/2023	03/2023	36(O) 0	1/1
426	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	560.09	560.09	07/2014 -	-	-	0/0
427	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 1,215.54	1,215.54	543.61	03/2021 03/2024	03/2024	36(O) 0	0/0
428	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 1,185.73	1,185.73	424.08	03/2021 03/2024	03/2024	36(O) 0	0/0
429	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 803.11	1,483.14	1,370.20	- 03/2022	03/2022	- 0	0/0
430	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	1,012.35	03/2020 03/2023	03/2023	36(O) 0	1/1
431	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,364.39	03/2020 -	12/2021	21(O) -	0/0
432	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
433	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 2,135.34	2,135.34	733.21	03/2021 12/2023	12/2023	33(O) 0	0/1
434	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	18(O) -	0/1
435	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	45(O) -	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
436	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	339.31	03/2020 -	-	-	1/2
437	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	359.00	116.87	- -	03/2024	- -	0/0
438	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	160.79	- -	09/2023	- -	0/0
439	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,631.75	2,223.37	1,966.82	03/2020 03/2024	03/2024	48(O) 0	0/0
440	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	126.35	03/2012 10/2023	10/2023	139(O) 0	0/0
441	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,650.00	1,737.74	12/2021 -	12/2021	0(O) -	0/0
442	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	872.65	942.56	03/2021 -	12/2021	9(O) -	0/0
443	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 -	844.10	254.99	- -	03/2024	- -	0/0
444	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 859.16	1,378.11	558.66	03/2019 03/2023	03/2023	48(O) 0	0/0
445	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,868.89	2,201.29	12/2021 -	03/2022	3(O) -	0/0
446	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	21(O) -	0/0
447	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,042.12	730.07	03/2021 -	12/2022	21(O) -	0/0
448	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
449	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 528.49	528.49	123.75	- 12/2022	-	-	0/0
450	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 154.15	154.15	109.05	- 12/2021	-	-	0/0
451	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT ,	04/2017	692.25 692.25	742.88	.89	03/2020 03/2024	03/2024	48(O) 12	0/0
452	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT ,	04/2018	537.31 537.31	537.31	.64	03/2024 03/2024	03/2024	0(O) 0	0/0
453	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	745.06	12/2011 -	06/2021	-	0/0
454	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	320.28	03/2019 -	-	-	0/0
455	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	6,753.42	1,905.63	12/2026 -	12/2025	-12(O) -	0/0
456	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	26,237.89	11/2002 -	12/2022	241(O) -	0/0
457	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,650.00	3,661.29	- 03/2022	03/2022	- 0	0/0
458	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	941.70	- 03/2023	03/2023	- 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
459	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	1,097.56	03/2021 -	12/2023	33(O) -	0/0
460	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	390.00	403.49	03/2021 -	03/2022	12(O) -	0/0
461	CHAKRADHARPUR TO GOILKERA 3RD LINE (34 KM) - [N22000507]SER,JHARKHAND ,	11/2015	354.54 -	354.54	302.08	12/2018 -	06/2020	-	0/0
462	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND ,	04/2018	428.65 -	472.50	1.61	06/2022 -	12/2025	42(O) -	0/0
463	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND ,	04/2018	390.39 -	511.75	110.13	12/2021 -	06/2022	6(O) -	0/0
464	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	5,174.30	158.11	-	12/2024	-	0/0
465	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2024	264(O) -	0/0
466	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	2,161.36	82.81	-	12/2023	-	0/0
467	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	1,530.09	325.32	03/2016 -	12/2026	129(O) -	1/1
468	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	-	12/2023	-	0/0
469	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
470	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	-	12/2025	-	0/0
471	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,000.00	2,477.01	03/2023 -	12/2022	-3(O) -	0/1
472	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	387.33	12/2018 -	06/2025	78(O) -	0/0
473	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	-	12/2023	-	0/0
474	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	36.97	03/2016 -	12/2023	93(O) -	0/0
475	HUBLI- CHIKAJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,954.21	1,205.02	03/2020 -	03/2023	36(O) -	1/5
476	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	760.00	647.09	03/2020 01/2022	01/2022	22(O) 1	1/2
477	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 889.00	732.89	495.11	03/2017 -	03/2025	96(O) -	0/0
478	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 1,566.00	2,815.62	264.51	-	-	-	0/0
479	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 369.55	709.69	256.70	-	03/2025	-	0/0
480	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 275.21	448.10	268.73	-	03/2025	-	0/0
481	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	934.32	-	03/2024	-	0/0
482	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 1,246.00	1,339.00	.82	-	03/2025	-	0/0
483	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
484	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 2,909.99	2,909.99	1,411.38	03/2021 03/2024	03/2024	36(O) 0	4/15
485	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 -	6,171.08	2,327.60	03/2022 -	03/2023	12(O) -	0/0
486	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 2,445.30	2,445.30	1,345.52	03/2020 -	03/2024	48(O) -	1/1
487	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	2,355.40	12/2020 -	12/2021	12(O) -	0/0
488	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	15(O) -	4/17
489	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	540.13	03/2022 -	12/2023	21(O) -	1/1
490	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	172.08	03/2019 -	-	-	0/0
491	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 1,268.32	1,268.32	1,123.85	02/2019 12/2021	12/2021	34(O) 0	0/1
492	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.94	1,370.94	838.56	12/2021 12/2023	12/2023	24(O) 0	0/0
493	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	350.17	06/2020 03/2023	03/2023	33(O) 0	0/0
494	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH ,	04/2017	495.18 -	495.18	.33	03/2022 -	03/2024	24(O) -	0/0
495	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,868.04	03/2004 06/2022	06/2022	219(O) 0	0/0
496	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	24(O) -	0/0
497	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	-	-	0/0
498	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
499	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023	0(O) -	0/0
500	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	24(O) -	0/0
501	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 -	325.00	325.52	03/2019 -	-	-	0/0
502	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	355.54	03/2022 -	03/2024	24(O) -	0/0
503	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
504	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
505	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.49	.00	03/2024 -	-	-	0/0
506	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	12(O) -	0/0
507	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	488.43	03/2023 -	03/2024	12(O) -	0/0
508	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,764.97	03/2024 -	03/2023	-12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
509	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023	0(O) -	0/0
510	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	322.26	03/2022 -	03/2024	24(O) -	0/0
511	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	239.26	03/2023 -	03/2024	12(O) -	0/0
512	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,900.00	2,041.94	03/2020 -	12/2021	21(O) -	0/0
513	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
514	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 3,176.60	3,176.60	1,492.13	03/2023 12/2023	12/2023	9(O) 0	0/1
515	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	269.73	03/2019 -	-	-	0/0
516	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 311.36	311.36	.00	- -	-	-	0/0
517	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 393.62	393.62	152.98	- 12/2022	-	-	0/0
518	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 852.50	1,096.00	40.47	12/2021 12/2024	12/2024	36(O) 0	0/1
519	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)- [220100288]NFR,MANIPUR ,	04/2003	4,454.17 12,264.00	14,322.00	12,012.77	03/2011 12/2023	12/2023	153(O) 0	0/0
520	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	4,083.02	264.34	03/2021 -	-	-	0/0
521	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 5,021.45	6,527.00	4,525.01	03/2014 -	12/2023	117(O) -	0/0
522	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,017.96	878.49	07/2012 -	11/2024	148(O) -	0/0
523	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,421.35	2,010.00	03/2000 -	03/2023	276(O) -	0/0
524	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202(O) -	1/9
525	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	4,541.38	3,936.64	12/2008 -	12/2021	156(O) -	0/0
526	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	638.35	02/2013 -	03/2024	133(O) -	0/0
527	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
528	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	116.44	12/2021 -	12/2021	0(O) -	0/0
529	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	610.00	595.91	01/2019 -	02/2022	37(O) -	0/0
530	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,524.68	1,524.68	1,004.89	03/2022 03/2023	03/2023	12(O) 0	0/0
531	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	882.29	03/2022 03/2025	03/2025	36(O) 0	0/0
532	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	191.39	- -	-	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
533	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	471.73	03/2022 12/2024	12/2024	33(O) 0	0/5
534	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	.00	- 04/2010	12/2027	- 72	0/0
535	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
536	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.58	- -	-	-	0/0
537	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 2,042.51	2,042.51	446.24	03/2019 -	12/2023	57(O) -	0/0
538	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	1,205.00	2.28	- -	03/2030	-	0/0
539	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 457.08	749.40	578.46	- 12/2021	03/2022	- 2	0/0
540	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	76.57	03/2020 -	-	-	0/0
541	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	333.46	- 12/2021	06/2022	- 3	0/0
542	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	750.00	157.51	03/2020 -	-	-	0/0
543	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,090.60	1,089.12	- -	-	-	0/0
544	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,172.16	308.35	03/2019 -	12/2027	105(O) -	0/0
545	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228(O) -	0/0
546	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	-	0/0
547	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	11.77	- -	03/2025	-	0/0
548	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	453.42	03/2022 -	03/2025	36(O) -	0/0
549	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	502.48	521.63	- -	03/2021	-	0/0
550	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONG WITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	618.75	03/2016 -	03/2025	108(O) -	0/0
551	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	96(O) -	0/0
552	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
553	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	201.29	03/2016 -	03/2025	108(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
554	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	439.30	507.59	03/2017 -	03/2025	96(O) -	0/0
555	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	-	0/0
556	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.11	- -	03/2025	- -	0/0
557	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
558	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	495.10	316.82	- -	03/2022	- -	0/0
559	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
560	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240(O) -	0/0
561	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKUPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	36.13	- -	03/2025	- -	0/0
562	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	40.65	- -	03/2025	- -	0/0
563	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	142.05	02/2012 -	03/2025	157(O) -	0/0
564	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	109.63	03/2014 -	03/2025	132(O) -	0/0
565	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
566	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,952.68	729.57	03/2023 -	03/2024	12(O) -	0/0
567	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	791.39	597.99	- -	09/2023	- -	0/0
568	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- -	12/2023	- -	0/0
569	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,404.03	1,100.11	- -	12/2025	- -	2/2
570	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 927.94	927.94	691.26	03/2020 -	02/2022	23(O) -	1/1
571	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	156(O) -	1/1
572	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	410.29	- -	03/2024	- -	0/0
573	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	701.81	334.01	03/2020 -	10/2022	31(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
574	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,104.00	983.01	03/2020 -	09/2021	-	0/0
575	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,877.81	1,878.00	1,496.77	03/2019 -	03/2024	60(O) -	0/0
576	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	929.86	958.41	03/2019 12/2021	12/2021	33(O) 0	0/38
577	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
578	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,613.72	03/2021 -	03/2024	36(O) -	0/0
579	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	18,841.98	12/2023 -	12/2023	0(O) -	0/0
580	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	-	0/0
581	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.13	243.28	03/2023 12/2025	12/2025	33(O) 0	0/0
582	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	839.00	839.36	03/2016 -	-	-	0/0
583	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE ,	03/2019	1,866.31 -	1,866.31	288.29	05/2023 -	12/2023	7(O) -	0/0
584	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	6,663.00	1,420.48	03/2015 -	03/2026	132(O) -	0/0
585	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
586	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,687.63	03/2009 12/2024	12/2024	189(O) -15	0/0
587	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,894.70	02/2015 -	06/2022	88(O) -	0/0
588	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	433.00	419.58	03/2009 12/2022	-	-	1/1
589	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	933.16	06/2021 03/2025	03/2025	45(O) 0	0/0
590	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	266.61	239.38	03/2015 -	03/2019	-	0/0
591	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	1,195.24	02/2019 -	03/2022	37(O) -	0/0
592	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	284.93	10/2020 03/2024	03/2024	41(O) 0	0/0
593	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 238.03	238.03	224.26	03/2020 -	03/2022	24(O) -	0/0
594	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	710.98	03/2022 03/2023	03/2023	12(O) 0	0/0
595	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	524.03	03/2022 03/2026	03/2026	48(O) 0	0/0
596	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	193.71	11/2018 -	03/2024	64(O) -	0/0
597	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	718.37	12/2018 03/2024	03/2024	63(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
598	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	1,312.96	1,119.38	03/2020 -	06/2022	27(O) -	0/0
599	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	2,024.04	12/2024 -	12/2026	24(O) -	0/0
600	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	2,156.59	03/2020 -	12/2021	21(O) -	0/0
601	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,536.00	1,269.37	03/2019 -	06/2022	39(O) -	0/0
602	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
603	MANSA-BHATINDA (PHASE-I) INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB ,	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108(O) -	0/0
604	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	860.41	769.95	02/2019 -	06/2022	40(O) -	0/0
605	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	821.64	.00	- -	-	-	0/1
606	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	322.98	.00	- -	-	-	0/0
607	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	480.00	384.12	03/2020 -	09/2021	-	0/0
608	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	2,215.27	4.60	- -	-	-	0/0
609	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	464.53	03/2018 -	-	-	0/0
610	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	413.98	08/2022 -	11/2022	3(O) -	0/0
611	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 4,084.69	8,600.00	1,856.78	12/2015 12/2023	12/2023	96(O) 0	0/0
612	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	1,549.09	712.68	03/2020 -	03/2025	60(O) -	0/0
613	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	774.51	492.88	06/2013 07/2022	07/2022	109(O) 0	1/4
614	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	3,081.20	1,718.56	02/2019 -	03/2025	73(O) -	0/0
615	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	227.40	65.02	- -	03/2030	- -	0/0
616	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	3,154.43	239.59	- -	12/2025	- -	0/0
617	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	133(O) -	0/0
618	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	839.01	.63	- -	03/2030	- -	0/0
619	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	603.23	1.68	- -	03/2030	- -	0/0
620	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	608.13	427.75	- 12/2021	02/2022	- 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
621	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	1,122.00	994.02	- 09/2021	12/2022	- 0	0/0
622	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	991.83	922.01	03/2005 -	12/2021	201(O) -	0/0
623	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
624	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	1,111.90	03/2022 -	06/2022	3(O) -	0/0
625	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,509.71	03/2020 -	06/2022	27(O) -	0/0
626	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.25	3.69	- -	-	-	0/0
627	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,373.74	654.79	03/2010 -	03/2024	168(O) -	1/1
628	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	839.78	03/2016 -	12/2021	69(O) -	0/0
629	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
630	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	653.38	03/2021 -	-	-	3/3
631	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	850.00	949.03	12/2024 -	12/2024	0(O) -	0/0
632	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 176.18	242.28	67.29	03/2022 03/2022	-	-	0/0
633	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 90.00	742.00	612.37	03/2020 06/2022	06/2022	27(O) 0	2/3
634	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
635	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
636	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
637	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	489.64	105.51	- -	-	-	0/0
638	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,824.00	1,465.45	03/2022 -	03/2022	0(O) -	0/0
639	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	531.20	03/2020 -	01/2022	22(O) -	4/6
640	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,000.00	982.28	03/2022 -	12/2024	33(O) -	0/0
641	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,400.00	1,438.92	03/2019 -	06/2022	39(O) -	0/0
642	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	1,089.92	03/2023 -	12/2024	21(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
643	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,825.00	1,777.07	12/2020 -	12/2022	24(O) -	0/0
644	RAMNA - SINGRAULI DOUBLING - [N22000417]ECCR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,487.37	03/2020 -	03/2024	48(O) -	0/0
645	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECCR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	324.29	03/2019 -	03/2022	36(O) -	0/0
646	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	72.08	04/2016 -	12/2021	68(O) -	0/0
647	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
648	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	341.66	.00	04/2017 -	10/2022	66(O) -	0/0
649	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,345.00	.00	01/2018 -	-	-	0/0
650	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
651	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	800.00	145.14	-	12/2023	-	0/0
652	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 600.00	366.71	332.87	01/2022 -	03/2022	2(O) -	0/0
653	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	355.22	12/2019 -	04/2021	-	0/0
654	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	76.74	03/2023 -	06/2025	27(O) -	0/0
655	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	1,046.53	03/2021 06/2023	06/2023	27(O) -6	1/6
656	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	2,364.27	12/2023 -	12/2023	0(O) -	0/0
657	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
658	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	22,716.11	5,917.58	12/2024 -	03/2025	3(O) -	0/0
659	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	275.06	03/2019 -	-	-	0/0
660	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
661	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
662	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	912.61	03/2019 12/2009	03/2025	72(O) 0	0/0
663	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
664	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
665	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	3,317.94	03/2016 -	03/2025	108(O) -	0/0
666	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	1,460.93	03/2016 -	03/2025	108(O) -	0/0
667	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	-	0/0
668	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	41.78	-	03/2025	-	0/0
669	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	38.20	-	-	-	0/0
670	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	-	03/2025	-	0/0
671	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	303.23	-	03/2022	-	0/0
672	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	1,167.00	1,095.12	12/2021 -	10/2021	-	0/0
673	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
674	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN - [N22000499]NFR, WEST BENGAL ,	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	-	0/0
675	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER, WEST BENGAL ,	04/2018	338.00 -	393.83	22.39	06/2022 -	06/2023	12(O) -	0/0
	Total		4,43,040.10 -	6,84,768.60	2,77,511.94				35/137
	<u>SOCIAL JUSTICE</u>								
676	CENTRE FOR DISABILITY SPORTS - [N38000001]CPWD, MADHYA PRADESH , EPC	02/2019	170.99 -	170.99	34.00	03/2024 -	03/2024	0(O) -	0/0
	Total		170.99 -	170.99	34.00				0/0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
677	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD EDUCATION, ANDHRA PRADESH ,	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	-	3/7
678	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION, ANDHRA PRADESH ,	02/2019	655.34 655.34	655.34	300.85	06/2020 11/2022	11/2022	29(O) 0	0/110
679	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION, ANDHRA PRADESH ,	09/2019	588.72 -	588.72	117.82	09/2022 06/2023	06/2023	9(O) 2	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
680	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR ,	02/2016	496.18 496.00	498.99	301.90	06/2017 -	03/2022	57(O) -	2/6
681	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR ,	09/2018	375.00 -	375.00	125.38	09/2020 -	11/2022	26(O) -	0/0
682	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATISGARH ,	03/2020	808.62 -	808.62	296.89	07/2022 -	10/2022	3(O) -	0/0
683	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD EDUCATION,GOA ,	05/2019	303.90 -	303.90	48.30	03/2020 02/2023	02/2023	35(O) 0	3/8
684	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH ,	11/2012	270.83 -	244.00	242.81	11/2014 11/2021	11/2021	-	7/8
685	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	85.88	06/2022 10/2022	10/2022	4(O) 0	0/0
686	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR ,	03/2019	424.93 -	424.93	80.19	07/2022 -	10/2022	3(O) -	0/0
687	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD EDUCATION,JAMMU AND KASHMIR ,	01/2018	676.00 748.19	676.00	223.43	04/2023 -	04/2023	0(O) -	0/0
688	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND ,	09/2012	171.86 -	171.86	111.29	03/2016 -	-	-	1/6
689	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	324.03	03/2022 -	10/2022	7(O) -	0/12
690	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	-	-	1/8
691	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	216.78	03/2021 -	02/2023	23(O) -	2/11
692	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA ,	01/2018	223.37 -	223.37	117.64	07/2020 -	12/2021	17(O) -	4/14
693	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA ,	09/2013	484.32 429.70	429.70	230.00	09/2014 06/2022	06/2022	93(O) 0	0/0
694	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA ,	01/2019	790.79 -	790.79	258.32	03/2022 -	06/2022	3(O) -	0/5
695	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB ,	01/2018	430.00 -	387.83	237.59	05/2020 -	06/2022	25(O) -	3/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
696	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB ,	10/2019	348.24 -	348.24	34.60	05/2022 -	10/2022	5(O) -	1/8
697	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN ,	12/2016	549.31 -	559.47	458.38	07/2019 -	-	-	3/6
698	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL , EPC	03/2020	193.83 -	193.83	51.77	06/2020 -	03/2022	21(O) -	0/14
	Total		10,139.61 -	10,047.96	4,113.00				30/228
	<u>HOME AFFAIRS</u>								
699	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI ,	10/2013	1,219.21 -	2,000.00	1,049.80	10/2019 -	05/2022	31(O) -	1/7
700	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI , EPC	06/2019	277.35 290.33	290.33	38.13	07/2022 12/2022	12/2022	5(O) 0	2/6
701	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD FOR MHA,HARYANA , EPC	01/2020	166.98 166.98	166.98	7.84	10/2023 04/2024	04/2024	6(O) 6	0/0
702	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAU LI - [N45000003]CPWD FOR MHA,UTTAR PRADESH ,	05/2019	199.31 -	199.31	20.53	01/2022 -	01/2020	-	0/0
703	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL , Central Sector Projects	10/2014	162.88 238.00	238.00	173.06	04/2018 08/2022	08/2022	52(O) 8	5/6
	Total		2,025.73 -	2,894.62	1,289.36				8/19
	<u>DPIIT</u>								
704	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI ,	11/2017	4,773.00 -	5,178.00	3,044.41	12/2019 05/2022	05/2022	29(O) 0	0/0
705	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE ,	09/2011	12,579.09 -	13,812.30	9,574.07	09/2019 01/2014	07/2021	-	0/0
	Total		17,352.09 -	18,990.30	12,618.48				0/0
	<u>DONER</u>								
706	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL FOR DONER,MEGHALAYA ,	04/2014	151.33 -	151.33	149.33	09/2017 -	08/2021	-	12/15
	Total		151.33 -	151.33	149.33				12/15
	<u>RENEWABLE ENERGY</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
707	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWDR ENERGY, DELHI ,	10/2017	271.90 -	271.90	90.99	11/2019 -	-	-	0/0
	Total		271.90 -	271.90	90.99				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
708	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022	39(O) 0	1/4
709	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51(O) 0	2/4
710	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	202.59	04/2017 03/2021	10/2021	-	3/4
711	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	77.75	10/2018 -	03/2022	41(O) -	1/4
712	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41(O) 0	2/4
713	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 237.80	238.00	148.90	11/2019 10/2021	10/2021	-	0/0
714	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	214.90	11/2019 06/2021	06/2021	-	0/0
715	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	229.32	07/2019 -	-	-	0/4
716	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
717	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,286.10	05/2014 -	-	-	0/0
718	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
719	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	243.29	10/2015 06/2021	-	-	4/4
720	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	.00	02/2017 -	-	-	0/0
721	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	968.97	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
722	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	266.63	- -	-	-	0/0
723	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	1,221.85	- -	-	-	0/0
724	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
725	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	1,321.09	- -	10/2021	-	0/0
726	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	2,499.00	1,009.50	03/2021 07/2021	07/2021	-	4/4
727	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,654.42	- -	09/2021	-	0/0
728	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	654.52	- -	02/2021	-	0/0
729	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	85.61	- -	06/2022	-	0/0
730	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	464.83	- -	-	-	0/0
731	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	353.43	333.09	12/2015 -	-	-	3/3
732	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 309.37	372.68	257.45	02/2017 10/2021	-	-	3/4
733	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	154.09	05/2017 10/2021	-	-	3/4
734	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	213.08	08/2017 02/2022	-	-	3/4
735	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 373.05	429.43	325.74	11/2017 01/2022	-	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
736	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 202.83	228.32	145.60	08/2018 12/2021	-	-	3/4
737	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 274.73	289.67	211.71	08/2018 11/2021	-	-	3/4
738	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 556.13	504.19	478.63	11/2018 07/2021	-	-	3/4
739	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	584.10	05/2016 09/2021	-	-	3/4
740	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 381.75	418.03	324.61	08/2018 10/2021	-	-	3/4
741	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	328.03	01/2017 12/2021	-	-	3/4
742	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 316.06	386.09	214.31	05/2016 11/2021	-	-	3/4
743	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	257.45	08/2016 12/2021	07/2021	-	3/4
744	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	359.86	09/2016 08/2021	-	-	3/4
745	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	315.76	08/2017 12/2021	-	-	3/4
746	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 381.75	263.45	118.05	09/2017 05/2022	-	-	1/4
747	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 596.38	576.48	418.18	01/2018 04/2022	-	-	2/4
748	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH , EPC	09/2018	597.67 -	597.67	252.65	01/2020 -	-	-	0/0
749	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH , EPC	09/2018	617.41 -	617.41	526.54	02/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
750	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2019	1,226.88 -	1,226.88	299.39	02/2021 -	-	-	0/0
751	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	1,601.10 -	1,601.10	69.79	02/2021 -	-	-	0/0
752	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH , EPC	03/2020	207.79 -	207.79	108.34	03/2021 -	04/2022	13(O) -	2/4
753	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH , EPC	06/2020	221.40 -	221.40	24.49	05/2021 -	12/2022	19(O) -	0/4
754	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH , EPC	08/2020	222.61 -	222.61	6.94	03/2021 -	03/2023	24(O) -	0/4
755	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	390.07	06/2018 -	03/2021	-	3/3
756	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	- 0	3/4
757	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	182.01	04/2017 03/2021	03/2022	59(O) 0	2/4
758	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	252.79	153.14	04/2017 -	03/2022	59(O) -	2/4
759	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	263.31	155.10	04/2017 -	03/2022	59(O) -	2/4
760	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	61.40	04/2017 -	02/2021	-	1/4
761	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	252.05	157.83	04/2017 -	03/2022	59(O) -	3/4
762	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
763	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	128.02	- 08/2021	12/2021	- 0	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
764	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022	- 0	2/4
765	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	335.59	- 11/2021	03/2022	- 0	0/0
766	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	118.08	- 03/2021	03/2022	- 0	3/4
767	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	94.23	- 04/2022	04/2022	- 0	3/4
768	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	84.29	- 04/2022	04/2022	- 0	3/4
769	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 -	210.50	145.76	- -	10/2021	-	4/4
770	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,251.08	- 03/2020	-	-	0/0
771	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	227.25	- -	09/2020	-	0/0
772	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	301.06 -	301.06	25.63	04/2022 -	04/2022	0(O) -	0/4
773	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH , EPC	09/2020	353.90 -	353.90	26.00	05/2022 -	05/2022	0(O) -	0/4
774	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	403.68 -	403.68	68.02	02/2020 -	-	-	0/0
775	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	342.55 -	342.55	195.00	02/2020 -	-	-	0/0
776	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	421.48 -	421.48	69.62	11/2020 -	-	-	0/0
777	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	543.05 -	543.05	155.44	11/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
778	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	486.70 -	486.70	100.72	10/2020 -	-	-	0/0
779	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	560.39 -	560.39	216.15	02/2020 -	-	-	0/0
780	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	347.78 -	347.78	149.95	09/2020 -	-	-	0/0
781	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	394.27 -	394.27	41.91	10/2020 -	-	-	0/0
782	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	450.65 -	450.65	59.86	11/2020 -	-	-	0/0
783	TADADEGE - HENKAR - [N24001315]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	550.45 -	550.45	13.03	03/2023 -	03/2023	0(O) -	0/4
784	LADDA - BASAI - [N24001316]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	445.96 -	445.96	.00	04/2023 -	04/2023	0(O) -	0/4
785	DOGINALA - GAU - [N24001320]NHIDCL,ARUNACHAL PRADESH , EPC	12/2020	242.30 -	242.30	.00	09/2022 -	09/2022	0(O) -	0/4
786	DEMBUEN - BRUNI - [N24001321]NHIDCL,ARUNACHAL PRADESH , EPC	12/2020	606.63 -	606.63	.00	03/2023 -	03/2023	0(O) -	0/4
787	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]MoRTH,ARUNACHAL PRADESH , EPC	02/2021	588.09 -	588.09	93.72	03/2024 -	03/2024	0(O) -	0/0
788	BALANCE WORK OF 2-LANING OF LONGDING-TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]MoRTH,ARUNACHAL PRADESH , EPC	01/2020	358.26 -	358.26	.52	02/2024 -	02/2024	0(O) -	0/0
789	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH , EPC	06/2020	437.60 -	437.60	7.78	08/2021 -	-	-	0/0
790	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH , EPC	06/2020	496.47 -	496.47	8.93	08/2021 -	-	-	0/0
791	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH , EPC	03/2021	182.55 -	182.55	.00	09/2021 -	09/2021	-	0/0
792	JORAM - KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390]NHIDCL,ARUNACHAL PRADESH ,	08/2020	228.71 -	228.71	40.08	04/2022 -	04/2022	0(O) -	2/4
793	JORAM - KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	294.04 -	294.04	79.46	04/2022 -	04/2022	0(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
794	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	199.03 -	199.03	58.18	04/2022 -	04/2022	0(O) -	2/4
795	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	184.88 -	184.88	40.92	04/2022 -	04/2022	0(O) -	2/4
796	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	612.58	612.58	02/2009 -	-	-	0/0
797	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	340.14	.00	04/2009 -	-	-	0/0
798	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	435.78	.00	11/2008 -	-	-	0/0
799	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	255.23	.00	11/2008 -	-	-	0/0
800	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	655.17	655.17	07/2009 -	-	-	0/0
801	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	372.30	05/2018 -	03/2022	46(O) -	3/4
802	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	113.03	06/2018 -	12/2021	42(O) -	1/4
803	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	179.86	06/2018 -	12/2021	42(O) -	2/4
804	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	169.08	11/2018 -	11/2021	-	4/4
805	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	516.16	11/2018 -	02/2022	39(O) -	3/4
806	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 -	390.73	346.72	05/2017 05/2022	05/2022	60(O) 0	0/0
807	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	207.70	- -	12/2021	- -	3/4
808	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	100.00	12/2018 -	12/2021	36(O) -	1/4
809	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	229.20	01/2016 -	03/2022	74(O) -	3/4
810	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	139.69	01/2016 -	03/2022	74(O) -	2/4
811	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74(O) -	2/3
812	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	272.86	- -	03/2023	- -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
813	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/2018	160.00 -	160.00	133.51	09/2021 -	02/2022	5(O) -	0/0
814	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	1,049.51	155.61	-	12/2021	-	2/4
815	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM ,	03/2020	166.94 -	166.94	42.69	12/2020 12/2022	-	-	0/0
816	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL,ASSAM , EPC	03/2020	220.20 -	220.20	37.93	12/2022 -	12/2022	0(O) -	1/4
817	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM , EPC	08/2020	208.84 -	208.84	20.73	04/2022 -	04/2022	0(O) -	1/4
818	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM , EPC	08/2020	278.46 -	278.46	62.66	03/2022 -	03/2022	0(O) -	1/4
819	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]NHIDCL,ASSAM , EPC	03/2020	216.49 -	216.49	42.19	03/2022 -	03/2022	0(O) -	1/4
820	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]NHIDCL,ASSAM , EPC	11/2020	4,997.04 -	4,997.04	557.28	09/2028 -	09/2028	0(O) -	0/4
821	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]NHIDCL,ASSAM , EPC	12/2020	804.00 -	804.00	46.60	08/2023 -	08/2023	0(O) -	0/4
822	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]NHIDCL,ASSAM , EPC	03/2020	261.13 -	261.13	23.56	06/2022 -	06/2022	0(O) -	0/4
823	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]NHIDCL,ASSAM , EPC	03/2020	217.50 -	217.50	34.17	06/2022 -	06/2022	0(O) -	0/4
824	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]NHIDCL,ASSAM , EPC	09/2019	761.54 -	761.54	140.46	05/2023 -	05/2023	0(O) -	1/4
825	DABOKA KATHKATI PACKAGE-2 - [N24001364]NHIDCL,ASSAM , EPC	03/2021	335.88 -	335.88	16.63	01/2024 -	01/2024	0(O) -	0/4
826	DABOKA KATHKATI PACKAGE-4 - [N24001365]NHIDCL,ASSAM , EPC	02/2021	260.07 -	260.07	34.33	12/2023 -	12/2023	0(O) -	0/4
827	DABOKA KATHKATI PACKAGE-5 - [N24001366]NHIDCL,ASSAM , EPC	03/2021	288.85 -	288.85	.00	01/2023 -	01/2023	0(O) -	0/4
828	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM , EPC	03/2021	636.42 -	636.42	.00	12/2022 -	12/2022	0(O) -	0/4
829	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]NHIDCL,ASSAM , EPC	03/2021	286.72 -	286.72	.00	01/2024 -	01/2024	0(O) -	0/4
830	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]MoRTH,ASSAM , EPC	02/2021	925.47 -	925.47	.00	07/2025 -	07/2025	0(O) -	0/0
831	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,198.39	02/2013 -	-	-	3/4
832	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.92	03/2014 -	-	-	0/0
833	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
834	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	506.02	07/2013 12/2021	-	-	2/3
835	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	591.00	578.00	11/2013 -	-	-	0/0
836	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 780.77	675.00	399.67	- -	-	-	0/0
837	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
838	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	445.90	04/2019 -	-	-	0/0
839	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	821.37	- -	10/2021	-	2/4
840	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 247.00	322.09	.00	04/2018 -	-	-	0/0
841	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	527.80	- -	-	-	1/4
842	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,182.94	278.12	- -	-	-	0/0
843	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	1,038.56	1,034.47	- -	-	-	3/4
844	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	649.27	651.24	04/2018	-	-	4/4
845	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	333.28	- -	-	-	0/0
846	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 683.82	560.70	698.84	07/2016 -	-	-	0/0
847	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	152.22	05/2016 -	-	-	0/0
848	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	527.97	05/2016 -	-	-	0/0
849	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 2,138.16	925.87	1,224.99	10/2016 -	-	-	0/0
850	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	.00	05/2017 -	-	-	0/0
851	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,532.47	12/2016 -	-	-	0/0
852	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	99.86	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
853	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	-	0/0
854	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	341.21	08/2017 -	02/2022	54(O) -	0/0
855	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 1,962.50	1,962.50	249.88	- 01/2021	-	-	0/0
856	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	113.25	- -	-	-	0/0
857	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
858	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	78.33	- -	-	-	0/0
859	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	79.35	- -	-	-	0/0
860	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	93.13	- -	-	-	0/0
861	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	252.17	- -	-	-	0/0
862	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR , EPC	10/2013	649.90 -	649.90	44.00	12/2020 -	-	-	0/0
863	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR , EPC	10/2013	446.97 -	446.97	.00	11/2020 -	-	-	0/0
864	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR , EPC	10/2013	464.09 -	464.09	60.06	11/2020 -	-	-	0/0
865	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR , EPC	10/2019	1,101.99 -	1,101.99	209.64	02/2020 -	-	-	0/4
866	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	241.71	- 01/2022	01/2022	- 1	0/0
867	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	439.27	05/2018 -	-	-	0/0
868	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
869	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 1,096.52	1,096.52	518.73	04/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
870	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	402.95	- -	03/2021	-	0/0
871	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 572.66	572.66	284.86	08/2016 06/2022	06/2022	70(O) 0	0/0
872	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	282.86	06/2017 03/2022	03/2022	57(O) 3	0/0
873	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 543.73	544.00	400.87	09/2016 03/2022	03/2022	66(O) 3	0/0
874	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 731.50	731.50	476.86	10/2016 06/2022	06/2022	68(O) 6	0/0
875	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 435.61	435.61	117.77	07/2016 12/2022	12/2022	77(O) 0	0/0
876	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	298.63	01/2018 01/2022	01/2022	48(O) 1	0/0
877	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	251.27	03/2015 03/2022	03/2022	84(O) 0	0/0
878	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	113.05	05/2019 03/2022	03/2022	34(O) 3	0/0
879	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	333.56	11/2017 01/2022	01/2022	50(O) 1	0/0
880	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	325.55	- -	-	-	0/4
881	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	118.37	- -	-	-	2/4
882	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	244.36	- -	-	-	3/4
883	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	560.12	- -	-	-	0/0
884	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	400.90	- -	-	-	0/0
885	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	365.21	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
886	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	308.10	05/2020 -	-	-	1/4
887	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 -	852.67	212.65	12/2019 -	-	-	1/4
888	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-	-	2/3
889	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	.00	07/2013 -	-	-	0/0
890	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	439.98	12/2015 -	-	-	3/3
891	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	737.67	-	-	-	2/2
892	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	203.40	-	-	-	1/1
893	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	505.33	-	-	-	2/2
894	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	421.85	-	-	-	2/2
895	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	.00	-	-	-	0/0
896	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	392.00	353.42	-	04/2021	-	0/0
897	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	285.03	-	-	-	0/0
898	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	199.86	-	-	-	0/3
899	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 1,361.00	1,361.00	451.40	- 01/2019	-	-	2/4
900	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	-	3/3
901	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
902	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,361.00	451.40	- 01/2019	-	-	2/4
903	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,043.00	2,003.16	-	-	-	0/0
904	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	564.11	-	07/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
905	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
906	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	614.62	11/2018 -	-	-	3/4
907	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	315.08	11/2018 -	-	-	4/4
908	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	187.80	05/2019 -	-	-	2/4
909	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	356.16	03/2018 -	-	-	2/4
910	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	186.00	06/2021 -	06/2021	-	3/4
911	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
912	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 3,485.00	2,288.00	3,450.00	11/2011 -	-	-	0/0
913	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	507.70	.00	06/2016 -	-	-	0/0
914	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	537.16	.00	07/2018 -	-	-	0/0
915	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	1,577.44	04/2019 -	09/2021	-	0/0
916	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	293.15	- 06/2021	12/2020	-	0/0
917	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	172.62	- -	-	-	0/0
918	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	925.96	341.09	- 02/2018	02/2018	-	0/0
919	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 906.65	922.64	387.49	- 02/2018	02/2018	-	0/0
920	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	138.07	- -	-	-	0/0
921	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	138.72	- -	-	-	0/0
922	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	179.30	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
923	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	927.71	- -	-	-	0/0
924	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	965.92	- -	-	-	0/0
925	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	1,039.87	- -	-	-	0/0
926	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	898.79	- -	-	-	0/0
927	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	1,068.04	- -	-	-	0/0
928	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	783.29	- -	-	-	0/0
929	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	892.38	- -	-	-	0/0
930	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	1,061.16	- -	-	-	0/0
931	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-	-	0/0
932	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 1,457.82	1,457.82	1,305.69	03/2018 03/2021	-	-	0/0
933	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	670.27	02/2019 -	-	-	0/0
934	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	- -	-	-	0/0
935	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	891.57	- -	-	-	0/0
936	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,341.10	- -	-	-	0/0
937	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P. - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	1,068.47	06/2020 -	09/2021	-	0/0
938	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 1,135.08	1,135.08	760.86	- 11/2021	-	-	0/0
939	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH , EPC	08/2020	272.98 -	272.98	12.49	04/2021 -	-	-	0/0
940	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH , EPC	08/2020	242.80 -	242.80	10.23	03/2021 -	-	-	0/0
941	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH , EPC	08/2020	349.20 -	349.20	41.20	04/2021 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
942	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MORTH,HIMACHAL PRADESH , EPC	02/2021	345.89 -	345.89	9.65	09/2021 -	-	-	0/0
943	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,116.66	07/2015 -	09/2020	-	0/0
944	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	-	0/0
945	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,654.22	07/2013 -	-	-	0/0
946	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,933.15	06/2014 -	10/2020	-	0/0
947	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	1,158.40	06/2019 -	-	-	0/0
948	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,763.58	12/2018 -	-	-	0/0
949	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	1,000.78	-	01/2021	-	2/3
950	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	232.23	08/2018 -	-	-	2/4
951	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	116.48	11/2018 -	-	-	1/4
952	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	88.07	07/2019 -	-	-	0/4
953	CONSTRUCTION OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]NHIDCL,JAMMU AND KASHMIR ,	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023	0(O) -	1/4
954	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]NHIDCL,JAMMU AND KASHMIR , EPC	08/2020	6,808.69 -	6,808.69	369.00	09/2026 -	09/2026	0(O) -	0/6
955	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	228.39 -	228.39	23.72	04/2022 -	04/2022	0(O) -	1/4
956	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	210.79 -	210.79	20.18	04/2022 -	04/2022	0(O) -	1/4
957	KHELLANI-KHANABAL PKG-1 - [N24001323]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	486.45 -	486.45	68.38	09/2022 -	09/2022	0(O) -	1/4
958	KHELLANI-KHANABAL PKG-6 - [N24001324]NHIDCL,JAMMU AND KASHMIR , EPC	02/2021	285.28 -	285.28	22.14	09/2022 -	09/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
959	KHELLANI-KHANABAL PKG-3 - [N24001341]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	398.51 -	398.51	4.68	12/2022 -	12/2022	0(O) -	0/4
960	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	260.40 -	260.40	.00	12/2022 -	12/2022	0(O) -	0/4
961	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	512.43 -	512.43	3.87	02/2023 -	02/2023	0(O) -	0/0
962	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	859.67 -	859.67	.00	08/2023 -	08/2023	0(O) -	0/0
963	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	497.09 -	497.09	5.78	02/2023 -	02/2023	0(O) -	0/0
964	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR , EPC	02/2021	431.28 -	431.28	24.77	03/2023 -	03/2023	0(O) -	0/0
965	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	486.00	406.73	- -	-	-	0/0
966	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	336.60	322.26	08/2018 -	-	-	0/0
967	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	120.40	- -	-	-	0/0
968	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	510.73	- -	-	-	0/0
969	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 1,073.10	1,005.08	.00	- 03/2021	-	-	0/0
970	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	109.08	09/2021 -	09/2021	-	0/4
971	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	-	-	3/3
972	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	122.11	11/2015 -	-	-	0/0
973	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	541.35	09/2017 -	09/2019	-	0/0
974	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	-	0/0
975	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,311.10	08/2018 -	-	-	0/0
976	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36(O) -	0/0
977	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	-	0/0
978	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	1,191.58	04/2020 -	12/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
979	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	870.00	348.00	03/2019 12/2022	06/2023	51(O) 6	0/0
980	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 1,918.36	1,108.00	1,481.35	08/2019 -	-	-	0/0
981	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	-	0/0
982	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,319.54	03/2020 -	-	-	0/0
983	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	171.98	- -	-	-	0/0
984	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,439.59	- -	11/2021	-	0/0
985	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,542.30	- -	-	-	0/0
986	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	185.07	09/2017	-	-	0/0
987	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	162.88	02/2017 -	-	-	0/0
988	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	72.08	06/2019 -	-	-	0/0
989	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	119.59	07/2018 -	-	-	0/0
990	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	111.51	10/2018 -	-	-	0/0
991	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	318.28	195.88	01/2019 -	-	-	0/0
992	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	386.41	347.46	10/2018 -	-	-	0/0
993	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	238.77	02/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
994	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	290.54	03/2017 -	-	-	0/0
995	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	223.35	03/2017 -	-	-	0/0
996	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	125.81	01/2016 -	-	-	0/0
997	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	82.24	05/2018 -	-	-	0/0
998	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	225.88	08/2017 -	-	-	0/0
999	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.28	05/2019 -	-	-	0/0
1000	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA , EPC	01/2017	264.34 -	264.34	185.07	09/2017 -	-	-	0/0
1001	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA , EPC	03/2019	423.15 -	423.15	151.10	12/2019 -	-	-	0/0
1002	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	.00	08/2012 -	-	-	0/0
1003	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	319.68	09/2017 -	-	-	0/0
1004	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	902.51	- 01/2020	01/2020	-	0/0
1005	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	599.30	06/2018 12/2021	12/2021	42(O) 2	0/0
1006	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,300.00	655.89	09/2017 -	-	-	0/0
1007	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1008	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA , EPC	02/2017	294.28 -	294.26	138.37	08/2017 -	-	-	0/0
1009	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA , EPC	02/2017	380.76 -	380.76	248.27	09/2017 -	-	-	0/0
1010	KARGIL- ZANSKR PACKAGE-5 - [N24001330]NHIDCL,LADAKH , EPC	08/2020	169.79 -	169.79	48.49	12/2023 -	12/2023	0(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1011	KARGIL-ZANSKR PACKAGE-1 - [N24001343]NHIDCL,LADAKH , EPC	03/2021	384.23 -	384.23	10.11	01/2023 -	01/2023	0(O) -	0/4
1012	KARGIL-ZANSKR PACKAGE-2 - [N24001344]NHIDCL,LADAKH , EPC	03/2021	404.89 -	404.89	1.98	01/2023 -	01/2023	0(O) -	0/4
1013	KARGIL-ZANSKR PACKAGE-3 - [N24001345]NHIDCL,LADAKH , EPC	08/2020	381.01 -	381.01	8.23	01/2023 -	01/2023	0(O) -	0/4
1014	KARGIL-ZANSKR PACKAGE-6 - [N24001346]NHIDCL,LADAKH , EPC	01/2021	239.81 -	239.81	36.62	05/2024 -	05/2024	0(O) -	1/4
1015	KARGIL-ZANSKR PACKAGE-7 - [N24001347]NHIDCL,LADAKH , EPC	01/2021	308.86 -	308.86	38.81	06/2024 -	06/2024	0(O) -	1/4
1016	KARGIL-ZANSKR PACKAGE-8 - [N24001348]NHIDCL,LADAKH , EPC	03/2021	398.37 -	398.37	9.04	01/2023 -	01/2023	0(O) -	0/4
1017	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1018	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
1019	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	297.87	- 03/2021	03/2022	- 0	0/0
1020	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	392.42	04/2015 -	-	-	0/0
1021	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	686.13	669.94	-	-	-	0/0
1022	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	691.38	669.35	-	-	-	0/0
1023	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	457.34	01/2020 06/2021	01/2022	24(O) 1	0/0
1024	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 927.73	927.73	773.30	02/2020 08/2021	01/2022	23(O) 1	0/0
1025	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	867.83	-	-	-	0/0
1026	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1027	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1028	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	742.47	-	-	-	0/0
1029	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADHYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	409.70	08/2017 06/2021	12/2022	64(O) 0	0/0
1030	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	193.99	01/2019 -	-	-	4/4
1031	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	485.68	10/2017 -	-	-	4/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1032	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	215.49	09/2017 -	-	-	4/4
1033	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	718.56	09/2017 11/2021	12/2021	51(O) 0	3/4
1034	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	293.31	- -	03/2022	- -	4/4
1035	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	415.50	- -	-	-	0/0
1036	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	02/2022	47(O) 2	0/0
1037	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 174.90	174.90	154.26	08/2018 08/2021	02/2022	42(O) 2	0/0
1038	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	67.54	03/2018 03/2022	04/2022	49(O) 0	0/0
1039	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	132.76	02/2018 09/2021	02/2022	48(O) 2	0/0
1040	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	133.46	03/2017 12/2021	02/2022	59(O) 2	0/0
1041	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	80.06	03/2018 09/2021	06/2022	51(O) 0	0/0
1042	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 -	226.88	182.97	08/2018 09/2021	02/2022	42(O) 2	0/0
1043	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	167.53	03/2018 10/2021	02/2022	47(O) 2	0/0
1044	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	219.86	07/2018 08/2021	02/2022	43(O) 2	0/0
1045	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	187.73	02/2018 03/2022	03/2022	49(O) 0	0/0
1046	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	231.61	03/2018 11/2021	01/2022	46(O) 1	0/0
1047	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	238.66	09/2019 09/2021	12/2021	27(O) 0	0/0
1048	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	635.00	07/2018 05/2021	01/2022	42(O) 1	0/0
1049	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 949.54	949.54	794.73	06/2019 04/2021	01/2022	31(O) 1	0/0
1050	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	322.21	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1051	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MORTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	404.69	03/2018 06/2021	02/2022	47(O) 2	0/0
1052	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MORTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	139.54	03/2021 11/2021	03/2022	12(O) 0	0/0
1053	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	490.00	- -	12/2021	- -	2/3
1054	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	422.00	- -	11/2022	- -	2/4
1055	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	790.00	- -	02/2022	- -	2/4
1056	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODMI - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	609.00	- -	10/2022	- -	2/4
1057	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	763.00	12/2019 -	12/2021	24(O) -	2/3
1058	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	570.00	03/2020 -	04/2022	25(O) -	2/3
1059	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	605.00	05/2020 -	05/2022	24(O) -	2/3
1060	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	647.00	03/2020 -	-	-	2/3
1061	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	716.00 -	716.00	59.57	07/2021 -	-	-	0/0
1062	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,641.30	03/2013 -	03/2022	108(O) -	0/0
1063	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1064	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MORTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	106.56	- -	-	-	0/4
1065	REHABILITATION AND UPGRADE OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MORTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	303.72	- -	-	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1066	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	112.51	- -	-	-	0/0
1067	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	410.01	05/2018 11/2020	11/2020	-	1/1
1068	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	744.73	706.78	05/2018 03/2022	03/2022	46(O) 0	0/0
1069	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 717.24	717.24	627.25	05/2018 06/2022	06/2022	49(O) 3	0/1
1070	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	238.84	03/2019 12/2021	06/2022	39(O) 0	0/0
1071	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	451.92	05/2018 04/2019	06/2021	-	0/1
1072	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0
1073	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	867.97	11/2016 -	-	-	0/0
1074	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1075	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29(O) -	0/0
1076	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29(O) -	0/0
1077	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MORTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	978.04	- -	-	-	0/0
1078	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MORTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	334.55	- -	-	-	0/0
1079	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	1,183.14	- 10/2021	12/2021	- 0	3/4
1080	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	474.80	- 01/2022	04/2022	- 0	2/4
1081	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	184.80	03/2019 -	-	-	0/0
1082	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	148.83	03/2019 -	-	-	0/0
1083	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	359.60	340.15	- 12/2016	05/2017	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1084	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA ,	02/2017	904.16 911.07	904.16	.00	02/2020 03/2021	-	-	0/0
1085	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA ,	03/2017	247.02 -	157.49	31.97	03/2020 -	-	-	0/0
1086	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	-	-	0/0
1087	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	.00	03/2020 -	-	-	0/3
1088	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA ,	03/2017	988.34 -	1,043.28	.00	03/2020 -	-	-	3/3
1089	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	-	0/0
1090	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	-	-	0/0
1091	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	.00	03/2020 -	-	-	0/3
1092	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA ,	12/2017	404.94 499.70	448.18	495.92	- 05/2021	09/2021	-	0/0
1093	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA ,	01/2018	607.00 -	607.00	510.71	- -	08/2021	-	0/1
1094	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA ,	01/2018	621.00 -	621.00	595.00	- -	-	-	2/3
1095	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI, MAHARASHTRA , EPC	03/2018	291.53 -	291.53	242.03	- -	02/2022	-	0/0
1096	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI, MAHARASHTRA , EPC	03/2018	289.21 -	289.21	227.37	- -	01/2022	-	0/0
1097	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	62.08	- -	07/2021	-	0/0
1098	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA ,	03/2018	642.13 -	807.00	724.40	- -	-	-	0/0
1099	SARSAM TO KOTHARI - [N24001002]MoRTH, MAHARASHTRA ,	02/2016	545.64 -	545.64	189.43	07/2019 -	-	-	0/4
1100	AKOLA TO AKOT - [N24001003]MoRTH, MAHARASHTRA ,	01/2017	313.95 -	313.95	109.24	06/2019 -	-	-	0/4
1101	AKOT TO ANJANGAON - [N24001006]MoRTH, MAHARASHTRA ,	01/2017	245.77 246.00	245.77	219.50	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1102	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	160.15	05/2019 -	-	-	0/0
1103	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	314.20	05/2019 -	-	-	0/4
1104	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	230.03	05/2019 -	-	-	0/4
1105	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	401.46	06/2019 -	-	-	0/4
1106	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	240.98	06/2019 -	-	-	0/0
1107	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	258.29	06/2019 -	-	-	0/0
1108	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	234.67	06/2019 -	-	-	0/0
1109	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	321.02	06/2019 -	-	-	0/0
1110	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	154.69	06/2019 -	-	-	3/4
1111	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	274.75	06/2019 -	-	-	0/0
1112	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	265.78	06/2019 -	-	-	0/4
1113	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 397.00	396.91	289.79	06/2019 -	-	-	3/4
1114	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 364.00	363.82	65.03	09/2019 -	-	-	1/4
1115	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	261.86	06/2019 -	-	-	0/4
1116	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 -	457.52	352.94	07/2019 -	-	-	2/4
1117	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	269.58	07/2019 -	-	-	3/4
1118	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	82.35	05/2019 -	-	-	1/4
1119	SHAHAPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	59.88	12/2019 -	-	-	1/4
1120	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	121.71	12/2019 -	-	-	0/4
1121	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	228.75	08/2019 -	-	-	2/4
1122	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	303.09	08/2019 -	-	-	2/4
1123	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	159.32	08/2019 -	-	-	2/4
1124	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	273.48	05/2019 -	-	-	0/4
1125	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	308.66	07/2019 -	-	-	2/4
1126	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	269.24	07/2019 -	-	-	2/4
1127	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	263.13	12/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1128	KAJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	304.78	07/2019 -	-	-	2/4
1129	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	9.66	05/2020 -	-	-	0/4
1130	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	130.60	-	-	-	0/4
1131	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	326.81	11/2019 -	-	-	2/4
1132	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	130.63	07/2019 -	-	-	2/4
1133	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	262.66	12/2019 -	-	-	0/4
1134	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	195.05	05/2020 -	-	-	0/4
1135	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	467.78	06/2019 -	-	-	0/4
1136	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	204.36	11/2019 -	-	-	0/4
1137	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	210.81	07/2019 -	-	-	0/4
1138	BHADGAON TO CHALSGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	204.49	11/2019 -	-	-	0/0
1139	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	151.60	07/2019 -	-	-	0/0
1140	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	220.46	12/2019 -	-	-	0/4
1141	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	128.89	12/2019 -	-	-	0/4
1142	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	143.39	12/2019 -	-	-	0/4
1143	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	166.31	12/2019 -	-	-	0/4
1144	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	197.17	06/2019 -	-	-	0/4
1145	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	116.92	11/2019 -	-	-	0/4
1146	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	223.81	07/2019 -	-	-	0/4
1147	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	302.13	07/2019 -	-	-	0/0
1148	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	194.17	06/2019 -	-	-	0/4
1149	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	136.94	12/2019 -	-	-	0/4
1150	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	97.86	12/2019 -	-	-	0/4
1151	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	138.05	12/2019 -	-	-	0/4
1152	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	107.85	12/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1153	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	219.86	12/2019 -	-	-	0/4
1154	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	111.20	02/2020 -	-	-	0/4
1155	DHANGRIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	137.57	02/2020 -	-	-	0/4
1156	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	177.80	12/2019 -	-	-	0/4
1157	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	203.39	12/2019 -	-	-	0/4
1158	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	218.03	12/2019 -	-	-	0/4
1159	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	133.93	12/2019 -	-	-	1/4
1160	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	456.93	09/2019 -	-	-	1/4
1161	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	137.99	12/2019 -	-	-	2/4
1162	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	173.39	08/2020 -	-	-	0/4
1163	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	137.37	12/2019 -	-	-	0/4
1164	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	159.42	08/2020 -	-	-	0/0
1165	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	155.48	12/2019 -	-	-	0/0
1166	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	161.25	08/2020 -	-	-	0/4
1167	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	146.73	12/2019 -	-	-	0/0
1168	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	199.34	12/2019 -	-	-	2/4
1169	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	88.39	12/2019 -	-	-	0/0
1170	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	208.76	06/2020 -	-	-	1/4
1171	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	174.63	12/2019 -	-	-	0/0
1172	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	139.25	12/2019 -	-	-	1/4
1173	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	52.22	12/2019 -	-	-	0/0
1174	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	242.32	12/2019 -	-	-	2/4
1175	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	159.96	05/2020 -	-	-	0/4
1176	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	249.13	06/2019 -	-	-	0/4
1177	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	159.96	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1178	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	156.87	11/2019 -	-	-	0/4
1179	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	-	-	0/0
1180	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	196.00	12/2019 -	-	-	0/4
1181	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	257.83	07/2019 -	-	-	0/4
1182	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	552.31	12/2019 02/2022	02/2022	26(O) 2	0/0
1183	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	284.02	07/2019 -	-	-	0/4
1184	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	192.24	12/2019 -	-	-	0/0
1185	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	170.33	03/2019 -	-	-	0/0
1186	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	199.61	- -	-	-	0/0
1187	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	189.64	03/2019 -	-	-	0/0
1188	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	45.13	05/2020 -	-	-	0/4
1189	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	160.37	12/2019 -	-	-	1/4
1190	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	233.89	07/2019 -	-	-	0/4
1191	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	470.17	08/2019 -	-	-	0/4
1192	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	190.69	07/2019 -	-	-	0/4
1193	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	170.80	07/2019 -	-	-	0/4
1194	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	174.16	07/2019 -	-	-	0/4
1195	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	191.12	06/2019 -	-	-	2/4
1196	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	201.73	03/2019 -	-	-	0/4
1197	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	97.70	03/2018 -	-	-	0/4
1198	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	9.66	05/2020 -	-	-	0/4
1199	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	145.87	12/2019 -	-	-	0/4
1200	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	164.16	12/2019 -	-	-	0/4
1201	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	167.95	04/2020 -	-	-	1/4
1202	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	74.00	04/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1203	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	172.47	09/2019 -	-	-	2/4
1204	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	139.71	09/2018 -	-	-	0/4
1205	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	791.90	12/2019 -	-	-	1/4
1206	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	1,039.81	11/2019 -	-	-	1/4
1207	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	333.22	06/2019 -	-	-	2/4
1208	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	59.85	07/2019 -	-	-	1/4
1209	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	178.97	06/2019 -	-	-	0/4
1210	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.40	07/2019 -	-	-	0/4
1211	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	210.10	11/2018 -	-	-	0/4
1212	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	155.96	06/2019 -	-	-	0/4
1213	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	186.62	06/2019 -	-	-	0/4
1214	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	330.00	06/2019 -	-	-	0/4
1215	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	232.56	06/2019 -	-	-	0/4
1216	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	325.92	06/2019 -	-	-	0/4
1217	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.64	06/2019 -	-	-	0/0
1218	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	169.64	07/2019 -	-	-	0/4
1219	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	295.35	06/2021 -	-	-	1/4
1220	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	725.27	12/2019 -	-	-	1/4
1221	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	631.68	11/2019 -	-	-	1/4
1222	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	840.10	02/2019 -	-	-	0/0
1223	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-	-	2/4
1224	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-	-	3/5
1225	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	85.47	06/2019 -	-	-	1/4
1226	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	246.86	12/2019 -	-	-	0/0
1227	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 -	313.58	192.50	04/2020 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1228	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA , EPC	02/2019	731.89 731.89	732.34	316.43	11/2019 -	-	-	0/0
1229	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA , EPC	02/2019	362.46 362.46	362.46	227.50	11/2019 -	-	-	0/0
1230	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA , EPC	02/2019	594.75 594.75	606.75	200.10	11/2019 -	-	-	0/0
1231	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	-	4/4
1232	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL,MANIPUR , EPC	03/2019	471.00 -	471.00	167.94	07/2022 -	07/2022	0(O) -	2/4
1233	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL,MANIPUR , EPC	03/2020	292.24 -	292.24	39.42	06/2022 -	06/2022	0(O) -	1/4
1234	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL,MANIPUR , EPC	06/2020	365.53 -	365.53	53.11	08/2022 -	08/2022	0(O) -	1/4
1235	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL,MANIPUR , EPC	03/2020	167.95 -	167.95	30.07	06/2022 -	06/2022	0(O) -	1/4
1236	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL,MANIPUR , EPC	07/2020	177.76 -	177.76	25.27	08/2022 -	08/2022	0(O) -	1/4
1237	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL,MANIPUR , EPC	08/2020	379.39 -	379.39	8.67	04/2022 -	04/2022	0(O) -	0/4
1238	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL,MANIPUR , EPC	08/2020	268.98 -	268.98	.00	04/2022 -	04/2022	0(O) -	0/4
1239	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL,MANIPUR , EPC	08/2020	228.97 -	228.97	.00	04/2022 -	04/2022	0(O) -	0/4
1240	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]NHIDCL,MANIPUR , EPC	03/2020	167.95 -	167.95	50.50	06/2022 -	06/2022	0(O) -	2/4
1241	MARIAM - PEREN PKG-1A - [N24001349]NHIDCL,MANIPUR , EPC	02/2021	226.32 -	226.32	.00	12/2022 -	12/2022	0(O) -	0/4
1242	MARIAM - PEREN (PKG 1B) - [N24001350]NHIDCL,MANIPUR , EPC	02/2021	188.36 -	188.36	.00	12/2022 -	12/2022	0(O) -	0/4
1243	MARIAM - PEREN PKG-2B - [N24001351]NHIDCL,MANIPUR , EPC	02/2021	232.26 -	232.26	.00	12/2022 -	12/2022	0(O) -	0/4
1244	IMPHAL – MOREH PACKAGE- 3 - [N24001352]NHIDCL,MANIPUR , EPC	03/2021	259.31 -	259.31	35.84	12/2022 -	12/2022	0(O) -	1/4
1245	IMPHAL - KHONGSANG PKG-2 - [N24001353]NHIDCL,MANIPUR , EPC	03/2021	195.14 -	195.14	.00	12/2022 -	12/2022	0(O) -	0/4
1246	TAMENGLONG - MAHUR PKG-3 - [N24001354]NHIDCL,MANIPUR , EPC	03/2021	234.08 -	234.08	9.86	12/2022 -	12/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1247	MARIAM - PEREN (PKG 2A) - [N24001398]NHIDCL,MANIPUR , EPC	07/2021	204.58 -	204.58	.00	03/2023 -	03/2023	0(O) -	0/0
1248	IMPHAL – MOREH (PACKAGE 4) - [N24001399]NHIDCL,MANIPUR , EPC	03/2021	277.99 -	277.99	.00	01/2023 -	01/2023	0(O) -	0/0
1249	SENAPATI- IMPHAL PKG-5B - [N24001400]NHIDCL,MANIPUR , EPC	03/2021	211.70 -	211.70	.00	01/2023 -	01/2023	0(O) -	0/4
1250	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR , EPC	07/2021	467.00 -	467.00	.00	03/2023 -	03/2023	0(O) -	0/0
1251	TAMENGLONG - MAHUR PKG-1 - [N24001402]NHIDCL,MANIPUR , EPC	07/2021	185.80 -	185.80	.00	03/2023 -	03/2023	0(O) -	0/0
1252	TAMENGLONG - MAHUR PKG-2 - [N24001403]NHIDCL,MANIPUR , EPC	07/2021	483.87 -	483.87	12.11	03/2023 -	03/2023	0(O) -	0/0
1253	TAMENGLONG - MAHUR PKG-4 - [N24001404]NHIDCL,MANIPUR , EPC	07/2021	198.77 -	198.77	.00	03/2023 -	03/2023	0(O) -	0/0
1254	CHURACHANPUR TUIVAI PKG-3 - [N24001405]NHIDCL,MANIPUR , EPC	07/2021	673.27 -	673.27	.00	10/2023 -	10/2023	0(O) -	0/0
1255	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 -	-	-	0/0
1256	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	198.39	- 09/2021	09/2021	-	2/4
1257	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	133.81	05/2019 -	03/2022	34(O) -	2/4
1258	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]NHIDCL,MEGHALAYA , EPC	11/2020	351.12 -	351.12	171.37	12/2023 -	12/2023	0(O) -	0/4
1259	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]NHIDCL,MEGHALAYA , EPC	11/2020	525.68 -	525.68	288.84	12/2023 -	12/2023	0(O) -	0/4
1260	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]NHIDCL,MEGHALAYA , EPC	11/2020	445.51 -	445.51	173.17	12/2023 -	12/2023	0(O) -	1/4
1261	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]NHIDCL,MEGHALAYA , EPC	11/2020	284.21 -	284.21	40.21	12/2023 -	12/2023	0(O) -	0/4
1262	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]NHIDCL,MEGHALAYA , EPC	10/2020	157.86 -	157.86	55.86	04/2022 -	04/2022	0(O) -	1/4
1263	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]NHIDCL,MEGHALAYA , EPC	03/2021	260.21 -	260.21	42.62	12/2022 -	12/2022	0(O) -	0/4
1264	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41,109.88	992.67	978.43	03/2011 12/2022	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1265	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 374.59	327.92	323.23	10/2010 12/2022	-	-	0/0
1266	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 434.65	377.99	368.39	10/2010 12/2022	-	-	0/0
1267	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	98.33	09/2019 -	04/2023	43(O) -	1/4
1268	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	107.05	09/2019 06/2023	07/2023	46(O) 0	1/4
1269	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	115.64	09/2019 04/2023	06/2023	45(O) 0	1/4
1270	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	128.15	09/2019 04/2023	04/2023	43(O) 0	1/4
1271	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	142.87	09/2019 06/2023	04/2023	43(O) 0	1/4
1272	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	137.11	09/2019 04/2023	06/2023	45(O) 0	1/4
1273	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	51.36	09/2019 03/2024	04/2024	55(O) 0	0/4
1274	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	90.39	09/2019 09/2023	09/2023	48(O) 0	1/4
1275	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	308.85	09/2014 12/2021	-	-	0/0
1276	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM ,	01/2017	205.95 -	205.95	123.24	01/2021 -	11/2021	-	0/0
1277	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM , EPC	09/2020	275.02 -	275.02	27.90	10/2022 -	10/2022	0(O) -	1/4
1278	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM , EPC	03/2020	206.88 -	206.88	33.21	07/2022 -	07/2022	0(O) -	1/4
1279	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM , EPC	03/2020	216.49 -	216.49	59.06	07/2022 -	07/2022	0(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1280	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM , EPC	03/2020	292.24 -	292.24	59.29	07/2022 -	07/2022	0(O) -	0/4
1281	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM , EPC	03/2020	281.78 -	281.78	120.63	07/2022 -	07/2022	0(O) -	2/4
1282	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]NHIDCL,MIZORAM , EPC	03/2021	374.39 -	374.39	43.01	12/2022 -	12/2022	0(O) -	0/4
1283	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]NHIDCL,MIZORAM , EPC	03/2021	233.25 -	233.25	12.72	12/2022 -	12/2022	0(O) -	0/4
1284	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]NHIDCL,MIZORAM , EPC	03/2021	674.71 -	674.71	34.80	06/2023 -	06/2023	0(O) -	0/4
1285	TLABUNG - LUNGLEI PKG-A - [N24001358]NHIDCL,MIZORAM , EPC	03/2021	698.44 -	698.44	.00	12/2022 -	12/2022	0(O) -	0/4
1286	TLABUNG - LUNGLEI PKG-B - [N24001359]NHIDCL,MIZORAM , EPC	03/2021	740.58 -	740.58	.00	01/2023 -	01/2023	0(O) -	0/4
1287	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	364.59	360.15	12/2009 09/2020	09/2020	-	0/0
1288	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1289	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1290	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014	12/2022	105(O)	0/0
1291	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	-	-	0/0
1292	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 1,928.22	1,928.22	1,890.04	04/2015 01/2021	12/2021	80(O) 0	3/4
1293	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,665.00	- -	-	-	0/0
1294	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	11/2021	-	0/0
1295	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	11/2018	-	0/0
1296	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	352.25	08/2016 -	05/2021	-	3/4
1297	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	311.17	08/2016 -	05/2021	-	3/4
1298	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	333.24	09/2018 -	03/2022	42(O) -	3/4
1299	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	132.56	09/2018 -	11/2022	50(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1300	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	182.63	09/2018 -	07/2022	46(O) -	2/4
1301	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	128.80	09/2018 -	05/2022	44(O) -	2/4
1302	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	100.70	09/2018 -	09/2022	48(O) -	2/4
1303	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	120.99	09/2018 -	12/2021	39(O) -	0/4
1304	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	125.87	09/2018 -	12/2021	39(O) -	0/4
1305	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	134.89	09/2018 -	11/2021	-	3/4
1306	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	157.06	09/2018 -	11/2021	-	3/4
1307	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	175.63	09/2018 -	11/2021	-	2/4
1308	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	112.26	09/2018 -	11/2021	-	1/4
1309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	77.62	09/2018 -	12/2021	39(O) -	1/4
1310	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	68.70	09/2018 -	10/2022	49(O) -	0/4
1311	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	118.61	12/2020 12/2021	-	-	0/0
1312	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	132.43	12/2020 12/2021	-	-	0/0
1313	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 369.96	369.96	322.13	09/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1314	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	104.81	11/2020 04/2022	-	-	0/0
1315	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	96.49	12/2022 -	07/2022	-5(O) -	0/0
1316	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND , EPC	09/2020	277.44 177.00	277.44	33.95	10/2022 -	10/2022	0(O) -	0/4
1317	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND , EPC	08/2020	202.36 118.56	202.36	7.02	04/2022 -	04/2022	0(O) -	0/4
1318	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND , EPC	09/2020	315.63 167.23	315.63	9.39	04/2022 -	04/2022	0(O) -	0/4
1319	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND , EPC	09/2020	257.15 -	257.15	52.44	04/2022 -	04/2022	0(O) -	1/4
1320	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND , EPC	03/2020	320.97 -	320.97	56.39	06/2022 -	06/2022	0(O) -	1/4
1321	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND , EPC	03/2020	355.79 -	355.79	70.73	06/2022 -	06/2022	0(O) -	1/4
1322	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND , EPC	03/2020	361.53 -	361.53	38.95	06/2022 -	06/2022	0(O) -	1/4
1323	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND , EPC	03/2020	330.78 -	330.78	67.50	12/2021 -	12/2021	0(O) -	1/4
1324	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND , EPC	03/2020	278.95 -	278.95	79.89	06/2022 -	06/2022	0(O) -	2/4
1325	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND , EPC	04/2020	330.80 -	330.80	49.90	12/2021 -	12/2021	0(O) -	1/4
1326	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]NHIDCL,NAGALAND , EPC	03/2020	206.53 -	206.53	81.84	06/2022 -	06/2022	0(O) -	2/4
1327	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]NHIDCL,NAGALAND , EPC	07/2021	258.52 -	258.52	20.00	03/2023 -	03/2023	0(O) -	0/0
1328	PEREN-DIMAPUR PKG-5 - [N24001407]NHIDCL,NAGALAND , EPC	02/2021	207.33 -	207.33	.00	03/2023 -	03/2023	0(O) -	0/0
1329	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	14.80	09/2014 -	-	-	0/0
1330	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,873.47	06/2014 -	-	-	0/0
1331	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	720.08	-	-	-	0/0
1332	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	284.66	-	03/2022	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1333	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	182.41	08/2015 -	-	-	0/0
1334	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	836.93	-	-	-	0/0
1335	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	637.56	08/2019 -	-	-	0/0
1336	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	1,125.65	-	-	-	0/0
1337	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	-	0/0
1338	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	101.27	06/2016 -	-	-	0/0
1339	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	1,058.45	03/2020 -	-	-	0/0
1340	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	225.64	07/2017 -	-	-	0/0
1341	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	290.00	-	-	-	0/0
1342	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	264.15	-	-	-	0/0
1343	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	473.95	-	03/2022	-	0/0
1344	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	413.00	-	-	-	0/0
1345	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	188.00	-	-	-	0/1
1346	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	330.58	-	08/2021	-	0/0
1347	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	394.94	-	-	-	0/1
1348	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	254.00	-	-	-	0/0
1349	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	512.80	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1350	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA ,	01/2018	999.00 -	999.00	178.93	- -	-	-	0/0
1351	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA ,	01/2018	503.88 -	503.88	138.56	- -	-	-	0/0
1352	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA , EPC	03/2018	806.11 -	806.11	415.39	- -	-	-	0/0
1353	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA - [N24000912]MoRTH, ODISHA ,	08/2016	287.70 -	287.70	216.18	02/2017 -	-	-	0/0
1354	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH, ODISHA ,	09/2016	295.67 -	295.67	208.91	02/2017 -	-	-	0/0
1355	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH, ODISHA ,	12/2016	223.50 -	223.50	144.36	08/2018 -	-	-	0/0
1356	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH, ODISHA ,	12/2016	206.88 -	206.88	127.72	04/2018 -	-	-	0/0
1357	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH, ODISHA ,	03/2018	214.23 -	214.23	115.67	08/2018 -	-	-	0/0
1358	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH, ODISHA ,	03/2018	199.16 -	199.16	124.19	08/2018 -	-	-	0/0
1359	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH, PUNJAB , EPC	11/2015	889.24 -	904.82	851.32	- -	-	-	0/0
1360	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB ,	09/2014	479.00 -	479.00	456.80	- -	03/2022	-	0/0
1361	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB ,	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	-	0/0
1362	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB ,	08/2016	1,169.61 - 1,367.00	2,280.00	1,367.00	- -	-	-	0/0
1363	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB ,	03/2017	754.54 -	756.27	449.44	03/2020 -	09/2022	30(O) -	0/0
1364	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB ,	02/2018	261.76 -	207.00	205.00	- -	02/2022	-	0/0
1365	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	- -	-	-	0/0
1366	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1367	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	201.14	08/2020 -	-	-	0/0
1368	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	734.04	10/2019 -	08/2021	-	0/0
1369	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 194.48	170.57	75.41	11/2020 -	-	-	0/0
1370	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	261.09	08/2020 -	-	-	0/0
1371	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414]NHAI,PUNJAB , EPC	12/2020	733.00 -	733.00	.00	01/2024 -	01/2024	0(O) -	0/0
1372	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB , EPC	12/2020	881.00 -	881.00	.00	04/2024 -	04/2024	0(O) -	0/0
1373	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB , EPC	12/2020	989.66 -	989.66	.00	01/2024 -	01/2024	0(O) -	0/0
1374	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB , EPC	12/2020	1,234.40 -	1,234.40	.00	04/2024 -	04/2024	0(O) -	0/0
1375	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB , EPC	12/2020	1,094.46 -	1,094.46	.00	04/2024 -	04/2024	0(O) -	0/0
1376	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]NHAI,PUNJAB , EPC	02/2021	1,269.96 -	1,269.96	.00	04/2024 -	04/2024	0(O) -	0/0
1377	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420]NHAI,PUNJAB , EPC	02/2021	853.66 -	853.66	.00	04/2024 -	04/2024	0(O) -	0/0
1378	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 -	-	-	0/0
1379	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	.00	10/2017 -	-	-	3/4
1380	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1381	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	12/2021	44(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1382	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1383	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	-	-	-	0/0
1384	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1385	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	191.80	06/2019 -	-	-	1/1
1386	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	690.17	06/2019 -	-	-	0/0
1387	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	870.48	-	-	-	0/0
1388	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1389	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,355.00	-	-	-	0/0
1390	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	1,513.48	-	03/2022	-	0/0
1391	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	23(O)	0/0
1392	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	964.60	10/2017 -	-	-	0/0
1393	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	330.46	-	-	-	0/0
1394	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	713.42	-	-	-	0/0
1395	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	307.43	-	-	-	0/0
1396	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	687.07	-	07/2021	-	0/0
1397	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 - 866.55	866.55	866.55	-	10/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1398	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	496.04	- -	-	-	0/0
1399	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	136.22	04/2018 -	-	-	3/4
1400	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	122.04	04/2018 -	07/2020	-	4/4
1401	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	328.41	06/2018 -	-	-	3/4
1402	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	242.67	05/2018 -	-	-	3/4
1403	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	164.94	- -	-	-	4/4
1404	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	216.79	08/2022 -	-	-	2/4
1405	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	69.53	08/2020 -	-	-	0/4
1406	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	51.56	11/2020 -	-	-	1/4
1407	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN , EPC	07/2020	319.09 -	319.09	12.89	09/2021 -	-	-	0/0
1408	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN , EPC	08/2020	216.72 -	216.72	44.71	12/2020 -	-	-	0/0
1409	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN , EPC	12/2020	379.23 -	379.23	16.94	10/2021 -	-	-	0/0
1410	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN , EPC	12/2020	339.65 -	339.65	28.53	10/2021 -	-	-	0/0
1411	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN , EPC	02/2021	240.99 -	240.99	.00	11/2021 -	11/2021	-	0/0
1412	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	295.14	10/2017 -	-	-	3/4
1413	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	76.23	- -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1414	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	154.83	11/2017 -	12/2021	49(O) -	2/4
1415	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	63.83	06/2018 -	-	-	1/4
1416	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM , EPC	03/2019	402.94 -	402.94	69.72	04/2022 -	04/2022	0(O) -	1/4
1417	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL,SIKKIM , EPC	08/2020	295.97 -	295.97	32.85	04/2023 -	04/2023	0(O) -	1/4
1418	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM , EPC	03/2020	242.97 -	242.97	59.98	06/2022 -	06/2022	0(O) -	1/4
1419	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]NHIDCL,SIKKIM , EPC	08/2020	311.00 -	311.00	26.51	04/2023 -	04/2023	0(O) -	0/4
1420	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]NHIDCL,SIKKIM , EPC	07/2020	345.38 -	345.38	86.64	04/2023 -	04/2023	0(O) -	0/4
1421	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]NHIDCL,SIKKIM , EPC	09/2020	183.31 -	183.31	76.84	05/2022 -	05/2022	0(O) -	0/4
1422	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]NHIDCL,SIKKIM , EPC	09/2020	262.84 -	262.84	120.72	05/2023 -	05/2023	0(O) -	0/4
1423	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]NHIDCL,SIKKIM , EPC	08/2020	292.80 -	292.80	42.83	05/2022 -	05/2022	0(O) -	0/4
1424	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM 27.200 (END OF RO - [N24001336]NHIDCL,SIKKIM , EPC	08/2020	230.45 -	230.45	2.58	04/2023 -	04/2023	0(O) -	0/4
1425	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]NHIDCL,SIKKIM , EPC	10/2020	493.42 -	493.42	.00	11/2023 -	11/2023	0(O) -	0/4
1426	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]NHIDCL,SIKKIM , EPC	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023	0(O) -	0/4
1427	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]NHIDCL,SIKKIM , EPC	01/2021	332.20 -	332.20	.00	09/2023 -	09/2023	0(O) -	0/4
1428	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]NHIDCL,SIKKIM , EPC	12/2020	410.60 -	410.60	.00	02/2024 -	02/2024	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1429	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-	-	0/0
1430	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	7.73	06/2013 -	09/2021	-	0/0
1431	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	81.67	05/2013 -	02/2022	105(O) -	0/0
1432	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	271.64	08/2013 -	-	-	0/0
1433	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	97.97	04/2014 -	01/2022	93(O) -	0/0
1434	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 273.27	268.92	229.77	08/2015 -	-	-	0/4
1435	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	-	-	0/0
1436	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	32.96	12/2017 -	05/2023	65(O) -	0/0
1437	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1438	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1439	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	434.59	08/2018 -	01/2022	41(O) -	0/0
1440	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	403.81	07/2018 -	12/2021	41(O) -	0/0
1441	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	252.08	03/2020 -	12/2021	21(O) -	0/0
1442	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	403.81	07/2016 -	12/2021	65(O) -	0/0
1443	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59(O) -	0/0
1444	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	178.41	09/2017 -	-	-	0/0
1445	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	810.81	09/2017 -	07/2022	58(O) -	0/0
1446	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	248.71	-	12/2021	-	0/0
1447	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,296.93	346.17	-	01/2022	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1448	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	255.05	- -	12/2022	- -	0/0
1449	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	397.89	- -	03/2022	- -	0/0
1450	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	-	0/0
1451	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	339.86	- -	01/2022	- -	0/0
1452	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	12/2021	- -	0/0
1453	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU ,	03/2019	297.55 -	297.55	210.16	11/2019 -	-	-	3/4
1454	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 204.73	240.38	143.36	06/2019 -	-	-	3/4
1455	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU , EPC	07/2020	3,426.00 -	3,426.00	.00	12/2021 -	12/2021	0(O) -	0/0
1456	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU , EPC	08/2020	302.62 -	302.62	60.72	02/2021 -	-	-	1/4
1457	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0
1458	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	.00	03/2016 -	-	-	1/4
1459	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA- JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA , EPC	10/2014	295.47 -	295.47	207.71	02/2017 -	-	-	0/1
1460	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0
1461	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,056.08	1,020.25	11/2018 -	01/2022	38(O) -	0/0
1462	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1463	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	476.01	- -	-	-	0/0
1464	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	686.45	- -	-	-	0/0
1465	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	336.39	- -	-	-	0/0
1466	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1467	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	121.49	02/2019 -	-	-	0/0
1468	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	125.54	03/2019 -	-	-	0/0
1469	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	166.39	05/2019 -	-	-	0/0
1470	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	116.79	10/2019 -	-	-	0/0
1471	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	244.54	12/2019 -	-	-	0/0
1472	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	303.83	05/2019 -	-	-	0/0
1473	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	205.91	05/2019 -	-	-	0/0
1474	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH- SAMSHABAD SECTION) OF HYDERABAD- SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	153.40	05/2020 -	-	-	0/0
1475	WIDENING AND STRENGTHENING OF EXISTING 2- LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	219.16	12/2019 -	-	-	0/0
1476	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA ,	02/2018	206.13 -	206.13	184.68	06/2020 -	-	-	0/0
1477	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA ,	02/2018	294.13 -	294.13	154.02	11/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1478	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA ,	02/2018	220.28 -	220.28	160.80	11/2019 -	-	-	0/0
1479	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA ,	02/2018	426.52 -	426.52	394.24	04/2020 -	-	-	0/0
1480	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA ,	03/2018	322.81 -	322.81	219.66	09/2020 -	-	-	0/0
1481	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA ,	03/2018	626.76 -	626.76	214.79	07/2020 -	-	-	0/0
1482	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA ,	01/2017	605.08 -	605.08	409.44	10/2019 -	-	-	0/0
1483	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA ,	03/2018	192.67 -	192.67	165.01	07/2019 -	-	-	0/0
1484	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA ,	01/2019	193.19 -	193.19	110.26	-	-	-	0/0
1485	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	358.78	03/2018 -	-	-	3/4
1486	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA ,	10/2016	171.90 -	171.90	142.81	08/2020 -	11/2021	-	0/0
1487	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA , EPC	03/2020	247.76 -	247.76	27.82	01/2022 -	01/2022	0(O) -	1/4
1488	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA , EPC	06/2020	347.36 -	347.36	89.80	01/2022 -	01/2022	0(O) -	2/4
1489	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA , EPC	06/2020	277.50 -	277.50	106.99	01/2022 -	01/2022	0(O) -	1/4
1490	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]NHIDCL,TRIPURA , EPC	03/2020	154.51 -	154.51	42.33	07/2022 -	07/2022	0(O) -	1/4
1491	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL,TRIPURA , EPC	03/2020	178.43 -	178.43	17.99	07/2022 -	07/2022	0(O) -	1/4
1492	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA , EPC	01/2017	197.67 -	236.18	59.74	12/2022 -	12/2022	0(O) -	0/0
1493	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]NHIDCL,TRIPURA , EPC	11/2020	332.14 -	332.14	10.88	07/2022 -	07/2022	0(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1494	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]NHIDCL,TRIPURA , EPC	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022	0(O) -	0/4
1495	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]NHIDCL,TRIPURA , EPC	11/2020	280.91 -	280.91	90.44	07/2022 -	07/2022	0(O) -	2/4
1496	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]NHIDCL,TRIPURA , EPC	11/2020	206.78 -	206.78	65.92	07/2022 -	07/2022	0(O) -	1/4
1497	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA , EPC	06/2020	201.99 -	201.99	18.87	01/2022 -	01/2022	0(O) -	0/4
1498	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]NHIDCL,TRIPURA , EPC	09/2020	173.17 -	173.17	9.33	04/2022 -	04/2022	0(O) -	1/4
1499	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]NHIDCL,TRIPURA , EPC	06/2020	257.96 -	257.96	95.22	01/2022 -	01/2022	0(O) -	3/4
1500	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]NHIDCL,TRIPURA , EPC	03/2020	165.54 -	165.54	8.23	07/2022 -	07/2022	0(O) -	1/4
1501	MANU-SIMLUNG (PKG 4) - [N24001363]NHIDCL,TRIPURA , EPC	03/2021	354.79 -	354.79	10.23	12/2022 -	12/2022	0(O) -	0/4
1502	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	-	-	0/0
1503	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	469.31	459.07	01/2014 -	-	-	0/0
1504	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-	-	0/0
1505	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH , EPC	01/2014	282.41 319.96	319.96	193.56	03/2016 04/2022	04/2022	73(O) 0	0/0
1506	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1507	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	417.68	433.68	01/2016 -	-	-	0/0
1508	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	242.70	09/2016 -	-	-	0/0
1509	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	627.93	633.24	01/2016 -	-	-	0/0
1510	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1511	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1512	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1513	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1514	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1515	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	141.33	08/2015 -	01/2021	-	0/0
1516	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	987.94	.00	-	-	-	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1517	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	985.40	04/2019 -	-	-	0/0
1518	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	-	-	-	0/0
1519	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	-	-	-	0/0
1520	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1521	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	453.62	04/2019 10/2022	-	-	0/0
1522	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	-	-	-	0/0
1523	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 827.05	827.05	387.83	- 07/2022	07/2022	- 0	0/0
1524	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 1,201.51	1,201.51	1,077.55	- 06/2021	09/2021	-	0/0
1525	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1526	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	-	-	-	0/0
1527	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	-	-	-	0/0
1528	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	1,322.40	03/2020 12/2021	12/2021	21(O) 0	3/4
1529	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,297.83	03/2020 -	-	-	3/4
1530	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	772.56	03/2020 -	-	-	0/0
1531	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1532	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	1,084.94	- -	-	-	0/0
1533	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1534	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1535	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1536	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	75.10	- -	-	-	0/0
1537	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	886.68	- -	-	-	0/0
1538	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	1,176.70	- -	-	-	0/0
1539	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	-	0/0
1540	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,315.69	- -	-	-	0/0
1541	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,525.15	- -	-	-	0/0
1542	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	222.94	- -	-	-	0/0
1543	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	332.69	- -	-	-	0/0
1544	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0
1545	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	137.80	- -	03/2022	-	0/0
1546	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	145.76	09/2019 -	10/2019	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1547	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	-	0/0
1548	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	229.57	05/2019 -	04/2021	-	0/0
1549	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	1,720.10	01/2019 -	-	-	0/0
1550	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	147.70	03/2020 03/2020	03/2021	-	0/0
1551	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	183.54	10/2019 -	03/2021	-	0/0
1552	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	188.89	04/2020 -	03/2022	23(O) -	0/0
1553	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	124.69	02/2020 -	01/2021	-	0/0
1554	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	19(O) -	0/0
1555	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	237.81	09/2020 -	12/2021	15(O) -	0/0
1556	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	195.70	- -	01/2022	- -	0/0
1557	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	319.96	117.56	- -	03/2022	- -	0/0
1558	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH , EPC	10/2020	724.60 720.81	724.60	.00	03/2023 -	03/2023	0(O) -	0/0
1559	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]MoRTH,UTTAR PRADESH , EPC	07/2018	1,948.25 -	1,948.25	277.20	02/2024 -	02/2024	0(O) -	0/0
1560	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	-	-	0/0
1561	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	207.78	- 10/2022	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1562	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	- -	-	-	0/0
1563	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	723.26	07/2018 02/2022	-	-	0/0
1564	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	131.95	05/2018 -	03/2022	46(O) -	3/4
1565	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	220.25	06/2018 -	03/2022	45(O) -	3/4
1566	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	265.48	05/2018 -	03/2022	46(O) -	3/4
1567	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	214.90	12/2019 07/2021	07/2021	-	0/0
1568	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	185.44	12/2019 07/2021	07/2021	-	0/0
1569	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	234.12	12/2019 08/2021	08/2021	-	0/0
1570	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	207.83	06/2019 12/2021	12/2021	30(O) 0	0/0
1571	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	171.22	11/2019 07/2021	07/2021	-	0/0
1572	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	259.90	11/2019 05/2021	05/2021	-	0/0
1573	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	186.16	11/2019 10/2020	10/2020	-	0/0
1574	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	287.56	02/2020 09/2021	09/2021	-	0/0
1575	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	183.73	- 10/2021	10/2021	-	0/0
1576	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021	19(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1577	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	116.25	- -	-	-	0/0
1578	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	299.10	07/2018 -	07/2022	48(O) -	2/5
1579	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	234.88	174.51	12/2017 12/2020	12/2020	-	0/0
1580	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	01/2022	101(O) -	3/4
1581	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,893.57	08/2013 -	06/2023	118(O) -	3/4
1582	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	1,396.18	09/2014 -	-	-	0/0
1583	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 363.93	363.93	277.34	- -	-	-	0/0
1584	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 2,587.75	1,827.15	989.55	06/2018 -	-	-	0/0
1585	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	2,360.65	4,511.67	- -	-	-	0/0
1586	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	704.89	08/2018 -	-	-	0/0
1587	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 2,145.96	1,952.20	97.16	- -	-	-	0/0
1588	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH, WEST BENGAL ,	03/2016	271.17 291.20	291.20	120.51	11/2018 01/2021	03/2022	40(O) 0	0/0
1589	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	277.42	09/2019 11/2021	10/2021	-	0/0
1590	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	254.43	09/2020 01/2022	01/2022	16(O) 0	0/0
1591	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	113.26	11/2020 04/2021	06/2021	-	0/0
1592	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 254.30	254.30	118.39	10/2020 03/2021	06/2021	-	0/0
1593	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 213.97	213.97	27.15	08/2019 -	11/2022	39(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1594	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL ,	06/2016	236.78 263.26	263.26	78.47	08/2019 08/2022	08/2022	36(O) 0	0/0
1595	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL ,	04/2014	279.70 398.52	398.52	331.86	08/2017 -	02/2020	-	0/0
	Total		5,37,828.12 -	5,53,848.05	3,35,150.64				490/1510
	<u>SHIPPING AND PORTS</u>								
1596	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE ,	01/2018	5,369.18 4,633.81	4,633.81	1,967.38	03/2023 -	03/2023	0(O) -	1/7
	Total		5,369.18 -	4,633.81	1,967.38				1/7
	<u>TELECOMMUNICATIONS</u>								
1597	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI ,	10/2014	248.20 -	248.20	155.97	03/2018 -	01/2022	46(O) -	3/5
1598	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 24,664.00	24,664.00	20,545.00	07/2015 05/2020	03/2022	80(O) 0	0/0
1599	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE , Central Sector Projects	03/2020	431.16 422.87	422.87	70.25	06/2021 11/2021	03/2022	9(O) 0	0/0
	Total		14,013.36 -	25,335.07	20,771.22				3/5
	<u>URBAN DEVELOPMENT</u>								
1600	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR ,	02/2019	13,365.77 -	13,925.50	306.94	06/2024 -	06/2024	0(O) -	0/0
1601	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH ,	05/2019	299.97 299.97	299.97	27.44	09/2020 01/2023	01/2023	28(O) 0	0/6
1602	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	39,619.40	03/2016 08/2021	-	-	1/1
1603	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 217.00	217.00	187.08	04/2019 02/2022	02/2022	34(O) 0	1/2
1604	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	974.86	- -	12/2022	- -	0/9
1605	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 238.56	238.56	208.57	05/2020 01/2022	01/2022	20(O) 0	2/2
1606	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 422.00	422.00	135.75	03/2021 06/2023	06/2023	27(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1607	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 392.00	392.00	196.68	08/2020 06/2022	06/2022	22(O) 0	2/5
1608	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASपुरI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 1,100.80	1,100.80	35.90	07/2021 06/2023	06/2023	23(O) 0	0/6
1609	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 1,128.00	1,128.00	30.00	03/2022 -	06/2023	15(O) -	0/0
1610	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	2,711.33	03/2025 -	03/2025	0(O) -	0/1
1611	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	484.47	12/2020 09/2021	-	-	1/1
1612	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	9,834.10	12/2018 -	08/2022	44(O) -	0/1
1613	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	419.43	03/2024 -	03/2024	0(O) -	0/1
1614	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	373.31	03/2024 -	03/2024	0(O) -	0/1
1615	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 30,695.12	30,695.12	19,410.15	02/2019 03/2025	03/2025	73(O) 0	155/249
1616	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151]BMRL,KARNATAKA , EPC	06/2021	14,788.10 -	14,788.10	2,031.41	06/2026 -	06/2026	0(O) -	0/76
1617	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 6,218.14	6,218.14	6,065.82	07/2017 09/2020	09/2020	-	0/0
1618	BHOPAL METRO RAIL - [N28000124]MPMRL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	354.67	02/2023 -	02/2023	0(O) -	0/0
1619	INDORE METRO RAIL - [N28000125]MPMRL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	190.69	02/2023 -	02/2023	0(O) -	0/0
1620	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	8,443.80	03/2018 12/2021	12/2021	45(O) 0	0/0
1621	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	33,406.00	20,051.98	03/2020 03/2023	03/2023	36(O) 0	0/0
1622	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 11,420.00	11,420.00	7,565.74	11/2021 12/2022	12/2022	13(O) 0	0/0
1623	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	6,074.70	06/2025 -	06/2025	0(O) -	0/8
1624	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 18,380.00	18,380.00	17,619.68	12/2015 02/2019	02/2019	-	24/24
1625	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	3,006.98	03/2018 02/2021	02/2021	-	8/21
1626	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	6,928.00	03/2019 -	03/2019	-	0/0
1627	KANPUR METRO RAIL PROJECT - [N28000144]LMRL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	2,391.78	03/2024 -	03/2025	12(O) -	0/0
1628	AGRA METRO RAIL PROJECT - [N28000145]LMRL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	506.47	03/2024 -	05/2025	14(O) -	0/0
	Total		2,91,275.10 -	3,13,165.63	1,56,187.13				194/414

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>WATER RESOURCES</u>								
1629	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	18,335.60	03/2020 11/2021	04/2022	25(O) 0	0/19
1630	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL FOR WATER,BIHAR ,	10/2005	956.00 -	721.37	712.37	03/2015 -	-	-	5/7
1631	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	98.70	07/2021 -	04/2022	9(O) -	0/0
1632	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	413.29	.05	09/2020 -	03/2024	42(O) -	0/0
1633	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	60.61	12/2020 06/2021	07/2022	19(O) 0	0/0
1634	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	28.31	08/2021 -	04/2023	20(O) -	0/0
1635	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	26.45	10/2021 -	12/2023	26(O) -	0/0
1636	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	398.90	294.30	03/2020 -	02/2022	23(O) -	0/0
1637	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	338.67	01/2021 -	03/2022	14(O) -	0/0
1638	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	137.32	04/2021 -	04/2022	12(O) -	0/0
1639	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	65.53	11/2020 03/2021	12/2021	13(O) 0	0/0
1640	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	247.01	05/2021 -	06/2022	13(O) -	0/0
1641	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	42.75	06/2022 -	12/2022	6(O) -	0/0
1642	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	96.39	06/2022 -	12/2022	6(O) -	0/0
1643	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	665.78	251.88	12/2022 -	12/2022	0(O) -	0/0
1644	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	108.28	12/2021 -	12/2022	12(O) -	0/0
1645	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	160.52	02/2022 -	12/2022	10(O) -	0/0
1646	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	345.58	01/2021 -	12/2021	11(O) -	0/0
1647	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1648	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPP,MAHARASHTRA ,	03/2017	233.57 -	233.57	148.83	12/2019 -	12/2021	24(O) -	0/0
1649	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	132.29	09/2021 -	03/2022	6(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1650	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 261.12	261.12	.00	03/2022 -	04/2024	25(O) -	0/0
1651	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	96.64	09/2021 -	12/2021	3(O) -	0/0
1652	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	03/2024	31(O) -	0/0
1653	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	248.16	12/2020 -	12/2021	12(O) -	0/0
1654	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 330.05	330.05	260.12	12/2019 -	11/2021	-	0/0
1655	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	28.36	12/2021 -	12/2022	12(O) -	0/0
1656	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	80.97	10/2021 -	03/2022	5(O) -	0/0
1657	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	690.71	.00	06/2022 -	04/2024	22(O) -	0/0
1658	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 213.91	213.91	.00	07/2021 -	03/2024	32(O) -	0/0
1659	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	85.01	11/2019 03/2021	03/2022	28(O) 0	0/0
1660	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2024	24(O) -	0/0
1661	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2024	24(O) -	0/0
1662	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2024	24(O) -	0/0
1663	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 224.69	224.69	.00	02/2022 -	03/2024	25(O) -	0/0
1664	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	03/2024	21(O) -	0/0
1665	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	04/2024	19(O) -	0/0
1666	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 154.73	154.73	.00	02/2022 -	03/2024	25(O) -	0/0
1667	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	11.56	12/2021 -	09/2023	21(O) -	0/0
1668	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	222.84	12/2019 05/2022	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1669	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	253.59	04/2020 -	03/2022	23(O) -	0/0
1670	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	11.56	12/2021 -	09/2023	21(O) -	0/0
1671	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	11.56	12/2021 -	09/2023	21(O) -	0/0
	Total		24,702.19 -	70,243.27	22,941.81				5/26
	<u>DEFENCE PRODUCTION</u>								
1772	RESIDENTIAL QUARTERS FOR HAL BANGLORE - [N28000103]CPWD FOR DEFENC, KARNATAKA ,	12/2016	246.31 210.00	210.00	158.92	02/2020 10/2021	03/2022	25(O) 3	8/10
	Total		246.31 -	210.00	158.92				8/10
	<u>COMMERCE</u>								
1773	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC FOR COMMER, DELHI ,	06/2018	302.64 -	302.64	30.00	10/2020 -	-	-	0/0
	Total		302.64 -	302.64	30.00				0/0
	Grand Total		22,23,791.78	26,64,649.18	13,08,766.65				701/1972


Summary of projects in the Flash Report for the month of December, 2021

Project Implementation - Current Status:

Number of Projects in Previous Month	1679
Number of Projects completed/dropped/frozen in Current Month	14
Number of Projects elevated to the status of Major project during the current month	6
Number of Projects Added in Current Month	2
Number of Projects in Current Month	1673

Brief Analysis


Project Status with respect to Original Schedule: Out of 1673 projects, 9 projects are ahead of schedule, 269 projects are on schedule 557 projects are delayed. 737 projects do not have fixed dates of commissioning. 101 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

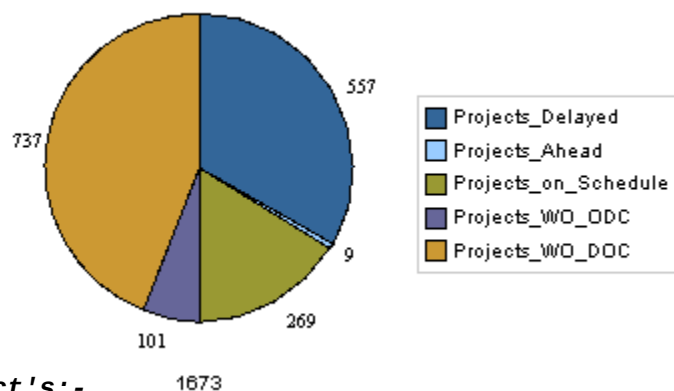

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1673 projects when sanctioned, was of the order of Rs. 2223791.78 crore but this was subsequently revised to Rs. 2664649.18 crore implying a cost overrun of 19.8%. The expenditure incurred on these projects till December, 2021 is Rs. 1308766.65 crore, which is 49.1% of the anticipated cost of the projects.

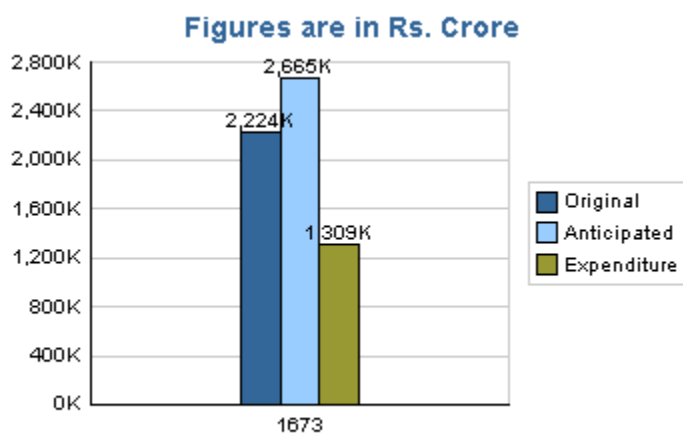

Sector wise current status of projects on the Flash Report

HOME AFFAIRS

Current Status:


Number of Projects 5

Number of Projects Delayed 4

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are delayed. 1 project does not have fixed dates of commissioning.

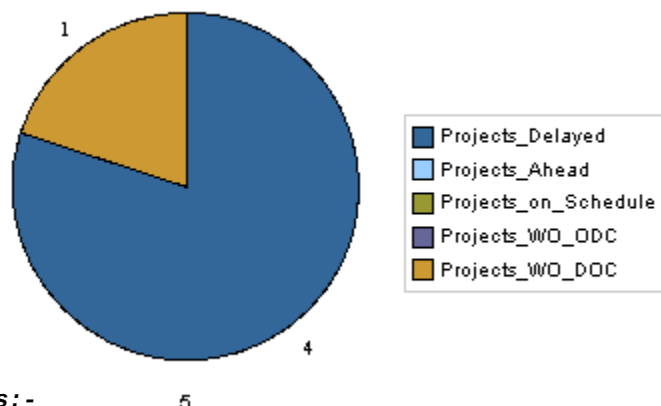


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 2025.73 crore but this was subsequently anticipated to Rs. 2894.62 crore implying a cost overrun of 42.9%. The expenditure incurred on these projects till December, 2021 is Rs. 1289.36 crore, which is 44.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

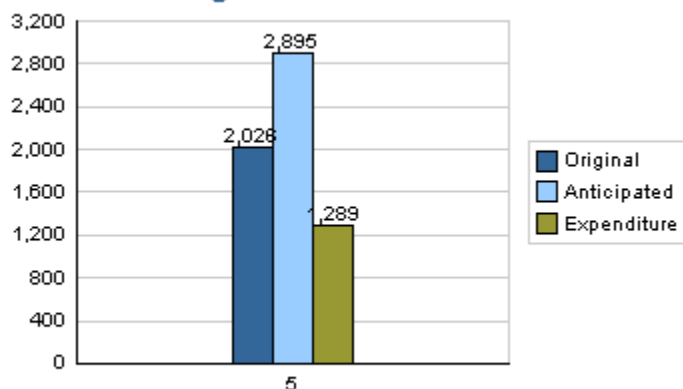

Sector wise current status of projects on the Flash Report

DEPARTMENT OF HIGHER EDUCATION


Current Status:

Number of Projects	22
Number of Projects On Schedule	1
Number of Projects Delayed	16

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 1 project is on schedule 16 projects are delayed. 5 projects do not have fixed dates of commissioning.

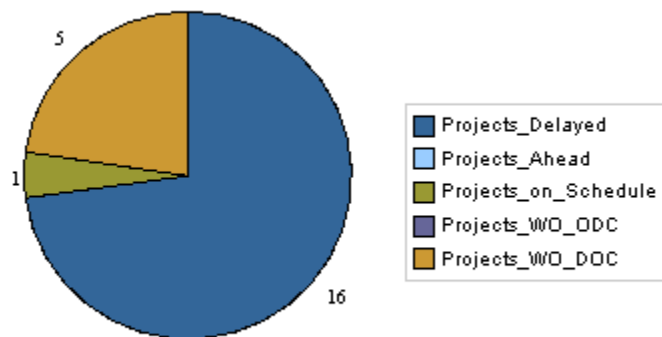


Total No Of Project's:- 22

Investment Scenario

Total original cost of implementation of 22 projects when sanctioned, was of the order of Rs. 10139.61 crore but this was subsequently anticipated to Rs. 10047.96 cr The expenditure incurred on these projects till December, 2021 is Rs. 4113 crore, which is 40.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

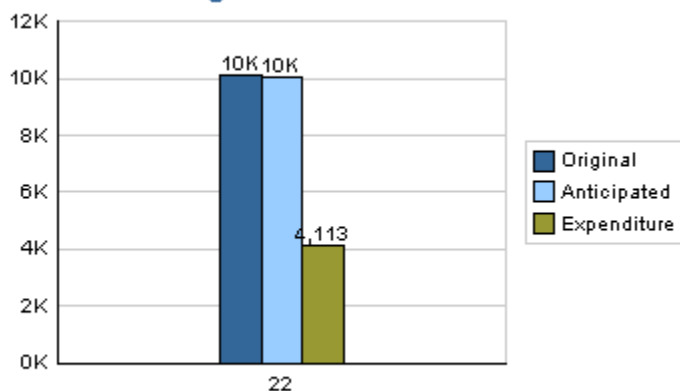

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	43
Number of Projects On Schedule	1
Number of Projects Delayed	38

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 43 projects, 1 project is on schedule 38 projects are delayed. 4 projects do not have fixed dates of commissioning.

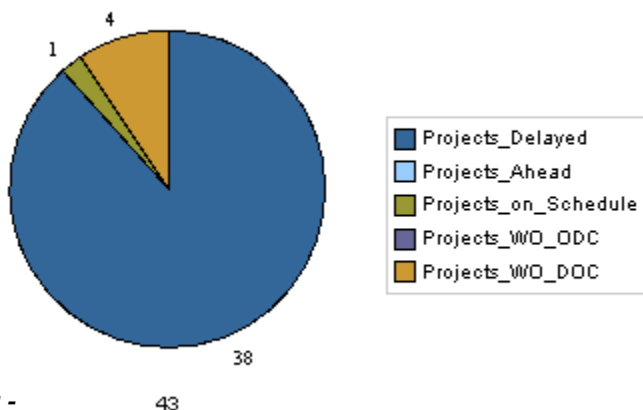


Total No Of Project's:-

43

Investment Scenario

Total original cost of implementation of 43 projects when sanctioned, was of the order of Rs. 24702.19 crore but this was subsequently anticipated to Rs. 70243.27 crore implying a cost overrun of 184.4%. The expenditure incurred on these projects till December, 2021 is Rs. 22941.81 crore, which is 32.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

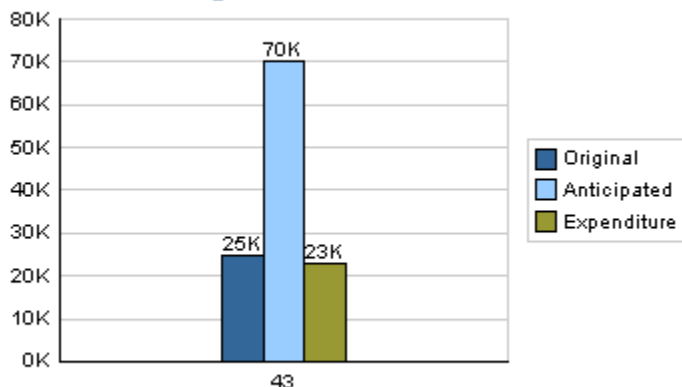

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	29
Number of Projects On Schedule	8
Number of Projects Delayed	14

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 8 projects are on schedule 14 projects are delayed. 6 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

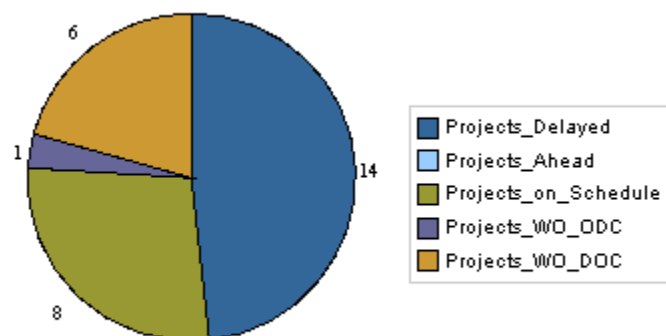


Total No Of Project's:-

29

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 291275.1 crore but this was subsequently anticipated to Rs. 313165.63 crore implying a cost overrun of 7.5%. The expenditure incurred on these projects till December, 2021 is Rs. 156187.13 crore, which is 49.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

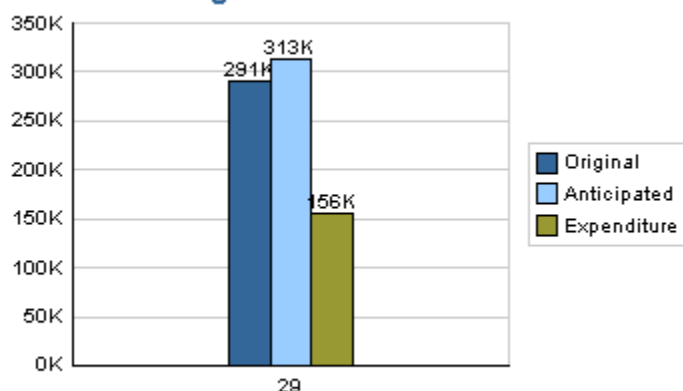

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are delayed.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14013.36 crore but this was subsequently anticipated to Rs. 25335.07 crore implying a cost overrun of 80.8%. The expenditure incurred on these projects till December, 2021 is Rs. 20771.22 crore, which is 82% of the anticipated cost of the projects.

Figures are in Rs. Crore

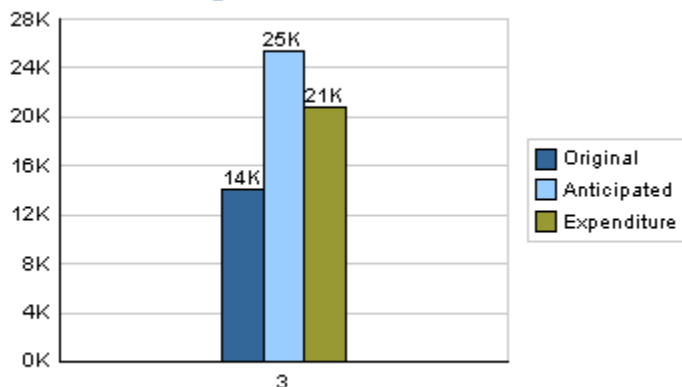

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	888
Number of Projects On Schedule	136
Number of Projects Delayed	115
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	39
Number of Projects Without Date Of Commissioning	597

Brief Analysis

Project Status with respect to Original Schedule: Out of 888 projects, 1 project is ahead of schedule, 136 projects are on schedule 115 projects are delayed. 597 projects do not have fixed dates of commissioning. 39 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

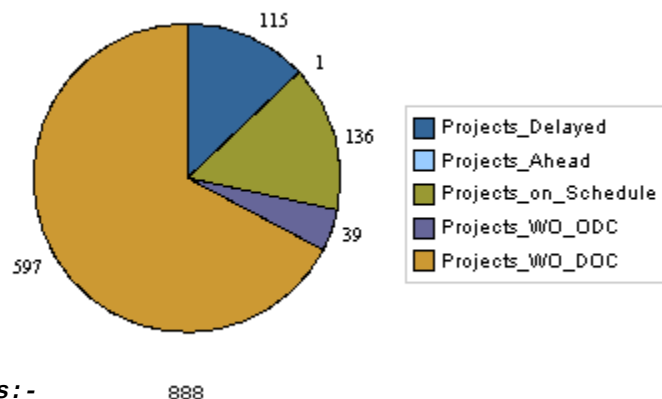


Total No Of Project's:-

888

Investment Scenario

Total original cost of implementation of 888 projects when sanctioned, was of the order of Rs. 537828.12 crore but this was subsequently anticipated to Rs. 553848.05 crore implying a cost overrun of 3%. The expenditure incurred on these projects till December, 2021 is Rs. 335150.64 crore, which is 60.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

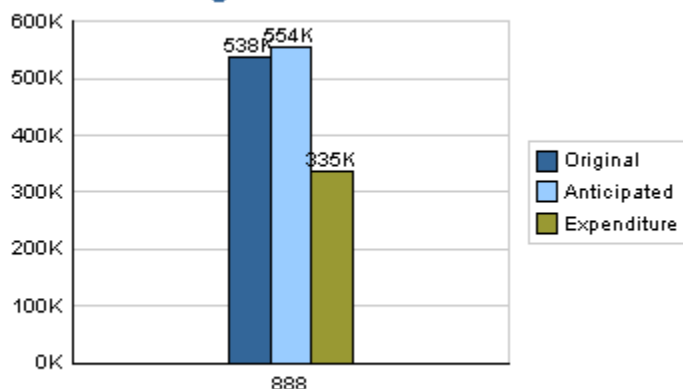

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	285
Number of Projects On Schedule	13
Number of Projects Delayed	145
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	54
Number of Projects Without Date Of Commissioning	69

Brief Analysis

Project Status with respect to Original Schedule: Out of 285 projects, 4 projects are ahead of schedule, 13 projects are on schedule 145 projects are delayed. 69 projects do not have fixed dates of commissioning. 54 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

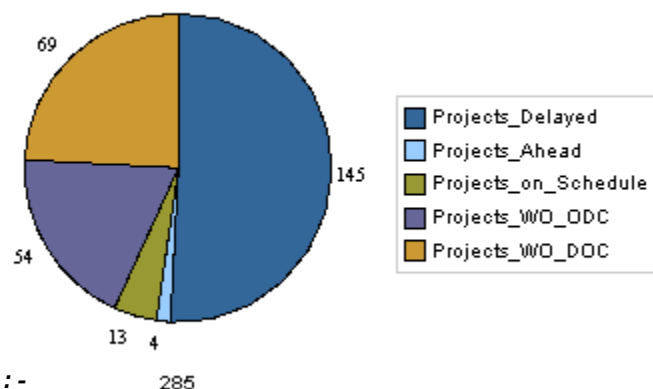


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 285 projects when sanctioned, was of the order of Rs. 443040.1 crore but this was subsequently anticipated to Rs. 684768.6 crore implying a cost overrun of 54.6%. The expenditure incurred on these projects till December, 2021 is Rs. 277511.94 crore, which is 40.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

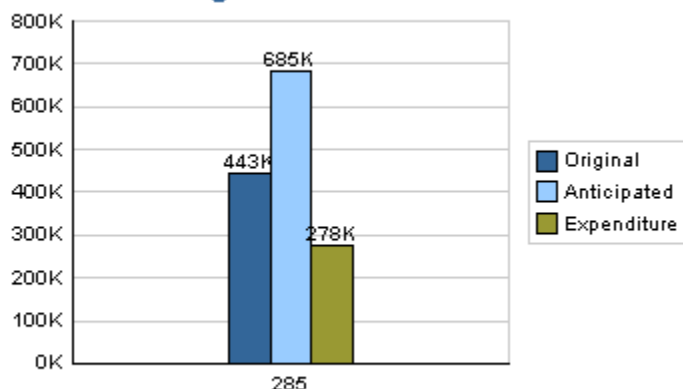

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	29
Number of Projects On Schedule	2
Number of Projects Delayed	5
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	18

Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 1 project is ahead of schedule, 2 projects are on schedule 5 projects are delayed. 18 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

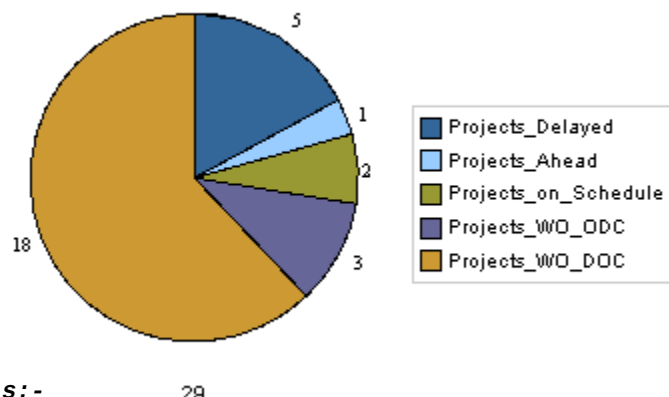


Total No Of Project's:-

29

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 15273.26 crore but this was subsequently anticipated to Rs. 15715.78 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till December, 2021 is Rs. 9278.31 crore, which is 59% of the anticipated cost of the projects.

Figures are in Rs. Crore

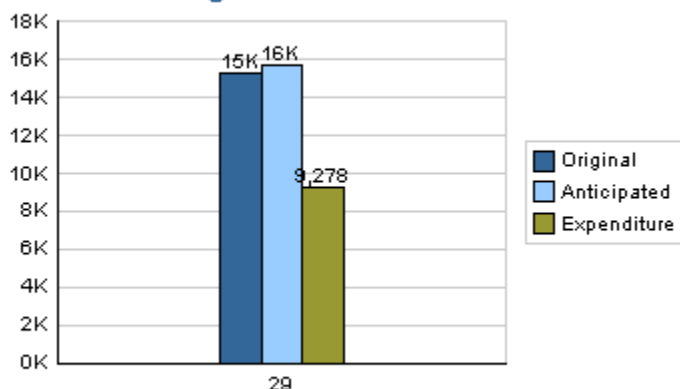

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	62
Number of Projects On Schedule	6
Number of Projects Delayed	45

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 62 projects, 6 projects are on schedule 45 projects are delayed. 10 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

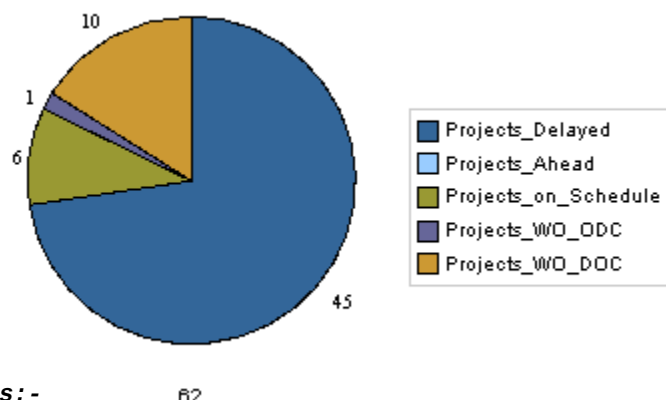


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 62 projects when sanctioned, was of the order of Rs. 207257.24 crore but this was subsequently anticipated to Rs. 270968.33 crore implying a cost overrun of 30.7%. The expenditure incurred on these projects till December, 2021 is Rs. 180166.07 crore, which is 66.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

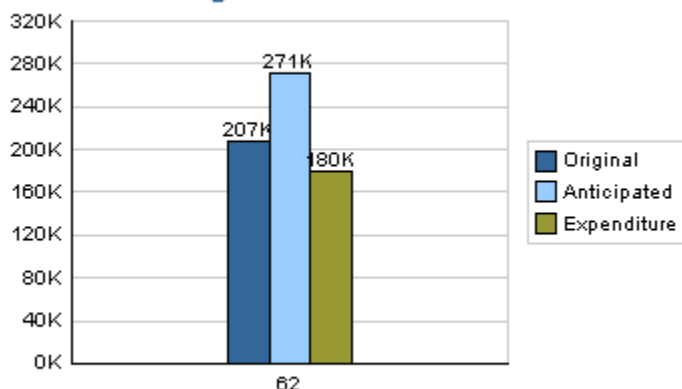

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	147
Number of Projects On Schedule	54
Number of Projects Delayed	84
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 147 projects, 3 projects are ahead of schedule, 54 projects are on schedule 84 projects are delayed. 4 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

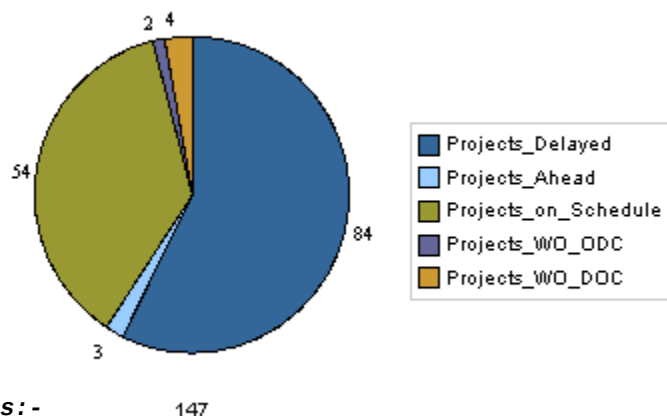


Total No Of Project's:-

147

Investment Scenario

Total original cost of implementation of 147 projects when sanctioned, was of the order of Rs. 339274.49 crore but this was subsequently anticipated to Rs. 350723.52 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till December, 2021 is Rs. 125031.63 crore, which is 35.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

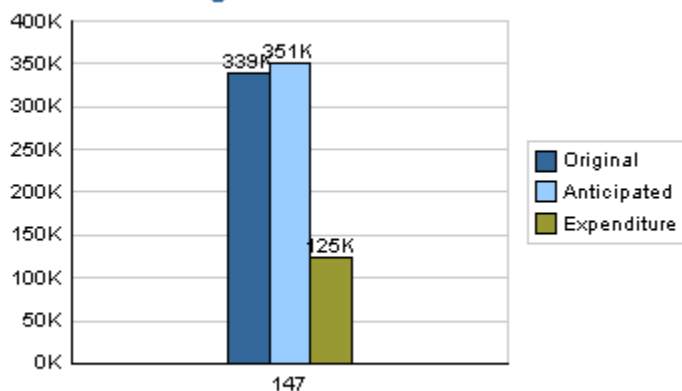

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	7
Number of Projects On Schedule	3
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 3 projects are on schedule 3 projects are delayed. 1 project does not have fixed dates of commissioning.

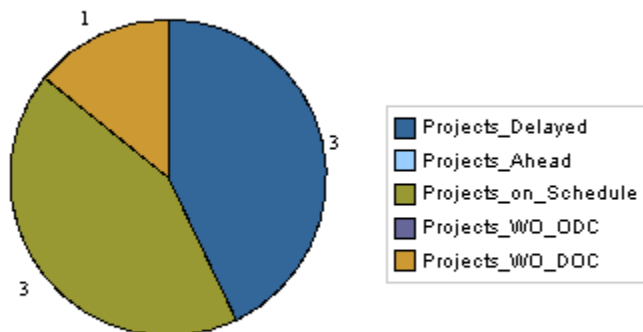


Total No Of Project's:- 7

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 22331.15 crore but this was subsequently anticipated to Rs. 29163.3 crore implying a cost overrun of 30.6%. The expenditure incurred on these projects till December, 2021 is Rs. 22761.7 crore, which is 78% of the anticipated cost of the projects.

Figures are in Rs. Crore

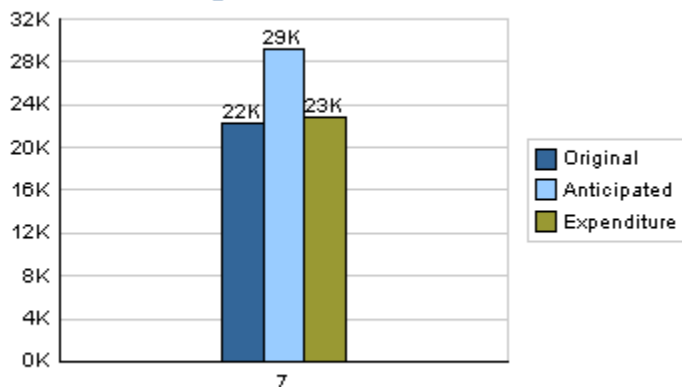

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	6
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are delayed. 2 projects do not have fixed dates of commissioning.

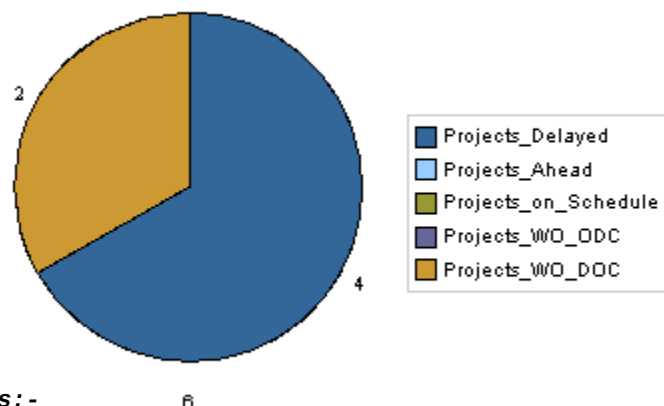


Total No Of Project's:- 6

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 7333.99 crore but this was subsequently anticipated to Rs. 7330.54 crore. The expenditure incurred on these projects till December, 2021 is Rs. 1819.26 crore, which is 24.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

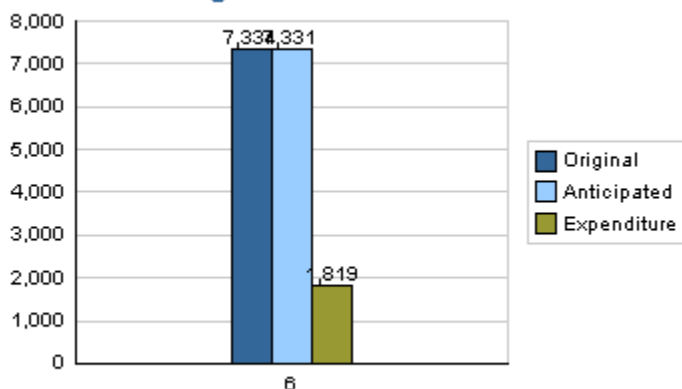

Sector wise current status of projects on the Flash Report

FERTILISERS

Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

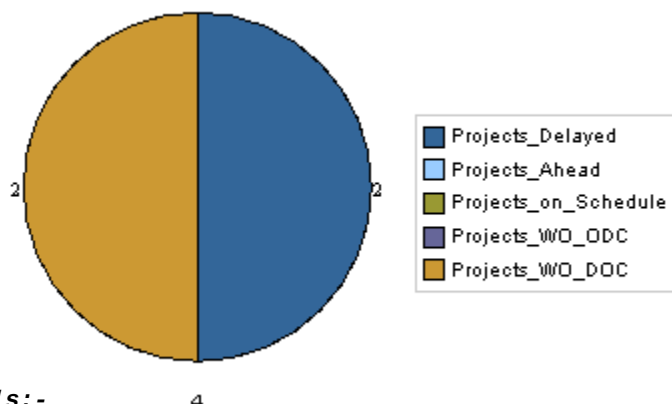


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till December, 2021 is Rs. 914.82 crore, which is 83.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

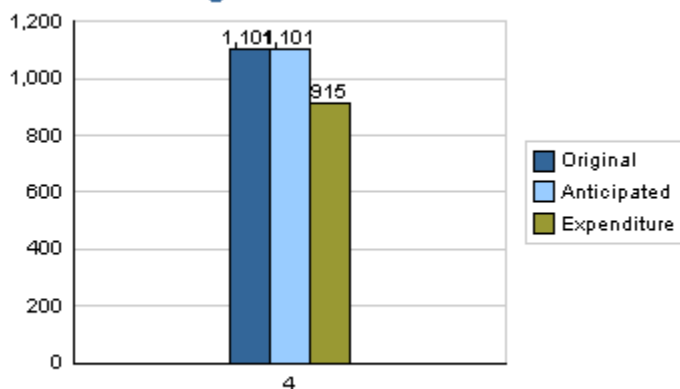

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	106
Number of Projects On Schedule	41
Number of Projects Delayed	55

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	9

Brief Analysis

Project Status with respect to Original Schedule: Out of 106 projects, 41 projects are on schedule 55 projects are delayed. 9 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

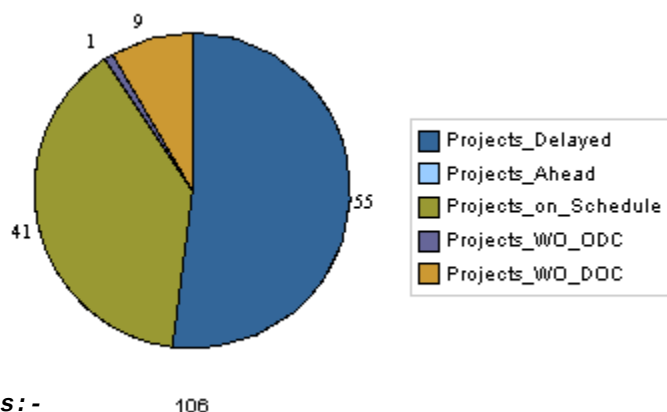


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 106 projects when sanctioned, was of the order of Rs. 149328.98 crore but this was subsequently anticipated to Rs. 153992.98 crore implying a cost overrun of 3.1%. The expenditure incurred on these projects till December, 2021 is Rs. 55306.02 crore, which is 35.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

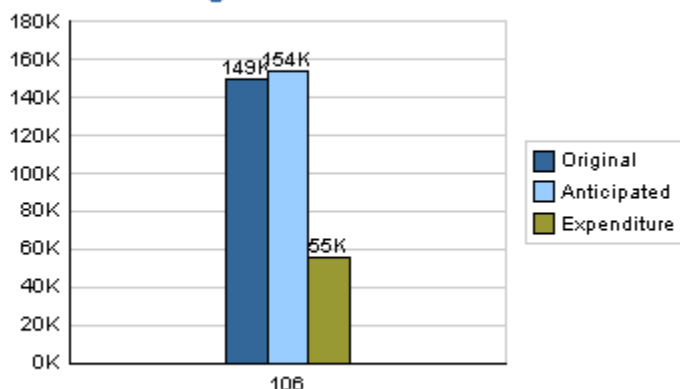

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	20
Number of Projects On Schedule	1
Number of Projects Delayed	18

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 1 project is on schedule 18 projects are delayed. 1 project does not have fixed dates of commissioning.

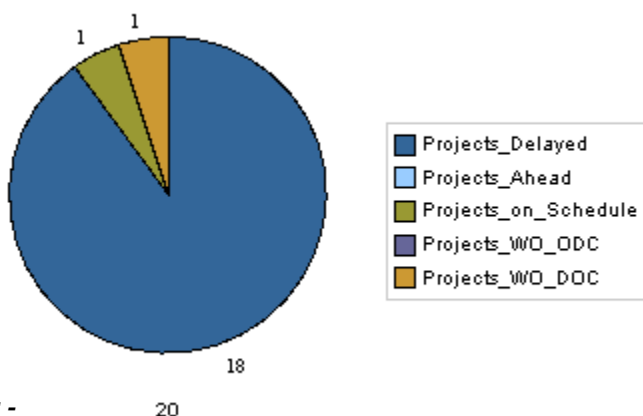


Total No Of Project's:-

20

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 14431.97 crore but this was subsequently anticipated to Rs. 15465.25 crore implying a cost overrun of 7.2%. The expenditure incurred on these projects till December, 2021 is Rs. 5714.71 crore, which is 37% of the anticipated cost of the projects.

Figures are in Rs. Crore

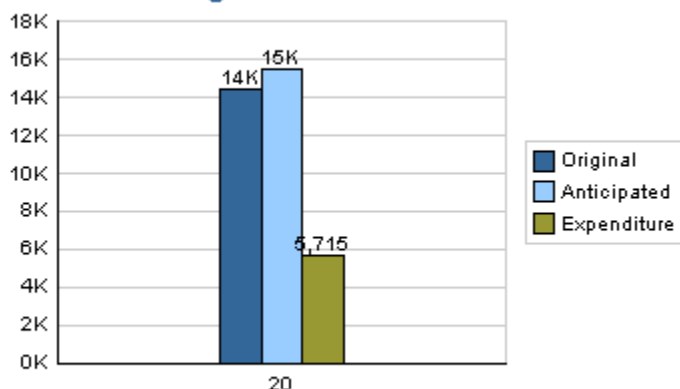

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 1 project is on schedule 4 projects are delayed.

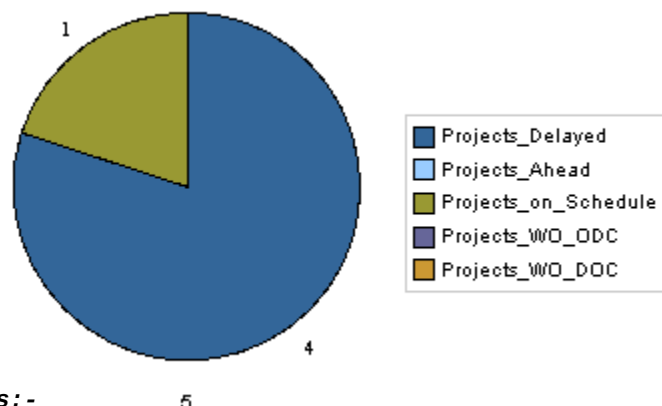


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 116741 crore but this was subsequently anticipated to Rs. 129969 crore implying a cost overrun of 11.3%. The expenditure incurred on these projects till December, 2021 is Rs. 70005.37 crore, which is 53.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

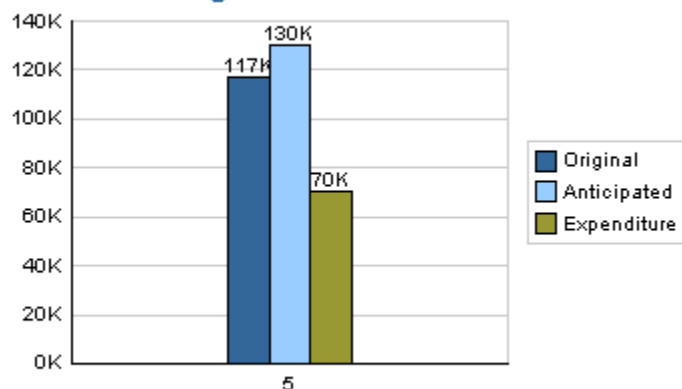

ANNEXURE

FLASH REPORT

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (DECEMBER 2021)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	3,159.99	1,642.71
2	ANDHRA PRADESH	67	1,12,107.24	1,58,677.58	83,084.01
3	ARUNACHAL PRADESH	43	23,906.6	37,842.94	20,583.18
4	ASSAM	48	48,689	57,952.53	14,028.77
5	BIHAR	98	1,23,227.91	1,59,169.38	83,613.55
6	CHHATISGARH	46	78,726.75	89,025.67	45,037.76
7	DELHI	30	84,192.81	85,286.8	53,048.43
8	GOA	10	5,332.77	5,343.26	2,814.61
9	GUJARAT	59	1,08,152.96	1,19,380.3	56,253.28
10	HARYANA	36	61,492.56	63,819.18	20,834.71
11	HIMACHAL PRADESH	20	22,264.08	33,301.38	21,353.35
12	JAMMU AND KASHMIR	30	48,180.49	74,107.74	49,072.88
13	JHARKHAND	41	69,363.87	75,272.33	35,295.28
14	KARNATAKA	56	85,354.49	97,051.69	51,190.08
15	KERALA	22	30,240.6	35,398.3	12,969.15
16	LADAKH	8	2,633.23	2,767.29	293.41
17	MADHYA PRADESH	78	68,627.95	77,288.11	35,592.61
18	MAHARASHTRA	229	2,06,831.47	2,29,792	1,26,950.31
19	MANIPUR	26	12,108.58	22,615.2	13,077.89
20	MEGHALAYA	13	5,269.68	8,391.62	2,723.47
21	MIZORAM	24	11,957.35	16,911.6	7,888.67
22	MULTI STATE	113	3,46,034.59	4,57,844.63	1,96,589.21
23	NAGALAND	35	15,989.03	20,373.15	5,277.32
24	ODISHA	78	1,09,287.57	1,17,479.3	51,740.77
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	28	18,344.99	20,091.84	7,485.46
27	RAJASTHAN	55	51,403.28	58,096.28	38,279.46
28	SIKKIM	18	7,278.84	14,598.73	2,967.68
29	TAMIL NADU	68	1,70,613.2	1,90,104.32	93,475.16
30	TELANGANA	51	38,003.46	41,083.48	22,934.9
31	TRIPURA	19	5,084.45	5,259.05	2,173.32
32	UTTAR PRADESH	113	1,51,519.42	1,55,425.03	83,281.84
33	UTTARAKHAND	30	35,588.83	50,291.17	25,170.86
34	WEST BENGAL	71	62,900.1	81,252.31	42,026.15
TOTAL		1,673	22,23,791.78	26,64,649.18	13,08,766.65

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	6,054.37	09/2010 -	10/2022
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	17,427.00	12/2015 -	12/2022
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,945.00	12/2016 -	12/2023
	Total		27,271.00	40,499.00	37,426.37		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
4	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	808.97	808.97	03/2013 -	03/2024
	<u>Singareni Colliers Company Limited</u>						
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	306.52	03/2015 -	03/2022
	Total		642.29 -	1,158.25	1,115.49		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
6	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	586.50	581.44	11/2013 -	09/2021
7	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
8	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	164.17	02/2018 -	03/2021
9	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.54	273.41	03/2019 -	03/2021
10	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	183.36	- -	12/2021
11	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
12	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021
13	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
	Total		2,168.38 -	2,578.50	2,507.85		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
14	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	559.57	02/2020 06/2021	11/2021
	<u>Oil & Natural Gas Corporation Limited</u>						
15	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	829.58	12/2020 05/2021	02/2022
	Total		1,320.92 -	1,290.86	1,389.15		
	<u>POWER</u>						
	<u>Satluj Jal Vidyut Nigam Limited</u>						
16	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	785.06	12/2021 06/2022	06/2022
	Total		648.33 -	947.89	785.06		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
17	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	325.00	325.52	03/2019 -	-
18	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023
	<u>Container Corporation Of India</u>						
19	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	487.13	434.63	03/2018 -	-
	<u>East Central Railways</u>						
20	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,650.00	3,661.29	- 03/2022	03/2022
21	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,370.20	- 03/2022	03/2022
22	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	390.00	403.49	03/2021 -	03/2022
23	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	560.09	560.09	07/2014 -	-
24	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	4/1997	324.73 -	1,080.00	1,086.41	03/2012 11/2022	11/2022
25	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	4/2006	378.56 -	1,858.75	386.36	- -	03/2023
26	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	958.41	03/2019 12/2021	12/2021
	<u>East Coast Railway</u>						
27	SAMBALPUR-TALCHER DOUBLING - [N22000315]	3/2011	1,111.99 -	1,539.28	1,195.24	02/2019 -	03/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Eastern Railways</u>						
28	DEOGHAR - SULTANGANJ (INL), ER - [N220100273]	4/2000	607.09 -	1,425.44	638.35	02/2013 -	03/2024
29	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	4/2010	365.17 -	439.30	507.59	03/2017 -	03/2025
30	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	410.29	- -	03/2024
31	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	4/2012	255.64 -	272.20	303.23	- -	03/2022
32	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	502.48	521.63	- -	03/2021
33	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	495.10	316.82	- -	03/2022
	<u>Metropolitan Rapid Transport Projects</u>						
34	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
35	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-
36	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [N220100164]	3/1996	495.44 -	2,980.41	1,868.04	03/2004 06/2022	06/2022
	<u>North East Frontier Railway</u>						
37	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266]	4/2000	1,180.19 -	4,541.38	3,936.64	12/2008 -	12/2021
38	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	373.87	333.46	- 12/2021	06/2022
39	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	1,873.21	1,586.23	03/2021 -	03/2022
40	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	2/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-
41	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	1,167.00	1,095.12	12/2021 -	10/2021
42	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,090.60	1,089.12	- -	-
43	AGARTALA-AKHAURA NL - [N22000195]	4/2012	569.63 -	742.00	612.37	03/2020 06/2022	06/2022
44	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,043.00	919.48	03/2019 -	03/2023
	<u>North Eastern Railway</u>						
45	HATHUA-BHATNI (N L) (NER) - [N220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
46	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,465.45	03/2022 -	03/2022
47	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	610.00	595.91	01/2019 -	02/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North Western Railway</u>						
48	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	2/1997	410.08 -	860.41	769.95	02/2019 -	06/2022
	<u>Northern Railway</u>						
49	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	745.06	12/2011 -	06/2021
50	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	839.00	839.36	03/2016 -	-
51	NANGALDAM-TALWARA(NL),NR - [N220100188]	3/1981	450.00 -	2,017.96	878.49	07/2012 -	11/2024
52	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	4/2007	336.91 -	791.39	597.99	- -	09/2023
	<u>Rail India Technical And Economic Service</u>						
53	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	653.38	03/2021 -	-
	<u>Rail Vikas Nigam Ltd.</u>						
54	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N220100325]	4/1998	1,202.70 -	2,440.53	1,894.70	02/2015 -	06/2022
55	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,477.01	03/2023 -	12/2022
56	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	3/2012	1,503.71 -	3,377.00	3,753.96	03/2020 -	03/2022
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327]	4/2000	133.41 207.00	433.00	419.58	03/2009 12/2022	-
58	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	872.65	942.56	03/2021 -	12/2021
59	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,868.89	2,201.29	12/2021 -	03/2022
60	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,536.00	1,269.37	03/2019 -	06/2022
61	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	2,009.00	2,156.59	03/2020 -	12/2021
62	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	2,900.00	2,041.94	03/2020 -	12/2021
63	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,400.00	1,438.92	03/2019 -	06/2022
64	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	949.03	12/2024 -	12/2024
65	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	943.60 -	1,000.00	982.28	03/2022 -	12/2024
66	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,515.82	12/2023 -	12/2023
67	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	950.00	839.78	03/2016 -	12/2021
68	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,650.00	1,737.74	12/2021 -	12/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
69	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,536.00	1,509.71	03/2020 -	06/2022
70	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,835.83	2,355.40	12/2020 -	12/2021
71	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,825.00	1,777.07	12/2020 -	12/2022
	<u>South Central Railway</u>						
72	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	4/1997	1,723.00 1.00	3,421.35	2,010.00	03/2000 -	03/2023
	<u>South Eastern Railway</u>						
73	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	4/2010	149.90 -	266.61	239.38	03/2015 -	03/2019
74	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	1,119.38	03/2020 -	06/2022
	<u>South Western Railway</u>						
75	HUBLI- CHIKJAJUR - [N22000325]	3/2015	1,156.94 -	1,954.21	1,205.02	03/2020 -	03/2023
76	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	760.00	647.09	03/2020 01/2022	01/2022
77	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	1,104.00	983.01	03/2020 -	09/2021
	<u>Southern Railway</u>						
78	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'- AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	3,081.20	1,718.56	02/2019 -	03/2025
79	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	1,549.09	712.68	03/2020 -	03/2025
80	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	2/1996	268.87 -	991.83	922.01	03/2005 -	12/2021
81	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	2,172.16	308.35	03/2019 -	12/2027
82	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	4/2007	931.98 -	1,122.00	994.02	- 09/2021	12/2022
83	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	608.13	427.75	- 12/2021	02/2022
84	KURUPPANTHARA-CHINGAVANAM - [N22000190]	4/2007	270.14 -	749.40	578.46	- 12/2021	03/2022
	<u>West Central Railway</u>						
85	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025
	<u>Western Railway</u>						
86	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	2,223.37	1,966.82	03/2020 03/2024	03/2024
87	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022
	Total		56,387.99 -	1,20,108.73	95,287.82		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
88	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257	3/2015	298.33 -	298.33	325.55	- -	-
89	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	322.24	308.85	09/2014 12/2021	-
90	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	3/2018	325.86 -	386.41	347.46	10/2018 -	-
91	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156	1/2017	166.67	166.67	185.07	09/2017	-
92	KALMATH TO ZARAP - [N24001137	9/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-
93	TALGAON TO KALMATH - [N24001136	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-
94	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKAALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	552.31	12/2019 02/2022	02/2022
95	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	346.72	05/2017 05/2022	05/2022
96	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574	11/2013	683.83 -	560.70	698.84	07/2016 -	-
97	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	1/1991	319.68 -	369.77	333.28	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
98	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	169.08	11/2018 -	11/2021
	<u>National Highways Authority Of India</u>						
99	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	612.58	612.58	02/2009 -	-
100	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-
101	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-
102	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
103	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	609.00	- -	10/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
104	ISMAILABAD-NARNAUL PKG-1 - [N24001193]	1/2019	996.65 -	996.65	1,061.16	- -	-
105	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	3/2018	642.13 -	807.00	724.40	- -	-
106	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]	3/2018	565.09 -	565.09	654.52	- -	02/2021
107	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]	3/2018	1,550.98 -	1,550.98	1,654.42	- -	09/2021
108	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	3/2018	1,120.57 -	1,332.00	1,525.15	- -	-
109	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	3/2018	925.40 -	1,197.00	1,176.70	- -	-
110	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]	3/2018	809.07 -	809.07	886.68	- -	-
111	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	2/2018	2,177.80 -	2,450.00	2,542.30	- -	-
112	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	2/2018	1,995.34 -	2,400.00	3,439.59	- -	11/2021
113	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]	10/2017	964.17 -	964.17	964.60	10/2017 -	-
114	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	3/2017	993.16 -	1,434.00	1,319.54	03/2020 -	-
115	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	3/2017	831.58 -	1,177.00	912.41	03/2020 -	-
116	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-
117	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	1,297.83	03/2020 -	-
118	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	723.26	07/2018 02/2022	-
119	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- [N24000636]	12/2016	1,031.95 -	1,031.95	1,513.48	- -	03/2022
120	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]	10/2016	447.75 -	447.75	1,341.10	- -	-
121	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]	10/2016	1,008.96 -	1,008.96	1,125.65	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
122	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	359.60	340.15	- 12/2016	05/2017
123	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627	11/2016	1,071.61 -	1,048.10	1,183.14	- 10/2021	12/2021
124	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,665.00	- -	-
125	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	9/2016	1,100.19 -	1,145.31	1,355.00	- -	-
126	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591	7/2016	688.70 -	688.70	870.48	- -	-
127	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	690.17	06/2019 -	-
128	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547	3/2016	1,404.50 -	1,404.50	2,977.58	- -	-
129	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546	2/2016	273.20 -	273.20	670.27	02/2019 -	-
130	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	985.40	04/2019 -	-
131	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	886.96	07/2008 -	-
132	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	8/2015	516.13 -	649.27	651.24	04/2018 -	-
133	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521	8/2015	854.80 -	1,038.56	1,034.47	- -	-
134	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520	8/2015	275.90 -	275.90	289.13	- -	-
135	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517	12/2015	479.20 -	479.20	712.89	05/2018 -	-
136	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	2,360.65	4,511.67	- -	-
137	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
138	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
139	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367	4/2014	495.78 -	627.93	633.24	01/2016 -	-
140	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	417.68	433.68	01/2016 -	-
141	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-
142	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	469.31	459.07	01/2014 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
143	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,873.47	06/2014 -	-
144	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,893.57	08/2013 -	06/2023
145	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	01/2022
146	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,364.18	03/2013 -	-
147	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,933.15	06/2014 -	10/2020
148	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	591.00	578.00	11/2013 -	-
149	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09	375.09	494.33	04/2014	-
150	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.92	03/2014 -	-
151	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,286.10	05/2014 -	-
152	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022
153	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.53	10/2013 -	-
154	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-
155	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	-
156	PATNA-MUZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	1,198.39	02/2013 -	-
157	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,654.22	07/2013 -	-
158	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-
159	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	3,116.66	07/2015 -	09/2020
160	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	8/2015	814.04 -	825.17	821.37	- -	10/2021
161	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
162	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
163	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
164	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	6/2015	845.24 -	941.00	902.51	- 01/2020	01/2020
165	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
166	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	844.08	04/2018 -	12/2021
167	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	706.78	05/2018 03/2022	03/2022
168	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020
169	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131	2/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-
170	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	3/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-
171	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-
172	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	2,641.30	03/2013 -	03/2022
173	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
174	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
175	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	-
	Total		84,780.18 -	92,963.39	1,22,701.14		
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
176	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	2,100.00	1,767.98	09/2018 09/2021	09/2021
	Total		1,682.85 -	2,100.00	1,767.98		
	<u>URBAN DEVELOPMENT</u>						
	<u>Delhi Metro Rail Corporation</u>						
177	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	39,619.40	03/2016 08/2021	-
	Total		38,585.00 -	38,585.00	39,619.40		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
178	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	398.90	294.30	03/2020 -	02/2022
179	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	338.67	01/2021 -	03/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		494.40 -	667.53	632.97		
	Grand Total		2,13,981.34	3,00,899.15	3,03,233.23		

FLASH REPORT

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]	1/2016	458.00 -	458.00	161.87	03/2020 06/2022	04/2022
	Total		458.00 -	458.00	161.87		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00 -	1,828.00	218.99	09/2025	05/2024
	Total		1,828.00 -	1,828.00	218.99		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
3	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	3,072.00	2,673.55	06/2021 08/2022	07/2022
	<u>Indian Oil Corporation Limited</u>						
4	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00 -	18,936.00	829.33	09/2024	08/2024
	Total		21,613.00 -	22,008.00	3,502.88		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
5	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,764.97	03/2024	03/2023
	<u>Rail Vikas Nigam Ltd.</u>						
6	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	1,905.63	12/2026	12/2025
7	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.19	12/2025	03/2025
8	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,477.01	03/2023	12/2022
	Total		9,445.24 -	14,104.67	6,147.80		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
9	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH - - [N24001180	3/2019	237.51 -	237.51	96.49	12/2022 -	07/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
10	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	142.87	09/2019 06/2023	04/2023
11	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946	3/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022
	Total		2,493.92 -	2,493.92	759.28		
	Grand Total		35,838.16	40,892.59	10,790.82		

FLASH REPORT

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	5,074.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	5,074.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	67.47	03/2023 -	03/2023
	Total		611.80 -	611.80	67.47		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
3	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	778.80	406.92	03/2023 -	03/2023
4	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	37.28	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
5	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	3.78	03/2027 -	03/2027
6	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY - [N06000020]	11/2015	1,210.12 -	1,210.12	49.12	03/2029 03/2029	03/2029
7	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	0.18	03/2027 -	03/2027
8	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	165.05	03/2024 -	03/2024
9	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.75	03/2026 -	03/2026
10	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	22.79	03/2029 -	03/2029
11	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	7.95	03/2025 -	03/2025
12	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	260.37	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
13	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,318.06	03/2029 -	03/2029
14	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	773.61	03/2027 -	03/2027
15	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,697.74	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Northern Coal Fields Limited</u>						
16	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
17	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
18	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
19	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
20	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	1.03	03/2023 -	03/2023
	<u>Singareni Colliers Company Limited</u>						
21	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	25.43	03/2023 -	03/2023
22	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	88.95	03/2023 -	03/2023
23	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	111.78	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
24	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,162.39	03/2023 -	03/2023
25	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	76.12	03/2026 -	03/2026
26	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
27	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	2,031.19	03/2029 -	03/2029
28	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [J060100093]	6/2010	11,816.40 -	11,816.40	4,645.12	03/2023 03/2016	03/2023
29	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	169.69	03/2022 -	03/2022
31	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	46.75	03/2026 -	03/2026
32	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
33	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	322.85	03/2029 -	03/2029
34	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	187.07	03/2024 -	03/2024
35	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
	<u>Western Coal Fields Limited</u>						
36	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
37	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
38	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	87.35	03/2023 -	03/2023
39	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	248.72	03/2022 -	03/2022
40	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	84.05	03/2028 -	03/2028
41	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	423.42	03/2025 -	03/2025
42	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
43	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	2.65	03/2026 -	03/2026
	Total		59,302.01 -	58,851.93	17,640.80		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
44	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	223.43	04/2023 -	04/2023
	Total		676.00 -	676.00	223.43		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
45	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	394.73	09/2023 -	09/2023
46	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	Total		2,981.00 -	3,232.00	394.73		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
47	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	299.02	03/2023 -	03/2023
48	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023
	<u>Gas Authority Of India Limited</u>						
49	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	149.60	10/2022 -	10/2022
50	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	99.81	07/2022 -	07/2022
51	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	111.42	10/2022 -	10/2022
52	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	553.20	07/2022 -	07/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
53	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	197.09	10/2022 -	10/2022
54	60 KTA POLYPROPYLENE PROJECT - [N16000429]	3/2019	910.56 -	910.56	117.31	04/2024 -	04/2024
55	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,789.70	05/2023 -	05/2023
56	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	255.92	04/2022 -	04/2022
57	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	166.06	07/2022 -	07/2022
58	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]	5/2019	8,797.00 -	8,797.00	178.78	04/2025 -	04/2025
59	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	355.80	11/2022 -	11/2022
<u>Hindustan Petroleum Corporation Limited</u>							
60	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	1,461.90	06/2022 -	06/2022
61	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	30.88	11/2022 -	11/2022
62	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	438.32	11/2022 -	11/2022
63	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]	9/2021	160.00 -	160.00	-	06/2024 -	06/2024
64	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	13.36	03/2024 -	03/2024
65	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	229.78	02/2023 -	02/2023
66	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	175.31	12/2022 -	12/2022
<u>Indian Oil Corporation Limited</u>							
67	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	516.61	08/2022 -	08/2022
68	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]	6/2019	2,880.00 -	2,880.00	113.40	08/2027 -	08/2027
69	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	505.01	09/2024 -	09/2024
70	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	132.46	01/2023 -	01/2023
71	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]	6/2019	347.00 -	347.00	105.90	02/2028 -	02/2028
72	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	1.12	08/2023 -	08/2023
73	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	687.88	05/2023 -	05/2023
74	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	40.12	12/2029 -	12/2029

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
75	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	45.10	12/2029 -	12/2029
76	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	182.84	12/2022 -	12/2022
77	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	26.31	12/2029 -	12/2029
78	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	42.90	03/2030 -	03/2030
79	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]	10/2018	613.00 -	613.00	161.96	12/2029 -	12/2029
80	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]	10/2018	176.00 -	176.00	79.72	08/2027 -	08/2027
81	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	2,089.45	04/2023 -	04/2023
82	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	130.22	02/2028 -	02/2028
83	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]	6/2019	439.00 -	439.00	127.63	02/2028 -	02/2028
84	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	66.77	02/2027 -	02/2027
85	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	579.94	01/2024 -	01/2024
86	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	206.62	04/2022 -	04/2022
87	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	61.04	07/2022 -	07/2022
88	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	26.64	10/2023 -	10/2023
89	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,605.89	02/2022 -	02/2022
90	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	111.34	08/2022 -	08/2022
91	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]	6/2019	2,996.00 -	2,996.00	309.12	02/2028 -	02/2028
92	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	202.71	03/2030 -	03/2030
	<u>Numaligarh Refinery Limited</u>						
93	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINERY - [N16000379]	1/2019	12,366.00 -	18,968.00	767.97	10/2024 -	10/2024
94	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	959.30	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
95	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	947.93	03/2026 -	03/2026
96	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	227.33	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
97	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON - [N16000433]	8/2021	218.38 -	218.38	-	02/2023 -	02/2023
98	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]	8/2021	885.63 -	885.63	183.01	02/2026 -	02/2026
99	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	141.98	08/2022 -	08/2022
100	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,800.96	03/2022 -	03/2022
	Total		1,59,283.93 -	1,64,441.37	20,235.74		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
101	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]	5/2021	674.92 -	674.92	76.91	09/2022 -	09/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						
102	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	4,611.25	01/2024 -	01/2024
103	SHIYAL SOLAR POWER PROJECT - [N18000297]	5/2021	296.20 -	296.20	0.21	10/2022 -	10/2022
104	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	585.06	01/2026 -	01/2026
105	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	207.51	11/2025 -	11/2025
106	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	313.58 -	313.58	112.91	12/2022 -	12/2022
	Total		14,222.32 -	14,222.32	5,593.85		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
107	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
108	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023
109	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
110	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023
	<u>North Eastern Railway</u>						
111	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	116.44	12/2021 -	12/2021
112	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
113	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,465.45	03/2022 -	03/2022
	<u>National High Speed Rail Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
114	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	18,841.98	12/2023 -	12/2023
	<u>Rail Vikas Nigam Ltd.</u>						
115	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	2,364.27	12/2023 -	12/2023
116	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,650.00	1,737.74	12/2021 -	12/2021
117	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,515.82	12/2023 -	12/2023
118	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	949.03	12/2024 -	12/2024
	<u>Western Railway</u>						
119	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	4/2018	537.31 -	537.31	0.64	03/2024 03/2024	03/2024
	Total		1,36,417.41 -	1,42,049.21	31,354.91		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
120	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]	7/2018	1,948.25 -	1,948.25	277.20	02/2024 -	02/2024
121	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	236.18	59.74	12/2022 -	12/2022
122	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]	2/2021	925.47 -	925.47	-	07/2025 -	07/2025
123	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]	2/2021	588.09 -	588.09	93.72	03/2024 -	03/2024
124	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]	1/2020	358.26 -	358.26	0.52	02/2024 -	02/2024
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
125	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023
126	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	-	12/2022 -	12/2022
127	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	8.67	04/2022 -	04/2022
128	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	171.37	12/2023 -	12/2023
129	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]	4/2020	330.80 -	330.80	49.90	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
130	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]	3/2020	206.53 -	206.53	81.84	06/2022 -	06/2022
131	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	9.39	04/2022 -	04/2022
132	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]	8/2020	278.46 -	278.46	62.66	03/2022 -	03/2022
133	CHURACHANPUR TUIVAI PKG-3 - [N24001405]	7/2021	673.27 -	673.27	-	10/2023 -	10/2023
134	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]	6/2020	277.50 -	277.50	106.99	01/2022 -	01/2022
135	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]	8/2020	230.45 -	230.45	2.58	04/2023 -	04/2023
136	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
137	IMPHAL – MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	35.84	12/2022 -	12/2022
138	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	4.68	12/2022 -	12/2022
139	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	48.49	12/2023 -	12/2023
140	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	25.27	08/2022 -	08/2022
141	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]	6/2020	347.36 -	347.36	89.80	01/2022 -	01/2022
142	IMPHAL – MOREH (PACKAGE 4) - [N24001399]	3/2021	277.99 -	277.99	-	01/2023 -	01/2023
143	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	10.23	12/2022 -	12/2022
144	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	27.90	10/2022 -	10/2022
145	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]	7/2020	210.79 -	210.79	20.18	04/2022 -	04/2022
146	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]	11/2020	206.78 -	206.78	65.92	07/2022 -	07/2022
147	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]	12/2020	804.00 -	804.00	46.60	08/2023 -	08/2023
148	DABOKA KATHKATI PACKAGE-4 - [N24001365]	2/2021	260.07 -	260.07	34.33	12/2023 -	12/2023
149	GOHA-KHELLANI PKG-3 - [N24001397]	2/2021	431.28 -	431.28	24.77	03/2023 -	03/2023
150	PEREN-DIMAPUR PKG-5 - [N24001407]	2/2021	207.33 -	207.33	-	03/2023 -	03/2023
151	KHELLANI-KHANABAL PKG-6 - [N24001324]	2/2021	285.28 -	285.28	22.14	09/2022 -	09/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
152	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]	9/2020	262.84 -	262.84	120.72	05/2023 -	05/2023
153	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	9.04	01/2023 -	01/2023
154	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]	7/2021	258.52 -	258.52	20.00	03/2023 -	03/2023
155	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]	8/2020	301.06 -	301.06	25.63	04/2022 -	04/2022
156	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]	10/2020	493.42 -	493.42	-	11/2023 -	11/2023
157	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
158	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]	6/2020	257.96 -	257.96	95.22	01/2022 -	01/2022
159	KHELLANI-KHANABAL PKG-4 - [N24001395]	7/2021	859.67 -	859.67	-	08/2023 -	08/2023
160	DABOKA KATHKATI PACKAGE-2 - [N24001364]	3/2021	335.88 -	335.88	16.63	01/2024	01/2024
161	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]	3/2020	247.76 -	247.76	27.82	01/2022 -	01/2022
162	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]	8/2020	294.04 -	294.04	79.46	04/2022 -	04/2022
163	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]	3/2021	260.21 -	260.21	42.62	12/2022 -	12/2022
164	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	26.00	05/2022 -	05/2022
165	DABOKA KATHKATI PACKAGE-5 - [N24001366]	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
166	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]	8/2020	184.88 -	184.88	40.92	04/2022 -	04/2022
167	SENAPATI- IMPHAL PKG-5B - [N24001400]	3/2021	211.70 -	211.70	-	01/2023 -	01/2023
168	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
169	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	288.84	12/2023 -	12/2023
170	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]	6/2020	365.53 -	365.53	53.11	08/2022 -	08/2022
171	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]	8/2020	311.00 -	311.00	26.51	04/2023 -	04/2023
172	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	8.23	01/2023 -	01/2023
173	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]	9/2020	257.15 -	257.15	52.44	04/2022 -	04/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
174	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]	3/2020	242.97 -	242.97	59.98	06/2022 -	06/2022
175	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]	11/2020	280.91 -	280.91	90.44	07/2022 -	07/2022
176	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
177	TAMENGLONG - MAHUR PKG-4 - [N24001404]	7/2021	198.77 -	198.77	-	03/2023 -	03/2023
178	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]	3/2019	471.00 -	471.00	167.94	07/2022 -	07/2022
179	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]	9/2020	277.44 -	277.44	33.95	10/2022 -	10/2022
180	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]	3/2020	220.20 -	220.20	37.93	12/2022 -	12/2022
181	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97 -	320.97	56.39	06/2022 -	06/2022
182	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]	6/2020	201.99 -	201.99	18.87	01/2022 -	01/2022
183	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]	11/2020	4,997.04 -	4,997.04	557.28	09/2028 -	09/2028
184	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]	3/2020	278.95 -	278.95	79.89	06/2022 -	06/2022
185	KHELLANI-KHANABAL PKG-2 - [N24001394]	7/2021	512.43 -	512.43	3.87	02/2023 -	02/2023
186	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]	3/2020	330.78 -	330.78	67.50	12/2021 -	12/2021
187	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]	3/2020	154.51 -	154.51	42.33	07/2022 -	07/2022
188	DEMBUEN - BRUNI - [N24001321]	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
189	KHELLANI-KHANABAL PKG-1 - [N24001323]	3/2021	486.45 -	486.45	68.38	09/2022 -	09/2022
190	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	1.98	01/2023 -	01/2023
191	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	34.80	06/2023 -	06/2023
192	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79 -	355.79	70.73	06/2022 -	06/2022
193	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]	3/2020	216.49 -	216.49	59.06	07/2022 -	07/2022
194	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]	8/2020	199.03 -	199.03	58.18	04/2022 -	04/2022
195	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]	3/2020	216.49 -	216.49	42.19	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
196	IMPHAL - KHONGSANG PKG-3 - [N24001401]	7/2021	467.00 -	467.00	-	03/2023 -	03/2023
197	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	-	12/2022 -	12/2022
198	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]	3/2021	636.42 -	636.42	-	12/2022 -	12/2022
199	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) [N24001283]	3/2020	281.78 -	281.78	120.63	07/2022 -	07/2022
200	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	12.72	12/2022 -	12/2022
201	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	10.11	01/2023 -	01/2023
202	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]	3/2020	292.24 -	292.24	39.42	06/2022 -	06/2022
203	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
204	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) [N24001278]	3/2020	206.88 -	206.88	33.21	07/2022 -	07/2022
205	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]	3/2020	178.43 -	178.43	17.99	07/2022 -	07/2022
206	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	23.72	04/2022 -	04/2022
207	TAMENGLONG - MAHUR PKG-1 - [N24001402]	7/2021	185.80 -	185.80	-	03/2023 -	03/2023
208	2-LANING OF KHOWAI - AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]	9/2020	173.17 -	173.17	9.33	04/2022 -	04/2022
209	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	20.73	04/2022 -	04/2022
210	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
211	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	43.01	12/2022 -	12/2022
212	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]	8/2020	292.80 -	292.80	42.83	05/2022 -	05/2022
213	2-LANING OF KHOWAI - AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]	3/2020	165.54 -	165.54	8.23	07/2022 -	07/2022
214	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]	7/2020	345.38 -	345.38	86.64	04/2023 -	04/2023
215	MARIAM - PEREN (PKG 2A) - [N24001398]	7/2021	204.58 -	204.58	-	03/2023 -	03/2023
216	KHELLANI-KHANABAL PKG-5 - [N24001396]	7/2021	497.09 -	497.09	5.78	02/2023 -	02/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
217	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	30.07	06/2022 -	06/2022
218	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333	9/2019	761.54 -	761.54	140.46	05/2023 -	05/2023
219	TLABUNG - LUNGLEI PKG-A - [N24001358	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
220	TAMENGLONG - MAHUR PKG-3 - [N24001354	3/2021	234.08 -	234.08	9.86	12/2022 -	12/2022
221	DOGINALA - GAU - [N24001320	12/2020	242.30 -	242.30	-	09/2022 -	09/2022
222	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312	3/2020	167.95 -	167.95	50.50	06/2022 -	06/2022
223	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331	3/2020	261.13 -	261.13	23.56	06/2022 -	06/2022
224	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	369.00	09/2026 -	09/2026
225	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022
226	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
227	KARGIL-ZANSKR PACKAGE-6 - [N24001346	1/2021	239.81 -	239.81	36.62	05/2024 -	05/2024
228	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322	9/2020	183.31 -	183.31	76.84	05/2022 -	05/2022
229	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284	3/2020	361.53 -	361.53	38.95	06/2022 -	06/2022
230	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251	3/2019	402.94 -	402.94	69.72	04/2022 -	04/2022
231	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
232	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	32.85	04/2023 -	04/2023
233	TADADEGE - HENKAR - [N24001315	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023
234	MARIAM - PEREN (PKG 1B) - [N24001350	2/2021	188.36 -	188.36	-	12/2022 -	12/2022
235	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339	10/2020	157.86 -	157.86	55.86	04/2022 -	04/2022
236	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281	3/2020	292.24 -	292.24	59.29	07/2022 -	07/2022
237	KARGIL-ZANSKR PACKAGE-7 - [N24001347	1/2021	308.86 -	308.86	38.81	06/2024 -	06/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
238	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334	11/2020	445.51 -	445.51	173.17	12/2023 -	12/2023
239	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335	11/2020	284.21 -	284.21	40.21	12/2023 -	12/2023
240	LADDA - BASAI - [N24001316	2/2021	445.96 -	445.96	-	04/2023 -	04/2023
241	TAMENGLONG - MAHUR PKG-2 - [N24001403	7/2021	483.87 -	483.87	12.11	03/2023 -	03/2023
242	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
243	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308	11/2020	332.14 -	332.14	10.88	07/2022 -	07/2022
244	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022
245	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	7.02	04/2022 -	04/2022
246	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390	8/2020	228.71 -	228.71	40.08	04/2022 -	04/2022
<u>National Highways Authority Of India</u>							
247	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
248	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
249	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
250	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
251	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
252	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
253	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416	12/2020	989.66 -	989.66	-	01/2024 -	01/2024
254	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
255	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 -	01/2024
Total			68,589.95 -	68,628.46	6,590.94		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
256	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,967.38	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,967.38		
	<u>SOCIAL JUSTICE</u>						
	<u>Central Public Works Department</u>						
257	CENTRE FOR DISABILITY SPORTS - [N38000001	2/2019	170.99 -	170.99	34.00	03/2024 -	03/2024
	Total		170.99 -	170.99	34.00		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
258	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124	11/2015	2,907.00 -	2,907.00	547.05	06/2023 -	06/2023
	<u>Steel Authority Of India Limited (Sail)</u>						
259	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	81.14	12/2023 -	12/2023
260	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	51.69	05/2023 -	05/2023
	Total		3,826.42 -	3,826.42	679.88		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
261	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	373.31	03/2024 -	03/2024
262	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	419.43	03/2024 -	03/2024
	<u>Bangalore Metro Rail Corporation Limited</u>						
263	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151	6/2021	14,788.10 -	14,788.10	2,031.41	06/2026 -	06/2026
	<u>Delhi Metro Rail Corporation</u>						
264	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135	7/2019	24,948.65 -	24,948.65	2,711.33	03/2025 -	03/2025
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
265	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	354.67	02/2023 -	02/2023
266	INDORE METRO RAIL - [N28000125	11/2018	7,500.80 -	7,500.80	190.69	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
267	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	6,074.70	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
268	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,925.50	306.94	06/2024 -	06/2024
	Total		1,15,223.21 -	1,15,782.94	12,462.48		
	<u>WATER RESOURCES</u>						
	<u>Delhi Jal Board</u>						
269	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	251.88	12/2022 -	12/2022
	Total		665.78 -	665.78	251.88		
	Grand Total		6,16,961.00	6,27,414.03	1,02,571.49		

FLASH REPORT

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,840.00	6,054.37	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010	10/2009	11,459.00 -	16,580.00	17,427.00	12/2015 -	12/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027	10/2009	12,320.00 -	17,079.00	13,945.00	12/2016 -	12/2023	38.63
	Total		27,271.00 -	40,499.00	37,426.37			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073	10/2013	417.23 -	707.73	494.81	09/2018 -	06/2022	69.63
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077	06/2018	1,383.00 -	1,938.00	568.01	09/2021 -	12/2023	40.13
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078	07/2018	346.27 -	480.33	140.13	09/2021 -	06/2023	38.72
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083	12/2016	1,142.00 -	1,232.00	397.52	03/2021 -	03/2023	7.88
	Total		3,288.50 -	4,358.06	1,600.47			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
8	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194	10/2015	243.00 -	334.27	28.43	04/2018 -	10/2022	37.56
9	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195	12/2015	304.13 -	341.22	79.48	03/2017 -	10/2022	12.20
	<u>Central Coal Fields Limited</u>							
10	MAGADH EXPANSION OC(51 MTY) - [N06000015	08/2008	6,964.33 6,964.33	7,254.37	814.20	07/2012 03/2028	03/2028	4.16
	<u>Eastern Coal Fields Limited</u>							
11	RANIGANJ MASTER PLAN - [N06000163	08/2009	2,661.73 -	5,146.48	625.36	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	808.97	808.97	03/2013 -	03/2024	68.70
	<u>Neyveli Lignite Corporation</u>							
13	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,421.14	12/2015 -	02/2021	35.10
14	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	12,939.55	11/2021 -	11/2022	.00
	<u>Singareni Colliers Company Limited</u>							
15	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86
16	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	123.72	03/2019 -	03/2022	11.42
17	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	204.84	03/2015 -	03/2023	5.85
18	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	306.52	03/2015 -	03/2022	114.60
	<u>South-Eastern Coal Fields Limited</u>							
19	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	200.47	03/2015 -	03/2022	201.44
	<u>Western Coal Fields Limited</u>							
20	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	87.35	03/2023 -	03/2023	117.98
21	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	299.67	213.92	03/2019 -	03/2022	1.39
22	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	08/2015	727.28 -	745.03	423.42	03/2025 -	03/2025	2.44
23	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	145.94	03/2023 -	03/2024	15.41
24	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	327.41	162.29	03/2019 -	03/2022	7.52
25	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	08/2016	319.76 -	404.45	248.72	03/2022 -	03/2022	26.49
26	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	37.55	03/2022 -	03/2025	.00
	Total		37,788.39 -	44,126.90	25,287.94			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
27	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	301.90	06/2017 -	03/2022	.57
28	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	-	1.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
29	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	10.22
	Total		1,231.49 -	1,263.46	890.91			
	<u>DPIIT</u>							
	<u>Dmic For Dpiit</u>							
30	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	9,574.07	09/2019 -	07/2021	9.80
	<u>Iicc For Dpiit</u>							
31	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	3,044.41	12/2019 -	05/2022	8.49
	Total		17,352.09 -	18,990.30	12,618.48			
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Cpwd For Health</u>							
32	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>							
33	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	586.50	581.44	11/2013 -	09/2021	41.63
34	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021	22.29
35	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68
36	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
37	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71
38	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	16.33
39	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
40	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	273.41	03/2019 -	03/2021	.13
41	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	183.36	- -	12/2021	21.58
42	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	231.05	- -	01/2021	.02
	<u>Nbcc For Health</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
43	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	8.88
	Total		5,589.39 -	6,374.57	3,834.62			
	<u>HEAVY INDUSTRY</u>							
	<u>Natrip Implementation Society</u>							
44	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,727.30	3,526.63	09/2011 -	03/2021	116.96
	Total		1,718.00 -	3,727.30	3,526.63			
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
45	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	1,049.80	10/2019 -	05/2022	64.04
46	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	173.06	04/2018 -	08/2022	46.12
47	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI [N45000002]	06/2019	277.35 -	290.33	38.13	07/2022 -	12/2022	4.68
	Total		1,659.44 -	2,528.33	1,260.99			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
48	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11
49	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	793.01	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							
50	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,778.50	12/2012 -	08/2024	102.71
51	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49 -	345.15	255.92	04/2022 -	04/2022	20.06
52	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 -	247.90	75.63	02/2021 -	10/2022	9.91
53	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	234.40	08/2020 -	03/2022	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
54	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	17,704.50	07/2020 -	07/2022	25.50
55	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	2,673.55	06/2021 -	07/2022	14.76
	<u>Indian Oil Corporation Limited</u>							
56	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	553.03	10/2017 -	09/2022	103.60
57	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,225.58	03/2021 -	03/2022	66.09
58	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00	3,338.00	3,124.58	12/2020	03/2022	43.82
59	ENNORE THIRUVALUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	4,159.59	12/2018 -	02/2022	33.98
60	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	05/2016	348.00 -	437.00	209.30	01/2021 -	08/2022	25.57
61	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	04/2017	163.02 -	207.36	129.75	04/2020 -	07/2022	27.20
62	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	319.61	226.65	06/2020 -	12/2021	35.43
63	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	04/2018	206.63 -	340.76	164.11	02/2020 -	07/2022	64.91
64	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	03/2018	588.20 -	730.20	206.83	-	05/2023	24.14
65	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	06/2019	371.00 -	427.00	35.56	09/2022 -	03/2023	15.09
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
66	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	543.02	03/2020 -	12/2021	9.64
67	DEVANGONTHI MARKETING TERMINAL - [N16000401]	06/2020	200.00 -	304.00	2.58	06/2023 -	01/2024	52.00
	<u>Numaligarh Refinery Limited</u>							
68	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY - [N16000379]	01/2019	12,366.00 -	18,968.00	767.97	10/2024 -	10/2024	53.39
	<u>Oil & Natural Gas Corporation Limited</u>							
69	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.34	1,604.42	05/2013 -	05/2022	132.23

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
70	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,888.99	04/2018 -	05/2022	5.80
71	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	773.03	03/2023 -	03/2022	38.20
72	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	1,640.35	03/2022 -	05/2023	23.16
73	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	3,119.98	05/2021 -	01/2022	2.17
	<u>Oil India Limited</u>							
74	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	399.74	02/2020 -	12/2021	17.41
	Total		65,726.53 -	90,012.48	48,310.01			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
75	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62 -	1,311.05	199.40	06/2006 -	-	126.58
76	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	9,357.83	09/2009 -	03/2023	152.52
77	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	14,738.05	09/2010 -	08/2023	218.08
	<u>National Thermal Power Corporation</u>							
78	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	5,326.00	03/2013 -	09/2024	96.99
79	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	12,556.00	06/2019 -	09/2023	18.38
80	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	743.00	09/2019 -	12/2024	30.48
81	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	9,014.00	07/2012 -	11/2021	97.38
82	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	16,604.00	05/2018 -	03/2022	33.47
83	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	19,466.00	10/2011 -	07/2023	145.16
84	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	149.93	08/2017 -	-	17.95
85	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	9,124.00	11/2020 -	10/2022	3.76
86	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,684.86	10/2017 -	-	7.41
87	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]	05/2016	1,885.13 -	2,311.89	2,094.59	12/2018 -	01/2022	22.64

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
88	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	633.80	530.53	11/2018 -	03/2022	19.66
89	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 -	524.83	368.49	09/2021 -	10/2022	4.70
90	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 -	852.90	541.97	09/2021 -	08/2022	6.85
91	NOKHRA - [N18000282]	03/2020	1,722.14 -	1,803.19	552.18	09/2021 -	10/2022	4.71
92	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	130.88	10/2021 -	10/2022	11.93
93	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	06/2019	401.90 -	442.03	225.90	04/2021 -	01/2022	9.99
<u>Power Grid Corporation Of India Limited</u>								
94	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	13,038.20	08/2013 -	05/2023	32.24
95	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	480.89	11/2016 -	02/2022	4.61
96	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,911.97	12/2018 -	03/2024	92.02
97	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	3,326.92	12/2018 -	03/2022	31.08
98	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 -	02/2022	14.11
99	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	168.20	07/2019 -	03/2022	17.99
<u>Satluj Jal Vidyut Nigam Limited</u>								
100	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	785.06	12/2021 -	06/2022	46.20
<u>Thdc India Limited</u>								
101	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,356.86	06/2013 -	12/2024	54.94
102	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,374.66	02/2016 -	06/2023	191.23
	Total		1,08,986.44 -	1,74,215.58	135,949.80			
<u>RAILWAYS</u>								
<u>Central Railways</u>								
103	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023	8.75
104	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	75.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
105	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	325.00	325.52	03/2019 -	-	76.57
106	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	111.08
107	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
108	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.49	-	03/2024 -	-	25.04
109	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	.89
110	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							
111	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	434.63	03/2018 -	-	25.65
112	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
113	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	- -	-	143.17
114	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
115	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,650.00	3,661.29	- -	03/2022	253.32
116	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,597.10	- -	03/2023	290.95
117	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	722.71	03/2012 -	09/2021	57.27
118	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,080.00	1,086.41	03/2012 -	11/2022	232.58
119	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	352.68	- -	12/2023	277.26
120	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	459.31	03/2020 -	-	3.33
121	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	316.22	- -	03/2025	36.67
122	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	958.41	03/2019 -	12/2021	37.04
123	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	941.70	- -	03/2023	253.52
124	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	15.58	- -	-	32.26
125	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	2.55	- -	03/2024	818.15

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
126	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	390.81	- -	03/2021	126.22
127	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	391.01
128	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	4.99	- -	-	376.78
129	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) [N22000180]	04/2004	372.14 -	1,470.50	1,467.70	- -	03/2023	295.15
130	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	819.01	540.73	03/2020 -	12/2024	49.45
131	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	560.09	560.09	07/2014 -	-	68.63
132	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23 -	390.00	403.49	03/2021 -	03/2022	11.99
133	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	543.61	03/2021 -	03/2024	63.37
134	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	424.08	03/2021 -	03/2024	62.06
135	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	1,370.20	- -	03/2022	350.27
<u>East Coast Railway</u>								
136	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	933.16	06/2021 -	03/2025	137.80
137	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,687.63	03/2009 -	12/2024	29.71
138	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,195.24	02/2019 -	03/2022	38.43
139	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	1,012.35	03/2020 -	03/2023	.07
140	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	224.26	03/2020 -	03/2022	52.77
141	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	193.71	11/2018 -	03/2024	15.45
<u>Eastern Railways</u>								
142	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	912.61	03/2019 12/2009	03/2025	36.22
143	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	638.35	02/2013 -	03/2024	134.80
144	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	507.59	03/2017 -	03/2025	20.30
145	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	1.76	- -	03/2025	44.46

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
146	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	495.10	316.82	-	03/2022	181.63
147	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017	03/2026	12.02
148	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	30.12	03/2005	03/2025	.01
149	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	36.13	-	03/2025	.25
150	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	142.05	02/2012	03/2025	36.15
151	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	410.29	-	03/2024	23.82
152	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	303.23	-	03/2022	6.48
153	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.31	03/2006	03/2025	34.08
154	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	-	-	03/2025	180.30
155	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	11.77	-	03/2025	51.19
156	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	453.42	03/2022	03/2025	133.39
157	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	521.63	-	03/2021	74.26
158	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	618.75	03/2016	03/2025	7.75
159	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	97.40	03/2017	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>								
160	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	953.27	03/2022	09/2023	117.23
161	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018	06/2022	.00
<u>Metropolitan Rapid Transport Projects</u>								
162	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006	-	224.37
163	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,868.04	03/2004	06/2022	501.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
164	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	774.51	492.88	06/2013 -	07/2022	56.23
165	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	75.91
	<u>North Central Railway</u>							
166	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	471.73	03/2022 -	12/2024	32.02
167	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	531.20	03/2020 -	01/2022	1.69
	<u>North East Frontier Railway</u>							
168	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	275.06	03/2019 -	-	106.51
169	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	6,527.00	4,525.01	03/2014 -	12/2023	172.70
170	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,936.64	12/2008 -	12/2021	284.80
171	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.00	12,012.77	03/2011 -	12/2023	221.54
172	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,043.00	919.48	03/2019 -	03/2023	170.77
173	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	1,029.65	03/2019 -	03/2024	302.54
174	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,663.00	1,420.48	03/2015 -	03/2026	186.39
175	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	6.74	- -	-	7.86
176	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	1,856.78	12/2015 -	12/2023	542.04
177	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,042.51	446.24	03/2019 -	12/2023	13.60
178	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	38.20	- -	-	71.62
179	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	612.37	03/2020 -	06/2022	30.26
180	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	4,083.02	264.34	03/2021 -	-	350.44
181	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	76.57	03/2020 -	-	94.45
182	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	333.46	- -	06/2022	54.80
183	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	157.51	03/2020 -	-	80.79

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
184	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,090.60	1,089.12	- -	-	33.13
185	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,939.39	03/2022 -	03/2023	32.15
186	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,586.23	03/2021 -	03/2022	115.07
187	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	1,167.00	1,095.12	12/2021 -	10/2021	93.77
188	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	186.55
North Eastern Railway								
189	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	0.15	- -	-	60.34
190	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	- -	-	358.99
191	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	116.44	12/2021 -	12/2021	267.13
192	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	610.00	595.91	01/2019 -	02/2022	106.78
193	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	- -	-	.16
194	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	1,824.00	1,465.45	03/2022 -	03/2022	40.80
195	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	72.08	04/2016 -	12/2021	.16
196	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	127.77
197	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	-	01/2018 -	-	.15
198	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	800.00	145.14	- -	12/2023	32.78
North Western Railway								
199	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	769.95	02/2019 -	06/2022	109.82
200	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	334.01	03/2020 -	10/2022	16.97
201	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	2,215.27	4.60	- -	-	153.55
202	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	191.39	- -	-	104.65
203	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	420.18 -	480.00	384.12	03/2020 -	09/2021	14.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Northern Railway</u>							
204	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	116.87	- -	03/2024	129.17
205	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	745.06	12/2011 -	06/2021	211.31
206	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	597.99	- -	09/2023	134.90
207	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	160.79	- -	09/2023	41.71
208	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	1.73	- -	03/2024	310.24
209	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	878.49	07/2012 -	11/2024	348.44
210	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	26,237.89	11/2002 -	12/2022	1,017.96
211	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	243.28	03/2023 -	12/2025	369.35
212	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	839.00	839.36	03/2016 -	-	34.24
	<u>Rail Vikas Nigam Ltd.</u>							
213	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,894.70	02/2015 -	06/2022	102.92
214	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	419.58	03/2009 03/2009	-	224.56
215	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	1,460.93	03/2016 -	03/2025	59.22
216	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	1,905.63	12/2026 -	12/2025	127.62
217	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	2,477.01	03/2023 -	12/2022	41.04
218	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	3,317.94	03/2016 -	03/2025	7.78
219	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95
220	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	3,753.96	03/2020 -	03/2022	124.58
221	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,650.00	1,737.74	12/2021 -	12/2021	69.12
222	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	942.56	03/2021 -	12/2021	35.42
223	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	2,201.29	12/2021 -	03/2022	20.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
224	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	839.78	03/2016 -	12/2021	50.15
225	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	3,515.82	12/2023 -	12/2023	9.32
226	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	982.28	03/2022 -	12/2024	5.98
227	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	949.03	12/2024 -	12/2024	9.83
228	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	1,438.92	03/2019 -	06/2022	51.02
229	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	5,917.58	12/2024 -	03/2025	40.08
230	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,900.00	2,041.94	03/2020 -	12/2021	306.46
231	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	2,024.04	12/2024 -	12/2026	42.47
232	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	2,156.59	03/2020 -	12/2021	111.91
233	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	1,269.37	03/2019 -	06/2022	62.89
234	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	1,777.07	12/2020 -	12/2022	54.24
235	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	2,355.40	12/2020 -	12/2021	23.55
236	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,509.71	03/2020 -	06/2022	102.11
	<u>Railway Electrification</u>							
237	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
238	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,042.28	03/2009 -	03/2024	102.85
239	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	1,373.74	654.79	03/2010 -	03/2024	18.38
240	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	-	-	161.86
241	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	729.57	03/2023 -	03/2024	5.16
242	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	691.26	03/2020 -	02/2022	31.75
243	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	42.44
244	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	2,010.00	03/2000 -	03/2023	98.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
245	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,388.38	03/2022 -	03/2024	7.06
246	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	242.28	67.29	03/2022 -	-	102.36
	<u>South East Central Railway</u>							
247	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,176.60	1,492.13	03/2023 -	12/2023	66.44
248	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	1,123.85	02/2019 -	12/2021	116.46
249	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	1,096.00	40.47	12/2021	12/2024	378.60
250	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	733.21	03/2021 -	12/2023	8.23
251	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	838.56	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>							
252	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
253	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	41.78	- -	03/2025	131.89
254	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
255	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	266.61	239.38	03/2015 -	03/2019	77.86
256	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	1,119.38	03/2020 -	06/2022	35.38
257	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
258	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 -	472.50	1.61	06/2022 -	12/2025	10.23
259	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39 -	511.75	110.13	12/2021 -	06/2022	31.09
260	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 -	393.83	22.39	06/2022 -	06/2023	16.52
	<u>South Western Railway</u>							
261	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	2,161.36	82.81	- -	12/2023	20.01
262	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	325.32	03/2016 -	12/2026	55.13
263	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	-	- -	12/2023	24.09
264	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	- -	12/2023	57.65

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
265	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,404.03	1,100.11	- -	12/2025	16.57
266	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	-	- -	12/2023	12.38
267	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	158.11	- -	12/2024	123.51
268	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2024	.02
269	HUBLI- CHIKKAJUR - [N22000325]	03/2015	1,156.94 -	1,954.21	1,205.02	03/2020 -	03/2023	68.91
270	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,104.00	983.01	03/2020 -	09/2021	28.31
271	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	760.00	647.09	03/2020 -	01/2022	31.49
272	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	1,496.77	03/2019 -	03/2024	16.31
273	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	732.89	495.11	03/2017 -	03/2025	13.67
	<u>Southern Railway</u>							
274	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	3,081.20	1,718.56	02/2019 -	03/2025	325.17
275	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,154.43	239.59	- -	12/2025	441.23
276	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,549.09	712.68	03/2020 -	03/2025	409.60
277	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	264.51	- -	-	79.80
278	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	247.32
279	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	2.28	- -	03/2030	130.17
280	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	839.01	0.63	- -	03/2030	.00
281	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	749.40	578.46	- -	03/2022	177.41
282	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	709.69	256.70	- -	03/2025	180.55
283	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.23	1.68	- -	03/2030	109.04
284	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	608.13	427.75	- -	02/2022	269.89
285	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,122.00	994.02	- -	12/2022	20.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
286	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	448.10	268.73	- -	03/2025	136.79
287	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	308.35	03/2019 -	12/2027	1,699.64
288	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	0.82	- -	03/2025	33.90
289	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	991.83	922.01	03/2005 -	-	268.89
	<u>West Central Railway</u>							
290	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,411.38	03/2021 -	03/2024	585.35
291	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	3,230.57
292	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.98 -	2,445.30	1,345.52	03/2020 -	03/2024	38.63
293	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	16.02
294	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	540.13	03/2022 -	12/2023	114.32
	<u>Western Railway</u>							
295	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,171.08	2,327.60	03/2022 -	03/2023	76.13
296	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	126.35	03/2012 -	10/2023	1.06
297	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,223.37	1,966.82	03/2020 -	03/2024	167.96
298	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	1,004.89	03/2022 -	03/2023	13.17
299	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2023	329.77
300	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	33.41
301	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,042.12	730.07	03/2021 -	12/2022	3.96
302	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM [N22000434]	03/2010	265.88 -	311.36	-	- -	-	17.11
303	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]	03/2012	217.38 -	393.62	152.98	- -	-	81.07
304	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]	03/2012	248.26 -	528.49	123.75	- -	-	112.88
305	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 [N22000437]	03/2012	153.83 -	154.15	109.05	- -	-	.21

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
306	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504	04/2017	692.25 -	742.88	0.89	03/2020 -	03/2024	7.31
	Total		2,35,664.70 -	4,84,630.20	230,303.71			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
307	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	978.43	03/2011 -	-	58.98
308	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	323.23	10/2010 -	-	69.30
309	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	229.77	08/2015 -	-	3.84
310	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	01/2014	282.41 -	319.96	193.56	03/2016 -	04/2022	13.30
311	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	244.36	- -	-	3.72
312	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	319.68	09/2017 -	-	36.24
313	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	346.72	05/2017 -	05/2022	45.75
314	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	851.32	- -	-	1.75
315	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	368.39	10/2010 -	-	93.80
316	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	333.28	- -	-	15.67
317	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	.26
318	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	101.27	06/2016 -	-	.02
319	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	116.25	- -	-	.06
320	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	148.90	11/2019 -	10/2021	.08

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
321	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	174.90	154.26	08/2018 -	02/2022	5.23
322	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	120.51	11/2018 -	03/2022	7.39
323	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	27.15	08/2019 -	11/2022	33.51
324	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	78.47	08/2019 -	08/2022	11.18
325	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	331.86	08/2017 -	02/2020	42.48
326	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	182.97	08/2018 -	02/2022	4.45
327	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING-KM 193/0 TO KM - [N24000899	03/2016	877.79 -	949.54	794.73	06/2019 -	01/2022	8.17
328	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	333.09	12/2015 -	-	6.07
329	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	169.64	07/2019 -	-	.31
330	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	404.69	03/2018 -	02/2022	9.23
331	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 -	318.28	195.88	01/2019 -	-	7.06
332	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 -	386.41	347.46	10/2018 -	-	18.58
333	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	369.96	322.13	09/2019 -	-	10.03
334	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	308.85	09/2014 -	-	72.36
335	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	1,251.08	- -	-	2.93
336	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	12.16
337	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 -	319.96	117.56	- -	03/2022	13.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
338	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	284.86	08/2016 -	06/2022	15.19
339	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	400.87	09/2016 -	03/2022	14.24
340	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	476.86	10/2016 -	06/2022	17.04
341	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	01/2017	197.67 -	236.18	59.74	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
342	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 -	252.79	153.14	04/2017 -	03/2022	29.48
343	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 -	263.31	155.10	04/2017 -	03/2022	29.48
344	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	352.25	08/2016 -	05/2021	3.73
345	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]	01/2017	198.22 -	252.05	157.83	04/2017 -	03/2022	27.16
346	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	295.14	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>							
347	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	612.58	612.58	02/2009 -	-	118.78
348	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	-	04/2009 -	-	70.23
349	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	435.78	-	11/2008 -	-	159.95
350	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	255.23	-	11/2008 -	-	64.62
351	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	655.17	07/2009 -	-	234.27
352	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,450.00	11/2011 -	-	106.50
353	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
354	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
355	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	16.67

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
356	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66
357	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	578.00	11/2013 -	-	15.53
358	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	459.07	01/2014 -	-	61.08
359	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 -	417.68	433.68	01/2016 -	-	18.88
360	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 -	627.93	633.24	01/2016 -	-	26.66
361	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13	744.73	706.78	05/2018	03/2022	40.22
362	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	277.34	-	-	.77
363	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	717.24	627.25	05/2018 -	06/2022	20.90
364	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	902.51	-	01/2020	11.33
365	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,827.15	989.55	06/2018 -	-	68.71
366	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	09/2015	934.46 -	1,457.82	1,305.69	03/2018 -	-	56.01
367	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	821.37	-	10/2021	1.37
368	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
369	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	527.80	-	-	6.11
370	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	278.12	-	-	1.33
371	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67 -	1,096.52	518.73	04/2018 -	-	50.90
372	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,511.67	-	-	41.78
373	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,034.47	-	-	21.50
374	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	651.24	04/2018 -	-	25.80
375	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 -	987.94	-	-	-	44.60
376	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
377	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	353.42	- -	04/2021	7.53
378	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 -	486.00	406.73	- -	-	6.11
379	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	14.40
380	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,367.00	- -	-	94.94
381	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	322.26	08/2018 -	-	3.98
382	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,481.35	08/2019 -	-	16.55
383	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	1,355.00	- -	-	4.10
384	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	359.60	340.15	- -	05/2017	23.69
385	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	723.26	07/2018 -	-	19.25
386	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]	01/2017	1,251.11 -	1,361.00	451.40	- -	-	8.78
387	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	1,297.83	03/2020 -	-	10.58
388	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	-	03/2020 -	-	31.88
389	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	-	03/2020 -	-	3.40
390	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	-	03/2020 -	-	5.56
391	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	1.06
392	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	-	03/2020 -	-	5.70
393	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	449.44	03/2020 -	09/2022	.23
394	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	99.86	03/2020 -	-	9.38
395	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	968.97	03/2020 -	-	13.97

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
396	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	1,058.45	03/2020 -	-	10.24
397	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	18.50
398	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	41.54
399	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48/O - [N24000675]	03/2017	993.16 -	1,434.00	1,319.54	03/2020 -	-	44.39
400	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	3.95
401	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	1.78
402	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,300.00	655.89	09/2017 -	-	15.65
403	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]	12/2017	404.94 -	448.18	495.92	-	09/2021	10.68
404	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 -	276.17	120.40	-	-	.99
405	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 -	1,853.42	14.19	-	-	30.09
406	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 -	1,296.93	346.17	-	01/2022	11.20
407	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 -	2,400.00	3,439.59	-	11/2021	20.28
408	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 -	2,450.00	2,542.30	-	-	12.50
409	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]	03/2018	1,261.98 -	1,952.20	97.16	-	-	54.69
410	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 -	1,197.00	1,176.70	-	-	29.35
411	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 -	1,332.00	1,525.15	-	-	18.87
412	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 -	1,361.00	451.40	-	-	29.35

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
413	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	1,009.50	03/2021 -	07/2021	63.05
414	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	78.33	- -	-	8.26
415	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	402.95	- -	03/2021	22.44
416	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	339.86	- -	01/2022	5.32
417	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	- -	12/2021	4.99
418	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	- -	11/2021	.12
419	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	925.96	341.09	- -	02/2018	45.89
420	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	922.64	387.49	- -	02/2018	15.98
421	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	03/2018	478.74 -	1,135.08	760.86	- -	-	137.10
422	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	724.40	- -	-	25.68
423	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	490.00	- -	12/2021	.00
424	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	422.00	- -	11/2022	27.86
425	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	609.00	- -	10/2022	305.58
426	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 -	732.34	316.43	11/2019 -	-	.06
427	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	200.10	11/2019 -	-	2.02
	Total		89,491.73 -	1,11,873.62	78,853.70			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
428	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	19,538.23	05/2015 -	03/2022	41.32
	<u>Rastrya Ispat Nigam Limited</u>							
429	FORGED WHEEL PLANT - [N12000116]	04/2014	1,682.85 -	2,100.00	1,767.98	09/2018 -	09/2021	24.79
	Total		17,207.85 -	24,040.00	21,306.21			
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
430	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	84.97
	Total		13,334.00	24,664.00	20,545.00			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
431	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	9,834.10	12/2018 -	08/2022	18.69
	<u>Bangalore Metro Rail Corporation Limited</u>							
432	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	02/2014	26,405.14 -	30,695.12	19,410.15	02/2019 -	03/2025	16.25
	<u>Central Public Works Department</u>							
433	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33 -	217.00	187.08	04/2019 -	02/2022	9.97
	<u>Chennai Metro Rail Ltd</u>							
434	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	18,380.00	17,619.68	12/2015 -	02/2019	25.89
	<u>Kochi Metro Rail Corporation Ltd</u>							
435	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	6,065.82	07/2017 -	09/2020	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>							
436	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	20,051.98	03/2020 -	03/2023	44.39
	<u>Patna Metro Rail Corporation</u>							
437	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 -	13,925.50	306.94	06/2024 -	06/2024	4.19
	Total		93,659.03 -	1,15,628.76	73,475.75			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>WATER RESOURCES</u>							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
438	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027	10/2017	254.13 -	413.29	0.05	09/2020 -	03/2024	62.63
439	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	398.90	294.30	03/2020 -	02/2022	76.68
	<u>Kolkata Metropolitan Development Authority</u>							
440	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032	05/2018	198.43 -	224.69	-	02/2022 -	03/2024	13.23
	<u>Polavaram Project Authority</u>							
441	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04	55,548.87	18,335.60	03/2020	04/2022	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
442	FARRUKHABAD I AND D AND STP WORKS - HAM - [N30000008	10/2017	213.62 -	261.12	-	03/2022 -	04/2024	22.24
443	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020	02/2011	279.91 -	330.05	260.12	12/2019 -	11/2021	17.91
444	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 -	234.03	28.36	12/2021 -	12/2022	.97
445	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	1.31
	Total		12,236.47 -	58,101.66	18,918.43			
	Grand Total		7,32,205.05	12,05,034.22	714,109.02			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (December 2021)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00	6,840.00	6,054.37	09/2010	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00	16,580.00	17,427.00	12/2015	12/2022	84	44.69	
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00	39,849.00	27,505.00	11/2020	11/2023	36	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00	17,079.00	13,945.00	12/2016	12/2023	84	38.63	
	Total		67,120.00	80,348.00	64,931.37					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28	402.00	397.85	06/2019 12/2021	01/2022	31	-8.28	NIL
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00	458.00	161.87	03/2020 06/2022	04/2022	25	0	NIL
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	417.23 707.73	707.73	494.81	09/2018 06/2022	06/2022	45	69.63	NIL
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	303.80 351.21	303.80	203.38	04/2020	06/2022	26	0	NIL
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]AAI, MAHARASHTRA	03/2017	475.39	475.39	184.10	04/2021	08/2022	16	0	NIL

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
10	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86	456.86	329.56	09/2020	09/2022	24	0	NIL
11	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH	02/2019	645.63	645.63	186.02	08/2022	11/2022	3	0	Working permission for diversion of kokila river, Shifting of 132 KV Power Grid line, Acquisition of 5 acres of Assam land, Construction of boundary wall, Construction of four lane approach road to Airport.
12	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28	951.28	513.93	10/2021	12/2022	14	0	NIL
13	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24	412.24	224.31	06/2021	12/2022	18	0	Nil
14	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10	177.10	108.20	02/2020 12/2021	12/2022	34	0	1. A portion of the site measuring 3.42 acres is fouling in the Runway extension and Basic Strip due to which the work will be delayed further 2. High mast transmission towers in the approach path of Runway 08 to be shifted by APTRANSCO (Govt. of AP undertaking) for final commissioning of the Project and this part of the work is yet to physically start. However work order is placed by State Government and agency mobilizing Men,materials & Machinery for the work.
15	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00	1,232.00	397.52	03/2021 03/2022	03/2023	24	7.88	Transportation strike from 1st week of November 2020, to end of the month at CEMENT Plant in Govt, of Assam & Meghalaya.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
16	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI, GUJARAT	01/2018	1,405.00 -	1,405.00	396.18	08/2022 -	03/2023	7	0	1) Resolving land swapping of Doshaliguna village. 2) Removal of structures of Lomakotadi village coming inside operational area. 3) Relocation of Juna Hirasar village 4) Relocation of wind mills.
17	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI, WEST BENGAL	01/2019	389.71 -	389.71	216.37	11/2021 04/2023	04/2023	17	0	2
18	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI, LADAKH	07/2018	346.27 -	480.33	140.13	09/2021 12/2022	06/2023	21	38.72	NIL
19	CCS INTERNATIONAL AIRPORT, LUCKNOW - [N04000077]AAI, UTTAR PRADESH	06/2018	1,383.00 1,938.00	1,938.00	568.01	09/2021 -	12/2023	27	40.13	NIL
20	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI, BIHAR	05/2018	1,216.90 -	1,216.90	249.46	10/2022 -	12/2023	14	0	AUGMENTATION OF STORM WATER DRAINAGE SYSTEM FOR CONNECTING NEW STORM WATER SYSTEM OF AIRPORT WITH ENLARGED CAPACITY.
21	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]AAI, TELANGANA	05/2020	353.61 -	353.61	95.77	05/2022 -	12/2023	19	0	NIL
22	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00 -	2,467.00	763.60	02/2022 -	06/2024	28	0	NIL
	Total		13,439.30 -	14,472.58	5,631.07					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
23	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	285.81	05/2014 -	03/2022	94	0	
24	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	334.27	28.43	04/2018 -	10/2022	54	37.56	
25	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	341.22	79.48	03/2017 -	10/2022	67	12.2	
26	MOONDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	508.61	03/2019 -	02/2023	47	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
27	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52	555.52	5.87	03/2021	03/2023	24	0	
28	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88	339.88	89.42	04/2014	04/2023	108	0	
	<u>Central Coal Fields Limited</u>									
29	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	124.85	03/2011	03/2022	132	0	
30	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	500.91	03/2016	03/2022	72	0	
31	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	93.13	03/2014	03/2022	96	0	
32	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND	08/2008	6,964.33	7,254.37	814.20	07/2012	03/2028	188	4.16	
33	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND	02/2012	4,983.58	4,983.58	370.76	03/2020	03/2028	96	0	
	<u>Eastern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
34	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73	5,146.48	625.36	08/2019	08/2024	60	93.35	i). Publication of final figure of Demographic survey report for Non-ECL houses by ADDA. ii). Publication of valuation of immovable properties for LTH households by ADDA to assess the financial implications for payment of cash compensation to affected beneficiaries. iii). Identification and finalization of balance 33.69 Ha land in non-coal bearing areas for construction of remaining flats in connection with implementation of this rehabilitation project. iv). As per resolution of review meeting taken by Sec(coal), CMPDI, RI-1 has identified land areas both in non-coal bearing and deep-seated coal bearing measures and report was sent to ADDA for utilization in rehabilitation purpose. WB Govt. is examining the status of encumbrance free land areas. Communication in this regard is yet to be received from State authority. v). Furthermore, CMPDI has examined the stability status of 192.74 acres Govt. vested land out of the list submitted by CEO, ADDA. The report was communicated to ADDA to check the encumbrance free status of land areas. Out of this 192.74 acres, ADDA has accepted only 37.23 acres encumbrance free land areas belong to mouza Mahatadih for rehabilitation purpose. The examination of encumbrance free status of balance 155.51 acres vested land areas is under way by concerned Deptt. of WB Govt. However, no updated status on the matter has yet been received from ADDA. vi). Shifting of affected families (on the basis of priority list to be prepared as per vulnerability of

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
35	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05	1,055.05	714.63	03/2018	03/2029	132	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2. Expediting the work of tree felling for hand over of 32.65 Ha forest land.
	<u>Mahanadi Coal Fields Limited</u>									
36	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53	808.97	808.97	03/2013	03/2024	132	68.7	
37	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15	479.15	254.06	03/2019	03/2024	60	0	
38	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38	1,375.38	683.47	03/2021	09/2025	54	0	
39	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY) - [N06000035]MCL, ODISHA	12/2007	8,416.19	8,416.19	1,166.07	03/2013	03/2028	180	0	
40	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY) - [N06000044]MCL, ODISHA	12/2007	3,504.21	3,504.21	606.54	03/2010	03/2029	228	0	
41	BHUBANESWARI EXPANSION OCP(40.0 MTY) - [N06000034]MCL, ODISHA	12/2007	3,145.45	3,145.45	661.05	03/2017	03/2031	168	0	
	<u>Neyveli Lignite Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
42	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00	17,237.80	12,939.55	11/2021 11/2022	11/2022	12	0	A.Land Acquisition (52.33 hectare) *Total Pocket land to be registered- 52.33ha (as per initial approval) *Total Pocket land registered- 46.2688 ha (as per current reconciliation) *Encumbrance Certificate has been received for all the registered land. *Balance 6.0612 ha is under acquisition. B.Railway Siding Land Acquisition (181.2663 hectare) *Total land is 181.2663 ha. *Total land acquired is 166.5853 ha. *Balance 14.681 ha land is in process of acquisition. C.PPA with UP Govt. for balance 25% power allocated by MoP (GoI) *PPA for 75% already signed with UPPCL for period of 25 years. *MoP has allocated 1843.68 MW power from GTPP to UP state on 02.01.2020 (136.32 MW shall remain unallocated). *Vide letter dated 11.02.2020, NUPPL requested UPPCL to sign the amended PPA agreement. *For signing of balance PPA, UPERC conducted three e-hearings on 21.07.2020, 28.08.2020 and 15.04.2021. *Vide letter dated 02.11.2021, NUPPL requested UPPCL for seeking permission from Honorable UPERC for permitting to generate and schedule up to 1279 MW (approved power limit of GTPP) from Unit-I and Unit-II so that NUPPL will be able to feed the entire power generated to the state of UP. *Next e-hearing is yet to be scheduled.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
43	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	37.83	08/2022 -	09/2023	13	0	
44	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	496.19	06/2015 03/2025	03/2025	117	-51.37	
	<u>Northern Coal Fields Limited</u>									
45	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	902.52	03/2021 -	03/2022	12	0	
46	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	481.57	03/2022 -	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
47	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	143.08	03/2015	03/2022	84	-32.3	
48	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	306.52	03/2015 -	03/2022	84	114.6	
49	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	144.15	07/2016 -	03/2022	68	-7.91	
50	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	123.72	03/2019 -	03/2022	36	11.42	
51	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	256.54	03/2019 -	03/2022	36	0	
52	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	16.86	
53	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	204.84	03/2015 -	03/2023	96	5.85	
	<u>South-Eastern Coal Fields Limited</u>									
54	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	200.47	03/2015 03/2020	03/2022	84	201.44	
55	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	232.34	03/2014 -	03/2023	108	0	
56	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	0	
57	AMGAON OPENCASE PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	149.09	03/2020 -	03/2023	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
58	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	68.86	03/2021 -	03/2024	36	0	
59	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	100.68	03/2021 04/2024	04/2024	37	0	
60	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH	07/2015	231.92 -	231.92	1.82	03/2022 -	03/2025	36	0	
61	AMADAND OPENCASET EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	129.53	03/2021 -	03/2025	48	0	
62	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	08/2015	1,186.64 -	1,186.64	243.93	03/2023 -	03/2026	36	0	
63	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.95	03/2014 -	03/2026	144	0	
64	DURGAPUR OPENCASET PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	0	
65	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2027	48	0	
66	MADANNAGAR OPENCASET PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	0	
	Western Coal Fields Limited									
67	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 299.67	299.67	213.92	03/2019 03/2022	03/2022	36	1.39	
68	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 327.41	327.41	162.29	03/2019 -	03/2022	36	7.52	
69	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA	11/2018	318.14 -	318.14	223.12	03/2021 09/2022	09/2022	18	0	
70	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	107.27	03/2021 09/2022	09/2022	18	0	
71	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	298.78	03/2021 09/2023	09/2023	30	0	
72	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 333.43	333.43	145.94	03/2023 -	03/2024	12	15.41	
73	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	159.36	03/2021 03/2024	03/2024	36	0	
74	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	37.55	03/2022 03/2025	03/2025	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
75	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 826.80	826.80	283.28	03/2020 03/2026	03/2026	72	-2.91	
76	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	281.25	23.52	03/2022 03/2026	03/2026	48	0	
77	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA	11/2014	1,184.33 -	1,184.33	393.29	03/2020 03/2027	03/2027	84	0	
	Total		75,193.53 -	78,249.01	28,115.99					
	<u>FERTILISERS</u>									
	<u>National Fertiliser Limited</u>									
78	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N0800014]NFL,HARYANA	01/2018	215.92 -	215.92	184.57	11/2019 06/2021	12/2021	25	0	
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
79	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72 -	426.72	324.01	04/2020 01/2022	01/2022	21	0	
	Total		642.64 -	642.64	508.58					
	<u>MINES</u>									
	<u>Central Public Works Department</u>									
80	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]CPWD, WEST BENGAL	04/2019	255.37 255.37	255.37	.86	04/2022 12/2024	12/2024	32	0	
	<u>National Aluminum Company Limited (Nalco)</u>									
81	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	355.00	95.45	11/2020 -	12/2023	37	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
82	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO, ODISHA	11/2017	483.00 483.00	483.00	10.40	04/2021 12/2023	12/2023	32	0	
83	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO, ODISHA	12/2014	5,540.00 6,435.90	5,540.00	1,182.87	04/2021 01/2024	01/2024	33	0	
	Total		6,633.37 -	6,633.37	1,289.58					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
84	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	19,538.23	05/2015 01/2022	03/2022	82	41.32	
	<u>Steel Authority Of India Limited (Sail)</u>									
85	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	209.03	06/2019 12/2021	02/2022	32	0	
86	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	566.58	10/2017 12/2021	11/2022	61	0	
	Total		16,821.88 -	23,236.88	20,313.84					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
87	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL, KARNATAKA	10/2018	206.26 -	206.26	163.25	03/2021 -	12/2021	9	0	
88	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	1,507.24	793.01	06/2019 -	02/2022	32	35.54	
89	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	640.00	368.06	12/2021 -	06/2022	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
90	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66	117.11	
91	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	248.55	142.91	06/2022 -	09/2022	3	0	
92	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	260.89	02/2021 -	03/2023	25	0	
93	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA	08/2019	1,607.00 -	1,607.00	304.87	08/2022 -	06/2023	10	0	
	<u>Chennai Petroleum Corporation Limited</u>									
94	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	315.00	295.84	08/2020 -	12/2021	16	-25.18	
	<u>Gas Authority Of India Limited</u>									
95	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,653.50	12/2020 -	01/2022	13	-30.59	
96	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 -	1,933.00	1,584.90	12/2020 12/2021	03/2022	15	0	
97	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00 -	2,433.00	2,213.00	12/2020 12/2021	03/2022	15	0	
98	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00 3,048.00	3,048.00	2,230.20	12/2020 12/2021	03/2022	15	-11.32	
99	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	234.40	08/2020 12/2021	03/2022	19	14.17	
100	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 217.92	217.92	105.90	04/2021 03/2022	03/2022	11	0	
101	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	198.90	04/2018 -	06/2022	50	-38.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
102	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	75.63	02/2021 -	10/2022	20	9.91	
103	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	1,008.20	12/2020 12/2021	06/2023	30	0	
104	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 3,060.00	3,060.00	2,705.00	12/2021 -	06/2023	18	-7.5	
105	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,778.50	12/2012 02/2022	08/2024	140	102.71	
	<u>Hindustan Petroleum Corporation Limited</u>									
106	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	303.40	224.20	03/2021	12/2021	9	0	
107	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	105.40	07/2020 -	01/2022	18	0	
108	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	194.72	06/2020 -	03/2022	21	0	
109	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	127.30	06/2020 -	03/2022	21	0	
110	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA	06/2018	380.00 -	380.00	339.20	11/2021 03/2022	03/2022	4	0	
111	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	210.94	128.96	08/2021 -	03/2022	7	0	
112	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	17,704.50	07/2020 07/2022	07/2022	24	25.5	
113	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 -	3,072.00	2,673.55	06/2021 08/2022	07/2022	13	14.76	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	193.31	09/2026 02/2027	02/2027	5	0	
115	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	515.69	03/2029 08/2029	08/2029	5	0	
116	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL	03/2019	5,830.20 -	5,830.20	146.12	03/2031 08/2031	08/2031	5	0	1. Laying of Gas pipeline along across NH-2 Application made by company in August 2020 for laying of Gas pipeline along across NH-2 for 22 km in Hooghly District to National Highway Authority of India. Permission awaited from PD PIU Durgapur NHAI Complex, Durgapur, WB. Assistance is sought for expediting the issue of demand note permissions to lay the CGD pipeline along across NH-2
	<u>Indian Oil Corporation Limited</u>									
117	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU	12/2016	228.00 -	228.00	160.74	11/2021 -	12/2021	1	0	
118	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 319.61	319.61	226.65	06/2020 12/2021	12/2021	18	35.43	
119	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	315.00	228.42	12/2021 08/2021	01/2022	1	0	
120	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	178.65	01/2021 06/2021	01/2022	12	0	
121	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	4,159.59	12/2018 02/2022	02/2022	38	33.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
122	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	470.06	02/2020 02/2022	02/2022	24	0	
123	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,225.58	03/2021 12/2021	03/2022	12	66.09	
124	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 3,338.00	3,338.00	3,124.58	12/2020 03/2022	03/2022	15	43.82	
125	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	606.58	07/2018 05/2021	03/2022	44	0	
126	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	279.29	10/2020 01/2022	03/2022	17	0	
127	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	167.51	03/2021 09/2021	03/2022	12	0	
128	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	136.20	08/2020 03/2022	03/2022	19	0	
129	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	360.74	02/2020 10/2021	03/2022	25	0	
130	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	399.21	03/2021 12/2021	03/2022	12	0	
131	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	883.78	10/2021 -	03/2022	5	0	
132	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	316.20	142.62	10/2021 03/2022	03/2022	5	0	
133	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	504.26	01/2021 03/2022	03/2022	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
134	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383] IOCL, HARYANA	09/2019	164.69 -	164.69	30.12	07/2021 03/2022	03/2022	8	0	
135	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340] IOCL, HARYANA	08/2018	1,636.00 -	1,636.00	954.75	08/2020 04/2022	04/2022	20	0	
136	SITARGANJ LPG PROJECT - [N16000282] IOCL, UTTARAKHAND	02/2017	160.10 -	160.10	105.42	02/2020 06/2021	06/2022	28	0	
137	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361] IOCL, ODISHA	11/2018	462.30 -	462.30	140.65	09/2021 06/2022	06/2022	9	0	
138	KHARAGPUR LPG BOTTLING PLANT - [N16000300] IOCL, WEST BENGAL	04/2017	163.02 207.36	207.36	129.75	04/2020 10/2021	07/2022	27	27.2	
139	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321] IOCL, HARYANA	04/2018	206.63 340.76	340.76	164.11	02/2020 07/2022	07/2022	29	64.91	
140	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338] IOCL, ODISHA	04/2018	5,654.00 -	5,654.00	3,566.10	10/2021 07/2022	07/2022	9	0	
141	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363] IOCL, HARYANA	12/2018	278.60 -	278.60	101.96	06/2021 07/2022	07/2022	13	0	
142	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268] IOCL, MAHARASHTRA	05/2016	348.00 437.00	437.00	209.30	01/2021 -	08/2022	19	25.57	
143	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324] IOCL, BIHAR	12/2017	199.36 -	199.36	90.83	10/2020 08/2022	08/2022	22	0	
144	LPG TERMINAL AT KOCHI - [N16000171] IOCL, KERALA	10/2015	607.06 1,236.00	1,236.00	553.03	10/2017 03/2022	09/2022	59	103.6	
145	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342] IOCL, ANDHRA PRADESH	08/2018	466.00 -	466.00	301.65	04/2021 12/2021	09/2022	17	0	
146	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362] IOCL, ODISHA	05/2019	3,361.00 -	3,361.00	2,099.36	08/2021 09/2022	09/2022	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
147	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	64.47	12/2019 03/2022	10/2022	34	0	
148	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	179.06	08/2021 -	11/2022	15	0	
149	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	1,255.00	373.81	12/2021 01/2023	01/2023	13	0	
150	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	16.06	07/2022 -	01/2023	6	0	
151	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	128.30	04/2022 -	02/2023	10	0	
152	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 427.00	427.00	35.56	09/2022 03/2023	03/2023	6	15.09	
153	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,199.60	2,281.94	673.16	12/2022 07/2023	07/2023	7	0	
154	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	109.24	04/2022 -	08/2023	16	0	
155	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	1,398.00	134.42	12/2023 -	01/2024	1	0	
156	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	5.59	09/2023 -	02/2024	5	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
157	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	543.02	03/2020 11/2020	12/2021	21	9.64	
158	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,789.68	12/2019 04/2021	03/2022	27	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
159	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA	06/2020	200.00 304.00	304.00	2.58	06/2023 01/2024	01/2024	7	52	
	<u>Oil & Natural Gas Corporation Limited</u>									
160	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	2,203.71	2,222.54	05/2021 12/2021	12/2021	7	-3.87	
161	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	05/2019	3,660.71 3,740.05	3,740.05	3,119.98	05/2021 01/2022	01/2022	8	2.17	
162	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	829.58	12/2020 05/2021	02/2022	14	-3.93	
163	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	2,001.34	1,604.42	05/2013 05/2022	05/2022	108	132.23	
164	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,888.99	04/2018 05/2022	05/2022	49	5.8	
165	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	25,090.00	15,071.32	06/2020 06/2022	06/2022	24	-26.23	
166	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	1,640.35	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									
167	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	510.00	486.90	12/2019 -	12/2021	24	-10.79	
168	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 652.10	638.60	399.74	02/2020 -	12/2021	22	17.41	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
169	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL, ASSAM	06/2016	224.75 222.21	198.00	184.60	08/2020 09/2021	12/2021	16	-11.9	
170	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL, MULTI STATE	05/2016	406.00 -	406.00	283.17	10/2020 -	03/2022	17	0	
	Total		1,49,775.64 -	1,56,064.01	95,977.38					
	POWER									
	Chenab Valley Power Projects [P] Limited									
171	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	2,056.81	04/2020 07/2025	07/2025	63	0	
	National Hydro-Electric Power Corporation									
172	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	9,357.83	09/2009 03/2023	03/2023	162	152.52	
173	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	14,738.05	09/2010 08/2023	08/2023	155	218.08	PPA is yet to be signed with Delhi DISCOMS for Power of 113 MW.
	National Thermal Power Corporation									
174	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 2,311.89	2,311.89	2,094.59	12/2018 -	01/2022	37	22.64	
175	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC, TELANGANA	06/2019	401.90 -	442.03	225.90	04/2021 10/2021	01/2022	9	9.99	
176	JETSAR SOLAR 160 MW - [N18000287]NTPC, RAJASTHAN	12/2019	702.28 -	702.28	586.88	03/2021 11/2021	01/2022	10	0	
177	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 17,304.00	17,304.00	16,604.00	05/2018 -	03/2022	46	33.47	
178	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 633.80	633.80	530.53	11/2018 -	03/2022	40	19.66	
179	ANTA SOLAR 90 MW - [N18000292]NTPC, RAJASTHAN	01/2021	382.22 -	382.22	4.15	03/2022 03/2022	05/2022	2	0	
180	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC, KERALA	09/2019	403.62 -	403.62	122.49	06/2021 12/2021	07/2022	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
181	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	852.90	541.97	09/2021 08/2022	08/2022	11	6.85	
182	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	1,522.71	1,009.07	09/2021 08/2022	08/2022	11	0	
183	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	1,316.22	888.48	09/2021 08/2022	08/2022	11	0	
184	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	1,221.73	140.11	07/2022 05/2022	08/2022	1	0	
185	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	599.99	62.06	07/2022 -	08/2022	1	0	
186	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	842.27	92.08	07/2022 -	08/2022	1	0	
187	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 10,997.70	10,998.00	9,124.00	11/2020 07/2022	10/2022	23	3.76	
188	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	524.83	368.49	09/2021 10/2022	10/2022	13	4.7	
189	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	1,803.19	552.18	09/2021 10/2022	10/2022	13	4.71	
190	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	293.03	130.88	10/2021 10/2022	10/2022	12	11.93	
191	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	1,782.00	836.25	09/2021 10/2022	10/2022	13	0	
192	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN	03/2020	1,749.31 -	1,749.31	1,339.51	09/2021 10/2022	10/2022	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
193	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 21,312.11	21,312.11	19,466.00	10/2011 07/2023	07/2023	141	145.16	•Support required for early completion of Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur rail route, which is critical to ease transportation of coal for Barh Project. Readiness of railway line Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur route (250km) is critical to ease transportation of coal for Barh Project. NTPC has funded Rs 664 Crores to Railways for development of following works in envisaged Coal transportation route. •Construction of Karnauti-Bakhtiyarpur flyover. •Construction of Manpur Flyover (ROR) •Electrification of Manpur-Tilaiya-Bakhtiyarpur section. (Charging from Tilaiya sub-station balance) Bakhtiyarpur ROR line: Acquisition of 12.241 Acres supplementary land is under process. Land award has been done. Payment to landowner is in progress. However, few Raiyats are unwilling to accept the compensation as the award has been issued based on reduced circle rate. State Govt support required to Railways for acquisition / possession of said Land. Support of Ministry of Railways is required for timely completion of above works.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
194	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58	17,007.00	12,556.00	06/2019 10/2022	09/2023	51	18.38	Support of State Govt of Jharkhand is required for following: 1.Maintaining Law & order and resolution of following issue: Agitation by villagers for compensation on already awarded land. Raiyats had stopped site works completely w.e.f. 23.02.2021 for demand of additional compensation for already acquired land, which continued till 30.03.2021. Work affected due to Agitation since 15.11.21. 2.Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. 3.Acquisition of Land by CCL for external CHP. 4.Early completion of Road Widening and strengthening of SH-7 from Hazaribagh to Bijupara. It is being done on deposit basis by RCD. The road diversion in project area needs to be completed on priority. 5.Repair of damaged bridge over Garhi River is critical for transportation of material for project. 6.Forest clearance in ATS lines.
195	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	5,326.00	03/2013 12/2021	09/2024	138	96.99	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
196	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,803.00	743.00	09/2019 12/2024	12/2024	63	30.48	•Support requested for resolving inter-ministerial issues. •All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSECL. State Govt is not ready to finalize power evacuation line in absence of PPA. •Shifting of balance Homesteads from Project area. (11 Nos + 01 School).
197	PATRATU STPP-I (3X800MW) - [N18000275]NTPC, JHARKHAND	11/2017	18,668.00 -	17,667.00	4,771.00	03/2023	02/2025	23	-5.36	1.Revision of the Banhardih Coal Mine development milestone schedules and funding arrangement. 2.Readiness of Start-up power and ATS matching with commissioning schedule of the project Expeditious Award of construction of power evacuation and start up power line is required. 3.Transfer & possession of balance land.
	<u>Power Grid Corporation Of India Limited</u>									
198	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	259.30	04/2016 12/2017	12/2021	68	0	
199	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	379.95	236.27	12/2019 09/2021	01/2022	25	0	
200	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	358.83	262.19	05/2020 08/2021	01/2022	20	0	
201	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE	05/2014	522.29 546.36	546.36	480.89	11/2016 12/2021	02/2022	63	4.61	
202	EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	235.53	157.92	06/2019 11/2021	02/2022	32	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
203	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 12/2020	02/2022	19	14.11	
204	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	90.75	03/2018 -	03/2022	48	0	
205	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	3,326.92	12/2018 12/2021	03/2022	39	31.08	
206	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	168.20	07/2019 07/2021	03/2022	32	17.99	
207	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	578.99	05/2017 12/2021	04/2022	59	0	
208	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	205.25	02/2019 04/2022	04/2022	38	0	
209	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	13,038.20	08/2013 11/2022	05/2023	117	32.24	
210	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	9,129.32	2,911.97	12/2018 03/2024	03/2024	63	92.02	
	<u>Satluj Jal Vidyut Nigam Limited</u>									
211	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	947.89	785.06	12/2021 06/2022	06/2022	6	46.2	1. Stay imposed by Hon'ble High Court of Uttarakhand on all construction activities within 200 m of the river. 2. Agitation by locals in project area. 3. Delay due to Covid-19 pandemic. 4. Geological challenges. 5. Change in Design and scope of work.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Thdc India Limited</u>									
212	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 1,587.16	1,587.16	648.84	09/2020 08/2022	08/2022	23	-24.57	(i) Start of Tree Felling Activities in 139 Ha priority Forest land pending with DFO, Singrauli. (ii) Private/ Tenancy Land (337.35 Ha): Disposal of pending cases & payment of Compensation to balance PAFs pending by Dist Admin, Singrauli. (iii) Declaration of Govt. land (53.13 Ha.) Land as Abadi Land awaited from Collector, Singrauli. (iv) Diversion of Forest Land for CEC & RS pending with DFO, Singrauli.
213	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 4,825.60	4,825.60	4,374.66	02/2016	06/2023	88	191.23	Pending signing of Lease Deed with GoUK for existing 3 Ha. Land at Asena Quarry after permission of extension of mining lease received on 19.04.21 from GoUK and Allotment of additional 4.916 Ha. Land for mining at Asena Quarry by GoUK.
214	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42	11,089.42	3,395.52	09/2023	08/2024	11	0	- Make-up Water related issues pending with Irrigation & Water Resources Dept, GoUP. - Law & Order Issues in taking possession of small patches of land acquired for Railway Siding & land within boundary of already acquired 1201 Acre land. - Signing of Lease deed by UPSIDC is getting delayed due to Court case filed by PAFs. - Help of District Administration required for demolition of old Nagla houses for final shifting.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
215	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	2,356.86	06/2013 12/2024	12/2024	138	54.94	Regular support on law & order issues is being provided by GoUK/ District Administration, Chamoli.
	Total		1,51,049.12 -	2,08,226.67	1,40,645.53					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Cpwd For Health</u>									
216	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29 -	150.29	70.91	03/2020 -	12/2021	21	0	
217	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	0	
218	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	0	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
219	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	262.64	05/2018 -	03/2022	46	0	
	<u>Nbcc For Health</u>									
220	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	9	8.88	
	Total		2,320.28 -	2,440.28	1,246.14					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
221	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	24	111.08	
222	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	24	75	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
223	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	12	.89	
224	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	355.54	03/2022 -	03/2024	24	0	
225	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	488.43	03/2023 -	03/2024	12	0	
226	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	322.26	03/2022 -	03/2024	24	0	
227	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	239.26	03/2023 -	03/2024	12	0	
East Central Railways										
228	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	929.86	958.41	03/2019 12/2021	12/2021	33	37.04	
229	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	324.29	03/2019 -	03/2022	36	0	Land acquisition
230	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	390.00	403.49	03/2021 -	03/2022	12	11.99	
231	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	1,080.00	1,086.41	03/2012 11/2022	11/2022	128	232.58	
232	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	1,051.33	03/2020 -	03/2023	36	0	
233	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	572.94	03/2020 03/2023	03/2023	36	0	
234	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,487.37	03/2020 -	03/2024	48	0	
235	SAGAILI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	543.61	03/2021 03/2024	03/2024	36	63.37	
236	MUZAFFARPUR SAGAILI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	424.08	03/2021 03/2024	03/2024	36	62.06	
237	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	540.73	03/2020 03/2023	12/2024	57	49.45	land acquisition
East Coast Railway										

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
238	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,195.24	02/2019 -	03/2022	37	38.43	
239	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	224.26	03/2020 -	03/2022	24	52.77	
240	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	1,012.35	03/2020 03/2023	03/2023	36	.07	
241	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	710.98	03/2022 03/2023	03/2023	12	0	
242	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	284.93	10/2020 03/2024	03/2024	41	0	
243	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	193.71	11/2018 -	03/2024	64	15.45	
244	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	718.37	12/2018 03/2024	03/2024	63	0	
245	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,687.63	03/2009 12/2024	12/2024	189	29.71	
246	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	933.16	06/2021 03/2025	03/2025	45	137.8	
247	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	769.95	03/2022 03/2024	03/2026	48	0	
248	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	524.03	03/2022 03/2026	03/2026	48	0	
	<u>Eastern Railways</u>									
249	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	638.35	02/2013 -	03/2024	133	134.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
250	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91	1,619.48	912.61	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30 KM between Kamarpukur and Jairambati in Hooghly district is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.
251	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99	545.70	149.31	03/2006	03/2025	228	34.08	Land is required for execution of the MM projects.
252	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98	2,137.81	453.42	03/2022	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
253	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	618.75	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to 41 nos. of un authorized crossings Amghata to Nabadwipghat work is dropped vide Bd's letter No. 2020/W-I/Compliance in Bd Mtg, dated 09.10.2020
254	CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 Km).- The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
255	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	201.29	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
256	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	507.59	03/2017 -	03/2025	96	20.3	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non-availability of land.
257	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bakrahat (9.75 Km) New line- Work could not be started due to non availability of land

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
258	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	142.05	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
259	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	109.63	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
260	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
261	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	45	0	
262	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	18	117.23	
	<u>Metropolitan Rapid Transport Projects</u>									
263	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,868.04	03/2004 06/2022	06/2022	219	501.57	
264	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	774.51	492.88	06/2013 07/2022	07/2022	109	56.23	
	<u>North Central Railway</u>									
265	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	680.00	531.20	03/2020 -	01/2022	22	1.69	
266	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 -	2,001.00	1,046.53	03/2021 06/2023	06/2023	27	0	NIL
267	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	471.73	03/2022 12/2024	12/2024	33	32.02	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
268	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53	4,329.53	76.74	03/2023	06/2025	27	0	Due follow up is in progress with U.P & M.P Govt. for land acquisition.
	<u>North East Frontier Railway</u>									
269	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,936.64	12/2008	12/2021	156	284.8	
270	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96	1,873.21	1,586.23	03/2021	03/2022	12	115.07	
271	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 90.00	742.00	612.37	03/2020 06/2022	06/2022	27	30.26	
272	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20	1,043.00	919.48	03/2019	03/2023	48	170.77	
273	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32	2,950.00	1,939.39	03/2022	03/2023	12	32.15	
274	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 12,264.00	14,322.00	12,012.77	03/2011 12/2023	12/2023	153	221.54	
275	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	6,527.00	4,525.01	03/2014	12/2023	117	172.7	
276	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,084.69	8,600.00	1,856.78	12/2015 12/2023	12/2023	96	542.04	
277	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	446.24	03/2019	12/2023	57	13.6	
278	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	1,029.65	03/2019	03/2024	60	302.54	
279	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52	6,663.00	1,420.48	03/2015	03/2026	132	186.39	
	<u>North Eastern Railway</u>									
280	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00	213.35	72.08	04/2016	12/2021	68	.16	
281	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00	610.00	595.91	01/2019	02/2022	37	106.78	
282	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 600.00	366.71	332.87	01/2022	03/2022	2	-38.88	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
283	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
284	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	66	127.77	
285	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-32.79	
	<u>North Western Railway</u>									
286	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	769.95	02/2019 -	06/2022	40	109.82	
287	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	334.01	03/2020 -	10/2022	31	16.97	
288	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	413.98	08/2022	11/2022	3	0	
	<u>Northern Railway</u>									
289	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	26,237.89	11/2002 -	12/2022	241	1017.96	
290	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,017.96	878.49	07/2012 -	11/2024	148	348.44	
291	MANSABHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	0	
292	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	1,540.13	243.28	03/2023 12/2025	12/2025	33	369.35	
	<u>Rail Vikas Nigam Ltd.</u>									
293	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	872.65	942.56	03/2021 -	12/2021	9	35.42	
294	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	839.78	03/2016 -	12/2021	69	50.15	
295	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,900.00	2,041.94	03/2020 -	12/2021	21	306.46	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
296	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	2,009.00	2,156.59	03/2020 -	12/2021	21	111.91	
297	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,364.39	03/2020 -	12/2021	21	-7.28	
298	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	2,355.40	12/2020 -	12/2021	12	23.55	
299	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	1,868.89	2,201.29	12/2021 -	03/2022	3	20.68	
300	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	3,753.96	03/2020 -	03/2022	24	124.58	
301	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	2,440.53	1,894.70	02/2015 -	06/2022	88	102.92	
302	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,438.92	03/2019 -	06/2022	39	51.02	
303	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,536.00	1,269.37	03/2019 -	06/2022	39	62.89	
304	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL, TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,111.90	03/2022 -	06/2022	3	-23.24	
305	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL, TAMIL NADU	02/2015	760.00 -	1,536.00	1,509.71	03/2020 -	06/2022	27	102.11	
306	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,777.07	12/2020 -	12/2022	24	54.24	
307	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	1,000.00	982.28	03/2022 -	12/2024	33	5.98	
308	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,089.92	03/2023 -	12/2024	21	0	
309	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	3,317.94	03/2016 -	03/2025	108	7.78	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
310	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,460.93	03/2016 -	03/2025	108	59.22	
311	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	22,716.11	5,917.58	12/2024 -	03/2025	3	40.08	
312	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	18.95	
313	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	3,327.72	2,024.04	12/2024 -	12/2026	24	42.47	
<u>South Central Railway</u>										
314	BHADRACHALAM ROAD- SATTUPALLI - [N22000287]SCR, MULTI STATE	04/2010	704.31 927.94	927.94	691.26	03/2020 -	02/2022	23	31.75	
315	MUNEERABAD- MAHABOBNAGAR (NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,010.00	03/2000 -	03/2023	276	98.57	
316	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,042.28	03/2009 -	03/2024	180	102.85	
317	MANOHARABAD-KOTHPALL NEW LINE (SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48 -	1,373.74	654.79	03/2010 -	03/2024	168	18.38	
318	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 -	1,952.68	729.57	03/2023 -	03/2024	12	5.16	
319	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	2,063.03	1,613.72	03/2021 -	03/2024	36	0	
320	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,388.38	03/2022 -	03/2024	24	7.06	
321	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	156	42.44	
<u>South East Central Railway</u>										
322	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR, MADHYA PRADESH	04/2010	585.93 1,268.32	1,268.32	1,123.85	02/2019 12/2021	12/2021	34	116.46	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
323	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 3,176.60	3,176.60	1,492.13	03/2023 12/2023	12/2023	9	66.44	
324	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 2,135.34	2,135.34	733.21	03/2021 12/2023	12/2023	33	8.23	
325	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	1,370.94	838.56	12/2021 12/2023	12/2023	24	.07	
326	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 852.50	1,096.00	40.47	12/2021 12/2024	12/2024	36	378.6	
	<u>South Eastern Railway</u>									
327	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.96	1,119.38 -	03/2020 -	06/2022	27	35.38	
328	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	511.75	110.13 -	12/2021 -	06/2022	6	31.09	
329	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	393.83	22.39	06/2022 -	06/2023	12	16.52	
330	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	1,097.56	03/2021 -	12/2023	33	0	
331	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	1,866.31	288.29	05/2023 -	12/2023	7	0	
332	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	54.99	
333	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	472.50	1.61	06/2022 -	12/2025	42	10.23	
334	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	130.97	
	<u>South Western Railway</u>									
335	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00 -	760.00	647.09	03/2020 01/2022	01/2022	22	31.49	
336	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,954.21	1,205.02	03/2020 -	03/2023	36	68.91	
337	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	36.97	03/2016 -	12/2023	93	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
338	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2024	264	.02	
339	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
340	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	1,878.00	1,496.77	03/2019 -	03/2024	60	16.31	
341	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	732.89	495.11	03/2017 -	03/2025	96	13.67	
342	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	387.33	12/2018 -	06/2025	78	0	
343	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	1,530.09	325.32	03/2016 -	12/2026	129	55.13	
<u>Southern Railway</u>										
344	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,549.09	712.68	03/2020 -	03/2025	60	409.6	
345	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,081.20	1,718.56	02/2019 -	03/2025	73	325.17	
346	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
347	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	308.35	03/2019 -	12/2027	105	1699.64	
348	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	133	247.32	
349	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	991.83	922.01	03/2005 -	12/2021	201	268.89	
<u>West Central Railway</u>										
350	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	15	16.02	
351	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	540.13	03/2022 -	12/2023	21	114.32	
352	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 2,909.99	2,909.99	1,411.38	03/2021 03/2024	03/2024	36	585.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
353	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	1,345.52	03/2020 -	03/2024	48	38.63	Work is suffering badly on this Critical project due pending forest land clearance. The detail position is as under: ∴ Niwas Road to Deoragram: Forest land 46.067 Ha from Railway Km 1261 to 1301 under DFO Singrauli in isolated patches. Application has been uploaded on Sep'2018. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 2055 Nos. trees cutting have been submitted on 18.06.2020 and 21.07.2020. However, APCCF/Bhopal vide letter dated 31.07.2020 has sought clarifications from MOEF. MOEF vide letter dated 24.09.2020 has clarified that case need to be processed further in FCA. GM/WCR vide letter dated 09.10.2020 has requested Railway Board to intervene in this matter. A meeting was held in Collector Singrauli office on 12.12.20. This meeting was chaired by Hon'ble MP/ Sidhi Smt Riti Pathak. Collector Singrauli has been requested to expedite this proposal. ∴ Vijaysota to Beohari: Forest Land 66.69 Ha under DFO Shahdol from Rly Km 1162 to 1189 in isolated patches. Application has been uploaded in Feb'2019. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 17454 Nos trees cutting have been submitted on 18.08.2020

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
354	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202	3230.57	
	<u>Western Railway</u>									
355	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	21	33.41	
356	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,042.12	730.07	03/2021 -	12/2022	21	3.96	
357	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 -	6,171.08	2,327.60	03/2022 -	03/2023	12	76.13	
358	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,524.68	1,524.68	1,004.89	03/2022 03/2023	03/2023	12	13.17	
359	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 859.16	1,378.11	558.66	03/2019 03/2023	03/2023	48	329.77	
360	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	350.17	06/2020 03/2023	03/2023	33	-13.76	
361	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	126.35	03/2012 10/2023	10/2023	139	1.06	
362	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,631.75	2,223.37	1,966.82	03/2020 03/2024	03/2024	48	167.96	
363	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 -	495.18	.33	03/2022 -	03/2024	24	0	
364	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 692.25	742.88	.89	03/2020 03/2024	03/2024	48	7.31	
365	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	882.29	03/2022 03/2025	03/2025	36	0	
	Total		1,88,052.74 -	3,23,144.80	1,73,203.80					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
366	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	282.08	207.83	06/2019 12/2021	12/2021	30	0	
367	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021	19	0	
368	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	238.66	09/2019 09/2021	12/2021	27	0	
369	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	237.81	09/2020	12/2021	15	0	
370	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	457.34	01/2020 06/2021	01/2022	24	0	
371	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 927.73	927.73	773.30	02/2020 08/2021	01/2022	23	-3.11	
372	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	254.43	09/2020 01/2022	01/2022	16	0	
373	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	231.61	03/2018 11/2021	01/2022	46	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
374	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	635.00	07/2018 05/2021	01/2022	42	0	
375	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 949.54	949.54	794.73	06/2019 04/2021	01/2022	31	8.17	
376	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	298.63	01/2018 01/2022	01/2022	48	0	
377	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	333.56	11/2017 01/2022	01/2022	50	0	
378	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	02/2022	47	0	
379	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 174.90	174.90	154.26	08/2018 08/2021	02/2022	42	5.23	
380	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	132.76	02/2018 09/2021	02/2022	48	0	
381	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	133.46	03/2017 12/2021	02/2022	59	0	
382	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	182.97	08/2018 09/2021	02/2022	42	4.45	
383	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	167.53	03/2018 10/2021	02/2022	47	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
384	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	219.86	07/2018 08/2021	02/2022	43	0	
385	REHABILITATION AND UPGRADEMENT OF NH 200 FROM KM 241.553 TO 312.600 MASANIKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	536.65	552.31	12/2019 02/2022	02/2022	26	0	
386	BALANCE WORK FOR REHABILITATION AND UPGRADEMENT OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	404.69	03/2018 06/2021	02/2022	47	9.23	
387	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	160.00	133.51	09/2021	02/2022	5	0	
388	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	120.51	11/2018 01/2021	03/2022	40	7.39	
389	UPGRADEMENT OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	187.73	02/2018 03/2022	03/2022	49	0	
390	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	139.54	03/2021 11/2021	03/2022	12	0	
391	REHABILITATION AND UPGRADEMENT OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.89	04/2020	03/2022	23	-8.28	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
392	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	19	12.16	
393	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	282.86	06/2017 03/2022	03/2022	57	0	
394	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	544.00	400.87	09/2016 03/2022	03/2022	66	14.24	
395	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	251.27	03/2015 03/2022	03/2022	84	0	
396	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	113.05	05/2019 03/2022	03/2022	34	0	
397	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE - I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 319.96	319.96	193.56	03/2016 04/2022	04/2022	73	13.3	
398	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	67.54	03/2018 03/2022	04/2022	49	0	
399	REHABILITATION AND UPGRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	207.79	108.34	03/2021 -	04/2022	13	0	
400	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	390.73	346.72	05/2017 05/2022	05/2022	60	45.75	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
401	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	80.06	03/2018 09/2021	06/2022	51	0	
402	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	572.66	284.86	08/2016 06/2022	06/2022	70	15.19	
403	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	731.50	476.86	10/2016 06/2022	06/2022	68	17.04	
404	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	78.47	08/2019 08/2022	08/2022	36	11.18	
405	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	27.15	08/2019 -	11/2022	39	33.51	
406	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	409.70	08/2017 06/2021	12/2022	64	0	
407	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	435.61	117.77	07/2016 12/2022	12/2022	77	-3.83	
408	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	24.49	05/2021 -	12/2022	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
409	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	6.94	03/2021 -	03/2023	24	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
410	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	113.03	06/2018 -	12/2021	42	0	
411	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	179.86	06/2018 -	12/2021	42	0	
412	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	289.99	100.00	12/2018 -	12/2021	36	0	
413	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	315.03	120.99	09/2018 -	12/2021	39	0	
414	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	240.64	125.87	09/2018 -	12/2021	39	0	
415	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	77.62	09/2018 -	12/2021	39	0	
416	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	154.83	11/2017 -	12/2021	49	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
417	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022	39	0	
418	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	588.95	516.16	11/2018 -	02/2022	39	0	
419	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	372.30	05/2018 -	03/2022	46	0	
420	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	229.20	01/2016 -	03/2022	74	0	
421	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	139.69	01/2016 -	03/2022	74	0	
422	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	182.01	04/2017 03/2021	03/2022	59	0	
423	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	252.79	153.14	04/2017 -	03/2022	59	29.48	
424	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	263.31	155.10	04/2017 -	03/2022	59	29.48	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
425	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22	252.05	157.83	04/2017	03/2022	59	27.16	
426	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL, UTTARAKHAND	03/2018	274.31	274.31	131.95	05/2018	03/2022	46	0	
427	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL, UTTARAKHAND	03/2018	403.36	403.36	220.25	06/2018	03/2022	45	0	
428	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL, UTTARAKHAND	03/2018	417.24	417.24	265.48	05/2018	03/2022	46	0	
429	2 LANE WITH HARD SHOULDER, REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS	03/2017	409.85	409.85	135.48	12/2017 03/2021	03/2022	51	0	
430	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS	02/2018	391.00	391.00	77.75	10/2018	03/2022	41	0	
431	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL, A & N ISLANDS	03/2018	234.27	234.27	75.22	10/2018 09/2020	03/2022	41	0	
432	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00	387.00	333.24	09/2018	03/2022	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
433	FOUR LANE OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	0	
434	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL, MEGHALAYA	03/2019	306.28 -	306.28	133.81	05/2019 -	03/2022	34	0	
435	CONSTRUCT ION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	128.80	09/2018 -	05/2022	44	0	
436	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57 -	339.57	182.63	09/2018 -	07/2022	46	0	
437	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL, UTTARAKHAND	03/2018	1,383.78 -	1,383.78	299.10	07/2018 -	07/2022	48	0	
438	CONSTRUCT ION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL, NAGALAND	03/2018	285.68 -	285.68	100.70	09/2018 -	09/2022	48	0	
439	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL, NAGALAND	03/2018	272.89 -	272.89	68.70	09/2018 -	10/2022	49	0	
440	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL, NAGALAND	03/2018	500.09 -	500.09	132.56	09/2018 -	11/2022	50	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
441	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	98.33	09/2019 -	04/2023	43	0	
442	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	128.15	09/2019 04/2023	04/2023	43	0	
443	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	142.87	09/2019 06/2023	04/2023	43	0	
444	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	115.64	09/2019 04/2023	06/2023	45	0	
445	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	137.11	09/2019 04/2023	06/2023	45	0	
446	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	107.05	09/2019 06/2023	07/2023	46	0	
447	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	90.39	09/2019 09/2023	09/2023	48	0	
448	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	51.36	09/2019 03/2024	04/2024	55	0	
	<u>National Highways Authority Of India</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
449	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 1,928.22	1,928.22	1,890.04	04/2015 01/2021	12/2021	80	0	
450	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	12/2021	44	0	
451	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	403.81	07/2018 -	12/2021	41	0	
452	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29	0	
453	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29	0	
454	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	599.30	06/2018 12/2021	12/2021	42	0	
455	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	252.08	03/2020 -	12/2021	21	0	
456	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	1,322.40	03/2020 12/2021	12/2021	21	0	
457	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	403.81	07/2016 -	12/2021	65	0	
458	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	718.56	09/2017 11/2021	12/2021	51	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
459	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97	990.97	763.00	12/2019	12/2021	24	0	
460	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84	1,078.84	2,301.82	08/2013	01/2022	101	0	
461	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00	624.00	97.97	04/2014	01/2022	93	0	
462	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96	1,056.08	1,020.25	11/2018	01/2022	38	-25.83	
463	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82	707.82	434.59	08/2018	01/2022	41	0	
464	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00	166.90	81.67	05/2013	02/2022	105	-55.37	
465	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64	950.64	341.21	08/2017	02/2022	54	0	
466	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55	1,724.55	2,641.30	03/2013	03/2022	108	0	
467	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13	744.73	706.78	05/2018 03/2022	03/2022	46	40.22	
468	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40	701.40	146.05	03/2019	03/2022	36	0	
469	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00	929.32	810.00	04/2020	03/2022	23	3.95	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
470	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	570.00	03/2020 -	04/2022	25	0	
471	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	605.00	05/2020 -	05/2022	24	0	
472	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 717.24	717.24	627.25	05/2018 06/2022	06/2022	49	20.9	
473	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	238.84	03/2019 12/2021	06/2022	39	0	
474	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59	0	
475	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	810.81	09/2017 -	07/2022	58	0	
476	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	449.44	03/2020 -	09/2022	30	.23	
477	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	18.66	
478	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	32.96	12/2017 -	05/2023	65	0	
479	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,893.57	08/2013 -	06/2023	118	0	
480	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	348.00	03/2019 12/2022	06/2023	51	-25.48	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		62,284.90	63,092.57	43,439.74					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
481	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	422.87	70.25	06/2021 11/2021	03/2022	9	-1.92	
	<u>Cpwd For Telecom</u>									
482	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20	248.20	155.97	03/2018	01/2022	46	0	
	<u>Department Of Telecommunication</u>									
483	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	24,664.00	20,545.00	07/2015 05/2020	03/2022	80	84.97	
	Total		14,013.36	25,335.07	20,771.22					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
484	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00	12,787.00	9,834.10	12/2018	08/2022	44	18.69	NA
	<u>Bangalore Metro Rail Corporation Limited</u>									
485	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	19,410.15	02/2019 03/2025	03/2025	73	16.25	NIL
	<u>Central Public Works Department</u>									
486	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 238.56	238.56	208.57	05/2020 01/2022	01/2022	20	0	
487	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 217.00	217.00	187.08	04/2019 02/2022	02/2022	34	9.97	Reason were mentioned during period of occurrence, available in previous months report.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
488	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 392.00	392.00	196.68	08/2020 06/2022	06/2022	22	0	
489	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 299.97	299.97	27.44	09/2020 01/2023	01/2023	28	0	
490	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 422.00	422.00	135.75	03/2021 06/2023	06/2023	27	0	
491	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 1,100.80	1,100.80	35.90	07/2021 06/2023	06/2023	23	-6.71	
492	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	1,128.00	30.00	03/2022	06/2023	15	0	
	<u>Lucknow Metro Rail Corporation Limited</u>									
493	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	2,391.78	03/2024 -	03/2025	12	0	NO
494	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	506.47	03/2024 -	05/2025	14	0	NO
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
495	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11,420.00	7,565.74	11/2021 12/2022	12/2022	13	0	•Delay in Slum R& R at Kamgar Putala & Rajiv Gandhi Nagar
	<u>Mumbai Metro Rail Corporation Ltd</u>									
496	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	20,051.98	03/2020 03/2023	03/2023	36	44.39	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
497	NAGPUR METRO RAIL - [N28000085]NMRC,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	8,443.80	03/2018 12/2021	12/2021	45	0	NIL
	Total		1,03,728.10 -	1,20,242.55	69,025.44					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>WATER RESOURCES</u>									
	<u>Brahmaputra Board</u>									
498	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57	233.57	148.83	12/2019	12/2021	24	0	
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
499	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62	191.62	65.53	11/2020	12/2021	13	0	
500	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77	398.90	294.30	03/2020	02/2022	23	76.68	
501	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63	268.63	338.67	01/2021	03/2022	14	0	
502	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06	230.06	98.70	07/2021	04/2022	9	0	
503	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37	356.37	137.32	04/2021	04/2022	12	0	
504	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42	277.42	247.01	05/2021	06/2022	13	0	
505	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15	236.15	60.61	12/2020	07/2022	19	0	
506	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89	578.89	42.75	06/2022	12/2022	6	0	
507	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00	824.00	96.39	06/2022	12/2022	6	0	
508	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19	305.19	28.31	08/2021	04/2023	20	0	
509	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02	294.02	26.45	10/2021	12/2023	26	0	
510	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13	413.29	.05	09/2020	03/2024	42	62.63	
	<u>Delhi Jal Board</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
511	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07	515.07	345.58	01/2021	12/2021	11	0	
512	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79	211.79	108.28	12/2021	12/2022	12	0	
513	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11	239.11	160.52	02/2022	12/2022	10	0	
	<u>Kolkata Metropolitan Development Authority</u>									
514	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32	272.32	253.59	04/2020	03/2022	23	0	
515	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA,WEST BENGAL	08/2017	185.22	185.22	11.56	12/2021	09/2023	21	0	
516	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA,WEST BENGAL	01/2018	172.10	172.10	11.56	12/2021	09/2023	21	0	
517	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA,WEST BENGAL	10/2017	164.93	164.93	11.56	12/2021	09/2023	21	0	
518	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA,WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022	03/2024	25	13.23	
519	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA,WEST BENGAL	03/2018	165.16	165.16	-	06/2022	03/2024	21	0	
520	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N30000042]KMDA,WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022	03/2024	25	-3.29	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
521	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96	384.96	-	04/2022	04/2024	24	0	
522	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53	287.53	-	04/2022	04/2024	24	0	
523	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31	234.31	-	04/2022	04/2024	24	0	
524	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12	307.12	-	09/2022	04/2024	19	0	
	<u>Polavaram Project Authority</u>									
525	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	18,335.60	03/2020 11/2021	04/2022	25	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									
526	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23	967.23	96.64	09/2021	12/2021	3	0	
527	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45	460.45	248.16	12/2020	12/2021	12	0	
528	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59	767.59	132.29	09/2021	03/2022	6	0	
529	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05	206.05	80.97	10/2021	03/2022	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
530	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam,UTTAR PRADESH	01/2019	231.79 -	234.03	28.36	12/2021 -	12/2022	12	.97	
531	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam,UTTAR PRADESH	03/2019	271.39 -	271.39	-	08/2021 -	03/2024	31	0	
532	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam,UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	03/2024	32	-28.25	
533	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam,UTTAR PRADESH	10/2017	213.62 261.12	261.12	-	03/2022 -	04/2024	25	22.24	
534	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UP JalNigam,UTTAR PRADESH	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	22	1.31	
<u>Uttarakhand Pey Jal Nigam</u>										
535	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UK JalNigam,UTTARA KHAND	03/2017	158.00 -	158.00	85.01	11/2019 03/2021	03/2022	28	0	
	Total		22,180.93 -	67,906.50	21,494.60					
<u>DEFENCE PRODUCTION</u>										
<u>Cpwd For Defence</u>										
536	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD FOR DEFENC,KARNATAKA	12/2016	246.31 210.00	210.00	158.92	02/2020 10/2021	03/2022	25	-14.74	
	Total		246.31 -	210.00	158.92					
<u>DEPARTMENT OF HIGHER EDUCATION</u>										
<u>Cpwd Of Higher Education</u>										

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
537	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA	01/2018	223.37 -	223.37	117.64	07/2020 -	12/2021	17	0	
538	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR	02/2016	496.18 496.00	498.99	301.90	06/2017 -	03/2022	57	.57	
539	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83 -	193.83	51.77	06/2020 -	03/2022	21	0	
540	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB	01/2018	430.00 -	387.83	237.59	05/2020 -	06/2022	25	-9.81	
541	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA	01/2019	790.79 -	790.79	258.32	03/2022 -	06/2022	3	0	
542	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	424.93	80.19	07/2022 -	10/2022	3	0	
543	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	808.62	296.89	07/2022 -	10/2022	3	0	
544	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	34.60	05/2022 -	10/2022	5	0	
545	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N420000006]CPWD EDUCATION,KARNATAKA	07/2019	851.00 851.00	851.00	324.03	03/2022 -	10/2022	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
546	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH	09/2018	392.51 -	392.51	85.88	06/2022 10/2022	10/2022	4	0	
547	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION,ANDHRA PRADESH	02/2019	655.34 655.34	655.34	300.85	06/2020 11/2022	11/2022	29	0	
548	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	375.00	125.38	09/2020 -	11/2022	26	0	
549	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	216.78	03/2021 -	02/2023	23	0	
550	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION,GOA	05/2019	303.90 -	303.90	48.30	03/2020 02/2023	02/2023	35	0	
551	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	588.72	117.82	09/2022 06/2023	06/2023	9	0	
	<u>Rites Of Higher Education</u>									
552	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 429.70	429.70	230.00	09/2014 06/2022	06/2022	93	-11.28	Due to Law and Order and subsequent delayed
	Total		8,120.38 -	8,026.40	2,827.94					
	<u>HOME AFFAIRS</u>									
	<u>Cpwd For Mha</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (December 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
553	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21	2,000.00	1,049.80	10/2019	05/2022	31	64.04	
554	NSG AT KOLKATA - [N28000104]CPWD FOR MHA, WEST BENGAL	10/2014	162.88	238.00	173.06	04/2018	08/2022	52	46.12	
555	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI	06/2019	277.35	290.33	38.13	07/2022	12/2022	5	4.68	
556	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD FOR MHA,HARYANA	01/2020	166.98	166.98	7.84	10/2023	04/2024	6	0	
	Total		1,826.42	2,695.31	1,268.83					
	<u>DPIIT</u>									
	<u>IICC For Dpiit</u>									
557	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00	5,178.00	3,044.41	12/2019	05/2022	29	8.49	
	Total		4,773.00	5,178.00	3,044.41					
	Grand Total		8,88,221.90	11,86,144.64	6,93,894.38					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	6,840.00	6,054.37	09/2010	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00	16,580.00	17,427.00	12/2015	12/2022	44.69	84
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00	17,079.00	13,945.00	12/2016	12/2023	38.63	84
	Total		27,271.00	40,499.00	37,426.37				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27	480.33	140.13	09/2021	06/2023	38.72	21
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23	707.73	494.81	09/2018	06/2022	69.63	45
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00	1,232.00	397.52	03/2021	03/2023	7.88	24
7	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00	1,938.00	568.01	09/2021	12/2023	40.13	27
	Total		3,288.50	4,358.06	1,600.47				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
8	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00	334.27	28.43	04/2018	10/2022	37.56	54
9	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13	341.22	79.48	03/2017	10/2022	12.20	67
	<u>Central Coal Fields Limited</u>								
10	MAGADH EXPANSION OC(51 MTY) - [N06000015]	08/2008	6,964.33	7,254.37	814.20	07/2012	03/2028	4.16	188
	<u>Eastern Coal Fields Limited</u>								
11	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73	5,146.48	625.36	08/2019	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
12	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068] <u>Neyveli Lignite Corporation</u>	11/2008	479.53 -	808.97	808.97	03/2013 -	03/2024	68.70	132
13	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152] <u>Singareni Colliers Company Limited</u>	07/2016	17,237.00 -	17,237.80	12,939.55	11/2021 -	11/2022	.00	12
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	306.52	03/2015 -	03/2022	114.60	84
15	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	123.72	03/2019 -	03/2022	11.42	36
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	204.84	03/2015 -	03/2023	5.85	96
17	RAMAGUNDAM OC-II EXTENSION - [N06000078] <u>South Eastern Coal Fields Limited</u>	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86	132
18	JAGANNATHPOR OCP(3.00MTY) - [N06000075] <u>Western Coal Fields Limited</u>	09/2008	152.43 -	459.49	200.47	03/2015	03/2022	201.44	84
19	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	37.55	03/2022 -	03/2025	.00	36
20	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	299.67	213.92	03/2019 -	03/2022	1.39	36
21	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	327.41	162.29	03/2019 -	03/2022	7.52	36
22	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	145.94	03/2023 -	03/2024	15.41	12
	Total		30,646.30 -	34,586.95	17,107.31				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								
23	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	301.90	06/2017 -	03/2022	.57	57
	Total		496.18 -	498.99	301.90				
	<u>DPIIT</u>								
	<u>Iicc For Dpiit</u>								
24	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	3,044.41	12/2019 -	05/2022	8.49	29
	Total		4,773.00 -	5,178.00	3,044.41				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Nbcc For Health</u>								
25	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	8.88	9
	Total		1,351.00 -	1,471.00	870.80				
	<u>HOME AFFAIRS</u>								
	<u>Cpwd For Mha</u>								
26	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	238.00	173.06	04/2018 -	08/2022	46.12	52
27	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002	06/2019	277.35 -	290.33	38.13	07/2022 -	12/2022	4.68	5
28	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	1,049.80	10/2019 -	05/2022	64.04	31
	Total		1,659.44 -	2,528.33	1,260.99				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
29	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11	66
30	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	793.01	06/2019 -	02/2022	35.54	32
	<u>Gas Authority Of India Limited</u>								
31	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 -	247.90	75.63	02/2021 -	10/2022	9.91	20
32	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	234.40	08/2020 -	03/2022	14.17	19
33	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,778.50	12/2012 -	08/2024	102.71	140
	<u>Hindustan Petroleum Corporation Limited</u>								
34	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VV SPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	2,673.55	06/2021 -	07/2022	14.76	13
35	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	17,704.50	07/2020 -	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								
36	KHARAGPUR LPG BOTTLING PLANT - [N16000300	04/2017	163.02 -	207.36	129.75	04/2020 -	07/2022	27.20	27

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
37	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	08/2017	236.00 -	319.61	226.65	06/2020 -	12/2021	35.43	18
38	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321	04/2018	206.63 -	340.76	164.11	02/2020 -	07/2022	64.91	29
39	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368	06/2019	371.00 -	427.00	35.56	09/2022 -	03/2023	15.09	6
40	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268	05/2016	348.00 -	437.00	209.30	01/2021 -	08/2022	25.57	19
41	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	1,236.00	553.03	10/2017 -	09/2022	103.60	59
42	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00 -	3,027.90	2,225.58	03/2021 -	03/2022	66.09	12
43	PARADIP HYDERABAD PIPELINE - [N16000194	01/2015	2,321.00 -	3,338.00	3,124.58	12/2020 -	03/2022	43.82	15
44	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	4,159.59	12/2018 -	02/2022	33.98	38
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
45	DEVANGONTHI MARKETING TERMINAL - [N16000401	06/2020	200.00 -	304.00	2.58	06/2023 -	01/2024	52.00	7
46	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	637.00	543.02	03/2020 -	12/2021	9.64	21
	<u>Oil & Natural Gas Corporation Limited</u>								
47	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	2,001.34	1,604.42	05/2013 -	05/2022	132.23	108
48	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,375.90	2,888.99	04/2018 -	05/2022	5.80	49
49	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	05/2019	3,660.71 -	3,740.05	3,119.98	05/2021 -	01/2022	2.17	8
50	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	04/2019	3,228.80 -	3,976.67	1,640.35	03/2022 -	05/2023	23.16	14
	<u>Oil India Limited</u>								
51	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	638.60	399.74	02/2020 -	12/2021	17.41	22
	Total		51,661.57 -	68,831.34	46,306.26				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
52	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	09/2002	3,919.59 -	9,897.59	9,357.83	09/2009 -	03/2023	152.52	162
53	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,992.43	14,738.05	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								
54	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	130.88	10/2021 -	10/2022	11.93	12
55	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	06/2019	401.90 -	442.03	225.90	04/2021 -	01/2022	9.99	9
56	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 -	524.83	368.49	09/2021 -	10/2022	4.70	13
57	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	633.80	530.53	11/2018 -	03/2022	19.66	40
58	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 -	852.90	541.97	09/2021 -	08/2022	6.85	11
59	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	743.00	09/2019 -	12/2024	30.48	63
60	NOKHRA - [N18000282]	03/2020	1,722.14 -	1,803.19	552.18	09/2021 -	10/2022	4.71	13
61	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]	05/2016	1,885.13 -	2,311.89	2,094.59	12/2018 -	01/2022	22.64	37
62	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	5,326.00	03/2013 -	09/2024	96.99	138
63	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	9,124.00	11/2020 -	10/2022	3.76	23
64	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	12,556.00	06/2019 -	09/2023	18.38	51
65	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	16,604.00	05/2018 -	03/2022	33.47	46
66	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	21,312.11	19,466.00	10/2011 -	07/2023	145.16	141
	<u>Power Grid Corporation Of India Limited</u>								
67	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	168.20	07/2019 -	03/2022	17.99	32
68	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	480.89	11/2016 -	02/2022	4.61	63
69	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 -	02/2022	14.11	19
70	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	3,326.92	12/2018 -	03/2022	31.08	39
71	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,911.97	12/2018 -	03/2024	92.02	63

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
72	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	13,038.20	08/2013 -	05/2023	32.24	117
	<u>Satluj Jal Vidyut Nigam Limited</u>								
73	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	785.06	12/2021 -	06/2022	46.20	6
	<u>Thdc India Limited</u>								
74	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,860.35	2,356.86	06/2013 -	12/2024	54.94	138
75	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,374.66	02/2016 -	06/2023	191.23	88
	Total		97,289.86 -	1,55,985.46	122,901.61				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
76	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	.89	12
77	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	75.00	24
78	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	111.08	24
	<u>East Central Railways</u>								
79	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23 -	390.00	403.49	03/2021 -	03/2022	11.99	12
80	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	540.73	03/2020 -	12/2024	49.45	57
81	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	958.41	03/2019 -	12/2021	37.04	33
82	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,080.00	1,086.41	03/2012 -	11/2022	232.58	128
83	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	424.08	03/2021 -	03/2024	62.06	36
84	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	543.61	03/2021 -	03/2024	63.37	36
	<u>East Coast Railway</u>								
85	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	224.26	03/2020 -	03/2022	52.77	24
86	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	193.71	11/2018 -	03/2024	15.45	64
87	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	1,012.35	03/2020 -	03/2023	.07	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
88	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,195.24	02/2019 -	03/2022	38.43	37
89	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	933.16	06/2021 -	03/2025	137.80	45
90	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,687.63	03/2009 -	12/2024	29.71	189
	<u>Eastern Railways</u>								
91	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108
92	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	507.59	03/2017 -	03/2025	20.30	96
93	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE- PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	.01	240
94	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	34.08	228
95	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	142.05	02/2012 -	03/2025	36.15	157
96	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI- SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	29.20	96
97	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	618.75	03/2016 -	03/2025	7.75	108
98	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	638.35	02/2013 -	03/2024	134.80	133
99	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	912.61	03/2019 12/2009	03/2025	36.22	72
100	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	453.42	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
101	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489]	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	.00	45
102	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	117.23	18
	<u>Metropolitan Rapid Transport Projects</u>								
103	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP [N22000028]	04/2006	495.74 -	774.51	492.88	06/2013 -	07/2022	56.23	109
104	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,868.04	03/2004 -	06/2022	501.57	219
	<u>North Central Railway</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
105	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	531.20	03/2020 -	01/2022	1.69	22
106	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	471.73	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
107	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	612.37	03/2020 -	06/2022	30.26	27
108	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,043.00	919.48	03/2019 -	03/2023	170.77	48
109	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,586.23	03/2021 -	03/2022	115.07	12
110	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING [N22000183]	04/2013	1,798.00 -	2,042.51	446.24	03/2019 -	12/2023	13.60	57
111	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	1,029.65	03/2019 -	03/2024	302.54	60
112	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,939.39	03/2022 -	03/2023	32.15	12
113	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,936.64	12/2008 -	12/2021	284.80	156
114	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	6,527.00	4,525.01	03/2014 -	12/2023	172.70	117
115	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,663.00	1,420.48	03/2015 -	03/2026	186.39	132
116	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	1,856.78	12/2015 -	12/2023	542.04	96
117	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.00	12,012.77	03/2011 -	12/2023	221.54	153
	<u>North Eastern Railway</u>								
118	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	72.08	04/2016 -	12/2021	.16	68
119	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	127.77	66
120	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	610.00	595.91	01/2019 -	02/2022	106.78	37
	<u>North Western Railway</u>								
121	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	334.01	03/2020 -	10/2022	16.97	31
122	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	769.95	02/2019 -	06/2022	109.82	40
	<u>Northern Railway</u>								
123	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	243.28	03/2023 -	12/2025	369.35	33

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
124	NANGALDAM-TALWARA(NL),NR - [N220100188	03/1981	450.00 -	2,017.96	878.49	07/2012 -	11/2024	348.44	148
125	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [N220100133	03/1995	2,500.00 -	27,949.00	26,237.89	11/2002 -	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>								
126	DHASA-JETALSAR (GC) - [N220000141	04/2012	644.38 -	872.65	942.56	03/2021 -	12/2021	35.42	9
127	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N220000213	04/2012	632.68 -	950.00	839.78	03/2016 -	12/2021	50.15	69
128	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N220000401	04/2015	943.60 -	1,000.00	982.28	03/2022 -	12/2024	5.98	33
129	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N220000404	04/2011	927.01 -	1,400.00	1,438.92	03/2019 -	06/2022	51.02	39
130	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N220000451	02/2015	760.00 -	1,536.00	1,509.71	03/2020 -	06/2022	102.11	27
131	BANASPANI- JAKHPURA - DOUBLING - [N220000412	03/2009	942.95 -	1,536.00	1,269.37	03/2019 -	06/2022	62.89	39
132	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N220000413	03/2012	1,183.25 -	1,825.00	1,777.07	12/2020 -	12/2022	54.24	24
133	BINA - KOTA DOUBLING WITH RE - [N220000414	04/2011	1,485.85 -	1,835.83	2,355.40	12/2020 -	12/2021	23.55	12
134	PALANPUR-SAMAKHAYALI (DL) - [N220000144	04/2013	1,548.66 -	1,868.89	2,201.29	12/2021 -	03/2022	20.68	3
135	SAMBALPUR - TITLAGARH - DOUBLING - [N220000410	03/2006	948.04 -	2,009.00	2,156.59	03/2020 -	12/2021	111.91	21
136	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N220100325	04/1998	1,202.70 -	2,440.53	1,894.70	02/2015 -	06/2022	102.92	88
137	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N220000109	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95	141
138	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N220000407	03/2009	713.48 -	2,900.00	2,041.94	03/2020 -	12/2021	306.46	21
139	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N220000409	01/1991	2,335.67 -	3,327.72	2,024.04	12/2024 -	12/2026	42.47	24
140	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM) - [N220000313	03/2012	1,503.71 -	3,377.00	3,753.96	03/2020 -	03/2022	124.58	24
141	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N220000110	04/2010	3,951.98 -	4,259.48	3,317.94	03/2016 -	03/2025	7.78	108
142	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N220000111	04/2010	2,913.51 -	4,639.00	1,460.93	03/2016 -	03/2025	59.22	108
143	RISHIKESH - KARNAPRAYAG NEW LINE - [N220000406	04/2011	16,216.00 -	22,716.11	5,917.58	12/2024 -	03/2025	40.08	3

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>South Central Railway</u>								
144	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	691.26	03/2020 -	02/2022	31.75	23
145	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	1,373.74	654.79	03/2010 -	03/2024	18.38	168
146	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	729.57	03/2023 -	03/2024	5.16	12
147	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,042.28	03/2009 -	03/2024	102.85	180
148	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	42.44	156
149	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	2,010.00	03/2000 -	03/2023	98.57	276
150	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,388.38	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>								
151	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	378.60	36
152	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	1,123.85	02/2019 -	12/2021	116.46	34
153	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	838.56	12/2021 -	12/2023	.07	24
154	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	733.21	03/2021 -	12/2023	8.23	33
155	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,176.60	1,492.13	03/2023 -	12/2023	66.44	9
	<u>South Eastern Railway</u>								
156	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 -	393.83	22.39	06/2022 -	06/2023	16.52	12
157	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 -	472.50	1.61	06/2022 -	12/2025	10.23	42
158	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39 -	511.75	110.13	12/2021 -	06/2022	31.09	6
159	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99	120
160	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	1,119.38	03/2020 -	06/2022	35.38	27
161	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>								
162	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	732.89	495.11	03/2017 -	03/2025	13.67	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
163	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	760.00	647.09	03/2020 -	01/2022	31.49	22
164	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2024	.02	264
165	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	325.32	03/2016 -	12/2026	55.13	129
166	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	1,496.77	03/2019 -	03/2024	16.31	60
167	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,954.21	1,205.02	03/2020 -	03/2023	68.91	36
	<u>Southern Railway</u>								
168	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	247.32	133
169	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) [N22000441]	02/1996	268.87 -	991.83	922.01	03/2005 -	-	268.89	201
170	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,549.09	712.68	03/2020 -	03/2025	409.60	60
171	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	308.35	03/2019 -	12/2027	1,699.64	105
172	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	3,081.20	1,718.56	02/2019 -	03/2025	325.17	73
	<u>West Central Railway</u>								
173	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	540.13	03/2022 -	12/2023	114.32	21
174	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,445.30	1,345.52	03/2020 -	03/2024	38.63	48
175	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	16.02	15
176	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,411.38	03/2021 -	03/2024	585.35	36
177	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
178	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	126.35	03/2012 -	10/2023	1.06	139
179	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]	04/2017	692.25 -	742.88	0.89	03/2020 -	03/2024	7.31	48
180	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,042.12	730.07	03/2021 -	12/2022	3.96	21
181	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2023	329.77	48
182	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	33.41	21

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
183	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	1,004.89	03/2022 -	03/2023	13.17	12
184	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,223.37	1,966.82	03/2020 -	03/2024	167.96	48
185	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,171.08	2,327.60	03/2022 -	03/2023	76.13	12
	Total		1,39,575.93 -	2,76,128.51	154,759.27				
	ROAD TRANSPORT AND HIGHWAYS								
	Ministry Of Road Transport And Highways (State Pwds)								
186	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	174.90	154.26	08/2018 -	02/2022	5.23	42
187	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	27.15	08/2019 -	11/2022	33.51	39
188	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	182.97	08/2018 -	02/2022	4.45	42
189	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	78.47	08/2019 -	08/2022	11.18	36
190	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	03/2016	271.17 291.20	291.20	120.51	11/2018 -	03/2022	7.39	40
191	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]	01/2014	282.41 -	319.96	193.56	03/2016 -	04/2022	13.30	73
192	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J - [N24001208]	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	12.16	19
193	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	346.72	05/2017 -	05/2022	45.75	60
194	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	404.69	03/2018 -	02/2022	9.23	47
195	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	400.87	09/2016 -	03/2022	14.24	66
196	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	284.86	08/2016 -	06/2022	15.19	70
197	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	476.86	10/2016 -	06/2022	17.04	68
198	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]	03/2016	877.79 -	949.54	794.73	06/2019 -	01/2022	8.17	31

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
199	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	157.83	04/2017 -	03/2022	27.16	59
200	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	153.14	04/2017 -	03/2022	29.48	59
201	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	155.10	04/2017 -	03/2022	29.48	59
	<u>National Highways Authority Of India</u>								
202	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	717.24	627.25	05/2018 -	06/2022	20.90	49
203	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	706.78	05/2018 -	03/2022	40.22	46
204	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	449.44	03/2020 -	09/2022	.23	30
205	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	3.95	23
206	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66	105
	Total		10,976.62 -	12,725.67	10,127.21				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
207	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	19,538.23	05/2015 -	03/2022	41.32	82
	Total		15,525.00 -	21,940.00	19,538.23				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
208	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	84.97	80
	Total		13,334.00 -	24,664.00	20,545.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
209	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	9,834.10	12/2018 -	08/2022	18.69	44

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Bangalore Metro Rail Corporation Limited</u>								
210	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	02/2014	26,405.14 -	30,695.12	19,410.15	02/2019 -	03/2025	16.25	73
	<u>Central Public Works Department</u>								
211	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33 -	217.00	187.08	04/2019 -	02/2022	9.97	34
	<u>Mumbai Metro Rail Corporation Ltd</u>								
212	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	20,051.98	03/2020 -	03/2023	44.39	36
	Total		60,511.47 -	77,105.12	49,483.31				
	<u>WATER RESOURCES</u>								
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
213	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	398.90	294.30	03/2020 -	02/2022	76.68	23
214	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	413.29	0.05	09/2020 -	03/2024	62.63	42
	<u>Kolkata Metropolitan Development Authority</u>								
215	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	03/2024	13.23	25
	<u>Polavaram Project Authority</u>								
216	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	18,335.60	03/2020 -	04/2022	447.22	25
	<u>Uttar Pradesh Jal Nigam</u>								
217	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	28.36	12/2021 -	12/2022	.97	12
218	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	04/2024	22.24	25
219	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	1.31	22
	Total		11,956.56 -	57,771.61	18,658.31				
	Grand Total		4,70,316.43	7,84,272.04	503,931.45				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	03/2022 12/2023	-
	Total		380.87 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Mahanadi Coal Fields Limited</u>				
3	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	03/2012 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
7	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
10	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	03/2016 -	09/2021
	Total		14,560.71 -		
	<u>FINANCE</u>				
	<u>Cpwd For Finance</u>				
11	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
12	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU	11/2017	348.77 -	11/2021 -	11/2021
	Total		557.77 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
SI.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
13	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	11/2019 05/2021	-
14	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	11/2019 05/2021	-
	Total		458.64 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
15	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 12/2022	12/2020
16	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		700.62 -		
	<u>STEEL</u>				
	<u>Raastriya Ispat Nigam Limited</u>				
17	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	09/2018 09/2021	09/2021
	Total		1,682.85 -		
	<u>PETROLEUM</u>				
	<u>Indian Oil Corporation Limited</u>				
18	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	02/2020 06/2021	11/2021
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
20	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 4,475.92	05/2021 05/2021	05/2021
21	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	03/2019 09/2021	09/2021
	Total		5,925.65 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-
	<u>National Thermal Power Corporation</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
23	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	07/2012 06/2020	11/2021
24	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
25	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
26	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
<u>Power Grid Corporation Of India Limited</u>					
27	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021
28	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 06/2021	06/2021
29	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALUR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021
30	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 07/2021	10/2021
31	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 09/2021	10/2021
	Total		37,698.21 -		
<u>HEAVY INDUSTRY</u>					
<u>Bharat Heavy Electricals Limited</u>					
32	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-
<u>Natrip Implementation Society</u>					
33	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 03/2021	03/2021
	Total		3,272.00 -		
<u>HEALTH AND FAMILY WELFARE</u>					
<u>Cpwd For Health</u>					
34	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	05/2021
<u>Hll Infra Tech Services Limited</u>					
35	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-
36	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
37	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Hospital Services Consultancy Corporation Ltd</u>				
38	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
39	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
40	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
41	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
42	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
43	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
44	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021
45	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	03/2021
46	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	03/2021
47	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021
48	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021
49	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021
50	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	10/2021
51	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	10/2021
	Total		6,803.41 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
52	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-
53	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
54	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-
55	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	-
56	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
57	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
58	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	-
59	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
60	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
61	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
62	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
63	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
64	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	03/2021
65	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012 09/2021	09/2021
66	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	-
67	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-
68	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
69	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
70	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
71	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
72	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
73	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
74	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
75	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
76	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>Eastern Railways</u>				
77	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021
78	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
79	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Metropolitan Rapid Transport Projects</u>				
80	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
81	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
82	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
83	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North East Frontier Railway</u>				
84	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	10/2021
85	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
86	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
87	DIMPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
88	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
89	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
90	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-
91	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
92	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-
93	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
94	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
95	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
96	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
97	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
98	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
99	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-DAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	420.18 -	03/2020 -	09/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
100	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
101	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
102	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
103	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
104	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021
105	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-
106	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
107	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 -	03/2021 -	-
108	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	03/2020 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
109	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 12/2022	-
	<u>Railway Electrification</u>				
110	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
111	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
112	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
113	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 176.18	03/2022 03/2022	-
	<u>South Eastern Railway</u>				
114	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	03/2019
115	CHAKRADHARPUR TO GOILKERA 3RD LINE (34 KM) - [N22000507]SER,JHARKHAND	11/2015	354.54 -	12/2018 -	06/2020
116	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
	<u>South Western Railway</u>				
117	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	09/2021
	<u>Southern Railway</u>				
118	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
119	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
	<u>Western Railway</u>				
120	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 311.36	- -	-
	Total		79,639.64 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
121	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019
122	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020
123	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH, RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
124	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH, ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
125	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH, UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020
126	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH, UTTARAKHAND	08/2016	234.88 -	12/2017 12/2020	12/2020
127	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021
128	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH, UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
129	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH, UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
130	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH, UTTAR PRADESH	10/2016	218.90 -	03/2020 03/2020	03/2021
131	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH, UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021
132	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH, UTTAR PRADESH	03/2016	249.50 -	05/2019 -	04/2021
133	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH, UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021
134	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH, A & N ISLANDS	11/2017	257.34 -	11/2019 06/2021	06/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
135	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021
136	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH, WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021
137	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH, GUJARAT	03/2018	351.00 -	06/2021 -	06/2021
138	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH, UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021
139	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH, UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021
140	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH, UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021
141	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH, ANDHRA PRADESH	01/2016	348.95 -	08/2016 12/2021	07/2021
142	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH, UTTARAKHAND	12/2017	248.22 -	12/2019 08/2021	08/2021
143	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH, PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021
144	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH, UTTARAKHAND	02/2018	418.88 -	02/2020 09/2021	09/2021
145	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH, JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021
146	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH, ARUNACHAL PRADESH	03/2021	182.55 -	09/2021 -	09/2021
147	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH, UTTARAKHAND	02/2018	293.68 -	- 10/2021	10/2021
148	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH, A & N ISLANDS	11/2017	237.80 237.80	11/2019 10/2021	10/2021
149	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2021	10/2021
150	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH, TRIPURA	10/2016	171.90 -	08/2020 -	11/2021
151	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH, MIZORAM	01/2017	205.95 -	01/2021 -	11/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
152	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	11/2021
153	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
154	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	02/2017 -	-
155	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
156	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
157	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
158	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
159	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
160	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
161	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
162	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
163	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
164	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-
165	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 273.27	08/2015 -	-
166	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
167	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
168	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-
169	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
170	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
171	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
172	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
173	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
174	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
175	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
176	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-
177	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
178	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
179	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-
180	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
181	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
182	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
183	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
184	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
185	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
186	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-
187	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
188	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 194.48	11/2020 -	-
189	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
190	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
191	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
192	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
193	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
194	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
195	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
196	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
197	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
198	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
199	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
200	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 10/2021	-
201	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 10/2021	-
202	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 02/2022	-
203	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 01/2022	-
204	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 12/2021	-
205	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 274.73	08/2018 11/2021	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
206	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 556.13	11/2018 07/2021	-
207	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	05/2016 09/2021	-
208	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
209	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
210	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
211	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
212	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
213	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 381.75	08/2018 10/2021	-
214	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2021	-
215	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 11/2021	-
216	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 08/2021	-
217	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 12/2021	-
218	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 381.75	09/2017 05/2022	-
219	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 596.38	01/2018 04/2022	-
220	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
221	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
222	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
223	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
224	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
225	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
226	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
227	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
228	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
229	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
230	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
231	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
232	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
233	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
234	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
235	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
236	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
237	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
238	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
239	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
240	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
241	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
242	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
243	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
244	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
245	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
246	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
247	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
248	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
249	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
250	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
251	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
252	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
253	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
254	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
255	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
256	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
257	AMD I TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
258	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
259	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
260	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
261	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
262	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
263	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
264	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
265	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
266	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
267	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
268	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
269	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
270	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
271	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
272	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78	07/2019	-
273	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
274	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
275	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
276	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
277	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
278	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
279	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
280	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
281	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
282	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
283	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
284	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
285	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
286	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
287	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
288	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
289	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
290	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
291	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
292	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
293	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
294	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
295	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
296	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
297	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
298	WADI GODRI TO DHANGRI PIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
299	DHANGRI PIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
300	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
301	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
302	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
303	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
304	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
305	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
306	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
307	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
308	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
309	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
310	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
311	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
312	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
313	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
314	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
315	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
316	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
317	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
318	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
319	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
320	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
321	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
322	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
323	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
324	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
325	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
326	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
327	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
328	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
329	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
330	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
331	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
332	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
333	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
334	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
335	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
336	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
337	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
338	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
339	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
340	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
341	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
342	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
343	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
344	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
345	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
346	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
347	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	-
348	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
349	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
350	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
351	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
352	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
353	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
354	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
355	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
356	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
357	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
358	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
359	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
360	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
361	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
362	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	06/2021 -	-
363	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
364	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
365	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
366	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
367	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
368	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
369	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
370	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
371	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
372	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
373	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
374	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
375	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
376	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
377	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
378	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
379	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
380	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
381	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
382	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
383	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
384	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-
385	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 12/2021	-
386	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 12/2021	-
387	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-
388	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 04/2022	-
389	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
390	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
391	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
392	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 204.73	06/2019 -	-
393	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
394	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
395	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
396	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
397	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
398	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
399	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
400	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
401	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
402	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
403	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
404	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
405	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	08/2021 -	-
406	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	08/2021 -	-
407	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
408	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
409	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
410	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-
411	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-
412	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	-
413	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	-
414	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
415	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
416	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-
417	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-
418	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-
419	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-
420	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2021	-
421	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
422	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN	03/2020	370.36 -	08/2022 -	-
423	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-
424	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
425	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
426	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	03/2021
427	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
428	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
429	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- 09/2021	09/2021
430	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 03/2021	10/2021
431	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	10/2018 -	10/2021
432	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	10/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
433	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	11/2021
434	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	11/2021
435	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	11/2021
436	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	11/2021
437	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	11/2021
438	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
439	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
440	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
441	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
442	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
443	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
444	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
National Highways Authority Of India					
445	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- 12/2016	05/2017
446	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- 02/2018	02/2018
447	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 906.65	- 02/2018	02/2018
448	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	11/2018
449	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
450	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
451	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- 01/2020	01/2020
452	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
453	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020
454	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
455	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
456	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
457	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
458	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
459	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
460	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
461	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
462	REHABILITATION AND UPGRADE OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
463	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
464	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	04/2021
465	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	05/2021
466	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	05/2018 04/2019	06/2021
467	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN	02/2018	716.76 -	- 07/2021	07/2021
468	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI, ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 07/2021	07/2021
469	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT	03/2018	1,437.64 -	- -	07/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
470	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021
471	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	08/2021
472	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021
473	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENMORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021
474	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021
475	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 1,201.51	- 06/2021	09/2021
476	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021
477	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 499.70	- 05/2021	09/2021
478	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021
479	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	10/2021
480	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021
481	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 866.55	- 10/2021	10/2021
482	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021
483	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	11/2021
484	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
485	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
486	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
487	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
488	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
489	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
490	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
491	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
492	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-
493	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
494	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
495	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
496	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
497	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
498	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
499	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
500	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
501	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
502	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
503	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
504	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
505	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
506	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
507	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
508	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 12/2021	-
509	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
510	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
511	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
512	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
513	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
514	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
515	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
516	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
517	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
518	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
519	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
520	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
521	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
522	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
523	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
524	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
525	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
526	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
527	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
528	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
529	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 363.93	- -	-
530	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
531	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
532	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
533	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
534	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
535	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-
536	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
537	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
538	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
539	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
540	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
541	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 1,457.82	03/2018 03/2021	-
542	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
543	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
544	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	-
545	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
546	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28	06/2018	-
547	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
548	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
549	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 -	-
550	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
551	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
552	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
553	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 247.00	04/2018 -	-
554	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
555	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-
556	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
557	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-
558	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
559	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 1,096.52	04/2018 -	-
560	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
561	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
562	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
563	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
564	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-
565	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
566	MEERUT-BULANDSHAHR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-
567	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
568	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
569	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-
570	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-
571	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-
572	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
573	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	04/2019 10/2022	-
574	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
575	4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-
576	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-
577	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-
578	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-
579	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-
580	SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-
581	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
582	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	-
583	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-
584	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	-
585	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-
586	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-
587	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-
588	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
589	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	-
590	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 1,367.00	- -	-
591	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
592	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI, HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
593	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	08/2018 -	-
594	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
595	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	08/2019 -	-
596	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-
597	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-
598	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	- -	-
599	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	- -	-
600	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
601	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	03/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
602	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
603	REHABILITATION AND UPGRADATION TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
604	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
605	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
606	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
607	4 LANE OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 02/2022	-
608	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
609	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 1,361.00	- 01/2019	-
610	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-
611	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
612	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
613	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
614	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
615	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
616	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
617	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
618	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
619	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
620	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
621	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
622	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	03/2020 -	-
623	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI, UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
624	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI, KARNATAKA	03/2017	831.58 -	03/2020 -	-
625	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI, KARNATAKA	03/2017	993.16 -	03/2020 -	-
626	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	06/2020 -	-
627	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56 -	07/2017 -	-
628	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT	10/2017	232.49 -	10/2017 -	-
629	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
630	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI, RAJASTHAN	10/2017	964.17 -	10/2017 -	-
631	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI, KERALA	09/2017	1,124.11 -	09/2017 -	-
632	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI, MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
633	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI, TAMIL NADU	09/2017	244.27 -	09/2017 -	-
634	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION - [N24000711]NHAI, RAJASTHAN	12/2017	1,308.73 -	- -	-
635	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI, UTTAR PRADESH	12/2017	1,232.21 -	- -	-
636	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI, BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-
637	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA	12/2017	686.65 -	- -	-
638	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA	12/2017	417.51 -	- -	-
639	6-LANNING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH	12/2017	328.67 -	- -	-
640	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI, ANDHRA PRADESH	12/2017	1,323.15 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
641	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI, ANDHRA PRADESH	12/2017	357.00 -	- -	-
642	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARPUR) - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	-
643	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 OF - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	-
644	REHABILITATION AND UPGRADE OF TWO LANING OF MAHESHKUNTA - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	- -	-
645	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	- -	-
646	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND	01/2018	273.46 -	- -	-
647	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND	01/2018	1,155.16 -	- -	-
648	FOUR LANING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI, MADHYA PRADESH	01/2018	770.73 -	- -	-
649	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA	01/2018	621.00 -	- -	-
650	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2) - [N24000732]NHAI, ODISHA	01/2018	668.86 -	- -	-
651	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA	01/2018	633.68 -	- -	-
652	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPASS - [N24000735]NHAI, ODISHA	01/2018	564.66 -	- -	-
653	REHABILITATION AND UPGRADE OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI, ODISHA	01/2018	686.65 -	- -	-
654	REHABILITATION SIX LANING UPGRADE CHANDIKHOLE BHADRAK - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	- -	-
655	REHABILITATION AND UPGRADE OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141) - [N24000738]NHAI, ODISHA	01/2018	999.00 -	- -	-
656	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	- -	-
657	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 -	- -	-
658	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-
659	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
660	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA	02/2018	1,424.77 -	- -	-
661	FOR REHABILITATION AND UPGRADE FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH	02/2018	670.50 -	- -	-
662	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI, KARNATAKA	02/2018	2,177.80 -	- -	-
663	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-
664	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI, UTTAR PRADESH	03/2018	809.07 -	- -	-
665	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI, UTTAR PRADESH	03/2018	925.40 -	- -	-
666	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	-
667	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
668	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	- -	-
669	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI, UTTAR PRADESH	03/2018	1,120.57 -	- -	-
670	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- 01/2019	-
671	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	-
672	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	-
673	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
674	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROAD - [N24000806]NHAI, UTTAR PRADESH	02/2018	972.77 -	- -	-
675	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI, ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
676	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI, ANDHRA PRADESH	03/2018	557.30 -	- -	-
677	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI, BIHAR	03/2018	496.20 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December
2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
678	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	- -	-
679	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-
680	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
681	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
682	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
683	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
684	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-
685	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
686	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-
687	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	- -	-
688	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA	03/2018	806.11 -	- -	-
689	REHABILITATION AND UPGRADEATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA	03/2018	198.05 -	- -	-
690	REHABILITATION AND UPGRADEATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA	03/2018	181.78 -	- -	-
691	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA	03/2018	642.13 -	- -	-
692	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI, JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-
693	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
694	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI, HARYANA	01/2019	1,051.91 -	- -	-
695	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI, HARYANA	01/2019	1,120.06 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
696	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
697	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
698	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
699	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
700	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
701	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
702	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
703	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
704	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
705	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
706	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
707	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
708	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
709	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
710	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-
711	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-
712	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	11/2019 -	-
713	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	11/2019 -	-
714	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	11/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
715	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
716	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
717	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 1,135.08	- 11/2021	-
	Total		3,80,275.21 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
718	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 18,380.00	12/2015 02/2019	02/2019
719	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	02/2021
	<u>Delhi Metro Rail Corporation</u>				
720	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	-
721	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
722	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
723	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019
	Total		69,629.79 -		
	<u>WATER RESOURCES</u>				
	<u>Delhi Jal Board</u>				
724	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Hscl For Water</u>				
725	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL FOR WATER,BIHAR	10/2005	956.00 -	03/2015 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
726	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 05/2022	-
	<u>Uttar Pradesh Jal Nigam</u>				
727	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	11/2021
	Total		1,855.48 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COMMERCE</u>				
	<u>Nbcc For Commerce</u>				
728	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Cpwd Of Higher Education</u>				
729	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 11/2021	11/2021
730	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND	09/2012	171.86 -	03/2016 -	-
731	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23 -	10/2012 -	-
732	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN	12/2016	549.31 -	07/2019 -	-
733	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD EDUCATION,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	-
	Total		1,343.23 -		
	<u>HOME AFFAIRS</u>				
	<u>Cpwd For Mha</u>				
734	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31 -	01/2022 -	01/2020
	Total		199.31 -		
	<u>DPIIT</u>				
	<u>Dmic For Dpiit</u>				
735	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021
	Total		12,579.09 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
736	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	08/2021
	Total		151.33 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				
737	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		6,18,288.35		

FLASH REPORT

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75				2/6
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
2	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80	229.80	96.11	-	12/2022	7(R3)	17/26
3	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20	730.20	206.83	-	05/2023	0(R3)	13/17
	Total		818.00	960.00	302.94				30/43
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
4	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL, JAMMU AND KASHMIR	03/2019	4,287.59	4,287.59	617.83	-	07/2025	11(R3)	0/0
	Total		4,287.59	4,287.59	617.83				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
5	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	190.34	183.36	-	12/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	546.71	-	12/2021	-	0/0
7	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	515.47	-	03/2022	-	0/0
	Total		1,340.57	1,374.35	1,245.54				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
8	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07	3,650.00	3,661.29	-	03/2022	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
9	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	1,483.14	1,370.20	- 03/2022	03/2022	0(R3)	0/0
10	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,597.10	- 03/2023	03/2023	0(R3)	0/0
11	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	941.70	- 03/2023	03/2023	0(R3)	0/0
12	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	-	0/0
13	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	153.43	- 03/2023	03/2023	0(R3)	0/0
14	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	1,467.70	- -	03/2023	-	0/0
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	352.68	- -	12/2023	-	0/0
16	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	2.55	- -	08/2024	-	0/0
17	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
18	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	519.33	316.22	- -	03/2025	-	0/0
	<u>Eastern Railways</u>								
19	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	316.82	- -	03/2022	-	0/0
20	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	303.23	- -	03/2022	-	0/0
21	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	410.29	- -	03/2024	-	0/0
22	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
23	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	11.77	- -	03/2025	-	0/0
24	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
25	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.11	- -	03/2025	-	0/0
26	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
27	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	36.13	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
28	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	40.65	- -	03/2025	-	0/0
29	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
30	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North Central Railway</u>								
31	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	-	- 04/2010	12/2027	212(R3)	0/0
	<u>North East Frontier Railway</u>								
32	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	378.87	333.46	- 12/2021	06/2022	6(R3)	0/0
	<u>North Eastern Railway</u>								
33	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH	04/2016	602.50 -	800.00	145.14	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
34	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	791.39	597.99	-	09/2023	-	0/0
35	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	419.00	160.79	- -	09/2023	-	0/0
36	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	359.00	116.87	- -	03/2024	-	0/0
37	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	<u>South Eastern Railway</u>								
38	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	41.78	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
39	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	2,161.36	82.81	- -	12/2023	-	0/0
40	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	12/2023	-	0/0
41	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	12/2023	-	0/0
42	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	12/2023	-	0/0
43	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	5,174.30	158.11	- -	12/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
44	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30	2,404.03	1,100.11	-	12/2025	-	2/2
45	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85	348.85	.36	-	12/2025	-	0/0
	<u>Southern Railway</u>								
46	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41	608.13	427.75	-	12/2021	2(R3)	0/0
47	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14	749.40	578.46	-	12/2021	3(R3)	0/0
48	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98	1,122.00	994.02	-	09/2021	15(R3)	0/0
49	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90	1,431.90	934.32	-	03/2024	-	0/0
50	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96	709.69	256.70	-	03/2025	-	0/0
51	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24	448.10	268.73	-	03/2025	-	0/0
52	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00	1,339.00	.82	-	03/2025	-	0/0
53	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	3,154.43	239.59	-	12/2025	-	0/0
54	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40	227.40	65.02	-	03/2030	-	0/0
55	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52	1,205.00	2.28	-	03/2030	-	0/0
56	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00	839.01	.63	-	03/2030	-	0/0
57	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57	603.23	1.68	-	03/2030	-	0/0
	<u>Western Railway</u>								
58	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10	844.10	254.99	-	03/2024	-	0/0
59	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38	393.62	152.98	-	12/2022	-	0/0
60	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26	528.49	123.75	-	12/2022	-	0/0
61	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83	154.15	109.05	-	12/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		29,485.07	54,948.43	18,612.92				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
62	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05	291.05	241.71	- 01/2022	01/2022	0(R3)	0/0
63	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59	306.59	195.70	- -	01/2022	-	0/0
64	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51	390.51	297.87	- 03/2021	03/2022	12(R3)	0/0
65	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	137.80	- -	03/2022	-	0/0
66	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45	319.96	117.56	- -	03/2022	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
67	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01	520.01	207.70	- -	12/2021	-	3/4
68	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79	245.79	204.42	- 01/2021	12/2021	11(R3)	3/4
69	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44	200.44	128.02	- 08/2021	12/2021	4(R3)	3/4
70	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51	1,049.51	155.61	- -	12/2021	-	2/4
71	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59	1,718.59	519.92	- 06/2022	03/2022	-3(R3)	2/4
72	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92	568.92	335.59	- 11/2021	03/2022	4(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
73	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL, ARUNACHAL PRADESH	12/2016	188.78 -	188.78	118.08	- 03/2021	03/2022	12(R3)	3/4
74	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL, ARUNACHAL PRADESH	02/2017	175.06 -	175.06	94.23	- 04/2022	04/2022	0(R3)	3/4
75	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL, ARUNACHAL PRADESH	02/2017	176.12 -	176.12	84.29	- 04/2022	04/2022	0(R3)	3/4
76	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL, ASSAM	10/2017	818.00 -	818.00	272.86	- -	03/2023	-	2/4
National Highways Authority Of India									
77	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61	1,048.10	1,183.14	- 10/2021	12/2021	2(R3)	3/4
78	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI, TAMIL NADU	12/2017	379.90 -	379.90	248.71	- -	12/2021	-	0/0
79	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI, UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
80	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	2,169.00	-	- -	12/2021	-	0/0
81	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI, MADHYA PRADESH	10/2019	743.88 -	743.89	490.00	- -	12/2021	-	1/3
82	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI, TAMIL NADU	02/2018	1,166.26 -	1,296.93	346.17	- -	01/2022	-	0/0
83	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI, TAMIL NADU	03/2018	1,016.92 -	1,071.00	339.86	- -	01/2022	-	0/0
84	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI, MAHARASHTRA	03/2018	289.21 -	289.21	227.37	- -	01/2022	-	0/0
85	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB	02/2018	261.76 -	207.00	205.00	- -	02/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
86	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	242.03	- -	02/2022	-	0/0
87	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	790.00	- -	02/2022	-	2/4
88	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	456.80	- -	03/2022	-	0/0
89	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	284.66	- -	03/2022	-	0/1
90	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	1,513.48	- -	03/2022	-	0/0
91	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	293.31	- -	03/2022	-	4/4
92	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	473.95	- -	03/2022	-	0/0
93	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	397.89	- -	03/2022	-	0/0
94	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	474.80	- 01/2022	04/2022	3(R3)	2/4
95	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	85.61	- -	06/2022	-	0/0
96	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 827.05	827.05	387.83	- 07/2022	07/2022	0(R3)	0/0
97	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	884.00	609.00	- -	10/2022	-	2/4
98	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	422.00	- -	11/2022	-	2/4

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (December 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
99	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	255.05	- -	12/2022	-	0/0
100	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	207.78	- 10/2022	-	-	0/0
	Total		26,440.55 -	26,912.82	13,045.80				40/64
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								
101	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	974.86	- -	12/2022	-	0/9
	Total		2,694.00 -	2,694.00	974.86				0/9
	Grand Total		65,338.51	91,449.92	34,953.64				74/124

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>ATOMIC ENERGY</u>					
	<u>Nuclear Power Corporation Of India Limited</u>					
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]NPCIL,TAMIL NADU	06/2017	49,621.00 -	09/2027 -	09/2027	0/0
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
2	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	04/2020 -	06/2022	0/0
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					
3	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	04/2018 -	10/2022	0/0
4	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	03/2017 -	10/2022	0/0
	<u>Eastern Coal Fields Limited</u>					
5	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
	<u>Neyveli Lignite Corporation</u>					
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
7	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>South-Eastern Coal Fields Limited</u>					
10	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0
11	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]SECL,MADHYA PRADESH	03/2021	496.28 -	03/2028 -	03/2028	0/0
12	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
13	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
14	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>STEEL</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Steel Authority Of India Limited (Sail)</u>					
15	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL, CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
16	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
17	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	12/2021 -	06/2022	0/0
18	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	08/2022	0/0
19	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	06/2022 -	09/2022	0/0
20	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL, KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
21	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL, MAHARASHTRA	08/2020	697.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
22	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	08/2020 -	12/2021	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
23	220 KV GRID SUPPLY - [N16000407]HPCL, ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	12/2021	0/0
24	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL, ANDHRA PRADESH	10/2020	210.94 -	08/2021 -	03/2022	0/0
25	RUF PITCH LOADING GANTRY - [N16000406]HPCL, ANDHRA PRADESH	10/2020	332.61 -	11/2022 -	11/2022	0/0
	<u>Indian Oil Corporation Limited</u>					
26	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 319.61	06/2020 12/2021	12/2021	0/0
27	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	10/2020 01/2022	03/2022	0/0
28	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL, BIHAR	04/2018	522.00 -	03/2021 12/2021	03/2022	0/0
29	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL, ANDHRA PRADESH	10/2018	316.20 -	10/2021 03/2022	03/2022	0/0
30	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL, HARYANA	09/2019	164.69 -	07/2021 03/2022	03/2022	0/0
31	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL, ODISHA	01/2020	202.16 -	07/2022 -	07/2022	0/0
32	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA	05/2016	348.00 437.00	01/2021 -	08/2022	0/0
33	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL, BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
34	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 12/2021	09/2022	0/0
35	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2022	0/0
36	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	12/2022	0/0
37	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	12/2021 01/2023	01/2023	0/0
38	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	01/2023	0/0
39	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
40	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,199.60	12/2022 07/2023	07/2023	0/0
41	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0
42	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	08/2023	0/0
43	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]IOCL,ASSAM	05/2021	412.00 -	10/2023 -	10/2023	0/0
44	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	01/2024 -	01/2024	0/0
45	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	01/2024	0/0
46	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	02/2024	0/0
47	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT	09/2020	18,936.00 -	09/2024 -	08/2024	0/0
48	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]IOCL,HARYANA	02/2021	34,627.00 -	09/2024 -	09/2024	0/0
49	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH	10/2018	177.00 -	02/2027 -	02/2027	0/0
50	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR	10/2018	176.00 -	08/2027 -	08/2027	0/0
51	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	08/2027 -	08/2027	0/0
52	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR	06/2019	439.00 -	02/2028 -	02/2028	0/0
53	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR	06/2019	347.00 -	02/2028 -	02/2028	0/0
54	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	02/2028 -	02/2028	0/0
55	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE	06/2019	303.00 -	02/2028 -	02/2028	0/0
56	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND	10/2018	613.00 -	12/2029 -	12/2029	0/0
57	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR	06/2019	988.00 -	12/2029 -	12/2029	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
58	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR	06/2019	163.00 -	12/2029 -	12/2029	0/0
59	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE	06/2019	169.00 -	12/2029 -	12/2029	0/0
60	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU	10/2018	2,998.00 -	03/2030 -	03/2030	0/0
61	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU	10/2018	1,304.00 -	03/2030 -	03/2030	0/0
62	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
	<u>Numaligarh Refinery Limited</u>					
63	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM	01/2019	12,366.00 18,968.00	10/2024 -	10/2024	0/0
64	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM	01/2019	10,228.00 9,058.00	10/2024 -	10/2024	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
65	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON - [N16000433]ONGC,ASSAM	08/2021	218.38 -	02/2023 -	02/2023	0/0
	<u>Oil India Limited</u>					
66	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 222.21	08/2020 09/2021	12/2021	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
67	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 07/2025	07/2025	0/0
68	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	- 08/2024	07/2025	0/0
	<u>National Hydro-Electric Power Corporation</u>					
69	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
70	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
71	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 2,311.89	12/2018 -	01/2022	0/0
72	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	04/2021 10/2021	01/2022	0/0
73	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	03/2021 11/2021	01/2022	0/0
74	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	11/2018 -	03/2022	0/0
75	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	03/2022 03/2022	05/2022	0/0
76	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	06/2021 12/2021	07/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
77	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	09/2021 08/2022	08/2022	0/0
78	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	09/2021 08/2022	08/2022	0/0
79	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	09/2021 08/2022	08/2022	0/0
80	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	07/2022 05/2022	08/2022	0/0
81	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	07/2022 -	08/2022	0/0
82	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	07/2022 -	08/2022	0/0
83	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]NTPC,GUJARAT	05/2021	674.92 -	09/2022 -	09/2022	0/0
84	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	09/2021 10/2022	10/2022	0/0
85	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	09/2021 10/2022	10/2022	0/0
86	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80	10/2021 10/2022	10/2022	0/0
87	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	09/2021 10/2022	10/2022	0/0
88	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN	03/2020	1,749.31 -	09/2021 10/2022	10/2022	0/0
89	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
90	TALAIALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-	0/0
Power Grid Corporation Of India Limited						
91	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021	0/0
92	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 06/2021	06/2021	0/0
93	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021	0/0
94	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 07/2021	10/2021	0/0
95	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 09/2021	10/2021	0/0
96	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	12/2021	0/0
97	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 09/2021	01/2022	0/0
98	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 08/2021	01/2022	0/0
99	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 11/2021	02/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
100	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 12/2020	02/2022	0/0
101	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2022	0/0
102	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	12/2018 12/2021	03/2022	0/0
103	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	07/2019 07/2021	03/2022	0/0
104	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 04/2022	04/2022	0/0
105	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	12/2018 03/2024	03/2024	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
106	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]SJVN,HIMACHAL PRADESH	10/2020	687.97 -	11/2025 -	11/2025	0/0
107	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH	11/2020	1,810.56 -	01/2026 -	01/2026	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
108	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Cpwd For Health</u>					
109	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
110	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
111	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
112	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>HII Infra Tech Services Limited</u>					
113	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-	0/0
114	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-	0/0
115	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
116	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
117	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
118	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
119	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021	0/0
120	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
121	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021	0/0
122	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021	0/0
123	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	10/2021	0/0
124	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	10/2021	0/0
125	GERIATRICS BLOCK- AIIMS DELHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	12/2021	0/0
126	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	12/2021	0/0
127	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	03/2022	0/0
128	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	03/2022	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
129	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2023	0/0
130	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
131	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2023	0/0
132	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
133	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
134	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
135	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
136	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
137	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
138	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
139	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
140	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95	03/2023	03/2024	0/0
141	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06	03/2019	-	0/0
142	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00	03/2024	-	0/0
<u>Container Corporation Of India</u>						
143	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17	03/2018	-	0/0
144	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00	03/2019	-	0/0
145	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70	03/2018	-	0/0
146	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00	03/2018	-	0/0
147	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32	03/2019	-	0/0
148	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00	03/2019	-	0/0
149	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00	03/2019	-	0/0
150	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50	03/2019	-	0/0
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
151	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
152	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
<u>East Central Railways</u>						
153	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECR,BIHAR	04/1999	325.00 735.20	- -	03/2021	0/0
154	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	477.88 751.55	03/2012 09/2021	09/2021	0/0
155	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]JECR,JHARKHAND	03/1999	1,033.07 3,020.95	- 03/2022	03/2022	0/0
156	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH	08/2015	528.57	03/2019	03/2022	0/0
157	GARHWA ROAD-RAMNA - [N22000465]JECR,JHARKHAND	03/2015	348.23	03/2021	03/2022	0/0
158	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]JECR,BIHAR	04/1991	329.39 803.11	- 03/2022	03/2022	0/0
159	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]JECR,BIHAR	04/1997	324.73 898.53	03/2012 11/2022	11/2022	0/0
160	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]JECR,BIHAR	04/2003	528.65 2,066.78	- 03/2023	03/2023	0/0
161	KODERMA-TILAIYA (NL), ECR - [220100305]JECR,JHARKHAND	04/2002	459.91 1,625.87	- 03/2023	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
162	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2023	0/0
163	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- 03/2023	03/2023	0/0
164	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2023	0/0
165	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	- -	12/2023	0/0
166	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
167	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
168	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2024	0/0
169	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	03/2021 03/2024	03/2024	0/0
170	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	03/2021 03/2024	03/2024	0/0
171	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00	03/2020 03/2023	12/2024	0/0
172	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	03/2025	0/0
173	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	-	0/0
174	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-	0/0
175	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
176	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-	0/0
177	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
178	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
179	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
180	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
181	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
182	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
183	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
<u>East Coast Railway</u>						
184	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
185	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	03/2020 -	03/2022	0/0
186	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
187	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2024	03/2024	0/0
188	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2024	0/0
189	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2024	03/2024	0/0
190	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 12/2024	12/2024	0/0
191	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 03/2025	03/2025	0/0
192	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2024	03/2026	0/0
193	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
<u>Eastern Railways</u>						
194	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021	0/0
195	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
196	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0
197	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	03/2022	0/0
198	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
199	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
200	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
201	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
202	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
203	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
204	PIRPAINI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
205	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR -CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
206	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
207	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
209	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
210	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
211	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
212	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
213	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
214	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
215	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
216	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
217	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
218	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
	<u>Kolkata Metro Rail Corporation Limited</u>					
219	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
220	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	03/2004 06/2022	06/2022	0/0
221	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
222	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
223	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-	0/0
224	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
225	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
226	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	06/2025	0/0
227	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- 04/2010	12/2027	0/0
	<u>North East Frontier Railway</u>					
228	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	10/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
229	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	12/2021	0/0
230	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2022	0/0
231	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- 12/2021	06/2022	0/0
232	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2023	0/0
233	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
234	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 12,264.00	03/2011 12/2023	12/2023	0/0
235	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 5,021.45	03/2014 -	12/2023	0/0
236	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 4,084.69	12/2015 12/2023	12/2023	0/0
237	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 2,042.51	03/2019 -	12/2023	0/0
238	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2024	0/0
239	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	03/2015 -	03/2026	0/0
240	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-	0/0
241	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
242	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
243	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-	0/0
244	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-	0/0
245	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-	0/0
246	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
247	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-	0/0
248	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-	0/0
<u>North Eastern Railway</u>						
249	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
250	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
251	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
252	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0
253	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
254	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 600.00	01/2022 -	03/2022	0/0
255	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
256	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
257	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
258	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
259	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	03/2025	0/0
260	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
261	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
262	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
263	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
	<u>North Western Railway</u>					
264	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	09/2021	0/0
265	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	06/2022	0/0
266	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	10/2022	0/0
267	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	11/2022	0/0
268	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
269	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
270	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021	0/0
271	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	12/2022	0/0
272	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	09/2023	0/0
273	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
274	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
275	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
276	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	11/2024	0/0
277	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	08/2016 -	08/2025	0/0
278	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 12/2025	12/2025	0/0
279	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-	0/0
280	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
281	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	12/2023	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
282	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
283	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	12/2021	0/0
284	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2021	0/0
285	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	12/2021	0/0
286	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	12/2021	0/0
287	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	12/2021	0/0
288	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2021	0/0
289	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
290	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
291	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	06/2022	0/0
292	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	06/2022	0/0
293	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
294	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	06/2022	0/0
295	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
296	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
297	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
298	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76 -	12/2023 -	12/2023	0/0
299	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
300	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
301	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
302	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
303	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
304	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
305	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
306	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
307	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
308	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2026	0/0
<u>Railway Electrification</u>						
309	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
310	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2023	0/0
311	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2024	0/0
312	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
313	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
314	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2024	0/0
315	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
316	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 176.18	03/2022 03/2022	-	0/0
<u>South East Central Railway</u>						
317	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	12/2021 12/2023	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>South Eastern Railway</u>					
318	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	03/2019	0/0
319	CHAKRADHARPUR TO GOILKERA 3RD LINE (34 KM) - [N22000507]SER,JHARKHAND	11/2015	354.54 -	12/2018 -	06/2020	0/0
320	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	06/2022	0/0
321	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	12/2021 -	06/2022	0/0
322	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	06/2022 -	06/2023	0/0
323	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2023	0/0
324	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	05/2023 -	12/2023	0/0
325	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	-	03/2025	0/0
326	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
327	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	06/2022 -	12/2025	0/0
328	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	03/2030	0/0
329	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
	<u>South Western Railway</u>					
330	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	09/2021	0/0
331	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	-	12/2023	0/0
332	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	-	12/2023	0/0
333	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	-	12/2023	0/0
334	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	-	12/2023	0/0
335	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
336	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
337	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
338	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	03/2019 -	03/2024	0/0
339	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	-	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
340	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	03/2017 -	03/2025	0/0
341	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	06/2025	0/0
342	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2025	0/0
<u>Southern Railway</u>						
343	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- 12/2021	02/2022	0/0
344	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- 12/2021	03/2022	0/0
345	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- 09/2021	12/2022	0/0
346	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	03/2024	0/0
347	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2025	0/0
348	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
349	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 369.55	- -	03/2025	0/0
350	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 275.21	- -	03/2025	0/0
351	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 1,246.00	- -	03/2025	0/0
352	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
353	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
354	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0
355	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	03/2030	0/0
356	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	03/2030	0/0
357	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	03/2030	0/0
358	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	03/2030	0/0
359	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	03/2030	0/0
360	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-	0/0
361	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
362	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Western Railway</u>					
363	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	1,037.15 -	03/2021 -	12/2022	0/0
364	SURENDRA NAGAR RAJKOT - [N22000392]WR, GUJARAT	04/2015	1,002.39 -	03/2021 -	12/2022	0/0
365	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	3,503.69 -	03/2022 -	03/2023	0/0
366	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 1,524.68	03/2022 03/2023	03/2023	0/0
367	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 859.16	03/2019 03/2023	03/2023	0/0
368	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR, MADHYA PRADESH	04/2016	700.00 603.69	06/2020 03/2023	03/2023	0/0
369	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 321.62	03/2012 10/2023	10/2023	0/0
370	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	829.74 1,631.75	03/2020 03/2024	03/2024	0/0
371	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	844.10 -	- -	03/2024	0/0
372	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR, MADHYA PRADESH	04/2017	495.18 -	03/2022 -	03/2024	0/0
373	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR, GUJARAT	04/2017	692.25 692.25	03/2020 03/2024	03/2024	0/0
374	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR, GUJARAT	04/2018	537.31 537.31	03/2024 03/2024	03/2024	0/0
375	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2025	03/2025	0/0
376	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR, MAHARASHTRA	03/2010	265.88 311.36	- -	-	0/0
377	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR, MAHARASHTRA	03/2012	217.38 393.62	- 12/2022	-	0/0
378	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR, GUJARAT	03/2012	248.26 528.49	- 12/2022	-	0/0
379	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR, GUJARAT	03/2012	153.83 154.15	- 12/2021	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
380	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH, UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019	0/0
381	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020	0/0
382	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH, ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020	0/0
383	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH, UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
384	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2020	12/2020	0/0
385	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021	0/0
386	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021	0/0
387	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021	0/0
388	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 03/2020	03/2021	0/0
389	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021	0/0
390	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	04/2021	0/0
391	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021	0/0
392	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 06/2021	06/2021	0/0
393	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021	0/0
394	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021	0/0
395	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021	0/0
396	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021	0/0
397	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021	0/0
398	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 08/2021	08/2021	0/0
399	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021	0/0
400	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 09/2021	09/2021	0/0
401	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	09/2021 -	09/2021	0/0
402	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- 10/2021	10/2021	0/0
403	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 237.80	11/2019 10/2021	10/2021	0/0
404	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2021	10/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
405	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021	0/0
406	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	01/2021 -	11/2021	0/0
407	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	11/2021	0/0
408	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 12/2021	12/2021	0/0
409	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 12/2021	12/2021	0/0
410	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 09/2021	12/2021	0/0
411	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	12/2021	0/0
412	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 01/2022	01/2022	0/0
413	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 06/2021	01/2022	0/0
414	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 927.73	02/2020 08/2021	01/2022	0/0
415	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 01/2022	01/2022	0/0
416	UPGRADATION OF MAKSDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 11/2021	01/2022	0/0
417	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	01/2022	0/0
418	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 949.54	06/2019 04/2021	01/2022	0/0
419	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	01/2022	0/0
420	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 01/2022	01/2022	0/0
421	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 01/2022	01/2022	0/0
422	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 10/2021	02/2022	0/0
423	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 174.90	08/2018 08/2021	02/2022	0/0
424	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 09/2021	02/2022	0/0
425	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 12/2021	02/2022	0/0
426	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	08/2018 09/2021	02/2022	0/0
427	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 10/2021	02/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
428	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 08/2021	02/2022	0/0
429	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 02/2022	02/2022	0/0
430	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	03/2018 06/2021	02/2022	0/0
431	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 -	02/2022	0/0
432	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- 03/2021	03/2022	0/0
433	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	11/2018 01/2021	03/2022	0/0
434	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	03/2022	0/0
435	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2022	03/2022	0/0
436	CONSTRUCTION ON TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 11/2021	03/2022	0/0
437	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	03/2022	0/0
438	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2022	0/0
439	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	03/2022	0/0
440	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 03/2022	03/2022	0/0
441	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	09/2016 03/2022	03/2022	0/0
442	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 03/2022	03/2022	0/0
443	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 03/2022	03/2022	0/0
444	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 319.96	03/2016 04/2022	04/2022	0/0
445	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 03/2022	04/2022	0/0
446	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 05/2022	05/2022	0/0
447	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 09/2021	06/2022	0/0
448	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	08/2016 06/2022	06/2022	0/0
449	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	10/2016 06/2022	06/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
450	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	07/2022	0/0
451	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	08/2019 08/2022	08/2022	0/0
452	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	08/2019 -	11/2022	0/0
453	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	12/2022	0/0
454	REHABILITATION AND UPGRADE OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	07/2016 12/2022	12/2022	0/0
455	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH, TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
456	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACHAL PRADESH - [N24001373]MoRTH,ARUNACHAL PRADESH	01/2020	358.26 -	02/2024 -	02/2024	0/0
457	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]MoRTH,UTTAR PRADESH	07/2018	1,948.25 -	02/2024 -	02/2024	0/0
458	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACHAL PRADESH - [N24001372]MoRTH,ARUNACHAL PRADESH	02/2021	588.09 -	03/2024 -	03/2024	0/0
459	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]MoRTH,ASSAM	02/2021	925.47 -	07/2025 -	07/2025	0/0
460	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
461	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
462	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-	0/0
463	REHABILITATION AND UPGRADE OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
464	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
465	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-	0/0
466	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-	0/0
467	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-	0/0
468	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-	0/0
469	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-	0/0
470	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-	0/0
471	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
472	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
473	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-	0/0
474	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
475	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
476	FOUR LANEING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-	0/0
477	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
478	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
479	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
480	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
481	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
482	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
483	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-	0/0
484	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-	0/0
485	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 194.48	11/2020 -	-	0/0
486	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
487	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
488	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
489	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
490	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
491	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
492	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
493	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
494	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0
495	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0
496	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
497	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
498	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
499	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
500	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
501	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
502	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
503	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
504	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
505	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
506	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0
507	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
508	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
509	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
510	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
511	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
512	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-	0/0
513	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-	0/0
514	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-	0/0
515	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-	0/0
516	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
517	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
518	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
519	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-	0/0
520	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
521	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
522	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-	0/0
523	KHANGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-	0/0
524	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
525	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-	0/0
526	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-	0/0
527	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-	0/0
528	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-	0/0
529	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-	0/0
530	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-	0/0
531	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
532	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-	0/0
533	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
534	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
535	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-	0/0
536	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
537	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
538	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
539	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
540	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
541	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
542	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
543	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
544	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
545	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
546	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
547	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0
548	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
549	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-	0/0
550	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 12/2021	-	0/0
551	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 12/2021	-	0/0
552	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-	0/0
553	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 04/2022	-	0/0
554	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
555	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-	0/0
556	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-	0/0
557	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-	0/0
558	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-	0/0
559	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-	0/0
560	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-	0/0
561	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-	0/0
562	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-	0/0
563	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-	0/0
564	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-	0/0
565	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-	0/0
566	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-	0/0
567	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	08/2021 -	-	0/0
568	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	08/2021 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
569	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-	0/0
570	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-	0/0
571	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-	0/0
572	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-	0/0
573	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	-	0/0
574	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	-	0/0
575	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-	0/0
576	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-	0/0
577	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-	0/0
578	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-	0/0
579	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-	0/0
580	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-	0/0
581	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2021	-	0/0
582	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
583	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- 11/2021	03/2022	0/0
584	IMPHAL - MOREH (PACKAGE 4) - [N24001399]NHIDCL,MANIPUR	03/2021	277.99 -	01/2023 -	01/2023	0/0
585	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR	07/2021	512.43 -	02/2023 -	02/2023	0/0
586	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR	07/2021	497.09 -	02/2023 -	02/2023	0/0
587	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR	02/2021	431.28 -	03/2023 -	03/2023	0/0
588	MARIAM - PEREN (PKG 2A) - [N24001398]NHIDCL,MANIPUR	07/2021	204.58 -	03/2023 -	03/2023	0/0
589	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR	07/2021	467.00 -	03/2023 -	03/2023	0/0
590	TAMENGLONG - MAHUR PKG-1 - [N24001402]NHIDCL,MANIPUR	07/2021	185.80 -	03/2023 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
591	TAMENGLONG - MAHUR PKG-2 - [N24001403]NHIDCL, MANIPUR	07/2021	483.87 -	03/2023 -	03/2023	0/0
592	TAMENGLONG - MAHUR PKG-4 - [N24001404]NHIDCL, MANIPUR	07/2021	198.77 -	03/2023 -	03/2023	0/0
593	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]NHIDCL, NAGALAND	07/2021	258.52 -	03/2023 -	03/2023	0/0
594	PEREN-DIMAPUR PKG-5 - [N24001407]NHIDCL, NAGALAND	02/2021	207.33 -	03/2023 -	03/2023	0/0
595	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL, JAMMU AND KASHMIR	07/2021	859.67 -	08/2023 -	08/2023	0/0
596	CHURACHANPUR TUIVAI PKG-3 - [N24001405]NHIDCL, MANIPUR	07/2021	673.27 -	10/2023 -	10/2023	0/0
National Highways Authority Of India						
597	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	- 02/2018	02/2018	0/0
598	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI, HARYANA	03/2018	795.50 906.65	- 02/2018	02/2018	0/0
599	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	11/2018	0/0
600	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019	0/0
601	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
602	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- 01/2020	01/2020	0/0
603	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
604	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020	0/0
605	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020	0/0
606	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020	0/0
607	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
608	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
609	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020	0/0
610	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020	0/0
611	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
612	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	- -	03/2021	0/0
613	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
614	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
615	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN	02/2018	716.76 -	- 07/2021	07/2021	0/0
616	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
617	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
618	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI, ODISHA	01/2018	614.48 -	- -	08/2021	0/0
619	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021	0/0
620	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021	0/0
621	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 1,201.51	- 06/2021	09/2021	0/0
622	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
623	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA	12/2017	404.94 499.70	- 05/2021	09/2021	0/0
624	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI, ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
625	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI, ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
626	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 866.55	- 10/2021	10/2021	0/0
627	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI, KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
628	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	11/2021	0/0
629	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	12/2021	0/0
630	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	07/2018 -	12/2021	0/0
631	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	07/2019 -	12/2021	0/0
632	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	07/2019 -	12/2021	0/0
633	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	06/2018 12/2021	12/2021	0/0
634	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI, TAMIL NADU	03/2017	848.45 -	03/2020 -	12/2021	0/0
635	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	07/2016 -	12/2021	0/0
636	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI, TAMIL NADU	12/2017	379.90 -	- -	12/2021	0/0
637	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI, UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
638	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	12/2021	0/0
639	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021	0/0
640	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	01/2022	0/0
641	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	01/2022	0/0
642	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	01/2022	0/0
643	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	01/2022	0/0
644	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	01/2022	0/0
645	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	01/2022	0/0
646	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	02/2022	0/0
647	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
648	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	02/2022	0/0
649	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	02/2022	0/0
650	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2022	0/0
651	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 03/2022	03/2022	0/0
652	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2022	0/0
653	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	03/2022	0/0
654	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	03/2022	0/0
655	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	03/2022	0/0
656	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	03/2022	0/0
657	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	03/2022	0/0
658	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 12/2021	06/2022	0/0
659	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2022	0/0
660	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 827.05	- 07/2022	07/2022	0/0
661	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
662	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022	0/0
663	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	09/2022	0/0
664	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
665	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	12/2022	0/0
666	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 720.81	03/2023 -	03/2023	0/0
667	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	05/2023	0/0
668	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 12/2022	06/2023	0/0
669	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414]NHAI,PUNJAB	12/2020	733.00 -	01/2024 -	01/2024	0/0
670	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	01/2024 -	01/2024	0/0
671	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB	12/2020	881.00 -	04/2024 -	04/2024	0/0
672	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB	12/2020	1,234.40 -	04/2024 -	04/2024	0/0
673	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB	12/2020	1,094.46 -	04/2024 -	04/2024	0/0
674	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]NHAI,PUNJAB	02/2021	1,269.96 -	04/2024 -	04/2024	0/0
675	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - - [N24001420]NHAI,PUNJAB	02/2021	853.66 -	04/2024 -	04/2024	0/0
676	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
677	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
678	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
679	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
680	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
681	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
682	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-	0/0
683	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
684	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
685	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
686	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
687	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
688	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
689	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
690	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
691	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
692	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
693	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
694	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
695	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
696	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
697	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
698	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
699	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
700	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
701	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
702	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
703	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
704	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-	0/0
705	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
706	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
707	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
708	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
709	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
710	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
711	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 363.93	- -	-	0/0
712	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-	0/0
713	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-	0/0
714	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
715	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
716	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
717	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-	0/0
718	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
719	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
720	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-	0/0
721	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
722	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
723	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,457.82	03/2018 03/2021	-	0/0
724	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
725	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
726	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
727	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
728	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
729	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
730	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
731	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
732	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
733	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
734	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
735	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	-	0/0
736	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
737	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
738	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
739	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
740	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 1,096.52	04/2018 -	-	0/0
741	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
742	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
743	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0
744	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
745	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
746	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-	0/0
747	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
748	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
749	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
750	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
751	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 10/2022	-	0/0
752	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- 10/2022	-	0/0
753	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
754	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
755	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
756	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-	0/0
757	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
758	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
759	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
760	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
761	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
762	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-	0/0
763	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-	0/0
764	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	-	0/0
765	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
766	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-	0/0
767	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
768	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-	0/0
769	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-	0/0
770	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-	0/0
771	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
772	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
773	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	-	0/0
774	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	-	0/0
775	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
776	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
777	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
778	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
779	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 02/2022	-	0/0
780	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
781	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
782	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
783	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-	0/0
784	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
785	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-	0/0
786	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-	0/0
787	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-	0/0
788	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
789	REHABILITATION AND UPGRADATION BY 4-LANNING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	-	0/0
790	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
791	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
792	SIX LANNING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0
793	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-	0/0
794	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
795	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
796	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-	0/0
797	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
798	FOUR LANNING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
799	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
800	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-	0/0
801	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-	0/0
802	REHABILITATION AND UPGRADATION OF FOUR LANNING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
803	6-LANNING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
804	SIX LANNING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
805	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
806	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
807	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
808	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
809	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
810	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
811	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
812	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
813	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
814	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
815	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
816	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
817	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
818	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
819	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
820	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
821	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
822	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
823	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
824	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-	0/0
825	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
826	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
827	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
828	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
829	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
830	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
831	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
832	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
833	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
834	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
835	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
836	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
837	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
838	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-	0/0
839	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
840	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
841	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
842	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
843	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
844	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0
845	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
846	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
847	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-	0/0
848	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-	0/0
849	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0
850	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
851	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
852	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-	0/0
853	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
854	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-	0/0
855	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
856	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
857	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
858	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-	0/0
859	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-	0/0
860	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-	0/0
861	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
862	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-	0/0
863	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-	0/0
864	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-	0/0
865	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-	0/0
866	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-	0/0
867	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-	0/0
868	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-	0/0
869	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-	0/0
870	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	11/2019 -	-	0/0
871	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	11/2019 -	-	0/0
872	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	11/2019 -	-	0/0
873	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
874	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-	0/0
875	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 1,135.08	- 11/2021	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
876	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	06/2021 11/2021	03/2022	0/0
	<u>Department Of Telecommunication</u>					
877	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	07/2015 05/2020	03/2022	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
878	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 422.00	03/2021 06/2023	06/2023	0/0
879	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	03/2022 -	06/2023	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
880	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
881	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
882	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	03/2025	0/0
883	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	05/2025	0/0
	<u>Maharastra Metro Rail Corporation Ltd.</u>					
884	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11/2021 12/2022	12/2022	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
885	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	03/2020 03/2023	03/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
886	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
887	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
888	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 12/2021	12/2021	0/0
	<u>Patna Metro Rail Corporation</u>					
889	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL,BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	Brahmaputra Board					
890	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2021	0/0
	Bihar Urban Infrastructure Development Corporation Ltd					
891	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	12/2021	0/0
892	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	02/2022	0/0
893	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	03/2022	0/0
894	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	04/2022	0/0
895	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2022	0/0
896	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	06/2022	0/0
897	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	07/2022	0/0
898	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	12/2022	0/0
899	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	12/2022	0/0
900	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	04/2023	0/0
901	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	12/2023	0/0
902	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	03/2024	0/0
	Delhi Jal Board					
903	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	12/2021	0/0
904	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
905	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
906	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
907	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-	0/0
	Kolkata Metropolitan Development Authority					
908	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2022	0/0
909	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	12/2021 -	09/2023	0/0
910	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	12/2021 -	09/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
911	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	12/2021 -	09/2023	0/0
912	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	02/2022 -	03/2024	0/0
913	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	06/2022 -	03/2024	0/0
914	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	02/2022 -	03/2024	0/0
915	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2024	0/0
916	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2024	0/0
917	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2024	0/0
918	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	09/2022 -	04/2024	0/0
919	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 05/2022	-	0/0
	<u>Uttar Pradesh Jal Nigam</u>					
920	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP JalNigam, UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	11/2021	0/0
921	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 -	09/2021 -	12/2021	0/0
922	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45 -	12/2020 -	12/2021	0/0
923	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59 -	09/2021 -	03/2022	0/0
924	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05 -	10/2021 -	03/2022	0/0
925	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam, UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2022	0/0
926	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	08/2021 -	03/2024	0/0
927	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12 213.91	07/2021 -	03/2024	0/0
928	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam, UTTAR PRADESH	10/2017	213.62 261.12	03/2022 -	04/2024	0/0
929	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UP JalNigam, UTTAR PRADESH	02/2019	681.78 -	06/2022 -	04/2024	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
930	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UK JalNigam, UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	03/2022	0/0
	<u>SOCIAL JUSTICE</u>					
	<u>Central Public Works Department</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
931	CENTRE FOR DISABILITY SPORTS - [N38000001]CPWD,MADHYA PRADESH	02/2019	170.99 -	03/2024 -	03/2024	0/0
	<u>COMMERCE</u>					
	<u>Nbcc For Commerce</u>					
932	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-	0/0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>					
	<u>Cpwd Of Higher Education</u>					
933	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	07/2022 -	10/2022	0/0
934	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I - [N28000141]CPWD EDUCATION,CHHATISGARH	03/2020	808.62	07/2022	10/2022	0/0
935	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH	09/2018	392.51 -	06/2022 10/2022	10/2022	0/0
936	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	09/2020 -	11/2022	0/0
937	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD EDUCATION,JAMMU AND KASHMIR	01/2018	676.00 748.19	04/2023 -	04/2023	0/0
938	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	09/2022 06/2023	06/2023	0/0
	<u>Rites Of Higher Education</u>					
939	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 429.70	09/2014 06/2022	06/2022	0/0
	<u>HOME AFFAIRS</u>					
	<u>Cpwd For Mha</u>					
940	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDLAULI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31 -	01/2022 -	01/2020	0/0
941	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE - [N28000147]CPWD FOR MHA,HARYANA	01/2020	166.98 166.98	10/2023 04/2024	04/2024	0/0
	<u>DPIIT</u>					
	<u>Dmic For Dpiit</u>					
942	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021	0/0
	<u>Iicc For Dpiit</u>					
943	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	12/2019 05/2022	05/2022	0/0
	<u>RENEWABLE ENERGY</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (December 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Cpwd For Renewable Energy</u>					
944	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-	0/0
	Total		12,02,594.12 -			0/0
	Grand Total		12,02,594.12			0/0

FLASH REPORT

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA [N04000080]	1/2016	458.00 -	458.00	161.87	03/2020 06/2022	04/2022
	Total		458.00 -	458.00	161.87		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00 -	1,828.00	218.99	09/2025 -	05/2024
	Total		1,828.00 -	1,828.00	218.99		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
3	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	3,072.00	2,673.55	06/2021 08/2022	07/2022
	<u>Indian Oil Corporation Limited</u>						
4	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00 -	18,936.00	829.33	09/2024 -	08/2024
	Total		21,613.00 -	22,008.00	3,502.88		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
5	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,764.97	03/2024 -	03/2023
	<u>Rail Vikas Nigam Ltd.</u>						
6	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	1,905.63	12/2026 -	12/2025
7	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
8	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,477.01	03/2023 -	12/2022
	Total		9,445.24 -	14,104.67	6,147.80		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
9	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	96.49	12/2022 -	07/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
10	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	142.87	09/2019 06/2023	04/2023
11	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946	3/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022
	Total		2,493.92 -	2,493.92	759.28		
	Grand Total		35,838.16	40,892.59	10,790.82		

FLASH REPORT

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	5,074.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	5,074.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	494.81	09/2018 06/2022	06/2022
3	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71 -	389.71	216.37	11/2021 04/2023	04/2023
4	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT [N04000091]	4/2020	611.80 -	611.80	67.47	03/2023 -	03/2023
	Total		1,418.74 -	1,709.24	778.65		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
5	MAGADH EXPANSION OC(51 MTY) - [N06000015]	8/2008	6,964.33 6,964.33	7,254.37	814.20	07/2012 03/2028	03/2028
6	RECAST EPR AMRAPALI OC - [N06000103]	2/2012	4,983.58 4,983.58	4,983.58	370.76	03/2020 03/2028	03/2028
7	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	778.80	406.92	03/2023 -	03/2023
8	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	37.28	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
9	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY - [N06000020]	11/2015	1,210.12 -	1,210.12	49.12	03/2029 03/2029	03/2029
10	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	260.37	03/2022 -	03/2022
11	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.75	03/2026 -	03/2026
12	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	22.79	03/2029 -	03/2029
13	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	7.95	03/2025 -	03/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	.18	03/2027 -	03/2027
15	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	3.78	03/2027 -	03/2027
16	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	165.05	03/2024 -	03/2024
	<u>Mahanadi Coal Fields Limited</u>						
17	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,697.74	03/2026 -	03/2026
18	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY) - [N06000035]	12/2007	8,416.19 8,416.19	8,416.19	1,166.07	03/2013 03/2028	03/2028
19	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,318.06	03/2029 -	03/2029
20	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	773.61	03/2027 -	03/2027
21	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY) - [N06000044]	12/2007	3,504.21 3,504.21	3,504.21	606.54	03/2010 03/2029	03/2029
	<u>Neyveli Lignite Corporation</u>						
22	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	496.19	06/2015 03/2025	03/2025
23	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	12,939.55	11/2021 11/2022	11/2022
	<u>Northern Coal Fields Limited</u>						
24	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
25	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
26	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
27	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	1.03	03/2023 -	03/2023
28	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
	<u>Singareni Colliers Company Limited</u>						
29	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	88.95	03/2023 -	03/2023
30	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	111.78	03/2024 -	03/2024
31	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	25.43	03/2023 -	03/2023
	<u>South-Eastern Coal Fields Limited</u>						
32	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023
33	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	322.85	03/2029 -	03/2029
34	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
36	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	2,031.19	03/2029 -	03/2029
37	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	187.07	03/2024 -	03/2024
38	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.68	03/2021 04/2024	04/2024
39	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	46.75	03/2026 -	03/2026
40	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
41	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	76.12	03/2026 -	03/2026
42	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,162.39	03/2023 -	03/2023
43	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	169.69	03/2022 -	03/2022
	<u>Western Coal Fields Limited</u>						
44	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) [N06000141]	11/2015	313.34 -	313.34	159.36	03/2021 03/2024	03/2024
45	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
46	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
47	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	2.65	03/2026 -	03/2026
48	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	107.27	03/2021 09/2022	09/2022
49	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	223.12	03/2021 09/2022	09/2022
50	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
51	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	298.78	03/2021 09/2023	09/2023
52	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	289.29 -	289.30	37.55	03/2022 03/2025	03/2025
53	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	248.72	03/2022 -	03/2022
54	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	7/2016	281.25 -	281.25	23.52	03/2022 03/2026	03/2026
55	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	423.42	03/2025 -	03/2025
56	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	299.67	213.92	03/2019 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	87.35	03/2023 -	03/2023
58	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]	11/2014	1,184.33 -	1,184.33	393.29	03/2020 03/2027	03/2027
59	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	84.05	03/2028 -	03/2028
60	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]	11/2015	851.60 -	826.80	283.28	03/2020 03/2026	03/2026
	Total		94,521.11 -	93,592.08	31,229.76		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
61	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	223.43	04/2023 -	04/2023
62	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]	2/2019	655.34 -	655.34	300.85	06/2020 11/2022	11/2022
63	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	85.88	06/2022 10/2022	10/2022
64	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]	9/2019	588.72 -	588.72	117.82	09/2022 06/2023	06/2023
65	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]	5/2019	303.90 -	303.90	48.30	03/2020 02/2023	02/2023
	<u>Rites Of Higher Education</u>						
66	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	9/2013	484.32 -	429.70	230.00	09/2014 06/2022	06/2022
	Total		3,100.79 -	3,046.17	1,006.28		
	<u>DPIIT</u>						
	<u>Iicc For Dpiit</u>						
67	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	3,044.41	12/2019 05/2022	05/2022
	Total		4,773.00 -	5,178.00	3,044.41		
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
68	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	324.01	04/2020 01/2022	01/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		426.72 -	426.72	324.01		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
69	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	394.73	09/2023 -	09/2023
70	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	Total		2,981.00 -	3,232.00	394.73		
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
71	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	173.06	04/2018 08/2022	08/2022
72	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	7.84	10/2023 04/2024	04/2024
73	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]	6/2019	277.35 -	290.33	38.13	07/2022 12/2022	12/2022
	Total		607.21 -	695.31	219.03		
	<u>MINES</u>						
	<u>Central Public Works Department</u>						
74	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]	4/2019	255.37 -	255.37	.86	04/2022 12/2024	12/2024
	<u>National Aluminum Company Limited (Nalco)</u>						
75	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	1,182.87	04/2021 01/2024	01/2024
76	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	10.40	04/2021 12/2023	12/2023
	Total		6,278.37 -	6,278.37	1,194.13		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
77	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 08/2022	08/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
78	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	299.02	03/2023 -	03/2023
79	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023
	<u>Gas Authority Of India Limited</u>						
80	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	255.92	04/2022 -	04/2022
81	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	197.09	10/2022 -	10/2022
82	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	111.42	10/2022 -	10/2022
83	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	355.80	11/2022 -	11/2022
84	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]	5/2019	8,797.00 -	8,797.00	178.78	04/2025 -	04/2025
85	60 KTA POLYPROPYLENE PROJECT - [N16000429]	3/2019	910.56 -	910.56	117.31	04/2024 -	04/2024
86	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,789.70	05/2023 -	05/2023
87	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]	8/2018	217.92 -	217.92	105.90	04/2021 03/2022	03/2022
88	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	553.20	07/2022 -	07/2022
89	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	149.60	10/2022 -	10/2022
90	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	99.81	07/2022 -	07/2022
91	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	166.06	07/2022 -	07/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
92	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	26,264.00	17,704.50	07/2020 07/2022	07/2022
93	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	30.88	11/2022 -	11/2022
94	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	229.78	02/2023 -	02/2023
95	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	146.12	03/2031 08/2031	08/2031
96	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	515.69	03/2029 08/2029	08/2029
97	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	193.31	09/2026 02/2027	02/2027

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
98	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	438.32	11/2022 -	11/2022
99	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	339.20	11/2021 03/2022	03/2022
100	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	175.31	12/2022 -	12/2022
101	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	1,461.90	06/2022 -	06/2022
102	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]	9/2021	160.00 -	160.00	-	06/2024 -	06/2024
103	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	13.36	03/2024 -	03/2024
	Indian Oil Corporation Limited						
104	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	3,338.00	3,124.58	12/2020 03/2022	03/2022
105	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	6,025.00	4,159.59	12/2018 02/2022	02/2022
106	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	340.76	164.11	02/2020 07/2022	07/2022
107	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]	8/2017	236.00 -	319.61	226.65	06/2020 12/2021	12/2021
108	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,605.89	02/2022 -	02/2022
109	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	136.20	08/2020 03/2022	03/2022
110	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	2,360.01	09/2022 03/2022	03/2022
111	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	206.83	- 05/2023	05/2023
112	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	687.88	05/2023 -	05/2023
113	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	206.62	04/2022 -	04/2022
114	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	373.81	12/2021 01/2023	01/2023
115	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	673.16	12/2022 07/2023	07/2023
116	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	427.00	35.56	09/2022 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
117	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	101.96	06/2021 07/2022	07/2022
118	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	2,099.36	08/2021 09/2022	09/2022
119	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	140.65	09/2021 06/2022	06/2022
120	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	470.06	02/2020 02/2022	02/2022
121	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS [N16000420]	6/2019	2,880.00 -	2,880.00	113.40	08/2027 -	08/2027
122	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	42.90	03/2030 -	03/2030
123	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	202.71	03/2030 -	03/2030
124	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	66.77	02/2027 -	02/2027
125	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS [N16000416]	10/2018	613.00 -	613.00	161.96	12/2029 -	12/2029
126	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS [N16000415]	10/2018	176.00 -	176.00	79.72	08/2027 -	08/2027
127	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	26.64	10/2023 -	10/2023
128	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	505.01	09/2024 -	09/2024
129	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM [N16000411]	10/2020	1,614.00 -	1,614.00	1.12	08/2023 -	08/2023
130	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	182.84	12/2022 -	12/2022
131	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	111.34	08/2022 -	08/2022
132	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	579.94	01/2024 -	01/2024
133	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	61.04	07/2022 -	07/2022
134	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY [N16000393]	6/2020	1,019.00 -	1,019.00	132.46	01/2023 -	01/2023
135	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	2,089.45	04/2023 -	04/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	30.12	07/2021 03/2022	03/2022
137	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	504.26	01/2021 03/2022	03/2022
138	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	130.22	02/2028 -	02/2028
139	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	40.12	12/2029 -	12/2029
140	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]	6/2019	2,996.00 -	2,996.00	309.12	02/2028 -	02/2028
141	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]	6/2019	347.00 -	347.00	105.90	02/2028 -	02/2028
142	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	26.31	12/2029 -	12/2029
143	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]	6/2019	439.00 -	439.00	127.63	02/2028 -	02/2028
144	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	45.10	12/2029 -	12/2029
145	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	142.62	10/2021 03/2022	03/2022
146	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	954.75	08/2020 04/2022	04/2022
147	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	3,566.10	10/2021 07/2022	07/2022
148	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	516.61	08/2022 -	08/2022
149	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	90.83	10/2020 08/2022	08/2022
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
150	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	304.00	2.58	06/2023 01/2024	01/2024
	<u>Numaligarh Refinery Limited</u>						
151	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	18,968.00	767.97	10/2024 -	10/2024
152	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	959.30	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
153	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	2,001.34	1,604.42	05/2013 05/2022	05/2022
154	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON [N16000433]	8/2021	218.38 -	218.38	-	02/2023 -	02/2023
155	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]	8/2021	885.63 -	885.63	183.01	02/2026 -	02/2026
156	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	227.33	03/2025 -	03/2025
157	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	141.98	08/2022 -	08/2022
158	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,800.96	03/2022 -	03/2022
159	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	947.93	03/2026 -	03/2026
160	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	25,090.00	15,071.32	06/2020 06/2022	06/2022
161	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	2,222.54	05/2021 12/2021	12/2021
162	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	3,119.98	05/2021 01/2022	01/2022
163	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	1,640.35	03/2022 05/2023	05/2023
164	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,375.90	2,888.99	04/2018 05/2022	05/2022
165	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	773.03	03/2023 03/2022	03/2022
	Total		2,68,861.29 -	2,76,653.21	86,144.32		
	<u>POWER</u>						
	<u>Chenab Valley Power Projects [P] Limited</u>						
166	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	2,056.81	04/2020 07/2025	07/2025
	<u>National Hydro-Electric Power Corporation</u>						
167	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	9,897.59	9,357.83	09/2009 03/2023	03/2023
168	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	19,992.43	14,738.05	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
169	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,803.00	743.00	09/2019 12/2024	12/2024
170	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	19,466.00	10/2011 07/2023	07/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
171	DEVIKOT SOLAR 150MW - [N18000281]	1/2020	798.24 -	852.90	541.97	09/2021 08/2022	08/2022
172	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	293.03	130.88	10/2021 10/2022	10/2022
173	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]	3/2020	1,782.00 -	1,782.00	836.25	09/2021 10/2022	10/2022
174	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	888.48	09/2021 08/2022	08/2022
175	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]	5/2021	674.92 -	674.92	76.91	09/2022 -	09/2022
176	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	1,339.51	09/2021 10/2022	10/2022
177	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71 -	1,522.71	1,009.07	09/2021 08/2022	08/2022
178	NOKHRA - [N18000282]	3/2020	1,722.14 -	1,803.19	552.18	09/2021 10/2022	10/2022
179	DEVIKOT SOLAR 90MW - [N18000280]	3/2020	501.29 -	524.83	368.49	09/2021 10/2022	10/2022
	<u>Power Grid Corporation Of India Limited</u>						
180	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]	2/2017	322.30 -	322.30	205.25	02/2019 04/2022	04/2022
181	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,911.97	12/2018 03/2024	03/2024
	<u>Satluj Jal Vidyut Nigam Limited</u>						
182	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	4,611.25	01/2024 -	01/2024
183	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	785.06	12/2021 06/2022	06/2022
184	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	313.58 -	313.58	112.91	12/2022 -	12/2022
185	SHIYAL SOLAR POWER PROJECT - [N18000297]	5/2021	296.20 -	296.20	.21	10/2022 -	10/2022
186	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	207.51	11/2025 -	11/2025
187	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	585.06	01/2026 -	01/2026
	<u>Thdc India Limited</u>						
188	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,860.35	2,356.86	06/2013 12/2024	12/2024
189	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	648.84	09/2020 08/2022	08/2022
	Total		62,588.72 -	1,01,030.78	64,530.35		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
190	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023
191	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
192	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023
193	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
	<u>East Central Railways</u>						
194	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,650.00	3,661.29	- 03/2022	03/2022
195	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	4/1997	324.73 -	1,080.00	1,086.41	03/2012 11/2022	11/2022
196	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,370.20	- 03/2022	03/2022
197	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	4/2016	731.64 -	1,185.73	424.08	03/2021 03/2024	03/2024
198	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	4/2016	744.04 -	1,215.54	543.61	03/2021 03/2024	03/2024
199	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE [N22000350]	12/2015	1,491.47 -	1,491.47	572.94	03/2020 03/2023	03/2023
200	ARARIA-SUPAUL (NL) - [N22000177]	4/2008	1,605.17 -	1,605.17	153.43	- 03/2023	03/2023
201	KODERMA-TILAIYA (NL), ECR - [220100305]	4/2002	459.91 -	1,625.87	941.70	- 03/2023	03/2023
202	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	958.41	03/2019 12/2021	12/2021
203	HAJIPUR-SAGauli VIA VAISHALI (NL), ECR - [220100303]	4/2003	528.65 -	2,066.78	1,597.10	- 03/2023	03/2023
	<u>East Coast Railway</u>						
204	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	4/2005	810.78 -	1,928.07	933.16	06/2021 03/2025	03/2025
205	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	3/2013	843.04 -	843.04	284.93	10/2020 03/2024	03/2024
206	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	2,923.13 -	3,791.66	1,687.63	03/2009 12/2024	12/2024
207	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	718.37	12/2018 03/2024	03/2024
208	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	524.03	03/2022 03/2026	03/2026
209	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	710.98	03/2022 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
210	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	1,012.35	03/2020 03/2023	03/2023
	<u>Metropolitan Rapid Transport Projects</u>						
211	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	2,980.41	1,868.04	03/2004 06/2022	06/2022
212	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	774.51	492.88	06/2013 07/2022	07/2022
	<u>North Central Railway</u>						
213	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	471.73	03/2022 12/2024	12/2024
214	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	1,046.53	03/2021 06/2023	06/2023
	<u>North East Frontier Railway</u>						
215	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	14,322.00	12,012.77	03/2011 12/2023	12/2023
216	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	8,600.00	1,856.78	12/2015 12/2023	12/2023
217	AGARTALA-AKHAURA NL - [N22000195]	4/2012	569.63 -	742.00	612.37	03/2020 06/2022	06/2022
	<u>North Eastern Railway</u>						
218	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
219	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,465.45	03/2022 -	03/2022
220	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	116.44	12/2021 -	12/2021
	<u>Northern Railway</u>						
221	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.13	243.28	03/2023 12/2025	12/2025
	<u>National High Speed Rail Corporation Limited</u>						
222	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	18,841.98	12/2023 -	12/2023
	<u>Rail Vikas Nigam Ltd.</u>						
223	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,650.00	1,737.74	12/2021 -	12/2021
224	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,515.82	12/2023 -	12/2023
225	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	2,364.27	12/2023 -	12/2023
226	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	949.03	12/2024 -	12/2024
	<u>South East Central Railway</u>						
227	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	3,176.60	1,492.13	03/2023 12/2023	12/2023
228	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.94	838.56	12/2021 12/2023	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
229	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	4/2015	1,973.00 -	2,135.34	733.21	03/2021 12/2023	12/2023
230	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438	4/2010	585.93 -	1,268.32	1,123.85	02/2019 12/2021	12/2021
231	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	6/2018	229.00 -	1,096.00	40.47	12/2021 12/2024	12/2024
	<u>South Western Railway</u>						
232	ARSIKERE-TUMKUR - [N22000332	3/2015	578.00 -	760.00	647.09	03/2020 01/2022	01/2022
	<u>West Central Railway</u>						
233	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,411.38	03/2021 03/2024	03/2024
	<u>Western Railway</u>						
234	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	4/2008	318.24 -	321.62	126.35	03/2012 10/2023	10/2023
235	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	2,223.37	1,966.82	03/2020 03/2024	03/2024
236	CHOTTAUDEPUR-DHAR(NL) - [N22000138	4/2007	1,347.26 -	1,524.68	1,004.89	03/2022 03/2023	03/2023
237	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH- KODINAR (GC) - [N22000143	4/1994	320.66 -	1,378.11	558.66	03/2019 03/2023	03/2023
238	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505	4/2018	537.31 -	537.31	.64	03/2024 03/2024	03/2024
239	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504	4/2017	692.25 -	742.88	.89	03/2020 03/2024	03/2024
240	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493	4/2016	700.00 -	603.69	350.17	06/2020 03/2023	03/2023
241	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	4/2007	1,640.04 -	1,640.04	882.29	03/2022 03/2025	03/2025
	Total		1,80,676.80 -	2,27,145.64	78,316.67		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
242	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281	12/2015	291.05 -	291.05	241.71	- 01/2022	01/2022
243	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	346.72	05/2017 05/2022	05/2022
244	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	319.96	193.56	03/2016 04/2022	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
245	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	207.83	06/2019 12/2021	12/2021
246	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021
247	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	6/2016	236.78 -	263.26	78.47	08/2019 08/2022	08/2022
248	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421	7/2018	1,948.25 -	1,948.25	277.20	02/2024 -	02/2024
249	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408	2/2021	925.47 -	925.47	-	07/2025 -	07/2025
250	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373	1/2020	358.26 -	358.26	52	02/2024 -	02/2024
251	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372	2/2021	588.09 -	588.09	93.72	03/2024 -	03/2024
252	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	236.18	59.74	12/2022 -	12/2022
253	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229	12/2014	379.16 -	379.16	333.56	11/2017 01/2022	01/2022
254	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228	11/2017	188.80 -	188.80	113.05	05/2019 03/2022	03/2022
255	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226	12/2014	496.02 -	496.02	251.27	03/2015 03/2022	03/2022
256	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224	3/2017	423.79 -	423.79	298.63	01/2018 01/2022	01/2022
257	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTALGAON TO KUNKURI - [N24001222	3/2016	452.94 -	435.61	117.77	07/2016 12/2022	12/2022
258	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	1/2016	624.98 -	731.50	476.86	10/2016 06/2022	06/2022
259	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	1/2016	476.20 544.00	544.00	400.87	09/2016 03/2022	03/2022
260	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218	11/2015	335.32 -	335.32	282.86	06/2017 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
261	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	1/2016	497.14 -	572.66	284.86	08/2016 06/2022	06/2022
262	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	552.31	12/2019 02/2022	02/2022
263	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]	11/2017	254.17 -	254.17	187.73	02/2018 03/2022	03/2022
264	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]	2/2018	426.18 -	426.18	254.43	09/2020 01/2022	01/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
265	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 - [N24000744]	3/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022
266	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	33.21	07/2022 -	07/2022
267	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	27.90	10/2022 -	10/2022
268	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
269	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
270	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	8.67	04/2022 -	04/2022
271	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	25.27	08/2022 -	08/2022
272	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]	3/2020	167.95 -	167.95	30.07	06/2022 -	06/2022
273	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]	6/2020	365.53 -	365.53	53.11	08/2022 -	08/2022
274	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]	3/2020	292.24 -	292.24	39.42	06/2022 -	06/2022
275	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023
276	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	288.84	12/2023 -	12/2023
277	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	171.37	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
278	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]	3/2020	167.95 -	167.95	50.50	06/2022 -	06/2022
279	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]	11/2020	206.78 -	206.78	65.92	07/2022 -	07/2022
280	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]	11/2020	280.91 -	280.91	90.44	07/2022 -	07/2022
281	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022
282	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]	11/2020	332.14 -	332.14	10.88	07/2022 -	07/2022
283	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]	4/2020	330.80 -	330.80	49.90	12/2021 -	12/2021
284	PEREN-DIMAPUR PKG-5 - [N24001407]	2/2021	207.33 -	207.33	-	03/2023 -	03/2023
285	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]	7/2021	258.52 -	258.52	20.00	03/2023 -	03/2023
286	CHURACHANDPUR TUIVAI PKG-3 - [N24001405]	7/2021	673.27 -	673.27	-	10/2023 -	10/2023
287	TAMENGLONG - MAHUR PKG-4 - [N24001404]	7/2021	198.77 -	198.77	-	03/2023 -	03/2023
288	TAMENGLONG - MAHUR PKG-2 - [N24001403]	7/2021	483.87 -	483.87	12.11	03/2023 -	03/2023
289	TAMENGLONG - MAHUR PKG-1 - [N24001402]	7/2021	185.80 -	185.80	-	03/2023 -	03/2023
290	IMPHAL - KHONGSANG PKG-3 - [N24001401]	7/2021	467.00 -	467.00	-	03/2023 -	03/2023
291	SENAPATI- IMPHAL PKG-5B - [N24001400]	3/2021	211.70 -	211.70	-	01/2023 -	01/2023
292	IMPHAL - MOREH (PACKAGE 4) - [N24001399]	3/2021	277.99 -	277.99	-	01/2023 -	01/2023
293	MARIAM - PEREN (PKG 2A) - [N24001398]	7/2021	204.58 -	204.58	-	03/2023 -	03/2023
294	GOHA-KHELLANI PKG-3 - [N24001397]	2/2021	431.28 -	431.28	24.77	03/2023 -	03/2023
295	KHELLANI-KHANABAL PKG-5 - [N24001396]	7/2021	497.09 -	497.09	5.78	02/2023 -	02/2023
296	KHELLANI-KHANABAL PKG-4 - [N24001395]	7/2021	859.67 -	859.67	-	08/2023 -	08/2023
297	KHELLANI-KHANABAL PKG-2 - [N24001394]	7/2021	512.43 -	512.43	3.87	02/2023 -	02/2023
298	JORAM - KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]	8/2020	184.88 -	184.88	40.92	04/2022 -	04/2022
299	JORAM - KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]	8/2020	199.03 -	199.03	58.18	04/2022 -	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
300	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]	8/2020	294.04 -	294.04	79.46	04/2022 -	04/2022
301	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390]	8/2020	228.71 -	228.71	40.08	04/2022 -	04/2022
302	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]	3/2020	206.53 -	206.53	81.84	06/2022 -	06/2022
303	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
304	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]	3/2021	636.42 -	636.42	-	12/2022 -	12/2022
305	DABOKA KATHKATI PACKAGE-5 - [N24001366]	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
306	DABOKA KATHKATI PACKAGE-4 - [N24001365]	2/2021	260.07 -	260.07	34.33	12/2023 -	12/2023
307	DABOKA KATHKATI PACKAGE-2 - [N24001364]	3/2021	335.88 -	335.88	16.63	01/2024 -	01/2024
308	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	10.23	12/2022 -	12/2022
309	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
310	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
311	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]	3/2021	260.21 -	260.21	42.62	12/2022 -	12/2022
312	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
313	TLABUNG - LUNGLEI PKG-A - [N24001358]	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
314	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	34.80	06/2023 -	06/2023
315	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	12.72	12/2022 -	12/2022
316	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	43.01	12/2022 -	12/2022
317	TAMENGLONG - MAHUR PKG-3 - [N24001354]	3/2021	234.08 -	234.08	9.86	12/2022 -	12/2022
318	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
319	IMPHAL – MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	35.84	12/2022 -	12/2022
320	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	-	12/2022 -	12/2022
321	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	-	12/2022 -	12/2022
322	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	-	12/2022 -	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
323	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	9.04	01/2023 -	01/2023
324	KARGIL-ZANSKR PACKAGE-7 - [N24001347]	1/2021	308.86 -	308.86	38.81	06/2024 -	06/2024
325	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	36.62	05/2024 -	05/2024
326	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	8.23	01/2023 -	01/2023
327	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	1.98	01/2023 -	01/2023
328	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	10.11	01/2023 -	01/2023
329	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
330	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	4.68	12/2022 -	12/2022
331	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) [N24001339]	10/2020	157.86 -	157.86	55.86	04/2022 -	04/2022
332	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
333	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]	10/2020	493.42 -	493.42	-	11/2023 -	11/2023
334	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]	8/2020	230.45 -	230.45	2.58	04/2023 -	04/2023
335	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]	11/2020	284.21 -	284.21	40.21	12/2023 -	12/2023
336	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]	11/2020	445.51 -	445.51	173.17	12/2023 -	12/2023
337	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]	9/2019	761.54 -	761.54	140.46	05/2023 -	05/2023
338	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022
339	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]	3/2020	261.13 -	261.13	23.56	06/2022 -	06/2022
340	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	48.49	12/2023 -	12/2023
341	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]	3/2020	165.54 -	165.54	8.23	07/2022 -	07/2022
342	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]	12/2020	804.00 -	804.00	46.60	08/2023 -	08/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
343	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327	8/2020	292.80 -	292.80	42.83	05/2022 -	05/2022
344	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326	11/2020	4,997.04 -	4,997.04	557.28	09/2028 -	09/2028
345	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325	9/2020	262.84 -	262.84	120.72	05/2023 -	05/2023
346	KHELLANI-KHANABAL PKG-6 - [N24001324	2/2021	285.28 -	285.28	22.14	09/2022 -	09/2022
347	KHELLANI-KHANABAL PKG-1 - [N24001323	3/2021	486.45 -	486.45	68.38	09/2022 -	09/2022
348	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322	9/2020	183.31 -	183.31	76.84	05/2022 -	05/2022
349	DEMBUEN - BRUNI - [N24001321	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
350	DOGINALA - GAU - [N24001320	12/2020	242.30 -	242.30	-	09/2022 -	09/2022
351	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319	6/2020	257.96 -	257.96	95.22	01/2022 -	01/2022
352	2-LANING OF KHOWAI - AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318	9/2020	173.17 -	173.17	9.33	04/2022 -	04/2022
353	2-LANING FROM JOLAIBARI - BELONIA - [N24001317	6/2020	201.99 -	201.99	18.87	01/2022 -	01/2022
354	LADDA - BASAI - [N24001316	2/2021	445.96 -	445.96	-	04/2023 -	04/2023
355	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285	3/2020	330.78 -	330.78	67.50	12/2021 -	12/2021
356	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	79.89	06/2022 -	06/2022
357	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284	3/2020	361.53 -	361.53	38.95	06/2022 -	06/2022
358	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283	3/2020	281.78 -	281.78	120.63	07/2022 -	07/2022
359	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282	3/2020	355.79 -	355.79	70.73	06/2022 -	06/2022
360	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281	3/2020	292.24 -	292.24	59.29	07/2022 -	07/2022
361	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280	3/2020	320.97 -	320.97	56.39	06/2022 -	06/2022
362	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279	3/2020	216.49 -	216.49	59.06	07/2022 -	07/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
363	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	42.19	03/2022 -	03/2022
364	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	167.94	07/2022 -	07/2022
365	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	17.99	07/2022 -	07/2022
366	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	20.18	04/2022 -	04/2022
367	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265	3/2020	154.51 -	154.51	42.33	07/2022 -	07/2022
368	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264	7/2020	228.39 -	228.39	23.72	04/2022 -	04/2022
369	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263	6/2020	277.50 -	277.50	106.99	01/2022 -	01/2022
370	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	32.85	04/2023 -	04/2023
371	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251	3/2019	402.94 -	402.94	69.72	04/2022 -	04/2022
372	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	62.66	03/2022 -	03/2022
373	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249	6/2020	347.36 -	347.36	89.80	01/2022 -	01/2022
374	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248	8/2020	208.84 -	208.84	20.73	04/2022 -	04/2022
375	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247	3/2020	247.76 -	247.76	27.82	01/2022 -	01/2022
376	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	37.93	12/2022 -	12/2022
377	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245	9/2020	353.90 -	353.90	26.00	05/2022 -	05/2022
378	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244	8/2020	301.06 -	301.06	25.63	04/2022 -	04/2022
379	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262	7/2020	345.38 -	345.38	86.64	04/2023 -	04/2023
380	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261	8/2020	311.00 -	311.00	26.51	04/2023 -	04/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
381	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260	9/2020	257.15 -	257.15	52.44	04/2022 -	04/2022
382	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	9/2020	315.63 -	315.63	9.39	04/2022 -	04/2022
383	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	7.02	04/2022 -	04/2022
384	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	33.95	10/2022 -	10/2022
385	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	369.00	09/2026 -	09/2026
386	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	59.98	06/2022 -	06/2022
387	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023
388	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	90.39	09/2019 09/2023	09/2023
389	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972	2/2017	175.06 -	175.06	94.23	- 04/2022	04/2022
390	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973	2/2017	176.12 -	176.12	84.29	- 04/2022	04/2022
391	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	128.15	09/2019 04/2023	04/2023
National Highways Authority Of India							
392	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	706.78	05/2018 03/2022	03/2022
393	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564	3/2016	1,408.00 -	827.05	387.83	- 07/2022	07/2022
394	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	1,322.40	03/2020 12/2021	12/2021
395	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566	4/2016	804.97 -	804.97	599.30	06/2018 12/2021	12/2021
396	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
397	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
398	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
399	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
400	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI - [N24001416	12/2020	989.66 -	989.66	-	01/2024 -	01/2024
401	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
402	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 -	01/2024
403	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
404	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
405	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	717.24	627.25	05/2018 06/2022	06/2022
	Total		81,515.78 -	81,730.11	15,427.02		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
406	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,967.38	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,967.38		
	<u>SOCIAL JUSTICE</u>						
	<u>Central Public Works Department</u>						
407	CENTRE FOR DISABILITY SPORTS - [N38000001	2/2019	170.99 -	170.99	34.00	03/2024 -	03/2024
	Total		170.99 -	170.99	34.00		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
408	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]	11/2015	2,907.00 -	2,907.00	547.05	06/2023 -	06/2023
	<u>Steel Authority Of India Limited (Sail)</u>						
409	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	377.18 -	377.18	51.69	05/2023 -	05/2023
410	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]	11/2020	542.24 -	542.24	81.14	12/2023 -	12/2023
	Total		3,826.42 -	3,826.42	679.88		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
411	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	419.43	03/2024 -	03/2024
412	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	373.31	03/2024 -	03/2024
	<u>Bangalore Metro Rail Corporation Limited</u>						
413	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	30,695.12	19,410.15	02/2019 03/2025	03/2025
414	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151]	6/2021	14,788.10 -	14,788.10	2,031.41	06/2026 -	06/2026
	<u>Central Public Works Department</u>						
415	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33 -	217.00	187.08	04/2019 02/2022	02/2022
416	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]	10/2016	422.00 -	422.00	135.75	03/2021 06/2023	06/2023
417	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]	10/2016	392.00 -	392.00	196.68	08/2020 06/2022	06/2022
418	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]	10/2016	1,180.00 -	1,100.80	35.90	07/2021 06/2023	06/2023
419	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	208.57	05/2020 01/2022	01/2022
420	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE VI-5 SHOPS COMMUNI - [N28000149]	5/2019	299.97 -	299.97	27.44	09/2020 01/2023	01/2023
	<u>Delhi Metro Rail Corporation</u>						
421	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS [N28000135]	7/2019	24,948.65 -	24,948.65	2,711.33	03/2025 -	03/2025
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
422	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	7,565.74	11/2021 12/2022	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Mumbai Metro Rail Corporation Ltd</u>						
423	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	7/2013	23,136.00 -	33,406.00	20,051.98	03/2020 03/2023	03/2023
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
424	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	354.67	02/2023 -	02/2023
425	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	190.69	02/2023 -	02/2023
	<u>Nagpur Metro Rail Corporation Ltd</u>						
426	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	8,443.80	03/2018 12/2021	12/2021
	<u>National Capital Region Transport Corp</u>						
427	DELHI-GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	6,074.70	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
428	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,925.50	306.94	06/2024 -	06/2024
	Total		1,87,594.21 -	2,02,654.39	68,725.57		
	<u>WATER RESOURCES</u>						
	<u>Delhi Jal Board</u>						
429	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	251.88	12/2022 -	12/2022
	Total		665.78 -	665.78	251.88		
	Grand Total		9,54,997.11	10,62,290.02	3,59,342.07		

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 3,492.00	6,840.00	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	12/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 - 12,320.00	17,079.00	12/2016 -	12/2023	38.63
	Total		27,271.00 - 27,271.00	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	06/2023	38.72
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2023	7.88
	Total		1,488.27 - 1,488.27	1,712.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>						
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 - 479.53	808.97	03/2013 -	03/2024	68.70
	<u>Neyveli Lignite Corporation</u>						
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	11/2022	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Singareni Colliers Company Limited</u>						
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86
10	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2022	11.42
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 - 447.06	473.22	03/2015 -	03/2023	5.85
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2022	114.60
	<u>Western Coal Fields Limited</u>						
13	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 - 289.29	289.30	03/2022 -	03/2025	.00
	Total		22,093.43 .00 22,093.43	25,237.09			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
14	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00 496.00	498.99	06/2017 -	03/2022	.60
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 - 549.31	559.47	07/2019 -	-	1.85
16	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00 199.00	205.00	09/2020 -	-	3.02
	Total		1,231.49 695.00 1,244.31	1,263.46			
	<u>DPIIT</u>						
	<u>Dmic For Dpiit</u>						
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	07/2021	9.80
	<u>Iicc For Dpiit</u>						
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	05/2022	8.49

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		17,352.09 17,352.09	18,990.30			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 1,577.00	1,828.00	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>						
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 414.11	586.50	11/2013 -	09/2021	41.63
21	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 204.44	250.00	05/2017 -	03/2021	22.29
22	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 293.65	325.00	05/2017 -	01/2020	10.68
23	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 168.90	191.20	05/2017 -	07/2019	13.20
24	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 505.58	585.00	03/2018 -	09/2019	15.71
25	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 152.95	177.92	02/2018 -	03/2021	16.33
26	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 244.00	248.00	09/2018 -	05/2019	1.64
27	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 272.19	272.54	03/2019 -	03/2021	.13
28	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 156.56	190.34	- -	12/2021	21.58
29	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 249.01	249.07	- -	01/2021	.02
	<u>Nbcc For Health</u>						
30	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 1,351.00	1,471.00	09/2021 -	06/2022	8.88
	Total		5,589.39 5,589.39	6,374.57			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	05/2022	64.04
	Total		1,219.21 .00 1,219.21	2,000.00			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
32	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 - 2,677.00	3,072.00	06/2021 -	07/2022	14.76
	<u>Oil & Natural Gas Corporation Limited</u>						
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128	03/2011	861.79 - 1,846.46	2,001.34	05/2013 -	05/2022	132.23
	Total		3,538.79 .00 4,523.46	5,073.34			
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
34	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 - 14,366.58	17,007.00	06/2019 -	09/2023	18.38
35	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 - 1,381.84	1,803.00	09/2019 -	12/2024	30.48
36	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
37	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	01/2016	10,598.98 - 10,997.70	10,998.00	11/2020 -	10/2022	3.76
38	PAKRI BARWADIH COAL MINING PROJECT - [N18000225	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
39	DEVIKOT SOLAR 90MW - [N18000280	03/2020	501.29 - 501.29	524.83	09/2021 -	10/2022	4.70

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
40	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 - 798.24	852.90	09/2021 -	08/2022	6.85
41	NOKHRA - [N18000282]	03/2020	1,722.14 - 1,722.14	1,803.19	09/2021 -	10/2022	4.71
42	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 - 261.80	293.03	10/2021 -	10/2022	11.93
43	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	06/2019	401.90 - 401.90	442.03	04/2021 -	01/2022	9.99
	<u>Power Grid Corporation Of India Limited</u>						
44	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	02/2022	14.11
	<u>Satluj Jal Vidyut Nigam Limited</u>						
45	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 - 648.33	947.89	12/2021 -	06/2022	46.20
	Total		39,946.06 7,738.00 40,344.82	45,018.94			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
46	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 - 3,168.29	3,445.48	03/2023 -	03/2023	8.75
47	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	1,387.52	03/2021 -	03/2023	75.00
48	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 - 184.06	325.00	03/2019 -	-	76.57
49	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,794.60	03/2021 -	03/2023	111.08
50	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 - 2,425.00	5,341.68	03/2024 -	03/2024	120.28
51	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 - 2,750.00	3,438.49	03/2024 -	-	25.04
52	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,283.49	03/2022 -	03/2023	.89

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
54	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
55	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 - 387.70	487.13	03/2018 -	-	25.65
56	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	-	.21
	<u>East Central Railways</u>						
57	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,038.07 - 3,020.95	3,650.00	- -	03/2022	253.32
58	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 - 898.53	1,080.00	03/2012 -	11/2022	232.58
59	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 - 380.00	519.33	- -	03/2025	36.67
60	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 - 678.54	929.86	03/2019 -	12/2021	37.04
61	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 - 415.67	549.75	- -	-	32.26
62	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 - 326.20	2,995.01	- -	03/2024	818.15
63	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 - 378.56	1,858.75	- -	03/2023	391.01
64	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 - 211.00	1,006.00	- -	-	376.78
65	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 - 548.00	819.01	03/2020 -	12/2024	49.45
66	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 - 332.15	560.09	07/2014 -	-	68.63
67	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23 - 348.23	390.00	03/2021 -	03/2022	11.99

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
68	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 - 803.11	1,483.14	- -	03/2022	350.27
	<u>East Coast Railway</u>						
69	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 - 1,111.99	1,539.28	02/2019 -	03/2022	38.43
70	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2024	15.45
	<u>Eastern Railways</u>						
71	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
72	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
73	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 - 365.17	439.30	03/2017 -	03/2025	20.30
74	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46
75	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 - 175.80	495.10	- -	03/2022	181.63
76	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
77	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01
78	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25
79	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 - 499.96	680.68	02/2012 -	03/2025	36.15
80	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
81	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
82	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
83	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30
84	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
85	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
86	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 - 288.35	502.48	- -	03/2021	74.26
87	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
88	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225]	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
89	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	09/2023	117.23
90	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	06/2022	.00
<u>Metropolitan Rapid Transport Projects</u>							
91	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37
92	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 - 495.44	2,980.41	03/2004 -	06/2022	501.57
93	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	774.51	06/2013 -	07/2022	56.23
94	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	-	75.91
<u>North Central Railway</u>							
95	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
96	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00 668.00	680.00	03/2020 -	01/2022	1.80
<u>North East Frontier Railway</u>							

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
97	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 - 200.34	614.00	03/2019 -	-	106.51
98	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 5,021.45	6,527.00	03/2014 -	12/2023	172.70
99	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 - 2,531.34	4,541.38	12/2008 -	12/2021	284.80
100	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 12,264.00	14,322.00	03/2011 -	12/2023	221.54
101	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,043.00	03/2019 -	03/2023	170.77
102	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 - 2,132.03	2,145.00	03/2019 -	03/2024	302.54
103	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 - 2,326.52	6,663.00	03/2015 -	03/2026	186.39
104	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 - 333.76	360.00	- -	-	7.86
105	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 4,084.69	8,600.00	12/2015 -	12/2023	542.04
106	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 - 221.42	380.00	- -	-	71.62
107	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 90.00	742.00	03/2020 -	06/2022	30.26
108	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	4,083.02	03/2021 -	-	350.44
109	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
110	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	373.87	- -	06/2022	54.80
111	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	750.00	03/2020 -	-	80.79
112	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 - 819.23	1,090.60	- -	-	33.13

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
113	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15
			2,232.32				
114	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	03/2021 -	03/2022	115.07
			870.96				
115	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	1,167.00	12/2021 -	10/2021	93.77
			602.27				
116	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	04/2010 -	-	186.55
			380.60				
<u>North Eastern Railway</u>							
117	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
			142.45				
118	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -		358.99
			307.00				
119	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
			243.78				
120	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	610.00	01/2019 -	02/2022	106.78
			295.00				
121	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
			643.00				
122	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	1,824.00	03/2022 -	03/2022	40.80
			1,295.42				
123	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	12/2021	.16
			213.00				
124	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	04/2017 -	10/2022	127.77
			150.00				
125	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
			1,343.00				
126	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	800.00	- -	12/2023	32.78
			602.50				
<u>North Western Railway</u>							
127	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	06/2022	109.82
			410.08				

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
128	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	10/2022	16.97
129	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 - 873.71	2,215.27	- -	-	153.55
130	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
131	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	420.18 - 420.18	480.00	03/2020 -	09/2021	14.24
	<u>Northern Railway</u>						
132	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	359.00	- -	03/2024	129.17
133	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	06/2021	211.31
134	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 - 336.91	791.39	- -	09/2023	134.90
135	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
136	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
137	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,017.96	07/2012 -	11/2024	348.44
138	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 - 328.14	1,540.13	03/2023 -	12/2025	369.35
139	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 625.00	839.00	03/2016 -	-	34.24
	<u>Rail Vikas Nigam Ltd.</u>						
140	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
141	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	433.00	03/2009 03/2009	-	109.18
142	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,639.00	03/2016 -	03/2025	59.22

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
143	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	12/2025	127.62
144	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,000.00	03/2023 -	12/2022	41.04
145	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,259.48	03/2016 -	03/2025	7.78
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
147	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	3,377.00	03/2020 -	03/2022	124.58
148	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 - 975.62	1,650.00	12/2021 -	12/2021	69.12
149	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 - 644.38	872.65	03/2021 -	12/2021	35.42
150	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 - 1,548.66	1,868.89	12/2021 -	03/2022	20.68
151	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	950.00	03/2016 -	12/2021	50.15
152	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32
153	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,000.00	03/2022 -	12/2024	5.98
154	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 - 773.94	850.00	12/2024 -	12/2024	9.83
155	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,400.00	03/2019 -	06/2022	51.02
156	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	22,716.11	12/2024 -	03/2025	40.08
157	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,900.00	03/2020 -	12/2021	306.46
158	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
159	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	12/2021	111.91
160	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,536.00	03/2019 -	06/2022	62.89
161	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	1,825.00	12/2020 -	12/2022	54.24
162	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	12/2021	23.55
163	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	06/2022	102.11
	<u>Railway Electrification</u>						
164	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -		60.77
	<u>South Central Railway</u>						
165	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2024	102.85
166	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 - 1,160.48	1,373.74	03/2010 -	03/2024	18.38
167	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86
168	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
169	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 - 2,132.77	3,037.95	03/2014 -	03/2027	42.44
170	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
171	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2024	7.06
172	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 176.18	242.28	03/2022 -	-	30.96
	<u>South East Central Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 - 852.50	1,096.00	12/2021 -	12/2024	378.60
	<u>South Eastern Railway</u>						
174	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
175	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
176	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
177	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 - 149.90	266.61	03/2015 -	03/2019	77.86
178	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 - 969.83	1,312.96	03/2020 -	06/2022	35.38
179	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 - 1,027.40	2,373.00	03/2003 -	03/2030	130.97
180	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 - 428.65	472.50	06/2022 -	12/2025	10.23
181	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39 - 390.39	511.75	12/2021 -	06/2022	31.09
182	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 - 338.00	393.83	06/2022 -	06/2023	16.52
	<u>South Western Railway</u>						
183	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 - 1,801.01	2,161.36	- -	12/2023	20.01
184	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 - 986.30	1,530.09	03/2016 -	12/2026	55.13
185	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 - 558.00	692.43	- -	12/2023	24.09
186	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	466.65	- -	12/2023	57.65
187	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,404.03	- -	12/2025	16.57

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
188	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 - 327.25	367.77	- -	12/2023	12.38
189	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	5,174.30	- -	12/2024	123.51
190	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 - 1,382.78	1,383.00	03/2002 -	03/2024	.02
191	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,954.21	03/2020 -	03/2023	68.91
192	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,104.00	03/2020 -	09/2021	28.31
193	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	760.00	03/2020 -	01/2022	31.49
194	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,877.81	1,878.00	03/2019 -	03/2024	16.31
Southern Railway							
195	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 - 724.69	3,081.20	02/2019 -	03/2025	325.17
196	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 - 582.83	3,154.43	- -	12/2025	441.23
197	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,549.09	03/2020 -	03/2025	409.60
198	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
199	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	527.37	02/2019 -	03/2030	247.32
200	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	1,205.00	- -	03/2030	130.17
201	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	839.01	- -	03/2030	.00
202	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 457.08	749.40	- -	03/2022	177.41

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
203	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 369.55	709.69	- -	03/2025	180.55
204	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	603.23	- -	03/2030	109.04
205	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	608.13	- -	02/2022	269.89
206	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	1,122.00	- -	12/2022	20.39
207	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 275.21	448.10	- -	03/2025	136.79
208	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,172.16	03/2019 -	12/2027	1,699.64
209	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,246.00	1,339.00	- -	03/2025	33.90
210	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	991.83	03/2005 -	-	268.89
<u>West Central Railway</u>							
211	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
212	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 - 2,478.23	2,875.12	03/2022 -	06/2023	16.02
<u>Western Railway</u>							
213	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 - 3,503.69	6,171.08	03/2022 -	03/2023	76.13
214	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 - 1,631.75	2,223.37	03/2020 -	03/2024	167.96
215	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 - 859.16	1,378.11	03/2019 -	03/2023	329.77
216	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 - 1,037.15	1,383.69	03/2021 -	12/2022	33.41
217	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 - 1,002.39	1,042.12	03/2021 -	12/2022	3.96

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
218	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504	04/2017	692.25 - 692.25	742.88	03/2020 -	03/2024	7.31
	Total		1,84,953.87 4,842.30 2,04,872.30	3,42,235.05			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
219	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 - 280.16	290.59	- -	-	3.72
220	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW-NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00 348.00	348.43	09/2017 -	-	.12
221	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	05/2017 -	05/2022	45.75
222	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75
223	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67
224	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
225	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	10/2021	.08
226	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	08/2018 -	02/2022	4.45
227	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	12/2015 -	-	6.07
228	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929	09/2016	372.68 -	372.68	02/2017 -	-	.00
229	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	02/2017	429.43 -	429.43	11/2017 -	-	.00
230	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	03/2018	228.32 -	228.32	08/2018 -	-	.00
			202.83				

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
231	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]	03/2018	289.67 290.00 274.73	289.67	08/2018 -	-	-.11
232	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00 995.00	995.09	05/2016 -	-	.01
233	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]	01/2018	418.03 - 381.75	418.03	08/2018 -	-	.00
234	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]	01/2016	386.09 - 316.06	386.09	05/2016 -	-	.00
235	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00 203.00	203.21	05/2019 -	-	.10
236	SHEGAON TO DEORI PHATA - [N24001010]	02/2017	373.10 373.00 373.00	373.10	05/2019 -	-	.03
237	MEHKAR TO CHIKALI - [N24001011]	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15
238	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00 548.00	548.03	06/2019 -	-	.01
239	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00 391.00	391.06	06/2019 -	-	.02
240	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
241	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	-	40.76
242	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00 257.00	257.38	12/2019 -	-	.15
243	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
244	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	-	.05
245	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	-	.08
246	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	-	.24

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
247	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	-	.06
248	WADIGODRI TO DHANGRIPIPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	-	.12
249	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	-	.06
250	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	-	.08
251	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	-	.14
252	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	-	.01
253	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	-	.13
254	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	-	.07
255	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	-	.11
256	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	-	.01
257	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	-	.03
258	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	-	.06
259	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	-	.47
260	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	-	.08
261	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00 356.00	536.65	12/2019 -	02/2022	50.74
262	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	-	.02

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
263	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	-	.16
264	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	-	.08
265	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	-	26.19
266	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	-	2.47
267	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31
268	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	-	.03
269	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01
270	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00
271	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	-	.01
272	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00 215.00	215.16	09/2019 -	10/2019	.07
273	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	03/2021	.13
274	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]	12/2017	297.30 - 297.30	318.28	01/2019 -	-	7.06
275	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	03/2018	325.86 - 325.86	386.41	10/2018 -	-	18.58
276	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 - 186.96	322.24	09/2014 -	-	72.36
277	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 - 1,979.00	2,036.90	- -	-	2.93
278	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]	03/2018	288.30 - 288.30	323.36	08/2020 -	03/2022	12.16

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
279	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 - 281.45	319.96	- -	03/2022	13.68
280	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00 543.73	544.00	09/2016 -	03/2022	.00
281	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239	03/2018	240.38 - 204.73	240.38	06/2019 -	-	.00
282	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 - 197.67	236.18	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
283	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 - 195.23	252.79	04/2017 -	03/2022	29.48
284	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 - 203.36	263.31	04/2017 -	03/2022	29.48
285	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 - 373.07	387.00	08/2016 -	05/2021	3.73
286	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 - 198.22	252.05	04/2017 -	03/2022	27.16
287	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
288	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	09/2020	277.44 - 177.00	277.44	10/2022 -	10/2022	.00
289	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258	08/2020	202.36 - 118.56	202.36	04/2022 -	04/2022	.00
290	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	09/2020	315.63 - 167.23	315.63	04/2022 -	04/2022	.00
	<u>National Highways Authority Of India</u>						
291	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 - 280.00	612.58	02/2009 -	-	118.78
292	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23
293	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
294	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
295	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 - 196.00	655.17	07/2009 -	-	234.27
296	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
297	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
298	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
299	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
300	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 - 511.54	591.00	11/2013 -	-	15.53
301	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	07/2012	291.36 - 291.36	469.31	01/2014 -	-	61.08
302	2-LANING WITH PAVED SHOULDERS OF RAEARELI - BANDA SECTION OF NH-232 - [N24000360	04/2014	351.34 - 351.34	417.68	01/2016 -	-	18.88
303	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEARELI - [N24000367	04/2014	495.78 - 495.78	627.93	01/2016 -	-	26.66
304	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 - 531.13	744.73	05/2018 -	03/2022	40.22
305	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
306	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 - 814.04	825.17	- -	10/2021	1.37
307	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
308	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501	08/2015	322.09 - 247.00	322.09	04/2018 -	-	.00
309	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 - 642.41	681.67	- -	-	6.11

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
310	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	-	1.33
311	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	-	41.78
312	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	-	21.50
313	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	-	25.80
314	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	-	44.60
315	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84
316	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	04/2021	7.53
317	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 - 458.03	486.00	- -	-	6.11
318	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	1,588.29	09/2019 -	-	14.40
319	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 - 1,367.00	2,280.00	- -	-	94.94
320	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 - 323.72	336.60	08/2018 -	-	3.98
321	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 - 1,100.19	1,145.31	- -	-	4.10
322	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 - 290.73	359.60	- -	05/2017	23.69
323	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 - 605.84	722.46	07/2018 -	-	19.25
324	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
325	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 - 744.64	982.00	03/2020 -	-	31.88

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
326	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	-	3.40
327	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 - 988.34	1,043.28	03/2020 -	-	5.56
328	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	-	1.06
329	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	-	5.70
330	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 - 754.54	756.27	03/2020 -	09/2022	.23
331	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 - 672.89	736.01	03/2020 -	-	9.38
332	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
333	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	-	10.24
334	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
335	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54
336	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
337	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 - 894.00	929.32	04/2020 -	03/2022	3.95
338	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	-	1.78
339	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 - 1,124.11	1,300.00	09/2017 -	-	15.65
340	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 - 273.46	276.17	- -	-	.99
341	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
342	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 - 1,166.26	1,296.93	- -	01/2022	11.20
343	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 - 1,995.34	2,400.00	- -	11/2021	20.28
344	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
345	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35
346	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
347	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 - 1,052.21	1,361.00	- -	-	29.35
348	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 - 1,532.62	2,499.00	03/2021 -	07/2021	63.05
349	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 - 496.20	537.17	- -	-	8.26
350	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
351	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 - 1,016.92	1,071.00	- -	01/2022	5.32
352	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96 - 2,065.96	2,169.00	- -	12/2021	4.99
353	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 - 1,294.47	1,296.00	- -	11/2021	.12
354	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 - 634.70	925.96	- -	02/2018	45.89
355	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 - 906.65	922.64	- -	02/2018	15.98
356	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	03/2018	642.13 - 642.13	807.00	- -	-	25.68
357	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]	10/2019	743.88 - 743.88	743.89	- -	12/2021	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
358	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	11/2022	27.86
359	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 - 217.96	884.00	- -	10/2022	305.58
360	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 - 720.81	724.60	03/2023 -	03/2023	.00
361	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 - 731.89	732.34	11/2019 -	-	.06
362	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 - 594.75	606.75	11/2019 -	-	2.02
	Total		95,972.54 17,965.00 95,321.57	1,12,468.39			
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
363	FORGED WHEEL PLANT - [N12000116	04/2014	1,682.85 - 1,682.85	2,100.00	09/2018 -	09/2021	24.79
	Total		1,682.85 .00 1,682.85	2,100.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
364	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 - 10,773.00	12,787.00	12/2018 -	08/2022	18.69
	<u>Mumbai Metro Rail Corporation Ltd</u>						
365	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 - 23,136.00	33,406.00	03/2020 -	03/2023	44.39
	<u>Patna Metro Rail Corporation</u>						
366	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	02/2019	13,365.77 - 13,365.77	13,925.50	06/2024 -	06/2024	4.19
	Total		47,274.77 .00 47,274.77	60,118.50			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(December 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
367	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027	10/2017	254.13 - 254.13	413.29	09/2020 -	03/2024	62.63
368	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 - 225.77	398.90	03/2020 -	02/2022	76.68
	<u>Uttar Pradesh Jal Nigam</u>						
369	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 - 231.79	234.03	12/2021 -	12/2022	.97
370	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	02/2019	681.78 - 681.78	690.71	06/2022 -	04/2024	1.31
	Total		1,393.47 .00 1,393.47	1,736.93			
	Grand Total		4,51,007.23 31,240.30 4,71,670.94	6,64,827.90			

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	12320	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	12/2022	11459	84
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	12/2022	177.1	34
6	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	AAI	01/2018	08/2022	03/2023	1405	7
7	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	AAI	05/2020	05/2022	12/2023	353.61	19
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	06/2019	01/2022	438.28	31
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2023	1142	24
10	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	09/2022	456.86	24
11	UPGRADATION OF JABALPUR AIRPORT	AAI	06/2016	06/2021	12/2022	412.24	18
12	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	AAI	05/2018	10/2022	12/2023	1216.9	14
13	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	04/2022	458	25
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2022	417.23	45
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	06/2024	2467	28
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	AAI	08/2018	10/2021	12/2022	951.28	14
17	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	06/2022	303.8	26
18	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2023	1383	27
19	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	06/2023	346.27	21
20	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	AAI	03/2017	04/2021	08/2022	475.39	16
21	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	04/2023	389.71	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
22	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	10/2022	304.13	67
23	RECAST EPR AMRAPALI OC	CCL	02/2012	03/2020	03/2028	4983.58	96
24	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2025	869.44	48
25	BHATADI EXPANSION OC MINE	WCL	02/2016	03/2019	03/2022	304.52	36
26	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	11/2022	17237	12
27	RPR FOR JAMUNIA UG (0.90 MTY)	WCL	07/2016	03/2022	03/2026	281.25	48
28	RECAST PR FOR DHANKASA UG (1.00 MTY)	WCL	09/2016	03/2022	03/2025	289.29	36
29	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	09/2023	328	30
30	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
31	UKNI DEEP OC	WCL	11/2018	03/2021	09/2022	318.14	18
32	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
33	GARJANBAHAL OCP	MCL	11/2014	03/2021	09/2025	1375.38	54
34	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	WCL	11/2014	03/2020	03/2027	1184.33	84
35	AMRITDHARA OC PROJECT	SECL	02/2015	03/2023	03/2027	481.6	48
36	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
37	RAJNAGAR OCP RPR (1.70 MTY)	SECL	12/2014	03/2021	04/2024	357.8	37
38	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
39	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	03/2022	289.45	94
40	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	03/2022	295.56	36
41	BATURA OCP (2.0 MTY)	SECL	08/2015	03/2023	03/2026	1186.64	36
42	KISTARAM OCP	SCCL	11/2010	03/2015	03/2022	242.29	84
43	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2026	178.44	144
44	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	03/2025	1458.17	117

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
45	MADANNAGAR OPENCAST PROJECT	SECL	10/2015	03/2024	03/2027	1875.32	36
46	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	WCL	11/2015	03/2021	03/2024	313.34	36
47	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	WCL	11/2015	03/2020	03/2026	851.6	72
48	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	BCCL	02/2014	03/2021	03/2023	555.52	24
49	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2029	1055.05	132
50	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2022	397.09	36
51	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
52	BATURA HIGHWALL PROJECT	SECL	07/2015	03/2022	03/2025	231.92	36
53	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
54	DURGAPUR OPENCAST PROJECT	SECL	02/2015	03/2023	03/2026	916.24	36
55	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2022	510.85	72
56	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY)	MCL	12/2007	03/2013	03/2028	8416.19	180
57	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2023	321.5	108
58	BHUBANESWARI EXPENSION OCP(40.0 MTY)	MCL	12/2007	03/2017	03/2031	3145.45	168
59	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	132
60	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY)	MCL	12/2007	03/2010	03/2029	3504.21	228
61	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	04/2023	339.88	108
62	MOONIDIH XV SEAM UG	BCCL	08/2011	03/2019	02/2023	1230.27	47
63	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2023	447.06	96
64	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	84
65	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2022	417.33	68
66	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2022	1783.09	12
67	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
68	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2028	6964.33	188
69	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
70	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2022	163.51	132
71	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2022	162.46	96
72	BELLORA-NAIGAON DEEP OC	WCL	11/2018	03/2021	09/2022	252.71	18
73	PACHWARA SOUTH COAL BLOCK	NLC	07/2013	08/2022	09/2023	1795.01	13
74	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12
75	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
76	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	10/2022	243	54

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
77	RESIDENTIAL QUARTERS FOR HAL, BANGLORE	CPWD FOR DEFEN	12/2016	02/2020	03/2022	246.31	25

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
78	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD EDUCATION	09/2018	09/2020	11/2022	375	26
79	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	CPWD EDUCATION	02/2019	06/2020	11/2022	655.34	29
80	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD EDUCATION	07/2019	03/2021	02/2023	753.63	23
81	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD EDUCATION	07/2019	03/2022	10/2022	851	7
82	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	CPWD EDUCATION	03/2020	06/2020	03/2022	193.83	21
83	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD EDUCATION	02/2016	06/2017	03/2022	496.18	57
84	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	CPWD EDUCATION	01/2018	07/2020	12/2021	223.37	17
85	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD EDUCATION	01/2018	05/2020	06/2022	430	25
86	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	CPWD EDUCATION	09/2019	09/2022	06/2023	588.72	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
87	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	CPWD EDUCATION	05/2019	03/2020	02/2023	303.9	35
88	CONSTRUCTION AND DEVELOPMENT OF NATIONAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	MITES OF HIGH	09/2013	09/2014	06/2022	484.32	93

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
89	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	05/2022	4773	29

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
90	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	01/2022	426.72	21
91	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	NFL	01/2018	11/2019	12/2021	215.92	25

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
92	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD FOR HEALTH	03/2018	09/2020	04/2022	195	19
93	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	06/2022	1351	9
94	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	03/2022	363.99	46
95	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	CPWD FOR HEALTH	09/2017	03/2020	12/2021	150.29	21
96	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD FOR HEALTH	12/2018	06/2021	05/2022	260	11

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
97	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MHA	10/2013	10/2019	05/2022	1219.21	31
98	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	CPWD FOR MHA	01/2020	10/2023	04/2024	166.98	6
99	NSG AT KOLKATA	CPWD FOR MHA	10/2014	04/2018	08/2022	162.88	52

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
100	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	01/2024	5540	33
101	CONVERSION OF FLAT BOTTOM SETTLERS	NALCO	12/2015	11/2020	12/2023	355	37

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	CPWD	04/2019	04/2022	12/2024	255.37	32
103	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	12/2023	483	32

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFI	06/2020	06/2023	01/2024	200	7
105	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	12/2021	224.75	16
106	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	ONGC	02/2019	05/2021	12/2021	2292.46	7
107	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14
108	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	ONGC	05/2019	05/2021	01/2022	3660.71	8
109	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	06/2022	462.3	9
110	Fuel Quality Upgradation Project at Paradip Refinery	IOCL	05/2019	08/2021	09/2022	3361	13
111	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	07/2022	278.6	13
112	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	BPCL	07/2017	02/2021	03/2023	580.2	25
113	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2023	371	6
114	PIPELINE REPLACEMENT PROJECT (PRP-VI)	ONGC	05/2019	12/2020	02/2022	763.92	14
115	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	BPCL	08/2019	08/2022	06/2023	1607	10
116	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2023	2281.94	7
117	PX-PTA REVAMP AT PANIPAT REFINERY	IOCL	08/2019	12/2021	01/2023	1255	13
118	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	01/2022	196.26	18
119	LPG BP PROJECT CHITTOOR	IOCL	07/2019	07/2022	01/2023	167	6
120	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	03/2022	164.69	8
121	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
122	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	03/2022	522	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
123	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	BPCL	10/2018	03/2021	12/2021	206.26	9
124	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	10/2022	225.54	20
125	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
126	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	03/2022	909	14
127	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	02/2022	598	24
128	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	03/2022	286.42	19
129	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	GAIL	08/2018	04/2021	03/2022	217.92	11
130	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	03/2022	255.4	19
131	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	08/2022	199.36	22
132	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	03/2022	906	25
133	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	12/2021	543.91	22
134	BARAUNI-GUWAHATI PIPELINE	GAIL	06/2018	12/2021	06/2023	3308	18
135	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	IOCL	07/2018	01/2021	01/2022	189	12
136	ETHYLENE GLYCOL PROJECT AT PARADIP	IOCL	04/2018	10/2021	07/2022	5654	9
137	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	04/2022	1636	20
138	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	IOCL	08/2018	04/2021	09/2022	466	17
139	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	GAIL	07/2015	12/2020	01/2022	2881.4	13
140	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	03/2022	1933	15
141	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	03/2022	2433	15
142	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	03/2022	3437	15
143	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2023	1740	30
144	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677	13
145	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	07/2022	163.02	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
146	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	12/2021	421	16
147	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	IOCL	08/2017	08/2021	11/2022	318.8	15
148	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	49
149	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	06/2022	160.1	28
150	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	10/2022	161.59	34
151	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	08/2024	2915	140
152	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	12/2021	581	21
153	220 KV GRID SUPPLY	HPCL	10/2020	03/2021	12/2021	303.4	9
154	SULPHUR FORMING UNIT IN SRU	HPCL	10/2020	08/2021	03/2022	210.94	7
155	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	09/2022	607.06	59
156	AUGMENTATION OF PARADIP-HALDIA- DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	03/2022	1823	12
157	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321	15
158	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	03/2022	690	44
159	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2022	861.79	108
160	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	06/2022	327.78	50
161	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
162	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
163	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	06/2022	34012	24
164	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497	38
165	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	03/2022	1810	27
166	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	OIL	05/2016	10/2020	03/2022	406	17
167	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	12/2021	571.66	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
168	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	08/2022	348	19
169	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND	IOCL	08/2017	06/2020	12/2021	236	18
170	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	03/2022	466.43	17
171	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
172	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	03/2022	249.26	21
173	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	03/2022	161.5	21
174	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	03/2022	206.5	12
175	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	29
176	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	BPCL	07/2020	12/2021	06/2022	640	6

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
177	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	03/2022	529.68	40
178	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11
179	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	02/2025	18668	23
180	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	01/2022	1885.13	37
181	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	03/2022	5111.33	39
182	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	01/2022	379.95	25
183	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	04/2022	322.3	38
184	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	141
185	KAYAMKULAM SOLAR 70 MW	NTPC	09/2019	06/2021	07/2022	403.62	13
186	FATEHGARH SOLAR 296MW	NTPC	03/2020	09/2021	10/2022	1749.31	13
187	ETTAYAPURAM SOLAR 230MW	NTPC	03/2020	09/2021	08/2022	1316.22	11
188	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	03/2022	12964.6	46
189	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	162

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
190	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
191	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	05/2023	11130.19	117
192	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2021	374.63	68
193	EASTERN REGION STRENGTHENING SCHEME- XII	PGCIL	05/2014	11/2016	02/2022	522.29	63
194	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	09/2024	2978.48	138
195	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
196	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2023	14366.58	51
197	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	63
198	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITION)	PGCIL	03/2015	03/2018	03/2022	197.4	48
199	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	04/2022	1394.52	59
200	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2024	2491.58	138
201	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657	88
202	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
203	EASTERN REGION STRENGTHENING SCHEME- XVIII	PGCIL	03/2017	07/2020	02/2022	3500	19
204	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	03/2022	186.17	32
205	DEVIKOT SOLAR 90MW	NTPC	03/2020	09/2021	10/2022	501.29	13
206	DEVIKOT SOLAR 150MW	NTPC	01/2020	09/2021	08/2022	798.24	11
207	NOKHRA	NTPC	03/2020	09/2021	10/2022	1722.14	13
208	KAWAS SOLAR 56 MW	NTPC	08/2020	10/2021	10/2022	261.8	12
209	RAMAGUNDAM FLOATING SOLAR 100 MW	NTPC	06/2019	04/2021	01/2022	401.9	9
210	SAMBHU KI BHURJ SOLAR 250 MW	NTPC	01/2020	09/2021	08/2022	1522.71	11
211	SAMBHU KI BHURJ-II SOLAR 300MW	NTPC	03/2020	09/2021	10/2022	1782	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
212	JETSAR SOLAR 160 MW	NTPC	12/2019	03/2021	01/2022	702.28	10
213	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10/2022	10598.98	23
214	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	02/2022	235.53	32
215	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	63
216	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	6
217	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	01/2022	358.83	20

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
218	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	SER	04/2018	06/2022	06/2023	338	12
219	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	06/2022	390.39	6
220	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM)	SER	04/2018	06/2022	12/2025	428.65	42
221	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
222	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
223	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
224	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2025	644.78	96
225	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288	18
226	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	06/2022	3055	45
227	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
228	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	NCR	03/2018	03/2023	06/2025	4329.53	27
229	JHANSI BINA DOUBLING	NCR	09/2016	03/2021	06/2023	2001	27
230	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2021	1402.02	21
231	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
232	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
233	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
234	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2023	2478.23	15
235	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	12/2023	582.13	21
236	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
237	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2022	528.57	36
238	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	06/2022	760	27
239	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2026	2499.71	48
240	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
241	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	64
242	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63
243	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
244	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	12
245	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
246	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
247	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	06/2022	969.83	27
248	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	06/2022	569.63	27
249	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	69
250	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
251	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
252	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
253	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
254	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
255	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36
256	RAMPUR DUMRA - TAL - RAJENDRAPUL	ECR	12/2015	03/2020	03/2023	1491.47	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DOUBLING INCLUDING GANGA BRIDGE						
257	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.2	180
258	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
259	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
260	RAMGANJMUUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2024	424.6	36
261	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
262	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
263	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
264	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	117
265	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	168
266	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
267	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
268	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
269	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
270	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
271	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
272	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
273	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
274	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
275	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
276	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.3	129
277	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
278	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
279	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	02/2022	704.31	23
280	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	156
281	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
282	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
283	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
284	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	06/2022	495.44	219
285	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
286	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	128
287	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	12/2021	1180.19	156
288	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2024	2923.13	189
289	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
290	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	07/2022	495.74	109
291	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.2	48
292	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
293	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	132
294	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	96
295	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	40
296	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450	148
297	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500	241
298	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
299	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
300	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
301	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
302	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60
303	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	10/2023	318.24	139
304	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	48
305	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
306	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
307	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
308	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
309	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2022	155.81	24
310	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	36
311	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600	31
312	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	01/2022	578	22
313	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	60
314	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	12/2021	678.54	33
315	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
316	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	12
317	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2025	1640.04	36
318	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	12/2021	644.38	9
319	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	48
320	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	21
321	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
322	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
323	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	12/2024	548	57
324	NEW BONGAIGAON-RANGIA-KAMAKGHYA	NFR	04/2013	03/2019	12/2023	1798	57

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DOUBLING						
325	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	03/2030	151.84	133
326	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2024	1763.93	48
327	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
328	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
329	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
330	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
331	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631	24
332	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	01/2022	668.7	22
333	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
334	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33
335	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
336	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
337	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	39
338	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
339	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	21
340	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
341	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	21
342	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	12/2021	213	68
343	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
344	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
345	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
346	GARHWA ROAD-RAMNA	ECR	03/2015	03/2021	03/2022	348.23	12
347	CHANDIGARH-BADDI	NR	04/2007	03/2023	12/2025	328.14	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
348	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	36
349	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	36
350	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
351	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	34
352	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	12/2021	268.87	201
353	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
354	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	SER	03/2019	05/2023	12/2023	1866.31	7
355	ANAND GODHRA DOUBLING PROJECT 79 KMS	WR	04/2017	03/2020	03/2024	692.25	48
356	NIMACH BADI SADRI NEW LINE PROJECT	WR	04/2017	03/2022	03/2024	495.18	24
357	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
358	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE	NHAI	03/2019	05/2020	05/2022	1047	24
359	REHABILITATION AND UPGRADEMENT OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION	MoRTH	03/2017	01/2018	01/2022	423.79	48
360	REHABILITATION AND UPGRADEMENT OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2022	624.98	68
361	REHABILITATION AND UPGRADEMENT OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MoRTH	11/2015	06/2017	03/2022	335.32	57
362	REHABILITATION AND UPGRADEMENT OF BAREIL TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	01/2022	877.79	31
363	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	NHIDCL	03/2019	05/2019	03/2022	306.28	34
364	REHABILITATION AND UPGRADEMENT OF NH 200 FROM KM 241.553 TO 312.600 MASANIKAALA TO RENGAPALI ODISHA	MoRTH	03/2016	12/2019	02/2022	536.65	26
365	BALANCE WORK FOR REHABILITATION AND UPGRADEMENT OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	02/2022	392.33	47
366	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	MoRTH	01/2019	03/2021	03/2022	264.5	12
367	REHABILITATION AND UPGRADEMENT OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MoRTH	03/2018	04/2020	03/2022	263.89	23
368	FOUR LANING WIDENING AND	MoRTH	03/2018	08/2020	03/2022	288.3	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J						
369	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	MoRTH	03/2016	09/2020	12/2021	296.5	15
370	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MoRTH	01/2016	08/2016	06/2022	497.14	70
371	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	02/2022	162.56	47
372	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	02/2022	166.21	42
373	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	MoRTH	03/2016	11/2018	03/2022	271.17	40
374	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	04/2022	169.63	49
375	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	01/2022	426.18	16
376	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	02/2022	184.62	48
377	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	11/2022	160.27	39
378	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	08/2022	236.78	36
379	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	02/2022	205.05	59
380	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	12/2021	641.17	65
381	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
382	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	07/2022	1176.37	59
383	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	12/2021	990.61	51
384	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	07/2022	1227.87	58
385	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	03/2022	454.89	46
386	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
387	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
388	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	02/2022	588.95	39
389	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	MoRTH	01/2014	03/2016	04/2022	282.41	73
390	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MoRTH	11/2010	05/2017	05/2022	268.08	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
391	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	NHIDCL	12/2015	12/2018	12/2021	289.99	36
392	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	01/2022	628.45	24
393	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	01/2022	957.54	23
394	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	12/2022	511.83	64
395	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	03/2022	294.17	74
396	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	03/2022	252	74
397	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	MoRTH	03/2020	03/2021	04/2022	207.79	13
398	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	MoRTH	06/2020	05/2021	12/2022	221.4	19
399	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	MoRTH	08/2020	03/2021	03/2023	222.61	24
400	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	02/2022	374	105
401	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM)	NHAI	04/2012	04/2014	01/2022	624	93
402	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	03/2022	1724.55	108
403	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105
404	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	01/2022	1078.84	101
405	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2023	998.79	118
406	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2021	1928.22	80
407	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	12/2021	822.9	44
408	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	05/2023	563.92	65
409	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	46
410	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2022	593.26	49
411	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	06/2022	649.5	39
412	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	01/2022	1423.96	38
413	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
414	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	01/2022	707.82	41
415	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	12/2021	641.17	41
416	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2021	546	29
417	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2021	591.66	29
418	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	12/2021	804.97	42
419	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	06/2023	1167.42	51
420	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	12/2021	848.45	21
421	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3 (EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	12/2021	1373.28	21
422	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	09/2022	754.54	30
423	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2022	284.09	59
424	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	NHIDCL	02/2017	04/2017	03/2022	195.23	59
425	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	NHIDCL	02/2017	04/2017	03/2022	203.36	59
426	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	NHIDCL	01/2017	04/2017	03/2022	198.22	59
427	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	03/2022	894	23
428	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	NHIDCL	03/2018	05/2018	03/2022	274.31	46
429	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	NHIDCL	03/2018	06/2018	03/2022	403.36	45
430	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	NHIDCL	03/2018	05/2018	03/2022	417.24	46
431	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	NHIDCL	03/2015	10/2018	01/2022	262.97	39
432	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	NHIDCL	03/2017	12/2017	03/2022	409.85	51
433	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	NHIDCL	02/2018	10/2018	03/2022	391	41
434	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	NHIDCL	03/2018	10/2018	03/2022	234.27	41
435	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	NHIDCL	02/2017	09/2018	03/2022	387	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
436	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
437	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	07/2022	339.57	46
438	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
439	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
440	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	NHIDCL	03/2018	09/2018	12/2021	315.03	39
441	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	NHIDCL	03/2018	09/2018	12/2021	240.64	39
442	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2021	215.79	39
443	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
444	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	NHIDCL	11/2017	11/2017	12/2021	290.05	49
445	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MORTH	06/2017	06/2019	12/2021	282.08	30
446	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	MORTH	05/2018	05/2020	12/2021	248	19
447	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	NHIDCL	03/2015	01/2016	03/2022	829	74
448	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	NHIDCL	03/2018	07/2018	07/2022	1383.78	48
449	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
450	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	07/2023	640.07	46
451	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
452	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
453	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
454	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
455	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
456	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	09/2023	428.11	48
457	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MORTH	03/2018	03/2018	06/2022	214.69	51
458	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MORTH	03/2018	08/2018	02/2022	217.22	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
459	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	02/2022	233.04	47
460	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	02/2022	249.05	43
461	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2022	254.17	49
462	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	01/2022	279.44	46
463	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	12/2021	373.82	27
464	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	01/2022	809.16	42
465	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MoRTH	01/2016	09/2016	03/2022	476.2	66
466	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	12/2022	452.94	77
467	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	03/2022	496.02	84
468	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	12/2021	990.97	24
469	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH-43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	01/2022	379.16	50
470	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	03/2022	188.8	34
471	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	04/2022	847	25

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
472	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	02/2022	262.87	32
473	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	11/2022	1034.01	61
474	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	03/2022	15525	82

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
475	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD FOR TELECOM	10/2014	03/2018	01/2022	248.2	46
476	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	13334	80
477	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	BSNL	03/2020	06/2021	03/2022	431.16	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
478	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	CPWD	05/2019	09/2020	01/2023	299.97	28
479	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2021	8680	45
480	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	23136	36
481	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	CPWD	11/2017	05/2020	01/2022	238.56	20
482	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	CPWD	10/2016	03/2021	06/2023	422	27
483	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	CPWD	10/2016	08/2020	06/2022	392	22
484	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	12/2022	11420	13
485	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	10773	44
486	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	06/2023	1180	23
487	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	CPWD	10/2016	03/2022	06/2023	1128	15
488	KANPUR METRO RAIL PROJECT	LMRCL	05/2019	03/2024	03/2025	11076.48	12
489	AGRA METRO RAIL PROJECT	LMRCL	05/2019	03/2024	05/2025	8379.62	14
490	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2025	26405.14	73
491	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	02/2022	197.33	34

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
492	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	BUIDCO	08/2017	06/2022	12/2022	824	6
493	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	BUIDCO	08/2017	06/2022	12/2022	578.89	6
494	INTERCEPTION AND DIVERSION WITH STP AT BALLY	KMDA	10/2017	12/2021	09/2023	164.93	21
495	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	KMDA	01/2018	12/2021	09/2023	172.1	21
496	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	KMDA	12/2014	04/2020	03/2022	272.32	23
497	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	KMDA	08/2017	12/2021	09/2023	185.22	21
498	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	BUIDCO	03/2017	05/2021	06/2022	277.42	13
499	INTERCEPTION AND DIVERSION WITH STP	KMDA	05/2018	02/2022	03/2024	160	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AT HUGHLY-CHINSURAH						
500	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
501	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	BUIDCO	05/2017	11/2020	12/2021	191.62	13
502	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	BUIDCO	05/2017	04/2021	04/2022	356.37	12
503	SAIDPUR SEWER NETWORK PATNA	BUIDCO	04/2015	01/2021	03/2022	268.63	14
504	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	02/2022	225.77	23
505	SEWER NETWORKS, SPS AND STP, MUNGER	BUIDCO	03/2018	10/2021	12/2023	294.02	26
506	SEWER NETWORKS SPS AND STP HAJIPUR	BUIDCO	03/2018	08/2021	04/2023	305.19	20
507	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	KMDA	08/2017	09/2022	04/2024	307.12	19
508	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	KMDA	03/2018	06/2022	03/2024	165.16	21
509	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	BPB	03/2017	12/2019	12/2021	233.57	24
510	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	KMDA	05/2018	02/2022	03/2024	198.43	25
511	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	KMDA	12/2018	04/2022	04/2024	234.31	24
512	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR	KMDA	03/2019	04/2022	04/2024	287.53	24
513	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	KMDA	01/2019	04/2022	04/2024	384.96	24
514	I AND D AND STP AT CHAPPRA	BUIDCO	11/2018	12/2020	07/2022	236.15	19
515	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	42
516	SEWER NETWORK SPS AND STP BEGUSARAI	BUIDCO	03/2018	07/2021	04/2022	230.06	9
517	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	03/2024	298.12	32
518	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	UPJalNigam	02/2019	06/2022	04/2024	681.78	22
519	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	UPJalNigam	01/2019	12/2021	12/2022	231.79	12
520	MATHURA SEWERAGE SCHEME	UPJalNigam	12/2017	12/2020	12/2021	460.45	12
521	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR	DJB	12/2018	01/2021	12/2021	515.07	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DELHI						
522	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
523	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12
524	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	UPJaNigam	03/2019	08/2021	03/2024	271.39	31
525	FARRUKHABAD I AND D AND STP WORKS HAM	UPJaNigam	10/2017	03/2022	04/2024	213.62	25
526	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	UPJaNigam	05/2017	09/2021	03/2022	767.59	6
527	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	UKJaNigam	03/2017	11/2019	03/2022	158	28

FLASH REPORT

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(DECEMBER 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	417.23	707.73	290.5
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	1383	1938	555

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
10	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
11	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	6964.33	7254.37	290.04
12	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	479.53	808.97	329.44
13	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC FOR DPIIT	09/2011	09/2019	12579.09	13812.3	1233.21
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
16	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	414.11	586.5	172.39
17	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD FOR HEALTH	03/2019	09/2025	1577	1828	251

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	AIIMS BILASPUR	IBCC FOR HEALTH	04/2018	09/2021	1351	1471	120
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3727.3	2009.3
HOME AFFAIRS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MH	10/2013	10/2019	1219.21	2000	780.79
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
21	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	1236	628.94
22	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
23	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
24	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
25	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
26	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
27	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
28	DEVANGONTHI MARKETING TERMINAL	MANGALORE RE	06/2020	06/2023	200	304	104
29	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY	NRL	01/2019	10/2024	12366	18968	6602
30	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
31	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
32	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	206.63	340.76	134.13
33	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3072	395
34	ENMORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
35	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
36	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
37	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	2001.34	1139.55
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
38	LOKTAK D/S HEP(NHPC)	NHPC	12/1999	06/2006	578.62	1311.05	732.43
39	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
40	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978
41	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	529.68	633.8	104.12
42	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	1885.13	2311.89	426.76
43	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10998	399.02
44	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
45	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
46	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4825.6	3168.6
47	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
48	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
49	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	10566	5213
50	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1803	421.16
51	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	17007	2640.42
52	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	947.89	299.56
53	EASTERN REGION STRENGTHENING SCHEME- XVIII	PGCIL	03/2017	07/2020	3500	3994	494
54	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
55	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
56	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
57	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
58	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
59	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
60	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3650	2616.93
61	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
62	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
63	RAMGANJMUHDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
64	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	433	299.59
65	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	1160.48	1373.74	213.26
66	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
67	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
68	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	6527	4133.53
69	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
70	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	3154.43	2571.6
71	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	3081.2	2356.51
72	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
73	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83
74	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
75	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
76	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
77	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
78	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
79	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
80	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	986.3	1530.09	543.79
81	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	2161.36	360.35
82	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	325	140.94
83	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1043	657.8
84	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	774.51	278.77
85	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	14322	9867.83
86	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
87	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	4541.38	3361.19
88	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
89	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1080	755.27
90	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
91	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
92	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
93	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	872.65	228.27
94	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1650	674.38
95	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	1347.26	1524.68	177.42
96	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
97	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	610	315
98	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
99	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
100	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
101	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1205	681.48
102	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	527.37	375.53
103	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2042.51	244.51
104	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
105	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
106	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
107	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
108	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
109	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
110	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
111	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	150	341.66	191.66
112	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	760	1536	776
113	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	991.83	722.96
114	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
115	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	WR	03/2012	N.A.	248.26	528.49	280.23
116	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	WR	03/2012	N.A.	217.38	393.62	176.24
117	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	242.28	122.55
118	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3176.6	1268.09
119	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
120	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	2478.23	2875.12	396.89
121	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
122	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	1825	641.75
123	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1536	593.05

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
124	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96
125	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
126	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2900	2186.52
127	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	22716.11	6500.11
128	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1400	472.99
129	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
130	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1339	339
131	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
132	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	12/2021	602.27	1167	564.73
133	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25
134	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68
135	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
136	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	560.09	227.94
137	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
138	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
139	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
140	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.49	688.49
141	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
142	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	1763.93	2445.3	681.37
143	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	1295.42	1824	528.58
144	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
145	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
146	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	502.48	214.13

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
147	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
148	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
149	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
150	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2172.16	2051.46
151	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
152	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1090.6	271.37
153	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	750	335.16
154	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
155	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
156	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
157	ERNAKULAM-KUMBALAM	SR	04/2010	N.A.	189.24	448.1	258.86
158	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	931.98	1122	190.02
159	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	608.13	443.72
160	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.23	314.66
161	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	742	172.37
162	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
163	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	709.69	456.73
164	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	749.4	479.26
165	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
166	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	149.9	266.61	116.71
167	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
168	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
169	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
170	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
171	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1383.69	346.54
172	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	1868.89	320.23
173	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1954.21	797.27
174	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
175	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3377	1873.29
176	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	2223.37	1393.63
177	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	1549.09	1245.11
178	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	2315	5174.3	2859.3
179	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
180	MUNEERABAD-MAHABOONNAGAR(NL),SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
181	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	390.39	511.75	121.36
182	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	NFR	02/1999	04/2010	380.6	1090.6	710
183	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	839	214
184	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
185	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
186	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
187	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
188	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
189	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
190	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	800	197.5
191	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
192	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
193	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
194	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	929.86	251.32
195	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1878	263.41
196	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	760	182
197	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	2215.27	1341.56
198	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
199	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1104	243.57
200	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
201	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
202	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
203	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2017.96	1567.96
204	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
205	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
206	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6663	4336.48
207	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
208	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4794.6	2523.1
209	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL	RVNL	04/2010	03/2023	2127	3000	873
210	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
211	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	2132.77	3037.95	905.18
212	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
213	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
214	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2404.03	341.73
215	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
216	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
217	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
218	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
219	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1387.52	594.63
220	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	3168.29	3445.48	277.19
221	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	6171.08	2667.39
222	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
223	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
224	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
225	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	612.58	332.58
226	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
227	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
228	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	624.41	992.67	368.26
229	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
230	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
231	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	193.69	327.92	134.23
232	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	624.98	731.5	106.52
233	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
234	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
235	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	186.96	322.24	135.28
236	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MoRTH	04/2014	08/2017	279.7	398.52	118.82
237	FOUR LANING OF AKKALKOT-SOLAPUR SECTION	NHAI	03/2018	N.A.	642.13	807	164.87

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4						
238	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	NHAI	03/2018	N.A.	478.74	1135.08	656.34
239	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	NHAI	03/2018	N.A.	795.5	922.64	127.14
240	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	925.96	291.26
241	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
242	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
243	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
244	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1361	308.79
245	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
246	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
247	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	1952.2	690.22
248	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
249	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
250	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	NHAI	02/2018	N.A.	1166.26	1296.93	130.67
251	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
252	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
253	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
254	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
255	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	N.A.	1251.11	1361	109.89
256	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
257	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
258	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
259	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	1588.29	199.95

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
260	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
261	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1300	175.89
262	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
263	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
264	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
265	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
266	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
267	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
268	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	726.67	1096.52	369.85
269	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
270	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	934.46	1457.82	523.36
271	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1827.15	744.15
272	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	593.26	717.24	123.98
273	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	744.73	213.6
274	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
275	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
276	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
277	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	268.08	390.73	122.65
278	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
279	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
280	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
281	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
282	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
283	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
284	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
285	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415
286	FORGED WHEEL PLANT	RINL	04/2014	09/2018	1682.85	2100	417.15
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
287	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
288	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	26405.14	30695.12	4289.98
289	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	18380	3780
290	PATNA METRO RAIL CORPORATION LIMITED	PATNA METRO	02/2019	06/2024	13365.77	13925.5	559.73
291	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	23136	33406	10270
292	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
293	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
WATER RESOURCES							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
294	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83
295	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	254.13	413.29	159.16
296	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	225.77	398.9	173.13

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	1,2320.00	1,7079.00	4759	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	12/2022	1,1459.00	1,6580.00	5121	84
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	06/2023	346.27	480.33	134.06	21
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2022	417.23	707.73	290.5	45
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2023	1383.00	1938.00	555	27

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5146.48	2484.75	60
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	349.28	186.52	84
9	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2028	6964.33	7254.37	290.04	188
10	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	459.49	307.06	84
11	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	808.97	329.44	132

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	05/2022	4773.00	5178.00	405	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	06/2022	1351.00	1471.00	120	9

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
14	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MHA	10/2013	10/2019	05/2022	1219.21	2000.00	780.79	31

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFIN	06/2020	06/2023	01/2024	200.00	304.00	104	7
16	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
17	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677.00	3072.00	395	13
18	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497.00	6025.00	1528	38
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	3375.90	185.21	49
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	08/2024	2915.00	5909.00	2994	140
21	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	09/2022	607.06	1236.00	628.94	59
22	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	03/2022	1823.00	3027.90	1204.9	12
23	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321.00	3338.00	1017	15
24	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2022	861.79	2001.34	1139.55	108
25	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678.00	1472.00	794	66
26	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
27	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

519

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
28	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	340.76	134.13	29

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	03/2022	529.68	633.80	104.12	40
30	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	2,1312.11	12619.1	141
31	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	02/2022	3500.00	3994.00	494	19
32	NPGCL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	03/2022	1,2964.60	1,7304.00	4339.4	46
33	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	9897.59	5978	162
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
35	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	05/2023	1,1130.19	1,4719.10	3588.91	117
36	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	09/2024	2978.48	5867.38	2888.9	138
37	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2023	1,4366.58	1,7007.00	2640.42	51
38	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	1803.00	421.16	63
39	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2024	2491.58	3860.35	1368.77	138
40	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657.00	4825.60	3168.6	88
41	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10/2022	1,0598.98	1,0998.00	399.02	23
42	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	03/2022	5111.33	6700.00	1588.67	39
43	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE	PGCIL	12/2014	12/2018	03/2024	4754.42	9129.32	4374.9	63

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

520

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	TRANSMISSION AND DISTRIBUTION SYSTEM IN A P								
44	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	01/2022	1885.13	2311.89	426.76	37
45	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	947.89	299.56	6

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
46	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	06/2022	390.39	511.75	121.36	6
47	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	1400.00	472.99	39
48	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	2900.00	2186.52	21
49	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
50	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	2009.00	1060.96	21
51	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1536.00	593.05	39
52	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	1825.00	641.75	24
53	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	1835.83	349.98	12
54	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2023	2478.23	2875.12	396.89	15
55	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	12/2023	582.13	1247.64	665.51	21
56	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
57	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	12/2024	548.00	819.01	271.01	57
58	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798.00	2042.51	244.51	57
59	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	03/2030	151.84	527.37	375.53	133

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

521

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
60	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	06/2022	569.63	742.00	172.37	27
61	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	950.00	317.32	69
62	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2172.16	2051.46	105
63	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
64	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
65	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.20	1043.00	657.8	48
66	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60
67	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	6663.00	4336.48	132
68	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	8600.00	7260.52	96
69	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	860.41	450.33	40
70	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450.00	2017.96	1567.96	148
71	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500.00	2,7949.00	25449	241
72	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
73	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
74	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.20	2120.16	1074.96	180
75	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
76	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

522

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
77	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2024	424.60	2909.99	2485.39	36
78	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
79	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
80	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	3081.20	2356.51	73
81	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	6527.00	4133.53	117
82	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	1373.74	213.26	168
83	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
84	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	6171.08	2667.39	12
85	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	1387.52	594.63	24
86	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR -BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
87	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.30	1530.09	543.79	129
88	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	02/2022	704.31	927.94	223.63	23
89	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	3037.95	905.18	156
90	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4794.60	2523.1	24
91	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	06/2022	495.44	2980.41	2484.97	219
92	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
93	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	1080.00	755.27	128

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

523

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
94	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	12/2021	1180.19	4541.38	3361.19	156
95	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2024	2923.13	3791.66	868.53	189
96	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,4322.00	9867.83	153
97	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	07/2022	495.74	774.51	278.77	109
98	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
99	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2025	303.98	1549.09	1245.11	60
100	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	2223.37	1393.63	48
101	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	3377.00	1873.29	24
102	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
103	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	1954.21	797.27	36
104	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600.00	701.81	101.81	31
105	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	01/2022	578.00	760.00	182	22
106	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	1878.00	263.41	60
107	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	12/2021	678.54	929.86	251.32	33
108	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	610.00	315	37
109	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	1524.68	177.42	12
110	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	12/2021	644.38	872.65	228.27	9
111	RAJKOT-VERAVAL,WANSJALIA TO	WR	04/1994	03/2019	03/2023	320.66	1378.11	1057.45	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

524

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
112	JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)								
112	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	1383.69	346.54	21
113	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
114	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
115	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2024	1763.93	2445.30	681.37	48
116	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631.00	3887.48	256.48	24
117	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	810.02	108.41	64
118	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
119	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	1873.21	1002.25	12
120	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	06/2022	969.83	1312.96	343.13	27
121	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
122	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3176.60	1268.09	9
123	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	1268.32	682.39	34
124	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	12/2021	268.87	991.83	722.96	201
125	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	06/2022	760.00	1536.00	776	27
126	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150.00	341.66	191.66	66
127	CHANDIGARH-BADDI	NR	04/2007	03/2023	12/2025	328.14	1540.13	1211.99	33
128	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	1215.54	471.5	36

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

525

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
129	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	1185.73	454.09	36
130	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288.00	4970.11	2682.11	18
131	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
132	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
133	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	06/2022	624.98	731.50	106.52	68
134	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	744.73	213.6	46
135	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105
136	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2022	593.26	717.24	123.98	49
137	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	05/2022	268.08	390.73	122.65	60

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
138	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	03/2022	1,5525.00	2,1940.00	6415	82

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
139	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	1,3334.00	2,4664.00	11330	80

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
140	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	1,0773.00	1,2787.00	2014	44

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

526

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
141	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	2,3136.00	3,3406.00	10270	36
142	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2025	2,6405.14	3,0695.12	4289.98	73

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
143	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	02/2022	225.77	398.90	173.13	23
144	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25
145	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	413.29	159.16	42

FLASH REPORT

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above								(December 2021)
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00	166.90	05/2013	02/2022	-55.37	105
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00	364.59	12/2009	09/2020	-39.64	129
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36	469.31	01/2014	-	61.08	0
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00	475.00	05/2013	-	46.15	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00	485.00	08/2013	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00	486.00	05/2010	-	.00	0
7	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00	516.00	07/2008	-	.00	0
8	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07	530.07	08/2016	06/2020	.00	46
9	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00	571.00	10/2013	-	.00	0
10	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00	574.00	03/2014	-	.00	0
11	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00	575.00	07/2013	-	.00	0
12	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54	591.00	11/2013	-	15.53	0
13	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00	617.00	08/2012	-	.00	0
14	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	01/2022	.00	93
15	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18	637.18	06/2019	09/2019	.00	3
16	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - PPP BOT (Hybrid Annuity) - [N24001340]	11/2019	716.00	716.00	07/2021	-	.00	0
18	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	-	.00	0
19	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	-	.00	0
20	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	12/2021	.00	44
21	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	-	.00	0
22	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	-	.00	0
23	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	-	.00	0
24	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	06/2023	.00	118
25	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	-	.00	0
26	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	01/2022	.00	101
27	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	10/2020	.00	76
28	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	-	.00	0
29	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	-	.00	0
30	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88	1,226.88	02/2021	-	.00	0
31	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	-	.00	0
32	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	-	.00	0
33	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	-	.00	0
34	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	-	.00	0
35	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
36	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0
37	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0
38	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	-	21.90	0
39	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
40	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10	1,601.10	02/2021	-	.00	0
41	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
42	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
43	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
44	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
45	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	03/2022	.00	108
46	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
47	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
48	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	12/2021	.00	80
49	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	09/2020	.00	62
50	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
51	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	09/2021	.00	29
52	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,159.00	01/2019	-	.00	0
53	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	-	106.50	0
54	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	2,360.65	-	-	41.78	0
55	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(December
2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
56	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
57	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		68,482.89 -	72,035.06				
	Grand Total		68,482.89	72,035.06				

FLASH REPORT

List of projects original without Date of Commissioning

Costing Rs.		150 Crore and above				(December 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1	<u>COAL</u> <u>Singareni Colliers Company Limited</u>								
	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75	-			2/6
2	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u>								
	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	190.34	183.36	-	12/2021	-	0/0
	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	546.71	-	12/2021	-	0/0
4	<u>HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH</u>	03/2018	601.02	601.02	515.47	-	03/2022	-	0/0
	Total		1,340.57	1,374.35	1,245.54				0/0
5	<u>RAILWAYS</u> <u>East Central Railways</u>								
	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56	1,858.75	386.36	-	03/2023	-	0/0
	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 1,470.50	1,470.50	1,467.70	-	03/2023	-	0/0
7	<u>KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR</u>	04/1997	162.87 614.45	614.45	352.68	-	12/2023	-	0/0
	BIHTA-AURANGABAD (NL) - [N22000170]ECR, BIHAR	04/2008	326.20	2,995.01	2.55	-	03/2024	-	0/0
	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
10	<u>SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR</u>	05/2015	380.00	519.33	316.22	-	03/2025	-	0/0
	<u>Eastern Railways</u>								
	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80	495.10	316.82	-	03/2022	-	0/0
12	<u>BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL</u>	04/2012	255.64	272.20	303.23	-	03/2022	-	0/0
	MONIGRAM- NIMTITA - [N22000301]ER, MULTI STATE	04/2012	250.93	310.70	410.29	-	03/2024	-	0/0
	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	450.00	1,261.34	-	-	03/2025	-	0/0

Costing Rs. 150 Crore and above (December 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	260.10	11.77	-	03/2025	-	0/0
16	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	71.43	-	03/2025	-	0/0
17	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	250.55	20.11	-	03/2025	-	0/0
18	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17	527.54	1.76	-	03/2025	-	0/0
19	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47	298.22	36.13	-	03/2025	-	0/0
20	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96	336.96	40.65	-	03/2025	-	0/0
21	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
<u>Metropolitan Rapid Transport Projects</u>									
22	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
<u>North Eastern Railway</u>									
23	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH	04/2016	602.50	800.00	145.14	-	12/2023	-	0/0
<u>Northern Railway</u>									
24	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91	791.39	597.99	-	09/2023	-	0/0
25	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68	419.00	160.79	-	09/2023	-	0/0
26	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65	359.00	116.87	-	03/2024	-	0/0
27	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22	841.90	1.73	-	03/2024	-	0/0
<u>South Eastern Railway</u>									
28	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37	620.00	41.78	-	03/2025	-	0/0
<u>South Western Railway</u>									
29	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01	2,161.36	82.81	-	12/2023	-	0/0
30	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00	692.43	-	-	12/2023	-	0/0
31	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00	466.65	-	-	12/2023	-	0/0
32	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25	367.77	-	-	12/2023	-	0/0

Costing Rs. 150 Crore and above						(December 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
33	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00	5,174.30	158.11	-	12/2024	-	0/0
34	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30	2,404.03	1,100.11	-	12/2025	-	2/2
35	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85	348.85	.36	-	12/2025	-	0/0
	<u>Southern Railway</u>								
36	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90	1,431.90	934.32	-	03/2024	-	0/0
37	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96	709.69	256.70	-	03/2025	-	0/0
38	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24	448.10	268.73	-	03/2025	-	0/0
39	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00	1,339.00	.82	-	03/2025	-	0/0
40	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	3,154.43	239.59	-	12/2025	-	0/0
41	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40	227.40	65.02	-	03/2030	-	0/0
42	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52	1,205.00	2.28	-	03/2030	-	0/0
43	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO JRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00	839.01	.63	-	03/2030	-	0/0
44	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57	603.23	1.68	-	03/2030	-	0/0
	<u>Western Railway</u>								
45	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10	844.10	254.99	-	03/2024	-	0/0
	Total		21,270.86	38,557.31	8,169.73				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
46	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59	306.59	195.70	-	01/2022	-	0/0
47	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	137.80	-	03/2022	-	0/0
48	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45	319.96	117.56	-	03/2022	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								

Costing Rs. 150 Crore and above (December 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
49	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	520.01	207.70	- -	12/2021	-	3/4
50	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	1,049.51	155.61	- -	12/2021	-	2/4
51	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM <u>National Highways Authority Of India</u>	10/2017	818.00 -	818.00	272.86	- -	03/2023	-	2/4
52	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	248.71	- -	12/2021	-	0/0
53	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
54	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	2,169.00	-	- -	12/2021	-	0/0
55	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	490.00	- -	12/2021	-	1/3
56	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	346.17	- -	01/2022	-	0/0
57	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	339.86	- -	01/2022	-	0/0
58	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	227.37	- -	01/2022	-	0/0
59	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	205.00	- -	02/2022	-	0/0
60	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	242.03	- -	02/2022	-	0/0
61	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	790.00	- -	02/2022	-	2/4

Costing Rs. 150 Crore and above (December 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	456.80	- -	03/2022	-	0/0
63	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	284.66	- -	03/2022	-	0/1
64	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	1,513.48	- -	03/2022	-	0/0
65	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	293.31	- -	03/2022	-	4/4
66	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	473.95	- -	03/2022	-	0/0
67	FOUR LANING OF MADURAI-CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	397.89	- -	03/2022	-	0/0
68	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	85.61	- -	06/2022	-	0/0
69	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	884.00	609.00	- -	10/2022	-	2/4
70	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	422.00	- -	11/2022	-	2/4
71	FOUR LANINIG OF CHETTICULAM TO NATHAM SECTION OF NH-785 FROM CHETTICULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	255.05	- -	12/2022	-	0/0
	Total		18,220.80 -	19,341.41	8,768.12				18/32
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								
72	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	974.86	- -	12/2022	-	0/9
	Total		2,694.00 -	2,694.00	974.86				0/9
	Grand Total		43,798.96	62,239.80	19,312.00				22/49

FLASH REPORT

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	03/2022 12/2023	-
	Total		380.87 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Mahanadi Coal Fields Limited</u>				
3	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	03/2012 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
7	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
10	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	03/2016 -	09/2021
	Total		14,560.71 -		
	<u>FINANCE</u>				
	<u>Cpwd For Finance</u>				
11	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
12	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU	11/2017	348.77 -	11/2021 -	11/2021
	Total		557.77 -		

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
13	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	11/2019 05/2021	-
14	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	11/2019 05/2021	-
	Total		458.64 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
15	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 12/2022	12/2020
16	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020	-
	Total		700.62 -		
	<u>STEEL</u>				
	<u>Raastriya Ispat Nigam Limited</u>				
17	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	09/2018 09/2021	09/2021
	Total		1,682.85 -		
	<u>PETROLEUM</u>				
	<u>Indian Oil Corporation Limited</u>				
18	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	02/2020 06/2021	11/2021
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
20	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 4,475.92	05/2021 05/2021	05/2021
21	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	03/2019 09/2021	09/2021
	Total		5,925.65 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	07/2012 06/2020	11/2021

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
24	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
25	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
26	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
	<u>Power Grid Corporation Of India Limited</u>				
27	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021
28	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 06/2021	06/2021
29	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021
30	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALAR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 07/2021	10/2021
31	HVDC BIPOLE LINK BETWEEN WR AND SR-NORTH TRICHUR - SCHEME - II AC SYSTEM STRENGTHENING AT PUGALAR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 09/2021	10/2021
	Total		37,698.21 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
32	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-
	<u>Natrip Implementation Socity</u>				
33	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 03/2021	03/2021
	Total		3,272.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Cpwd For Health</u>				
34	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	05/2021
	<u>HII Infra Tech Services Limited</u>				
35	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-
36	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
37	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
38	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
39	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
40	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
41	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	03/2018 -	09/2019
42	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	05/2017 -	01/2020
43	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
44	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	- -	01/2021
45	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	05/2017 -	03/2021
46	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC, PUNJAB	07/2016	152.95 -	02/2018 -	03/2021
47	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC, ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021
48	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	- -	03/2021
49	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	09/2021
50	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	10/2021
51	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	10/2021
	Total		6,803.41 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
52	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 -	03/2019 -	-
53	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
54	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	-
55	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 -	-
56	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
57	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
58	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	03/2019 -	-
59	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
60	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
61	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
62	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
63	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
64	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 735.20	- -	03/2021
65	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	477.88 751.55	03/2012 09/2021	09/2021
66	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 516.02	03/2020 -	-
67	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR	04/2008	633.87 -	- -	-
68	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
69	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR, BIHAR	04/2008	445.25 -	- -	-
70	GAYA-CHATRA (NL) - [N22000169]ECR, MULTI STATE	04/2008	415.67 -	- -	-
71	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
72	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
73	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
74	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
75	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
76	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR, BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>Eastern Railways</u>				
77	BANDEL-BOINCHI 3RD LINE - [N22000221]ER, MULTI STATE	04/2011	288.35 -	- -	03/2021
78	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
79	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
80	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
81	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
82	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
83	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North East Frontier Railway</u>				
84	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	10/2021
85	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
86	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
87	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
88	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
89	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
90	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-
91	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
92	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-
93	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
94	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
95	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
96	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
97	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
98	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
99	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	420.18 -	03/2020 -	09/2021
100	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
101	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
102	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
103	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
104	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021
105	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-
106	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
107	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 -	03/2021 -	-
108	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	03/2020 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
109	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 12/2022	-
	<u>Railway Electrification</u>				
110	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
111	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
112	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
113	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 176.18	03/2022 03/2022	-
	<u>South Eastern Railway</u>				
114	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	03/2019
115	CHAKRADHARPUR TO GOILKERA 3RD LINE (34 KM) - [N22000507]SER,JHARKHAND	11/2015	354.54 -	12/2018 -	06/2020
116	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
	<u>South Western Railway</u>				
117	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	09/2021
	<u>Southern Railway</u>				
118	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-
119	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
	<u>Western Railway</u>				
120	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 311.36	- -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
121	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 393.62	- 12/2022	-
122	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 528.49	- 12/2022	-
123	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 154.15	- 12/2021	-
	Total		80,259.11 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
124	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019
125	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020
126	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH, RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
127	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH, ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
128	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020
129	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2020	12/2020
130	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021
131	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
132	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
133	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 03/2020	03/2021
134	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021
135	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	04/2021
136	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
137	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 06/2021	06/2021
138	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021
139	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH, WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021
140	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH, GUJARAT	03/2018	351.00 -	06/2021 -	06/2021
141	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH, UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021
142	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH, UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021
143	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH, UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021
144	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH, ANDHRA PRADESH	01/2016	348.95 -	08/2016 12/2021	07/2021
145	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH, UTTARAKHAND	12/2017	248.22 -	12/2019 08/2021	08/2021
146	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH, PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021
147	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH, UTTARAKHAND	02/2018	418.88 -	02/2020 09/2021	09/2021
148	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH, JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021
149	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH, ARUNACHAL PRADESH	03/2021	182.55 -	09/2021 -	09/2021
150	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH, UTTARAKHAND	02/2018	293.68 -	- 10/2021	10/2021
151	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 237.80	11/2019 10/2021	10/2021
152	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2021	10/2021
153	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH, TRIPURA	10/2016	171.90 -	08/2020 -	11/2021
154	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH, MIZORAM	01/2017	205.95 -	01/2021 -	11/2021

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
155	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	11/2021
156	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
157	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	02/2017 -	-
158	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
159	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
160	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
161	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26/200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
162	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
163	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
164	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
165	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
166	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
167	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-
168	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 273.27	08/2015 -	-
169	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
170	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
171	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-
172	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
173	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
174	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
175	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
176	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
177	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
178	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
179	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-
180	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
181	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
182	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-
183	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
184	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
185	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
186	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
187	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
188	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
189	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-
190	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
191	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 194.48	11/2020 -	-
192	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
193	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
194	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
195	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
196	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
197	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
198	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
199	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
200	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAYDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
201	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
202	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH.0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
203	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 10/2021	-
204	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 10/2021	-
205	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 02/2022	-
206	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 01/2022	-
207	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 12/2021	-
208	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 274.73	08/2018 11/2021	-
209	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 556.13	11/2018 07/2021	-
210	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	05/2016 09/2021	-
211	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
213	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
214	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
215	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
216	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 381.75	08/2018 10/2021	-
217	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2021	-
218	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 11/2021	-
219	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 08/2021	-
220	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 12/2021	-
221	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 381.75	09/2017 05/2022	-
222	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 596.38	01/2018 04/2022	-
223	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
224	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
225	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
226	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
227	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
228	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
229	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
230	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
231	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
232	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
233	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
234	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
235	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
236	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
237	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
238	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
239	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
240	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
241	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
242	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
243	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
244	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
245	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
246	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
247	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
248	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
249	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
250	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
251	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
252	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
253	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
254	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
255	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
256	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
257	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
258	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
259	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
260	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
261	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
262	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
263	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
264	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
265	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
266	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
267	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
268	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
269	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
270	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
271	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
272	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
273	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
274	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
275	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
276	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
277	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
278	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
279	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
280	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
281	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
282	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
283	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
284	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
285	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
286	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
287	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
288	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
289	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
290	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
291	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
292	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
293	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
294	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
295	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
296	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
297	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
298	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
299	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
300	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
301	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
302	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
303	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
304	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
305	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
306	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
307	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
308	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
309	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
310	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
311	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
312	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
313	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
314	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
315	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
316	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
317	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
318	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
319	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
320	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
321	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
322	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
323	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
324	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
325	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
326	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
327	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
328	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
329	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
330	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
331	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
332	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
333	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
334	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
335	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
336	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
337	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
338	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
339	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
340	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
341	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
342	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
343	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
344	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
345	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
346	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
347	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
348	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
349	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
350	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	-
351	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
352	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
353	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
354	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
355	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
356	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
357	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
358	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
359	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
360	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
361	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
362	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
363	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
364	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
365	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	06/2021 -	-
366	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
367	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
368	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
369	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
370	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
371	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
372	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
373	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
374	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
375	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
376	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
377	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
378	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
379	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
380	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
381	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
382	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
383	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
384	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
385	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
386	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
387	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-
388	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 12/2021	-
389	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 12/2021	-
390	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
391	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 04/2022	-
392	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
393	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
394	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
395	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 204.73	06/2019 -	-
396	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
397	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
398	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
399	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
400	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
401	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
402	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
403	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
404	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
405	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
406	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
407	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
408	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	08/2021 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
409	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	08/2021 -	-
410	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
411	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
412	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
413	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-
414	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-
415	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	-
416	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	-
417	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
418	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-
419	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-
420	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-
421	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-
422	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-
423	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2021	-
424	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
425	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN	03/2020	370.36 -	08/2022 -	-
426	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-
427	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-
National Highways And Infrastructure Development Corporation Ltd.					

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
428	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
429	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	03/2021
430	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
431	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
432	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- 09/2021	09/2021
433	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 03/2021	10/2021
434	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	10/2018 -	10/2021
435	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	10/2021
436	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	11/2021
437	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	11/2021
438	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	11/2021
439	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	11/2021
440	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	11/2021
441	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
442	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
443	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
444	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
445	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
446	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
447	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
	<u>National Highways Authority Of India</u>				
448	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- 12/2016	05/2017
449	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- 02/2018	02/2018
450	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 906.65	- 02/2018	02/2018
451	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	-	11/2018
452	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019
453	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGOUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
454	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
455	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
456	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020
457	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
458	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
459	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
460	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
461	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
462	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
463	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
464	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
465	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
466	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
467	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	04/2021
468	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021
469	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 04/2019	06/2021
470	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- 07/2021	07/2021
471	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 07/2021	07/2021
472	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021
473	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021
474	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	08/2021
475	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021
476	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021
477	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021
478	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 1,201.51	- 06/2021	09/2021
479	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021
480	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 499.70	- 05/2021	09/2021
481	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021
482	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	10/2021
483	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021
484	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 866.55	- 10/2021	10/2021
485	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
486	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	11/2021
487	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
488	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
489	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
490	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
491	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
492	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
493	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
494	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
495	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-
496	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
497	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
498	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
499	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
500	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
501	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
502	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
503	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
504	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
505	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
506	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
507	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
508	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
509	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
510	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
511	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 12/2021	-
512	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
513	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
514	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
515	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-
516	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
517	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
518	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
519	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
520	WIDENING OF KHEDE-SINAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
521	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
522	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
523	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
524	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
525	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
526	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
527	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
528	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
529	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
530	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
531	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
532	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 363.93	- -	-
533	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
534	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
535	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
536	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
537	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
538	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-
539	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	-
540	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	-
541	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-
542	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
543	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
544	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 1,457.82	03/2018 03/2021	-
545	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
546	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
547	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	-
548	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
549	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
550	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
551	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
552	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 -	-
553	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
554	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
555	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
556	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 247.00	04/2018 -	-
557	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
558	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
559	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
560	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-
561	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
562	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 1,096.52	04/2018 -	-
563	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
564	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
565	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
566	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
567	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-
568	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
569	MEERUT-BULANDSHAHR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-
570	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
571	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
572	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-
573	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-
574	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-
575	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
576	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	04/2019 10/2022	-
577	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- 10/2022	-
578	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
579	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
580	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
581	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
582	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
583	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
584	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
585	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
586	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
587	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
588	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
589	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
590	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
591	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
592	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
593	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
594	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 - 1,367.00	- -	-
595	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
596	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
597	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
598	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
599	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
600	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-
601	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-
602	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	- -	-
603	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	- -	-
604	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
605	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	03/2019 -	-
606	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
607	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-
608	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-
609	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-
610	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-
611	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	07/2018 02/2022	-
612	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-
613	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 1,361.00	- 01/2019	-
614	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-
615	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
616	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
617	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
618	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
619	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA	03/2017	988.34 -	03/2020 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
620	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
621	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
622	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
623	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
624	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
625	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
626	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	-
627	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
628	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
629	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
630	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	-
631	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
632	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
633	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
634	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
635	4-LANNING OF THALSERRY-MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-
636	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
637	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
638	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
639	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
640	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
641	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
642	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
643	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
644	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
645	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
646	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
647	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
648	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
649	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
650	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
651	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
652	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
653	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
654	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
655	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
656	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
657	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
658	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
659	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
660	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
661	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
662	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-
663	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-
664	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA	02/2018	1,424.77 -	- -	-
665	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH	02/2018	670.50 -	- -	-
666	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI, KARNATAKA	02/2018	2,177.80 -	- -	-
667	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-
668	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI, UTTAR PRADESH	03/2018	809.07 -	- -	-
669	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI, UTTAR PRADESH	03/2018	925.40 -	- -	-
670	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	-
671	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
672	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	- -	-
673	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI, UTTAR PRADESH	03/2018	1,120.57 -	- -	-
674	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- 01/2019	-
675	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	-
676	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	-
677	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
678	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI, UTTAR PRADESH	02/2018	972.77 -	- -	-
679	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI, ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
680	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI, ANDHRA PRADESH	03/2018	557.30 -	- -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
681	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI, BIHAR	03/2018	496.20 -	- -	-
682	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	- -	-
683	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-
684	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
685	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
686	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
687	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
688	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-
689	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
690	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-
691	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	- -	-
692	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA	03/2018	806.11 -	- -	-
693	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA	03/2018	198.05 -	- -	-
694	REHABILITATION AND UPGADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA	03/2018	181.78 -	- -	-
695	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA	03/2018	642.13 -	- -	-
696	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI, JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-
697	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
698	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI, HARYANA	01/2019	1,051.91 -	- -	-

Costing Rs. 150 Crore and above				(December 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
699	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
700	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
701	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
702	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
703	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
704	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
705	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
706	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
707	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
708	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
709	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
710	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
711	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
712	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
713	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
714	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-
715	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-
716	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	11/2019 -	-
717	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	11/2019 -	-
718	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	11/2019 -	-
719	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
720	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
721	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 1,135.08	- 11/2021	-
	Total		3,80,995.21 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
722	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 18,380.00	12/2015 02/2019	02/2019
723	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL, TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	02/2021
	<u>Delhi Metro Rail Corporation</u>				
724	DELHI MRTS PHASE-III - [N28000056]DMRC, DELHI	09/2011	38,585.00 -	03/2016 08/2021	-
725	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC, DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
726	KOCHI METRO RAIL PROJECT - [N28000081]KMRL, KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
727	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019
	Total		69,629.79 -		
	<u>WATER RESOURCES</u>				
	<u>Delhi Jal Board</u>				
728	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFGARH DRAIN DHANSA TO - [N30000018]DJB, DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Hscl For Water</u>				
729	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL FOR WATER, BIHAR	10/2005	956.00 -	03/2015 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
730	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 05/2022	-
	<u>Uttar Pradesh Jal Nigam</u>				
731	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam, UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	11/2021
	Total		1,855.48 -		
	<u>COMMERCE</u>				
	<u>Nbcc For Commerce</u>				

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
732	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Cpwd Of Higher Education</u>				
733	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 11/2021	11/2021
734	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND	09/2012	171.86 -	03/2016 -	-
735	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23 -	10/2012 -	-
736	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN	12/2016	549.31 -	07/2019 -	-
737	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD EDUCATION,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	-
	Total		1,343.23 -		
	<u>HOME AFFAIRS</u>				
	<u>Cpwd For Mha</u>				
738	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAUJI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31 -	01/2022 -	01/2020
	Total		199.31 -		
	<u>DPIIT</u>				
	<u>Dmic For Dpiit</u>				
739	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021
	Total		12,579.09 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
740	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	08/2021
	Total		151.33 -		
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				

Costing Rs. 150 Crore and above					(December 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
741	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		6,19,627.82		

FLASH REPORT

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(December 2021)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,TAMIL NADU	09/2003	3,492.00 -	6,840.00	6,054.37	09/2010 -	10/2022	145	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	17,427.00	12/2015 -	12/2022	84	-
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	27,505.00	11/2020 -	11/2023	36	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,945.00	12/2016 -	12/2023	84	-
	Total		67,120.00 -	80,348.00	64,931.37				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	438.28 -	402.00	397.85	06/2019 12/2021	01/2022	31	1
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	303.80	203.38	04/2020 -	06/2022	26	-
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39 -	475.39	184.10	04/2021 -	08/2022	16	-
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	329.56	09/2020 -	09/2022	24	-
9	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH	02/2019	645.63 -	645.63	186.02	08/2022 -	11/2022	3	-
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	513.93	10/2021 -	12/2022	14	-
11	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24 -	412.24	224.31	06/2021 -	12/2022	18	-
12	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	108.20	02/2020 12/2021	12/2022	34	12
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	397.52	03/2021 03/2022	03/2023	24	12
14	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	1,405.00	396.18	08/2022 -	03/2023	7	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH	07/2018	346.27 -	480.33	140.13	09/2021 12/2022	06/2023	21	6
16	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 1,938.00	1,938.00	568.01	09/2021 -	12/2023	27	-
17	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	249.46	10/2022 -	12/2023	14	-
18	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]AAI,TELANGANA	05/2020	353.61 -	353.61	95.77	05/2022 -	12/2023	19	-
19	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	763.60	02/2022 -	06/2024	28	-
	Total		12,174.36 -	12,917.14	4,758.02				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
20	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	285.81	05/2014 -	03/2022	94	-
21	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	28.43	04/2018 -	10/2022	54	-
22	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	79.48	03/2017 -	10/2022	67	-
23	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	508.61	03/2019 -	02/2023	47	-
24	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2023	24	-
25	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	89.42	04/2014 -	04/2023	108	-
	<u>Central Coal Fields Limited</u>								
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	124.85	03/2011 -	03/2022	132	-
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	500.91	03/2016 -	03/2022	72	-
28	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	93.13	03/2014 -	03/2022	96	-
	<u>Eastern Coal Fields Limited</u>								
29	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	5,146.48	625.36	08/2019 -	08/2024	60	-
30	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	714.63	03/2018 -	03/2029	132	-
	<u>Mahanadi Coal Fields Limited</u>								
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	808.97	808.97	03/2013 -	03/2024	132	-
32	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	254.06	03/2019 -	03/2024	60	-
33	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	683.47	03/2021 -	09/2025	54	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
34	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL, ODISHA	12/2007	3,145.45 -	3,145.45	661.05	03/2017 -	03/2031	168	-
	<u>Neyveli Lignite Corporation</u>								
35	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC, JHARKHAND	07/2013	1,795.01 -	1,795.01	37.83	08/2022 -	09/2023	13	-
	<u>Northern Coal Fields Limited</u>								
36	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	902.52	03/2021 -	03/2022	12	-
37	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL, MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	481.57	03/2022 -	03/2023	12	-
	<u>Singareni Colliers Company Limited</u>								
38	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84	-
39	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	306.52	03/2015 -	03/2022	84	-
40	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	384.32	144.15	07/2016 -	03/2022	68	-
41	KAKATIYAKHANI OPENCASST-2 PROJECT - [N06000129]SCCL, TELANGANA	05/2015	397.09 -	442.42	123.72	03/2019	03/2022	36	-
42	KAKATIYAKHANI OPENCASST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	256.54	03/2019 -	03/2022	36	-
43	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	-
44	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	473.22	204.84	03/2015 -	03/2023	96	-
	<u>South-Eastern Coal Fields Limited</u>								
45	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 459.49	459.49	200.47	03/2015 03/2020	03/2022	84	24
46	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATISGARH	06/2010	11,816.40 -	11,816.40	4,645.12	03/2023 03/2016	03/2023	0	84
47	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	232.34	03/2014 -	03/2023	108	-
48	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	-
49	AMGAON OPENCASST PROJECT RCE - [N06000135]SECL, CHHATISGARH	07/2015	316.10 -	316.10	149.09	03/2020 -	03/2023	36	-
50	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	68.86	03/2021 -	03/2024	36	-
51	BATURA HIGHWALL PROJECT - [N06000134]SECL, MADHYA PRADESH	07/2015	231.92 -	231.92	1.82	03/2022 -	03/2025	36	-
52	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL, MADHYA PRADESH	03/2016	869.44 -	869.44	129.53	03/2021 -	03/2025	48	-
53	BATURA OCP (2.0 MTY) - [N06000049]SECL, MADHYA PRADESH	08/2015	1,186.64 -	1,186.64	243.93	03/2023 -	03/2026	36	-
54	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	5.95	03/2014 -	03/2026	144	-
55	DURGAPUR OPENCASST PROJECT - [N06000136]SECL, CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	-
56	AMRITDHARA OC PROJECT - [N06000122]SECL, MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2027	48	-
57	MADANNAGAR OPENCASST PROJECT - [N06000140]SECL, CHHATISGARH	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Western Coal Fields Limited</u>								
58	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 327.41	327.41	162.29	03/2019 -	03/2022	36	-
59	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 333.43	333.43	145.94	03/2023 -	03/2024	12	-
	Total		39,974.43 -	43,508.86	14,527.03				
	<u>FERTILISERS</u>								
	<u>National Fertiliser Limited</u>								
60	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	184.57	11/2019 06/2021	12/2021	25	6
	Total		215.92 -	215.92	184.57				
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
61	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	355.00	95.45	11/2020 -	12/2023	37	-
	Total		355.00 -	355.00	95.45				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmhc)</u>								
62	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	19,538.23	05/2015 01/2022	03/2022	82	2
	<u>Steel Authority Of India Limited (Sail)</u>								
63	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	209.03	06/2019 12/2021	02/2022	32	2
64	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	566.58	10/2017 12/2021	11/2022	61	11
	Total		16,821.88 -	23,236.88	20,313.84				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
65	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	206.26	163.25	03/2021 -	12/2021	9	-
66	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	793.01	06/2019 -	02/2022	32	-
67	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA	07/2020	640.00 -	640.00	368.06	12/2021 -	06/2022	6	-
68	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	248.55	142.91	06/2022 -	09/2022	3	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
69	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	260.89	02/2021 -	03/2023	25	-
70	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA	08/2019	1,607.00 -	1,607.00	304.87	08/2022 -	06/2023	10	-
	<u>Chennai Petroleum Corporation Limited</u>								
71	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	315.00	295.84	08/2020 -	12/2021	16	-
	<u>Gas Authority Of India Limited</u>								
72	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,653.50	12/2020 -	01/2022	13	-
73	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 -	1,933.00	1,584.90	12/2020 12/2021	03/2022	15	3
74	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00 -	2,433.00	2,213.00	12/2020 12/2021	03/2022	15	3
75	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00 3,048.00	3,048.00	2,230.20	12/2020 12/2021	03/2022	15	3
76	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	234.40	08/2020 12/2021	03/2022	19	3
77	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	198.90	04/2018 -	06/2022	50	-
78	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	75.63	02/2021 -	10/2022	20	-
79	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	1,008.20	12/2020 12/2021	06/2023	30	18
80	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 3,060.00	3,060.00	2,705.00	12/2021 -	06/2023	18	-
81	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,778.50	12/2012 02/2022	08/2024	140	30
	<u>Hindustan Petroleum Corporation Limited</u>								
82	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	303.40	224.20	03/2021 -	12/2021	9	-
83	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	105.40	07/2020 -	01/2022	18	-
84	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	194.72	06/2020 -	03/2022	21	-
85	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	127.30	06/2020 -	03/2022	21	-
86	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	210.94	128.96	08/2021 -	03/2022	7	-
	<u>Indian Oil Corporation Limited</u>								
87	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU	12/2016	228.00 -	228.00	160.74	11/2021 -	12/2021	1	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
88	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	315.00	228.42	12/2021 08/2021	01/2022	1	5
89	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	178.65	01/2021 06/2021	01/2022	12	7
90	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,225.58	03/2021 12/2021	03/2022	12	3
91	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	606.58	07/2018 05/2021	03/2022	44	10
92	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	279.29	10/2020 01/2022	03/2022	17	2
93	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	167.51	03/2021 09/2021	03/2022	12	6
94	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	360.74	02/2020 10/2021	03/2022	25	5
95	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	399.21	03/2021 12/2021	03/2022	12	3
96	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	883.78	10/2021 -	03/2022	5	-
97	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	105.42	02/2020 06/2021	06/2022	28	12
98	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 207.36	207.36	129.75	04/2020 10/2021	07/2022	27	9
99	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	209.30	01/2021 -	08/2022	19	-
100	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	553.03	10/2017 03/2022	09/2022	59	6
101	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	301.65	04/2021 12/2021	09/2022	17	9
102	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	64.47	12/2019 03/2022	10/2022	34	7
103	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	179.06	08/2021 -	11/2022	15	-
104	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	96.11	- 05/2022	12/2022	-	7
105	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	16.06	07/2022 -	01/2023	6	-
106	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	128.30	04/2022 -	02/2023	10	-
107	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	109.24	04/2022 -	08/2023	16	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]JOCL,TAMIL NADU	10/2020	1,398.00 -	1,398.00	134.42	12/2023 -	01/2024	1	-
109	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]JOCL,TAMIL NADU	10/2020	921.00 -	921.00	5.59	09/2023 -	02/2024	5	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
110	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	543.02	03/2020 11/2020	12/2021	21	13
111	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,789.68	12/2019 04/2021	03/2022	27	11
	<u>Oil & Natural Gas Corporation Limited</u>								
112	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	829.58	12/2020 05/2021	02/2022	14	9
	<u>Oil India Limited</u>								
113	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	510.00	486.90	12/2019 -	12/2021	24	-
114	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 652.10	638.60	399.74	02/2020 -	12/2021	22	-
115	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 222.21	198.00	184.60	08/2020 09/2021	12/2021	16	3
116	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	283.17	10/2020 -	03/2022	17	-
	Total		42,874.55 -	46,573.96	30,831.23				
	POWER								
	<u>Chenab Valley Power Projects [P] Limited</u>								
117	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	4,287.59	617.83	- 08/2024	07/2025	-	11
	<u>National Thermal Power Corporation</u>								
118	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 2,311.89	2,311.89	2,094.59	12/2018 -	01/2022	37	-
119	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	442.03	225.90	04/2021 10/2021	01/2022	9	3
120	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	702.28	586.88	03/2021 11/2021	01/2022	10	2
121	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	16,604.00	05/2018 -	03/2022	46	-
122	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	633.80	530.53	11/2018 -	03/2022	40	-
123	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	382.22	4.15	03/2022 03/2022	05/2022	2	2
124	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	403.62	122.49	06/2021 12/2021	07/2022	13	7
125	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	1,221.73	140.11	07/2022 05/2022	08/2022	1	3

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
126	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	599.99	62.06	07/2022 -	08/2022	1	-
127	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	842.27	92.08	07/2022 -	08/2022	1	-
128	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 10,997.70	10,998.00	9,124.00	11/2020 07/2022	10/2022	23	3
129	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	17,007.00	12,556.00	06/2019 10/2022	09/2023	51	11
130	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	5,326.00	03/2013 12/2021	09/2024	138	33
131	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,667.00	4,771.00	03/2023 -	02/2025	23	-
	<u>Power Grid Corporation Of India Limited</u>								
132	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	259.30	04/2016 12/2017	12/2021	68	48
133	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	236.27	12/2019 09/2021	01/2022	25	4
134	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	262.19	05/2020 08/2021	01/2022	20	5
135	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	480.89	11/2016 12/2021	02/2022	63	2
136	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	157.92	06/2019 11/2021	02/2022	32	3
137	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 12/2020	02/2022	19	14
138	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	90.75	03/2018 -	03/2022	48	-
139	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	3,326.92	12/2018 12/2021	03/2022	39	3
140	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	168.20	07/2019 07/2021	03/2022	32	8
141	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	578.99	05/2017 12/2021	04/2022	59	4
142	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	13,038.20	08/2013 11/2022	05/2023	117	6
	<u>Thdc India Limited</u>								
143	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 4,825.60	4,825.60	4,374.66	02/2016 -	06/2023	88	-
144	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	3,395.52	09/2023 -	08/2024	11	-
	Total		1,06,970.31 -	1,25,705.80	82,326.86				

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Cpwd For Health</u>								
145	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29 -	150.29	70.91	03/2020 -	12/2021	21	-
146	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
147	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
148	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	262.64	05/2018 -	03/2022	46	-
	<u>Nbcc For Health</u>								
149	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	9	-
	Total		2,320.28 -	2,440.28	1,246.14				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
150	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	24	-
151	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	24	-
152	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	12	-
153	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	355.54	03/2022 -	03/2024	24	-
154	ITARSI-NAGPUR (BAL) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	488.43	03/2023 -	03/2024	12	-
155	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	322.26	03/2022 -	03/2024	24	-
156	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	239.26	03/2023 -	03/2024	12	-
	<u>East Central Railways</u>								
157	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	324.29	03/2019 -	03/2022	36	-
158	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	390.00	403.49	03/2021 -	03/2022	12	-
159	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	1,051.33	03/2020 -	03/2023	36	-
160	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,487.37	03/2020 -	03/2024	48	-
161	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	540.73	03/2020 03/2023	12/2024	57	21

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>East Coast Railway</u>								
162	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,195.24	02/2019 -	03/2022	37	-
163	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	224.26	03/2020 -	03/2022	24	-
164	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	193.71	11/2018 -	03/2024	64	-
165	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	769.95	03/2022 03/2024	03/2026	48	24
	<u>Eastern Railways</u>								
166	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	638.35	02/2013 -	03/2024	133	-
167	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	912.61	03/2019 12/2009	03/2025	72	183
168	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228	-
169	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	453.42	03/2022 -	03/2025	36	-
170	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	618.75	03/2016 -	03/2025	108	-
171	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	96	-
172	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	201.29	03/2016 -	03/2025	108	-
173	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	507.59	03/2017 -	03/2025	96	-
174	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240	-
175	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	142.05	02/2012 -	03/2025	157	-
176	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	109.63	03/2014 -	03/2025	132	-
177	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
178	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	45	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
179	GEVRA ROAD PENDRA ROAD - [N22000488]JRCON, CHHATISGARH	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	18	-
	<u>North Central Railway</u>								
180	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR, UTTAR PRADESH	04/2015	668.70 668.00	680.00	531.20	03/2020 -	01/2022	22	-
181	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	76.74	03/2023 -	06/2025	27	-
182	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	2,030.50	-	- 04/2010	12/2027	-	212
	<u>North East Frontier Railway</u>								
183	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,936.64	12/2008 -	12/2021	156	-
184	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	1,873.21	1,586.23	03/2021 -	03/2022	12	-
185	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	373.87	333.46	- 12/2021	06/2022	-	6
186	NEW B.G. LINE FROM TETELIA TO BYRNihat (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	1,043.00	919.48	03/2019 -	03/2023	48	-
187	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	2,950.00	1,939.39	03/2022 -	03/2023	12	-
188	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 5,021.45	6,527.00	4,525.01	03/2014 -	12/2023	117	-
189	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	446.24	03/2019 -	12/2023	57	-
190	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	2,145.00	1,029.65	03/2019 -	03/2024	60	-
191	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	6,663.00	1,420.48	03/2015 -	03/2026	132	-
	<u>North Eastern Railway</u>								
192	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	213.35	72.08	04/2016 -	12/2021	68	-
193	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	610.00	595.91	01/2019 -	02/2022	37	-
194	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER, UTTAR PRADESH	04/2016	600.00 600.00	366.71	332.87	01/2022 -	03/2022	2	-
195	ETAH - KASGANJ - NEW LINE - [N22000462]NER, UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
196	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER, UTTAR PRADESH	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	66	-
197	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER, UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
	<u>North Western Railway</u>								
198	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	860.41	769.95	02/2019 -	06/2022	40	-
199	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	701.81	334.01	03/2020 -	10/2022	31	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
200	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	413.98	08/2022 -	11/2022	3	-
	<u>Northern Railway</u>								
201	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	26,237.89	11/2002 -	12/2022	241	-
202	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,017.96	878.49	07/2012 -	11/2024	148	-
203	MANSABHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	-
	<u>Rail Vikas Nigam Ltd.</u>								
204	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	872.65	942.56	03/2021 -	12/2021	9	-
205	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	839.78	03/2016 -	12/2021	69	-
206	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,900.00	2,041.94	03/2020 -	12/2021	21	-
207	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	2,156.59	03/2020 -	12/2021	21	-
208	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,364.39	03/2020 -	12/2021	21	-
209	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	2,355.40	12/2020 -	12/2021	12	-
210	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	2,201.29	12/2021 -	03/2022	3	-
211	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	3,753.96	03/2020 -	03/2022	24	-
212	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,894.70	02/2015 -	06/2022	88	-
213	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,438.92	03/2019 -	06/2022	39	-
214	BANASPAANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,269.37	03/2019 -	06/2022	39	-
215	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,111.90	03/2022 -	06/2022	3	-
216	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,509.71	03/2020 -	06/2022	27	-
217	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,777.07	12/2020 -	12/2022	24	-
218	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	982.28	03/2022 -	12/2024	33	-
219	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,089.92	03/2023 -	12/2024	21	-
220	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	3,317.94	03/2016 -	03/2025	108	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,460.93	03/2016 -	03/2025	108	-
222	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	22,716.11	5,917.58	12/2024 -	03/2025	3	-
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-
224	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	3,327.72	2,024.04	12/2024 -	12/2026	24	-
	<u>South Central Railway</u>								
225	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTI STATE	04/2010	704.31 927.94	927.94	691.26	03/2020 -	02/2022	23	-
226	MUNEERABAD-MAHABOONNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,010.00	03/2000 -	03/2023	276	-
227	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,042.28	03/2009 -	03/2024	180	-
228	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48 -	1,373.74	654.79	03/2010 -	03/2024	168	-
229	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 -	1,952.68	729.57	03/2023 -	03/2024	12	-
230	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	2,063.03	1,613.72	03/2021 -	03/2024	36	-
231	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,388.38	03/2022 -	03/2024	24	-
232	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	156	-
	<u>South Eastern Railway</u>								
233	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA	11/2015	969.83 -	1,312.96	1,119.38	03/2020 -	06/2022	27	-
234	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER, JHARKHAND	04/2018	390.39 -	511.75	110.13	12/2021 -	06/2022	6	-
235	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER, WEST BENGAL	04/2018	338.00 -	393.83	22.39	06/2022 -	06/2023	12	-
236	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER, JHARKHAND	03/2016	1,724.20 -	1,724.20	1,097.56	03/2021 -	12/2023	33	-
237	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER, MULTI STATE	03/2019	1,866.31 -	1,866.31	288.29	05/2023 -	12/2023	7	-
238	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
239	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER, JHARKHAND	04/2018	428.65 -	472.50	1.61	06/2022 -	12/2025	42	-
240	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
241	HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA	03/2015	1,156.94 -	1,954.21	1,205.02	03/2020 -	03/2023	36	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
242	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	36.97	03/2016 -	12/2023	93	-
243	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2024	264	-
244	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
245	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	1,878.00	1,496.77	03/2019 -	03/2024	60	-
246	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	732.89	495.11	03/2017 -	03/2025	96	-
247	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	387.33	12/2018 -	06/2025	78	-
248	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	1,530.09	325.32	03/2016 -	12/2026	129	-
	<u>Southern Railway</u>								
249	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	608.13	427.75	- 12/2021	02/2022	-	2
250	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	749.40	578.46	- 12/2021	03/2022	-	3
251	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,122.00	994.02	- 09/2021	12/2022	-	15
252	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,549.09	712.68	03/2020 -	03/2025	60	-
253	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,081.20	1,718.56	02/2019 -	03/2025	73	-
254	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
255	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	308.35	03/2019 -	12/2027	105	-
256	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	133	-
257	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	991.83	922.01	03/2005 -	12/2021	201	-
	<u>West Central Railway</u>								
258	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	15	-
259	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	540.13	03/2022 -	12/2023	21	-
260	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	1,345.52	03/2020 -	03/2024	48	-
261	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202	-
	<u>Western Railway</u>								
262	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	21	-
263	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,042.12	730.07	03/2021 -	12/2022	21	-

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
264	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 -	6,171.08	2,327.60	03/2022 -	03/2023	12	-
265	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 -	495.18	.33	03/2022 -	03/2024	24	-
	Total		1,51,388.09 -	2,53,363.23	1,36,299.45				
	ROAD TRANSPORT AND HIGHWAYS								
	Ministry Of Road Transport And Highways (State Pwds)								
266	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	238.66	09/2019 09/2021	12/2021	27	3
267	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	237.81	09/2020 -	12/2021	15	-
268	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	457.34	01/2020 06/2021	01/2022	24	7
269	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 927.73	927.73	773.30	02/2020 08/2021	01/2022	23	5
270	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	231.61	03/2018 11/2021	01/2022	46	2
271	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	635.00	07/2018 05/2021	01/2022	42	8
272	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 949.54	949.54	794.73	06/2019 04/2021	01/2022	31	9
273	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	02/2022	47	4
274	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 174.90	174.90	154.26	08/2018 08/2021	02/2022	42	6
275	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	132.76	02/2018 09/2021	02/2022	48	5
276	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	133.46	03/2017 12/2021	02/2022	59	2
277	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	182.97	08/2018 09/2021	02/2022	42	5
278	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	167.53	03/2018 10/2021	02/2022	47	4
279	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	219.86	07/2018 08/2021	02/2022	43	6

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
280	BALANCE WORK FOR REHABILITATION AND UPGADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	404.69	03/2018 06/2021	02/2022	47	8
281	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	160.00	133.51	09/2021 -	02/2022	5	-
282	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	297.87	- 03/2021	03/2022	-	12
283	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	120.51	11/2018 01/2021	03/2022	40	14
284	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	139.54	03/2021 11/2021	03/2022	12	4
285	REHABILITATION AND UPGADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.89	04/2020 -	03/2022	23	-
286	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	19	-
287	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	67.54	03/2018 03/2022	04/2022	49	1
288	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	207.79	108.34	03/2021 -	04/2022	13	-
289	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	80.06	03/2018 09/2021	06/2022	51	9
290	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	27.15	08/2019 -	11/2022	39	-
291	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	409.70	08/2017 06/2021	12/2022	64	18
292	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	24.49	05/2021 -	12/2022	19	-
293	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	6.94	03/2021 -	03/2023	24	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
294	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	113.03	06/2018 -	12/2021	42	-
295	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	179.86	06/2018 -	12/2021	42	-
296	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	289.99	100.00	12/2018 -	12/2021	36	-
297	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	-	11
298	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	315.03	120.99	09/2018 -	12/2021	39	-
299	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	240.64	125.87	09/2018 -	12/2021	39	-
300	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	77.62	09/2018 -	12/2021	39	-
301	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	154.83	11/2017 -	12/2021	49	-
302	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	200.44	128.02	- 08/2021	12/2021	-	4
303	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	588.95	516.16	11/2018 -	02/2022	39	-
304	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	372.30	05/2018 -	03/2022	46	-
305	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	229.20	01/2016 -	03/2022	74	-
306	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	139.69	01/2016 -	03/2022	74	-
307	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	182.01	04/2017 03/2021	03/2022	59	12

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
308	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	252.79	153.14	04/2017 -	03/2022	59	-
309	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	263.31	155.10	04/2017 -	03/2022	59	-
310	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	252.05	157.83	04/2017 -	03/2022	59	-
311	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL, UTTARAKHAND	03/2018	274.31 -	274.31	131.95	05/2018 -	03/2022	46	-
312	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL, UTTARAKHAND	03/2018	403.36 -	403.36	220.25	06/2018 -	03/2022	45	-
313	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL, UTTARAKHAND	03/2018	417.24 -	417.24	265.48	05/2018 -	03/2022	46	-
314	2 LANE WITH HARD SHOULDER, REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51	12
315	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS	02/2018	391.00 -	391.00	77.75	10/2018 -	03/2022	41	-
316	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL, A & N ISLANDS	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41	18
317	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00 -	387.00	333.24	09/2018 -	03/2022	42	-
318	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	-
319	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL, MEGHALAYA	03/2019	306.28 -	306.28	133.81	05/2019 -	03/2022	34	-
320	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL, ARUNACHAL PRADESH	09/2016	568.92 -	568.92	335.59	- 11/2021	03/2022	-	4
321	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL, ARUNACHAL PRADESH	12/2016	188.78 -	188.78	118.08	- 03/2021	03/2022	-	12

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
322	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	239.30	128.80	09/2018 -	05/2022	44	-
323	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	182.63	09/2018 -	07/2022	46	-
324	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	299.10	07/2018 -	07/2022	48	-
325	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	100.70	09/2018 -	09/2022	48	-
326	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	68.70	09/2018 -	10/2022	49	-
327	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	132.56	09/2018 -	11/2022	50	-
328	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	98.33	09/2019 -	04/2023	43	-
329	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	115.64	09/2019 04/2023	06/2023	45	2
330	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	137.11	09/2019 04/2023	06/2023	45	2
331	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	107.05	09/2019 06/2023	07/2023	46	1
332	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	51.36	09/2019 03/2024	04/2024	55	1
<u>National Highways Authority Of India</u>									
333	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 1,928.22	1,928.22	1,890.04	04/2015 01/2021	12/2021	80	11
334	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	12/2021	44	-

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
335	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	403.81	07/2018 -	12/2021	41	-
336	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29	-
337	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29	-
338	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	1,183.14	- 10/2021	12/2021	-	2
339	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	252.08	03/2020 -	12/2021	21	-
340	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	403.81	07/2016 -	12/2021	65	-
341	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	718.56	09/2017 11/2021	12/2021	51	1
342	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	763.00	12/2019 -	12/2021	24	-
343	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	01/2022	101	-
344	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	97.97	04/2014 -	01/2022	93	-
345	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	1,020.25	11/2018 -	01/2022	38	-
346	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	434.59	08/2018 -	01/2022	41	-
347	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	81.67	05/2013 -	02/2022	105	-
348	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	341.21	08/2017 -	02/2022	54	-
349	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,641.30	03/2013 -	03/2022	108	-
350	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36	-
351	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	23	-
352	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	474.80	- 01/2022	04/2022	-	3

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
353	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	570.00	03/2020 -	04/2022	25	-
354	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	605.00	05/2020 -	05/2022	24	-
355	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	238.84	03/2019 12/2021	06/2022	39	6
356	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59	-
357	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	810.81	09/2017 -	07/2022	58	-
358	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	449.44	03/2020 -	09/2022	30	-
359	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	-
360	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	32.96	12/2017 -	05/2023	65	-
361	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,893.57	08/2013 -	06/2023	118	-
362	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	348.00	03/2019 12/2022	06/2023	51	6
	Total		54,602.41 -	54,585.92	38,010.77				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
363	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	422.87	70.25	06/2021 11/2021	03/2022	9	4
	<u>Cpwd For Telecom</u>								
364	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20 -	248.20	155.97	03/2018 -	01/2022	46	-
	<u>Department Of Telecommunication</u>								
365	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	24,664.00	20,545.00	07/2015 05/2020	03/2022	80	22
	Total		14,013.36 -	25,335.07	20,771.22				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
366	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	9,834.10	12/2018 -	08/2022	44	-
	<u>Central Public Works Department</u>								

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
367	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	1,128.00	30.00	03/2022 -	06/2023	15	-
	<u>Lucknow Metro Rail Corporation Limited</u>								
368	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	2,391.78	03/2024 -	03/2025	12	-
369	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	506.47	03/2024 -	05/2025	14	-
	Total		31,357.10 -	33,371.10	12,762.35				
	<u>WATER RESOURCES</u>								
	<u>Brahmaputra Board</u>								
370	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	233.57	148.83	12/2019 -	12/2021	24	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
371	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	191.62	65.53	11/2020 03/2021	12/2021	13	9
372	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	398.90	294.30	03/2020 -	02/2022	23	-
373	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	268.63	338.67	01/2021 -	03/2022	14	-
374	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	230.06	98.70	07/2021 -	04/2022	9	-
375	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	356.37	137.32	04/2021 -	04/2022	12	-
376	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	277.42	247.01	05/2021 -	06/2022	13	-
377	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	236.15	60.61	12/2020 06/2021	07/2022	19	13
378	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	578.89	42.75	06/2022 -	12/2022	6	-
379	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	824.00	96.39	06/2022 -	12/2022	6	-
380	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	28.31	08/2021 -	04/2023	20	-
381	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	294.02	26.45	10/2021 -	12/2023	26	-
382	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	413.29	.05	09/2020 -	03/2024	42	-
	<u>Delhi Jal Board</u>								
383	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	515.07	345.58	01/2021 -	12/2021	11	-
384	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	108.28	12/2021 -	12/2022	12	-

Costing Rs. 150 Crore and above

(December 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
385	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	160.52	02/2022 -	12/2022	10	-
	<u>Kolkata Metropolitan Development Authority</u>								
386	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	272.32	253.59	04/2020 -	03/2022	23	-
387	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	185.22	11.56	12/2021 -	09/2023	21	-
388	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	172.10	11.56	12/2021 -	09/2023	21	-
389	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	164.93	11.56	12/2021 -	09/2023	21	-
390	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022 -	03/2024	25	-
391	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	165.16	-	06/2022 -	03/2024	21	-
392	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022 -	03/2024	25	-
393	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	384.96	-	04/2022 -	04/2024	24	-
394	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	287.53	-	04/2022 -	04/2024	24	-
395	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	234.31	-	04/2022 -	04/2024	24	-
396	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	307.12	-	09/2022 -	04/2024	19	-
	<u>Polavaram Project Authority</u>								
397	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	18,335.60	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								
398	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP Jal Nigam, UTTAR PRADESH	03/2018	967.23 -	967.23	96.64	09/2021 -	12/2021	3	-
399	MATHURA SEWERAGE SCHEME - [N30000019]UP Jal Nigam, UTTAR PRADESH	12/2017	460.45 -	460.45	248.16	12/2020 -	12/2021	12	-
400	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP Jal Nigam, UTTAR PRADESH	05/2017	767.59 -	767.59	132.29	09/2021 -	03/2022	6	-
401	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP Jal Nigam, UTTAR PRADESH	01/2019	206.05 -	206.05	80.97	10/2021 -	03/2022	5	-

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
402	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH	01/2019	231.79 -	234.03	28.36	12/2021 -	12/2022	12	-
403	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH	03/2019	271.39 -	271.39	-	08/2021 -	03/2024	31	-
404	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	03/2024	32	-
405	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH	10/2017	213.62 261.12	261.12	-	03/2022 -	04/2024	25	-
406	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	22	-
	Uttarakhand Pey Jal Nigam								
407	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	158.00	85.01	11/2019 03/2021	03/2022	28	12
	Total		22,180.93 -	67,906.50	21,494.60				
	DEFENCE PRODUCTION								
	Cpwd For Defence								
408	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD FOR DEFENC,KARNATAKA	12/2016	246.31 210.00	210.00	158.92	02/2020 10/2021	03/2022	25	5
	Total		246.31 -	210.00	158.92				
	DEPARTMENT OF HIGHER EDUCATION								
	Cpwd Of Higher Education								
409	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA	01/2018	223.37 -	223.37	117.64	07/2020 -	12/2021	17	-
410	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR	02/2016	496.18 496.00	498.99	301.90	06/2017 -	03/2022	57	-
411	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83 -	193.83	51.77	06/2020 -	03/2022	21	-
412	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB	01/2018	430.00 -	387.83	237.59	05/2020 -	06/2022	25	-
413	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA	01/2019	790.79 -	790.79	258.32	03/2022 -	06/2022	3	-
414	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	424.93	80.19	07/2022 -	10/2022	3	-

Costing Rs. 150 Crore and above

(December 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
415	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	808.62	296.89	07/2022 -	10/2022	3	-
416	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	34.60	05/2022 -	10/2022	5	-
417	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION,KARNATAKA	07/2019	851.00 851.00	851.00	324.03	03/2022 -	10/2022	7	-
418	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	375.00	125.38	09/2020 -	11/2022	26	-
419	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	216.78	03/2021 -	02/2023	23	-
	Total		5,695.59 -	5,656.23	2,045.09				
	HOME AFFAIRS								
	Cpwd For Mha								
420	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 -	2,000.00	1,049.80	10/2019	05/2022	31	-
	Total		1,219.21 -	2,000.00	1,049.80				
	Grand Total		5,69,529.73	7,77,729.89	4,51,806.71				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(December 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	6,840.00	09/2010	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00	16,580.00	12/2015	12/2022	44.69	84
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00	17,079.00	12/2016	12/2023	38.63	84
	Total		27,271.00	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27	480.33	09/2021	06/2023	38.72	21
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00	1,232.00	03/2021	03/2023	7.88	24
	Total		1,488.27	1,712.33				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73	5,146.48	08/2019	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>							
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53	808.97	03/2013	03/2024	68.70	132
	<u>Neyveli Lignite Corporation</u>							
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00	17,237.80	11/2021	11/2022	.00	12
	<u>Singareni Colliers Company Limited</u>							
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76	349.28	03/2015	03/2022	114.60	84
10	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09	442.42	03/2019	03/2022	11.42	36

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2023	5.85	96
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>Western Coal Fields Limited</u>							
13	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	03/2022 -	03/2025	.00	36
	Total		22,093.43 -	25,237.09				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	09/2020 -	-	10.22	0
15	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	03/2022	.57	57
16	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	-	1.85	0
	Total		1,231.49 -	1,263.46				
	<u>DPIIT</u>							
	<u>Dmic For Dpiit</u>							
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	09/2019 -	07/2021	9.80	22
	<u>licc For Dpiit</u>							
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	05/2022	8.49	29
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Cpwd For Health</u>							
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	09/2025 -	09/2025	15.92	0
	<u>Hospital Services Consultancy Corporation Ltd</u>							
20	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	03/2021	16.33	37
21	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	- -	12/2021	21.58	0

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
22	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR [N21000010]	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20	26
23	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64	8
24	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	01/2021	.02	0
25	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29	46
26	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13	24
27	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32
28	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR [N21000011]	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71	18
29	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003] <u>Nbcc For Health</u>	02/2013	414.11 -	586.50	11/2013 -	09/2021	41.63	94
30	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	09/2021 -	06/2022	8.88	9
	Total		5,589.39 -	6,374.57				
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	05/2022	64.04	31
	Total		1,219.21 -	2,000.00				
	<u>PETROLEUM</u>							
	<u>Hindustan Petroleum Corporation Limited</u>							
32	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	06/2021 -	07/2022	14.76	13
	<u>Oil & Natural Gas Corporation Limited</u>							
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.34	05/2013 -	05/2022	132.23	108
	Total		3,538.79 -	5,073.34				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
34	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	10/2021 -	10/2022	11.93	12
35	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	06/2019	401.90 -	442.03	04/2021 -	01/2022	9.99	9
36	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 -	524.83	09/2021 -	10/2022	4.70	13
37	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 -	852.90	09/2021 -	08/2022	6.85	11
38	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95	0
39	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	09/2019 -	12/2024	30.48	63
40	NOKHRA - [N18000282]	03/2020	1,722.14 -	1,803.19	09/2021 -	10/2022	4.71	13
41	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41	0
42	TELANGANA SUPER THERMAL POWER PROJECT PHASE I [N18000212]	01/2016	10,598.98 -	10,998.00	11/2020 -	10/2022	3.76	23
43	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	06/2019 -	09/2023	18.38	51
	<u>Power Grid Corporation Of India Limited</u>							
44	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	07/2020 -	02/2022	14.11	19
	<u>Satluj Jal Vidyut Nigam Limited</u>							
45	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	12/2021 -	06/2022	46.20	6
	Total		39,946.06 -	45,018.94				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
46	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	325.00	03/2019 -	-	76.57	0
47	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	03/2022 -	03/2023	.89	12
48	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	03/2021 -	03/2023	75.00	24
49	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94	0
50	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.49	03/2024 -	-	25.04	0
51	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	03/2023 -	03/2023	8.75	0
52	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2023	.00	-12

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
53	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181	02/1997	2,271.50 -	4,794.60	03/2021 -	03/2023	111.08	24
54	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28	0
	<u>Container Corporation Of India</u>							
55	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	03/2019 -	-	.21	0
56	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	01/2013	387.70 -	487.13	03/2018 -	-	25.65	0
	<u>East Central Railways</u>							
57	GARHWA ROAD-RAMNA - [N22000465	03/2015	348.23 -	390.00	03/2021 -	03/2022	11.99	12
58	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00 -	519.33	-	03/2025	36.67	0
59	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 -	549.75	-	-	32.26	0
60	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15 -	560.09	07/2014 -	-	68.63	0
61	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	03/2020 -	12/2024	49.45	57
62	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	03/2019 -	12/2021	37.04	33
63	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	-	-	376.78	0
64	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,080.00	03/2012 -	11/2022	232.58	128
65	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	-	03/2022	350.27	0
66	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	-	03/2023	391.01	0
67	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	-	03/2024	818.15	0
68	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	03/1999	1,033.07 -	3,650.00	-	03/2022	253.32	0
	<u>East Coast Railway</u>							
69	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	11/2018 -	03/2024	15.45	64
70	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43	37
	<u>Eastern Railways</u>							
71	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	-	03/2025	51.19	0
72	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	-	03/2022	6.48	0

Costing Rs. 150 Crore and above					(December 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 -	298.22	- -	03/2025	.25	0
74	MONIGRAM- NIMITTA - [N22000301	04/2012	250.93 -	310.70	- -	03/2024	23.82	0
75	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
76	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	03/2017 -	03/2025	20.30	96
77	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
78	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	- -	03/2022	181.63	0
79	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	502.48	- -	03/2021	74.26	0
80	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	- -	03/2025	44.46	0
81	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
82	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
83	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
84	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
85	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 -	1,261.34	- -	03/2025	180.30	0
86	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
87	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
88	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
89	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,055.15	09/2018 -	06/2022	.00	45
90	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	09/2023	117.23	18
	<u>Metropolitan Rapid Transport Projects</u>							

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
91	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP [N22000028]	04/2006	495.74 -	774.51	06/2013 -	07/2022	56.23	109
92	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	06/2022	501.57	219
93	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37	0
94	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	-	75.91	0
	<u>North Central Railway</u>							
95	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	01/2022	1.69	22
96	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
97	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	-	7.86	0
98	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	- -	06/2022	54.80	0
99	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62	0
100	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
101	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	-	106.51	0
102	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	03/2020 -	06/2022	30.26	27
103	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	03/2020 -	-	80.79	0
104	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,043.00	03/2019 -	03/2023	170.77	48
105	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,090.60	- -	-	33.13	0
106	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	04/2010 -	-	186.55	0
107	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	1,167.00	12/2021 -	10/2021	93.77	-2
108	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	03/2021 -	03/2022	115.07	12
109	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2024	302.54	60

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
110	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15	12
111	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	03/2021 -	-	350.44	0
112	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266	04/2000	1,180.19 -	4,541.38	12/2008 -	12/2021	284.80	156
113	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	6,527.00	03/2014 -	12/2023	172.70	117
114	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 -	6,663.00	03/2015 -	03/2026	186.39	132
115	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	8,600.00	12/2015 -	12/2023	542.04	96
116	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	14,322.00	03/2011 -	12/2023	221.54	153
<u>North Eastern Railway</u>								
117	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00 -	213.35	04/2016 -	12/2021	.16	68
118	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	-	-	60.34	0
119	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459	04/2017	150.00 -	341.66	04/2017 -	10/2022	127.77	66
120	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	610.00	01/2019 -	02/2022	106.78	37
121	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136	03/2013	643.00 -	644.00	-	-	.16	0
122	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50 -	800.00	-	12/2023	32.78	0
123	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13	0
124	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15	0
125	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	1,409.09	-	-	358.99	0
126	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	03/2015	1,295.42 -	1,824.00	03/2022 -	03/2022	40.80	0
<u>North Western Railway</u>								
127	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152	04/2013	420.18 -	480.00	03/2020 -	09/2021	14.24	18
128	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	701.81	03/2020 -	10/2022	16.97	31
129	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	860.41	02/2019 -	06/2022	109.82	40

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
130	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	2,215.27	- -	-	153.55	0
131	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	- -	-	104.65	0
	<u>Northern Railway</u>							
132	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
133	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
134	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	- -	09/2023	134.90	0
135	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	839.00	03/2016 -	-	34.24	0
136	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	- -	03/2024	310.24	0
137	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	06/2021	211.31	114
138	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	03/2023 -	12/2025	369.35	33
139	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	07/2012 -	11/2024	348.44	148
	<u>Rail Vikas Nigam Ltd.</u>							
140	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	03/2009 03/2009	-	224.56	0
141	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
142	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	12/2021	35.42	9
143	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15	69
144	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98	33
145	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2022	51.02	39
146	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	03/2020 -	06/2022	102.11	27
147	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	03/2019 -	06/2022	62.89	39
148	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,650.00	12/2021 -	12/2021	69.12	0
149	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	12/2020 -	12/2022	54.24	24
150	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	12/2020 -	12/2021	23.55	12

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
151	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68	3
152	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	03/2020 -	12/2021	111.91	21
153	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
155	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,900.00	03/2020 -	12/2021	306.46	21
156	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04	-3
157	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
158	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58	24
159	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
160	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22	108
162	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62	-12
163	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08	3
	<u>Railway Electrification</u>							
164	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77	0
	<u>South Central Railway</u>							
165	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	242.28	03/2022 -	-	102.36	0
166	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	1,373.74	03/2010 -	03/2024	18.38	168
167	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
168	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2024	102.85	180
169	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86	0
170	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	03/2014 -	03/2027	42.44	156

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
171	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
172	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>							
173	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
	<u>South Eastern Railway</u>							
174	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	266.61	03/2015 -	03/2019	77.86	48
175	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510	04/2018	338.00 -	393.83	06/2022 -	06/2023	16.52	12
176	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508	04/2018	428.65 -	472.50	06/2022 -	12/2025	10.23	42
177	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509	04/2018	390.39 -	511.75	12/2021 -	06/2022	31.09	6
178	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	- -	03/2025	131.89	0
179	DIGHA-JALESWAR INCLUDING MM FOR DIGHA- EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
180	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76	0
181	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	03/2020 -	06/2022	35.38	27
182	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
183	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	04/2013	327.25 -	367.77	- -	12/2023	12.38	0
184	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	- -	12/2023	57.65	0
185	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL [N22000276	04/2013	558.00 -	692.43	- -	12/2023	24.09	0
186	ARSIKERE-TUMKUR - [N22000332	03/2015	578.00 -	760.00	03/2020 -	01/2022	31.49	22
187	YELAHANKA-PENUKONDA - [N22000328	05/2015	860.43 -	1,104.00	03/2020 -	09/2021	28.31	18
188	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	1,382.78 -	1,383.00	03/2002 -	03/2024	.02	264
189	BAGALKOT-KUDACHI NL - [N22000258	04/2010	986.30 -	1,530.09	03/2016 -	12/2026	55.13	129
190	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,878.00	03/2019 -	03/2024	16.31	60
191	HUBLI- CHIKJAJUR - [N22000325	03/2015	1,156.94 -	1,954.21	03/2020 -	03/2023	68.91	36

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
192	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	2,161.36	- -	12/2023	20.01	0
193	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,404.03	- -	12/2025	16.57	0
194	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	- -	12/2024	123.51	0
	<u>Southern Railway</u>							
195	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	448.10	- -	03/2025	136.79	0
196	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	02/2019 -	03/2030	247.32	133
197	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.23	- -	03/2030	109.04	0
198	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	608.13	- -	02/2022	269.89	0
199	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	709.69	- -	03/2025	180.55	0
200	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	749.40	- -	03/2022	177.41	0
201	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	839.01	- -	03/2030	.00	0
202	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	991.83	03/2005 -	-	268.89	201
203	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,122.00	- -	12/2022	20.39	0
204	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	- -	03/2030	130.17	0
205	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	- -	03/2025	33.90	0
206	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,549.09	03/2020 -	03/2025	409.60	60
207	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	03/2019 -	12/2027	1,699.64	105
208	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80	0
209	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	3,081.20	02/2019 -	03/2025	325.17	73
210	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,154.43	- -	12/2025	441.23	0
	<u>West Central Railway</u>							
211	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,875.12	03/2022 -	06/2023	16.02	15
212	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>							

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
213	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504	04/2017	692.25 -	742.88	03/2020 -	03/2024	7.31	48
214	SURENDRA NAGAR RAJKOT - [N22000392	04/2015	1,002.39 -	1,042.12	03/2021 -	12/2022	3.96	21
215	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH- KODINAR (GC) - [N22000143	04/1994	320.66 -	1,378.11	03/2019 -	03/2023	329.77	48
216	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	1,037.15 -	1,383.69	03/2021 -	12/2022	33.41	21
217	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	2,223.37	03/2020 -	03/2024	167.96	48
218	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	6,171.08	03/2022 -	03/2023	76.13	12
	Total		1,84,953.87 -	3,42,235.05				
	ROAD TRANSPORT AND HIGHWAYS							
	Ministry Of Road Transport And Highways (State Pwds)							
219	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	-	.00	0
220	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	-	.00	0
221	WADIGODRI TO DHANGRIPIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	-	.00	0
222	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	-	.00	0
223	REHABILITATION AND UPGRADATION OF KABRAI- BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	10/2019	.00	1
224	DHANGRIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	-	.00	0
225	MANGRUPHIR TO MAHAN - [N24001087	03/2018	222.13 222.00	222.13	11/2019 -	-	.00	0
226	KUNDRAI TO WAZAR - [N24001077	01/2018	225.25 225.00	225.25	12/2019 -	-	.00	0
227	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	08/2018 -	02/2022	4.45	42
228	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	-	.00	0
229	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	03/2018	228.32 -	228.32	08/2018 -	-	.00	0
230	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 -	236.18	12/2022 -	12/2022	19.48	0

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
231	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	10/2021	.08	23
232	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	-	.00	0
233	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	03/2021	.00	14
234	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239	03/2018	240.38 -	240.38	06/2019 -	-	.00	0
235	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00	244.04	03/2019 -	-	.00	0
236	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	-	.00	0
237	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00	264.41	03/2019 -	-	.00	0
238	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	-	.00	0
239	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	03/2018	289.67 290.00	289.67	08/2018 -	-	.00	0
240	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	-	3.72	0
241	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31	0
242	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	-	.00	0
243	MALEGAON TO RISOD - [N24001089	02/2018	303.24 303.00	303.24	12/2019 -	-	.00	0
244	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161	12/2017	297.30 -	318.28	01/2019 -	-	7.06	0
245	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 -	319.96	- -	03/2022	13.68	0
246	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	-	72.36	0
247	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.00	0
248	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J - [N24001208	03/2018	288.30 -	323.36	08/2020 -	03/2022	12.16	19
249	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	-	.00	0
250	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
251	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00	341.16	06/2019 -	-	.00	0
252	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00	344.25	08/2020 -	-	.00	0
253	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00	344.85	12/2019 -	-	.00	0
254	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	0
255	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	353.43	12/2015 -	-	6.07	0
256	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	369.77	- -	-	15.67	0
257	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]	09/2016	372.68 -	372.68	02/2017 -	-	.00	0
258	SHEGAON TO DEORI PHATA - [N24001010]	02/2017	373.10 373.00	373.10	05/2019 -	-	.00	0
259	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00	381.08	05/2020 -	-	.00	0
260	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]	01/2016	386.09 -	386.09	05/2016 -	-	.00	0
261	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	03/2018	325.86 -	386.41	10/2018 -	-	18.58	0
262	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	05/2017 -	05/2022	45.75	60
263	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00	391.06	06/2019 -	-	.00	0
264	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00	393.10	12/2019 -	-	.00	0
265	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00	404.33	05/2020 -	-	.00	0
266	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00	407.19	06/2019 -	-	.00	0
267	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]	01/2018	418.03 -	418.03	08/2018 -	-	.00	0
268	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI [N24001056]	02/2017	422.02 422.00	422.02	07/2019 -	-	.00	0
269	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	06/2020 -	-	.00	0
270	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]	02/2017	429.43 -	429.43	11/2017 -	-	.00	0

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
271	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06	0
272	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANI KALA TO RENGAPALI ODISHA - [N24001091	03/2016	536.65 356.00	536.65	12/2019 -	02/2022	.00	26
273	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	09/2016 -	03/2022	14.24	66
274	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	-	.00	0
275	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00	743.21	06/2021 -	-	.00	0
276	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75	0
277	PARSHURAM GHAT TO ARAWALI - [N24001133	04/2016	983.14 983.00	983.14	12/2019 -	-	.00	0
278	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	-	.00	0
279	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00	0
280	KALMATH TO ZARAP - [N24001137	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	-	.00	0
281	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	-	.00	0
282	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	- -	-	2.93	0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
283	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258	08/2020	202.36 -	202.36	04/2022 -	04/2022	.00	0
284	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	04/2017 -	03/2022	27.16	59
285	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	04/2017 -	03/2022	29.48	59
286	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	04/2017 -	03/2022	29.48	59
287	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	09/2020	277.44 -	277.44	10/2022 -	10/2022	.00	0
288	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	09/2020	315.63 -	315.63	04/2022 -	04/2022	.00	0

Costing Rs. 150 Crore and above

(December
2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
289	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	08/2016 -	05/2021	3.73	57
290	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30	0
	<u>National Highways Authority Of India</u>							
291	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	-	64.62	0
292	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	- -	-	.99	0
293	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501	08/2015	322.09 -	322.09	04/2018 -	-	.00	0
294	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 -	336.60	08/2018 -	-	3.98	0
295	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	04/2009 -	-	70.23	0
296	SIX LANNING FROM EXISTING KM 494.410 (DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550 (DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	359.60	- -	05/2017	23.69	0
297	CONSTRUCTION OF 4-LANE LADDOVAL BYPASS - [N24000572	05/2016	364.56 -	392.00	- -	04/2021	7.53	0
298	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	04/2014	351.34 -	417.68	01/2016 -	-	18.88	0
299	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	11/2008 -	-	159.95	0
300	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	07/2012	291.36 -	469.31	01/2014 -	-	61.08	0
301	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
302	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594	07/2016	458.03 -	486.00	- -	-	6.11	0
303	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	- -	-	8.26	0
304	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	11/2013 -	-	15.53	0
305	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	11/2019 -	-	2.02	0
306	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	612.58	02/2009 -	-	118.78	0
307	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367	04/2014	495.78 -	627.93	01/2016 -	-	26.66	0
308	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	08/2015	516.13 -	649.27	04/2018 -	-	25.80	0

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
309	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	07/2009 -	-	234.27	0
310	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	- -	-	6.11	0
311	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	-	19.25	0
312	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]	10/2020	724.60 -	724.60	03/2023 -	03/2023	.00	0
313	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]	02/2019	731.89 -	732.34	11/2019 -	-	.06	0
314	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	-	9.38	0
315	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]	10/2019	743.88 -	743.89	- -	12/2021	.00	0
316	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	744.73	05/2018 -	03/2022	40.22	46
317	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	09/2022	.23	30
318	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	03/2018	642.13 -	807.00	- -	-	25.68	0
319	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	- -	10/2021	1.37	0
320	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]	12/2017	656.98 -	840.00	- -	11/2022	27.86	0
321	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]	12/2017	217.96 -	884.00	- -	10/2022	305.58	0
322	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 -	922.64	- -	02/2018	15.98	0
323	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	925.96	- -	02/2018	45.89	0
324	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	04/2020 -	03/2022	3.95	23
325	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	- -	01/2020	11.33	0
326	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	-	31.88	0

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
327	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 -	987.94	- -	-	44.60	0
328	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	- -	-	21.50	0
329	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	-	5.56	0
330	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	-	3.40	0
331	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06	0
332	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,071.00	- -	01/2022	5.32	0
333	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 - [N24000623]	09/2016	1,100.19 -	1,145.31	- -	-	4.10	0
334	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	-	5.70	0
335	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	-	41.54	0
336	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	- -	-	1.33	0
337	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	-	13.97	0
338	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 -	1,197.00	- -	-	29.35	0
339	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44	0
340	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 -	1,296.00	- -	11/2021	.12	0
341	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 -	1,296.93	- -	01/2022	11.20	0
342	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,300.00	09/2017 -	-	15.65	0
343	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	0
344	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0

Costing Rs. 150 Crore and above

(December 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
345	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,361.00	- -	-	29.35	0
346	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	-	10.24	0
347	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
348	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
349	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	1,588.29	09/2019 -	-	14.40	0
350	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
351	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH- [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09	0
352	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	06/2020 -	-	1.78	0
353	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	12/2021	4.99	0
354	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 -	2,280.00	- -	-	94.94	0
355	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 -	2,360.65	- -	-	41.78	0
356	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28	0
357	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	-	18.50	0
358	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50	0
359	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	07/2021	63.05	4
360	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
361	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84	0
362	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		95,972.54 -	1,12,468.39				

Costing Rs. 150 Crore and above

(December
2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>STEEL</u>							
	<u>Rastriya Ispat Nigam Limited</u>							
363	FORGED WHEEL PLANT - [N12000116	04/2014	1,682.85 -	2,100.00	09/2018 -	09/2021	24.79	36
	Total		1,682.85 -	2,100.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
364	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	12/2018 -	08/2022	18.69	44
	<u>Mumbai Metro Rail Corporation Ltd</u>							
365	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	33,406.00	03/2020 -	03/2023	44.39	36
	<u>Patna Metro Rail Corporation</u>							
366	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	02/2019	13,365.77 -	13,925.50	06/2024 -	06/2024	4.19	0
	Total		47,274.77 -	60,118.50				
	<u>WATER RESOURCES</u>							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
367	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	398.90	03/2020 -	02/2022	76.68	23
368	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027	10/2017	254.13 -	413.29	09/2020 -	03/2024	62.63	42
	<u>Uttar Pradesh Jal Nigam</u>							
369	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 -	234.03	12/2021 -	12/2022	.97	12
370	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	02/2019	681.78 -	690.71	06/2022 -	04/2024	1.31	22
	Total		1,393.47 -	1,736.93				
	Grand Total		4,51,007.23	6,64,827.90				

Details of North East Projects Costing Rs.150 crore and above (as on					31.12.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (-) [11/2022]	645.63 (-) [645.63]	186.02 (0.00) [3]
	<u>Power</u>				
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	14,738.05 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
3	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (-) [394.00]	390.07 (0.00) [0]
4	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [10/2021]	210.50 (-) [210.50]	145.76 (0.00) [0]
5	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	8/2021 (-) [0/0]	496.47 (-) [496.47]	8.93 (0.00) [0]
6	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	227.25 (0.00) [0]
7	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	8/2021 (-) [0/0]	437.60 (-) [437.60]	7.78 (0.00) [0]
8	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	93.72 (0.00) [0]
9	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	0.52 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	68.02 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	155.44 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	59.86 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	100.72 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	216.15 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25	3/2019	9/2020 (-)	347.78 (-)	149.95 (0.00)

	(PACKAGE		[0/0]	[347.78]	[0]
16	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	41.91 (0.00) [0]
17	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	195.00 (0.00) [0]
18	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	69.62 (0.00) [0]
19	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (8/2021) [12/2021]	200.44 (-) [200.44]	128.02 (0.00) [-]
20	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (11/2021) [3/2022]	568.92 (-) [568.92]	335.59 (0.00) [-]
21	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (3/2021) [3/2022]	188.78 (-) [188.78]	118.08 (0.00) [-]
22	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (1/2021) [12/2021]	245.79 (-) [245.79]	204.42 (0.00) [-]
23	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (6/2022) [3/2022]	1,718.59 (-) [1,718.59]	519.92 (0.00) [-]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	25.63 (0.00) [0]
25	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	26.00 (0.00) [0]
26	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	0.00 (0.00) [0]
27	DOGINALA - GAU	12/2020	9/2022 (-) [9/2022]	242.30 (-) [242.30]	0.00 (0.00) [0]
28	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
29	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (-) [4/2022]	228.71 (-) [228.71]	40.08 (0.00) [0]
30	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (-) [4/2022]	294.04 (-) [294.04]	79.46 (0.00) [0]
31	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (-) [4/2022]	199.03 (-) [199.03]	58.18 (0.00) [0]
32	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (-) [4/2022]	184.88 (-) [184.88]	40.92 (0.00) [0]
33	LADDA - BASAI	2/2021	4/2023 (-) [4/2023]	445.96 (-) [445.96]	0.00 (0.00) [0]
34	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	13.03 (0.00) [0]
35	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2021) [3/2022]	284.09 (284.09) [284.09]	182.01 (0.00) [59]

36	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [3/2022]	195.23 (-) [252.79]	153.14 (57.56) [59]
37	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST]	2/2017	4/2017 (-) [3/2022]	203.36 (-) [263.31]	155.10 (59.95) [59]
38	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [3/2022]	198.22 (-) [252.05]	157.83 (53.83) [59]
39	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX]	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	61.40 (0.00) [0]
40	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2022) [4/2022]	175.06 (-) [175.06]	94.23 (0.00) [-]
41	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2022) [4/2022]	176.12 (-) [176.12]	84.29 (0.00) [-]
42	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,251.08 (57.90) [0]
43	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	9/2021 (-) [9/2021]	182.55 (-) [182.55]	0.00 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
44	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2022) [3/2023]	1,142.00 (-) [1,232.00]	397.52 (90.00) [24]
	<u>Health And Family Welfare</u>				
45	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (-) [747.80]	446.44 (-127.20) [0]
46	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
47	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [11/2021]	557.00 (-) [557.00]	559.57 (0.00) [0]
48	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (9/2021) [12/2021]	224.75 (222.21) [198.00]	184.60 (-26.75) [16]
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [12/2021]	543.91 (652.10) [638.60]	399.74 (94.69) [22]
50	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	26.64 (0.00) [0]
51	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [2/2023]	218.38 (-) [218.38]	0.00 (0.00) [0]
52	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (18,968.00) [18,968.00]	767.97 (6,602.00) [0]
53	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (9,058.00) [9,058.00]	959.30 (-1,170.00) [0]
	<u>Railways</u>				
54	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-)	2,232.32 (-)	1,939.39 (717.68)

			[3/2023]	[2,950.00]	[12]
55	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2022]	870.96 (-) [1,873.21]	1,586.23 (1,002.25) [12]
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,043.00]	919.48 (657.80) [48]
	Road Transport And Highways				
57	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (5/2022) [5/2022]	268.08 (-) [390.73]	346.72 (122.65) [60]
58	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	23.56 (0.00) [0]
59	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
60	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	42.19 (0.00) [0]
61	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	207.70 (0.00) [-]
62	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [2/2022]	588.95 (-) [588.95]	516.16 (0.00) [39]
63	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2021]	289.99 (-) [289.99]	100.00 (0.00) [36]
64	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561)	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	139.69 (0.00) [74]
65	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	113.03 (0.00) [42]
66	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	229.20 (0.00) [74]
67	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	557.28 (0.00) [0]
68	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	37.93 (0.00) [0]
69	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	42.69 (0.00) [0]
70	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	0.00 (0.00) [0]
71	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	16.63 (0.00) [0]
72	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	34.33 (0.00) [0]
73	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	0.00 (0.00) [0]
74	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-)	168.39 (-)	169.08 (0.00)

			[11/2021]	[168.39]	[0]
75	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [3/2023]	818.00 (-) [818.00]	272.86 (0.00) [-]
76	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [463.49]	179.86 (0.00) [42]
77	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
78	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	372.30 (0.00) [46]
79	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [612.58]	612.58 (332.58) [0]
80	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
81	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	46.60 (0.00) [0]
82	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
83	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
84	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
85	OUR LANING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	155.61 (0.00) [-]
86	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [2/2022]	160.00 (-) [160.00]	133.51 (0.00) [5]
87	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [12/2022]	636.42 (-) [636.42]	0.00 (0.00) [0]
88	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
89	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	140.46 (0.00) [0]
90	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	20.73 (0.00) [0]
91	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	62.66 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
92	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (1,311.05) [1,311.05]	199.40 (732.43) [0]
	<u>Railways</u>				
93	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (12/2023) [12/2023]	4,454.17 (12,264.00) [14,322.00]	12,012.77 (9,867.83) [153]

	Road Transport And Highways				
94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	50.50 (0.00) [0]
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	39.42 (0.00) [0]
96	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	53.11 (0.00) [0]
97	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	30.07 (0.00) [0]
98	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	25.27 (0.00) [0]
99	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [10/2023]	673.27 (-) [673.27]	0.00 (0.00) [0]
100	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
101	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [3/2023]	467.00 (-) [467.00]	0.00 (0.00) [0]
102	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	0.00 (0.00) [0]
103	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	35.84 (0.00) [0]
104	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
105	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
106	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	8.67 (0.00) [0]
107	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	167.94 (0.00) [0]
108	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	0.00 (0.00) [0]
109	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	0.00 (0.00) [0]
110	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	0.00 (0.00) [0]
111	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	0.00 (0.00) [0]
112	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]
113	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	0.00 (0.00) [0]

114	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	12.11 (0.00) [0]
115	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	9.86 (0.00) [0]
116	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	0.00 (0.00) [0]
117	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [0]
	<u>MEGHALAYA</u>				
	<u>Department Of Higher Education</u>				
118	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (6/2022) [6/2022]	484.32 (429.70) [429.70]	230.00 (-54.62) [93]
	<u>Doner</u>				
119	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [8/2021]	151.33 (-) [151.33]	149.33 (0.00) [0]
	<u>Health And Family Welfare</u>				
120	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [3/2022]	363.99 (-) [363.99]	262.64 (0.00) [46]
	<u>Railways</u>				
121	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.34 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
122	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.37 (0.00) [0]
123	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [3/2022]	306.28 (-) [306.28]	133.81 (0.00) [34]
124	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	40.21 (0.00) [0]
125	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	288.84 (0.00) [0]
126	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	173.17 (0.00) [0]
127	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	42.62 (0.00) [0]
128	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2022]	157.86 (-) [157.86]	55.86 (0.00) [0]
129	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
130	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (9/2021) [9/2021]	553.51 (-) [553.51]	198.39 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
131	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-)	2,393.47 (5,021.45)	4,525.01 (4,133.53)

			[12/2023]	[6,527.00]	[117]
	Road Transport And Highways				
132	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [11/2021]	205.95 (-) [205.95]	123.24 (0.00) [0]
133	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2022) [0/0]	195.04 (434.65) [377.99]	368.39 (182.95) [0]
134	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2021) [0/0]	186.96 (-) [322.24]	308.85 (135.28) [0]
135	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2022) [0/0]	193.69 (374.59) [327.92]	323.23 (134.23) [0]
136	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	27.90 (0.00) [0]
137	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	33.21 (0.00) [0]
138	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	59.06 (0.00) [0]
139	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	59.29 (0.00) [0]
140	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	120.63 (0.00) [0]
141	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	43.01 (0.00) [0]
142	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	12.72 (0.00) [0]
143	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	34.80 (0.00) [0]
144	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
145	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
146	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	98.33 (0.00) [43]
147	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	642.96 (-) [642.96]	115.64 (0.00) [45]
148	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	518.53 (-) [518.53]	137.11 (0.00) [45]
149	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [4/2023]	537.82 (-) [537.82]	142.87 (0.00) [43]
150	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [4/2023]	473.18 (-) [473.18]	128.15 (0.00) [43]
151	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC	4/2017	9/2019 (6/2023)	640.07 (-)	107.05 (0.00)

	IMPROVEMENTS FRO		[7/2023]	[640.07]	[46]
152	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (3/2024) [4/2024]	404.29 (-) [404.29]	51.36 (0.00) [55]
153	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (9/2023) [9/2023]	428.11 (-) [428.11]	90.39 (0.00) [48]
154	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2022) [0/0]	624.41 (1,109.88) [992.67]	978.43 (368.26) [0]
	NAGALAND				
	Railways				
155	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
156	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	1,420.48 (4,336.48) [132]
	Road Transport And Highways				
157	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	128.80 (0.00) [44]
158	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	100.70 (0.00) [48]
159	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	175.63 (0.00) [0]
160	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	333.24 (0.00) [42]
161	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	132.56 (0.00) [50]
162	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	56.39 (0.00) [0]
163	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	70.73 (0.00) [0]
164	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	38.95 (0.00) [0]
165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	67.50 (0.00) [0]
166	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	49.90 (0.00) [0]
167	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	79.89 (0.00) [0]
168	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [6/2022]	206.53 (-) [206.53]	81.84 (0.00) [0]
169	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (4/2022) [0/0]	217.35 (-) [217.35]	104.81 (0.00) [0]
170	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	52.44 (0.00) [0]

171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (118.56) [202.36]	7.02 (0.00) [0]
172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (177.00) [277.44]	33.95 (0.00) [0]
173	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	182.63 (0.00) [46]
174	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	120.99 (0.00) [39]
175	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	125.87 (0.00) [39]
176	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	112.26 (0.00) [0]
177	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	77.62 (0.00) [39]
178	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	68.70 (0.00) [49]
179	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	157.06 (0.00) [0]
180	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	134.89 (0.00) [0]
181	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	352.25 (13.93) [0]
182	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	311.17 (0.00) [0]
183	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (369.96) [369.96]	322.13 (33.71) [0]
184	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	0.00 (0.00) [0]
185	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	20.00 (0.00) [0]
186	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	167.62 (-) [167.62]	118.61 (0.00) [0]
187	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]
188	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (167.23) [315.63]	9.39 (0.00) [0]
189	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [7/2022]	237.51 (-) [237.51]	96.49 (0.00) [-5]
	<u>SIKKIM</u>				
	<u>Railways</u>				
190	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023)	1,339.48 (4,084.69)	1,856.78 (7,260.52)

			[12/2023]	[8,600.00]	[96]
	Road Transport And Highways				
191	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	2.58 (0.00) [0]
192	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [11/2023]	493.42 (-) [493.42]	0.00 (0.00) [0]
193	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	26.51 (0.00) [0]
194	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	86.64 (0.00) [0]
195	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	76.84 (0.00) [0]
196	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	120.72 (0.00) [0]
197	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	76.23 (0.00) [0]
198	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [12/2021]	290.05 (-) [290.05]	154.83 (0.00) [49]
199	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (-) [12/2023]	816.79 (-) [816.79]	2.20 (0.00) [0]
200	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
201	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	69.72 (0.00) [0]
202	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	32.85 (0.00) [0]
203	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	59.98 (0.00) [0]
204	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	42.83 (0.00) [0]
205	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	295.14 (59.37) [0]
206	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
207	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
	TRIPURA				
	Civil Aviation				
208	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2021) [1/2022]	438.28 (-) [402.00]	397.85 (-36.28) [31]
	Railways				
209	AGARTALA-AKHAURA NL	4/2012	3/2020 (6/2022)	569.63 (90.00)	612.37 (172.37)

			[6/2022]	[742.00]	[27]
	Road Transport And Highways				
210	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	358.78 (0.00) [0]
211	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	18.87 (0.00) [0]
212	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	27.82 (0.00) [0]
213	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	89.80 (0.00) [0]
214	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	9.33 (0.00) [0]
215	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	8.23 (0.00) [0]
216	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	65.92 (0.00) [0]
217	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	90.44 (0.00) [0]
218	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	7.72 (0.00) [0]
219	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (-) [7/2022]	332.14 (-) [332.14]	10.88 (0.00) [0]
220	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	10.23 (0.00) [0]
221	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	17.99 (0.00) [0]
222	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	42.33 (0.00) [0]
223	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	106.99 (0.00) [0]
224	STRENGTHENING OF CHURAI BARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	95.22 (0.00) [0]
225	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	59.74 (38.51) [0]
226	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	142.81 (0.00) [0]
	Total			1,30,283.53 (76,331.92) [1,83,944.82]	68,720.30 (53,661.29)

Details of State wise Projects Costing Rs.150 crore and above (as on					31.12.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (6/2022) [6/2022]	417.23 (707.73) [707.73]	494.81 (290.50) [45]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (3/2021) [3/2022]	409.85 (-) [409.85]	135.48 (0.00) [51]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	229.32 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (3/2021) [10/2021]	277.17 (-) [277.17]	202.59 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (1/2022) [1/2022]	262.97 (-) [262.97]	63.74 (0.00) [39]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (6/2021) [6/2021]	257.34 (-) [238.00]	214.90 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [3/2022]	391.00 (-) [391.00]	77.75 (0.00) [41]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (9/2020) [3/2022]	234.27 (-) [234.27]	75.22 (0.00) [41]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (10/2021) [10/2021]	237.80 (237.80) [238.00]	148.90 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [3/2023]	611.80 (-) [611.80]	67.47 (0.00) [0]
11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (12/2021) [12/2022]	177.10 (-) [177.10]	108.20 (0.00) [34]
	<u>Department Of Higher Education</u>				
12	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-) [0/0]	186.00 (199.00) [205.00]	130.63 (19.00) [0]
13	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC	9/2019	9/2022 (6/2023) [6/2023]	588.72 (-) [588.72]	117.82 (0.00) [9]
14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (11/2022) [11/2022]	655.34 (655.34) [655.34]	300.85 (0.00) [29]

	Health And Family Welfare				
15	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [3/2022]	601.02 (-) [601.02]	515.47 (0.00) [-]
16	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2021]	272.19 (-) [272.54]	273.41 (0.35) [0]
	Petroleum				
17	220 KV GRID SUPPLY	10/2020	3/2021 (-) [12/2021]	303.40 (-) [303.40]	224.20 (0.00) [9]
18	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	8/2027 (-) [8/2027]	2,880.00 (-) [2,880.00]	113.40 (0.00) [0]
19	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (12/2021) [9/2022]	466.00 (-) [466.00]	301.65 (0.00) [17]
20	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [3/2023]	580.20 (-) [580.20]	260.89 (0.00) [25]
21	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY	9/2021	6/2024 (-) [6/2024]	160.00 (-) [160.00]	0.00 (0.00) [0]
22	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (6/2022) [6/2022]	34,012.00 (-) [25,090.00]	15,071.32 (-8,922.00) [24]
23	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [1/2023]	167.00 (-) [167.00]	16.06 (0.00) [6]
24	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	128.30 (0.00) [10]
25	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (3/2022) [3/2022]	316.20 (-) [316.20]	142.62 (0.00) [5]
26	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [11/2022]	332.61 (-) [332.61]	30.88 (0.00) [0]
27	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [3/2022]	210.94 (-) [210.94]	128.96 (0.00) [7]
28	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [1/2022]	196.26 (-) [196.26]	105.40 (0.00) [18]
29	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	17,704.50 (5,336.00) [24]
	Railways				
30	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2024]	3,631.00 (-) [3,887.48]	1,388.38 (256.48) [24]
31	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2024]	1,045.20 (-) [2,120.16]	1,042.28 (1,074.96) [180]
32	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (3/2024) [3/2026]	2,499.71 (-) [2,499.71]	769.95 (0.00) [48]
33	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [0/0]	234.50 (-) [235.00]	14.14 (0.50) [0]
34	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018	387.70	434.63

			(-) [0/0]	(-) [487.13]	(99.43) [0]
35	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	3,515.82 (302.42) [0]
36	VIJAYAWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [3,377.00]	3,753.96 (1,873.29) [24]
	<u>Road Transport And Highways</u>				
37	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	266.63 (0.00) [0]
38	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (-) [0/0]	1,226.88 (-) [1,226.88]	299.39 (0.00) [0]
39	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021 (-) [0/0]	1,601.10 (-) [1,601.10]	69.79 (0.00) [0]
40	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
41	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	464.83 (0.00) [0]
42	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (5/2022) [0/0]	263.45 (381.75) [263.45]	118.05 (0.00) [0]
43	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (1/2022) [0/0]	429.43 (373.05) [429.43]	325.74 (0.00) [0]
44	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [6/2022]	314.43 (-) [314.43]	85.61 (0.00) [-]
45	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD	8/2016	1/2017 (12/2021) [0/0]	350.61 (-) [350.61]	328.03 (0.00) [0]
46	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (-) [0/0]	333.21 (-) [353.43]	333.09 (20.22) [0]
47	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI- KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (7/2021) [7/2021]	1,532.62 (-) [2,499.00]	1,009.50 (966.38) [0]
48	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (4/2022) [0/0]	576.48 (596.38) [576.48]	418.18 (0.00) [0]
49	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (12/2021) [7/2021]	348.95 (-) [348.95]	257.45 (0.00) [0]
50	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	3/2020	3/2021 (-) [4/2022]	207.79 (-) [207.79]	108.34 (0.00) [13]
51	REHABILITATION AND UPGRADATION OF DHINDI- DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (11/2021) [0/0]	386.09 (316.06) [386.09]	214.31 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF EXISTING NH- 167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (10/2021) [0/0]	290.15 (-) [290.15]	154.09 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF EXISTING NH- 565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
54	REHABILITATION AND UPGRADATION OF GIDDALUR-	3/2018	/	565.09	654.52

	VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS		(-) [2/2021]	(-) [565.09]	(0.00) [0]
55	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (9/2021) [0/0]	995.09 (995.00) [995.09]	584.10 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (8/2021) [0/0]	444.84 (-) [444.84]	359.86 (0.00) [0]
57	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (12/2021) [0/0]	376.25 (-) [376.25]	315.76 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (11/2021) [0/0]	289.67 (274.73) [289.67]	211.71 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (7/2021) [0/0]	504.19 (556.13) [504.19]	478.63 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (6/2021) [0/0]	271.45 (-) [271.45]	243.29 (0.00) [0]
61	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (2/2022) [0/0]	319.28 (-) [319.28]	213.08 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (10/2021) [0/0]	372.68 (309.37) [372.68]	257.45 (0.00) [0]
63	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (12/2021) [0/0]	228.32 (202.83) [228.32]	145.60 (0.00) [0]
64	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING-KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (10/2021) [0/0]	418.03 (381.75) [418.03]	324.61 (0.00) [0]
65	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	8/2020	3/2021 (-) [3/2023]	222.61 (-) [222.61]	6.94 (0.00) [24]
66	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/	1,959.00	1,321.09
			(-) [10/2021]	(-) [1,959.00]	(0.00) [0]
67	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (-) [0/0]	597.67 (-) [597.67]	252.65 (0.00) [0]
68	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN	9/2018	2/2019 (-) [0/0]	617.41 (-) [617.41]	526.54 (0.00) [0]
69	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/	1,323.15	1,221.85
			(-) [0/0]	(-) [1,323.15]	(0.00) [0]
70	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/	1,550.98	1,654.42
			(-) [9/2021]	(-) [1,550.98]	(0.00) [0]
71	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,286.10 (0.00) [0]
72	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	968.97 (145.48) [0]
73	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
74	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-)	1,684.00 (-)	0.00 (0.00)

			[0/0]	[1,684.00]	[0]
75	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	6/2020	5/2021 (-) [12/2022]	221.40 (-) [221.40]	24.49 (0.00) [19]
	<u>Water Resources</u>				
76	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2021) [4/2022]	10,151.04 (55,548.87) [55,548.87]	18,335.60 (45,397.83) [25]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
77	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (-) [11/2022]	645.63 (-) [645.63]	186.02 (0.00) [3]
	<u>Power</u>				
78	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	14,738.05 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
79	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (-) [394.00]	390.07 (0.00) [0]
80	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/	210.50	145.76
			(-) [10/2021]	(-) [210.50]	(0.00) [0]
81	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	8/2021 (-) [0/0]	496.47 (-) [496.47]	8.93 (0.00) [0]
82	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/	243.89	227.25
			(-) [9/2020]	(-) [243.89]	(0.00) [0]
83	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	8/2021 (-) [0/0]	437.60 (-) [437.60]	7.78 (0.00) [0]
84	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	93.72 (0.00) [0]
85	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	0.52 (0.00) [0]
86	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	68.02 (0.00) [0]
87	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	155.44 (0.00) [0]
88	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	59.86 (0.00) [0]
89	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	100.72 (0.00) [0]
90	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	216.15 (0.00) [0]
91	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	149.95 (0.00) [0]
92	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	41.91 (0.00) [0]
93	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN	3/2019	2/2020	342.55	195.00

	SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2		(-) [0/0]	(-) [342.55]	(0.00) [0]
94	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	69.62 (0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (8/2021) [12/2021]	200.44 (-) [200.44]	128.02 (0.00) [-]
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (11/2021) [3/2022]	568.92 (-) [568.92]	335.59 (0.00) [-]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (3/2021) [3/2022]	188.78 (-) [188.78]	118.08 (0.00) [-]
98	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (1/2021) [12/2021]	245.79 (-) [245.79]	204.42 (0.00) [-]
99	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (6/2022) [3/2022]	1,718.59 (-) [1,718.59]	519.92 (0.00) [-]
100	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	25.63 (0.00) [0]
101	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	26.00 (0.00) [0]
102	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	0.00 (0.00) [0]
103	DOGINALA - GAU	12/2020	9/2022 (-) [9/2022]	242.30 (-) [242.30]	0.00 (0.00) [0]
104	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
105	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (-) [4/2022]	228.71 (-) [228.71]	40.08 (0.00) [0]
106	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (-) [4/2022]	294.04 (-) [294.04]	79.46 (0.00) [0]
107	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (-) [4/2022]	199.03 (-) [199.03]	58.18 (0.00) [0]
108	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (-) [4/2022]	184.88 (-) [184.88]	40.92 (0.00) [0]
109	LADDA - BASAI	2/2021	4/2023 (-) [4/2023]	445.96 (-) [445.96]	0.00 (0.00) [0]
110	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	13.03 (0.00) [0]
111	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2021) [3/2022]	284.09 (284.09) [284.09]	182.01 (0.00) [59]
112	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [3/2022]	195.23 (-) [252.79]	153.14 (57.56) [59]
113	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825	2/2017	4/2017 (-)	203.36 (-)	155.10 (59.95)

	[EXIST		[3/2022]	[263.31]	[59]
114	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [3/2022]	198.22 (-) [252.05]	157.83 (53.83) [59]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	61.40 (0.00) [0]
116	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2022) [4/2022]	175.06 (-) [175.06]	94.23 (0.00) [-]
117	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2022) [4/2022]	176.12 (-) [176.12]	84.29 (0.00) [-]
118	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,251.08 (57.90) [0]
119	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	9/2021 (-) [9/2021]	182.55 (-) [182.55]	0.00 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
120	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2022) [3/2023]	1,142.00 (-) [1,232.00]	397.52 (90.00) [24]
	<u>Health And Family Welfare</u>				
121	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (-) [747.80]	446.44 (-127.20) [0]
122	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
123	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [11/2021]	557.00 (-) [557.00]	559.57 (0.00) [0]
124	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (9/2021) [12/2021]	224.75 (222.21) [198.00]	184.60 (-26.75) [16]
125	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [12/2021]	543.91 (652.10) [638.60]	399.74 (94.69) [22]
126	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	26.64 (0.00) [0]
127	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [2/2023]	218.38 (-) [218.38]	0.00 (0.00) [0]
128	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (18,968.00) [18,968.00]	767.97 (6,602.00) [0]
129	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (9,058.00) [9,058.00]	959.30 (-1,170.00) [0]
	<u>Railways</u>				
130	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,939.39 (717.68) [12]
131	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2022]	870.96 (-) [1,873.21]	1,586.23 (1,002.25) [12]
132	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL	9/2006	3/2019	385.20	919.48

	PROJECT), NEFR		(-) [3/2023]	(-) [1,043.00]	(657.80) [48]
	<u>Road Transport And Highways</u>				
133	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (5/2022) [5/2022]	268.08 (-) [390.73]	346.72 (122.65) [60]
134	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	23.56 (0.00) [0]
135	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
136	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	42.19 (0.00) [0]
137	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	207.70 (0.00) [-]
138	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [2/2022]	588.95 (-) [588.95]	516.16 (0.00) [39]
139	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2021]	289.99 (-) [289.99]	100.00 (0.00) [36]
140	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	139.69 (0.00) [74]
141	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	113.03 (0.00) [42]
142	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	229.20 (0.00) [74]
143	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	557.28 (0.00) [0]
144	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	37.93 (0.00) [0]
145	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	42.69 (0.00) [0]
146	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	0.00 (0.00) [0]
147	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	16.63 (0.00) [0]
148	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	34.33 (0.00) [0]
149	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	0.00 (0.00) [0]
150	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2021]	168.39 (-) [168.39]	169.08 (0.00) [0]
151	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [3/2023]	818.00 (-) [818.00]	272.86 (0.00) [-]
152	FOUR LANING OF JHANJHI JN TO DEMOW SECTION	6/2015	6/2018	463.49	179.86

	FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5		(-) [12/2021]	(-) [463.49]	(0.00) [42]
153	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
154	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	372.30 (0.00) [46]
155	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [612.58]	612.58 (332.58) [0]
156	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
157	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	46.60 (0.00) [0]
158	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
159	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
160	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
161	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	155.61 (0.00) [-]
162	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [2/2022]	160.00 (-) [160.00]	133.51 (0.00) [5]
163	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [12/2022]	636.42 (-) [636.42]	0.00 (0.00) [0]
164	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
165	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	140.46 (0.00) [0]
166	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	20.73 (0.00) [0]
167	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	62.66 (0.00) [0]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
168	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [12/2023]	1,216.90 (-) [1,216.90]	249.46 (0.00) [14]
	<u>Department Of Higher Education</u>				
169	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [3/2022]	496.18 (496.00) [498.99]	301.90 (2.81) [57]
170	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (-) [375.00]	125.38 (0.00) [26]
	<u>Petroleum</u>				
171	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO	1/2020	4/2023	14,810.00	2,089.45

	9.0 MMTPA		(-) [4/2023]	(-) [14,810.00]	(0.00) [0]
172	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS	6/2019	12/2029 (-) [12/2029]	988.00 (-) [988.00]	45.10 (0.00) [0]
173	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	439.00 (-) [439.00]	127.63 (0.00) [0]
174	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	10/2018	8/2027 (-) [8/2027]	176.00 (-) [176.00]	79.72 (0.00) [0]
175	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA	6/2019	12/2029 (-) [12/2029]	163.00 (-) [163.00]	26.31 (0.00) [0]
176	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	6/2019	2/2028 (-) [2/2028]	347.00 (-) [347.00]	105.90 (0.00) [0]
177	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2/2028 (-) [2/2028]	2,996.00 (-) [2,996.00]	309.12 (0.00) [0]
178	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	197.09 (0.00) [0]
179	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (12/2021) [3/2022]	522.00 (-) [522.00]	399.21 (0.00) [12]
180	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (8/2022) [8/2022]	199.36 (-) [199.36]	90.83 (0.00) [22]
181	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021) [1/2022]	189.00 (-) [189.00]	178.65 (0.00) [12]
182	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (9/2021) [3/2022]	206.50 (-) [206.50]	167.51 (0.00) [12]
183	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	111.34 (0.00) [0]
	Power				
184	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [7/2023]	8,692.97 (21,312.11) [21,312.11]	19,466.00 (12,619.14) [141]
185	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (6/2020) [11/2021]	5,353.00 (10,566.00) [10,566.00]	9,014.00 (5,213.00) [0]
186	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	4,611.25 (0.00) [0]
187	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (-) [3/2022]	12,964.60 (17,304.00) [17,304.00]	16,604.00 (4,339.40) [46]
	Railways				
188	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]
189	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (-) [1,605.17]	153.43 (0.00) [-]
190	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	2.55 (2,668.81) [-]

191	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/	378.56	386.36
			(-)	(-)	(1,480.19)
			[3/2023]	[1,858.75]	[-]
192	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-)	(-)	(0.00)
			[0/0]	[205.00]	[0]
193	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF,	4/1991	/	329.39	1,370.20
			(3/2022)	(803.11)	(1,153.75)
			[3/2022]	[1,483.14]	[-]
194	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	1.15
			(-)	(-)	(0.00)
			[0/0]	[445.25]	[0]
195	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	1,597.10
			(3/2023)	(2,066.78)	(1,538.13)
			[3/2023]	[2,066.78]	[-]
196	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	1,086.41
			(11/2022)	(898.53)	(755.27)
			[11/2022]	[1,080.00]	[128]
197	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	540.73
			(3/2023)	(-)	(271.01)
			[12/2024]	[819.01]	[57]
198	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	352.68
			(-)	(614.45)	(451.58)
			[12/2023]	[614.45]	[-]
199	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.74
			(-)	(-)	(26.24)
			[0/0]	[360.00]	[0]
200	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	1,051.33
			(-)	(1,200.20)	(0.00)
			[3/2023]	[1,200.20]	[36]
201	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	459.31
			(-)	(516.02)	(16.61)
			[0/0]	[516.02]	[0]
202	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.39
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
203	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	722.71
			(9/2021)	(751.55)	(273.67)
			[9/2021]	[751.55]	[0]
204	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	4.99
			(-)	(-)	(795.00)
			[0/0]	[1,006.00]	[0]
205	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	424.08
			(3/2024)	(1,185.73)	(454.09)
			[3/2024]	[1,185.73]	[36]
206	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.59
			(-)	(-)	(0.00)
			[0/0]	[281.30]	[0]
207	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.53
			(-)	(-)	(0.00)
			[3/2024]	[228.05]	[-]
208	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	560.09
			(-)	(-)	(227.94)
			[0/0]	[560.09]	[0]
209	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.31
			(-)	(-)	(0.00)
			[0/0]	[620.57]	[0]
210	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	1,029.65
			(-)	(2,132.03)	(1,612.13)
			[3/2024]	[2,145.00]	[60]
211	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING	12/2015	3/2020	1,491.47	572.94

	INCLUDING GANGA BRIDGE		(3/2023) [3/2023]	(-) [1,491.47]	(0.00) [36]
212	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (3/2024) [3/2024]	744.04 (1,215.54) [1,215.54]	543.61 (471.50) [36]
213	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (735.20) [735.20]	390.81 (410.20) [0]
214	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2023]	372.14 (1,470.50) [1,470.50]	1,467.70 (1,098.36) [-]
215	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [3/2025]	380.00 (-) [519.33]	316.22 (139.33) [-]
216	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [678.62]	3.20 (0.00) [0]
	<u>Road Transport And Highways</u>				
217	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [0/0]	511.54 (-) [591.00]	578.00 (79.46) [0]
218	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
219	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (12/2021) [0/0]	575.00 (-) [575.00]	506.02 (0.00) [0]
220	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	0.00 (0.00) [0]
221	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [0/0]	464.09 (-) [464.09]	60.06 (0.00) [0]
222	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [0/0]	649.90 (-) [649.90]	44.00 (0.00) [0]
223	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [0/0]	446.97 (-) [446.97]	0.00 (0.00) [0]
224	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	10/2019	2/2020 (-) [0/0]	1,101.99 (-) [1,101.99]	209.64 (0.00) [0]
225	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	252.17 (0.00) [0]
226	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	79.35 (0.00) [0]
227	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (1/2021) [0/0]	2,598.00 (1,962.50) [1,962.50]	249.88 (-635.50) [0]
228	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	11.00 (-7.71) [0]
229	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [537.17]	78.33 (40.97) [0]
230	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (683.82) [560.70]	698.84 (-123.13) [0]
231	ENGINEERING, PROCUREMENT, AND CONSTRUCTION	2/2016	5/2016	178.85	152.22

	OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P		(-) [0/0]	(-) [152.62]	(-26.23) [0]
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [478.35]	527.97 (-74.95) [0]
233	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [0/0]	1,167.45 (-) [1,182.94]	278.12 (15.49) [0]
234	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [0/0]	642.41 (-) [681.67]	527.80 (39.26) [0]
235	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [0/0]	322.09 (247.00) [322.09]	0.00 (0.00) [0]
236	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (2,138.16) [925.87]	1,224.99 (-482.98) [0]
237	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [10/2021]	814.04 (-) [825.17]	821.37 (11.13) [0]
238	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
239	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	445.90 (0.00) [0]
240	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.92 (0.00) [0]
241	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	1,198.39 (0.00) [0]
242	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	1,532.47 (0.00) [0]
243	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	113.25 (0.00) [0]
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	333.28 (50.09) [0]
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (780.77) [675.00]	399.67 (0.00) [0]
246	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
247	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	341.21 (0.00) [54]
248	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	93.13 (0.00) [0]
249	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [1,038.56]	1,034.47 (183.76) [0]
250	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [649.27]	651.24 (133.14) [0]
251	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM	3/2017	3/2020 (-)	672.89 (-)	99.86 (63.12)

	EXISTING KM.89.020 (DESIGN		[0/0]	[736.01]	[0]
	<u>Urban Development</u>				
252	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [6/2024]	13,365.77 (-) [13,925.50]	306.94 (559.73) [0]
	<u>Water Resources</u>				
253	I AND D AND STP AT CHAPPRA	11/2018	12/2020 (6/2021) [7/2022]	236.15 (-) [236.15]	60.61 (0.00) [19]
254	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [3/2024]	254.13 (-) [413.29]	0.05 (159.16) [42]
255	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [0/0]	956.00 (-) [721.37]	712.37 (-234.63) [0]
256	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [3/2022]	268.63 (-) [268.63]	338.67 (0.00) [14]
257	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [4/2022]	230.06 (-) [230.06]	98.70 (0.00) [9]
258	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [4/2023]	305.19 (-) [305.19]	28.31 (0.00) [20]
259	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [12/2023]	294.02 (-) [294.02]	26.45 (0.00) [26]
260	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [4/2022]	356.37 (-) [356.37]	137.32 (0.00) [12]
261	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [12/2022]	824.00 (-) [824.00]	96.39 (0.00) [6]
262	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [12/2022]	578.89 (-) [578.89]	42.75 (0.00) [6]
263	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [2/2022]	225.77 (-) [398.90]	294.30 (173.13) [23]
264	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [6/2022]	277.42 (-) [277.42]	247.01 (0.00) [13]
265	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (3/2021) [12/2021]	191.62 (-) [191.62]	65.53 (0.00) [13]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
266	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	49.42 (0.00) [60]
267	AMGAON OPENCASE PROJECT RCE	7/2015	3/2020 (-) [3/2023]	316.10 (-) [316.10]	149.09 (0.00) [36]
268	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	322.85 (0.00) [0]
269	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	169.69 (0.00) [0]
270	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029 (-)	5,241.40 (-)	2,031.19 (0.00)

			[3/2029]	[5,241.40]	[0]
271	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2026]	916.24 (-) [916.24]	11.38 (0.00) [36]
272	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	4,645.12 (0.00) [0]
273	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2022]	152.43 (459.49) [459.49]	200.47 (307.06) [84]
274	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	187.07 (0.00) [0]
275	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
276	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	5.95 (0.00) [144]
277	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	3,162.39 (0.00) [0]
278	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2027]	1,875.32 (-) [1,875.32]	0.00 (0.00) [36]
279	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	46.75 (0.00) [0]
280	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2023]	321.50 (-) [321.50]	232.34 (0.00) [108]
281	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	9.08 (0.00) [0]
282	PORDA CHINTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
283	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	76.12 (0.00) [0]
	<u>Department Of Higher Education</u>				
284	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [10/2022]	808.62 (-) [808.62]	296.89 (0.00) [3]
	<u>Petroleum</u>				
285	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT	3/2021	3/2024 (-) [3/2024]	456.00 (-) [456.00]	13.36 (0.00) [0]
	<u>Power</u>				
286	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [0/0]	3,004.00 (-) [3,004.00]	1,395.48 (0.00) [0]
	<u>Railways</u>				
287	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [0/0]	393.98 (-) [393.98]	339.31 (0.00) [0]
288	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [9/2023]	2,288.00 (-) [4,970.11]	953.27 (2,682.11) [18]
289	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2023)	1,973.00 (2,135.34)	733.21 (162.34)

			[12/2023]	[2,135.34]	[33]
290	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [6/2022]	3,055.00 (-) [3,055.15]	2,707.85 (0.15) [45]
291	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2023]	1,160.00 (1,160.83) [1,160.83]	1,012.35 (0.83) [36]
292	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
293	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2021]	1,402.02 (-) [1,300.00]	1,364.39 (-102.02) [21]
	Road Transport And Highways				
294	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	402.95 (231.09) [0]
295	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [0/0]	726.67 (1,096.52) [1,096.52]	518.73 (369.85) [0]
296	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
297	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	439.27 (0.00) [0]
298	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (1/2022) [1/2022]	291.05 (-) [291.05]	241.71 (0.00) [-]
299	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (3/2022) [3/2022]	335.32 (-) [335.32]	282.86 (0.00) [57]
300	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (3/2022) [3/2022]	476.20 (543.73) [544.00]	400.87 (67.80) [66]
301	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (3/2022) [3/2022]	496.02 (-) [496.02]	251.27 (0.00) [84]
302	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (6/2022) [6/2022]	497.14 (572.66) [572.66]	284.86 (75.52) [70]
303	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (6/2022) [6/2022]	624.98 (731.50) [731.50]	476.86 (106.52) [68]
304	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (12/2022) [12/2022]	452.94 (435.61) [435.61]	117.77 (-17.33) [77]
305	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (1/2022) [1/2022]	423.79 (-) [423.79]	298.63 (0.00) [48]
306	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (3/2022) [3/2022]	188.80 (-) [188.80]	113.05 (0.00) [34]
307	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (1/2022) [1/2022]	379.16 (-) [379.16]	333.56 (0.00) [50]
	Steel				
308	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (1/2022) [3/2022]	15,525.00 (21,940.00) [21,940.00]	19,538.23 (6,415.00) [82]
309	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023	2,907.00	547.05

			(-) [6/2023]	(-) [2,907.00]	(0.00) [0]
310	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	81.14 (0.00) [0]
	<u>Urban Development</u>				
311	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	5/2019	9/2020 (1/2023) [1/2023]	299.97 (299.97) [299.97]	27.44 (0.00) [28]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
312	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [6/2022]	303.80 (351.21) [303.80]	203.38 (0.00) [26]
	<u>Commerce</u>				
313	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [0/0]	302.64 (-) [302.64]	30.00 (0.00) [0]
	<u>Dpiit</u>				
314	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (5/2022) [5/2022]	4,773.00 (-) [5,178.00]	3,044.41 (405.00) [29]
	<u>Health And Family Welfare</u>				
315	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [3/2021]	204.44 (-) [250.00]	249.24 (45.56) [0]
316	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
317	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [12/2021]	156.56 (-) [190.34]	183.36 (33.78) [-]
318	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [9/2021]	414.11 (-) [586.50]	581.44 (172.39) [0]
	<u>Heavy Industry</u>				
319	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [0/0]	1,554.00 (-) [900.00]	815.00 (-654.00) [0]
	<u>Home Affairs</u>				
320	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	6/2019	7/2022 (12/2022) [12/2022]	277.35 (290.33) [290.33]	38.13 (12.98) [5]
321	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [5/2022]	1,219.21 (-) [2,000.00]	1,049.80 (780.79) [31]
	<u>Power</u>				
322	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (12/2021) [4/2022]	1,394.52 (-) [1,394.52]	578.99 (0.00) [59]
	<u>Railways</u>				
323	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	160.79 (123.32) [-]
324	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [359.00]	116.87 (202.35) [-]
	<u>Renewable Energy</u>				
325	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [0/0]	271.90 (-) [271.90]	90.99 (0.00) [0]

	Telecommunications				
326	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	3/2018 (-) [1/2022]	248.20 (-) [248.20]	155.97 (0.00) [46]
	Urban Development				
327	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (2/2022) [2/2022]	197.33 (217.00) [217.00]	187.08 (19.67) [34]
328	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	2,711.33 (0.00) [0]
329	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (9/2021) [0/0]	565.00 (-) [565.00]	484.47 (0.00) [0]
330	DELHI MRTS PHASE-III	9/2011	3/2016 (8/2021) [0/0]	38,585.00 (-) [38,585.00]	39,619.40 (0.00) [0]
331	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (1/2022) [1/2022]	238.56 (238.56) [238.56]	208.57 (0.00) [20]
332	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (6/2023) [6/2023]	1,180.00 (1,100.80) [1,100.80]	35.90 (-79.20) [23]
333	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (6/2022) [6/2022]	392.00 (392.00) [392.00]	196.68 (0.00) [22]
334	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [6/2023]	1,128.00 (1,128.00) [1,128.00]	30.00 (0.00) [15]
335	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (6/2023) [6/2023]	422.00 (422.00) [422.00]	135.75 (0.00) [27]
336	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [12/2022]	2,694.00 (-) [2,694.00]	974.86 (0.00) [-]
	Water Resources				
337	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
338	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [12/2021]	515.07 (-) [515.07]	345.58 (0.00) [11]
339	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	251.88 (0.00) [0]
340	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	108.28 (0.00) [12]
341	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	160.52 (0.00) [10]
	GOA				
	Department Of Higher Education				
342	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (2/2023) [2/2023]	303.90 (-) [303.90]	48.30 (0.00) [35]
	Health And Family Welfare				
343	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [1/2021]	249.01 (-) [249.07]	231.05 (0.06) [0]
	Road Transport And Highways				

344	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	244.36 (10.43) [0]
345	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	118.37 (0.00) [0]
346	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	560.12 (0.00) [0]
347	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	325.55 (0.00) [0]
348	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [0/0]	852.67 (-) [852.67]	212.65 (0.00) [0]
349	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [0/0]	634.32 (-) [634.32]	308.10 (0.00) [0]
350	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	400.90 (0.00) [0]
351	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	365.21 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
352	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [12/2022]	11,459.00 (-) [16,580.00]	17,427.00 (5,121.00) [84]
	<u>Civil Aviation</u>				
353	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022 (-) [3/2023]	1,405.00 (-) [1,405.00]	396.18 (0.00) [7]
	<u>Petroleum</u>				
354	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	687.88 (0.00) [0]
355	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (5/2023) [5/2023]	588.20 (730.20) [730.20]	206.83 (142.00) [-]
356	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023 (-) [8/2023]	1,614.00 (-) [1,614.00]	1.12 (0.00) [0]
357	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [6/2022]	327.78 (-) [200.00]	198.90 (-127.78) [50]
358	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2021) [3/2022]	906.00 (-) [906.00]	360.74 (0.00) [25]
359	LAB REVAMP AT GUJARAT REFINERY	10/2019	4/2022 (-) [4/2022]	403.00 (-) [403.00]	206.62 (0.00) [0]
360	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024 (-) [8/2024]	18,936.00 (-) [18,936.00]	829.33 (0.00) [-1]
361	REDEVELOPMENT OF LINCH FIELD	4/2021	3/2025 (-) [3/2025]	631.03 (-) [631.03]	227.33 (0.00) [0]
362	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022 (-) [8/2022]	444.87 (-) [444.87]	141.98 (0.00) [0]

363	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [970.30]	947.93 (-192.26) [0]
364	REDEVELOPMENT OF SOBHASAN COMPLEX	8/2021	2/2026 (-) [2/2026]	885.63 (-) [885.63]	183.01 (0.00) [0]
365	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (-) [12/2022]	1,378.00 (-) [1,378.00]	182.84 (0.00) [0]
366	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [10/2022]	225.54 (247.90) [247.90]	75.63 (22.36) [20]
	<u>Power</u>				
367	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR)	5/2021	9/2022 (-) [9/2022]	674.92 (-) [674.92]	76.91 (0.00) [0]
368	GUJARAT 200 MW (GUVNL TENDER)	1/2021	7/2022 (-) [8/2022]	842.27 (-) [842.27]	92.08 (0.00) [1]
369	KAWAS SOLAR 56 MW	8/2020	10/2021 (10/2022) [10/2022]	261.80 (-) [293.03]	130.88 (31.23) [12]
370	SHIYAL SOLAR POWER PROJECT	5/2021	10/2022 (-) [10/2022]	296.20 (-) [296.20]	0.21 (0.00) [0]
	<u>Railways</u>				
371	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,650.00]	1,737.74 (674.38) [0]
372	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2024) [3/2024]	829.74 (1,631.75) [2,223.37]	1,966.82 (1,393.63) [48]
373	ANAND GODHRA DOUBLING PROJECT 79 KMS	4/2017	3/2020 (3/2024) [3/2024]	692.25 (692.25) [742.88]	0.89 (50.63) [48]
374	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (10/2023) [10/2023]	318.24 (321.62) [321.62]	126.35 (3.38) [139]
375	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [12/2021]	644.38 (-) [872.65]	942.56 (228.27) [9]
376	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS	4/2018	3/2024 (3/2024) [3/2024]	537.31 (537.31) [537.31]	0.64 (0.00) [0]
377	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (-) [3/2024]	844.10 (-) [844.10]	254.99 (0.00) [-]
378	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
379	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (12/2021) [0/0]	153.83 (154.15) [154.15]	109.05 (0.32) [0]
380	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,868.89]	2,201.29 (320.23) [3]
381	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2023) [3/2023]	320.66 (859.16) [1,378.11]	558.66 (1,057.45) [48]
382	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (-)	1,002.39 (-)	730.07 (39.73)

			[12/2022]	[1,042.12]	[21]
383	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (-) [12/2022]	1,037.15 (-) [1,383.69]	1,199.84 (346.54) [21]
384	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (12/2022) [0/0]	248.26 (528.49) [528.49]	123.75 (280.23) [0]
	Road Transport And Highways				
385	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	199.86 (0.00) [0]
386	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	285.03 (0.00) [0]
387	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [0/0]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [0]
388	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	439.98 (0.00) [0]
389	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [4/2021]	364.56 (-) [392.00]	353.42 (27.44) [0]
390	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
391	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	564.11 (0.00) [0]
392	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [0/0]	2,702.05 (-) [2,043.00]	2,003.16 (-659.05) [0]
393	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	187.80 (0.00) [0]
394	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (-) [962.43]	356.16 (0.00) [0]
395	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	614.62 (0.00) [0]
396	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	737.67 (0.00) [0]
397	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	505.33 (0.00) [0]
398	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	203.40 (0.00) [0]
399	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	421.85 (0.00) [0]
400	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.44 (0.00) [0]
401	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
402	KANDLA - MUNDRA PORT	1/2011	7/2013 (-)	953.88 (-)	0.00 (0.00)

			[0/0]	[953.88]	[0]
403	SIX LANNING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (1/2019) [0/0]	1,052.21 (-) [1,361.00]	451.40 (308.79) [0]
404	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (1/2019) [0/0]	1,251.11 (1,361.00) [1,361.00]	451.40 (109.89) [0]
405	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
406	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	186.00 (0.00) [0]
407	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	315.08 (0.00) [0]
	<u>Urban Development</u>				
408	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [8/2022]	10,773.00 (-) [12,787.00]	9,834.10 (2,014.00) [44]
409	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	419.43 (0.00) [0]
410	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	373.31 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
411	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (6/2021) [12/2021]	215.92 (-) [215.92]	184.57 (0.00) [25]
	<u>Health And Family Welfare</u>				
412	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2019]	505.58 (-) [585.00]	586.96 (79.42) [0]
	<u>Home Affairs</u>				
413	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	1/2020	10/2023 (4/2024) [4/2024]	166.98 (166.98) [166.98]	7.84 (0.00) [6]
	<u>Petroleum</u>				
414	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	505.01 (0.00) [0]
415	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [3/2022]	909.00 (-) [909.00]	504.26 (0.00) [14]
416	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (7/2022) [7/2022]	206.63 (340.76) [340.76]	164.11 (134.13) [29]
417	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (2/2027) [2/2027]	520.00 (-) [520.00]	193.31 (0.00) [5]
418	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [3/2022]	164.69 (-) [164.69]	30.12 (0.00) [8]
419	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (2/2022) [2/2022]	598.00 (-) [598.00]	470.06 (0.00) [24]
420	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [7/2022]	278.60 (-) [278.60]	101.96 (0.00) [13]

421	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (4/2022) [4/2022]	1,636.00 (-) [1,636.00]	954.75 (0.00) [20]
422	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	12/2021 (1/2023) [1/2023]	1,255.00 (-) [1,255.00]	373.81 (0.00) [13]
423	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (3,199.60) [2,281.94]	673.16 (0.00) [7]
424	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (12/2021) [3/2022]	286.42 (327.01) [327.01]	234.40 (40.59) [19]
	<u>Railways</u>				
425	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [0/0]	346.32 (-) [346.32]	320.28 (0.00) [0]
426	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [6/2021]	287.00 (-) [893.45]	745.06 (606.45) [0]
	<u>Road Transport And Highways</u>				
427	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [507.70]	0.00 (-95.25) [0]
428	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	0.00 (-37.12) [0]
429	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [9/2021]	2,128.72 (-) [2,128.72]	1,577.44 (0.00) [0]
430	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [0/0]	247.25 (-) [247.25]	179.30 (0.00) [0]
431	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (6/2021) [12/2020]	1,484.30 (-) [1,484.30]	293.15 (0.00) [0]
432	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]
433	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	1,061.16 (0.00) [0]
434	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (-) [0/0]	1,243.45 (-) [1,243.45]	1,068.04 (0.00) [0]
435	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (-) [0/0]	889.36 (-) [889.36]	783.29 (0.00) [0]
436	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (-) [0/0]	1,018.79 (-) [1,018.79]	892.38 (0.00) [0]
437	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (-) [0/0]	1,051.91 (-) [1,051.91]	927.71 (0.00) [0]
438	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	965.92 (0.00) [0]
439	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (-) [0/0]	1,137.42 (-) [1,137.42]	1,039.87 (0.00) [0]
440	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (-)	1,033.19 (-)	898.79 (0.00)

			[0/0]	[1,033.19]	[0]
441	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [0/0]	1,108.00 (3,485.00) [2,288.00]	3,450.00 (1,180.00) [0]
442	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [0/0]	275.12 (-) [275.12]	172.62 (0.00) [0]
443	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.78 (-) [181.78]	138.72 (0.00) [0]
444	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [0/0]	198.05 (-) [198.05]	138.07 (0.00) [0]
445	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (2/2018) [2/2018]	795.50 (906.65) [922.64]	387.49 (127.14) [0]
446	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (2/2018) [2/2018]	634.70 (-) [925.96]	341.09 (291.26) [0]
HIMACHAL PRADESH					
Department Of Higher Education					
447	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (11/2021) [11/2021]	270.83 (-) [244.00]	242.81 (-26.83) [0]
448	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022 (10/2022) [10/2022]	392.51 (-) [392.51]	85.88 (0.00) [4]
Health And Family Welfare					
449	AIIMS BILASPUR	4/2018	9/2021 (-) [6/2022]	1,351.00 (-) [1,471.00]	870.80 (120.00) [9]
450	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [5/2022]	260.00 (-) [260.00]	25.38 (0.00) [11]
Power					
451	DHAULASIDH HYDROELECTRIC PROJECT (66 MW)	10/2020	11/2025 (-) [11/2025]	687.97 (-) [687.97]	207.51 (0.00) [0]
452	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	585.06 (0.00) [0]
453	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (3/2023) [3/2023]	3,919.59 (9,897.59) [9,897.59]	9,357.83 (5,978.00) [162]
Railways					
454	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2025]	2,966.99 (-) [6,753.42]	1,905.63 (3,786.43) [-12]
Road Transport And Highways					
455	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [0/0]	273.20 (-) [273.20]	670.27 (0.00) [0]
456	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	1,068.47 (0.00) [0]
457	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,960.92 (0.00) [0]
458	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (3/2021) [0/0]	934.46 (1,457.82) [1,457.82]	1,305.69 (523.36) [0]

459	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (11/2021) [0/0]	478.74 (1,135.08) [1,135.08]	760.86 (656.34) [0]
460	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	891.57 (0.00) [0]
461	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [0/0]	447.75 (-) [447.75]	1,341.10 (0.00) [0]
462	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K	2/2021	9/2021 (-) [0/0]	345.89 (-) [345.89]	9.65 (0.00) [0]
463	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50.	8/2020	3/2021 (-) [0/0]	242.80 (-) [242.80]	10.23 (0.00) [0]
464	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA	8/2020	4/2021 (-) [0/0]	272.98 (-) [272.98]	12.49 (0.00) [0]
465	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75	8/2020	4/2021 (-) [0/0]	349.20 (-) [349.20]	41.20 (0.00) [0]
466	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	0.00 (0.00) [0]
	<u>JAMMU AND KASHMIR</u>				
	<u>Department Of Higher Education</u>				
467	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (748.19) [676.00]	223.43 (0.00) [0]
468	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (-) [10/2022]	424.93 (-) [424.93]	80.19 (0.00) [3]
	<u>Health And Family Welfare</u>				
469	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	218.99 (0.00) [-16]
470	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
471	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	394.73 (0.00) [0]
	<u>Power</u>				
472	KIRU HYDRO ELECTRIC PROJECT	3/2019	/ (8/2024) [7/2025]	4,287.59 (-) [4,287.59]	617.83 (0.00) [-]
473	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (7/2025) [7/2025]	8,112.12 (-) [8,112.12]	2,056.81 (0.00) [63]
	<u>Railways</u>				
474	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2022]	2,500.00 (27,949.00) [27,949.00]	26,237.89 (25,449.00) [241]
	<u>Road Transport And Highways</u>				
475	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	369.00 (0.00) [0]
476	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	1,000.78 (-132.75) [0]
477	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-	12/2019	12/2023	2,680.42	878.00

	MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA		(-) [12/2023]	(-) [2,680.42]	(0.00) [0]
478	DONIPAWA TO ASHAJIPORA BYPASS PKG-7	3/2021	12/2022 (-) [12/2022]	260.40 (-) [260.40]	0.00 (0.00) [0]
479	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [0/0]	2,168.66 (-) [2,168.66]	1,158.40 (0.00) [0]
480	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,763.58 (0.00) [0]
481	GOHA-KHELLANI PKG-3	2/2021	3/2023 (-) [3/2023]	431.28 (-) [431.28]	24.77 (0.00) [0]
482	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,654.22 (0.00) [0]
483	KHELLANI-KHANABAL PKG-1	3/2021	9/2022 (-) [9/2022]	486.45 (-) [486.45]	68.38 (0.00) [0]
484	KHELLANI-KHANABAL PKG-2	7/2021	2/2023 (-) [2/2023]	512.43 (-) [512.43]	3.87 (0.00) [0]
485	KHELLANI-KHANABAL PKG-3	3/2021	12/2022 (-) [12/2022]	398.51 (-) [398.51]	4.68 (0.00) [0]
486	KHELLANI-KHANABAL PKG-4	7/2021	8/2023 (-) [8/2023]	859.67 (-) [859.67]	0.00 (0.00) [0]
487	KHELLANI-KHANABAL PKG-5	7/2021	2/2023 (-) [2/2023]	497.09 (-) [497.09]	5.78 (0.00) [0]
488	KHELLANI-KHANABAL PKG-6	2/2021	9/2022 (-) [9/2022]	285.28 (-) [285.28]	22.14 (0.00) [0]
489	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	4,758.92 (360.00) [0]
490	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,116.66 (0.00) [0]
491	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [10/2020]	1,100.70 (-) [1,100.70]	2,933.15 (0.00) [0]
492	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [4/2022]	228.39 (-) [228.39]	23.72 (0.00) [0]
493	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (-) [4/2022]	210.79 (-) [210.79]	20.18 (0.00) [0]
494	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	88.07 (0.00) [0]
495	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	232.23 (0.00) [0]
496	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	116.48 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				

497	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	165.05 (0.00) [0]
498	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2022]	163.51 (-) [163.51]	124.85 (0.00) [132]
499	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	260.37 (0.00) [0]
500	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2022]	162.46 (-) [162.46]	93.13 (0.00) [96]
501	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [3/2022]	289.45 (-) [289.45]	285.81 (0.00) [94]
502	MAGADH EXPANSION OC(51 MTY)	8/2008	7/2012 (3/2028) [3/2028]	6,964.33 (7,254.37) [7,254.37]	814.20 (290.04) [188]
503	MOONIDIH XV SEAM UG	8/2011	3/2019 (-) [2/2023]	1,230.27 (-) [1,230.27]	508.61 (0.00) [47]
504	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [4/2023]	339.88 (-) [339.88]	89.42 (0.00) [108]
505	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2023]	555.52 (-) [555.52]	5.87 (0.00) [24]
506	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [778.80]	406.92 (-774.26) [0]
507	PACHWARA SOUTH COAL BLOCK	7/2013	8/2022 (-) [9/2023]	1,795.01 (-) [1,795.01]	37.83 (0.00) [13]
508	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [10/2022]	243.00 (334.27) [334.27]	28.43 (91.27) [54]
509	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2020]	269.82 (-) [269.82]	213.80 (0.00) [0]
510	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2022]	510.85 (-) [510.85]	500.91 (0.00) [72]
511	RECAST EPR AMRAPALI OC	2/2012	3/2020 (3/2028) [3/2028]	4,983.58 (4,983.58) [4,983.58]	370.76 (0.00) [96]
512	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	37.28 (0.00) [0]
	<u>Department Of Higher Education</u>				
513	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [0/0]	171.86 (-) [171.86]	111.29 (0.00) [0]
	<u>Petroleum</u>				
514	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [3/2022]	161.50 (-) [161.50]	127.30 (0.00) [21]
515	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS	10/2018	12/2029 (-) [12/2029]	613.00 (-) [613.00]	161.96 (0.00) [0]
516	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-)	226.45 (-)	149.60 (0.00)

			[10/2022]	[226.45]	[0]
517	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	111.42 (0.00) [0]
518	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	773.03 (314.52) [-12]
519	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [9/2022]	248.55 (-) [248.55]	142.91 (0.00) [3]
	<u>Power</u>				
520	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [9/2023]	14,366.58 (-) [17,007.00]	12,556.00 (2,640.42) [51]
521	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,684.86 (314.04) [0]
522	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [2/2025]	18,668.00 (-) [17,667.00]	4,771.00 (-1,001.00) [23]
	<u>Railways</u>				
523	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2023]	1,724.20 (-) [1,724.20]	1,097.56 (0.00) [33]
524	CHAKRADHARPUR TO GOILKERA 3RD LINE (34 KM)	11/2015	12/2018 (-) [6/2020]	354.54 (-) [354.54]	302.08 (0.00) [0]
525	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [3/2022]	348.23 (-) [390.00]	403.49 (41.77) [12]
526	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	3/1999	/ (3/2022) [3/2022]	1,033.07 (3,020.95) [3,650.00]	3,661.29 (2,616.93) [-]
527	KODERMA-TILAIYA (NL), ECR	4/2002	/ (3/2023) [3/2023]	459.91 (1,625.87) [1,625.87]	941.70 (1,165.96) [-]
528	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM)	4/2018	6/2022 (-) [12/2025]	428.65 (-) [472.50]	1.61 (43.85) [42]
529	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	4/2018	12/2021 (-) [6/2022]	390.39 (-) [511.75]	110.13 (121.36) [6]
	<u>Road Transport And Highways</u>				
530	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (3/2021) [0/0]	1,005.08 (1,073.10) [1,005.08]	0.00 (0.00) [0]
531	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	120.40 (2.71) [0]
532	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [0/0]	323.72 (-) [336.60]	322.26 (12.88) [0]
533	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	510.73 (0.00) [0]
534	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [486.00]	406.73 (27.97) [0]
535	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	109.08 (0.00) [0]

	<u>Steel</u>				
536	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [11/2022]	1,034.01 (-) [1,034.01]	566.58 (0.00) [61]
537	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (12/2021) [2/2022]	262.87 (-) [262.87]	209.03 (0.00) [32]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
538	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (10/2021) [3/2022]	246.31 (210.00) [210.00]	158.92 (-36.31) [25]
	<u>Department Of Higher Education</u>				
539	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (-) [10/2022]	851.00 (851.00) [851.00]	324.03 (0.00) [7]
	<u>Petroleum</u>				
540	BSVI UPGRADATION	9/2016	12/2019 (4/2021) [3/2022]	1,810.00 (1,810.00) [1,810.00]	1,789.68 (0.00) [27]
541	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	175.31 (0.00) [0]
542	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (1/2024) [1/2024]	200.00 (304.00) [304.00]	2.58 (104.00) [7]
543	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	1,461.90 (0.00) [0]
544	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [12/2021]	206.26 (-) [206.26]	163.25 (0.00) [9]
545	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [12/2021]	581.00 (637.00) [637.00]	543.02 (56.00) [21]
546	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (3/2022) [3/2022]	380.00 (-) [380.00]	339.20 (0.00) [4]
	<u>Railways</u>				
547	ARSIKERE-TUMKUR	3/2015	3/2020 (1/2022) [1/2022]	578.00 (-) [760.00]	647.09 (182.00) [22]
548	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2026]	986.30 (-) [1,530.09]	325.32 (543.79) [129]
549	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,383.00]	7.35 (0.22) [264]
550	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [367.77]	0.00 (40.52) [-]
551	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [692.43]	0.00 (134.43) [-]
552	GADAG-WADI NL	4/2013	12/2018 (-) [6/2025]	2,841.84 (-) [2,841.84]	387.33 (0.00) [78]
553	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [12/2022]	2,127.00 (-) [3,000.00]	2,477.01 (873.00) [-3]
554	HUBLI- CHIKJAJUR	3/2015	3/2020	1,156.94	1,205.02

			(-) [3/2023]	(-) [1,954.21]	(797.27) [36]
555	HUBLI-ANKOLA(NL),SWR	4/1997	/	2,315.00	158.11
			(-) [12/2024]	(-) [5,174.30]	(2,859.30) [-]
556	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017	644.78	495.11
			(-) [3/2025]	(889.00) [732.89]	(88.11) [96]
557	MARIKUPPAM - KUPPAM	4/2012	3/2016	279.54	36.97
			(-) [12/2023]	(-) [279.54]	(0.00) [93]
558	SHIMOGA-HARIHAR NL	4/2011	3/2016	832.47	0.94
			(-) [3/2024]	(-) [832.47]	(0.00) [96]
559	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/	1,801.01	82.81
			(-) [12/2023]	(-) [2,161.36]	(360.35) [-]
560	WHITE FIELD-KOLAR NL	4/2011	/	348.85	0.36
			(-) [12/2025]	(-) [348.85]	(0.00) [-]
	Road Transport And Highways				
561	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019	1,167.42	348.00
			(12/2022) [6/2023]	(-) [870.00]	(-297.42) [51]
562	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/	486.78	171.98
			(-) [0/0]	(-) [486.78]	(0.00) [0]
563	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016	1,655.01	1,867.51
			(-) [12/2020]	(-) [1,655.01]	(0.00) [0]
564	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019	701.40	146.05
			(-) [3/2022]	(-) [701.40]	(0.00) [36]
565	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019	870.00	36.30
			(-) [11/2020]	(-) [870.00]	(0.00) [0]
566	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	3/2019	12/2019	423.15	151.10
			(-) [0/0]	(-) [423.15]	(0.00) [0]
567	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019	157.32	0.28
			(-) [0/0]	(188.00) [157.32]	(0.00) [0]
568	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018	171.60	82.24
			(-) [0/0]	(-) [171.60]	(0.00) [0]
569	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018	1,388.00	1,311.10
			(-) [0/0]	(-) [1,388.00]	(0.00) [0]
570	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020	1,664.20	1,191.58
			(-) [12/2020]	(-) [1,664.20]	(0.00) [0]
571	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018	946.00	818.53
			(-) [0/0]	(-) [946.00]	(0.00) [0]
572	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018	325.86	347.46
			(-) [0/0]	(-) [386.41]	(60.55) [0]
573	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017	175.50	162.88
			(-) [0/0]	(-) [175.50]	(0.00) [0]
574	RECONSTRUCTION TO TWO LANE WITH PAVED	3/2018	6/2019	159.97	72.08

	SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2		(-) [0/0]	(-) [159.97]	(0.00) [0]
575	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,434.00]	1,319.54 (440.84) [0]
576	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.58 (-) [1,177.00]	912.41 (345.42) [0]
577	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,542.30 (272.20) [0]
578	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,439.59 (404.66) [0]
579	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	122.11 (0.00) [0]
580	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [9/2019]	709.00 (-) [709.00]	541.35 (0.00) [0]
581	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [0/0]	950.69 (1,918.36) [1,108.00]	1,481.35 (157.31) [0]
582	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	290.54 (0.00) [0]
583	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	223.35 (0.00) [0]
584	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	238.77 (0.00) [0]
585	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT	1/2017	9/2017 (-) [0/0]	264.34 (-) [264.34]	185.07 (0.00) [0]
586	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [0/0]	191.60 (-) [191.60]	111.51 (0.00) [0]
587	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	225.88 (0.00) [0]
588	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	185.07 (0.00) [0]
589	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [318.28]	195.88 (20.98) [0]
590	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	119.59 (0.00) [0]
591	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	125.81 (0.00) [0]
	Urban Development				
592	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B	6/2021	6/2026 (-) [6/2026]	14,788.10 (-) [14,788.10]	2,031.41 (0.00) [0]
593	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (3/2025) [3/2025]	26,405.14 (30,695.12) [30,695.12]	19,410.15 (4,289.98) [73]
	KERALA				

	Department Of Higher Education				
594	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [2/2023]	753.63 (-) [753.63]	216.78 (0.00) [23]
595	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [0/0]	165.23 (-) [165.23]	118.52 (0.00) [0]
	Health And Family Welfare				
596	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	70.91 (0.00) [21]
	Petroleum				
597	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	793.01 (395.24) [32]
598	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [9/2022]	607.06 (1,236.00) [1,236.00]	553.03 (628.94) [59]
599	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	425.30 (0.00) [0]
	Power				
600	KAYAMKULAM SOLAR 70 MW	9/2019	6/2021 (12/2021) [7/2022]	403.62 (-) [403.62]	122.49 (0.00) [13]
	Railways				
601	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (1,566.00) [2,815.62]	264.51 (1,249.62) [0]
602	ERNAKULAM-KUMBALAM	4/2010	/ (-) [3/2025]	189.24 (275.21) [448.10]	268.73 (258.86) [-]
603	KUMBALAM-TURAVUR	4/2011	/ (-) [3/2025]	252.96 (369.55) [709.69]	256.70 (456.73) [-]
604	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
605	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [3/2024]	1,431.90 (-) [1,431.90]	934.32 (0.00) [-]
606	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [3/2025]	1,000.00 (1,246.00) [1,339.00]	0.82 (339.00) [-]
	Road Transport And Highways				
607	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (1/2020) [1/2020]	845.24 (-) [941.00]	902.51 (95.76) [0]
608	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (12/2021) [12/2021]	804.97 (-) [804.97]	599.30 (0.00) [42]
609	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [0/0]	1,124.11 (-) [1,300.00]	655.89 (175.89) [0]
610	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
611	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [0/0]	255.75 (348.00) [348.43]	319.68 (92.68) [0]
612	SIX LANNING OF VADAKKANCHERRY	2/2010	8/2012	617.00	0.00

	THRISSURESECTION KM 240 270KM		(-) [0/0]	(-) [617.00]	(0.00) [0]
613	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK	2/2017	8/2017 (-) [0/0]	294.28 (-) [294.26]	138.37 (-0.02) [0]
614	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49)	2/2017	9/2017 (-) [0/0]	380.76 (-) [380.76]	248.27 (0.00) [0]
	<u>Urban Development</u>				
615	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (9/2020) [9/2020]	5,181.79 (6,218.14) [6,218.14]	6,065.82 (1,036.35) [0]
	<u>LADAKH</u>				
	<u>Civil Aviation</u>				
616	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (12/2022) [6/2023]	346.27 (-) [480.33]	140.13 (134.06) [21]
	<u>Road Transport And Highways</u>				
617	KARGIL-ZANSKR PACKAGE-1	3/2021	1/2023 (-) [1/2023]	384.23 (-) [384.23]	10.11 (0.00) [0]
618	KARGIL-ZANSKR PACKAGE-2	3/2021	1/2023 (-) [1/2023]	404.89 (-) [404.89]	1.98 (0.00) [0]
619	KARGIL-ZANSKR PACKAGE-3	8/2020	1/2023 (-) [1/2023]	381.01 (-) [381.01]	8.23 (0.00) [0]
620	KARGIL-ZANSKR PACKAGE-5	8/2020	12/2023 (-) [12/2023]	169.79 (-) [169.79]	48.49 (0.00) [0]
621	KARGIL-ZANSKR PACKAGE-6	1/2021	5/2024 (-) [5/2024]	239.81 (-) [239.81]	36.62 (0.00) [0]
622	KARGIL-ZANSKR PACKAGE-7	1/2021	6/2024 (-) [6/2024]	308.86 (-) [308.86]	38.81 (0.00) [0]
623	KARGIL-ZANSKR PACKAGE-8	3/2021	1/2023 (-) [1/2023]	398.37 (-) [398.37]	9.04 (0.00) [0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
624	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021 (-) [12/2022]	412.24 (-) [412.24]	224.31 (0.00) [18]
	<u>Coal</u>				
625	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2025]	869.44 (-) [869.44]	129.53 (0.00) [48]
626	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2027]	481.60 (-) [481.60]	0.00 (0.00) [48]
627	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2025]	231.92 (-) [231.92]	1.82 (0.00) [36]
628	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2026]	1,186.64 (-) [1,186.64]	243.93 (0.00) [36]
629	BATURA WEST OC PROJECT (0.80 MTY)	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]
630	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023	998.71	1.03

			(-) [3/2023]	(-) [998.71]	(0.00) [0]
631	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2023]	1,255.17 (-) [1,255.17]	481.57 (0.00) [12]
632	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	2.65 (0.00) [0]
633	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2022]	1,783.09 (-) [1,783.09]	902.52 (0.00) [12]
634	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	68.86 (0.00) [36]
635	NIGAH EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
636	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (4/2024) [4/2024]	357.80 (-) [357.80]	100.68 (0.00) [37]
637	RPR FOR JAMUNIA UG (0.90 MTY)	7/2016	3/2022 (3/2026) [3/2026]	281.25 (-) [281.25]	23.52 (0.00) [48]
638	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
639	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
Petroleum					
640	CGD PROJECT AT REWA DISTRICT	10/2018	2/2027 (-) [2/2027]	177.00 (-) [177.00]	66.77 (0.00) [0]
641	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (12/2021) [12/2021]	236.00 (319.61) [319.61]	226.65 (83.61) [18]
Power					
642	AMELIA COAL MINE	1/2017	9/2020 (8/2022) [8/2022]	2,104.21 (1,587.16) [1,587.16]	648.84 (-517.05) [23]
Railways					
643	ANUPPUR-KATNI	4/2015	12/2021 (12/2023) [12/2023]	1,370.00 (1,370.94) [1,370.94]	838.56 (0.94) [24]
644	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2021]	1,485.85 (-) [1,835.83]	2,355.40 (349.98) [12]
645	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (12/2021) [12/2021]	585.93 (1,268.32) [1,268.32]	1,123.85 (682.39) [34]
646	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [603.69]	350.17 (-96.31) [33]
647	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2024]	1,763.93 (2,445.30) [2,445.30]	1,345.52 (681.37) [48]
648	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [12/2023]	582.13 (1,247.64) [1,247.64]	540.13 (665.51) [21]
649	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-)	2,478.23 (-)	1,035.16 (396.89)

			[6/2023]	[2,875.12]	[15]
650	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [0/0]	174.00 (-) [174.00]	172.08 (0.00) [0]
651	NIMACH BADI SADRI NEW LINE PROJECT	4/2017	3/2022 (-) [3/2024]	495.18 (-) [495.18]	0.33 (0.00) [24]
652	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2024) [3/2024]	424.60 (2,909.99) [2,909.99]	1,411.38 (2,485.39) [36]
653	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (-) [3/2023]	3,503.69 (-) [6,171.08]	2,327.60 (2,667.39) [12]
	Road Transport And Highways				
654	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (8/2021) [2/2022]	249.05 (-) [249.05]	219.86 (0.00) [43]
655	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	11/2019	7/2021 (-) [0/0]	716.00 (-) [716.00]	59.57 (0.00) [0]
656	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	322.21 (0.00) [0]
657	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [3/2022]	950.27 (-) [950.27]	293.31 (0.00) [-]
658	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [2/2022]	392.33 (428.55) [428.55]	404.69 (36.22) [47]
659	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	193.99 (0.00) [0]
660	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [204.65]	215.49 (-169.75) [0]
661	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (11/2021) [12/2021]	990.61 (-) [990.61]	718.56 (0.00) [51]
662	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (3/2021) [3/2022]	390.51 (-) [390.51]	297.87 (0.00) [-]
663	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	422.00 (183.02) [-]
664	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [12/2021]	743.88 (-) [743.89]	490.00 (0.01) [-]
665	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [2/2022]	1,094.97 (-) [1,094.97]	790.00 (0.00) [-]
666	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [10/2022]	217.96 (-) [884.00]	609.00 (666.04) [-]
667	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (12/2021) [2/2022]	205.05 (-) [205.05]	133.46 (0.00) [59]
668	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (11/2021) [3/2022]	264.50 (-) [264.50]	139.54 (0.00) [12]
669	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF	6/2015	3/2016 (-)	1,012.90 (-)	226.10 (0.00)

	MADHYA		[0/0]	[1,012.90]	[0]
670	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
671	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [0/0]	928.83 (-) [928.83]	867.83 (0.00) [0]
672	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [0/0]	794.30 (-) [691.38]	669.35 (-102.92) [0]
673	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [0/0]	795.76 (-) [686.13]	669.94 (-109.63) [0]
674	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [0/0]	810.22 (-) [810.22]	742.47 (0.00) [0]
675	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [0/0]	639.97 (-) [639.97]	485.68 (0.00) [0]
676	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	415.50 (0.00) [0]
677	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (8/2021) [1/2022]	957.54 (927.73) [927.73]	773.30 (-29.81) [23]
678	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
679	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
680	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (6/2021) [1/2022]	628.45 (-) [628.45]	457.34 (0.00) [24]
681	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	410.72 (-) [410.72]	392.42 (0.00) [0]
682	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [12/2021]	990.97 (-) [990.97]	763.00 (0.00) [24]
683	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [5/2022]	1,047.00 (-) [1,047.00]	605.00 (0.00) [24]
684	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [4/2022]	847.00 (-) [847.00]	570.00 (0.00) [25]
685	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [0/0]	996.27 (-) [996.27]	647.00 (0.00) [0]
686	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (3/2022) [4/2022]	169.63 (-) [169.63]	67.54 (0.00) [49]
687	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (4/2021) [1/2022]	877.79 (949.54) [949.54]	794.73 (71.75) [31]
688	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (5/2021) [1/2022]	809.16 (-) [809.16]	635.00 (0.00) [42]
689	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (6/2021) [12/2022]	511.83 (-) [511.83]	409.70 (0.00) [64]

690	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (3/2022) [3/2022]	254.17 (-) [254.17]	187.73 (0.00) [49]
691	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [2/2022]	233.04 (-) [233.04]	167.53 (0.00) [47]
692	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (11/2021) [1/2022]	279.44 (-) [279.44]	231.61 (0.00) [46]
693	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (8/2021) [2/2022]	166.21 (174.90) [174.90]	154.26 (8.69) [42]
694	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (9/2021) [2/2022]	184.62 (-) [184.62]	132.76 (0.00) [48]
695	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (9/2021) [6/2022]	214.69 (-) [214.69]	80.06 (0.00) [51]
696	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (9/2021) [2/2022]	217.22 (-) [226.88]	182.97 (9.66) [42]
697	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [2/2022]	162.56 (-) [162.56]	137.52 (0.00) [47]
698	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (9/2021) [12/2021]	373.82 (-) [373.82]	238.66 (0.00) [27]
	<u>Social Justice</u>				
699	CENTRE FOR DISABILITY SPORTS	2/2019	3/2024 (-) [3/2024]	170.99 (-) [170.99]	34.00 (0.00) [0]
	<u>Urban Development</u>				
700	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	354.67 (0.00) [0]
701	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	190.69 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
702	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [8/2022]	475.39 (-) [475.39]	184.10 (0.00) [16]
	<u>Coal</u>				
703	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (333.43) [333.43]	145.94 (44.53) [12]
704	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (745.03) [745.03]	423.42 (17.75) [0]
705	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (9/2022) [9/2022]	252.71 (-) [252.71]	107.27 (0.00) [18]
706	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (409.68) [409.68]	87.35 (221.74) [0]
707	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2022]	304.52 (327.41) [327.41]	162.29 (22.89) [36]
708	DHUPTALA OC(SASTI UG TO OC)	2/2019	3/2028 (-)	720.87 (-)	84.05 (0.00)

			[3/2028]	[720.87]	[0]
709	GHONSA EXPANSION DEEP OC	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	57.00 (0.00) [0]
710	NEW MAJRI UG TO OC	5/2015	3/2019 (3/2022) [3/2022]	295.56 (299.67) [299.67]	213.92 (4.11) [36]
711	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	3/2020 (3/2027) [3/2027]	1,184.33 (-) [1,184.33]	393.29 (0.00) [84]
712	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	11/2015	3/2021 (3/2024) [3/2024]	313.34 (-) [313.34]	159.36 (0.00) [36]
713	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	11/2015	3/2020 (3/2026) [3/2026]	851.60 (826.80) [826.80]	283.28 (-24.80) [72]
714	SASTI EXPANSION OC	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	52.55 (0.00) [0]
715	UKNI DEEP OC	11/2018	3/2021 (9/2022) [9/2022]	318.14 (-) [318.14]	223.12 (0.00) [18]
	<u>Department Of Higher Education</u>				
716	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [12/2021]	223.37 (-) [223.37]	117.64 (0.00) [17]
	<u>Fertilisers</u>				
717	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (1/2022) [1/2022]	426.72 (-) [426.72]	324.01 (0.00) [21]
	<u>Health And Family Welfare</u>				
718	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [12/2021]	582.99 (-) [582.99]	546.71 (0.00) [-]
719	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	259.46 (0.00) [0]
	<u>Petroleum</u>				
720	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [3/2022]	249.26 (-) [249.26]	194.72 (0.00) [21]
721	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [8/2022]	348.00 (437.00) [437.00]	209.30 (89.00) [19]
722	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (5/2022) [5/2022]	861.79 (1,846.46) [2,001.34]	1,604.42 (1,139.55) [108]
723	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (12/2021) [12/2021]	2,292.46 (-) [2,203.71]	2,222.54 (-88.75) [7]
724	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,475.92) [3,596.00]	3,526.55 (-410.83) [0]
725	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-) [6/2022]	640.00 (-) [640.00]	368.06 (0.00) [6]
726	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2022]	2,494.68 (-) [2,354.72]	1,800.96 (-139.96) [0]
727	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT	8/2020	3/2023 (-)	697.00 (-)	299.02 (0.00)

	MUMBAI R		[3/2023]	[697.00]	[0]
728	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (-) [2/2022]	1,945.00 (-) [1,945.00]	1,605.89 (0.00) [0]
729	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2022) [5/2022]	3,190.69 (3,375.90) [3,375.90]	2,888.99 (185.21) [49]
730	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	1,640.35 (747.87) [14]
731	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (1/2022) [1/2022]	3,660.71 (3,740.05) [3,740.05]	3,119.98 (79.34) [8]
732	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (5/2021) [2/2022]	763.92 (-) [733.86]	829.58 (-30.06) [14]
733	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND	5/2019	4/2025 (-) [4/2025]	8,797.00 (-) [8,797.00]	178.78 (0.00) [0]
<u>Railways</u>					
734	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [0/0]	184.06 (-) [325.00]	325.52 (140.94) [0]
735	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2023]	2,271.50 (-) [4,794.60]	2,921.95 (2,523.10) [24]
736	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (6/2022) [6/2022]	495.44 (-) [2,980.41]	1,868.04 (2,484.97) [219]
737	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	667.42 (205.27) [0]
738	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [12/2021]	713.48 (-) [2,900.00]	2,041.94 (2,186.52) [21]
739	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
740	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
741	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	488.43 (0.00) [12]
742	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [1,387.52]	358.30 (594.63) [24]
743	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	322.26 (0.00) [24]
744	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [0/0]	305.00 (-) [305.00]	269.73 (0.00) [0]
745	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (311.36) [311.36]	0.00 (45.48) [0]
746	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [0/0]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]
747	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-)	3,627.47 (3,627.00)	1,764.97 (0.00)

			[3/2023]	[3,627.47]	[-12]
748	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
749	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (3,176.60) [3,176.60]	1,492.13 (1,268.09) [9]
750	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
751	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.49]	0.00 (688.49) [0]
752	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (12/2022) [0/0]	217.38 (393.62) [393.62]	152.98 (176.24) [0]
753	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (12/2024) [12/2024]	229.00 (852.50) [1,096.00]	40.47 (867.00) [36]
754	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	239.26 (0.00) [12]
755	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	524.21 (11.30) [12]
756	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,445.48]	1,418.98 (277.19) [0]
757	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	355.54 (0.00) [24]
Road Transport And Highways					
758	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
759	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	510.71 (0.00) [0]
760	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	595.00 (0.00) [0]
761	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	867.97 (0.00) [0]
762	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [0/0]	744.64 (-) [982.00]	0.00 (237.36) [0]
763	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (10/2021) [12/2021]	1,071.61 (-) [1,048.10]	1,183.14 (-23.51) [-]
764	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [0/0]	446.17 (-) [446.17]	148.83 (0.00) [0]
765	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [0/0]	1,098.06 (-) [1,160.64]	0.00 (62.58) [0]
766	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	978.04 (0.00) [0]
767	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-)	1,101.58 (-)	334.55 (0.00)

			[0/0]	[1,101.58]	[0]
768	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [0/0]	400.25 (-) [400.25]	184.80 (0.00) [0]
769	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/	1,064.88 (-) [1,021.00]	474.80 (-43.88) [-]
770	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [0/0]	1,059.73 (-) [1,071.00]	18.75 (11.27) [0]
771	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [0/0]	1,030.44 (-) [1,065.51]	0.00 (35.07) [0]
772	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [0/0]	988.34 (-) [1,043.28]	0.00 (54.94) [0]
773	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [6/2021]	505.00 (-) [504.00]	451.92 (-1.00) [0]
774	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [0/0]	422.38 (-) [422.38]	228.75 (0.00) [0]
775	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [0/0]	955.40 (-) [955.40]	470.17 (0.00) [0]
776	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	109.24 (0.00) [0]
777	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	219.50 (0.00) [0]
778	AMDIT TO SAONER	1/2017	6/2019 (-) [0/0]	396.91 (397.00) [396.91]	289.79 (0.00) [0]
779	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [0/0]	426.06 (426.00) [426.06]	208.76 (0.00) [0]
780	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [0/0]	309.94 (310.00) [309.94]	192.24 (0.00) [0]
781	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	330.00 (0.00) [0]
782	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [0/0]	241.69 (242.00) [241.69]	167.95 (0.00) [0]
783	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [0/0]	289.11 (290.00) [289.11]	139.71 (0.00) [0]
784	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [0/0]	259.55 (260.00) [259.55]	204.49 (0.00) [0]
785	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	274.75 (0.00) [0]
786	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [0/0]	743.21 (743.00) [743.21]	295.35 (0.00) [0]
787	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	169.64 (0.90) [0]

788	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	159.96 (0.00) [0]
789	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [0/0]	206.97 (207.00) [206.97]	145.87 (0.00) [0]
790	CHIKALI TO DHAD	3/2018	12/2019 (-) [0/0]	189.46 (189.00) [189.46]	107.85 (0.00) [0]
791	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [0/0]	548.03 (548.00) [548.03]	401.46 (0.00) [0]
792	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [0/0]	393.10 (393.00) [393.10]	242.32 (0.00) [0]
793	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	201.73 (0.00) [0]
794	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	62.08 (0.00) [0]
795	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2021) [6/2022]	649.50 (-) [649.50]	238.84 (0.00) [39]
796	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [2/2022]	291.53 (-) [291.53]	242.03 (0.00) [-]
797	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [1/2022]	289.21 (-) [289.21]	227.37 (0.00) [-]
798	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2022) [6/2022]	593.26 (717.24) [717.24]	627.25 (123.98) [49]
799	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (3/2022) [3/2022]	531.13 (-) [744.73]	706.78 (213.60) [46]
800	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	106.56 (0.00) [0]
801	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	31.97 (-89.53) [0]
802	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (-) [414.00]	410.01 (-0.51) [0]
803	DAHEGAON TO KUHI	1/2017	6/2019 (-) [0/0]	228.89 (229.00) [228.89]	154.69 (0.00) [0]
804	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [0/0]	182.63 (-) [182.63]	137.99 (0.00) [0]
805	DEORI TO AMGAON	1/2017	5/2019 (-) [0/0]	409.62 (410.00) [409.62]	273.48 (0.00) [0]
806	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [0/0]	219.91 (-) [219.91]	146.73 (0.00) [0]
807	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [0/0]	296.19 (-) [254.00]	254.85 (-42.19) [0]
808	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019	336.21	219.86

			(-) [0/0]	(336.00) [336.21]	(0.00) [0]
809	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [0/0]	217.14 (217.00) [217.14]	137.57 (0.00) [0]
810	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [0/0]	391.06 (391.00) [391.06]	240.98 (0.00) [0]
811	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	325.92 (0.00) [0]
812	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
813	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [807.00]	724.40 (164.87) [0]
814	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (3/2021) [0/0]	904.16 (911.07) [904.16]	0.00 (0.00) [0]
815	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	333.22 (0.00) [0]
816	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	223.81 (0.00) [0]
817	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [0/0]	294.87 (295.00) [294.87]	139.25 (0.00) [0]
818	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [0/0]	355.17 (-) [355.17]	269.58 (0.00) [0]
819	INDAPUR TO VADPALE	1/2017	12/2019 (-) [0/0]	1,202.52 (1,203.00) [1,202.52]	791.90 (0.00) [0]
820	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [0/0]	461.96 (-) [461.96]	326.81 (0.00) [0]
821	JALGAON TO BHADGAON	1/2018	11/2019 (-) [0/0]	307.54 (308.00) [307.54]	204.36 (0.00) [0]
822	JALGAON TO NANDURA	3/2018	12/2019 (-) [0/0]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
823	JALKOT TO TOGRI	7/2018	8/2020 (-) [0/0]	299.92 (300.00) [299.92]	173.39 (0.00) [0]
824	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (-) [356.66]	130.60 (0.00) [0]
825	KAJ TO KUSALAM	1/2017	7/2019 (-) [0/0]	554.78 (-) [554.78]	304.78 (0.00) [0]
826	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	467.78 (0.00) [0]
827	KALMATH TO ZARAP	9/2016	3/2020 (-) [0/0]	1,338.13 (1,338.00) [1,338.13]	1,346.39 (0.00) [0]
828	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	631.68 (0.00) [0]

			[0/0]	[1,230.02]	[0]
829	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [0/0]	407.19 (407.00) [407.19]	194.17 (0.00) [0]
830	KARAD TO TAGAON	1/2017	6/2019 (-) [0/0]	537.81 (538.00) [537.81]	197.17 (0.00) [0]
831	KARAD TO VITA	1/2018	12/2019 (-) [0/0]	344.85 (245.00) [344.85]	220.46 (0.00) [0]
832	KARWANDI TO RAJURI	3/2018	12/2019 (-) [0/0]	276.95 (277.00) [276.95]	136.94 (0.00) [0]
833	KATOL TO WARUD	1/2017	6/2019 (-) [0/0]	463.62 (664.00) [463.62]	265.78 (0.00) [0]
834	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [0/0]	249.29 (-) [249.29]	155.48 (0.00) [0]
835	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [0/0]	203.21 (203.00) [203.21]	160.15 (0.00) [0]
836	KHERDA TO NAGZARI	3/2018	12/2019 (-) [0/0]	181.30 (-) [181.30]	137.37 (0.00) [0]
837	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	594.75 (594.75) [606.75]	200.10 (12.00) [0]
838	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	257.83 (0.00) [0]
839	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [0/0]	281.78 (282.00) [281.78]	74.00 (0.00) [0]
840	KOTHARI TO DHANORA	9/2018	8/2020 (-) [0/0]	301.38 (301.00) [301.38]	159.42 (0.00) [0]
841	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	290.64 (0.00) [0]
842	KUNDRAI TO WAZAR	1/2018	12/2019 (-) [0/0]	225.25 (225.00) [225.25]	199.34 (0.00) [0]
843	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	190.69 (0.00) [0]
844	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [0/0]	243.45 (244.00) [243.45]	164.16 (0.00) [0]
845	LATUR TO PANGAON	3/2018	12/2019 (-) [0/0]	336.47 (336.00) [336.47]	203.39 (0.00) [0]
846	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [0/0]	237.40 (-) [237.40]	9.66 (0.00) [0]
847	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [0/0]	256.15 (-) [256.15]	174.63 (0.00) [0]
848	MALEGAON TO RISOD	2/2018	12/2019 (-) [0/0]	303.24 (303.00) [303.24]	196.00 (0.00) [0]

849	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [0/0]	322.55 (-) [322.55]	191.12 (0.00) [0]
850	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [0/0]	457.52 (-) [457.52]	352.94 (0.00) [0]
851	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [0/0]	222.13 (222.00) [222.13]	156.87 (0.00) [0]
852	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [0/0]	228.54 (-) [228.54]	159.32 (0.00) [0]
853	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [0/0]	418.36 (-) [418.36]	263.13 (0.00) [0]
854	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [0/0]	486.19 (-) [486.19]	308.66 (0.00) [0]
855	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	151.60 (0.00) [0]
856	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	230.03 (0.00) [0]
857	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	233.89 (0.00) [0]
858	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	731.89 (731.89) [732.34]	316.43 (0.45) [0]
859	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	234.67 (0.00) [0]
860	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
861	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [0/0]	162.34 (-) [162.34]	59.85 (0.00) [0]
862	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [0/0]	376.72 (377.00) [376.72]	261.86 (0.00) [0]
863	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	222.40 (0.00) [0]
864	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [12/2021]	546.00 (-) [546.00]	309.98 (0.00) [29]
865	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [12/2021]	591.66 (-) [591.66]	319.05 (0.00) [29]
866	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [0/0]	244.04 (244.00) [244.04]	170.33 (0.00) [0]
867	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [0/0]	274.50 (275.00) [274.50]	143.39 (0.00) [0]
868	NANDED TO JALKOT	12/2017	9/2019 (-) [0/0]	456.93 (457.00) [456.93]	456.93 (0.00) [0]
869	NANDGAON TO MORSHI	1/2017	6/2019	385.87	258.29

			(-) [0/0]	(386.00) [385.87]	(0.00) [0]
870	NASHIK TO PETH	12/2015	11/2018 (-) [0/0]	289.60 (-) [289.60]	210.10 (0.00) [0]
871	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [0/0]	406.54 (407.00) [406.54]	172.47 (0.00) [0]
872	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [0/0]	420.63 (421.00) [420.63]	195.05 (0.00) [0]
873	OMREGA TO AUSA	3/2018	12/2019 (-) [0/0]	272.04 (272.00) [272.04]	218.03 (0.00) [0]
874	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [0/0]	344.25 (344.00) [344.25]	161.25 (0.00) [0]
875	PAHUR TO BODHWAD	1/2017	5/2020 (-) [0/0]	244.93 (-) [244.93]	159.96 (0.00) [0]
876	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	155.96 (0.00) [0]
877	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [0/0]	227.19 (227.00) [227.19]	138.05 (0.00) [0]
878	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [0/0]	381.08 (302.00) [381.08]	9.66 (0.00) [0]
879	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	170.80 (0.00) [0]
880	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [0/0]	238.19 (238.00) [238.19]	177.80 (0.00) [0]
881	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [0/0]	205.72 (206.00) [205.72]	85.47 (0.00) [0]
882	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	725.27 (0.00) [0]
883	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [0/0]	420.57 (-) [420.57]	269.24 (0.00) [0]
884	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [0/0]	170.00 (-) [170.00]	121.71 (0.00) [0]
885	PEN TO KHOPOLI	3/2018	3/2018 (-) [0/0]	301.39 (302.00) [301.39]	97.70 (0.00) [0]
886	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [0/0]	595.77 (-) [595.77]	303.09 (0.00) [0]
887	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [0/0]	223.46 (-) [223.46]	52.22 (0.00) [0]
888	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [0/0]	228.31 (-) [228.31]	88.39 (0.00) [0]
889	PUNE-SATARA(NH-4)	10/2010	3/2013 (-)	1,724.55 (-)	2,641.30 (0.00)

			[3/2022]	[1,724.55]	[108]
890	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	210.81 (0.00) [0]
891	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	303.72 (0.00) [0]
892	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	112.51 (0.00) [0]
893	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (2/2022) [2/2022]	536.65 (356.00) [536.65]	552.31 (0.00) [26]
894	RISOD TO HINGOLI	2/2018	12/2019 (-) [0/0]	355.99 (-) [355.99]	246.86 (0.00) [0]
895	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [0/0]	362.96 (-) [362.96]	178.97 (0.00) [0]
896	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [0/0]	415.25 (415.25) [415.25]	262.66 (0.00) [0]
897	SANGOLA TO JATH	1/2018	12/2019 (-) [0/0]	257.38 (257.00) [257.38]	166.31 (0.00) [0]
898	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	174.16 (0.00) [0]
899	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	189.43 (0.00) [0]
900	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	199.61 (0.00) [0]
901	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	284.02 (0.00) [0]
902	SELDOH TO PANVAR	7/2018	5/2020 (-) [0/0]	404.33 (404.00) [404.33]	45.13 (0.00) [0]
903	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [0/0]	150.79 (-) [150.79]	59.88 (0.00) [0]
904	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [0/0]	373.10 (373.00) [373.10]	314.20 (0.00) [0]
905	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [0/0]	211.34 (-) [211.34]	130.63 (0.00) [0]
906	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	186.62 (0.00) [0]
907	SHIVUR TO YEOLA	3/2018	12/2019 (-) [0/0]	181.08 (-) [181.08]	97.86 (0.00) [0]
908	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	232.56 (0.00) [0]
909	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (5/2021) [9/2021]	404.94 (499.70) [448.18]	495.92 (43.24) [0]

910	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (12/2016) [5/2017]	290.73 (-) [359.60]	340.15 (68.87) [0]
911	TAKARKHED TO JALNA	9/2017	6/2019 (-) [0/0]	417.90 (418.00) [417.90]	249.13 (0.00) [0]
912	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [0/0]	264.41 (264.00) [264.41]	189.64 (0.00) [0]
913	TALGAON TO KALMATH	10/2016	3/2020 (-) [0/0]	904.70 (905.00) [904.70]	969.90 (0.00) [0]
914	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [0/0]	195.64 (196.00) [195.64]	116.92 (0.00) [0]
915	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	302.13 (0.00) [0]
916	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [0/0]	1,598.47 (1,560.00) [1,598.47]	1,039.81 (0.00) [0]
917	VITA TO NAGAJ	3/2018	12/2019 (-) [0/0]	304.58 (305.00) [304.58]	128.89 (0.00) [0]
918	WADI TO ASOLA	1/2017	9/2019 (-) [0/0]	363.82 (364.00) [363.82]	65.03 (0.00) [0]
919	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [0/0]	194.23 (194.00) [194.23]	111.20 (0.00) [0]
920	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [0/0]	376.19 (-) [376.19]	82.35 (0.00) [0]
921	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	840.10 (0.00) [0]
922	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	362.46 (362.46) [362.46]	227.50 (0.00) [0]
923	WARDHA TO ARVI	2/2018	4/2020 (-) [0/0]	313.58 (-) [313.58]	192.50 (0.00) [0]
924	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [0/0]	216.90 (217.00) [216.90]	160.37 (0.00) [0]
925	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [0/0]	165.51 (-) [165.51]	133.93 (0.00) [0]
926	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
<u>Urban Development</u>					
927	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	3/2020 (3/2023) [3/2023]	23,136.00 (-) [33,406.00]	20,051.98 (10,270.00) [36]
928	NAGPUR METRO RAIL	8/2014	3/2018 (12/2021) [12/2021]	8,680.00 (-) [8,680.00]	8,443.80 (0.00) [45]
929	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (12/2022) [12/2022]	11,420.00 (11,420.00) [11,420.00]	7,565.74 (0.00) [13]

	<u>Water Resources</u>				
930	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2021]	233.57 (-) [233.57]	148.83 (0.00) [24]
	<u>MANIPUR</u>				
	<u>Power</u>				
931	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (1,311.05) [1,311.05]	199.40 (732.43) [0]
	<u>Railways</u>				
932	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (12/2023) [12/2023]	4,454.17 (12,264.00) [14,322.00]	12,012.77 (9,867.83) [153]
	<u>Road Transport And Highways</u>				
933	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	50.50 (0.00) [0]
934	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	39.42 (0.00) [0]
935	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	53.11 (0.00) [0]
936	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	30.07 (0.00) [0]
937	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	25.27 (0.00) [0]
938	CHURACHANDPUR TUIVAI PKG-3	7/2021	10/2023 (-) [10/2023]	673.27 (-) [673.27]	0.00 (0.00) [0]
939	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
940	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [3/2023]	467.00 (-) [467.00]	0.00 (0.00) [0]
941	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	0.00 (0.00) [0]
942	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	35.84 (0.00) [0]
943	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
944	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
945	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	8.67 (0.00) [0]
946	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	167.94 (0.00) [0]
947	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	0.00 (0.00) [0]
948	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-)	204.58 (-)	0.00 (0.00)

			[3/2023]	[204.58]	[0]
949	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	0.00 (0.00) [0]
950	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	0.00 (0.00) [0]
951	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]
952	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	0.00 (0.00) [0]
953	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	12.11 (0.00) [0]
954	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	9.86 (0.00) [0]
955	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	0.00 (0.00) [0]
956	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [0]
	<u>MEGHALAYA</u>				
	<u>Department Of Higher Education</u>				
957	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (6/2022) [6/2022]	484.32 (429.70) [429.70]	230.00 (-54.62) [93]
	<u>Doner</u>				
958	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR	4/2014	9/2017 (-) [8/2021]	151.33 (-) [151.33]	149.33 (0.00) [0]
	<u>Health And Family Welfare</u>				
959	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [3/2022]	363.99 (-) [363.99]	262.64 (0.00) [46]
	<u>Railways</u>				
960	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.34 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
961	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4- LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.37 (0.00) [0]
962	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [3/2022]	306.28 (-) [306.28]	133.81 (0.00) [34]
963	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	40.21 (0.00) [0]
964	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	288.84 (0.00) [0]
965	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	173.17 (0.00) [0]
966	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	42.62 (0.00) [0]

967	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2022]	157.86 (-) [157.86]	55.86 (0.00) [0]
968	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
969	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (9/2021) [9/2021]	553.51 (-) [553.51]	198.39 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
970	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [12/2023]	2,393.47 (5,021.45) [6,527.00]	4,525.01 (4,133.53) [117]
	<u>Road Transport And Highways</u>				
971	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [11/2021]	205.95 (-) [205.95]	123.24 (0.00) [0]
972	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2022) [0/0]	195.04 (434.65) [377.99]	368.39 (182.95) [0]
973	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2021) [0/0]	186.96 (-) [322.24]	308.85 (135.28) [0]
974	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2022) [0/0]	193.69 (374.59) [327.92]	323.23 (134.23) [0]
975	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	27.90 (0.00) [0]
976	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	33.21 (0.00) [0]
977	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	59.06 (0.00) [0]
978	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	59.29 (0.00) [0]
979	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	120.63 (0.00) [0]
980	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	43.01 (0.00) [0]
981	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	12.72 (0.00) [0]
982	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	34.80 (0.00) [0]
983	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
984	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
985	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	98.33 (0.00) [43]
986	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED	4/2017	9/2019	640.07	107.05

	SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO		(6/2023) [7/2023]	(-) [640.07]	(0.00) [46]
987	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	642.96 (-) [642.96]	115.64 (0.00) [45]
988	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [4/2023]	473.18 (-) [473.18]	128.15 (0.00) [43]
989	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	518.53 (-) [518.53]	137.11 (0.00) [45]
990	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (9/2023) [9/2023]	428.11 (-) [428.11]	90.39 (0.00) [48]
991	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (3/2024) [4/2024]	404.29 (-) [404.29]	51.36 (0.00) [55]
992	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [4/2023]	537.82 (-) [537.82]	142.87 (0.00) [43]
993	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2022) [0/0]	624.41 (1,109.88) [992.67]	978.43 (368.26) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
994	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
995	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (9/2023) [9/2023]	328.00 (-) [328.00]	298.78 (0.00) [30]
996	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (404.45) [404.45]	248.72 (84.69) [0]
997	RECAST PR FOR DHANKASA UG (1.00 MTY)	9/2016	3/2022 (3/2025) [3/2025]	289.29 (-) [289.30]	37.55 (0.01) [36]
	<u>Dpiit</u>				
998	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (1/2014) [7/2021]	12,579.09 (-) [13,812.30]	9,574.07 (1,233.21) [0]
	<u>Heavy Industry</u>				
999	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	4/2011	9/2011 (3/2021) [3/2021]	1,718.00 (3,727.30) [3,727.30]	3,526.63 (2,009.30) [0]
	<u>Petroleum</u>				
1000	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	3/2021 (12/2021) [3/2022]	1,823.00 (3,027.90) [3,027.90]	2,225.58 (1,204.90) [12]
1001	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2021]	571.66 (-) [510.00]	486.90 (-61.66) [24]
1002	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [6/2023]	3,308.00 (3,060.00) [3,060.00]	2,705.00 (-248.00) [18]
1003	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	438.32 (0.00) [0]
1004	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [3/2022]	3,437.00 (3,048.00) [3,048.00]	2,230.20 (-389.00) [15]

1005	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS	6/2019	12/2029 (-) [12/2029]	169.00 (-) [169.00]	40.12 (0.00) [0]
1006	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	130.22 (0.00) [0]
1007	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	355.80 (0.00) [0]
1008	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [3/2022]	2,433.00 (-) [2,433.00]	2,213.00 (0.00) [15]
1009	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (8/2022) [7/2022]	2,677.00 (-) [3,072.00]	2,673.55 (395.00) [13]
1010	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [8/2024]	2,915.00 (5,909.00) [5,909.00]	3,778.50 (2,994.00) [140]
1011	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [1/2022]	2,881.40 (-) [2,000.00]	1,653.50 (-881.40) [13]
1012	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	1,789.70 (0.00) [0]
1013	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (3/2022) [3/2022]	2,321.00 (3,338.00) [3,338.00]	3,124.58 (1,017.00) [15]
1014	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (5/2021) [3/2022]	690.00 (-) [690.00]	606.58 (0.00) [44]
1015	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2022]	406.00 (-) [406.00]	283.17 (0.00) [17]
1016	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	553.20 (0.00) [0]
	<u>Power</u>				
1017	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (3/2024) [3/2024]	4,754.42 (9,129.32) [9,129.32]	2,911.97 (4,374.90) [63]
1018	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (8/2021) [1/2022]	358.83 (-) [358.83]	262.19 (0.00) [20]
1019	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (12/2021) [2/2022]	522.29 (546.36) [546.36]	480.89 (24.07) [63]
1020	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (12/2020) [2/2022]	3,500.00 (3,500.00) [3,994.00]	3,099.43 (494.00) [19]
1021	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (11/2021) [2/2022]	235.53 (-) [235.53]	157.92 (0.00) [32]
1022	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (4/2022) [4/2022]	322.30 (-) [322.30]	205.25 (0.00) [38]
1023	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [3/2022]	197.40 (-) [197.40]	90.75 (0.00) [48]
1024	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (9/2021) [6/2021]	5,070.13 (-) [5,070.13]	4,231.07 (0.00) [0]

1025	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (7/2021) [10/2021]	14,733.37 (-) [14,733.37]	11,773.07 (0.00) [0]
1026	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (9/2021) [10/2021]	1,931.39 (-) [1,931.39]	1,825.25 (0.00) [0]
1027	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (12/2021) [3/2022]	5,111.33 (6,700.00) [6,700.00]	3,326.92 (1,588.67) [39]
1028	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (11/2022) [5/2023]	11,130.19 (14,719.10) [14,719.10]	13,038.20 (3,588.91) [117]
1029	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (9/2021) [1/2022]	379.95 (-) [379.95]	236.27 (0.00) [25]
1030	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (7/2021) [6/2021]	808.63 (-) [808.63]	690.59 (0.00) [0]
1031	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [12/2021]	374.63 (-) [374.63]	259.30 (0.00) [68]
	<u>Railways</u>				
1032	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	18,841.98 (0.00) [0]
1033	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2021]	288.35 (-) [502.48]	521.63 (214.13) [0]
1034	BARIARPUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.11 (-200.00) [-]
1035	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (-) [2/2022]	704.31 (927.94) [927.94]	691.26 (223.63) [23]
1036	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2022]	175.80 (-) [495.10]	316.82 (319.30) [-]
1037	CHANDIGARH-BADDI	4/2007	3/2023 (12/2025) [12/2025]	328.14 (-) [1,540.13]	243.28 (1,211.99) [33]
1038	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	40.65 (-1.00) [-]
1039	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [3/2030]	523.52 (-) [1,205.00]	2.28 (681.48) [-]
1040	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2022]	295.00 (-) [610.00]	595.91 (315.00) [37]
1041	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	116.44 (651.22) [0]
1042	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	97.40 (173.89) [96]
1043	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2023) [3/2023]	1,347.26 (1,524.68) [1,524.68]	1,004.89 (177.42) [12]
1044	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2025) [3/2025]	1,640.04 (1,640.04) [1,640.04]	882.29 (0.00) [36]

1045	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [439.30]	507.59 (74.13) [96]
1046	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/	336.91	597.99
			(-) [9/2023]	(-) [791.39]	(454.48) [-]
1047	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	638.35 (818.35) [133]
1048	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/	2,030.50	0.00
			(4/2010) [12/2027]	(-) [2,030.50]	(0.00) [-]
1049	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1050	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/	11,589.00	0.00
			(-) [0/0]	(30,357.00) [28,181.00]	(16,592.00) [0]
1051	GAYA-CHATRA (NL)	4/2008	/	415.67	15.58
			(-) [0/0]	(-) [549.75]	(134.08) [0]
1052	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (12/2024) [12/2024]	2,912.96 (-) [3,845.60]	471.73 (932.64) [33]
1053	HAJIPUR - BACHAWARA	5/2015	3/2019 (12/2021) [12/2021]	678.54 (678.54) [929.86]	958.41 (251.32) [33]
1054	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/	172.03	11.77
			(-) [3/2025]	(-) [260.10]	(88.07) [-]
1055	HATHUA-BHATNI (NL) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1056	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2024]	1,614.59 (1,877.81) [1,878.00]	1,496.77 (263.41) [60]
1057	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.75 (0.00) [0]
1058	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	0.02
			(-) [3/2025]	(-) [166.89]	(0.00) [-]
1059	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [0/0]	625.00 (-) [839.00]	839.36 (214.00) [0]
1060	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2027]	2,132.77 (-) [3,037.95]	347.10 (905.18) [156]
1061	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	618.75 (71.58) [108]
1062	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/	174.56	71.43
			(-) [3/2025]	(-) [174.56]	(0.00) [-]
1063	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,613.72 (0.00) [36]
1064	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [1,952.68]	729.57 (95.73) [12]
1065	KURUPPANTHARA-CHINGAVANAM	4/2007	/	270.14	578.46

			(12/2021) [3/2022]	(457.08) [749.40]	(479.26) [-]
1066	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	149.31 (138.71) [228]
1067	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,908.60 (8,000.84) [202]
1068	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	109.63 (0.00) [132]
1069	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2027]	120.70 (-) [2,172.16]	308.35 (2,051.46) [105]
1070	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	142.05 (180.72) [157]
1071	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	410.29 (59.77) [-]
1072	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2023]	1,723.00 (1.00) [3,421.35]	2,010.00 (1,698.35) [276]
1073	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [0/0]	414.84 (-) [750.00]	157.51 (335.16) [0]
1074	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [11/2024]	450.00 (-) [2,017.96]	878.49 (1,567.96) [148]
1075	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	3/2019	5/2023 (-) [12/2023]	1,866.31 (-) [1,866.31]	288.29 (0.00) [7]
1076	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	30.12 (0.05) [240]
1077	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [0/0]	242.22 (-) [471.00]	76.57 (228.78) [0]
1078	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (12/2021) [6/2022]	241.52 (-) [373.87]	333.46 (132.35) [-]
1079	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [12/2023]	1,798.00 (2,042.51) [2,042.51]	446.24 (244.51) [57]
1080	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,090.60]	1,089.12 (271.37) [0]
1081	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [12/2021]	1,180.19 (2,531.34) [4,541.38]	3,936.64 (3,361.19) [156]
1082	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [10/2022]	600.00 (-) [701.81]	334.01 (101.81) [31]
1083	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	453.42 (1,221.83) [36]
1084	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1085	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-)	2,082.75 (-)	191.39 (2,179.61)

			[0/0]	[4,262.36]	[0]
1086	RAYADURGA-TUMKUR NL	4/2007	/	2,062.30	1,100.11
			(-)	(-)	(341.73)
			[12/2025]	[2,404.03]	[-]
1087	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/	297.47	36.13
			(-)	(-)	(0.75)
			[3/2025]	[298.22]	[-]
1088	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016	277.28	201.29
			(-)	(-)	(-10.96)
			[3/2025]	[266.32]	[108]
1089	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/	296.00	0.00
			(-)	(-)	(170.65)
			[12/2023]	[466.65]	[-]
1090	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/	450.00	0.00
			(-)	(-)	(811.34)
			[3/2025]	[1,261.34]	[-]
1091	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/	365.17	1.76
			(-)	(-)	(162.37)
			[3/2025]	[527.54]	[-]
1092	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020	16,592.00	22,485.00
			(-)	(51,101.00)	(34,509.00)
			[0/0]	[51,101.00]	[0]
1093	YELAHANKA-PENUKONDA	5/2015	3/2020	860.43	983.01
			(-)	(-)	(243.57)
			[9/2021]	[1,104.00]	[0]
	<u>Road Transport And Highways</u>				
1094	4 LANING OF NAGPUR-BETUL	2/2011	8/2014	2,498.76	2,531.46
			(-)	(-)	(0.00)
			[0/0]	[2,498.76]	[0]
1095	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015	1,928.22	1,890.04
			(1/2021)	(1,928.22)	(0.00)
			[12/2021]	[1,928.22]	[80]
1096	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/	1,294.47	0.00
			(-)	(-)	(1.53)
			[11/2021]	[1,296.00]	[0]
1097	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/	998.70	0.00
			(-)	(-)	(-36.70)
			[11/2018]	[962.00]	[0]
1098	GWALIOR-JHANSI, NH-75	12/2003	12/2009	604.00	360.15
			(9/2020)	(-)	(-239.41)
			[9/2020]	[364.59]	[0]
1099	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013	754.00	1,364.18
			(-)	(-)	(0.00)
			[0/0]	[754.00]	[0]
1100	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/	1,244.10	1,665.00
			(-)	(-)	(0.00)
			[0/0]	[1,244.10]	[0]
1101	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011	1,693.75	2,848.49
			(-)	(-)	(0.00)
			[0/0]	[1,693.75]	[0]
1102	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014	2,848.00	3,379.45
			(-)	(-)	(531.45)
			[12/2022]	[3,379.45]	[105]
	<u>Shipping And Ports</u>				
1103	JAL MARG VIKAS PROJECT	1/2018	3/2023	5,369.18	1,967.38
			(-)	(4,633.81)	(-735.37)
			[3/2023]	[4,633.81]	[0]
	<u>Telecommunications</u>				
1104	NETWORK FOR SPECTRUM	3/2012	7/2015	13,334.00	20,545.00
			(5/2020)	(24,664.00)	(11,330.00)
			[3/2022]	[24,664.00]	[80]

1105	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021 (11/2021) [3/2022]	431.16 (422.87) [422.87]	70.25 (-8.29) [9]
	<u>Urban Development</u>				
1106	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	6,074.70 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1107	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1108	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	1,420.48 (4,336.48) [132]
	<u>Road Transport And Highways</u>				
1109	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	128.80 (0.00) [44]
1110	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	100.70 (0.00) [48]
1111	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	175.63 (0.00) [0]
1112	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	333.24 (0.00) [42]
1113	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	132.56 (0.00) [50]
1114	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	56.39 (0.00) [0]
1115	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	70.73 (0.00) [0]
1116	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	38.95 (0.00) [0]
1117	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	67.50 (0.00) [0]
1118	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	49.90 (0.00) [0]
1119	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	79.89 (0.00) [0]
1120	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [6/2022]	206.53 (-) [206.53]	81.84 (0.00) [0]
1121	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (4/2022) [0/0]	217.35 (-) [217.35]	104.81 (0.00) [0]
1122	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	52.44 (0.00) [0]
1123	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (118.56) [202.36]	7.02 (0.00) [0]

1124	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (177.00) [277.44]	33.95 (0.00) [0]
1125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	182.63 (0.00) [46]
1126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	120.99 (0.00) [39]
1127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	125.87 (0.00) [39]
1128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	112.26 (0.00) [0]
1129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	77.62 (0.00) [39]
1130	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	68.70 (0.00) [49]
1131	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	157.06 (0.00) [0]
1132	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	134.89 (0.00) [0]
1133	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	352.25 (13.93) [0]
1134	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	311.17 (0.00) [0]
1135	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (369.96) [369.96]	322.13 (33.71) [0]
1136	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	0.00 (0.00) [0]
1137	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	20.00 (0.00) [0]
1138	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	167.62 (-) [167.62]	118.61 (0.00) [0]
1139	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]
1140	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (167.23) [315.63]	9.39 (0.00) [0]
1141	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [7/2022]	237.51 (-) [237.51]	96.49 (0.00) [-5]
	ODISHA				
	Coal				
1142	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [0/0]	207.28 (-) [207.28]	206.89 (0.00) [0]
1143	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-)	479.15 (-)	254.06 (0.00)

			[3/2024]	[479.15]	[60]
1144	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3/2017 (-) [3/2031]	3,145.45 (-) [3,145.45]	661.05 (0.00) [168]
1145	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY)	12/2007	3/2010 (3/2029) [3/2029]	3,504.21 (3,504.21) [3,504.21]	606.54 (0.00) [228]
1146	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY)	12/2007	3/2013 (3/2028) [3/2028]	8,416.19 (8,416.19) [8,416.19]	1,166.07 (0.00) [180]
1147	GARJANBAHAL OCP	11/2014	3/2021 (-) [9/2025]	1,375.38 (-) [1,375.38]	683.47 (0.00) [54]
1148	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2024]	479.53 (-) [808.97]	808.97 (329.44) [132]
1149	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	773.61 (0.00) [0]
1150	NAINI COAL MINE	3/2020	3/2024 (-) [3/2024]	494.30 (-) [494.30]	111.78 (0.00) [0]
1151	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,318.06 (0.00) [0]
1152	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	2,697.74 (0.00) [0]
1153	TALABIRA II AND III OCP	7/2017	7/2020 (-) [4/2020]	2,401.07 (-) [2,401.07]	918.03 (0.00) [0]
	<u>Department Of Higher Education</u>				
1154	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [6/2022]	790.79 (-) [790.79]	258.32 (0.00) [3]
	<u>Mines</u>				
1155	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (1/2024) [1/2024]	5,540.00 (6,435.90) [5,540.00]	1,182.87 (0.00) [33]
1156	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [12/2023]	355.00 (-) [355.00]	95.45 (0.00) [37]
1157	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (12/2023) [12/2023]	483.00 (483.00) [483.00]	10.40 (0.00) [32]
1158	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [0/0]	534.00 (-) [534.00]	394.68 (0.00) [0]
	<u>Petroleum</u>				
1159	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [6/2023]	1,607.00 (-) [1,607.00]	304.87 (0.00) [10]
1160	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (6/2022) [6/2022]	462.30 (-) [462.30]	140.65 (0.00) [9]
1161	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (8/2021) [1/2022]	315.00 (-) [315.00]	228.42 (0.00) [1]
1162	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	166.06 (0.00) [0]

1163	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	99.81 (0.00) [0]
1164	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [3/2022]	1,933.00 (-) [1,933.00]	1,584.90 (0.00) [15]
1165	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (7/2022) [7/2022]	5,654.00 (-) [5,654.00]	3,566.10 (0.00) [9]
1166	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (9/2022) [9/2022]	3,361.00 (-) [3,361.00]	2,099.36 (0.00) [13]
1167	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	61.04 (0.00) [0]
1168	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2023) [3/2023]	371.00 (427.00) [427.00]	35.56 (56.00) [6]
1169	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	579.94 (0.00) [0]
1170	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [10/2022]	161.59 (-) [161.59]	64.47 (0.00) [34]
1171	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [3/2022]	1,297.50 (-) [1,297.50]	883.78 (0.00) [5]
	<u>Power</u>				
1172	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [1/2022]	1,885.13 (2,311.89) [2,311.89]	2,094.59 (426.76) [37]
	<u>Railways</u>				
1173	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,536.00]	1,269.37 (593.05) [39]
1174	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2024) [3/2024]	843.04 (843.04) [843.04]	284.93 (0.00) [41]
1175	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2024) [3/2024]	1,172.92 (1,172.92) [1,172.92]	718.37 (0.00) [63]
1176	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [3/2019]	149.90 (-) [266.61]	239.38 (116.71) [0]
1177	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2023]	1,547.38 (1,547.38) [1,547.38]	710.98 (0.00) [12]
1178	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2024]	701.61 (-) [810.02]	193.71 (108.41) [64]
1179	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (12/2022) [0/0]	133.41 (207.00) [433.00]	419.58 (299.59) [0]
1180	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (12/2024) [12/2024]	2,923.13 (3,791.66) [3,791.66]	1,687.63 (868.53) [189]
1181	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	524.03 (0.00) [48]
1182	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-)	969.83 (-)	1,119.38 (343.13)

			[6/2022]	[1,312.96]	[27]
1183	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2022]	155.81 (238.03) [238.03]	224.26 (82.22) [24]
1184	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [12/2021]	948.04 (-) [2,009.00]	2,156.59 (1,060.96) [21]
1185	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2022]	1,111.99 (-) [1,539.28]	1,195.24 (427.29) [37]
1186	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,894.70 (1,237.83) [88]
1187	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (3/2025) [3/2025]	810.78 (1,928.07) [1,928.07]	933.16 (1,117.29) [45]
1188	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	2,024.04 (992.05) [24]
	<u>Road Transport And Highways</u>				
1189	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [0/0]	1,282.94 (-) [1,282.94]	720.08 (0.00) [0]
1190	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [0/0]	2,510.04 (-) [2,510.04]	637.56 (0.00) [0]
1191	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [3/2022]	752.28 (-) [752.28]	284.66 (0.00) [-]
1192	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [0/0]	1,069.65 (-) [1,069.65]	836.93 (0.00) [0]
1193	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	14.80 (0.00) [0]
1194	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [0/0]	1,008.96 (-) [1,008.96]	1,125.65 (0.00) [0]
1195	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [0/0]	564.66 (-) [564.66]	394.94 (0.00) [0]
1196	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [0/0]	476.56 (-) [476.56]	225.64 (0.00) [0]
1197	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	188.00 (0.00) [0]
1198	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [3/2022]	953.09 (-) [953.09]	473.95 (0.00) [-]
1199	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [0/0]	668.86 (-) [668.86]	413.00 (0.00) [0]
1200	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	330.58 (0.00) [0]
1201	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [0/0]	503.88 (-) [503.88]	138.56 (0.00) [0]
1202	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000	3/2017	3/2020 (-)	1,288.07 (-)	1,058.45 (131.93)

	TO KM		[0/0]	[1,420.00]	[0]
1203	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/	686.65	290.00
			(-)	(-)	(0.00)
			[0/0]	[686.65]	[0]
1204	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/	686.65	254.00
			(-)	(-)	(0.00)
			[0/0]	[686.65]	[0]
1205	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/	417.51	264.15
			(-)	(-)	(0.00)
			[0/0]	[417.51]	[0]
1206	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/	999.00	178.93
			(-)	(-)	(0.00)
			[0/0]	[999.00]	[0]
1207	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016	171.96	101.27
			(-)	(172.00)	(0.04)
			[0/0]	[172.00]	[0]
1208	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/	1,522.00	512.80
			(-)	(-)	(0.00)
			[0/0]	[1,522.00]	[0]
1209	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014	1,047.00	1,873.47
			(-)	(-)	(0.00)
			[0/0]	[1,047.00]	[0]
1210	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/	806.11	415.39
			(-)	(-)	(0.00)
			[0/0]	[806.11]	[0]
1211	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016	191.50	183.94
			(-)	(192.00)	(0.50)
			[0/0]	[192.00]	[0]
1212	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015	191.08	182.41
			(-)	(-)	(0.00)
			[0/0]	[191.08]	[0]
1213	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA	8/2016	2/2017	287.70	216.18
			(-)	(-)	(0.00)
			[0/0]	[287.70]	[0]
1214	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018	214.23	115.67
			(-)	(-)	(0.00)
			[0/0]	[214.23]	[0]
1215	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018	223.50	144.36
			(-)	(-)	(0.00)
			[0/0]	[223.50]	[0]
1216	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018	199.16	124.19
			(-)	(-)	(0.00)
			[0/0]	[199.16]	[0]
1217	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017	295.67	208.91
			(-)	(-)	(0.00)
			[0/0]	[295.67]	[0]
1218	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018	206.88	127.72
			(-)	(-)	(0.00)
			[0/0]	[206.88]	[0]
	<u>Steel</u>				
1219	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023	377.18	51.69
			(-)	(-)	(0.00)
			[5/2023]	[377.18]	[0]
	<u>PONDICHERRY</u>				
	<u>Health And Family Welfare</u>				
1220	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020	195.00	16.41
			(-)	(-)	(0.00)
			[4/2022]	[195.00]	[19]
	<u>PUNJAB</u>				
	<u>Department Of Higher Education</u>				
1221	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN	10/2019	5/2022	348.24	34.60

	INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.		(-) [10/2022]	(-) [348.24]	(0.00) [5]
1222	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [6/2022]	430.00 (-) [387.83]	237.59 (-42.17) [25]
	<u>Fertilisers</u>				
1223	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (5/2021) [0/0]	218.83 (-) [218.83]	200.30 (0.00) [0]
1224	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (5/2021) [0/0]	239.81 (-) [239.81]	205.94 (0.00) [0]
	<u>Health And Family Welfare</u>				
1225	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [0/0]	703.00 (-) [557.48]	553.85 (-145.52) [0]
1226	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [3/2021]	152.95 (-) [177.92]	164.17 (24.97) [0]
	<u>Petroleum</u>				
1227	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,421.46]	229.78 (0.00) [0]
	<u>Railways</u>				
1228	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	190.00 (0.00) [108]
1229	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	<u>Road Transport And Highways</u>				
1230	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (1,367.00) [2,280.00]	1,367.00 (1,110.39) [0]
1231	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [904.82]	851.32 (15.58) [0]
1232	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [0/0]	1,388.34 (-) [1,588.29]	798.71 (199.95) [0]
1233	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [9/2022]	754.54 (-) [756.27]	449.44 (1.73) [30]
1234	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1	12/2020	1/2024 (-) [1/2024]	733.00 (-) [733.00]	0.00 (0.00) [0]
1235	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH-	2/2021	4/2024 (-) [4/2024]	1,269.96 (-) [1,269.96]	0.00 (0.00) [0]
1236	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR-	2/2021	4/2024 (-) [4/2024]	853.66 (-) [853.66]	0.00 (0.00) [0]
1237	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO	12/2020	4/2024 (-) [4/2024]	1,094.46 (-) [1,094.46]	0.00 (0.00) [0]
1238	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI	12/2020	1/2024 (-) [1/2024]	989.66 (-) [989.66]	0.00 (0.00) [0]
1239	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO	12/2020	4/2024 (-) [4/2024]	1,234.40 (-) [1,234.40]	0.00 (0.00) [0]

1240	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO	12/2020	4/2024 (-) [4/2024]	881.00 (-) [881.00]	0.00 (0.00) [0]
1241	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [2/2022]	261.76 (-) [207.00]	205.00 (-54.76) [-]
1242	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [3/2022]	479.00 (-) [479.00]	456.80 (0.00) [-]
1243	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [8/2021]	1,069.59 (-) [1,069.59]	734.04 (0.00) [0]
1244	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [0/0]	196.05 (-) [196.05]	143.03 (0.00) [0]
1245	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (-) [199.90]	124.52 (0.00) [0]
1246	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [0/0]	170.57 (194.48) [170.57]	75.41 (0.00) [0]
1247	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [0/0]	293.64 (-) [293.64]	261.09 (0.00) [0]
1248	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [0/0]	293.10 (-) [293.10]	201.14 (0.00) [0]
RAJASTHAN					
Atomic Energy					
1249	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2023]	12,320.00 (-) [17,079.00]	13,945.00 (4,759.00) [84]
Coal					
1250	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020 (-) [0/0]	2,112.60 (-) [2,112.60]	93.05 (0.00) [0]
1251	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]
1252	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020 (-) [0/0]	2,196.30 (-) [2,196.30]	143.95 (0.00) [0]
1253	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
Department Of Higher Education					
1254	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (-) [0/0]	549.31 (-) [559.47]	458.38 (10.16) [0]
Petroleum					
1255	LPG BP PROJECT JODHPUR	3/2018	/ (5/2022) [12/2022]	229.80 (-) [229.80]	96.11 (0.00) [-]
Power					
1256	ANTA SOLAR 90 MW	1/2021	3/2022 (3/2022) [5/2022]	382.22 (-) [382.22]	4.15 (0.00) [2]
1257	BHENSARA 320 MW	1/2021	7/2022 (5/2022) [8/2022]	1,221.73 (-) [1,221.73]	140.11 (0.00) [1]
1258	CHHATTARGARH 150 MW	2/2021	7/2022	599.99	62.06

			(-) [8/2022]	(-) [599.99]	(0.00) [1]
1259	FATEHGARH SOLAR 296MW	3/2020	9/2021 (10/2022) [10/2022]	1,749.31 (-) [1,749.31]	1,339.51 (0.00) [13]
1260	JETSAR SOLAR 160 MW	12/2019	3/2021 (11/2021) [1/2022]	702.28 (-) [702.28]	586.88 (0.00) [10]
1261	SAMBHU KI BHURJ SOLAR 250 MW	1/2020	9/2021 (8/2022) [8/2022]	1,522.71 (-) [1,522.71]	1,009.07 (0.00) [11]
1262	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (10/2022) [10/2022]	1,782.00 (-) [1,782.00]	836.25 (0.00) [13]
	Railways				
1263	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/	873.71	4.60
			(-) [0/0]	(-) [2,215.27]	(1,341.56) [0]
1264	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/	822.00	0.00
			(-) [0/0]	(-) [821.64]	(-0.36) [0]
1265	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [6/2022]	410.08 (-) [860.41]	769.95 (450.33) [40]
1266	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [11/2022]	808.85 (-) [808.85]	413.98 (0.00) [3]
1267	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [9/2021]	420.18 (-) [480.00]	384.12 (59.82) [0]
1268	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [0/0]	493.17 (-) [493.17]	464.53 (0.00) [0]
1269	PUSHKAR-MERTA	4/2013	/	323.00	0.00
			(-) [0/0]	(-) [322.98]	(-0.02) [0]
	Road Transport And Highways				
1270	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [0/0]	370.36 (-) [370.36]	216.79 (0.00) [0]
1271	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	0.00 (0.00) [0]
1272	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [0]
1273	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG-	2/2021	11/2021 (-) [11/2021]	240.99 (-) [240.99]	0.00 (0.00) [0]
1274	4/2 LANNING WITH PS DAUSA-LALSOT-KAUNTHUN SECTION OF NH-11A	7/2016	/	688.70	870.48
			(-) [0/0]	(-) [688.70]	(0.00) [0]
1275	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II	8/2020	12/2020 (-) [0/0]	216.72 (-) [216.72]	44.71 (0.00) [0]
1276	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II.	12/2020	10/2021 (-) [0/0]	339.65 (-) [339.65]	28.53 (0.00) [0]
1277	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I.	12/2020	10/2021 (-) [0/0]	379.23 (-) [379.23]	16.94 (0.00) [0]

1278	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I.	7/2020	9/2021 (-) [0/0]	319.09 (-) [319.09]	12.89 (0.00) [0]
1279	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [3/2022]	1,031.95 (-) [1,031.95]	1,513.48 (0.00) [-]
1280	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [0/0]	178.13 (-) [178.13]	164.94 (0.00) [0]
1281	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [12/2021]	822.90 (-) [822.90]	844.08 (0.00) [44]
1282	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	496.04 (0.00) [0]
1283	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [7/2020]	163.95 (-) [163.95]	122.04 (0.00) [0]
1284	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (7/2021) [7/2021]	716.76 (-) [716.76]	687.07 (0.00) [0]
1285	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	307.43 (0.00) [0]
1286	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	330.46 (0.00) [0]
1287	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [0/0]	763.23 (-) [763.23]	191.80 (0.00) [0]
1288	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM	6/2016	6/2019 (-) [0/0]	649.00 (-) [649.00]	690.17 (0.00) [0]
1289	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	964.60 (0.00) [0]
1290	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1291	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020 (-) [0/0]	196.23 (-) [196.00]	51.56 (-0.23) [0]
1292	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [0/0]	1,100.19 (-) [1,145.31]	1,355.00 (45.12) [0]
1293	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [3/2022]	894.00 (-) [929.32]	810.00 (35.32) [23]
1294	TWO LANING WITH PAVED SHOULDER OF KARAU II - DHOLPUR	9/2014	9/2016 (-) [0/0]	425.19 (-) [425.19]	276.40 (0.00) [0]
1295	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [0/0]	275.90 (-) [275.90]	289.13 (0.00) [0]
1296	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1297	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU R	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	550.35 (0.00) [0]
1298	UP-GRADATION TO TWO LANING WITH PAVED	3/2020	8/2020	255.23	69.53

	SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO		(-) [0/0]	(-) [255.23]	(0.00) [0]
1299	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (10/2021) [10/2021]	874.25 (866.55) [866.55]	866.55 (-7.70) [0]
1300	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	328.41 (0.00) [0]
1301	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [0/0]	1,103.88 (-) [1,103.88]	713.42 (0.00) [0]
1302	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	242.67 (0.00) [0]
1303	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	136.22 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1304	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [12/2023]	1,339.48 (4,084.69) [8,600.00]	1,856.78 (7,260.52) [96]
	<u>Road Transport And Highways</u>				
1305	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	2.58 (0.00) [0]
1306	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [11/2023]	493.42 (-) [493.42]	0.00 (0.00) [0]
1307	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	26.51 (0.00) [0]
1308	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	86.64 (0.00) [0]
1309	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	76.84 (0.00) [0]
1310	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	120.72 (0.00) [0]
1311	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	76.23 (0.00) [0]
1312	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [12/2021]	290.05 (-) [290.05]	154.83 (0.00) [49]
1313	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (-) [12/2023]	816.79 (-) [816.79]	2.20 (0.00) [0]
1314	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
1315	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	69.72 (0.00) [0]
1316	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	32.85 (0.00) [0]
1317	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO	3/2020	6/2022 (-)	242.97 (-)	59.98 (0.00)

	KM 40.00		[6/2022]	[242.97]	[0]
1318	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	42.83 (0.00) [0]
1319	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	295.14 (59.37) [0]
1320	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
1321	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1322	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6	6/2017	9/2027 (-) [9/2027]	49,621.00 (-) [49,621.00]	5,074.00 (0.00) [0]
1323	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	27,505.00 (0.00) [36]
1324	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2022]	3,492.00 (-) [6,840.00]	6,054.37 (3,348.00) [145]
	<u>Civil Aviation</u>				
1325	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (12/2023) [0/0]	380.87 (-) [380.87]	16.17 (0.00) [0]
1326	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [6/2024]	2,467.00 (-) [2,467.00]	763.60 (0.00) [28]
1327	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [12/2022]	951.28 (-) [951.28]	513.93 (0.00) [14]
	<u>Coal</u>				
1328	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (3/2025) [3/2025]	1,458.17 (709.06) [709.06]	496.19 (-749.11) [117]
1329	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (7,980.79) [7,980.79]	7,421.14 (2,073.68) [0]
	<u>Finance</u>				
1330	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [7/2021]	209.00 (-) [208.96]	208.93 (-0.04) [0]
1331	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	204.00 (0.00) [0]
	<u>Mines</u>				
1332	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (12/2022) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [0]
	<u>Petroleum</u>				
1333	AUGMENTATION OF CTMPL	12/2016	11/2021 (-) [12/2021]	228.00 (-) [228.00]	160.74 (0.00) [1]
1334	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	202.71 (0.00) [0]
1335	CGD PROJECT AT SALEM DISTRICT	10/2018	3/2030 (-)	1,304.00 (-)	42.90 (0.00)

			[3/2030]	[1,304.00]	[0]
1336	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [2/2024]	921.00 (-) [921.00]	5.59 (0.00) [5]
1337	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (1/2022) [3/2022]	466.43 (-) [466.43]	279.29 (0.00) [17]
1338	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (2/2022) [2/2022]	4,497.00 (6,025.00) [6,025.00]	4,159.59 (1,528.00) [38]
1339	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1340	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (9/2021) [9/2021]	650.82 (-) [624.35]	455.96 (-26.47) [0]
1341	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [8/2022]	678.00 (1,472.00) [1,472.00]	19.44 (794.00) [66]
1342	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [12/2021]	421.00 (-) [315.00]	295.84 (-106.00) [16]
1343	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [1/2024]	1,398.00 (-) [1,398.00]	134.42 (0.00) [1]
	<u>Power</u>				
1344	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (8/2022) [8/2022]	1,316.22 (-) [1,316.22]	888.48 (0.00) [11]
1345	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (7/2021) [3/2022]	186.17 (219.66) [219.66]	168.20 (33.49) [32]
	<u>Railways</u>				
1346	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [3/2030]	151.84 (-) [527.37]	2.59 (375.53) [133]
1347	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (9/2021) [12/2022]	931.98 (-) [1,122.00]	994.02 (190.02) [-]
1348	ERODE-PALANI	4/2008	/ (-) [3/2030]	288.57 (-) [603.23]	1.68 (314.66) [-]
1349	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (7/2022) [7/2022]	495.74 (-) [774.51]	492.88 (278.77) [109]
1350	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2022]	760.00 (-) [1,536.00]	1,509.71 (776.00) [27]
1351	MADURAI-BODINAYAKKANUR	4/2008	/ (12/2021) [2/2022]	164.41 (-) [608.13]	427.75 (443.72) [-]
1352	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [6/2022]	1,700.00 (-) [1,305.00]	1,111.90 (-395.00) [3]
1353	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [3,081.20]	1,718.56 (2,356.51) [73]
1354	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [3/2030]	839.00 (-) [839.01]	0.63 (0.01) [-]
1355	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT	2/1996	3/2005	268.87	922.01

	SYSTEM (PHASE II)		(-) [12/2021]	(-) [991.83]	(722.96) [201]
1356	TIDIVANAM-NAGARI (NL)	9/2006	/	582.83	239.59
			(-) [12/2025]	(-) [3,154.43]	(2,571.60) [-]
1357	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/	227.40	65.02
			(-) [3/2030]	(-) [227.40]	(0.00) [-]
1358	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020	303.98	712.68
			(-) [3/2025]	(-) [1,549.09]	(1,245.11) [60]
1359	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024	1,567.00	0.00
			(-) [3/2026]	(-) [1,567.00]	(0.00) [24]
	Road Transport And Highways				
1360	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013	485.00	271.64
			(-) [0/0]	(-) [485.00]	(0.00) [0]
1361	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014	624.00	97.97
			(-) [1/2022]	(-) [624.00]	(0.00) [93]
1362	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017	244.27	178.41
			(-) [0/0]	(-) [244.27]	(0.00) [0]
1363	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017	1,227.87	810.81
			(-) [7/2022]	(-) [1,227.87]	(0.00) [58]
1364	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015	258.97	229.77
			(-) [0/0]	(273.27) [268.92]	(9.95) [0]
1365	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013	600.00	7.73
			(-) [9/2021]	(-) [600.00]	(0.00) [0]
1366	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/	1,016.92	339.86
			(-) [1/2022]	(-) [1,071.00]	(54.08) [-]
1367	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017	1,387.11	980.46
			(-) [0/0]	(-) [1,387.11]	(0.00) [0]
1368	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/	628.71	397.89
			(-) [3/2022]	(-) [628.71]	(0.00) [-]
1369	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/	2,065.96	0.00
			(-) [12/2021]	(-) [2,169.00]	(103.04) [-]
1370	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/	1,166.26	346.17
			(-) [1/2022]	(-) [1,296.93]	(130.67) [-]
1371	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016	641.17	403.81
			(-) [12/2021]	(-) [641.17]	(0.00) [65]
1372	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/	505.35	255.05
			(-) [12/2022]	(-) [505.35]	(0.00) [-]
1373	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017	1,176.37	742.16
			(-) [7/2022]	(-) [1,176.37]	(0.00) [59]
1374	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018	707.82	434.59
			(-) [1/2022]	(-) [707.82]	(0.00) [41]
1375	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM	3/2017	3/2020	848.45	252.08

	KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.		(-) [12/2021]	(-) [848.45]	(0.00) [21]
1376	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [12/2021]	641.17 (-) [641.17]	403.81 (0.00) [41]
1377	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	7/2020	12/2021 (-) [12/2021]	3,426.00 (-) [3,426.00]	0.00 (0.00) [0]
1378	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [12/2021]	379.90 (-) [379.90]	248.71 (0.00) [-]
1379	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,342.23 (0.00) [0]
1380	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1381	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1382	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [2/2022]	374.00 (-) [166.90]	81.67 (-207.10) [105]
1383	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1384	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [5/2023]	563.92 (-) [563.92]	32.96 (0.00) [65]
1385	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (204.73) [240.38]	143.36 (0.00) [0]
1386	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8	8/2020	2/2021 (-) [0/0]	302.62 (-) [302.62]	60.72 (0.00) [0]
1387	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	210.16 (0.00) [0]
	<u>Urban Development</u>				
1388	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (2/2021) [2/2021]	3,770.00 (-) [3,770.00]	3,006.98 (0.00) [0]
1389	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (2/2019) [2/2019]	14,600.00 (18,380.00) [18,380.00]	17,619.68 (3,780.00) [0]
	<u>TELANGANA</u>				
	<u>Civil Aviation</u>				
1390	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (-) [12/2023]	353.61 (-) [353.61]	95.77 (0.00) [19]
	<u>Coal</u>				
1391	GODAVARIKHANI COAL MINE	7/2019	3/2023 (-) [3/2023]	438.98 (-) [438.98]	88.95 (0.00) [0]
1392	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2023]	447.06 (-) [473.22]	204.84 (26.16) [96]
1393	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	256.54 (0.00) [36]
1394	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019	397.09	123.72

			(-) [3/2022]	(-) [442.42]	(45.33) [36]
1395	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2022]	417.33 (-) [384.32]	144.15 (-33.01) [68]
1396	KISTARAM OCP	11/2010	3/2015 (-) [3/2022]	242.29 (-) [164.04]	143.08 (-78.25) [84]
1397	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	416.07 (70.65) [132]
1398	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2022]	162.76 (-) [349.28]	306.52 (186.52) [84]
1399	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [9/2021]	430.45 (-) [415.37]	213.44 (-15.08) [0]
1400	SRP OC-II EXPANSION PROJECT	11/2016	/ (-) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [-]
1401	VENKATESH KHANI COAL MINE	10/2020	3/2023 (-) [3/2023]	484.51 (-) [484.51]	25.43 (0.00) [0]
	<u>Health And Family Welfare</u>				
1402	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	190.46 (0.00) [0]
	<u>Petroleum</u>				
1403	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	109.24 (0.00) [16]
	<u>Power</u>				
1404	RAMAGUNDAM FLOATING SOLAR 100 MW	6/2019	4/2021 (10/2021) [1/2022]	401.90 (-) [442.03]	225.90 (40.13) [9]
1405	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [10/2022]	10,598.98 (10,997.70) [10,998.00]	9,124.00 (399.02) [23]
	<u>Railways</u>				
1406	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2021]	632.68 (-) [950.00]	839.78 (317.32) [69]
1407	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [0/0]	636.38 (-) [636.38]	653.38 (0.00) [0]
1408	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-) [0/0]	458.25 (-) [458.25]	3.69 (0.00) [0]
1409	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (3/2022) [0/0]	119.73 (176.18) [242.28]	67.29 (122.55) [0]
1410	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2024]	1,160.48 (-) [1,373.74]	654.79 (213.26) [168]
1411	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1412	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [850.00]	949.03 (76.06) [0]
	<u>Road Transport And Highways</u>				

1413	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [0/0]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [0]
1414	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [0/0]	283.15 (-) [283.15]	153.40 (0.00) [0]
1415	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [0/0]	626.76 (-) [626.76]	214.79 (0.00) [0]
1416	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.95 (0.00) [0]
1417	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1418	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	336.39 (0.00) [0]
1419	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	476.01 (0.00) [0]
1420	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	686.45 (0.00) [0]
1421	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (-) [0/0]	828.29 (-) [828.29]	0.00 (0.00) [0]
1422	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (-) [1/2022]	1,423.96 (-) [1,056.08]	1,020.25 (-367.88) [38]
1423	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [0/0]	192.67 (-) [192.67]	165.01 (0.00) [0]
1424	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [0/0]	605.08 (-) [605.08]	409.44 (0.00) [0]
1425	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [0/0]	426.52 (-) [426.52]	394.24 (0.00) [0]
1426	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	0.00 (0.00) [0]
1427	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [0/0]	294.13 (-) [294.13]	154.02 (0.00) [0]
1428	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	160.80 (0.00) [0]
1429	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [0/0]	322.81 (-) [322.81]	219.66 (0.00) [0]
1430	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [295.47]	207.71 (0.00) [0]
1431	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [0/0]	248.83 (-) [248.83]	125.54 (0.00) [0]
1432	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [0/0]	298.32 (-) [298.32]	121.49 (0.00) [0]
1433	WIDENING AND STRENGTHENING OF EXISTING 2-LANE	1/2018	12/2019	230.03	219.16

	TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4		(-) [0/0]	(-) [230.03]	(0.00) [0]
1434	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [0/0]	206.13 (-) [206.13]	184.68 (0.00) [0]
1435	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	110.26 (0.00) [0]
1436	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	116.79 (0.00) [0]
1437	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	244.54 (0.00) [0]
1438	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	166.39 (0.00) [0]
1439	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	303.83 (0.00) [0]
1440	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	205.91 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1441	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2021) [1/2022]	438.28 (-) [402.00]	397.85 (-36.28) [31]
	<u>Railways</u>				
1442	AGARTALA-AKHAURA NL	4/2012	3/2020 (6/2022) [6/2022]	569.63 (90.00) [742.00]	612.37 (172.37) [27]
	<u>Road Transport And Highways</u>				
1443	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	358.78 (0.00) [0]
1444	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	18.87 (0.00) [0]
1445	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	27.82 (0.00) [0]
1446	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	89.80 (0.00) [0]
1447	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	9.33 (0.00) [0]
1448	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	8.23 (0.00) [0]
1449	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	65.92 (0.00) [0]
1450	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	90.44 (0.00) [0]
1451	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	7.72 (0.00) [0]
1452	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022	332.14	10.88

			(-) [7/2022]	(-) [332.14]	(0.00) [0]
1453	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	10.23 (0.00) [0]
1454	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	17.99 (0.00) [0]
1455	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	42.33 (0.00) [0]
1456	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	106.99 (0.00) [0]
1457	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	95.22 (0.00) [0]
1458	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	59.74 (38.51) [0]
1459	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	142.81 (0.00) [0]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1460	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [12/2023]	1,383.00 (1,938.00) [1,938.00]	568.01 (555.00) [27]
	<u>Coal</u>				
1461	KHADIA EXPANSION OCP	6/2021	3/2025 (-) [3/2025]	491.67 (-) [491.67]	0.00 (0.00) [0]
1462	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (11/2022) [11/2022]	17,237.00 (-) [17,237.80]	12,939.55 (0.80) [12]
	<u>Health And Family Welfare</u>				
1463	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [0/0]	785.00 (-) [715.06]	604.15 (-69.94) [0]
1464	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [3/2021]	268.84 (-) [268.84]	243.92 (0.00) [0]
	<u>Home Affairs</u>				
1465	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI	5/2019	1/2022 (-) [1/2020]	199.31 (-) [199.31]	20.53 (0.00) [0]
	<u>Petroleum</u>				
1466	60 KTA POLYPROPYLENE PROJECT	3/2019	4/2024 (-) [4/2024]	910.56 (-) [910.56]	117.31 (0.00) [0]
1467	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	516.61 (0.00) [0]
1468	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (345.15) [345.15]	255.92 (57.66) [0]
1469	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (8/2029) [8/2029]	3,450.20 (-) [3,450.20]	515.69 (0.00) [5]
1470	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (3/2022)	217.92 (217.92)	105.90 (0.00)

			[3/2022]	[217.92]	[11]
1471	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (3/2022) [3/2022]	255.40 (-) [255.40]	136.20 (0.00) [19]
1472	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2022]	318.80 (-) [318.80]	179.06 (0.00) [15]
	<u>Power</u>				
1473	DEVIKOT SOLAR 150MW	1/2020	9/2021 (8/2022) [8/2022]	798.24 (-) [852.90]	541.97 (54.66) [11]
1474	DEVIKOT SOLAR 90MW	3/2020	9/2021 (10/2022) [10/2022]	501.29 (-) [524.83]	368.49 (23.54) [13]
1475	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	3,395.52 (0.00) [11]
1476	NOKHRA	3/2020	9/2021 (10/2022) [10/2022]	1,722.14 (-) [1,803.19]	552.18 (81.05) [13]
1477	PARASAN SOLAR POWER PROJECT	8/2021	12/2022 (-) [12/2022]	313.58 (-) [313.58]	112.91 (0.00) [0]
	<u>Railways</u>				
1478	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1479	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (600.00) [366.71]	332.87 (-233.29) [2]
1480	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1481	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,825.00]	1,777.07 (641.75) [24]
1482	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [12/2023]	602.50 (-) [800.00]	145.14 (197.50) [-]
1483	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1484	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1485	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	72.08 (0.35) [68]
1486	JHANSI BINA DOUBLING	9/2016	3/2021 (6/2023) [6/2023]	2,001.00 (-) [2,001.00]	1,046.53 (0.00) [27]
1487	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [6/2025]	4,329.53 (-) [4,329.53]	76.74 (0.00) [27]
1488	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1489	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2022]	528.57 (-) [528.57]	324.29 (0.00) [36]
1490	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019	927.01	1,438.92

			(-) [6/2022]	(-) [1,400.00]	(472.99) [39]
1491	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	2,364.27 (0.00) [0]
1492	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [1/2022]	668.70 (668.00) [680.00]	531.20 (11.30) [22]
1493	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	1,089.92 (0.00) [21]
1494	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [341.66]	0.00 (191.66) [66]
1495	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,345.00]	0.00 (2.00) [0]
1496	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,487.37 (0.00) [48]
1497	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,824.00]	1,465.45 (528.58) [0]
1498	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	355.22 (-149.01) [0]
1499	UNCHAHAR-AMETHI	4/2012	/	1,229.00	105.51
			(-) [0/0]	(-) [489.64]	(-739.36) [0]
1500	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [1,000.00]	982.28 (56.40) [33]
	<u>Road Transport And Highways</u>				
1501	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	242.70 (0.00) [0]
1502	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [417.68]	433.68 (66.34) [0]
1503	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [627.93]	633.24 (132.15) [0]
1504	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [469.31]	459.07 (177.95) [0]
1505	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1506	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/	1,120.57	1,525.15
			(-) [0/0]	(-) [1,332.00]	(211.43) [0]
1507	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/	1,668.00	946.08
			(-) [0/0]	(-) [1,668.00]	(0.00) [0]
1508	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1509	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/	1,408.00	387.83
			(7/2022) [7/2022]	(827.05) [827.05]	(-580.95) [-]
1510	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74	3/2016	/	1,737.00	1,077.55

	FROM KM 73.00 TO KM 175.00		(6/2021) [9/2021]	(1,201.51) [1,201.51]	(-535.49) [0]
1511	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	2,977.58 (0.00) [0]
1512	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1513	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1514	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,118.76 (382.01) [0]
1515	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN)	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1516	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	985.40 (0.00) [0]
1517	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROAD	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1518	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD	7/2018	2/2024 (-) [2/2024]	1,948.25 (-) [1,948.25]	277.20 (0.00) [0]
1519	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1520	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1521	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR ROAD	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1522	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1523	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (4/2022) [4/2022]	282.41 (319.96) [319.96]	193.56 (37.55) [73]
1524	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,087.00]	1,084.94 (-145.21) [0]
1525	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [0/0]	1,989.00 (-) [1,989.00]	772.56 (0.00) [0]
1526	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]
1527	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	75.10 (0.00) [0]
1528	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	886.68 (0.00) [0]
1529	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [1,197.00]	1,176.70 (271.60) [0]
1530	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-)	667.00 (-)	549.07 (0.00)

			[0/0]	[667.00]	[0]
1531	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	464.05 (0.00) [0]
1532	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1533	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1534	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1535	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J)	3/2018	8/2020 (-) [3/2022]	288.30 (-) [323.36]	222.57 (35.06) [19]
1536	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (12/2021) [12/2021]	1,373.28 (-) [1,373.28]	1,322.40 (0.00) [21]
1537	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [0/0]	1,184.71 (-) [1,310.00]	1,297.83 (125.29) [0]
1538	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (10/2022) [0/0]	899.00 (-) [899.00]	453.62 (0.00) [0]
1539	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.00 (0.00) [0]
1540	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [3/2022]	281.45 (-) [319.96]	117.56 (38.51) [-]
1541	MEERUT-BULANDSHAHAR	1/2016	/ (-) [0/0]	683.24 (-) [987.94]	0.00 (304.70) [0]
1542	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [3/2022]	326.99 (327.00) [326.99]	137.80 (0.00) [-]
1543	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [12/2021]	296.50 (-) [296.50]	237.81 (0.00) [15]
1544	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	222.94 (-348.73) [0]
1545	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	332.69 (-345.24) [0]
1546	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [3/2022]	263.89 (-) [242.05]	188.89 (-21.84) [23]
1547	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [1/2021]	185.18 (-) [185.18]	124.69 (0.00) [0]
1548	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [4/2021]	249.50 (-) [249.50]	229.57 (0.00) [0]
1549	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (3/2020) [3/2021]	218.90 (-) [218.90]	147.70 (0.00) [0]
1550	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [1/2022]	306.59 (-) [306.59]	195.70 (0.00) [-]

1551	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [10/2019]	215.16 (215.00) [215.16]	145.76 (0.00) [0]
1552	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [3/2021]	240.30 (240.00) [240.30]	200.10 (0.00) [0]
1553	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [3/2021]	208.88 (-) [208.88]	183.54 (0.00) [0]
1554	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	1,720.10 (0.00) [0]
1555	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,315.69 (0.00) [0]
1556	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [3/2023]	724.60 (720.81) [724.60]	0.00 (0.00) [0]
1557	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1558	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [1/2021]	164.54 (-) [164.54]	141.33 (0.00) [0]
	<u>Steel</u>				
1559	FORGED WHEEL PLANT	4/2014	9/2018 (9/2021) [9/2021]	1,682.85 (-) [2,100.00]	1,767.98 (417.15) [0]
	<u>Urban Development</u>				
1560	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [5/2025]	8,379.62 (-) [8,379.62]	506.47 (0.00) [14]
1561	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2025]	11,076.48 (-) [11,076.48]	2,391.78 (0.00) [12]
1562	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	6,928.00 (0.00) [0]
	<u>Water Resources</u>				
1563	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [4/2024]	213.62 (261.12) [261.12]	0.00 (47.50) [25]
1564	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [3/2022]	206.05 (-) [206.05]	80.97 (0.00) [5]
1565	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2022]	231.79 (-) [234.03]	28.36 (2.24) [12]
1566	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [3/2024]	271.39 (-) [271.39]	0.00 (0.00) [31]
1567	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [3/2024]	298.12 (213.91) [213.91]	0.00 (-84.21) [32]
1568	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [3/2022]	767.59 (-) [767.59]	132.29 (0.00) [6]
1569	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [12/2021]	460.45 (-) [460.45]	248.16 (0.00) [12]
1570	SEWERAGE SCHEME INTERCEPTION AND DIVERSION	2/2019	6/2022	681.78	0.00

	WITH STP WORKS AT MEERUT UTTAR PRADESH		(-) [4/2024]	(-) [690.71]	(8.93) [22]
1571	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [11/2021]	279.91 (330.05) [330.05]	260.12 (50.14) [0]
1572	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [12/2021]	967.23 (-) [967.23]	96.64 (0.00) [3]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1573	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2022]	456.86 (-) [456.86]	329.56 (0.00) [24]
	<u>Petroleum</u>				
1574	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [6/2022]	160.10 (-) [160.10]	105.42 (0.00) [28]
	<u>Power</u>				
1575	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.93 (274.07) [0]
1576	NAITWAR MORI HEP	10/2017	12/2021 (6/2022) [6/2022]	648.33 (-) [947.89]	785.06 (299.56) [6]
1577	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [9/2024]	2,978.48 (5,867.38) [5,867.38]	5,326.00 (2,888.90) [138]
1578	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2023]	1,657.00 (4,825.60) [4,825.60]	4,374.66 (3,168.60) [88]
1579	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (12/2024) [12/2024]	2,491.58 (3,860.35) [3,860.35]	2,356.86 (1,368.77) [138]
	<u>Railways</u>				
1580	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1581	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [22,716.11]	5,917.58 (6,500.11) [3]
	<u>Road Transport And Highways</u>				
1582	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [3/2022]	403.36 (-) [403.36]	220.25 (0.00) [45]
1583	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [3/2022]	417.24 (-) [417.24]	265.48 (0.00) [46]
1584	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (2/2022) [0/0]	605.84 (-) [722.46]	723.26 (116.62) [0]
1585	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [0/0]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [0]
1586	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [3/2022]	274.31 (-) [274.31]	131.95 (0.00) [46]
1587	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [7/2022]	1,383.78 (-) [1,383.78]	299.10 (0.00) [48]
1588	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM);	5/2018	5/2020 (12/2021)	248.00 (-)	109.23 (0.00)

	DESIGN		[12/2021]	[248.00]	[19]
1589	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (10/2022) [0/0]	720.00 (-) [720.00]	207.78 (0.00) [0]
1590	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [0/0]	478.51 (-) [478.00]	315.11 (-0.51) [0]
1591	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (7/2021) [7/2021]	232.81 (-) [232.81]	171.22 (0.00) [0]
1592	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (5/2021) [5/2021]	283.51 (-) [283.51]	259.90 (0.00) [0]
1593	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (7/2021) [7/2021]	257.34 (-) [257.34]	214.90 (0.00) [0]
1594	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (12/2021) [12/2021]	282.08 (-) [282.08]	207.83 (0.00) [30]
1595	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (7/2021) [7/2021]	200.34 (-) [200.34]	185.44 (0.00) [0]
1596	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (9/2021) [9/2021]	418.88 (-) [418.88]	287.56 (0.00) [0]
1597	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (10/2020) [10/2020]	266.52 (-) [266.52]	186.16 (0.00) [0]
1598	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (12/2020) [12/2020]	234.88 (-) [234.88]	174.51 (0.00) [0]
1599	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (10/2021) [10/2021]	293.68 (-) [293.68]	183.73 (0.00) [0]
1600	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	116.25 (0.27) [0]
1601	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (8/2021) [8/2021]	248.22 (-) [248.22]	234.12 (0.00) [0]
	<u>Water Resources</u>				
1602	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (3/2021) [3/2022]	158.00 (-) [158.00]	85.01 (0.00) [28]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1603	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (4/2023) [4/2023]	389.71 (-) [389.71]	216.37 (0.00) [17]
1604	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (6/2022) [4/2022]	458.00 (-) [458.00]	161.87 (0.00) [25]
	<u>Coal</u>				
1605	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [10/2022]	304.13 (341.22) [341.22]	79.48 (37.09) [67]
1606	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY	11/2015	3/2029 (3/2029) [3/2029]	1,210.12 (-) [1,210.12]	49.12 (0.00) [0]
1607	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-)	502.68 (-)	22.79 (0.00)

			[3/2029]	[502.68]	[0]
1608	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	0.18 (0.00) [0]
1609	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	625.36 (2,484.75) [60]
1610	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	7.95 (0.00) [0]
1611	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	1.75 (0.00) [0]
1612	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2029]	1,055.05 (-) [1,055.05]	714.63 (0.00) [132]
1613	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	3.78 (0.00) [0]
	<u>Department Of Higher Education</u>				
1614	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [3/2022]	193.83 (-) [193.83]	51.77 (0.00) [21]
	<u>Health And Family Welfare</u>				
1615	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1616	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1617	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [10/2021]	651.99 (-) [651.99]	609.49 (0.00) [0]
1618	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [10/2021]	355.15 (-) [355.15]	321.31 (0.00) [0]
	<u>Home Affairs</u>				
1619	NSG AT KOLKATA	10/2014	4/2018 (8/2022) [8/2022]	162.88 (238.00) [238.00]	173.06 (75.12) [52]
	<u>Mines</u>				
1620	CONSTRUCTION OF BASEMENT G FLOOR 10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	4/2019	4/2022 (12/2024) [12/2024]	255.37 (255.37) [255.37]	0.86 (0.00) [32]
	<u>Petroleum</u>				
1621	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (3/2022) [3/2022]	3,712.00 (-) [3,696.00]	2,360.01 (-16.00) [-6]
1622	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (8/2031) [8/2031]	5,830.20 (-) [5,830.20]	146.12 (0.00) [5]
1623	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2023]	1,740.00 (-) [1,740.00]	1,008.20 (0.00) [30]
1624	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	132.46 (0.00) [0]
1625	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [7/2022]	163.02 (207.36) [207.36]	129.75 (44.34) [27]
	<u>Power</u>				

1626	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [3/2022]	529.68 (633.80) [633.80]	530.53 (104.12) [40]
1627	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (6/2021) [6/2021]	454.11 (-) [454.11]	345.21 (0.00) [0]
1628	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [12/2024]	1,381.84 (-) [1,803.00]	743.00 (421.16) [63]
	Railways				
1629	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (-) [2,373.00]	485.04 (1,345.60) [324]
1630	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	303.23 (16.56) [-]
1631	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	41.78 (352.63) [-]
1632	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1633	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [0]
1634	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1635	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [0/0]	221.42 (-) [380.00]	38.20 (158.58) [0]
1636	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [0/0]	297.32 (200.34) [614.00]	275.06 (316.68) [0]
1637	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,090.60]	1,089.12 (710.00) [0]
1638	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [10/2021]	602.27 (-) [1,167.00]	1,095.12 (564.73) [0]
1639	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1640	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	1,460.93 (1,725.49) [108]
1641	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1642	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	3,317.94 (307.50) [108]
1643	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	4/2018	6/2022 (-) [6/2023]	338.00 (-) [393.83]	22.39 (55.83) [12]
1644	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	912.61 (430.57) [72]
1645	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]

	Road Transport And Highways				
1646	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (2,587.75) [1,827.15]	989.55 (744.15) [0]
1647	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2023]	998.79 (-) [998.79]	1,893.57 (0.00) [118]
1648	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [1/2022]	1,078.84 (-) [1,078.84]	2,301.82 (0.00) [101]
1649	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	1,396.18 (0.00) [0]
1650	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [0/0]	361.15 (363.93) [363.93]	277.34 (2.78) [0]
1651	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (1/2021) [3/2022]	271.17 (291.20) [291.20]	120.51 (20.03) [40]
1652	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [11/2022]	160.27 (213.97) [213.97]	27.15 (53.70) [39]
1653	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (8/2022) [8/2022]	236.78 (263.26) [263.26]	78.47 (26.48) [36]
1654	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (3/2021) [6/2021]	254.30 (254.30) [254.30]	118.39 (0.00) [0]
1655	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [0/0]	767.03 (-) [767.03]	704.89 (0.00) [0]
1656	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (2,145.96) [1,952.20]	97.16 (690.22) [0]
1657	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (-) [2/2020]	279.70 (398.52) [398.52]	331.86 (118.82) [0]
1658	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (11/2021) [10/2021]	396.86 (396.86) [396.86]	277.42 (0.00) [0]
1659	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [2,360.65]	4,511.67 (695.65) [0]
1660	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (4/2021) [6/2021]	218.70 (218.70) [218.70]	113.26 (0.00) [0]
1661	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (1/2022) [1/2022]	426.18 (426.18) [426.18]	254.43 (0.00) [16]
	Water Resources				
1662	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (5/2022) [0/0]	274.76 (-) [274.76]	222.84 (0.00) [0]
1663	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2024]	384.96 (-) [384.96]	0.00 (0.00) [24]
1664	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2024]	234.31 (-) [234.31]	0.00 (0.00) [24]
1665	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-)	165.16 (-)	0.00 (0.00)

			[3/2024]	[165.16]	[21]
1666	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [3/2024]	160.00 (154.73) [154.73]	0.00 (-5.27) [25]
1667	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2024]	287.53 (-) [287.53]	0.00 (0.00) [24]
1668	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [9/2023]	164.93 (-) [164.93]	11.56 (0.00) [21]
1669	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [3/2024]	198.43 (224.69) [224.69]	0.00 (26.26) [25]
1670	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [4/2024]	307.12 (-) [307.12]	0.00 (0.00) [19]
1671	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [9/2023]	172.10 (-) [172.10]	11.56 (0.00) [21]
1672	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [9/2023]	185.22 (-) [185.22]	11.56 (0.00) [21]
1673	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [3/2022]	272.32 (-) [272.32]	253.59 (0.00) [23]
	Total			22,23,791.78 (8,03,337.38) [26,64,649.18]	13,08,766.65 (4,40,857.40)

FLASH REPORT
