

**424th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
February, 2021**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for February 2021 contains information on the status of the 1736 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, 1736 projects, 15 projects are added. 547 projects are delayed with respect to their original schedules and 95 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these projects, 37 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)


S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report	Additional delayed Mega Projects
1	ROAD TRANSPORT AND HIGHWAYS	908	139	29	4
2	RAILWAYS	312	157	22	14
3	PETROLEUM	138	68	11	7
4	COAL	101	44	9	5
5	POWER	78	45	13	2
6	WATER RESOURCES	49	17	0	0
7	URBAN DEVELOPMENT	34	11	4	3
8	HEALTH AND FAMILY WELFARE	29	13	1	0
9	HUMAN RESOURCE DEVELOPMENT	26	14	3	0
10	CIVIL AVIATION	19	12	0	0
11	STEEL	9	5	1	1
12	MINES	5	2	0	0
13	ATOMIC ENERGY	4	4	0	0
14	FERTILISERS	4	4	1	0
15	HOME AFFAIRS	4	2	1	1
16	RURAL DEVELOPMENT	4	3	0	0
17	TELECOMMUNICATIONS	3	2	0	0
18	FINANCE	2	1	0	0
19	DPIIT	2	2	0	0
20	HEAVY INDUSTRY	1	0	0	0
21	SHIPPING AND PORTS	1	0	0	0
22	DEFENCE PRODUCTION	1	1	0	0
23	COMMERCE	1	0	0	0
24	CULTURE DEVELOPMENT	1	1	0	0
Total		1736	547	95	37

3. Total original cost of implementation of the 1736 projects was ₹22,32,019.72 crore and their anticipated completion cost is likely to be ₹26,61,205.74 crore, which reflects overall cost overruns of ₹7,31,133.44 crore (32.76 % of original cost). The expenditure incurred on these projects till February 2021 is ₹12,78,270.71 crore, which is 48.03% of the anticipated cost of the projects. The information can be viewed graphically as:

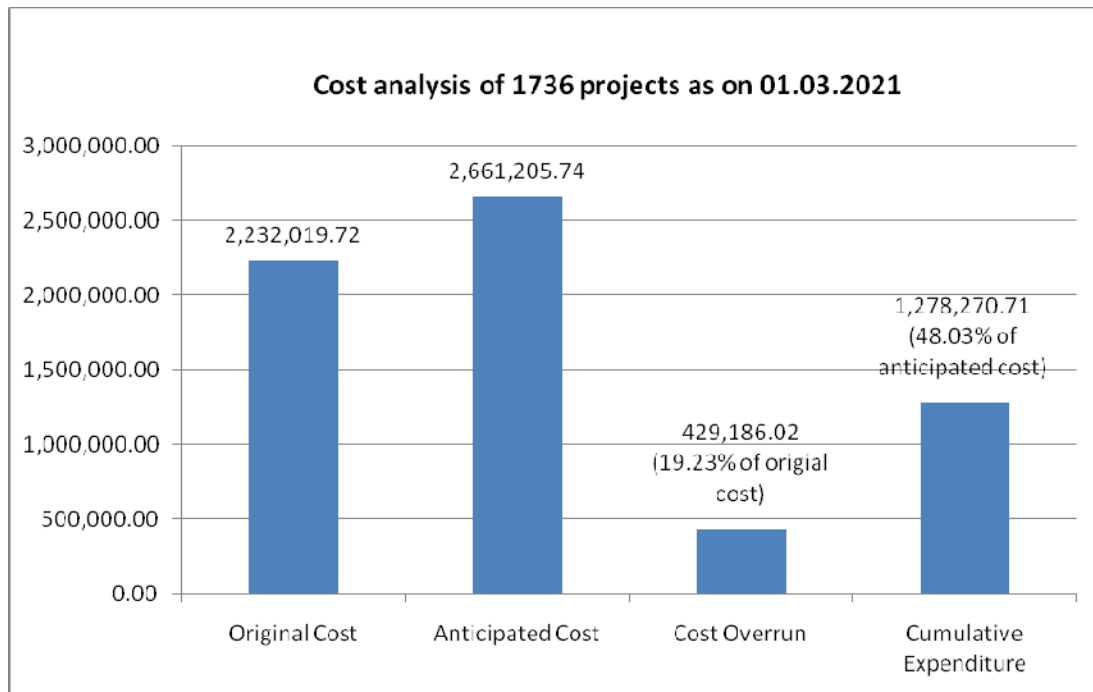


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.


5. Out of the 1736 projects, 12 projects are ahead of schedule, 247 are on schedule, 547 are delayed, 449 projects reported cost overrun and 148 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 409 if delay is calculated on the basis of latest schedule of completion. Further, for 930 projects neither the year of commissioning nor the tentative gestation period has been reported.

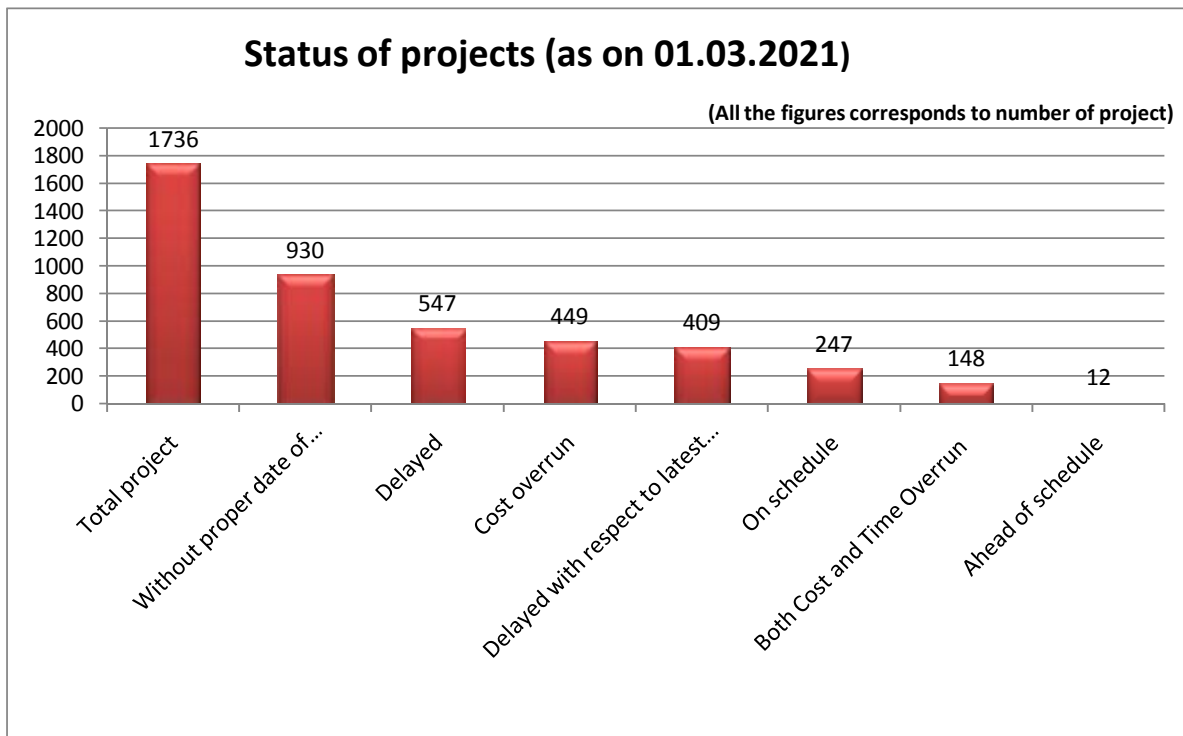

6. Out of 547 delayed projects, 109 (18.99%) projects have overall delay in the range of 1 to 12 months, 132 (23.48%) projects have delay in the range of 13 to 24 months, 187 (33.51%) projects have delay in the range of 25 to 60 months and 119 (20.61%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

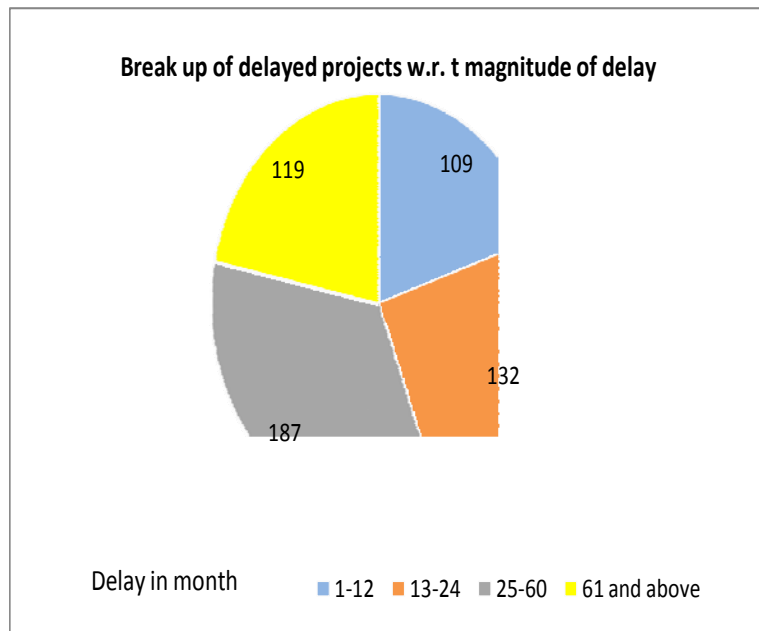

7. The status of online reporting of projects can be viewed month wise as:

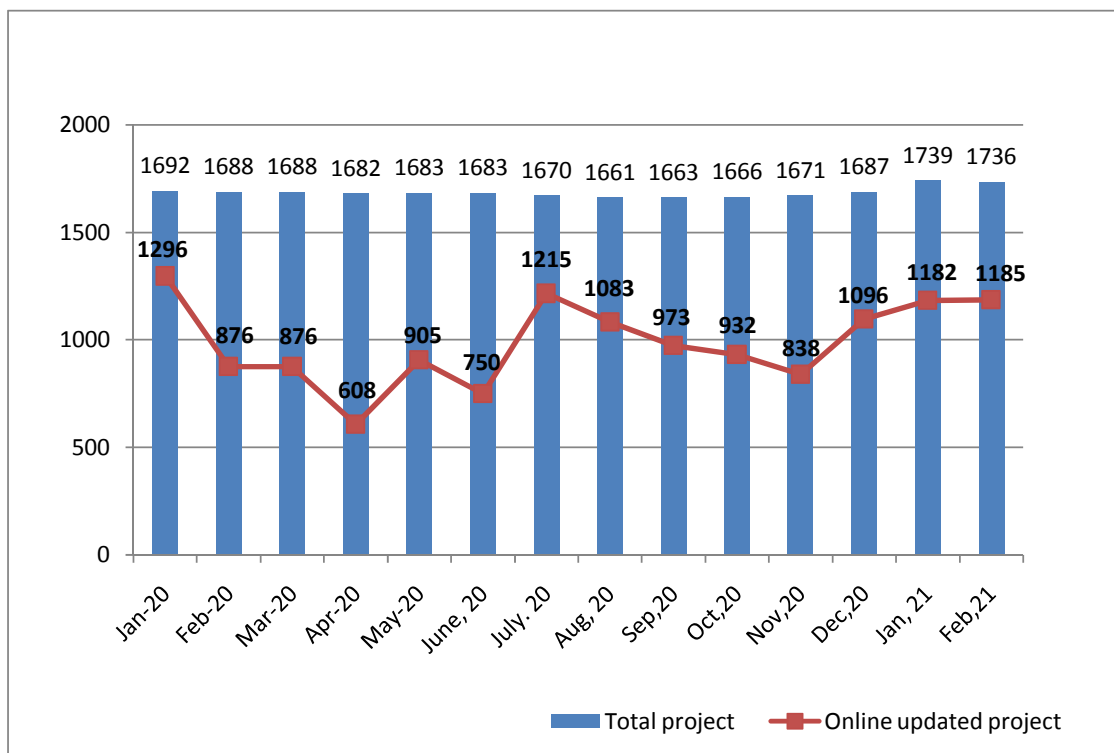

The average time overrun in these 547 delayed projects is 44.59 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to

enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-03-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	5.78
COAL					
7	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
8	BHANEAGAON OC	02/2015	187.94	409.68	117.98
9	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
10	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
11	RPR FOR JAMUNIA UG (0.90 MTY)	07/2016	281.25	409.87	45.73
DPIIT					
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80

13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
HEALTH AND FAMILY WELFARE					
14	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
15	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	20.55
16	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
17	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
18	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	15.71
HOME AFFAIRS					
19	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
20	NSG AT KOLKATA	10/2014	162.88	238.00	46.12
HUMAN RESOURCE DEVELOPMENT					
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
22	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	350.69	19.28
23	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	10.22
24	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	1.85
25	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
PETROLEUM					
26	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
27	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1846.46	114.26
28	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
29	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
30	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	43.82
POWER					
31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
33	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52
34	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
35	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	97.38
RAILWAYS					
36	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
37	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	2172.16	1699.64
38	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
39	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
40	RAMGANJMUNDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
ROAD TRANSPORT AND HIGHWAYS					
41	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
42	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
43	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
44	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95

45	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	94.94
RURAL DEVELOPMENT					
46	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	3.96
47	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	2.23
STEEL					
48	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	41.32
TELECOMMUNICATIONS					
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
50	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
51	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	44.39
52	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
53	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
54	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	18.69
WATER RESOURCES					
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
56	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	01/2019	231.79	234.03	0.97

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-03-2021)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	24.10
COAL					
7	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
9	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
10	BHANEGAON OC	02/2015	187.94	409.68	221.74
11	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
DPIIT					
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
HEALTH AND FAMILY WELFARE					
14	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00

15	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
16	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	85.12
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
18	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	45.56
HOME AFFAIRS					
19	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
20	NSG AT KOLKATA	10/2014	162.88	238.00	75.12
HUMAN RESOURCE DEVELOPMENT					
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
22	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	350.69	56.69
23	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	19.00
24	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	10.16
25	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
PETROLEUM					
26	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
27	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00
28	ENNORE THIRUVALUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
29	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
30	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
POWER					
31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
32	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
33	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
35	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	5213.00
RAILWAYS					
36	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
37	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
38	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
39	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
40	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12264.15	7809.98
ROAD TRANSPORT AND HIGHWAYS					
41	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
42	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
43	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2587.50	1199.16
44	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
45	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
RURAL DEVELOPMENT					
46	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	5.93
47	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	4.51
STEEL					

48	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	6415.00
	TELECOMMUNICATIONS				
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
	URBAN DEVELOPMENT				
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	10270.00
51	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
52	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
53	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
54	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4720.73	456.73
	WATER RESOURCES				
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
56	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	01/2019	231.79	234.03	2.24

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-03-2021)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	03/2023	75
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	02/2022	74
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
	CIVIL AVIATION				
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2021	33
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	06/2021	16
7	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	06/2021	15
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	05/2021	13
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	03/2021	03/2022	12
	COAL				
10	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	03/2010	03/2029	228
11	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	03/2013	03/2028	180
12	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	03/2017	03/2031	168
13	MAGADH EXPANSION OC(51 MTY)	08/2008	07/2012	03/2025	152
14	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2022	132
	CULTURE DEVELOPMENT				
15	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	04/2014	09/2017	03/2021	42
16	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	02/2020	06/2021	16
	DPIIT				
17	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	07/2021	22
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	10/2021	22
	FERTILISERS				
19	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	03/2021	16
20	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	03/2021	16

21	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	02/2021	15
22	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	04/2021	12
	FINANCE				
23	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	04/2021	18
	HEALTH AND FAMILY WELFARE				
24	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	03/2021	88
25	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	03/2021	46
26	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	12/2021	43
27	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	04/2021	38
28	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	03/2019	03/2021	24
	HOME AFFAIRS				
29	NSG AT KOLKATA	10/2014	04/2018	12/2021	44
30	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	12/2021	26
	HUMAN RESOURCE DEVELOPMENT				
31	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	06/2021	63
32	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	10/2021	52
33	PERMANENT CAMPUS FOR IIM BODH GAYA	09/2018	09/2020	11/2022	26
34	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	04/2019	04/2021	24
35	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	01/2018	05/2020	02/2022	21
	MINES				
36	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	12/2022	20
37	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	02/2021	3
	PETROLEUM				
38	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
39	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	03/2021	94
40	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
41	LPG TERMINAL AT KOCHI	10/2015	10/2017	03/2022	53
42	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	03/2017	03/2021	48
	POWER				
43	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
44	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	03/2022	150
45	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	02/2021	146
46	BARH STPP(3X660MW) NTPC	02/2005	10/2011	04/2022	126
47	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2023	126
	RAILWAYS				
48	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
49	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
50	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
51	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2022	241
52	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
	ROAD TRANSPORT AND HIGHWAYS				
53	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	06/2021	128
54	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	10/2010	06/2021	128
55	VARANASI-AURANGABAD KM.786 TO KM.978.40 10	09/2011	03/2014	12/2022	105

56	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	03/2022	103
57	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	05/2010	05/2013	08/2021	99
	RURAL DEVELOPMENT				
58	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	03/2021	63
59	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	03/2021	51
60	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016	03/2021	51
	STEEL				
61	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2021	74
62	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	12/2021	50
63	FORGED WHEEL PLANT	04/2014	09/2018	03/2021	30
64	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	06/2019	05/2021	23
65	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	09/2020	05/2021	8
	TELECOMMUNICATIONS				
66	NETWORK FOR SPECTRUM	03/2012	07/2015	06/2021	71
67	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	11/2021	5
	URBAN DEVELOPMENT				
68	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	03/2023	98
69	DELHI MRTS PHASE-III	09/2011	03/2016	09/2021	66
70	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2019	06/2024	64
71	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	08/2022	44
72	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	07/2021	12/2024	41
	WATER RESOURCES				
73	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
74	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	04/2022	25
75	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	05/2021	17
76	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	02/2017	11/2019	03/2021	16
77	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	03/2017	11/2019	03/2021	16

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-03-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	291.75	09/2018	06/2021
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	438.28	438.28	335.58	06/2019	N.A.
3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	01/2016	458.00	458.00	105.12	03/2020	06/2021
4	UPGRADATION OF JABALPUR AIRPORT	06/2016	412.24	412.24 11	0.00	06/2021	06/2021

5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	303.80	303.80	115.88	04/2020	05/2021
COAL							
6	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	158.25	09/2020	N.A.
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
8	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	173.83	09/2020	N.A.
9	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
10	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	18.35	04/2018	12/2021
COMMERCE							
11	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	60.00	10/2020	N.A.
DPIIT							
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	8715.07	09/2019	07/2021
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	2419.54	12/2019	10/2021
HEALTH AND FAMILY WELFARE							
14	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
15	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	481.52	11/2013	03/2021
16	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	449.74	06/2020	07/2021
17	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	524.06	04/2020	07/2021
18	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
HEAVY INDUSTRY							
19	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	900.00	815.00	09/2019	N.A.
HOME AFFAIRS							
20	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	166.98	166.98	0.00	10/2023	10/2023
21	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE-C/O 336 NOS. TYPE-II QTRS. , 96	01/2020	166.98	166.98	0.29	05/2022	05/2022
HUMAN RESOURCE DEVELOPMENT							
22	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF	09/2013	484.32	626.26	0.00	09/2014	N.A.

	TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA						
23	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	171.72	171.72	53.94	03/2020	06/2021
24	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676.00	676.00	0.00	04/2023	04/2023
25	STUDY IN INDIA	03/2018	150.00	150.00	0.00	04/2018	N.A.
26	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	418.00	418.00	110.00	03/2019	N.A.
PETROLEUM							
27	IRUGUR- DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	17.80	02/2017	08/2022
28	ENNORE-TRICHY- MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
29	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1112.00	1507.24	711.00	06/2019	02/2022
30	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI- MANMAD- AHMEDNAGAR- SOLAPUR PIPELI	05/2016	261.00	261.00	147.12	01/2021	04/2021
31	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI- MANMAD- AHMEDNAGAR- SOLAPUR PIPELINE	05/2016	212.00	212.00	138.76	01/2021	04/2021
POWER							
32	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13233.01	09/2010	08/2023
34	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3380.97	10/2017	N.A.
35	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	241.55	04/2016	06/2021
36	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1664.74	04/2020	07/2025
RAILWAYS							
37	HOWRAH-AMTA- CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
38	NANGALDAM- TALWARA(NL),NR	03/1981	450.00	2200.00	714.78	07/2012	03/2024
39	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.07	03/2019	N.A.
40	LAKSHMIKANTAPUR- NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA- CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	149.30	03/2006	03/2025
41	MUZAFFARPUR- SITAMARHI NEW LINE	01/1991	332.15	546.71	541.83	07/2014	N.A.
ROAD TRANSPORT AND HIGHWAYS							

42	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	446.60	N.A.	N.A.
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	238.01	N.A.	N.A.
44	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
45	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	318.64	08/2016	N.A.
46	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	358.22	377.64	343.70	10/2016	N.A.
SHIPPING AND PORTS							
47	JAL MARG VIKAS PROJECT	01/2018	5369.18	4633.81	1814.28	03/2023	03/2023
STEEL							
48	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	2907.00	2907.00	185.08	06/2023	06/2023
49	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	17.50	12/2023	12/2023
50	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	377.18	377.18	0.63	05/2023	05/2023
TELECOMMUNICATIONS							
51	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	16594.00	07/2015	06/2021
52	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	248.20	248.20	80.10	03/2018	N.A.
53	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	431.16	0.00	06/2021	11/2021
URBAN DEVELOPMENT							
54	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.

55	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	N.A.
56	DELHI MRTS PHASE-III	09/2011	38585.00	38585.00	39838.90	03/2016	09/2021
57	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	884.30	884.30	812.00	12/2015	N.A.
58	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6059.17	07/2017	09/2020
WATER RESOURCES							
59	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	279.91	222.79	12/2019	01/2021
60	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	198.28	12/2019	05/2021
61	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	225.77	263.72	03/2020	03/2021
62	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	210.94	04/2020	03/2021
63	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	274.08	01/2021	N.A.

N.A.: Not Available.

Table-E

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates
(as on 01-03-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	5915.80
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	16297.00
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12320.00	0.00	12992.00
COAL					
4	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	0.00	292.49
5	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	0.00	246.55
HEALTH AND FAMILY WELFARE					
6	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	481.52
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	229.39
8	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
PETROLEUM					
11	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	352.56	0.00	455.00

12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	0.00	4852.63
13	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	0.00	2750.24
	POWER				
14	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	8154.49
15	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	487.49	0.00	590.30
16	MUNPL-MEJA TPP - JV (2X660 MW)	04/2012	9750.89	0.00	11130.00
17	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	11846.00	0.00	13766.78
18	KHARGONE STPP STAGE I (1320 MW)	03/2015	9870.51	0.00	10019.31
	RAILWAYS				
19	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	714.78
20	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	541.83
21	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	1194.00
22	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	697.29
23	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	928.36
	ROAD TRANSPORT AND HIGHWAYS				
24	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	0.00	318.64
25	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	612.58
26	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	325.28
27	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	0.00	251.39
28	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	0.00	655.17
	TELECOMMUNICATIONS				
29	NETWORK FOR SPECTRUM	03/2012	13334.00	0.00	16594.00
	URBAN DEVELOPMENT				
30	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16365.87
31	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39838.90
32	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	0.00	4683.08
	WATER RESOURCES				
33	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	0.00	263.72
34	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	0.00	274.08

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-03-2021)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				

1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	N.A.	N.A.
COAL					
2	RANIGANJ MASTER PLAN	08/2009	08/2019	N.A.	N.A.
3	PATHERDIH NLW WASHERY	10/2012	04/2014	N.A.	04/2020
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	12/2019	N.A.	N.A.
6	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	09/2020	N.A.	N.A.
COMMERCE					
7	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
8	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
9	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
10	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
11	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
12	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	05/2019
HEAVY INDUSTRY					
13	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	12/2020	N.A.
HUMAN RESOURCE DEVELOPMENT					
14	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
15	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	N.A.	N.A.
16	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	N.A.	N.A.
17	STUDY IN INDIA	03/2018	04/2018	N.A.	N.A.
18	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	03/2019	N.A.	N.A.
MINES					
19	UTKAL D AND E COAL BLOCK	05/2016	01/2020	N.A.	N.A.
PETROLEUM					
20	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
21	MUMBAI REFINERY EXPANSION PROJECT	09/2015	03/2020	N.A.	N.A.
22	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	06/2017	10/2019	11/2020	N.A.
23	BS-VI PROJECTS	09/2017	12/2019	N.A.	01/2021
POWER					
24	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
25	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
26	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	06/2014	N.A.	N.A.
27	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
28	MUNPL-MEJA TPP - JV (2X660 MW)	04/2012	02/2017	06/2020	01/2021
RAILWAYS					
29	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
30	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-	04/1983	03/2019	N.A.	N.A.

	ITAHAR(NL),NEFR				
31	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
32	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	02/2009	N.A.	N.A.
33	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	03/1996	03/2017	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
34	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
35	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
38	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
STEEL					
39	COKE OVEN BATTERY-5	12/2011	12/2017	12/2020	12/2020
TELECOMMUNICATIONS					
40	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	03/2018	N.A.	N.A.
URBAN DEVELOPMENT					
41	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
42	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	N.A.	N.A.
43	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
44	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	11/2019	N.A.	N.A.
45	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	12/2015	N.A.	N.A.
WATER RESOURCES					
46	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	12/2019	N.A.	01/2021
47	SAIDPUR SEWER NETWORK PATNA	04/2015	01/2021	N.A.	N.A.
48	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	03/2017	08/2019	N.A.	N.A.
49	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	N.A.	N.A.
50	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	05/2017	05/2020	N.A.	N.A.

.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	908	29
2	RAILWAYS	312	22
3	PETROLEUM	138	11
4	COAL	101	9
5	POWER	78	13
6	WATER RESOURCES	49	0
7	URBAN DEVELOPMENT	34	4
8	HEALTH AND FAMILY WELFARE	29	1
9	HUMAN RESOURCE DEVELOPMENT	26	3
10	CIVIL AVIATION	19	0
11	STEEL	9	1
12	MINES	5	0
13	ATOMIC ENERGY	4	0
14	FERTILISERS	4	1
15	HOME AFFAIRS	4	1
16	RURAL DEVELOPMENT	4	0
17	TELECOMMUNICATIONS	3	0
18	FINANCE	2	0
19	DPIIT	2	0
20	HEAVY INDUSTRY	1	0
21	SHIPPING AND PORTS	1	0
22	DEFENCE PRODUCTION	1	0
23	COMMERCE	1	0
24	CULTURE DEVELOPMENT	1	0
	Total	1736	95

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2020			
	<u>STEEL</u>			
1	INSTALLATION OF NEW HOT STRIP MILL AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000094]	3,127.30	04/2018	3,201.42
	<u>PETROLEUM</u>			
2	INTEGRATED DEVELOPMENT OF B-127 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000131]	2,059.63	03/2015	2,011.80
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000197]	6,068.80	04/2019	4,956.05
4	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000212]	4,619.94	12/2017	4,663.66
5	INDMAX PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000243]	2,582.00	11/2019	1,718.52
6	MOTIHARI AMLEKHGANJ PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000254]	324.00	06/2020	129.09
7	DEVELOPMENT OF B-147 FIELD Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000292]	546.15	11/2019	537.69
8	BS-VI PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000310]	3,380.00	09/2019	2,381.00
9	BS-VI PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000320]	1,222.00	09/2019	764.17
10	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000322]	2,934.40	09/2019	1,957.94
11	BS-VI PROJECT AT PANIPAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000325]	3,529.00	07/2019	2,095.75
12	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR (GAS AUTHORITY OF INDIA LIMITED) - [N16000330]	221.45	10/2022	63.59
13	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000366]	154.84	11/2019	128.71
	June,2020			
	<u>COAL</u>			
14	RKP OCP PHASE-I (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000079]	209.78	03/2015	104.19
15	RG OC -III EXTENSION (PHASE -II) PROJECT (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000100]	365.01	06/2015	365.01
	July,2020			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
16	KULDA OCP (MAHANADI COALFIELDS LTD) (MAHANADI COAL FIELDS LIMITED) - [060100092]	302.96	03/2010	281.80
	<u>PETROLEUM</u>			
17	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000204]	2,818.88	03/2019	2,907.03
18	BS-VI PROJECT AT MATHURA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000306]	666.64	09/2019	493.90
19	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000335]	766.37	12/2019	606.49
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
20	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000347]	723.54	02/2018	1,163.64
21	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000492]	867.66	05/2018	1,289.81
22	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000604]	320.30	01/2019	237.81
23	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000667]	648.32	03/2020	511.34
24	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) Central Sector Projects(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000700]	648.33	06/2017	229.94
25	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000951]	382.81	01/2015	338.18
26	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000952]	179.32	11/2017	129.04
27	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000953]	155.77	09/2016	111.65
28	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000954]	378.07	01/2014	188.65
29	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000955]	511.21	10/2013	813.54
30	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000956]	501.00	09/2013	659.98
31	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000960]	621.43	10/2016	429.97
32	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000961]	163.54	07/2017	108.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>TELECOMMUNICATIONS</u>			
33	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000105]	418.26	06/2017	367.04
34	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000113]	231.80	10/2018	119.92
	<u>URBAN DEVELOPMENT</u>			
35	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000101]	768.88	02/2014	1,125.98
36	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000102]	324.87	12/2015	270.24
37	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000062]	156.57	08/2016	159.35
38	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000108]	206.58	03/2019	185.84
	August,2020			
	<u>COAL</u>			
39	MANUGURU OC-II EXTENSION PHASE-II (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000080]	181.19	03/2012	170.60
	<u>PETROLEUM</u>			
40	RESID UPGRADATION PROJECT (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000184]	3,110.36	11/2015	2,915.00
41	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000255]	224.00	04/2019	164.61
42	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000256]	135.00	03/2019	156.65
43	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000260]	554.00	02/2020	375.80
44	50MW WIND ENERGY POWER PROJECT (OIL INDIA LIMITED) - [N16000298]	500.00	06/2017	368.24
45	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP (INDIAN OIL CORPORATION LIMITED) - [N16000354]	204.00	09/2019	162.53
46	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE (OIL INDIA LIMITED) - [N18000148]	871.35	03/2015	565.63
	<u>URBAN DEVELOPMENT</u>			
47	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000109]	253.92	06/2016	1,113.24

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
48	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000110]	200.00	03/2018	131.15
49	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000111]	787.29	12/2016	285.30
50	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000112]	170.00	04/2018	88.91
51	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG Central Sector Projects(HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000114]	185.37	03/2016	178.30
52	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000093]	154.00	11/2015	280.32
	September,2020			
	<u>HUMAN RESOURCE DEVELOPMENT</u>			
53	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000088]	388.00	05/2017	452.80
	October,2020			
	<u>COAL</u>			
54	PENGANGA OCP(REVISED) (WESTERN COAL FIELDS LIMITED) - [N06000066]	441.82	03/2020	259.82
55	GAURI DEEP OC (WESTERN COAL FIELDS LIMITED) - [N06000181]	164.96	03/2019	96.37
	December,2020			
56	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000114]	337.66	03/2019	258.65
	<u>PETROLEUM</u>			
57	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000277]	429.00	01/2019	373.62
58	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000284]	208.35	07/2020	170.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
59	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000505]	1,583.79	01/2019	1,648.90
60	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000669]	165.50	03/2020	117.09

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
61	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000670]	239.68	03/2020	219.75
	January,2021			
	<u>COAL</u>			
62	KULDA EXPN OC. (5.00 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000115]	289.03	03/2018	115.24
	<u>PETROLEUM</u>			
63	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000169]	993.00	01/2012	1,693.00
64	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000238]	1,879.00	06/2020	1,694.25
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
65	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000324]	194.11	05/2018	196.23
66	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000325]	179.82	01/2019	199.53
67	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000411]	218.31	02/2018	292.55
68	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000614]	183.65	11/2016	187.33
69	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000770]	158.65	06/2018	110.62
70	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000920]	223.67	02/2017	112.81
71	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000921]	208.34	02/2016	112.87
72	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000947]	259.52	-	184.51
73	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000977]	189.91	-	160.05

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	February, 2021			
	<u>STEEL</u>			
74	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000096]	1,154.18	12/2017	1,027.04
75	CENTRAL DISPATCH YARD (RASTRIYA ISPAT NIGAM LIMITED) - [N12000119]	320.66	08/2018	280.96

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	August,2021			
	<u>COAL</u>			
1	KALYANIKHANI 6 INCLINE PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000147]	477.65	03/2020	2.11
2	RAMPURAM SHAFT BLOCK (SINGARENI COLLIERS COMPANY LIMITED) - [N06000174]	431.92	-	0.00
3	SRAVANAPALLI OPENCAST PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000175]	412.70	-	0.76
	<u>HUMAN RESOURCE DEVELOPMENT</u>			
4	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000092]	216.69	03/2015	52.00
	September,2021			
	<u>COAL</u>			
5	KOYAGUDEM OPENCAST PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000146]	426.79	03/2018	0.72
	January,2021			
6	SHANTIKHANI LONGWALL PROJ-SCCL (SINGARENI COLLIERS COMPANY LIMITED) - [N06000017]	249.03	03/2012	326.69
7	KAKATIYA LONGWALL (SINGARENI COLLIERS COMPANY LIMITED) - [N06000048]	453.63	12/2012	121.91
8	BAROUD OC EXPANSION (RCE)- 3MTY (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000099]	258.56	03/2016	182.04
9	KAPURIA UG(PSLW) (BHARAT COKING COAL LIMITED) - [N06000108]	988.35	04/2017	45.26
10	BIJARI OC RCE (1.50 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000111]	164.49	03/2020	82.60
11	MALACHUA OPENCAST PROJECT (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000139]	488.33	03/2023	30.47
12	SAONER I UG TO OC PHASE I (WESTERN COAL FIELDS LIMITED) - [N06000177]	162.10	03/2022	36.94
	<u>PETROLEUM</u>			
13	HALDIA BARAUNI PRODUCT PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000251]	1,021.00	12/2020	4.45
14	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000309]	1,342.00	08/2020	6.30
15	2G ETHANOL BIO REFINERY AT BARGARH (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000341]	750.00	12/2020	34.73

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	February, 2021			
16	HALDIA LPG IMPORT FACILITY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000223]	694.00	10/2018	971.84
17	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000269]	342.00	03/2021	0.00
18	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM (INDIAN OIL CORPORATION LIMITED) - [N16000270]	247.00	03/2021	0.00
19	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN (OIL INDIA LIMITED) - [N16000299]	350.00	01/2019	2.06
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
20	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000429]	225.02	12/2018	26.00
21	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000682]	168.32	04/2017	43.28
22	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000684]	216.71	04/2017	26.84
23	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000974]	199.02	-	14.21
24	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000975]	184.88	-	6.85
	<u>TELECOMMUNICATIONS</u>			
25	CONVERGENT BILLING AND CRM-MTNL(DELHI) (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000011]	249.00	02/2007	0.00
26	CONVERGENT BILLING AND CRM(MUMBAI) (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000016]	247.00	02/2007	0.00
27	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (DEPARTMENT OF TELECOMMUNICATION) - [N26000065]	1,077.00	03/2009	0.00
28	DELHI CONVERGENT BILLING AND CRM PE-5834 (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000099]	229.41	03/2012	0.00
29	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY (INDIAN TELEPHONE INDUSTRY) - [N26000102]	2,111.17	09/2014	253.90
	<u>WATER RESOURCES</u>			
30	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR(Uttar Pradesh Jal Nigam) - [N30000012]	857.26	08/2021	0.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
31	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA (Uttar Pradesh Jal Nigam) - [N30000023]	317.19	08/2021	0.00

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1739
No of Projects Completed/Dropped/Frozen in Current Month	18
No of Projects added in Current Month	15
No of Projects in Current Month	1736

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	547 (31.51%)	12 (.69%)	247 (14.23%)	115 (6.62%)	815 (46.95%)	1736
Latest Approved (Date)	409 (23.56%)	19 (1.09%)	388 (22.35%)	105 (6.05%)	815 (46.95%)	1736

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1469	18,11,790.80	20,00,367.53	9,02,675.78	45.10	1,88,576.73	10.40
Project with Revision in Cost	267	6,57,105.54	6,60,838.21	3,75,594.93	56.80	3,732.67	.60
Total	1,736	24,68,896.34	26,61,205.74	12,78,270.71	48.03	1,92,309.40	7.79
Original Cost of All Projects							
Original Cost	1,736	22,32,019.72	26,61,205.74	12,78,270.71	48.03	4,29,186.02	19.23

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	547	9,50,776.50	12,41,791.08	7,16,487.04	57.70	2,91,014.58	30.61
Latest Approved (RCE)	409	7,69,895.78	8,88,903.48	5,01,908.61	56.50	1,19,007.70	15.46

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	95	1,80,135.87	1,98,324.49	1,31,479.18	66.30	18,188.62	10.10
Total	95	1,80,135.87	1,98,324.49	1,31,479.18	66.29	18,188.62	10.10

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	3	1,905.50	2,153.66	13.02
3	COAL	101	1,45,653.01	1,44,237.84	-0.97	14	28,978.66	34,696.87	19.73
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0.00
7	STEEL	9	25,452.51	31,567.51	24.03	1	15,525.00	21,940.00	41.32
8	PETROLEUM	138	2,95,617.09	3,02,198.67	2.23	26	61,914.04	80,292.67	29.68
9	POWER	78	2,95,137.42	3,66,945.59	24.33	29	1,63,505.25	2,37,386.77	45.19
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,594.81	2.11	12	5,589.39	6,253.60	11.88
12	RAILWAYS	312	4,62,095.03	6,98,959.98	51.26	211	2,30,736.04	4,78,634.95	107.44
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,60,277.95	3.57	130	92,826.35	1,18,797.47	27.98
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	34	2,82,747.18	3,01,054.80	6.47	6	58,069.05	76,455.87	31.66
17	WATER RESOURCES	49	26,781.06	71,946.50	168.65	2	10,382.83	55,782.90	437.26
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	5	2,009.81	2,240.41	11.47
21	HOME AFFAIRS	4	1,716.05	2,571.96	49.88	2	1,382.09	2,238.00	61.93

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	2.96
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		1736	22,32,019.72	26,61,205.74	19.23	449	7,31,133.44	12,01,389.25	64.32

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	78	1,23,127.88	1,70,658.55	38.60	16	47,279.32	1,04,034.99	120.04
2	ARUNACHAL PRADESH	42	24,624.65	44,255.46	79.72	8	11,662.41	31,293.22	168.33
3	ASSAM	47	42,046.33	45,719.63	8.74	19	9,301.62	14,291.97	53.65
4	BIHAR	109	1,23,051.26	1,59,414.14	29.55	35	42,074.64	79,557.34	89.09
5	GOA	11	5,629.77	5,640.26	0.19	2	529.17	539.66	1.98
6	GUJARAT	58	1,04,455.60	1,15,668.59	10.73	16	33,231.01	45,423.09	36.69
7	HARYANA	43	30,316.35	32,837.14	8.32	7	3,872.20	6,803.47	75.70
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	3	8,237.58	18,122.01	119.99
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	4	6,582.27	32,776.33	397.95
10	KARNATAKA	60	71,320.53	76,413.21	7.14	13	16,299.05	21,689.15	33.07
11	KERALA	22	37,466.85	42,063.18	12.27	12	18,147.21	22,767.58	25.46
12	MADHYA PRADESH	84	91,161.40	1,04,937.48	15.11	21	35,588.36	50,361.89	41.51
13	MAHARASHTRA	241	2,16,637.38	2,39,566.06	10.58	31	61,506.65	89,687.02	45.82
14	MANIPUR	12	8,137.49	15,887.67	95.24	1	4,454.17	12,264.15	175.34
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	2	1,390.78	4,709.28	238.61
16	MIZORAM	18	9,030.03	12,978.73	43.73	5	3,593.57	7,542.27	109.88
17	NAGALAND	38	18,265.97	22,463.91	22.98	2	2,699.59	7,298.00	170.34
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	17	27,755.43	36,328.65	30.89
19	PUNJAB	29	15,325.05	18,249.98	19.09	8	5,301.19	8,645.53	63.09
20	RAJASTHAN	60	53,090.50	61,077.72	15.04	13	19,470.60	27,458.05	41.02
21	SIKKIM	14	5,074.99	12,481.74	145.95	3	1,909.76	9,316.51	387.84
22	TAMIL NADU	71	1,19,185.26	1,38,236.09	15.98	22	38,174.33	58,897.84	54.29
23	TRIPURA	13	3,479.87	3,662.68	5.25	3	921.97	1,104.78	19.83
24	UTTAR PRADESH	134	1,78,012.58	1,85,558.75	4.24	29	54,826.89	64,532.54	17.70
25	WEST BENGAL	75	65,583.67	83,081.74	26.68	28	29,736.16	47,570.82	59.98
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	2	655.03	679.33	3.71
27	CHANDIGARH	2	349.15	570.00	63.25	2	349.15	570.00	63.25
28	DELHI	35	90,445.77	91,842.87	1.54	9	11,777.30	13,907.60	18.09
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	12	39,499.71	50,796.46	28.60
31	JHARKHAND	42	70,673.40	69,045.14	-2.30	13	25,347.32	31,532.99	24.40
32	UTTARAKHAND	32	34,539.29	46,026.02	33.26	9	24,756.17	36,269.40	46.51
33	TELANGANA	47	36,326.25	38,960.97	7.25	9	5,330.83	8,459.77	58.70

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						150	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
34	MULTI STATE	128	3,66,425.54	4,80,969.26	31.26	73	1,38,872.00	2,56,157.56	84.46
Total		1736	22,32,019.72	26,61,205.74	19.23	449	7,31,133.44	12,01,389.25	64.32

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	12	9,931.85	10,045.95	5 - 33
3	COAL	101	1,45,653.01	1,44,237.84	-0.97	44	71,443.37	67,942.20	8 - 228
4	FINANCE	2	557.77	557.73	-0.01	1	209.00	208.96	18 - 18
5	FERTILISERS	4	1,101.28	1,101.28	0.00	4	1,101.28	1,101.28	12 - 16
6	MINES	5	7,078.62	7,075.17	-0.05	2	5,895.00	5,895.00	3 - 20
7	STEEL	9	25,452.51	31,567.51	24.03	5	18,768.09	25,183.09	8 - 74
8	PETROLEUM	138	2,95,617.09	3,02,198.67	2.23	68	1,21,399.61	1,27,799.43	1 - 110
9	POWER	78	2,95,137.42	3,66,945.59	24.33	45	2,07,656.15	2,73,404.51	4 - 155
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,594.81	2.11	13	4,940.96	4,754.30	11 - 88
12	RAILWAYS	312	4,62,095.03	6,98,959.98	51.26	157	2,02,568.46	3,31,130.18	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,60,277.95	3.57	139	79,212.04	82,198.44	1 - 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	2	13,765.16	25,095.16	5 - 71
16	URBAN DEVELOPMENT	34	2,82,747.18	3,01,054.80	6.47	11	1,05,664.03	1,17,868.83	4 - 98
17	WATER RESOURCES	49	26,781.06	71,946.50	168.65	17	15,212.03	60,375.23	4 - 72
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	1	246.31	246.31	16 - 16
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	14	6,229.82	6,276.31	3 - 63
21	HOME AFFAIRS	4	1,716.05	2,571.96	49.88	2	1,382.09	2,238.00	26 - 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	3	527.83	538.27	51 - 63
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	1	151.33	151.33	42 - 42
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 22
Total		1736	22,32,019.72	26,61,205.74	19.23	547	9,50,776.50	12,41,791.08	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	78	1,23,127.88	1,70,658.55	38.60	24	83,198.08	1,29,654.35	1 - 180
2	ARUNACHAL PRADESH	42	24,624.65	44,255.46	79.72	6	10,667.27	29,804.81	46 - 155
3	ASSAM	47	42,046.33	45,719.63	8.74	14	9,013.04	12,044.60	2 - 63
4	BIHAR	109	1,23,051.26	1,59,414.14	29.55	25	38,335.22	64,094.90	4 - 128
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	58	1,04,455.60	1,15,668.59	10.73	15	33,355.39	44,015.82	3 - 132
7	HARYANA	43	30,316.35	32,837.14	8.32	13	8,034.65	8,639.80	7 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	3	6,665.52	12,643.52	11 - 150
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	2	10,612.12	36,061.12	63 - 241
10	KARNATAKA	60	71,320.53	76,413.21	7.14	16	40,423.35	40,885.99	6 - 264
11	KERALA	22	37,466.85	42,063.18	12.27	8	12,453.35	13,698.06	13 - 53
12	MADHYA PRADESH	84	91,161.40	1,04,937.48	15.11	43	43,852.72	54,029.12	12 - 73
13	MAHARASHTRA	241	2,16,637.38	2,39,566.06	10.58	40	60,731.27	78,669.44	3 - 216
14	MANIPUR	12	8,137.49	15,887.67	95.24	2	4,971.74	12,721.92	36 - 153
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	2	515.32	515.32	42 - 43
16	MIZORAM	18	9,030.03	12,978.73	43.73	11	6,946.25	10,391.41	43 - 128
17	NAGALAND	38	18,265.97	22,463.91	22.98	14	6,473.72	10,762.04	38 - 117
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	34	70,651.90	73,985.06	2 - 228
19	PUNJAB	29	15,325.05	18,249.98	19.09	11	4,038.42	3,934.12	3 - 108
20	RAJASTHAN	60	53,090.50	61,077.72	15.04	13	16,568.36	22,133.47	14 - 75
21	SIKKIM	14	5,074.99	12,481.74	145.95	1	1,339.48	8,600.00	96 - 96
22	TAMIL NADU	71	1,19,185.26	1,38,236.09	15.98	28	75,362.81	87,687.94	3 - 198
23	TRIPURA	13	3,479.87	3,662.68	5.25	5	1,269.36	1,452.17	11 - 63
24	UTTAR PRADESH	134	1,78,012.58	1,85,558.75	4.24	39	61,754.26	62,460.89	2 - 68
25	WEST BENGAL	75	65,583.67	83,081.74	26.68	30	30,146.27	38,268.32	5 - 324
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	1	417.23	441.33	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	35	90,445.77	91,842.87	1.54	17	51,126.84	52,364.11	4 - 88
29	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	21	30,975.79	40,673.77	15 - 96
31	JHARKHAND	42	70,673.40	69,045.14	-2.30	19	53,677.79	47,347.49	12 - 152
32	UTTARAKHAND	32	34,539.29	46,026.02	33.26	6	22,461.02	33,218.80	3 - 126
33	TELANGANA	47	36,326.25	38,960.97	7.25	15	17,686.46	18,167.88	9 - 168
34	MULTI STATE	128	3,66,425.54	4,80,969.26	31.26	68	1,36,856.50	1,92,228.51	5 - 276
Total		1736	22,32,019.72	26,61,205.74	19.23	547	9,50,776.50	12,41,791.08	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	12	9,931.85	10,045.95	5 - 33
3	COAL	101	1,47,855.61	1,44,237.84	-2.45	39	43,453.44	43,700.30	0 - 168
4	FINANCE	2	557.77	557.73	-0.01	1	209.00	208.96	18 - 18
5	FERTILISERS	4	1,101.28	1,101.28	0.00	4	1,101.28	1,101.28	12 - 16
6	MINES	5	7,971.07	7,075.17	-11.24	1	355.00	355.00	3 - 3
7	STEEL	9	31,867.51	31,567.51	-0.94	1	263.36	263.36	8 - 8
8	PETROLEUM	138	3,09,190.06	3,02,198.67	-2.26	31	32,800.11	36,226.14	1 - 94
9	POWER	78	3,55,536.96	3,66,945.59	3.21	28	1,39,478.38	1,43,642.70	9 - 126
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,594.81	2.11	13	4,940.96	4,754.30	11 - 88
12	RAILWAYS	312	5,60,573.09	6,98,959.98	24.69	129	1,98,393.21	2,76,022.84	0 - 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,43,371.27	5,60,277.95	3.11	100	61,170.08	62,345.84	0 - 105
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	2	13,765.00	25,095.16	5 - 71
16	URBAN DEVELOPMENT	34	2,88,225.13	3,01,054.80	4.45	10	1,09,531.89	1,17,446.83	9 - 98
17	WATER RESOURCES	49	72,178.89	71,946.50	-0.32	12	59,378.93	59,144.30	4 - 72
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	1	246.31	246.31	16 - 16
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	14	6,242.64	6,276.31	3 - 63
21	HOME AFFAIRS	4	1,791.19	2,571.96	43.59	1	1,219.21	2,000.00	26 - 26
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	3	606.71	538.27	51 - 63
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	1	151.33	151.33	42 - 42
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 22
Total		1736	24,68,896.34	26,61,205.74	7.79	409	7,69,895.78	8,88,903.48	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	3	1,905.50	2,153.66	13.02
3	COAL	101	1,47,855.61	1,44,237.84	-2.45	10	22,371.99	25,581.10	14.34
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0.00
7	STEEL	9	31,867.51	31,567.51	-0.94	0	0.00	0.00	0.00
8	PETROLEUM	138	3,09,190.06	3,02,198.67	-2.26	7	14,643.45	19,281.20	31.67
9	POWER	78	3,55,536.96	3,66,945.59	3.21	12	72,224.73	85,706.71	18.67
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,594.81	2.11	12	5,589.39	6,253.60	11.88
12	RAILWAYS	312	5,60,573.09	6,98,959.98	24.69	190	1,94,005.59	3,45,310.63	77.99
13	ROAD TRANSPORT AND HIGHWAYS	908	5,43,371.27	5,60,277.95	3.11	149	1,03,438.31	1,27,447.37	23.21
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	2	13,765.00	25,095.16	82.31
16	URBAN DEVELOPMENT	34	2,88,225.13	3,01,054.80	4.45	4	52,773.00	69,971.73	32.59
17	WATER RESOURCES	49	72,178.89	71,946.50	-0.32	1	231.79	234.03	0.97
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	5	2,022.63	2,240.41	10.77
21	HOME AFFAIRS	4	1,791.19	2,571.96	43.59	1	1,219.21	2,000.00	64.04
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0.00
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		1736	24,68,896.34	26,61,205.74	7.79	401	5,30,998.68	7,70,764.90	45.15

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	74- 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	2	1,559.23	1,673.33	12- 33
3	COAL	101	1,47,855.61	1,44,237.84	-2.45	6	2,004.07	2,377.27	12- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0- 0
7	STEEL	9	31,867.51	31,567.51	-0.94	0	0.00	0.00	0- 0
8	PETROLEUM	138	3,09,190.06	3,02,198.67	-2.26	6	14,220.45	18,779.20	5- 48
9	POWER	78	3,55,536.96	3,66,945.59	3.21	3	10,746.00	16,983.67	9- 126
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,594.81	2.11	4	1,043.69	1,199.69	24- 88
12	RAILWAYS	312	5,60,573.09	6,98,959.98	24.69	85	1,17,867.39	2,05,456.97	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,43,371.27	5,60,277.95	3.11	11	12,860.37	15,356.47	8- 105
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	2	13,765.00	25,095.16	5- 71
16	URBAN DEVELOPMENT	34	2,88,225.13	3,01,054.80	4.45	2	33,909.00	46,193.00	44- 98
17	WATER RESOURCES	49	72,178.89	71,946.50	-0.32	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	4	1,538.31	1,614.15	6- 52
21	HOME AFFAIRS	4	1,791.19	2,571.96	43.59	1	1,219.21	2,000.00	26- 26
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0- 0
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 22
Total		1736	24,68,896.34	26,61,205.74	7.79	131	2,57,540.81	3,96,218.21	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	2	1,559.23	1,673.33	12- 33
3	COAL	101	1,45,653.01	1,44,237.84	-0.97	11	25,847.74	28,730.84	8- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0- 0
7	STEEL	9	25,452.51	31,567.51	24.03	1	15,525.00	21,940.00	74- 74
8	PETROLEUM	138	2,95,617.09	3,02,198.67	2.23	21	52,355.37	69,279.48	5- 110
9	POWER	78	2,95,137.42	3,66,945.59	24.33	19	1,22,937.52	1,90,759.23	9- 155
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,594.81	2.11	4	1,043.69	1,199.69	24- 88
12	RAILWAYS	312	4,62,095.03	6,98,959.98	51.26	110	1,39,971.62	2,78,974.12	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,60,277.95	3.57	23	18,437.24	22,896.45	1- 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	1	13,334.00	24,664.00	71- 71
16	URBAN DEVELOPMENT	34	2,82,747.18	3,01,054.80	6.47	2	33,909.00	46,193.00	44- 98
17	WATER RESOURCES	49	26,781.06	71,946.50	168.65	1	10,151.04	55,548.87	25- 25
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	4	1,525.49	1,614.15	6- 52
21	HOME AFFAIRS	4	1,716.05	2,571.96	49.88	2	1,382.09	2,238.00	26- 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	51- 63
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 22
Total		1736	22,32,019.72	26,61,205.74	19.23	208	4,82,954.46	8,05,563.24	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

List of projects completed/dropped/Frozen during current month							
Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	HALDIA LPG IMPORT FACILITY	03/2015	694.00	10/2018	1,097.54	N.A.	971.84
2	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	01/2015	342.00	03/2021	342.00	03/2021	0.00
3	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	01/2019	350.00	N.A.	2.06
4	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	07/2014	247.00	03/2021	247.00	03/2021	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
5	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS EPC	12/2015	225.02	12/2018	159.20	N.A.	26.00
6	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	02/2017	168.32	04/2017	168.32	02/2021	43.28
7	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	02/2017	199.02	N.A.	199.02	02/2021	14.21
8	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	02/2017	216.71	04/2017	216.71	02/2021	26.84
9	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	02/2017	184.88	N.A.	184.88	02/2021	6.85
	<u>STEEL</u>						
10	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	1,154.18	12/2017	1,154.18	01/2021	1,027.04
11	CENTRAL DISPATCH YARD	08/2015	320.66	08/2018	336.00	11/2020	280.96
	<u>TELECOMMUNICATIONS</u>						
12	CONVERGENT BILLING AND CRM(MUMBAI)	01/2006	247.00	02/2007	247.00	N.A.	0.00
13	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES	05/2006	1,077.00	03/2009	1,077.00	N.A.	0.00
14	DELHI CONVERGENT BILLING AND CRM	02/2006	229.41	03/2012	229.41	N.A.	0.00

<u>List of projects completed/dropped/Frozen during current month</u>							
(All Cost/ Expenditure in Rs. crore)							
				Original		Now anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	PE-5834						
15	CONVERGENT BILLING AND CRM-MTNL(DELHI)	12/2005	249.00	02/2007	229.41	N.A.	0.00
16	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY Central Sector Projects	09/2014	2,111.17	09/2014	2,011.17	N.A.	253.90
	<u>WATER RESOURCES</u>						
17	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR	12/2018	857.26	08/2021	842.25	06/2022	0.00
18	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA	02/2019	317.19	08/2021	317.19	08/2021	0.00

TABLE-14

List of projects added Rs. 150 Crore and above					(February 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	BAROUD OC EXPANSION (3-10 MTY)	8/2020	2,309.80	3/2029	2,309.80	3/2029
2	JAMPALI OCP RCE	5/2020	278.64	3/2024	278.64	3/2024
3	DIPKA OC EXPANSION 40 MTY	12/2020	5,241.40	3/2029	5,241.40	3/2029
4	PORDA CHINTAPANI OCP (10 MTY)	12/2020	2,310.12	3/2029	2,310.12	3/2029
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
5	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 EPC	9/2018	597.67	1/2020	597.67	1/2020
6	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN EPC	9/2018	617.41	2/2019	617.41	2/2019
7	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 PPP (BOT)	11/2019	1,226.88	2/2021	1,226.88	2/2021
8	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) PPP BOT (Hybrid Annuity)	11/2019	1,601.10	2/2021	1,601.10	2/2021
9	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K EPC	1/2017	197.67	12/2022	197.67	12/2022
10	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA EPC	7/2020	3,426.00	12/2021	3,426.00	12/2021
11	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT EPC	10/2013	649.90	12/2020	649.90	12/2020
12	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE EPC	10/2013	446.97	11/2020	446.97	11/2020
13	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA EPC	10/2013	464.09	11/2020	464.09	11/2020
14	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN EPC	10/2020	724.60	3/2023	724.60	3/2023
	<u>STEEL</u>					
15	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 Central Sector Projects	11/2015	2,907.00	6/2023	2,907.00	6/2023

List of projects added Rs. 150 Crore and above					(February 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC

TABLE-15

Milestones (Cumulative due & achieved)	Rs. 150	Crore and above
Total	5799	
Achieved up to month	2955	

TABLE-16

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(February 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	MADHUBAND NLW WASHERY BCCL	289.45	289.45	05/2014	02/2021	06/2021	4
2	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW NLC	17,237.00	17,237.80	11/2021	11/2021	07/2022	8
3	JAYANT EXPANSION OCP 10 TO 20 MTPA NCL Central Sector Projects	1,783.09	1,783.09	03/2021	03/2021	03/2022	12
4	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) NCL	1,255.17	1,255.17	03/2022	03/2022	03/2023	12
5	KANCHAN OC EXPANSION SECL	371.04	371.04	03/2021	03/2021	03/2024	36
6	RECAST PR FOR DHANKASA UG (1.00 MTY) WCL	289.29	289.30	03/2022	03/2022	03/2025	36
7	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) WCL	851.60	851.60	03/2020	03/2020	03/2026	72
8	EXPANSION PR OF JHANJRA UG(5.00 MTY) ECL	1,210.12	1,210.12	03/2022	03/2022	03/2029	84
9	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) WCL	1,184.33	1,184.33	03/2020	03/2020	03/2027	84
	<u>FERTILISERS</u>						
10	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY RCF	426.72	426.72	04/2020	03/2021	04/2021	1
	<u>STEEL</u>						
11	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	02/2021	03/2021	1
	<u>PETROLEUM</u>						
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	02/2021	03/2021	1
13	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	03/2021	04/2021	1
14	MMPL PIPELINE REROUTING PROJECT BPCL	449.58	449.58	12/2019	02/2021	03/2021	1
15	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY BPCL	3,313.00	3,288.96	02/2020	02/2021	03/2021	1

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (February 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	04/2021	05/2021	1
17	PUNE POL STORAGE DEPOT BPCL	282.64	282.64	08/2020	02/2021	03/2021	1
18	PARADIP SOMNATHPUR HALDIA PIPELINE IOCL	1,297.50	1,297.50	10/2021	10/2021	12/2021	2
19	PARADIP HYDERABAD PIPELINE IOCL	2,321.00	3,338.00	12/2020	03/2021	06/2021	3
20	PARADIP LPG IMPORT FACILITY IOCL	690.00	690.00	07/2018	02/2021	05/2021	3
21	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE IOCL	4,497.00	6,025.00	12/2018	08/2021	02/2022	6
22	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT ONGC	34,012.00	25,090.00	06/2020	08/2021	06/2022	10
	<u>POWER</u>						
23	EASTERN REGION STRENGTHENING SCHEME-XV PGCIL	454.11	454.11	04/2018	02/2021	03/2021	1
24	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	03/2021	04/2021	1
25	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII PGCIL	379.95	379.95	12/2019	05/2021	06/2021	1
26	EASTERN REGION STRENGTHENING SCHEME-XVIII PGCIL Central Sector Projects	3,500.00	3,994.00	07/2020	03/2021	04/2021	1
27	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY PGCIL Central Sector Projects	186.17	219.66	07/2019	03/2021	04/2021	1
28	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) PGCIL Central Sector Projects	445.89	445.89	02/2019	02/2021	03/2021	1
29	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	546.36	11/2016	03/2021	05/2021	2
30	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI CPWD	271.90	271.90	11/2019	03/2021	05/2021	2
31	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I PGCIL	374.63	374.63	04/2016	03/2021	06/2021	3

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (February 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
32	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO PGCIL	197.40	197.40	03/2018	03/2021	06/2021	3
33	DEVIKOT SOLAR 90MW NTPC EPC	501.29	501.29	09/2021	09/2021	01/2022	4
34	DEVIKOT SOLAR 150MW NTPC EPC	798.24	798.24	09/2021	09/2021	01/2022	4
35	NOKHRA NTPC EPC	1,722.14	1,722.14	09/2021	09/2021	01/2022	4
	<u>HEALTH AND FAMILY WELFARE</u>						
36	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI HSCC Central Sector Projects	268.84	268.84	N.A.	02/2021	03/2021	1
	<u>RAILWAYS</u>						
37	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) NFR	602.27	760.00	12/2021	03/2021	04/2021	1
38	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	02/2021	04/2021	2
39	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR ECR	477.88	751.55	03/2012	05/2021	07/2021	2
40	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,121.00	N.A.	02/2021	04/2021	2
41	ARSIKERE-TUMKUR SWR	578.00	783.00	03/2020	01/2021	03/2021	2
42	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM WR	691.84	1,017.91	03/2020	12/2020	02/2021	2
43	HAJIPUR - BACHAWARA ECR	678.54	929.86	03/2019	02/2021	05/2021	3
44	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I IRCON	3,055.00	3,055.15	09/2018	12/2021	03/2022	3
45	GADAG-WADI NL SWR	2,841.84	2,841.84	12/2018	12/2024	06/2025	6
46	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) NFR	4,454.17	12,264.15	03/2011	03/2023	12/2023	9
47	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) NFR	2,326.52	6,911.00	03/2015	03/2024	12/2024	9

List of projects reporting additional delayed Rs. 150 Crore and above (February 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
48	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) RVNL	713.48	2,725.00	03/2020	03/2021	12/2021	9
49	CHHAPRA-MUZAFFARPUR (NL) ECR	378.56	1,858.75	N.A.	03/2022	03/2023	12
50	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING NFR	1,798.00	2,042.51	03/2019	03/2023	03/2024	12
51	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC RVNL	927.01	1,400.00	03/2019	06/2021	06/2022	12
52	KARAILA ROAD - SHAKTINAGAR DOUBLING ECR	528.57	528.57	03/2019	03/2021	03/2022	12
53	GARHWA ROAD-RAMNA ECR	348.23	348.23	03/2021	12/2020	03/2022	15
54	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) ECR	162.87	614.45	N.A.	03/2022	12/2023	21
55	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) ECR	372.14	1,470.50	N.A.	03/2021	03/2023	24
56	SAMASTIPUR-DARBANGHA ECR	380.00	519.33	N.A.	02/2023	03/2025	25
57	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I SCR	2,132.77	3,037.95	03/2014	03/2024	03/2027	36
58	RAMNA - SINGRAULI DOUBLING ECR	2,436.21	2,436.21	03/2020	03/2021	03/2024	36
	ROAD TRANSPORT AND HIGHWAYS						
59	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS NHAI	364.56	392.00	N.A.	01/2021	02/2021	1
60	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I NHAI	1,100.19	1,145.31	N.A.	02/2021	03/2021	1
61	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP MoRTH	191.21	191.21	11/2019	01/2021	02/2021	1
62	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 MoRTH	249.50	249.50	05/2019	01/2021	02/2021	1
63	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT MoRTH	218.90	218.90	03/2020	01/2021	02/2021	1
64	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO MoRTH	208.88	208.88	10/2019	01/2021	02/2021	1

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (February 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
65	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF MoRTH	185.18	185.18	02/2020	12/2020	01/2021	1
66	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	01/2021	03/2021	2
67	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K NHAI	641.17	641.17	07/2018	12/2020	02/2021	2
68	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 NHAI	314.43	314.43	N.A.	04/2021	06/2021	2
69	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE MoRTH	208.50	208.50	11/2019	12/2020	02/2021	2
70	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS NHAI PPP (ANNUITY)	374.00	166.90	05/2013	05/2021	08/2021	3
71	4-LANING OF BRAHAMPORE-FARAKA NHAI PPP (BOT)	998.79	998.79	08/2013	12/2021	03/2022	3
72	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH NHAI	707.82	707.82	08/2018	12/2020	03/2021	3
73	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH NHAI Central Sector Projects	641.17	641.17	07/2016	11/2020	02/2021	3
74	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) NHAI EPC	291.53	291.53	N.A.	11/2021	02/2022	3
75	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 MoRTH	497.14	572.66	08/2016	03/2021	06/2021	3
76	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION MoRTH	335.32	335.32	06/2017	03/2021	06/2021	3
77	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V MoRTH	476.20	544.00	09/2016	03/2021	06/2021	3
78	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION MoRTH	624.98	731.50	10/2016	03/2021	06/2021	3
79	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI MoRTH	452.94	435.61	07/2016	03/2021	06/2021	3
80	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION MoRTH	496.02	496.02	03/2015	03/2021	06/2021	3

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
81	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV NHAI	894.00	929.32	04/2020	03/2021	07/2021	4
82	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI-KAWARDHA SECTION. MoRTH EPC	291.05	291.05	N.A.	10/2020	03/2021	5
83	FOUR LANNING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB NHAI	261.76	207.00	N.A.	01/2021	07/2021	6
84	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. NHAI	848.45	848.45	03/2020	02/2021	12/2021	10
85	4-LANNING OF STHIYATHOPU-CHOLOPURAM NHAI Central Sector Projects	1,227.87	1,227.87	09/2017	09/2021	07/2022	10
86	FOUR LANNING OF CHOLOPURAM-THANJAVUR NHAI Central Sector Projects	1,176.37	1,176.37	08/2017	02/2021	07/2022	17
87	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K MoRTH	196.23	196.00	11/2020	11/2020	08/2022	21
<u>URBAN DEVELOPMENT</u>							
88	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N CPWD	392.00	392.00	08/2020	12/2021	03/2022	3
89	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR NBCC	2,694.00	2,694.00	N.A.	03/2022	07/2022	4
90	DELHI MRTS PHASE-III DMRC	38,585.00	38,585.00	03/2016	03/2021	09/2021	6
91	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I CPWD	1,180.00	1,100.80	07/2021	09/2021	12/2024	39
<u>HUMAN RESOURCE DEVELOPMENT</u>							
92	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB CPWD	294.00	350.69	04/2019	03/2021	04/2021	1
93	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB CPWD	430.00	387.83	05/2020	12/2021	02/2022	2
94	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. CPWD	348.24	348.24	05/2022	05/2022	08/2022	3
<u>HOME AFFAIRS</u>							

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (February 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
95	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD	1,219.21	2,000.00	10/2019	09/2021	12/2021	3

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	58,335.80
CIVIL AVIATION	19	13,786.34	137,86.34	14,034.50	2,597.30
COAL	101	1,45,653.01	1,478,55.61	1,44,237.84	45,301.73
FINANCE	2	557.77	5,57.77	557.73	319.39
FERTILISERS	4	1,101.28	11,01.28	1,101.28	842.45
MINES	5	7,078.62	79,71.07	7,075.17	1,260.44
STEEL	9	25,452.51	318,67.51	31,567.51	22,119.24
PETROLEUM	138	2,95,617.09	3,091,90.06	3,02,198.67	1,04,628.98
POWER	78	2,95,137.42	3,555,36.96	3,66,945.59	2,51,832.37
HEAVY INDUSTRY	1	1,554.00	15,54.00	900.00	815.00
HEALTH AND FAMILY WELFARE	29	15,273.26	152,73.26	15,594.81	7,459.26
RAILWAYS	312	4,62,095.03	5,605,73.09	6,98,959.98	2,44,559.04
ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,433,71.27	5,60,277.95	3,48,803.37
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,814.28
TELECOMMUNICATIONS	3	14,013.36	140,13.20	25,343.36	16,674.10
URBAN DEVELOPMENT	34	2,82,747.18	2,882,25.13	3,01,054.80	1,34,498.88
WATER RESOURCES	49	26,781.06	721,78.89	71,946.50	21,022.75
DEFENCE PRODUCTION	1	246.31	2,46.31	246.31	115.20
COMMERCE	1	302.64	3,02.64	302.64	60.00
HUMAN RESOURCE DEVELOPMENT	26	11,077.40	110,90.22	11,265.83	2,413.56
HOME AFFAIRS	4	1,716.05	17,91.19	2,571.96	1,044.88
RURAL DEVELOPMENT	4	889.43	9,68.31	899.87	472.48
CULTURE DEVELOPMENT	1	151.33	1,51.33	151.33	145.60
DPIIT	2	17,352.09	173,52.09	18,990.30	11,134.61
Grand total	1736	22,32,019.72	24,68,896.34	26,61,205.74	12,78,270.71

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	78	1,23,127.88	1,70,658.55	38.60	10	41,926.16	97,304.43	1 - 180
2	ARUNACHAL PRADESH	42	24,624.65	44,255.46	79.72	2	8,782.23	27,919.77	134 - 155
3	ASSAM	47	42,046.33	45,719.63	8.74	8	6,161.24	9,418.06	2 - 48
4	BIHAR	109	1,23,051.26	1,59,414.14	29.55	10	30,865.91	56,867.93	15 - 128
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	58	1,04,455.60	1,15,668.59	10.73	10	29,488.68	40,276.89	3 - 132
7	HARYANA	43	30,316.35	32,837.14	8.32	3	828.42	1,520.46	7 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	1	3,919.59	9,897.59	150 - 150
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	1	2,500.00	27,949.00	241 - 241
10	KARNATAKA	60	71,320.53	76,413.21	7.14	3	2,315.94	3,076.00	12 - 20
11	KERALA	22	37,466.85	42,063.18	12.27	4	7,431.46	8,700.21	31 - 53
12	MADHYA PRADESH	84	91,161.40	1,04,937.48	15.11	13	22,053.99	32,844.74	12 - 73
13	MAHARASHTRA	241	2,16,637.38	2,39,566.06	10.58	14	39,513.58	61,864.28	9 - 216
14	MANIPUR	12	8,137.49	15,887.67	95.24	1	4,454.17	12,264.15	153 - 153
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	0	0.00	0.00	-
16	MIZORAM	18	9,030.03	12,978.73	43.73	3	2,782.20	6,227.36	108 - 128
17	NAGALAND	38	18,265.97	22,463.91	22.98	2	2,699.59	7,298.00	57 - 117
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	12	25,923.02	33,494.18	15 - 204
19	PUNJAB	29	15,325.05	18,249.98	19.09	3	1,201.49	1,284.88	18 - 38
20	RAJASTHAN	60	53,090.50	61,077.72	15.04	6	14,632.86	20,198.20	14 - 75
21	SIKKIM	14	5,074.99	12,481.74	145.95	1	1,339.48	8,600.00	96 - 96
22	TAMIL NADU	71	1,19,185.26	1,38,236.09	15.98	10	17,313.56	30,388.30	21 - 198
23	TRIPURA	13	3,479.87	3,662.68	5.25	3	921.97	1,104.78	24 - 63
24	UTTAR PRADESH	134	1,78,012.58	1,85,558.75	4.24	6	29,692.84	31,692.25	8 - 68
25	WEST BENGAL	75	65,583.67	83,081.74	26.68	10	17,118.86	25,256.24	28 - 324
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	1	417.23	441.33	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	35	90,445.77	91,842.87	1.54	4	6,610.76	7,927.23	22 - 88
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	9	25,751.75	35,569.08	21 - 84
31	JHARKHAND	42	70,673.40	69,045.14	-2.30	4	16,591.98	18,075.61	30 - 44
32	UTTARAKHAND	32	34,539.29	46,026.02	33.26	3	21,686.06	32,443.84	3 - 126
33	TELANGANA	47	36,326.25	38,960.97	7.25	6	2,178.29	3,153.93	9 - 132
34	MULTI STATE	128	3,66,425.54	4,80,969.26	31.26	45	95,851.15	1,52,504.52	5 - 276
Total		1736	22,32,019.72	26,61,205.74	19.23	208	4,82,954.46	8,05,563.24	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	160	14
2	ROAD TRANSPORT AND HIGHWAYS	156	4
3	PETROLEUM	55	7
4	POWER	46	2
5	COAL	30	5
6	URBAN DEVELOPMENT	23	3
7	CIVIL AVIATION	5	0
8	STEEL	5	1
9	ATOMIC ENERGY	4	0
10	HEALTH AND FAMILY WELFARE	4	0
11	DPIIT	2	0
12	MINES	1	0
13	SHIPPING AND PORTS	1	0
14	TELECOMMUNICATIONS	1	0
15	WATER RESOURCES	1	0
16	HOME AFFAIRS	1	1
	Total	495	37

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2020			
	<u>STEEL</u>			
1	INSTALLATION OF NEW HOT STRIP MILL AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000094]	3,127.30	04/2018	3,201.42
	<u>PETROLEUM</u>			
2	INTEGRATED DEVELOPMENT OF B-127 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000131]	2,059.63	03/2015	2,011.80
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000197]	6,068.80	04/2019	4,956.05
4	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000212]	4,619.94	12/2017	4,663.66
5	INDMAX PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000243]	2,582.00	11/2019	1,718.52
6	BS-VI PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000310]	3,380.00	09/2019	2,381.00
7	BS-VI PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000320]	1,222.00	09/2019	764.17
8	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000322]	2,934.40	09/2019	1,957.94
9	BS-VI PROJECT AT PANIPAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000325]	3,529.00	07/2019	2,095.75
	July,2020			
10	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000204]	2,818.88	03/2019	2,907.03
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000347]	723.54	02/2018	1,163.64
12	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000492]	867.66	05/2018	1,289.81
	<u>URBAN DEVELOPMENT</u>			
13	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000101]	768.88	02/2014	1,125.98
	August,2020			
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
14	RESID UPGRADATION PROJECT (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000184]	3,110.36	11/2015	2,915.00
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA- BARAUNI CRUDE OIL TRUNK PIPELINE (OIL INDIA LIMITED) - [N18000148]	871.35	03/2015	565.63
	<u>URBAN DEVELOPMENT</u>			
16	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000109]	253.92	06/2016	1,113.24
	December,2020			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000505]	1,583.79	01/2019	1,648.90
	January,2021			
	<u>PETROLEUM</u>			
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000169]	993.00	01/2012	1,693.00
19	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000238]	1,879.00	06/2020	1,694.25
	February,2021			
	<u>STEEL</u>			
20	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000096]	1,154.18	12/2017	1,027.04

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	January,2021			
	<u>PETROLEUM</u>			
1	HALDIA BARAUNI PRODUCT PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000251]	1,021.00	12/2020	4.45
2	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000309]	1,342.00	08/2020	6.30
	February,2021			
3	HALDIA LPG IMPORT FACILITY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000223]	694.00	10/2018	971.84
	<u>TELECOMMUNICATIONS</u>			
4	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (DEPARTMENT OF TELECOMMUNICATION) - [N26000065]	1,077.00	03/2009	0.00
5	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY (INDIAN TELEPHONE INDUSTRY) - [N26000102]	2,111.17	09/2014	253.90

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	484
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects Elevated in Current Month	8
No of Projects added in Current Month	7
No of Projects in Current Month	495

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	208 (42.02%)	7 (1.41%)	81 (16.36%)	38 (7.68%)	161 (32.53%)	495
Latest Approved (Date)	155 (31.31%)	9 (1.82%)	134 (27.07%)	36 (7.27%)	161 (32.53%)	495

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	412	13,71,924.57	15,53,417.56	6,87,230.49	44.20	1,81,492.99	13.20
Project with Revision in Cost	83	5,78,945.67	5,87,949.90	3,31,664.15	56.40	9,004.23	1.60
Total	495	19,50,870.24	21,41,367.46	10,18,894.64	47.58	1,90,497.22	9.76
Original Cost of All Projects							
Original Cost	495	17,18,768.08	21,41,367.46	10,18,894.64	47.58	4,22,599.38	24.59

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	208	7,97,946.14	10,96,241.62	6,40,016.10	58.40	2,98,295.48	37.38
Latest Approved (RCE)	155	6,58,142.61	7,81,214.88	4,47,234.96	57.20	1,23,072.27	18.70

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	37	1,55,331.20	1,72,063.70	1,14,452.40	66.50	16,732.50	10.80
Total	37	1,55,331.20	1,72,063.70	1,14,452.40	66.52	16,732.50	10.77

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 1000 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	30	1,08,556.34	1,13,115.57	4.20	3	25,805.84	30,365.07	17.67
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	5	24,006.86	30,121.86	25.47	1	15,525.00	21,940.00	41.32
6	PETROLEUM	55	2,62,018.90	2,68,216.38	2.37	15	57,503.55	74,997.97	30.42
7	POWER	46	2,81,387.51	3,52,790.87	25.38	23	1,60,825.94	2,34,302.65	45.69
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
9	RAILWAYS	160	3,93,671.88	6,22,186.96	58.05	121	1,99,497.85	4,29,297.92	115.19
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,183.92	6.57	43	58,063.48	75,012.62	29.19
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	23	2,78,636.14	2,96,792.02	6.52	5	57,954.79	76,189.87	31.46
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		495	17,18,768.08	21,41,367.46	24.59	222	6,48,573.79	10,88,339.27	67.81

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	10	45,532.51	1,02,125.54	124.29
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	3	10,761.23	29,956.67	178.38
3	ASSAM	6	27,224.48	29,754.21	9.29	4	4,630.48	7,160.21	54.63
4	BIHAR	27	87,426.57	1,21,814.59	39.33	15	33,512.04	67,900.06	102.61
5	GUJARAT	23	86,210.17	96,827.87	12.32	10	30,646.76	41,923.51	36.80
6	HARYANA	12	16,498.78	18,358.28	11.27	1	1,108.00	2,967.50	167.82
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	3	8,237.58	18,122.01	119.99
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	3	6,236.00	32,296.00	417.90
9	KARNATAKA	17	53,661.87	58,417.00	8.86	9	14,348.52	19,103.65	33.14
10	KERALA	10	31,871.86	35,970.00	12.86	7	15,996.96	20,119.14	25.77
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	11	31,854.48	45,006.24	41.29
12	MAHARASHTRA	49	1,39,827.20	1,66,044.35	18.75	20	57,187.57	84,111.65	47.08
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	175.34
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	130.69
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	197.05
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	11	26,251.24	34,290.60	30.62
18	PUNJAB	4	5,049.00	7,181.59	42.24	2	2,557.95	4,867.50	90.29
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	5	16,355.72	23,031.18	40.81
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	27	99,664.04	1,17,707.46	18.10	13	36,105.21	54,543.63	51.07
22	UTTAR PRADESH	48	1,40,935.26	1,48,074.66	5.07	14	48,992.89	57,073.42	16.49
23	WEST BENGAL	24	46,677.83	62,904.03	34.76	13	24,750.26	41,007.79	65.69
24	DELHI	9	80,186.38	81,749.70	1.95	3	10,256.21	11,898.73	16.01
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	8	37,748.96	48,488.81	28.45
26	JHARKHAND	16	56,545.31	60,711.44	7.37	7	23,642.14	29,364.27	24.20
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	4	23,213.06	34,244.91	47.52
28	TELANGANA	6	19,991.02	21,700.38	8.55	2	2,378.60	4,455.84	87.33
29	MULTI STATE	62	3,38,662.43	4,48,460.13	32.42	39	1,24,849.32	2,36,900.79	89.75
Total		495	17,18,768.08	21,41,367.46	24.59	222	6,48,573.79	10,88,339.27	67.81

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	4	6,397.00	6,487.00	7 - 12
3	COAL	30	1,08,556.34	1,13,115.57	4.20	14	54,081.96	56,156.44	8 - 228
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	20 - 20
5	STEEL	5	24,006.86	30,121.86	25.47	3	18,241.86	24,656.86	30 - 74
6	PETROLEUM	55	2,62,018.90	2,68,216.38	2.37	22	1,03,313.47	1,09,336.59	2 - 110
7	POWER	46	2,81,387.51	3,52,790.87	25.38	29	2,00,920.31	2,66,611.11	4 - 155
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	-
9	RAILWAYS	160	3,93,671.88	6,22,186.96	58.05	102	1,67,688.35	2,98,451.48	2 - 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,183.92	6.57	18	28,737.71	31,397.03	1 - 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71 - 71
13	URBAN DEVELOPMENT	23	2,78,636.14	2,96,792.02	6.52	6	1,03,849.14	1,16,053.94	36 - 98
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26 - 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 22
Total		495	17,18,768.08	21,41,367.46	24.59	208	7,97,946.14	10,96,241.62	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	9	77,591.98	1,23,929.47	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	3	10,035.33	29,172.87	60 - 155
3	ASSAM	6	27,224.48	29,754.21	9.29	4	4,630.48	7,160.21	2 - 48
4	BIHAR	27	87,426.57	1,21,814.59	39.33	9	32,035.52	57,490.05	15 - 128
5	GUJARAT	23	86,210.17	96,827.87	12.32	10	31,026.32	41,381.90	3 - 74
6	HARYANA	12	16,498.78	18,358.28	11.27	2	3,764.72	3,764.72	20 - 29
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	2	6,405.52	12,383.52	15 - 150
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	2	10,612.12	36,061.12	63 - 241
9	KARNATAKA	17	53,661.87	58,417.00	8.86	5	33,596.70	34,095.76	20 - 264
10	KERALA	10	31,871.86	35,970.00	12.86	4	10,137.40	11,274.92	13 - 44
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	14	30,976.81	40,755.44	12 - 73
12	MAHARASHTRA	49	1,39,827.20	1,66,044.35	18.75	15	44,494.24	66,503.66	9 - 216
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	108 - 108
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	117 - 117
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	23	60,801.54	68,182.07	2 - 228
18	PUNJAB	4	5,049.00	7,181.59	42.24	0	0.00	0.00	-
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	27	99,664.04	1,17,707.46	18.10	14	68,120.02	79,846.87	3 - 145
22	UTTAR PRADESH	48	1,40,935.26	1,48,074.66	5.07	13	52,637.34	53,864.45	4 - 48
23	WEST BENGAL	24	46,677.83	62,904.03	34.76	12	23,827.27	31,756.93	12 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	5	47,151.73	48,258.32	22 - 66
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	6	25,403.02	34,561.43	21 - 74
26	JHARKHAND	16	56,545.31	60,711.44	7.37	7	43,801.65	43,537.53	13 - 83
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	6	19,991.02	21,700.38	8.55	3	13,183.42	12,815.54	16 - 168
29	MULTI STATE	62	3,38,662.43	4,48,460.13	32.42	38	1,23,193.31	1,76,625.40	5 - 276
Total		495	17,18,768.08	21,41,367.46	24.59	208	7,97,946.14	10,96,241.62	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

Extent of time overrun in projects with respect to latest schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	4	6,397.00	6,487.00	7 - 12
3	COAL	30	1,10,782.59	1,13,115.57	2.11	10	32,620.94	32,620.94	0 - 168
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	-
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	-
6	PETROLEUM	55	2,74,937.84	2,68,216.38	-2.44	10	24,207.89	27,734.06	2 - 94
7	POWER	46	3,41,590.96	3,52,790.87	3.28	19	1,36,138.21	1,40,302.53	9 - 126
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	-
9	RAILWAYS	160	4,90,992.67	6,22,186.96	26.72	81	1,67,722.31	2,48,614.21	0 - 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,579.19	2,52,183.92	6.60	16	26,158.09	27,851.03	8 - 105
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71 - 71
13	URBAN DEVELOPMENT	23	2,83,962.35	2,96,792.02	4.52	6	1,08,139.00	1,16,053.94	36 - 98
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26 - 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 22
Total		495	19,50,870.24	21,41,367.46	9.76	155	6,58,142.61	7,81,214.88	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	30	1,10,782.59	1,13,115.57	2.11	2	19,898.73	22,384.28	12.49
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0.00
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	0.00
6	PETROLEUM	55	2,74,937.84	2,68,216.38	-2.44	4	13,229.29	17,636.86	33.32
7	POWER	46	3,41,590.96	3,52,790.87	3.28	10	71,533.96	84,807.22	18.56
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
9	RAILWAYS	160	4,90,992.67	6,22,186.96	26.72	106	1,64,818.82	2,99,474.10	81.70
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,579.19	2,52,183.92	6.60	45	61,194.33	78,063.29	27.57
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	23	2,83,962.35	2,96,792.02	4.52	4	52,773.00	69,971.73	32.59
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		495	19,50,870.24	21,41,367.46	9.76	181	4,48,879.43	6,63,021.78	47.71

[^] - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs.						1000	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	12- 12
3	COAL	30	1,10,782.59	1,13,115.57	2.11	0	0.00	0.00	0- 0
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0- 0
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	0- 0
6	PETROLEUM	55	2,74,937.84	2,68,216.38	-2.44	4	13,229.29	17,636.86	5- 38
7	POWER	46	3,41,590.96	3,52,790.87	3.28	3	10,746.00	16,983.67	9- 126
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	0- 0
9	RAILWAYS	160	4,90,992.67	6,22,186.96	26.72	59	1,06,157.30	1,88,145.17	2- 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,579.19	2,52,183.92	6.60	6	10,101.71	12,162.53	8- 105
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71- 71
13	URBAN DEVELOPMENT	23	2,83,962.35	2,96,792.02	4.52	2	33,909.00	46,193.00	44- 98
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26- 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 22
Total		495	19,50,870.24	21,41,367.46	9.76	82	2,36,646.60	3,68,506.53	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	12- 12
3	COAL	30	1,08,556.34	1,13,115.57	4.20	2	23,144.11	25,218.59	8- 62
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	5	24,006.86	30,121.86	25.47	1	15,525.00	21,940.00	74- 74
6	PETROLEUM	55	2,62,018.90	2,68,216.38	2.37	12	48,820.57	65,060.13	5- 110
7	POWER	46	2,81,387.51	3,52,790.87	25.38	17	1,22,229.06	1,89,993.21	9- 155
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	0- 0
9	RAILWAYS	160	3,93,671.88	6,22,186.96	58.05	77	1,25,194.15	2,57,242.27	2- 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,183.92	6.57	7	11,634.33	14,661.53	1- 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71- 71
13	URBAN DEVELOPMENT	23	2,78,636.14	2,96,792.02	6.52	2	33,909.00	46,193.00	44- 98
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26- 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 22
Total		495	17,18,768.08	21,41,367.46	24.59	127	4,50,925.56	7,63,242.90	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

<u>List of projects completed/dropped/Frozen during current month</u>					Rs. 1000		Crore and above	
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	
	<u>PETROLEUM</u>							
1	HALDIA LPG IMPORT FACILITY	03/2015	694.00	10/2018	1,097.54	N.A.	971.84	
	<u>STEEL</u>							
2	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	1,154.18	12/2017	1,154.18	01/2021	1,027.04	
	<u>TELECOMMUNICATIONS</u>							
3	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES	05/2006	1,077.00	03/2009	1,077.00	N.A.	0.00	
4	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY Central Sector Projects	09/2014	2,111.17	09/2014	2,011.17	N.A.	253.90	

TABLE-32

List of projects added Rs. 1000 Crore and above					(February 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	BAROUD OC EXPANSION (3-10 MTY)	8/2020	2,309.80	3/2029	2,309.80	3/2029
2	PORDA CHINTAPANI OCP (10 MTY)	12/2020	2,310.12	3/2029	2,310.12	3/2029
3	DIPKA OC EXPANSION 40 MTY	12/2020	5,241.40	3/2029	5,241.40	3/2029
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
4	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 PPP (BOT)	11/2019	1,226.88	2/2021	1,226.88	2/2021
5	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) PPP BOT (Hybrid Annuity)	11/2019	1,601.10	2/2021	1,601.10	2/2021
6	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA EPC	7/2020	3,426.00	12/2021	3,426.00	12/2021
	<u>STEEL</u>					
7	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 Central Sector Projects	11/2015	2,907.00	6/2023	2,907.00	6/2023

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2762	
Achieved up to month	1759	

TABLE-34

List of projects reporting additional delayed Rs. 1000 Crore and above							(February 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW NLC	17,237.00	17,237.80	11/2021	11/2021	07/2022	8
2	JAYANT EXPANSION OCP 10 TO 20 MTPA NCL Central Sector Projects	1,783.09	1,783.09	03/2021	03/2021	03/2022	12
3	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) NCL	1,255.17	1,255.17	03/2022	03/2022	03/2023	12
4	EXPANSION PR OF JHANJRA UG(5.00 MTY) ECL	1,210.12	1,210.12	03/2022	03/2022	03/2029	84
5	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) WCL	1,184.33	1,184.33	03/2020	03/2020	03/2027	84
	<u>STEEL</u>						
6	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	02/2021	03/2021	1
	<u>PETROLEUM</u>						
7	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	02/2021	03/2021	1
8	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY BPCL	3,313.00	3,288.96	02/2020	02/2021	03/2021	1
9	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	04/2021	05/2021	1
10	PARADIP SOMNATHPUR HALDIA PIPELINE IOCL	1,297.50	1,297.50	10/2021	10/2021	12/2021	2
11	PARADIP HYDERABAD PIPELINE IOCL	2,321.00	3,338.00	12/2020	03/2021	06/2021	3
12	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE IOCL	4,497.00	6,025.00	12/2018	08/2021	02/2022	6
13	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT ONGC	34,012.00	25,090.00	06/2020	08/2021	06/2022	10
	<u>POWER</u>						
14	EASTERN REGION STRENGTHENING SCHEME- XVIII PGCIL Central Sector Projects	3,500.00	3,994.00	07/2020	03/2021	04/2021	1

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above (February 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
15	NOKHRA NTPC EPC	1,722.14	1,722.14	09/2021	09/2021	01/2022	4
	<u>RAILWAYS</u>						
16	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	02/2021	04/2021	2
17	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM- CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,121.00	N.A.	02/2021	04/2021	2
18	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM WR	691.84	1,017.91	03/2020	12/2020	02/2021	2
19	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I IRCON	3,055.00	3,055.15	09/2018	12/2021	03/2022	3
20	GADAG-WADI NL SWR	2,841.84	2,841.84	12/2018	12/2024	06/2025	6
21	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) NFR	4,454.17	12,264.15	03/2011	03/2023	12/2023	9
22	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) NFR	2,326.52	6,911.00	03/2015	03/2024	12/2024	9
23	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) RVNL	713.48	2,725.00	03/2020	03/2021	12/2021	9
24	CHHAPRA-MUZAFFARPUR (NL) ECR	378.56	1,858.75	N.A.	03/2022	03/2023	12
25	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING NFR	1,798.00	2,042.51	03/2019	03/2023	03/2024	12
26	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC RVNL	927.01	1,400.00	03/2019	06/2021	06/2022	12
27	SAKRI-NIRMALI AND JHANJHARPUR- LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) ECR	372.14	1,470.50	N.A.	03/2021	03/2023	24
28	KADAPA-BANGALORE (NL), KADAPA- PENDLIMARRI PH-I SCR	2,132.77	3,037.95	03/2014	03/2024	03/2027	36
29	RAMNA - SINGRAULI DOUBLING ECR	2,436.21	2,436.21	03/2020	03/2021	03/2024	36
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
30	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I NHAI	1,100.19	1,145.31	N.A.	02/2021	03/2021	1

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above (February 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
31	FOUR LANNING OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	01/2021	03/2021	2
32	4-LANNING OF STHIYATHOPU-CHOLOPURAM NHAI Central Sector Projects	1,227.87	1,227.87	09/2017	09/2021	07/2022	10
33	FOUR LANNING OF CHOLOPURAM- THANJAVUR NHAI Central Sector Projects	1,176.37	1,176.37	08/2017	02/2021	07/2022	17
	<u>URBAN DEVELOPMENT</u>						
34	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR NBCC	2,694.00	2,694.00	N.A.	03/2022	07/2022	4
35	DELHI MRTS PHASE-III DMRC	38,585.00	38,585.00	03/2016	03/2021	09/2021	6
36	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I CPWD	1,180.00	1,100.80	07/2021	09/2021	12/2024	39
	<u>HOME AFFAIRS</u>						
37	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD	1,219.21	2,000.00	10/2019	09/2021	12/2021	3

TABLE-35

<u>Sector wise analysis of projects</u> Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	58,335.80
CIVIL AVIATION	5	7,613.90	76,13.90	7,703.90	1,118.82
COAL	30	1,08,556.34	1,107,82.59	1,13,115.57	35,848.97
MINES	1	5,540.00	64,35.90	5,540.00	698.73
STEEL	5	24,006.86	304,21.86	30,121.86	21,751.22
PETROLEUM	55	2,62,018.90	2,749,37.84	2,68,216.38	90,345.85
POWER	46	2,81,387.51	3,415,90.96	3,52,790.87	2,43,853.18
HEALTH AND FAMILY WELFARE	4	6,160.00	61,60.00	6,531.00	773.17
RAILWAYS	160	3,93,671.88	4,909,92.67	6,22,186.96	2,08,691.88
ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,365,79.19	2,52,183.92	1,77,554.67
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,814.28
TELECOMMUNICATIONS	1	13,334.00	133,34.00	24,664.00	16,594.00
URBAN DEVELOPMENT	23	2,78,636.14	2,839,62.35	2,96,792.02	1,32,509.65
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	16,995.57
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	874.24
DPIIT	2	17,352.09	173,52.09	18,990.30	11,134.61
Grand total	495	17,18,768.08	19,50,870.24	21,41,367.46	10,18,894.64


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	7	41,080.27	96,339.76	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	2	8,782.23	27,919.77	134 - 155
3	ASSAM	6	27,224.48	29,754.21	9.29	4	4,630.48	7,160.21	2 - 48
4	BIHAR	27	87,426.57	1,21,814.59	39.33	7	29,343.85	54,798.38	15 - 128
5	GUJARAT	23	86,210.17	96,827.87	12.32	8	28,618.93	38,974.51	3 - 74
6	HARYANA	12	16,498.78	18,358.28	11.27	0	0.00	0.00	-
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	1	3,919.59	9,897.59	150 - 150
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	1	2,500.00	27,949.00	241 - 241
9	KARNATAKA	17	53,661.87	58,417.00	8.86	1	1,156.94	1,656.00	20 - 20
10	KERALA	10	31,871.86	35,970.00	12.86	3	6,824.40	7,985.96	31 - 44
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	8	20,545.18	30,841.85	12 - 73
12	MAHARASHTRA	49	1,39,827.20	1,66,044.35	18.75	11	38,100.29	60,109.71	9 - 216
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	108 - 108
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	117 - 117
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	10	25,065.60	32,446.13	15 - 204
18	PUNJAB	4	5,049.00	7,181.59	42.24	0	0.00	0.00	-
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	27	99,664.04	1,17,707.46	18.10	7	16,362.78	28,484.63	27 - 145
22	UTTAR PRADESH	48	1,40,935.26	1,48,074.66	5.07	5	29,479.84	31,478.90	8 - 39
23	WEST BENGAL	24	46,677.83	62,904.03	34.76	6	16,254.80	24,199.79	63 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	2	5,992.21	7,178.00	22 - 26
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	5	24,001.00	33,261.43	21 - 74
26	JHARKHAND	16	56,545.31	60,711.44	7.37	2	16,090.78	17,382.66	33 - 40
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	6	19,991.02	21,700.38	8.55	0	0.00	0.00	-
29	MULTI STATE	62	3,38,662.43	4,48,460.13	32.42	29	87,656.69	1,42,359.18	5 - 276
Total		495	17,18,768.08	21,41,367.46	24.59	127	4,50,925.56	7,63,242.90	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

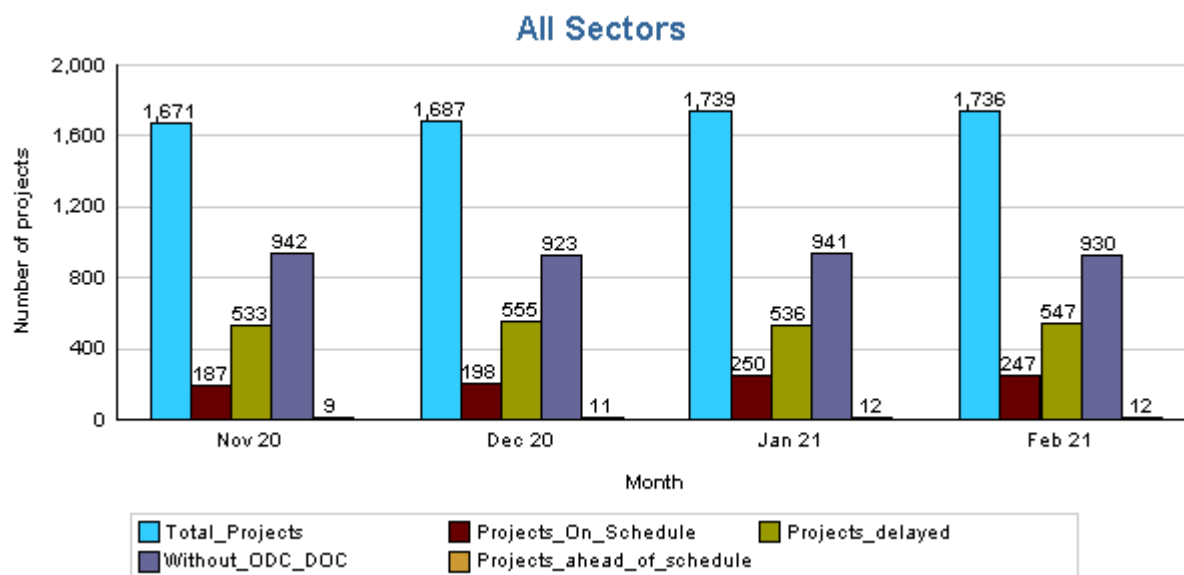

Break-up of 547 Delayed projects in February 2021

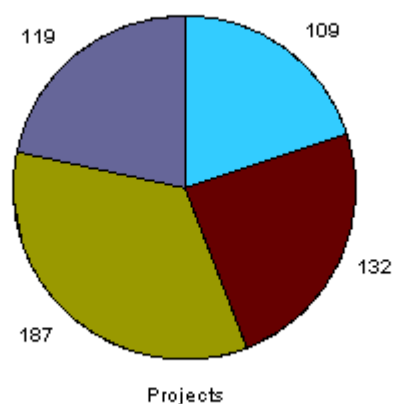


Delay in Months

Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

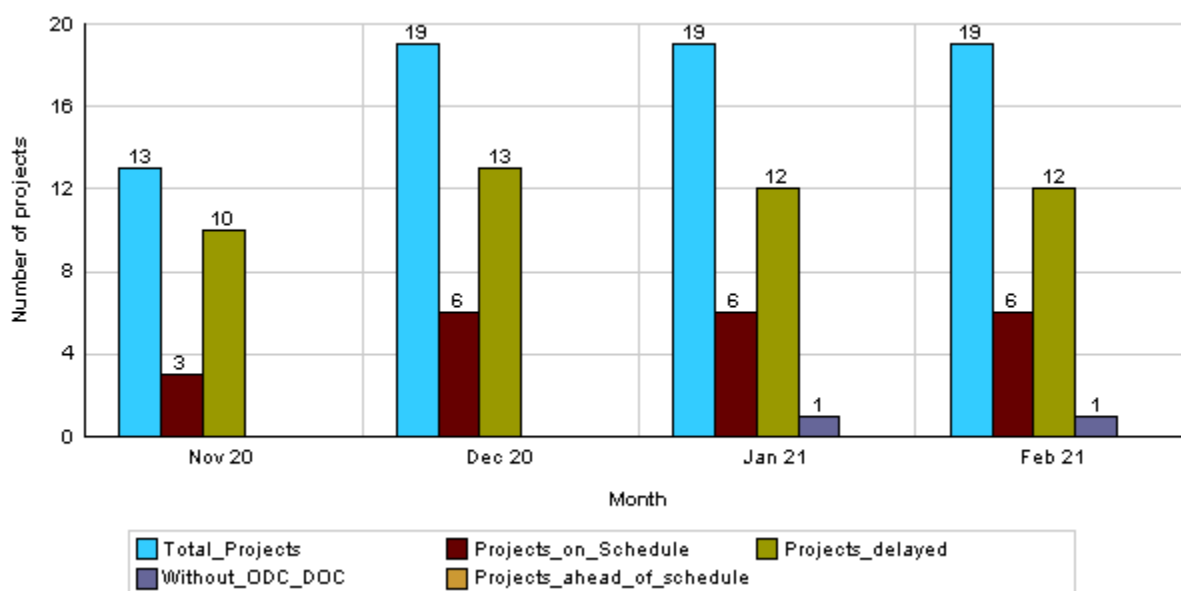


Break-up of 12 Delayed projects in February 2021




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	8	3	1	0

Graphical Presentation of RURAL DEVELOPMENT Sector

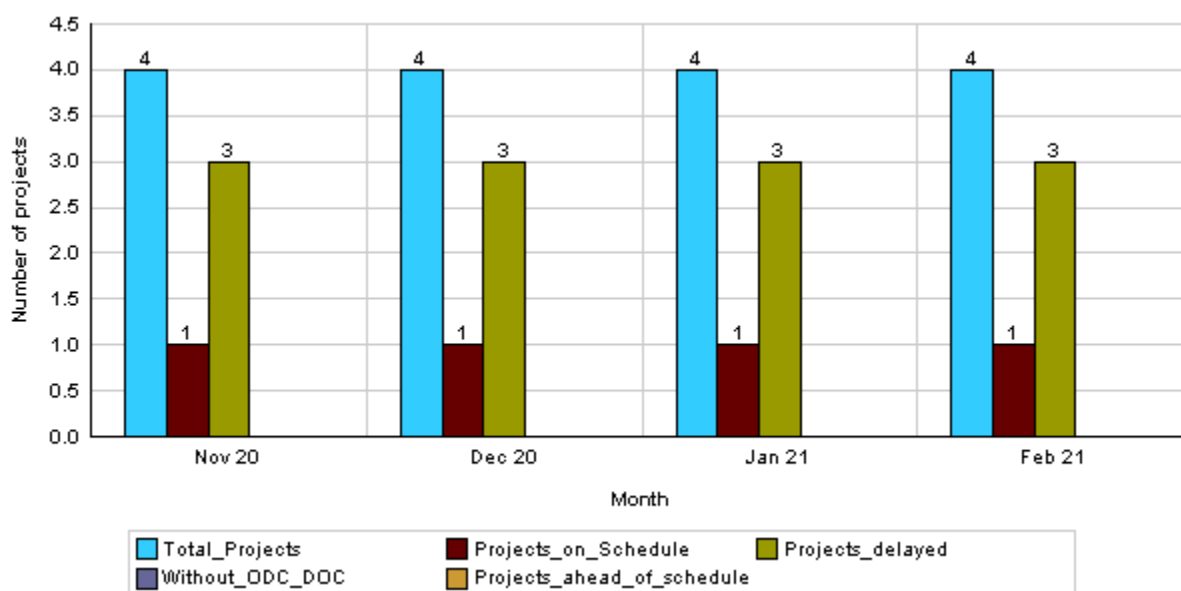


Break-up of 3 Delayed projects in February 2021

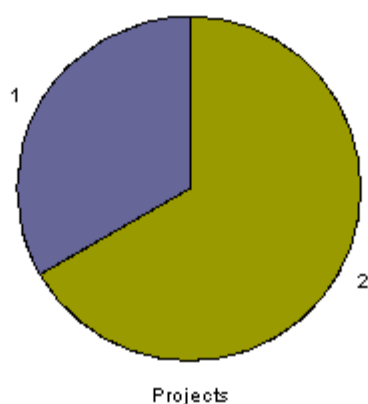

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	2	0
MORE THAN 60	0	0	0	1

Graphical Presentation of HOME AFFAIRS Sector

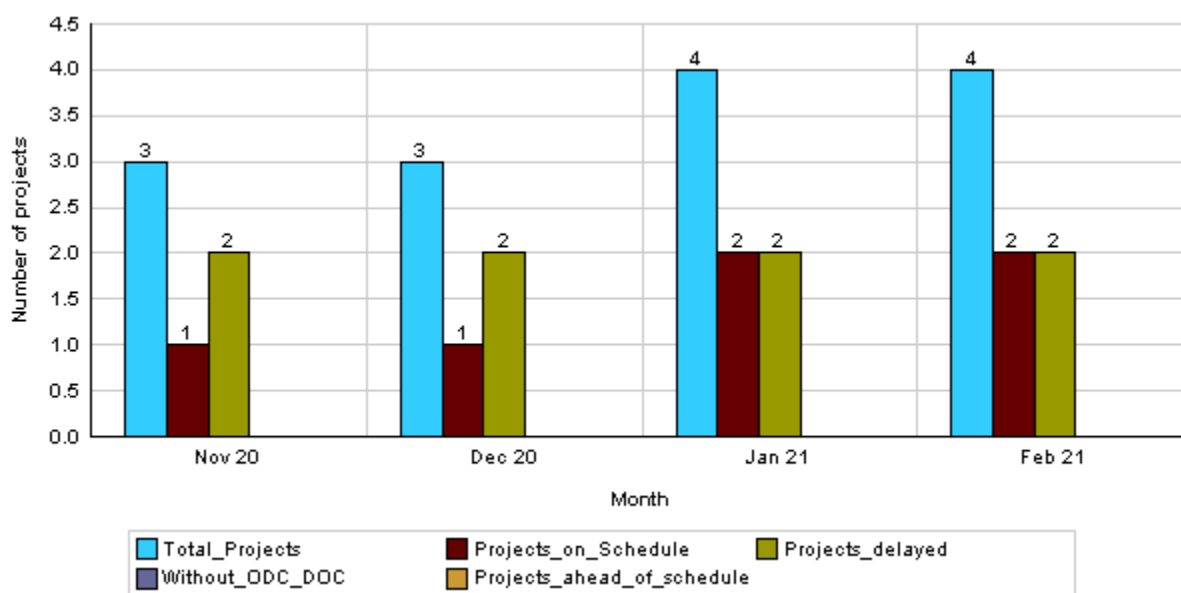


Break-up of 2 Delayed projects in February 2021




Delay in Months

Delay in Months	Projects
1-12	2
13-24	0
25-60	2
MORE THAN 60	0

Graphical Presentation of HUMAN RESOURCE DEVELOPMENT Sector

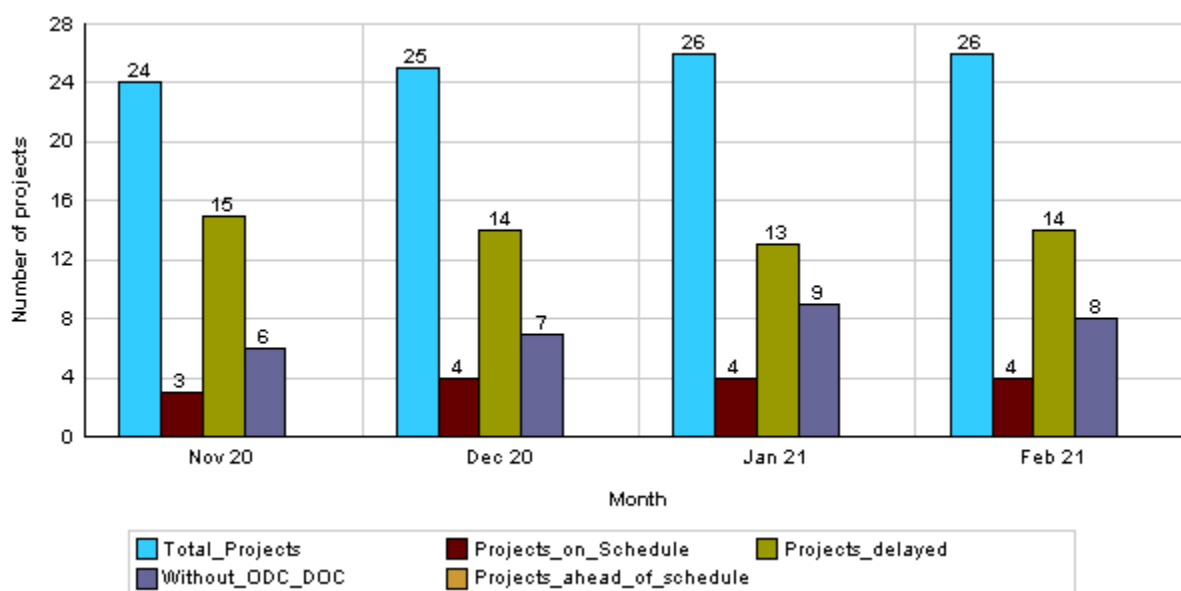


Break-up of 14 Delayed projects in February 2021

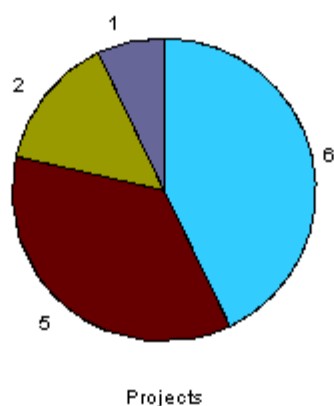


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
-----------------	------	-------	-------	--------------

Graphical Presentation of WATER RESOURCES Sector

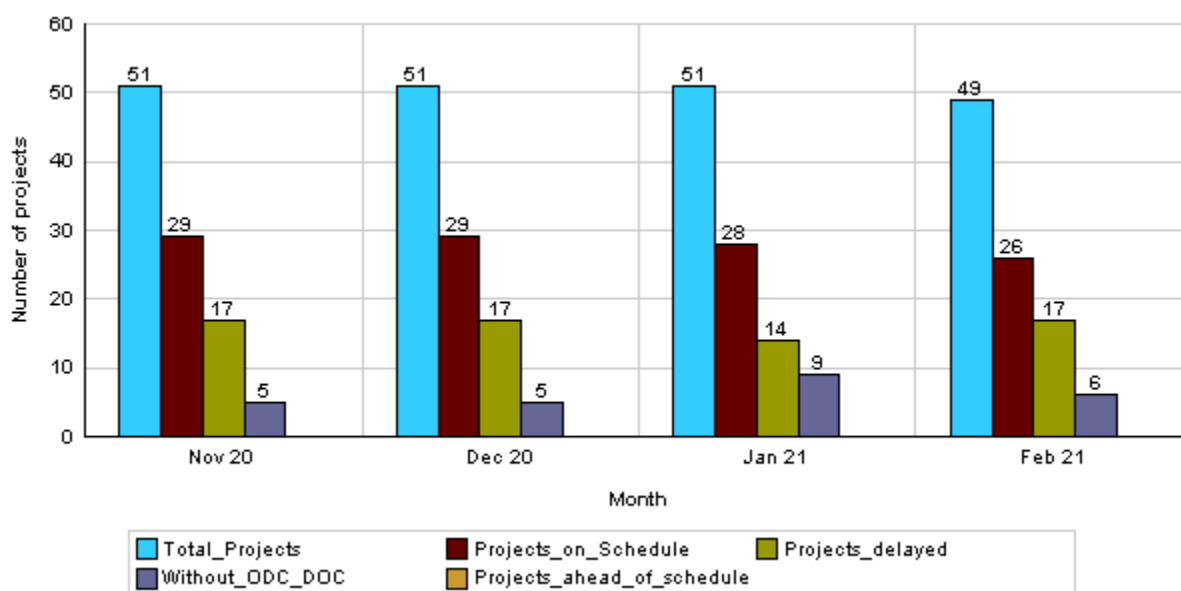


Break-up of 17 Delayed projects in February 2021

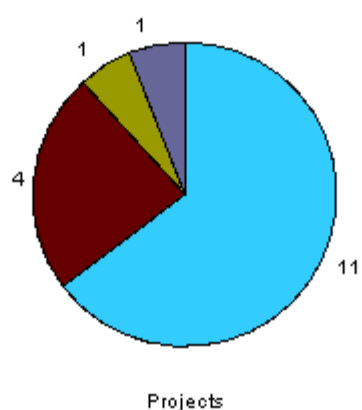


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

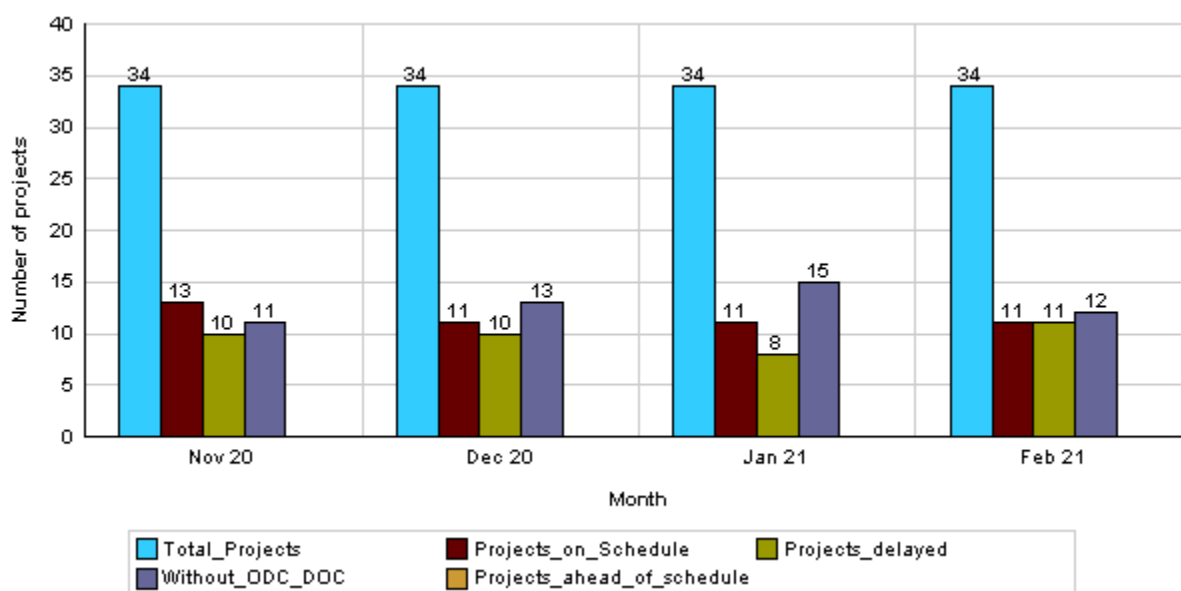


Break-up of 11 Delayed projects in February 2021

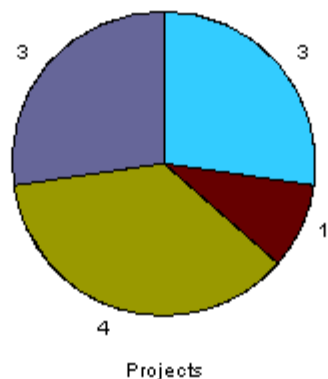


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of TELECOMMUNICATIONS Sector

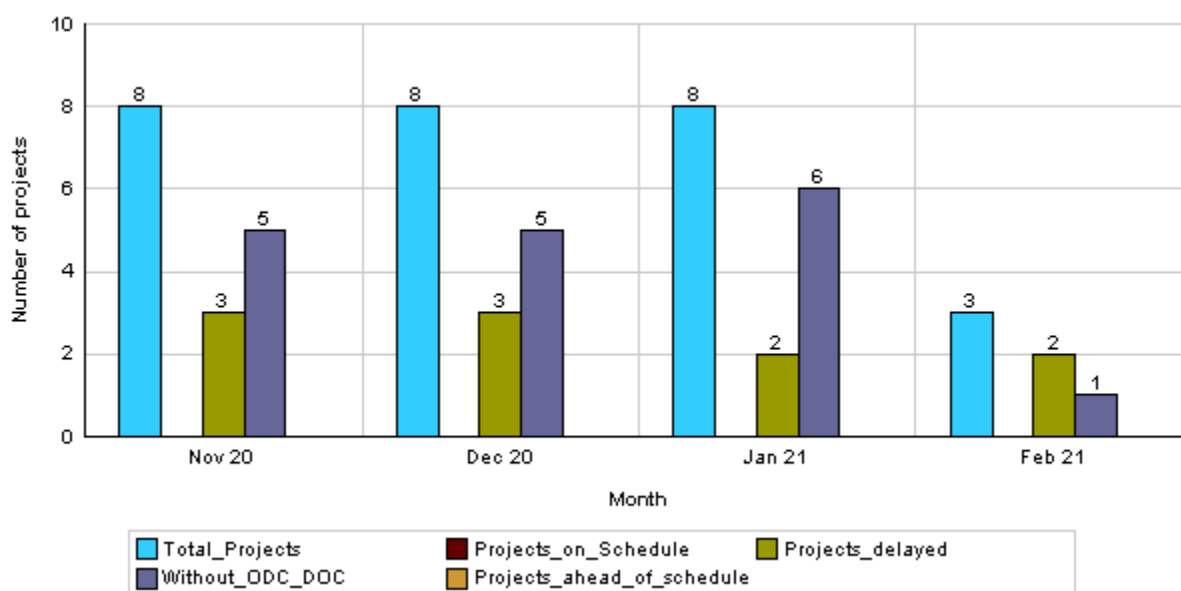


Break-up of 2 Delayed projects in February 2021

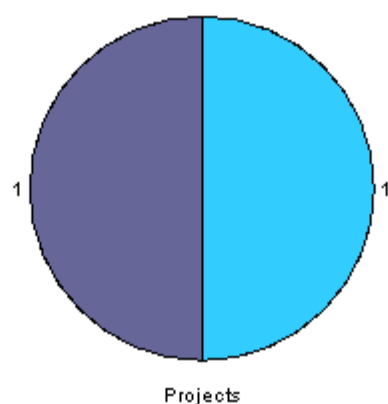


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

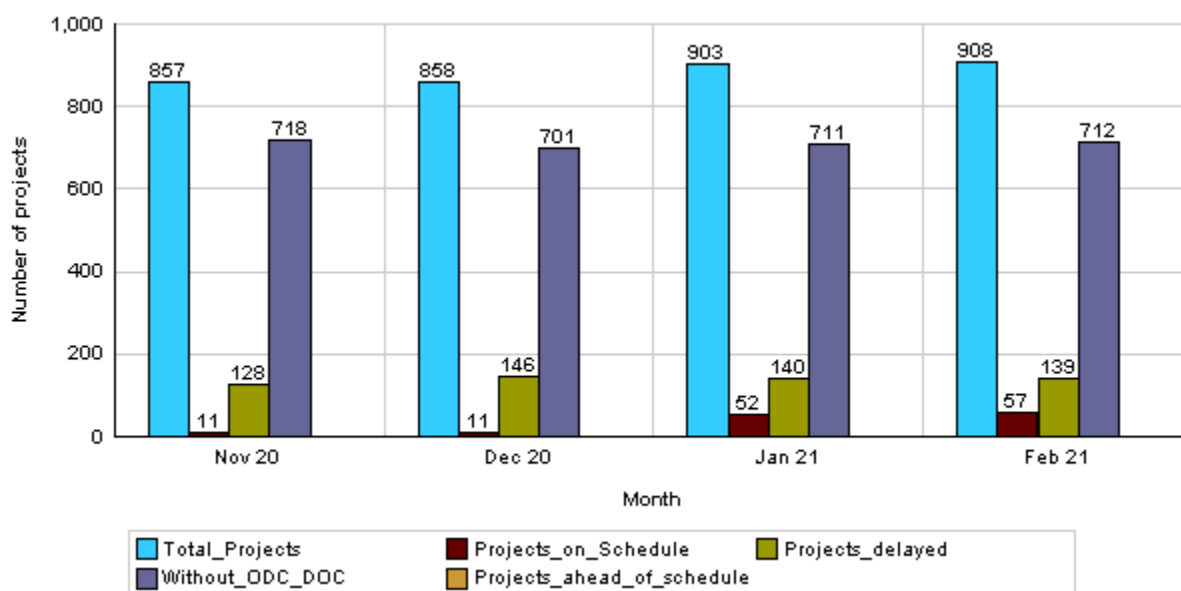


Break-up of 139 Delayed projects in February 2021

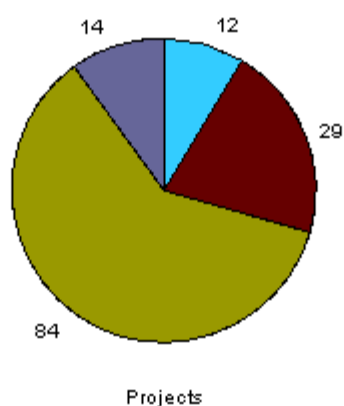


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

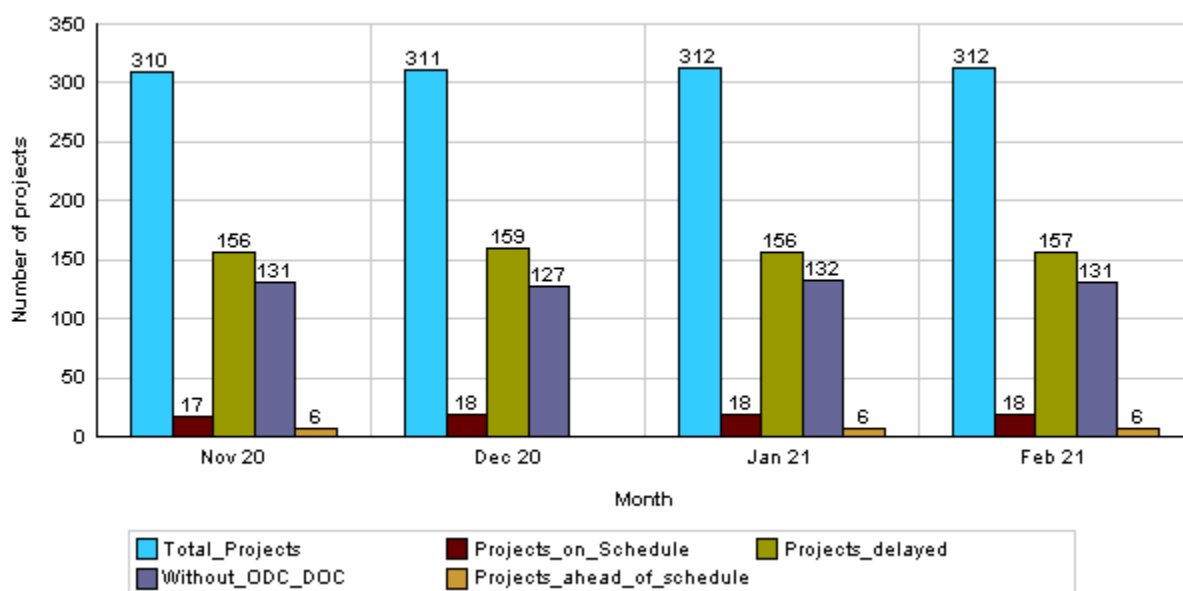


Break-up of 157 Delayed projects in February 2021

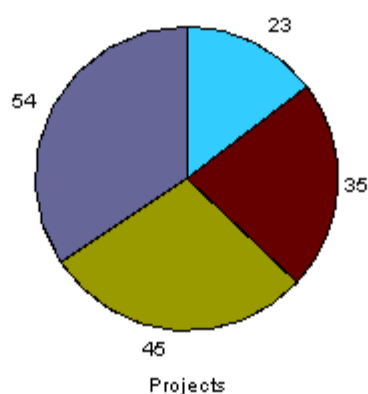


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

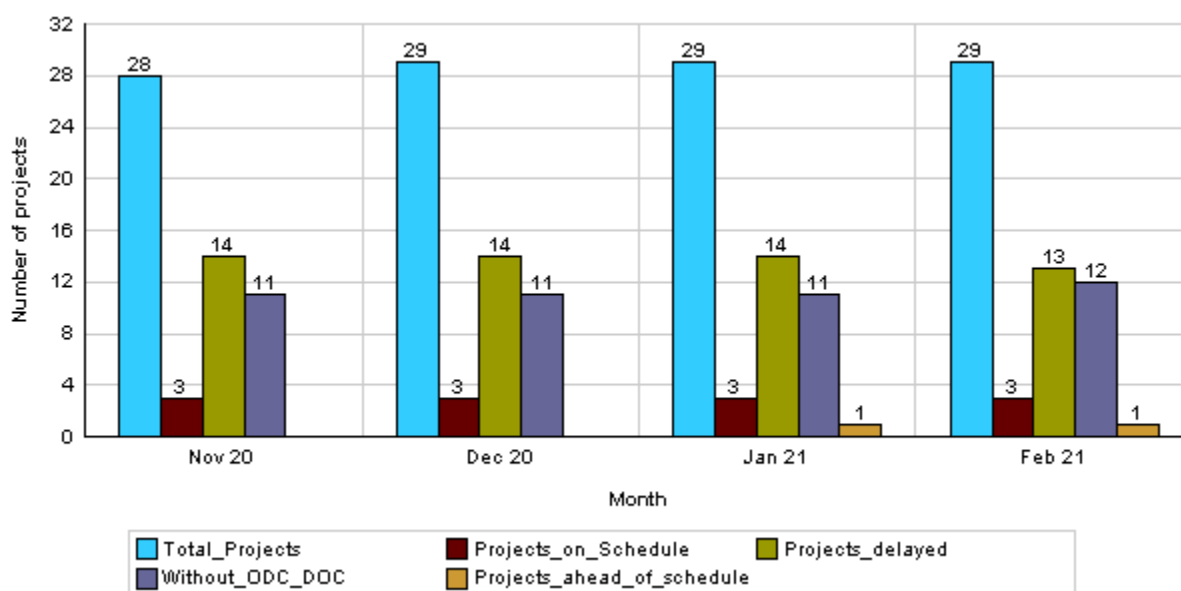


Break-up of 13 Delayed projects in February 2021

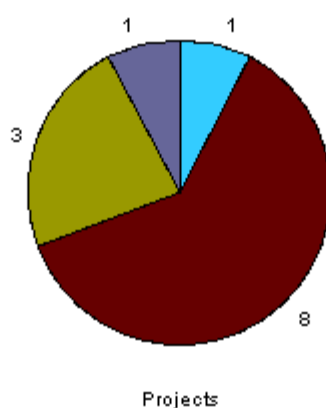


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

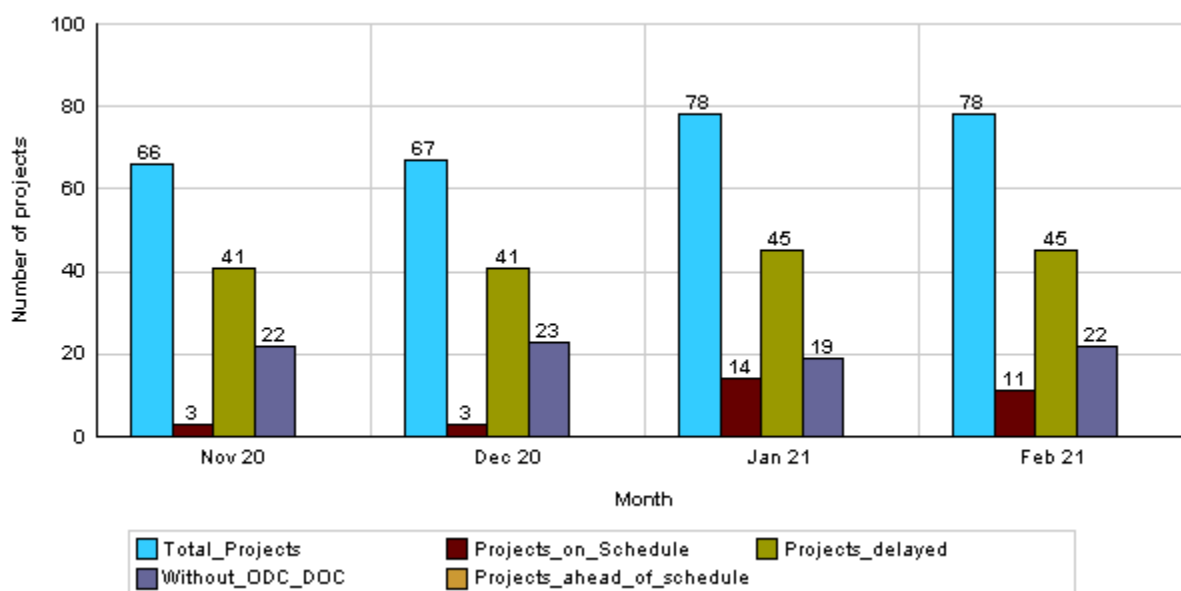


Break-up of 45 Delayed projects in February 2021

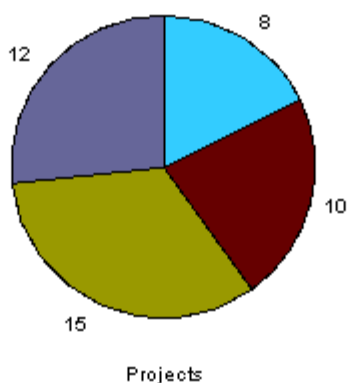


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of PETROLEUM Sector

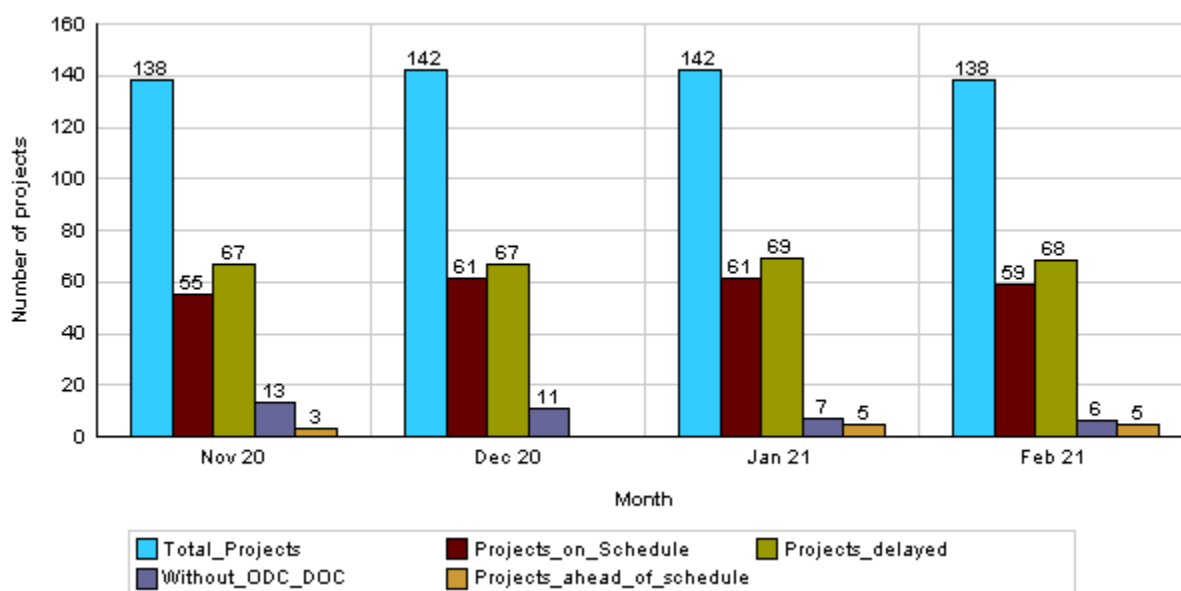


Break-up of 68 Delayed projects in February 2021

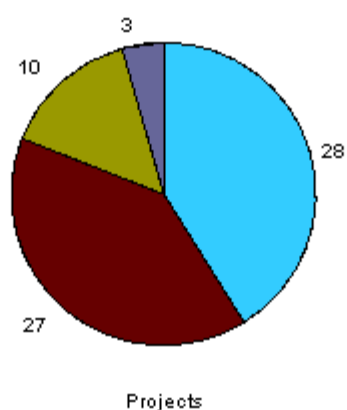


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of STEEL Sector

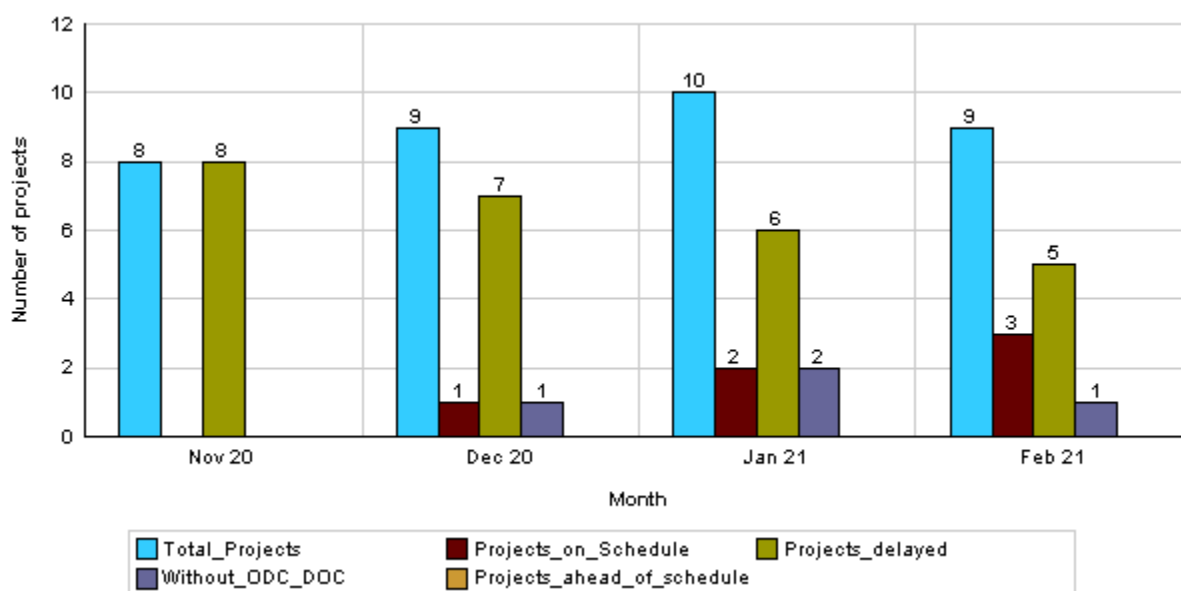


Break-up of 5 Delayed projects in February 2021

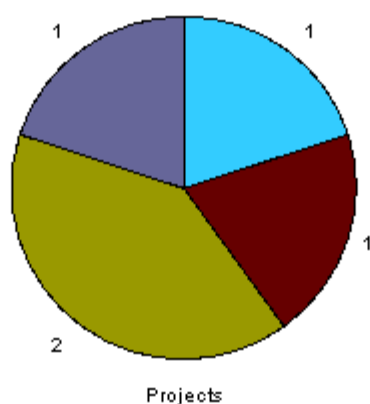


Delay in Months

Delay in Months	Count
1-12	1
13-24	1
25-60	2
MORE THAN 60	1

Graphical Presentation of MINES Sector

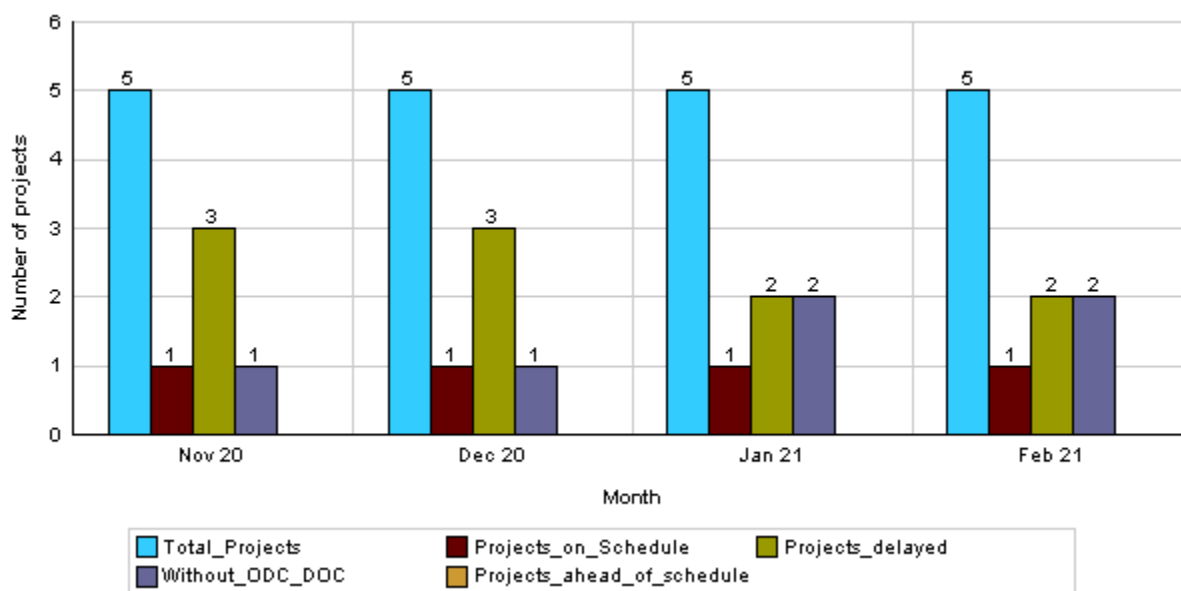


Break-up of 2 Delayed projects in February 2021

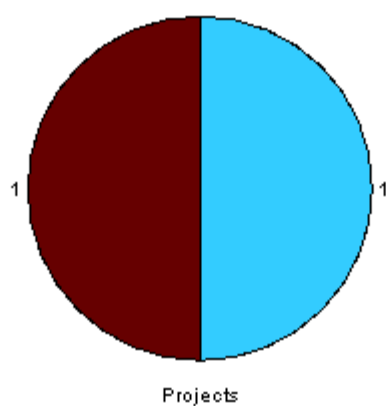


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	1	1	0	0

Graphical Presentation of FERTILISERS Sector

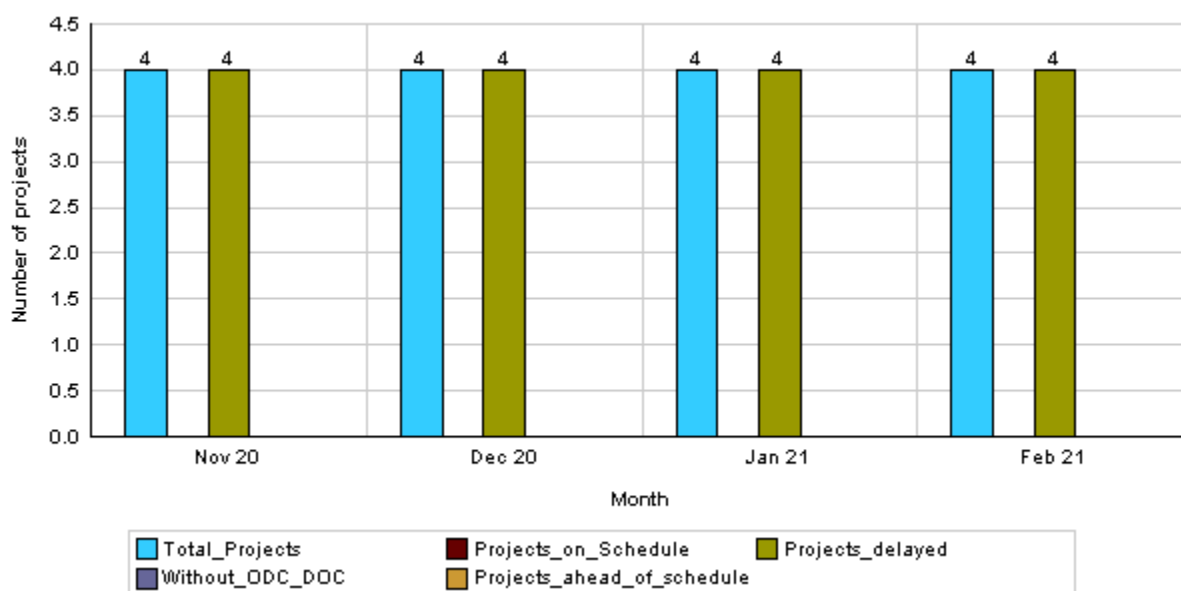


Break-up of 4 Delayed projects in February 2021

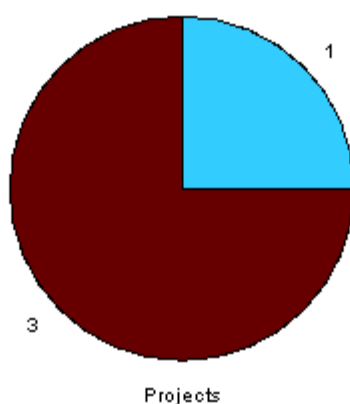


Delay in Months

Graphical Presentation of COAL Sector

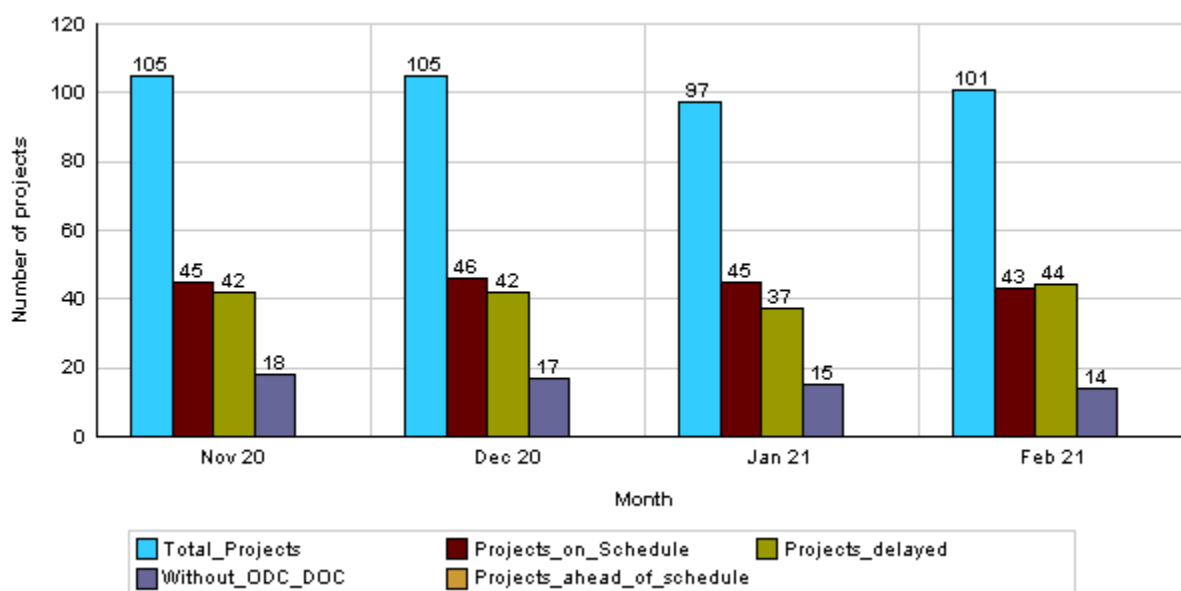


Break-up of 44 Delayed projects in February 2021

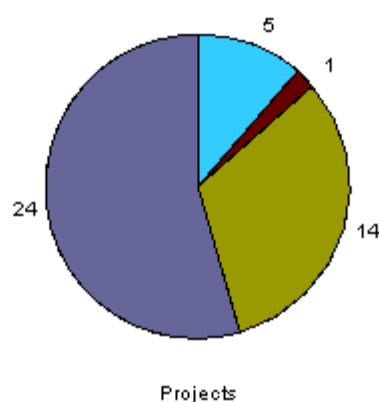


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of ATOMIC ENERGY Sector

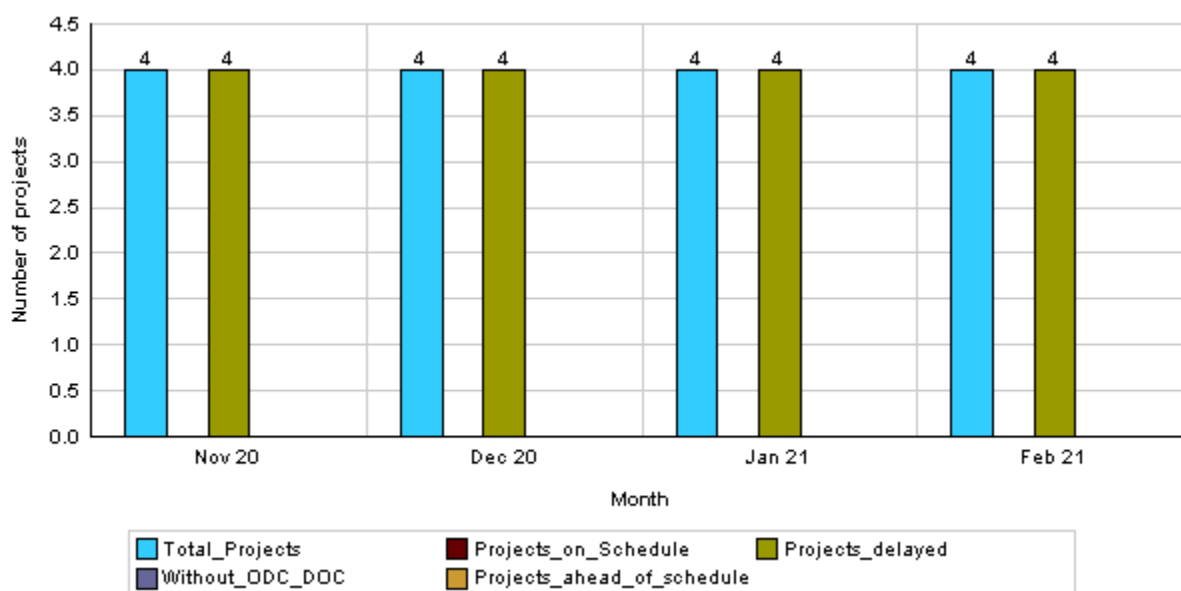

Break-up of 4 Delayed projects in February 2021

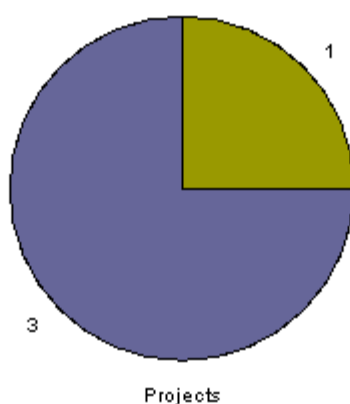

Delay in Months

Delay in Months	Count
1-12 (Blue)	0
13-24 (Dark Red)	0
25-60 (Olive Green)	1
MORE THAN 60 (Purple)	3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	16,297.00	12/2015 -	02/2022	74(O) -	58/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	17,079.00	12,992.00	12/2016 -	03/2023	75(O) -	44/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,840.00	5,915.80	09/2010 09/2016	10/2022	145(O) 0	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	23,131.00	11/2020 -	11/2023	36(O) -	28/76
	Total		67,120.00 -	80,348.00	58,335.80				213/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	33(O) -	0/0
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10 -	177.10	.00	02/2020 -	06/2021	16(O) -	0/0
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80 -	611.80	.00	03/2023 -	03/2023	0(O) -	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	12(O) -	0/0
9	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022	0(O) -	0/0
10	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13(O) -	0/0
11	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00 -	1,405.00	.00	08/2022 -	03/2023	7(O) -	0/0
12	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	346.27 -	480.33	51.11	09/2021 -	09/2021	0(O) -	0/0
13	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24 -	412.24	.00	06/2021 -	06/2021	0(O) -	0/0
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39 -	475.39	88.11	04/2021 -	04/2021	0(O) -	0/0
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5(O) -	0/0
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	.00	03/2022 -	03/2023	12(O) -	0/0
18	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	.00	05/2022 -	05/2022	0(O) -	0/0
19	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	438.28 -	438.28	335.58	06/2019 -	-	-	0/0
20	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12(O) -	0/0
21	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10(O) -	0/0
22	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	105.12	03/2020 -	06/2021	15(O) -	0/0
23	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	389.71 -	389.71	37.38	11/2021 -	10/2022	11(O) -	0/0
	Total		13,786.34 -	14,034.50	2,597.30				0/0
	<u>COAL</u>								
24	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	4,219.60	03/2023 03/2016	03/2023	0(O) 0	15/21
25	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,587.18	03/2023 -	03/2023	0(O) -	13/22
26	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	8.28	03/2023 -	03/2023	0(O) -	1/12
27	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	187.31	03/2015 03/2020	03/2022	84(O) 0	6/11
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	4.43	03/2014 -	03/2022	96(O) -	2/9
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	211.32	03/2014 -	03/2021	84(O) -	2/6
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	142.84	03/2022 -	03/2022	0(O) -	2/11
31	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60(O) -	1/7
32	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	124.35	03/2020 -	03/2023	36(O) -	3/6
33	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	9.71	03/2023 -	03/2023	0(O) -	1/12
34	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	2/6
35	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.95	03/2026 -	03/2026	0(O) -	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	24.44	03/2026 -	03/2026	0(O) -	0/2
37	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	2/2
38	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH ,	08/2020	2,309.80 -	2,309.80	.00	03/2029 -	03/2029	0(O) -	0/0
39	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH ,	05/2020	278.64 -	278.64	.00	03/2024 -	03/2024	0(O) -	0/0
40	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH ,	12/2020	2,310.12 -	2,310.12	.00	03/2029 -	03/2029	0(O) -	0/0
41	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH ,	12/2020	5,241.40 -	5,241.40	.00	03/2029 -	03/2029	0(O) -	0/0
42	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND ,	08/2008	6,964.33 7,254.37	706.40	639.01	07/2012 03/2025	03/2025	152(O) 0	6/6
43	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	106.63	03/2011 -	03/2022	132(O) -	6/6
44	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	401.87	03/2016 -	03/2022	72(O) -	6/6
45	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	96.86	03/2014 -	03/2022	96(O) -	6/6
46	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	20.22	04/2014 -	04/2023	108(O) -	4/7
47	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	457.98	04/2015 -	03/2022	83(O) -	2/6
48	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND ,	02/2012	4,983.58 5,136.15	4,983.58	244.12	03/2020 03/2024	03/2024	48(O) 0	7/7
49	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.54	03/2021 -	03/2021	0(O) -	0/2
50	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	280.46	05/2014 -	06/2021	85(O) -	0/8
51	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	207.34	04/2014 -	04/2020	-	0/10
52	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	163.16	03/2022 -	03/2022	0(O) -	4/22
53	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	97.54	03/2024 -	03/2024	0(O) -	0/17
54	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	238.83	03/2023 -	03/2023	0(O) -	1/1
55	TETARIAKHAR EXPANSION OCP - [N06000186]CCL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023	0(O) -	0/0
56	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	32.27	08/2022 -	09/2023	13(O) -	5/11
57	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 334.27	334.27	18.35	04/2018 -	12/2021	44(O) -	0/0
58	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/10
59	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	100.40	03/2021 -	03/2021	0(O) -	3/10
60	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	60.14	03/2021 -	03/2024	36(O) -	5/9
61	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.85	03/2022 -	03/2022	0(O) -	1/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	120.77	03/2021 -	03/2022	12(O) -	3/6
63	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	281.25 -	409.87	20.99	03/2022 -	03/2022	0(O) -	0/0
64	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	558.53	03/2021 -	03/2022	12(O) -	3/9
65	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	144.51	03/2022 -	03/2023	12(O) -	3/9
66	SEMARIA OPENCASST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
67	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
68	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.87	03/2026 -	03/2026	0(O) -	0/7
69	BLOCK-B EXPANSION OPENCASST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	1/7
70	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/8
71	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA ,	11/2014	1,184.33 -	1,184.33	368.56	03/2020 -	03/2027	84(O) -	5/8
72	BHANEAGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	409.68	85.82	03/2023 -	03/2023	0(O) -	7/11
73	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	160.23	03/2019 -	-	-	10/13
74	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	135.36	03/2020 -	03/2020	-	7/10
75	AMALGAMATED PAUNI-II OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	251.34	03/2021 -	03/2021	0(O) -	3/6
76	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	281.92	03/2025 -	03/2025	0(O) -	7/13
77	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	12(O) -	3/10
78	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA ,	11/2015	313.34 -	313.34	141.08	03/2021 -	03/2024	36(O) -	5/6
79	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA ,	11/2015	851.60 -	851.60	194.28	03/2020 -	03/2026	72(O) -	2/6
80	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	246.55	03/2019 -	-	-	4/9
81	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	142.28	03/2019 -	-	-	5/8
82	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	330.34	03/2020 -	03/2020	-	0/0
83	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	211.41	03/2021 -	03/2021	0(O) -	0/4
84	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	99.77	03/2021 -	03/2021	0(O) -	0/3
85	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	226.81	03/2022 -	03/2022	0(O) -	0/3
86	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	36(O) -	2/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	274.95	03/2021 -	03/2021	0(O) -	3/6
88	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
89	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168(O) -	11/12
90	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028	180(O) 0	8/10
91	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL,ODISHA ,	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029	228(O) 0	3/5
92	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	168.13	03/2012 -	03/2021	108(O) -	5/7
93	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108(O) -	6/9
94	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60(O) -	3/9
95	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026	0(O) -	7/15
96	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36(O) -	8/10
97	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027	0(O) -	3/12
98	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029	0(O) -	0/9
99	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	843.87	07/2020 -	04/2020	-	18/22
100	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
101	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
102	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	158.25	09/2020 -	-	-	0/0
103	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	173.83	09/2020 -	-	-	0/0
104	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,980.79	7,980.79	7,404.29	12/2015 -	02/2021	62(O) -	35/35
105	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	483.91	06/2015 03/2025	-	-	5/7
106	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132(O) -	1/2
107	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	129.58	03/2015 -	03/2022	84(O) -	3/5
108	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	292.49	03/2015 -	03/2022	84(O) -	12/29
109	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	21.17	03/2015 -	03/2022	84(O) -	10/13
110	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	124.04	07/2016 -	03/2022	68(O) -	26/28
111	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	193.33	03/2016 -	03/2021	60(O) -	38/39

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	106.68	03/2019 -	03/2022	36(O) -	17/18
113	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	169.95	03/2019 -	03/2022	36(O) -	6/11
114	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	-	03/2022	-	2/6
115	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	11,135.69	11/2021 07/2022	07/2022	8(O) 8	11/48
116	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	1,210.12 -	1,210.12	20.92	03/2022 03/2029	03/2029	84(O) 84	9/13
117	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	641.54	03/2018 -	03/2021	36(O) -	12/16
118	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	591.17	08/2019 -	-	-	0/19
119	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	1.39	03/2026 -	03/2026	0(O) -	4/22
120	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	10.11	03/2029 -	03/2029	0(O) -	1/22
121	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.50	03/2027 -	03/2027	0(O) -	1/27
122	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.03	03/2027 -	03/2027	0(O) -	0/22
123	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	.00	03/2025 -	03/2025	0(O) -	0/0
124	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 341.22	341.22	30.15	03/2017 -	10/2021	55(O) -	0/0
	Total		1,45,653.01 -	1,44,237.84	45,301.73				447/977
	<u>FINANCE</u>								
125	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	208.96	205.40	10/2019 -	04/2021	18(O) -	1/6
126	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	113.99	11/2021 -	11/2021	0(O) -	2/8
	Total		557.77 -	557.73	319.39				3/14
	<u>FERTILISERS</u>								
127	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	166.34	11/2019 -	03/2021	16(O) -	0/2
128	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	315.95	04/2020 03/2021	04/2021	12(O) 1	11/14
129	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	174.61	11/2019 -	02/2021	15(O) -	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	185.55	11/2019 -	03/2021	16(O) -	0/2
	Total		1,101.28 -	1,101.28	842.45				12/20
	<u>MINES</u>								
131	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	5,540.00	698.73	04/2021 12/2022	12/2022	20(O) 0	4/4
132	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	332.12	01/2020 -	-	-	2/3
133	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	93.85	11/2020 -	02/2021	3(O) -	2/3
134	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.74	04/2021 04/2021	04/2021	0(O) 0	2/2
135	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 06/2021	12/2020	-	1/1
	Total		7,078.62 -	7,075.17	1,260.44				11/13
	<u>STEEL</u>								
136	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,558.00	1,808.75	12/2017 12/2020	12/2020	-	5/6
137	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 21,940.00	21,940.00	17,691.25	05/2015 07/2021	07/2021	74(O) 0	70/86
138	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH ,	11/2020	542.24 -	542.24	17.50	12/2023 -	12/2023	0(O) -	0/0
139	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH , Central Sector Projects	11/2015	2,907.00 -	2,907.00	185.08	06/2023 -	06/2023	0(O) -	0/0
140	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	513.54	10/2017 12/2021	12/2021	50(O) 0	0/2
141	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	172.15	06/2019 05/2021	05/2021	23(O) 0	1/1
142	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	.63	05/2023 -	05/2023	0(O) -	0/0
143	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,552.60	09/2018 03/2021	03/2021	30(O) 1	5/5
144	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	177.74	09/2020 03/2021	05/2021	8(O) 0	1/4
	Total		25,452.51 -	31,567.51	22,119.24				82/104
	<u>PETROLEUM</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
145	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	13,352.70	07/2020 07/2022	07/2022	24(O) 0	92/111
146	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	25,090.00	10,477.71	06/2020 06/2022	06/2022	24(O) 10	15/20
147	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	267.12	04/2021 03/2021	03/2021	-1(O) 0	0/0
148	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	232.67	04/2021 -	07/2021	3(O) -	0/0
149	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	92.80	04/2022 -	02/2023	10(O) -	0/0
150	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	65.53	10/2021 -	10/2021	0(O) -	0/0
151	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	151.16	02/2021 -	03/2021	1(O) -	0/16
152	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	84.63	07/2020 -	07/2021	12(O) -	1/5
153	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	8.49	07/2022 -	07/2022	0(O) -	0/0
154	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH , EPC	10/2020	332.61 -	332.61	.00	11/2022 -	11/2022	0(O) -	0/0
155	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH , EPC	10/2020	303.40 -	303.40	.00	03/2021 -	03/2021	0(O) -	0/0
156	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH , EPC	10/2020	210.94 -	210.94	.00	08/2021 -	08/2021	0(O) -	0/0
157	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	502.00	403.62	08/2019 06/2021	06/2021	22(O) 0	6/13
158	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 303.75	303.75	180.83	05/2020 05/2021	05/2021	12(O) 0	4/5
159	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 638.60	652.10	136.05	02/2020 -	04/2021	14(O) -	1/14
160	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	471.42	02/2020 06/2021	06/2021	16(O) 0	5/5
161	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	222.21	144.80	08/2020 -	04/2021	8(O) -	0/0
162	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM ,	01/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024	0(O) -	0/0
163	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024	0(O) -	0/0
164	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	115.92	03/2021 09/2021	09/2021	6(O) 0	18/26
165	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	29.92	10/2020 02/2022	02/2022	16(O) 0	2/2
166	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	132.60	10/2022 -	10/2022	0(O) -	10/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
167	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	126.15	01/2021 06/2021	06/2021	5(O) 0	6/8
168	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	301.57	03/2021 12/2021	12/2021	9(O) 0	0/0
169	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR ,	06/2017	951.64 -	951.64	708.43	10/2019 11/2020	-	-	11/11
170	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	722.25	04/2023 -	04/2023	0(O) -	1/2
171	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR ,	06/2020	403.00 -	403.00	1.76	08/2022 -	08/2022	0(O) -	0/0
172	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	187.00	04/2018 -	04/2021	36(O) -	19/20
173	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	970.30	773.52	03/2026 -	03/2026	0(O) -	7/10
174	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	259.40	02/2020 10/2021	10/2021	20(O) 0	7/8
175	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 730.20	730.20	65.94	- 05/2023	05/2023	- 0	11/17
176	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	225.54	39.50	02/2021 -	12/2021	10(O) -	5/8
177	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	54.61	12/2021 -	12/2021	0(O) -	8/11
178	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	84.15	05/2023 -	05/2023	0(O) -	3/11
179	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	21.66	12/2022 -	09/2022	-3(O) -	0/0
180	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT ,	02/2020	444.87 -	444.87	79.65	08/2022 -	08/2022	0(O) -	0/0
181	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT , Central Sector Projects	09/2020	18,936.00 -	18,936.00	.00	09/2024 -	09/2024	0(O) -	0/0
182	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 300.00	300.00	253.92	11/2020 06/2021	06/2021	7(O) 0	42/46
183	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	75.17	02/2020 08/2021	08/2021	18(O) 0	5/7
184	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	587.98	08/2020 -	04/2022	20(O) -	6/7
185	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	222.31	01/2021 03/2022	03/2022	14(O) 0	2/6
186	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	240.52	02/2020 02/2022	02/2022	24(O) 0	4/5
187	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.01	327.01	166.90	08/2020 05/2021	05/2021	9(O) 0	13/16

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
188	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	25.82	06/2021 07/2022	07/2022	13(O) 0	1/3
189	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 -	2,281.94	429.94	12/2022 -	12/2022	0(O) -	0/0
190	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	151.68	10/2021 -	10/2021	0(O) -	0/0
191	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	13.16	07/2021 -	07/2021	0(O) -	0/0
192	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	91.57	09/2026 -	09/2026	0(O) -	0/0
193	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	634.60	03/2023 03/2022	03/2022	-12(O) 0	6/10
194	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	67.53	06/2020 09/2021	09/2021	15(O) 0	3/12
195	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	94.56	10/2022 -	10/2022	0(O) -	19/19
196	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	73.00	06/2022 -	06/2022	0(O) -	0/0
197	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	76.84	10/2022 -	10/2022	0(O) -	9/9
198	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,556.82	12/2019 04/2021	10/2021	22(O) 0	9/10
199	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 637.00	637.00	443.62	03/2020 11/2020	06/2021	15(O) 0	2/3
200	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	96.63	03/2021 -	03/2021	0(O) -	0/15
201	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	763.33	06/2022 -	06/2022	0(O) -	12/18
202	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	131.02	12/2022 -	12/2022	0(O) -	9/19
203	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	185.40	11/2021 -	11/2021	0(O) -	10/19
204	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 -	200.00	1.46	06/2023 -	06/2023	0(O) -	0/2
205	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 714.25	714.25	385.53	10/2017 03/2022	03/2022	53(O) 0	40/52
206	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 -	5,245.96	4,852.63	08/2018 11/2019	03/2021	31(O) 1	0/20
207	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 -	3,288.96	2,726.00	02/2020 03/2021	03/2021	13(O) 1	0/20
208	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	711.00	06/2019 -	02/2022	32(O) -	0/0
209	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	302.82	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
210	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 293.00	293.00	162.96	06/2020 09/2021	09/2021	15(O) 0	0/0
211	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,846.46	1,846.46	1,546.02	05/2013 12/2020	03/2021	94(O) 0	5/8
212	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,685.92	04/2018 05/2021	05/2021	37(O) 0	13/15
213	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,468.42	02/2022 -	02/2022	0(O) -	5/5
214	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	365.05	12/2019 03/2021	03/2021	15(O) 1	0/17
215	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	138.76	01/2021 -	04/2021	3(O) -	0/0
216	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	132.88	01/2021 -	10/2021	9(O) -	0/0
217	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	147.12	01/2021 -	04/2021	3(O) -	0/0
218	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	4,338.40	03/2020 -	-	-	118/135
219	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,475.92	3,596.00	3,494.45	05/2021 05/2021	05/2021	0(O) 0	14/15
220	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	241.79	08/2020 -	03/2021	7(O) -	0/15
221	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	121.72	06/2020 12/2021	09/2021	15(O) 0	2/12
222	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,203.71	1,565.69	05/2021 -	05/2021	0(O) -	4/6
223	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	974.84	03/2022 05/2023	05/2023	14(O) 0	4/6
224	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	2,305.03	05/2021 -	05/2021	0(O) -	4/6
225	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	06/2019	2,494.68 -	2,354.72	1,238.26	03/2022 -	03/2022	0(O) -	4/6
226	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	733.86	619.17	12/2020 05/2021	05/2021	5(O) 0	4/5
227	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA ,	07/2020	640.00 -	640.00	297.39	12/2021 -	12/2021	0(O) -	0/0
228	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021	48(O) 0	2/15

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
229	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	3,027.90	1,755.66	03/2021 -	08/2021	5(O) -	5/5
230	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	3,338.00	2,750.24	12/2020 -	06/2021	6(O) -	5/5
231	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	508.53	07/2018 02/2021	05/2021	34(O) 3	27/36
232	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	187.00	10/2020 -	03/2021	5(O) -	6/12
233	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	457.91	12/2019 -	04/2021	16(O) -	6/22
234	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,556.70	12/2020 -	05/2021	5(O) -	21/24
235	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	2,018.90	12/2020 12/2021	06/2021	6(O) 0	20/24
236	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 3,048.00	3,048.00	1,718.70	12/2020 12/2021	12/2021	12(O) 0	19/24
237	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,483.60	12/2012 02/2022	02/2022	110(O) 0	26/42
238	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 3,072.00	3,072.00	1,825.04	06/2021 08/2022	08/2022	14(O) 0	18/26
239	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 3,060.00	3,060.00	2,096.40	12/2021 -	12/2021	0(O) -	16/20
240	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	103.91	11/2022 -	11/2022	0(O) -	8/20
241	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	205.30	07/2022 -	07/2022	0(O) -	8/14
242	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	32.60	11/2022 -	11/2022	0(O) -	7/12
243	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	837.00	05/2023 -	05/2023	0(O) -	5/29
244	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,231.50	12/2020 12/2021	12/2021	12(O) 0	18/24
245	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	46.92	12/2019 03/2022	03/2022	27(O) 0	18/26
246	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	98.03	07/2022 -	07/2022	0(O) -	10/10
247	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	196.27	12/2021 -	06/2021	-6(O) -	3/3
248	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	74.18	07/2022 -	07/2022	0(O) -	9/9
249	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	2,561.15	10/2021 -	10/2021	0(O) -	6/10
250	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	589.44	10/2021 -	12/2021	2(O) -	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
251	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	6.63	09/2021 -	09/2021	0(O) -	1/5
252	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	1,568.98	08/2021 -	08/2021	0(O) -	7/11
253	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	1.93	09/2022 -	09/2022	0(O) -	0/8
254	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	08/2019	1,607.00 -	1,607.00	189.36	08/2022 -	08/2022	0(O) -	0/21
255	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	1.73	07/2022 -	07/2022	0(O) -	0/0
256	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	77.55	01/2024 -	01/2024	0(O) -	0/0
257	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL,PUNJAB ,	05/2020	1,421.46 -	1,244.50	54.49	02/2023 -	02/2023	0(O) -	5/22
258	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	80.21	- 05/2022	05/2022	- 0	16/26
259	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
260	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 1,472.00	1,472.00	17.80	02/2017 08/2022	08/2022	66(O) 0	0/0
261	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	624.35	446.46	03/2019 05/2021	05/2021	26(O) 0	4/5
262	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	6,025.00	3,409.77	12/2018 -	02/2022	38(O) -	5/5
263	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	125.61	11/2021 -	11/2021	0(O) -	5/5
264	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,528.75	12/2019 -	01/2021	-	0/0
265	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13(O) -	0/0
266	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	185.01	10/2020 -	08/2021	10(O) -	0/0
267	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL,TAMIL NADU ,	10/2020	921.00 -	921.00	3.05	09/2023 -	09/2023	0(O) -	0/0
268	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU , EPC	10/2020	1,398.00 -	1,398.00	75.59	12/2023 -	12/2023	0(O) -	0/0
269	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	65.87	04/2022 -	08/2023	16(O) -	0/0
270	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 345.15	345.15	196.18	04/2022 -	04/2022	0(O) -	43/43

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
271	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	136.81	08/2021 -	11/2021	3(O) -	0/0
272	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	17.21	08/2020 11/2021	11/2021	15(O) 0	1/1
273	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	398.94	08/2022 -	08/2022	0(O) -	3/3
274	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	688.49	12/2021 -	12/2021	0(O) -	0/21
275	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	153.20	03/2029 -	03/2029	0(O) -	0/0
276	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 -	217.92	76.80	04/2021 -	04/2021	0(O) -	12/14
277	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	85.89	02/2020 06/2021	06/2021	16(O) 0	19/26
278	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	778.20	12/2020 12/2021	12/2021	12(O) 0	13/24
279	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	88.03	04/2020 10/2021	10/2021	18(O) 0	18/26
280	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	1,793.18	09/2022 -	03/2022	-6(O) -	3/3
281	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	14.63	03/2031 -	03/2031	0(O) -	0/0
282	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	55.17	01/2023 -	01/2023	0(O) -	0/0
	Total		2,95,617.09 -	3,02,198.67	1,04,628.98				1020/1584
	POWER								
283	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	13,233.01	09/2010 08/2023	08/2023	155(O) 0	0/0
284	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	8,154.49	12/2009 02/2021	02/2021	134(O) -	30/30
285	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	18,308.58	10/2011 04/2022	04/2022	126(O) 0	32/48
286	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 10,566.00	10,566.00	8,680.05	07/2012 06/2020	04/2021	105(O) 0	13/25
287	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	15,463.61	05/2018 06/2021	07/2021	38(O) 0	40/45
288	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	1,479.16	01/2024 -	01/2024	0(O) -	16/27
289	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	-	41/41

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
290	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	2,369.23	11/2019 -	-	-	0/0
291	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	519.78	05/2017 07/2020	06/2021	49(O) 0	4/9
292	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	201.69	11/2019 -	05/2021	18(O) -	0/0
293	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	122.40	09/2018 06/2020	09/2020	-	0/0
294	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	119.53	06/2019 06/2020	09/2020	-	0/0
295	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT , EPC	08/2020	261.80 -	261.80	.00	10/2021 -	10/2021	0(O) -	0/0
296	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	8,825.13	09/2009 03/2022	03/2022	150(O) 0	3/5
297	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	286.90	01/2026 -	01/2026	0(O) -	0/0
298	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,664.74	04/2020 -	07/2025	63(O) -	0/0
299	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,389.42	11,612.82	06/2019 10/2022	10/2022	40(O) 0	29/30
300	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,380.97	10/2017 -	-	-	0/0
301	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	17,112.00	4,060.28	03/2023 -	09/2024	18(O) -	3/7
302	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	456.53	02/2019 05/2020	03/2021	25(O) 1	0/0
303	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA , EPC	09/2019	403.62 -	403.62	.00	06/2021 -	06/2021	0(O) -	0/0
304	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 15,105.22	15,105.22	13,657.43	01/2018 10/2020	02/2021	37(O) 0	43/43
305	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	-	41/41
306	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	464.00	09/2020 -	08/2022	23(O) -	10/16
307	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
308	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
309	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,630.84	10/2012 06/2020	03/2021	101(O) 0	8/11
310	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,869.26	08/2013 03/2022	03/2022	103(O) 0	23/26
311	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	590.30	06/2014 -	-	-	10/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
312	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,320.63	04/2016 04/2020	07/2020	-	12/12
313	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	241.55	04/2016 12/2017	06/2021	62(O) 3	0/0
314	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	477.66	11/2016 06/2020	05/2021	54(O) 2	10/12
315	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	3,269.93	03/2018 -	-	-	9/12
316	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 902.49	902.49	644.11	10/2017 12/2020	01/2021	-	5/5
317	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	200.16	07/2017 -	-	-	3/5
318	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	89.36	03/2018 -	06/2021	39(O) -	0/0
319	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	639.30	01/2018 04/2021	03/2021	38(O) 0	0/0
320	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	-	-	0/0
321	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	11,441.18	11/2019 04/2021	03/2021	16(O) 0	0/0
322	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	196.10	11/2019 -	-	-	0/0
323	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 516.12	516.12	415.85	01/2019 04/2020	04/2020	-	0/0
324	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	425.04	04/2019 -	-	-	0/0
325	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	200.36	02/2019 06/2021	06/2021	28(O) 0	0/0
326	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	148.03	06/2019 09/2020	04/2021	22(O) 1	0/0
327	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	224.72	12/2019 06/2020	06/2021	18(O) 1	0/0
328	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	4,041.83	04/2020 -	03/2021	11(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
329	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,129.32	2,002.54	12/2018 -	12/2021	36(O) -	0/0
330	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 6,700.00	6,700.00	2,541.14	12/2018 -	12/2021	36(O) -	0/0
331	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,508.04	04/2019 -	-	-	0/0
332	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,994.00	2,825.43	07/2020 -	04/2021	9(O) -	0/0
333	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,644.55	02/2020 09/2020	03/2021	13(O) 0	0/0
334	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	140.77	09/2019 04/2020	05/2020	-	0/0
335	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	239.65	05/2020 -	03/2021	10(O) -	0/0
336	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 13,140.91	13,140.91	11,641.13	12/2018 02/2021	04/2021	28(O) 0	39/42
337	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	1,746.41	12/2018 -	03/2021	27(O) -	0/0
338	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN , EPC	01/2020	1,522.71 -	1,522.71	.00	09/2021 -	09/2021	0(O) -	0/0
339	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN , EPC	03/2020	1,782.00 -	1,782.00	.00	09/2021 -	09/2021	0(O) -	0/0
340	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN , EPC	12/2019	702.28 -	702.28	.00	03/2021 -	03/2021	0(O) -	0/0
341	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN , EPC	03/2020	1,749.31 -	1,749.31	.00	09/2021 -	09/2021	0(O) -	0/0
342	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 219.66	219.66	157.07	07/2019 04/2021	04/2021	21(O) 1	0/0
343	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU , EPC	03/2020	1,316.22 -	1,316.22	.00	09/2021 -	09/2021	0(O) -	0/0
344	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	8,125.04	11/2020 03/2022	03/2022	16(O) 0	25/29
345	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA , EPC	06/2019	401.90 -	401.90	.00	04/2021 -	04/2021	0(O) -	0/0
346	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	10,016.10	7,966.63	07/2019 03/2021	03/2021	20(O) 0	38/42
347	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	11,130.00	02/2017 06/2020	01/2021	-	40/40
348	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	1,432.11	09/2023 -	08/2024	11(O) -	1/11
349	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	463.48	09/2020 01/2021	01/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
350	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	226.00	11/2020 04/2021	04/2021	5(O) 0	0/0
351	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH , EPC	03/2020	501.29 -	501.29	49.76	09/2021 01/2022	01/2022	4(O) 4	0/0
352	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH , EPC	01/2020	798.24 -	798.24	31.64	09/2021 01/2022	01/2022	4(O) 4	0/0
353	NOKHRA - [N18000282]NTPC,UTTAR PRADESH , EPC	03/2020	1,722.14 -	1,722.14	103.85	09/2021 01/2022	01/2022	4(O) 4	0/0
354	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,841.21	03/2013 12/2021	12/2022	117(O) 0	8/15
355	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	3,860.35	2,161.90	06/2013 -	12/2023	126(O) -	11/17
356	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	-	0/15
357	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	524.12	12/2021 -	12/2021	0(O) -	11/32
358	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.54	649.64	09/2019 11/2022	12/2024	63(O) 0	6/10
359	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	343.03	04/2018 03/2021	03/2021	35(O) 1	0/0
360	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 -	529.68	410.98	11/2018 -	05/2021	30(O) -	0/0
	Total		2,95,137.42 -	3,66,945.59	2,51,832.37				605/756
	<u>HEAVY INDUSTRY</u>								
361	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	900.00	815.00	09/2019 12/2020	-	-	0/0
	Total		1,554.00 -	900.00	815.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
362	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	24(O) -	0/0
363	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	358.42	- -	06/2021	- -	0/0
364	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0
365	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	296.84	05/2021 -	07/2022	14(O) -	0/0
366	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	499.23	481.52	11/2013 -	03/2021	88(O) -	0/0
367	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	229.39	05/2017 -	03/2021	46(O) -	2/2
368	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	3/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
369	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.64	128.08	- -	03/2021	- -	0/0
370	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	228.87	- -	12/2020	- -	0/0
371	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	2/2
372	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	648.37	09/2021 -	09/2021	0(O) -	2/4
373	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0
374	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	124.80	09/2023 -	09/2023	0(O) -	0/0
375	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
376	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	.00	09/2025 -	05/2024	-16(O) -	0/0
377	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	36.14	03/2020 -	12/2021	21(O) -	2/7
378	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	252.34	03/2019 -	01/2021	-	0/0
379	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	460.56	- -	06/2021	- -	0/0
380	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	234.12	05/2018 -	12/2021	43(O) -	0/0
381	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19(O) -	0/33
382	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	161.29	02/2018 -	04/2021	38(O) -	1/1
383	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	449.74	06/2020 -	07/2021	13(O) -	0/0
384	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	123.92	03/2020 -	05/2021	14(O) -	1/5
385	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	239.89	- -	03/2021	- -	0/0
386	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	524.06	04/2020 -	07/2021	15(O) -	0/0
387	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
388	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
389	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	280.39	03/2019 -	03/2021	24(O) -	0/0
390	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL ,	04/2018	651.99 -	651.99	455.70	- -	06/2021	- -	0/0
	Total		15,273.26 -	15,594.81	7,459.26				16/62
	<u>RAILWAYS</u>								
391	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
392	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	850.07	03/2009 -	03/2024	180(O) -	0/0
393	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
394	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	- -	-	-	1/1
395	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,643.25	1,214.20	03/2021 -	03/2024	36(O) -	0/1
396	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24(O) -	0/0
397	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
398	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	1,165.50	03/2022 -	03/2024	24(O) -	0/0
399	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023	0(O) -	0/0
400	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	604.03	03/2022 03/2024	03/2024	24(O) 0	0/0
401	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	36(O) -	0/0
402	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019 -	-	-	0/0
403	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,105.00	787.79	03/2019 -	03/2023	48(O) -	0/0
404	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 486.96	800.00	795.88	03/2019 -	03/2021	24(O) -	0/0
405	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,950.00	1,478.05	03/2022 -	03/2023	12(O) -	0/0
406	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	1,873.21	1,133.64	03/2021 -	05/2021	2(O) -	0/0
407	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]JECR,BIHAR ,	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	128(O) -	0/0
408	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]JECR,BIHAR ,	04/1997	162.87 -	614.45	340.21	- -	12/2023	- -	0/0
409	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]JECR,BIHAR ,	04/2003	528.65 -	2,066.78	1,529.08	- -	03/2023	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
410	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	436.36	03/2020 -	-	-	0/0
411	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
412	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	751.55	687.20	03/2012 -	07/2021	112(O) -	0/0
413	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N220000087]NFR,BIHAR ,	09/2006	532.87 2,132.03	2,145.00	968.95	03/2019 -	03/2024	60(O) -	0/0
414	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	- -	03/2022	- -	0/0
415	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	-	-	0/0
416	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.31	- -	-	-	0/0
417	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	- -	-	-	0/0
418	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	- -	0/0
419	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 -	735.20	379.57	- -	03/2021	- -	0/0
420	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	385.87	- -	03/2023	- -	0/0
421	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
422	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.74	- -	-	-	0/0
423	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	- -	-	-	0/0
424	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	- -	03/2024	- -	0/0
425	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	24.31	- -	03/2023	- -	0/0
426	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	- -	-	-	0/0
427	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	- -	-	-	0/0
428	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,470.50	1,123.21	- -	03/2023	- -	0/0
429	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	36(O) -	0/0
430	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	480.00	477.72	- -	-	-	0/1
431	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	519.33	266.24	- -	03/2025	- -	0/0
432	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	862.71	03/2020 -	03/2023	36(O) -	0/1
433	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	471.48	03/2020 -	03/2023	36(O) -	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
434	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	546.71	541.83	07/2014 -	-	-	0/0
435	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	309.44	03/2021 -	03/2024	36(O) -	0/0
436	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	15(O) -	0/0
437	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	726.31	543.57	-	-	-	0/0
438	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	1,483.14	1,194.00	-	03/2022	-	0/0
439	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	902.85	03/2020 03/2023	03/2023	36(O) 0	1/1
440	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,282.18	03/2020 -	12/2021	21(O) -	0/0
441	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
442	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,226.51	1,131.91	12/2019 -	10/2020	-	0/0
443	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33(O) -	0/1
444	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21(O) -	0/1
445	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42(O) -	0/1
446	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15(O) -	1/2
447	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	359.00	111.51	-	03/2024	-	0/0
448	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	127.91	-	09/2023	-	0/0
449	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,959.74	1,959.74	1,784.02	03/2020 12/2023	12/2023	45(O) 0	0/0
450	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 411.62	411.62	126.05	03/2012 03/2023	03/2023	132(O) 0	0/0
451	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	-	0/0
452	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,500.00	1,438.76	12/2021 -	12/2021	0(O) -	0/0
453	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	0(O) -	0/0
454	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	179.19	- 03/2024	03/2024	- 0	0/0
455	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48(O) 0	0/0
456	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,868.89	1,795.61	12/2021 -	03/2022	3(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
457	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,389.05	1,389.05	1,103.31	03/2021 12/2021	12/2021	9(O) -3	0/0
458	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	642.89	03/2021 12/2022	12/2022	21(O) 0	0/0
459	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
460	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
461	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
462	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
463	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 890.76	890.76	745.11	03/2019 10/2021	10/2021	31(O) 0	0/0
464	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 1,017.91	1,017.91	650.65	03/2020 02/2021	02/2021	11(O) 2	0/0
465	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	658.97	12/2011 -	06/2021	114(O) -	0/0
466	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	316.04	03/2019 -	03/2021	24(O) -	0/0
467	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	6,753.42	875.99	12/2026 -	12/2025	-12(O) -	0/0
468	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	22,879.22	11/2002 -	12/2022	241(O) -	0/0
469	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]JECR,JHARKHAND ,	03/1999	1,033.07 -	3,550.00	3,528.48	- -	03/2022	- -	0/0
470	KODERMA-TILAIYA (NL) ECR - [220100305]JECR,JHARKHAND ,	04/2002	459.91 -	1,625.87	767.07	- -	03/2023	- -	0/0
471	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	297.17	12/2018 12/2018	06/2021	30(O) 0	0/0
472	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	195.52	12/2016 -	08/2020	-	0/0
473	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,993.24	704.10	03/2021 03/2021	12/2023	33(O) 0	0/0
474	GARHWA ROAD-RAMNA - [N22000465]JECR,JHARKHAND ,	03/2015	348.23 -	348.23	316.23	03/2021 -	03/2022	12(O) -	0/0
475	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	- -	0/0
476	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
477	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,967.00	74.87	- -	12/2023	- -	0/0
478	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	307.78	03/2016 -	12/2023	93(O) -	1/1
479	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	558.00	.00	- -	12/2023	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
480	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
481	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	-	12/2023	-	0/0
482	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,000.00	2,181.62	03/2023 -	12/2022	-3(O) -	0/1
483	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	-	12/2023	-	0/0
484	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	277.39	12/2018 06/2025	06/2025	78(O) 6	0/0
485	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	327.25	.00	-	12/2023	-	0/0
486	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	35.01	03/2016 -	12/2023	93(O) -	0/0
487	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,656.00	1,119.96	03/2020 11/2021	11/2021	20(O) 0	1/5
488	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	783.00	613.57	03/2020 03/2021	03/2021	12(O) 2	1/2
489	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	998.00	463.35	03/2017 -	-	-	0/0
490	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	262.68	-	-	-	0/0
491	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	369.55	8.50	-	-	-	0/0
492	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	275.21	6.73	-	-	-	0/0
493	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	198.81	-	-	-	0/0
494	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,246.00	.81	-	-	-	0/0
495	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
496	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	24(O) -	0/15
497	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,413.76	1,416.77	-	08/2020	-	0/0
498	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 5,912.40	5,912.40	2,143.20	03/2022 03/2024	03/2024	24(O) 0	0/0
499	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,762.94	1,084.58	03/2020 -	03/2023	36(O) -	1/1
500	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	1,546.20	12/2020 -	12/2021	12(O) -	0/0
501	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12(O) -	0/10
502	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	254.64	03/2022 -	03/2023	12(O) -	1/1
503	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	172.08	03/2019 -	-	-	0/0
504	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34(O) -	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
505	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24(O) -	0/0
506	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	249.28	06/2020 03/2023	03/2023	33(O) 0	0/0
507	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216(O) -	0/0
508	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24(O) -	0/0
509	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84(O) -	0/0
510	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
511	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023	0(O) -	0/0
512	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24(O) -	0/0
513	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	315.00	312.62	03/2019 03/2020	03/2020	-	0/0
514	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24(O) -	0/0
515	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
516	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
517	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
518	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12(O) -	0/0
519	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12(O) -	0/0
520	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,204.21	03/2024 -	03/2023	-12(O) -	0/0
521	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023	0(O) -	0/0
522	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24(O) -	0/0
523	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12(O) -	0/0
524	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,725.00	2,531.51	03/2020 -	12/2021	21(O) -	0/0
525	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
526	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 2,753.05	3,524.81	982.38	03/2023 12/2023	12/2023	9(O) 0	0/1
527	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	269.73	03/2019 12/2020	12/2020	-	0/0
528	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
529	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
530	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36(O) -	0/1
531	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	12,264.15	10,777.52	03/2011 -	12/2023	153(O) -	0/0
532	NEW BG LINE FROM BYRNIAH TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	4,083.02	263.68	03/2021 -	03/2021	0(O) -	0/0
533	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 5,021.45	5,521.45	3,816.20	03/2014 -	03/2023	108(O) -	0/0
534	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12(O) -	0/1
535	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140(O) -	0/0
536	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,421.35	1,847.08	03/2000 -	03/2023	276(O) -	0/0
537	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202(O) -	0/9
538	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	4,541.38	3,645.92	12/2008 -	04/2021	148(O) -	0/0
539	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	133(O) -	0/0
540	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
541	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	112.02	12/2021 -	12/2021	0(O) -	0/0
542	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	37(O) -	0/0
543	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	897.00	03/2022 03/2023	03/2023	12(O) 0	0/0
544	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	866.05	03/2022 03/2025	03/2025	36(O) 0	0/0
545	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	186.12	- -	-	-	0/1
546	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33(O) -	0/3
547	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
548	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
549	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.55	- -	-	-	0/0
550	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 2,042.51	2,042.51	69.92	03/2019 -	03/2024	60(O) -	0/0
551	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	1,205.00	2.28	- 03/2024	03/2024	- 0	0/0
552	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	439.49	- -	12/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
553	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	73.97	03/2020 -	-	-	0/0
554	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	287.09	- -	12/2021	-	0/0
555	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	1,040.00	154.52	03/2020 -	-	-	0/0
556	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
557	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	105(O) -	0/0
558	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228(O) -	0/0
559	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	-	0/0
560	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	11.32	- -	03/2025	-	0/0
561	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	355.79	03/2022 -	03/2025	36(O) -	0/0
562	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	502.48	422.81	- -	03/2021	-	0/0
563	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	565.00	538.28	- -	05/2019	-	0/0
564	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	640.17	03/2016 -	03/2025	108(O) -	0/0
565	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	103.78	03/2017 -	03/2025	96(O) -	0/0
566	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
567	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	185.36	03/2016 -	03/2025	108(O) -	0/0
568	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	439.30	374.08	03/2017 -	03/2025	96(O) -	0/0
569	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28(O) -	0/0
570	BARIARPUUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.11	- -	03/2025	-	0/0
571	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
572	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	663.13	516.55	03/2020 -	03/2021	12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
573	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	495.10	283.97	- -	03/2022	- -	0/0
574	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
575	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
576	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
577	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
578	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	163.26	02/2012 -	03/2025	157(O) -	0/0
579	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	106.31	03/2014 -	03/2025	132(O) -	0/0
580	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
581	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,952.68	543.07	03/2023 -	03/2024	12(O) -	0/0
582	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 791.39	791.39	572.99	- -	03/2023	- -	0/0
583	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	296.10	.01	- -	12/2023	- -	0/0
584	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,432.50	1,111.69	- -	03/2025	- -	2/2
585	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 -	927.94	521.91	03/2020 03/2022	06/2021	15(O) 0	1/1
586	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	3,037.95	350.55	03/2014 -	03/2027	156(O) -	1/1
587	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	356.54	- -	03/2024	- -	0/0
588	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	701.81	172.41	03/2020 -	04/2022	25(O) -	0/0
589	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,147.00	881.92	03/2020 06/2021	06/2021	15(O) 0	0/0
590	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,870.41	1,528.14	03/2019 -	03/2021	24(O) -	0/0
591	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	929.86	738.84	03/2019 -	05/2021	26(O) -	0/38
592	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
593	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,370.71	03/2021 -	03/2024	36(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
594	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
595	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	11,158.98	12/2023 -	12/2023	0(O) -	0/0
596	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	-	0/0
597	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 1,540.13	1,540.13	242.12	03/2023 03/2025	03/2025	24(O) 0	0/0
598	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 781.00	859.00	852.73	03/2016 -	06/2021	63(O) -	0/0
599	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	6,911.00	1,125.27	03/2015 -	12/2024	117(O) -	0/0
600	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
601	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,413.99	03/2009 03/2026	03/2026	204(O) 0	0/0
602	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	-	0/0
603	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88(O) -	0/0
604	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	-	1/1
605	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	845.24	06/2021 03/2025	03/2025	45(O) 0	0/0
606	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
607	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 1,539.28	1,539.28	1,109.06	02/2019 12/2021	12/2021	34(O) 0	0/0
608	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	208.46	10/2020 03/2024	03/2024	41(O) 0	0/0
609	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 238.03	238.03	219.74	03/2020 03/2021	03/2022	24(O) 0	0/0
610	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	603.73	03/2022 03/2023	03/2023	12(O) 0	0/0
611	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	380.90	03/2022 03/2026	03/2026	48(O) 0	0/0
612	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 810.02	810.02	171.45	11/2018 03/2024	03/2024	64(O) 0	0/0
613	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	596.91	12/2018 03/2024	03/2024	63(O) 0	0/0
614	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	857.47	03/2020 03/2020	12/2021	21(O) 0	0/0
615	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	1,225.51	12/2024 -	12/2026	24(O) -	0/0
616	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	21(O) -	0/0
617	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
618	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]JRCON,ODISHA ,	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48(O) -	0/0
619	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
620	MANSA-BHATINDA (PHASE-I) INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB ,	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108(O) -	0/0
621	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	860.41	691.34	02/2019 -	11/2021	33(O) -	0/0
622	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	395.00	324.37	12/2019 -	02/2021	14(O) -	0/0
623	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	350.45	251.41	10/2018 -	-	-	0/0
624	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.00	.00	- -	-	-	0/1
625	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
626	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	420.18	307.78	03/2020 -	06/2021	15(O) -	0/0
627	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	375.00	337.30	11/2019 -	03/2021	16(O) -	0/0
628	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	525.00	459.43	02/2019 -	02/2020	-	0/0
629	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.60	- -	-	-	0/0
630	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	464.53	03/2018 -	-	-	0/0
631	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	167.74	08/2022 -	06/2022	-2(O) -	0/0
632	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 4,084.69	8,600.00	619.18	12/2015 12/2023	12/2023	96(O) 0	0/0
633	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	60(O) -	0/0
634	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102(O) -	1/4
635	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	73(O) -	0/0
636	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	227.40	63.90	- -	-	-	0/0
637	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	582.83	239.11	- -	12/2025	-	0/0
638	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	527.37	3.34	02/2019 -	-	-	0/0
639	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	- -	-	-	0/0
640	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	559.95	319.22	- -	03/2024	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
641	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
642	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	600.30	355.13	- 10/2021	09/2021	- 0	0/0
643	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	1,121.00	906.57	- 02/2021	04/2021	- 2	0/0
644	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	332.00	265.41	04/2014 03/2021	12/2020	-	0/0
645	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198(O) -	0/0
646	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	238.00	153.70	03/2018 -	-	-	0/0
647	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
648	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3(O) -	0/0
649	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27(O) -	0/0
650	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	478.70	03/2010 -	03/2024	168(O) -	1/1
651	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	799.01	03/2016 -	12/2021	69(O) -	0/0
652	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
653	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	535.71	03/2021 -	03/2021	0(O) -	3/3
654	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	850.00	705.50	12/2024 -	12/2024	0(O) -	0/0
655	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9(O) -	0/0
656	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24(O) -	2/3
657	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
658	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
659	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
660	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
661	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
662	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
663	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	929.79	03/2022 -	03/2022	0(O) -	0/0
664	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	-	4/6
665	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33(O) -	0/0
666	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,400.00	1,302.29	03/2019 -	06/2022	39(O) -	0/0
667	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	833.10	03/2023 -	12/2024	21(O) -	0/0
668	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24(O) -	0/0
669	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,111.96	03/2020 -	03/2024	48(O) -	0/0
670	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	217.40	03/2019 -	03/2022	36(O) -	0/0
671	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	68(O) -	0/0
672	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
673	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
674	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
675	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	476.60	04/2017 -	03/2021	47(O) -	0/0
676	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
677	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	63.70	- -	12/2023	-	0/0
678	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	199.70	01/2022 -	03/2022	2(O) -	0/0
679	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	80.76	12/2019 -	04/2021	16(O) -	0/0
680	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023	0(O) -	0/0
681	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021	0(O) -	0/6
682	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023	0(O) -	0/0
683	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
684	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	204.53	- -	-	-	0/0
685	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	22,716.11	2,768.76	12/2024 -	03/2025	3(O) -	0/0
686	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	275.07	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
687	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
688	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
689	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER, WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	903.03	03/2019 12/2009	03/2025	72(O) 0	0/0
690	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	970.10	12/2010 -	03/2025	171(O) -	7/7
691	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
692	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0
693	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,676.61	03/2016 -	03/2025	108(O) -	0/0
694	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	1,072.08	03/2016 -	03/2025	108(O) -	0/0
695	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
696	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- -	03/2025	- -	0/0
697	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	38.20	- -	-	-	0/0
698	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
699	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	239.06	- -	03/2022	- -	0/0
700	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	760.00	801.53	12/2021 -	04/2021	-8(O) -	0/0
701	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
702	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL ,	02/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-	-	0/0
	Total		4,62,095.03 -	6,98,959.98	2,44,559.04				33/139
	HUMAN RESOURCE DEVELOPMENT								
703	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD, ANDHRA PRADESH ,	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6(O) -	3/7

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
704	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH ,	02/2019	655.34 -	655.34	49.89	06/2020 -	-	-	0/110
705	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH ,	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4(O) -	0/0
706	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52(O) -	2/6
707	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR ,	09/2018	375.00 375.00	375.00	48.46	09/2020 -	11/2022	26(O) -	0/0
708	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD,CHHATTISGARH ,	03/2020	808.62 -	808.62	57.42	07/2022 -	07/2022	0(O) -	0/0
709	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD,GOA ,	05/2019	303.90 -	303.90	16.50	03/2020 -	-	-	0/8
710	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	226.16	11/2014 -	-	-	2/8
711	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	35.88	06/2022 -	06/2022	0(O) -	0/0
712	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR ,	03/2019	329.00 -	329.00	.00	07/2022 -	07/2022	0(O) -	0/0
713	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR ,	01/2018	676.00 -	676.00	.00	04/2023 -	04/2023	0(O) -	0/0
714	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63(O) -	1/6
715	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6(O) -	0/0
716	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	-	-	1/8
717	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15(O) -	0/0
718	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11(O) -	4/14
719	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	-	-	0/0
720	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE ,	03/2018	150.00 -	150.00	.00	04/2018 -	-	-	0/0
721	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE ,	08/2018	418.00 -	418.00	110.00	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
722	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	790.79	149.00	03/2022 -	06/2022	3(O) -	0/5
723	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	350.69	265.91	04/2019 -	04/2021	24(O) -	7/8
724	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	387.83	180.63	05/2020 -	02/2022	21(O) -	2/5
725	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD,PUNJAB ,	10/2019	348.24 -	348.24	15.20	05/2022 -	08/2022	3(O) -	0/7
726	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	20(O) -	3/6
727	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15(O) -	0/0
728	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL , EPC	03/2020	193.83 -	193.83	.45	06/2020 -	-	-	0/0
	Total		11,077.40 -	11,265.83	2,413.56				25/198
	<u>HOME AFFAIRS</u>								
729	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	874.24	10/2019 -	12/2021	26(O) -	1/7
730	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE - [N28000147]CPWD,HARYANA , EPC	01/2020	166.98 167.00	166.98	.00	10/2023 -	10/2023	0(O) -	0/0
731	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS 96 - [N45000001]CPWD,HARYANA ,	01/2020	166.98 -	166.98	.29	05/2022 -	05/2022	0(O) -	0/0
732	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 238.00	238.00	170.35	04/2018 12/2021	12/2021	44(O) 0	5/6
	Total		1,716.05 -	2,571.96	1,044.88				6/13
	<u>RURAL DEVELOPMENT</u>								
733	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI ,	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021	0(O) -	0/2
734	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	155.66	144.95	12/2015 -	03/2021	63(O) -	0/1
735	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2021	51(O) -	2/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
736	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	175.49	124.87	12/2016 -	03/2021	51(O) -	0/4
	Total		889.43 -	899.87	472.48				2/12
	<u>CULTURE DEVELOPMENT</u>								
737	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	145.60	09/2017 -	03/2021	42(O) -	12/15
	Total		151.33 -	151.33	145.60				12/15
	<u>DPIIT</u>								
738	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI ,	11/2017	4,773.00 -	5,178.00	2,419.54	12/2019 -	10/2021	22(O) -	0/0
739	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE ,	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 01/2014	07/2021	22(O) 0	0/0
	Total		17,352.09 -	18,990.30	11,134.61				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
740	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	26.44	10/2018 -	-	-	0/4
741	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	47.28	12/2017 -	-	-	0/4
742	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	172.78	04/2017 -	-	-	3/4
743	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	39.86	10/2018 -	-	-	0/4
744	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	24.96	10/2018 -	-	-	1/4
745	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	-	-	0/0
746	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	-	-	0/0
747	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	164.81	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
748	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
749	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,275.58	05/2014 -	-	-	0/0
750	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
751	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
752	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	225.81	10/2015 03/2021	03/2021	65(O) 0	3/4
753	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
754	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
755	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	1,634.05	11/2018 -	-	-	0/0
756	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
757	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	951.13	03/2020 -	-	-	0/0
758	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	234.49	- -	-	-	0/0
759	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	- -	0/0
760	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
761	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	- -	0/0
762	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	2,499.00	1,539.65	03/2021 10/2021	04/2021	1(O) 0	2/4
763	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,337.98	- -	09/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
764	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	550.75	- -	02/2021	- -	0/0
765	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	86.83	- -	06/2021	- -	0/0
766	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	351.02	- -	-	-	0/0
767	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	355.89	315.57	12/2015 -	-	-	3/3
768	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	214.00	02/2017 06/2021	02/2019	-	3/4
769	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	315.42	01/2018 -	-	-	4/4
770	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	214.00	05/2017 07/2021	05/2019	-	2/4
771	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	214.00	08/2017 05/2021	08/2019	-	2/4
772	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	293.60	11/2017 04/2021	11/2019	-	3/4
773	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	105.72	08/2018 03/2021	03/2021	31(O) 0	2/4
774	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	136.22	08/2018 -	-	-	2/3
775	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	177.78	08/2018 06/2021	02/2021	30(O) 0	3/4
776	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	294.12	373.98	07/2018 -	-	-	4/4
777	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	427.08	11/2018 04/2021	01/2021	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
778	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	476.77	05/2016 08/2021	04/2021	59(O) 0	3/4
779	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	279.86	08/2018 05/2021	08/2020	-	3/4
780	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	323.06	01/2017 12/2020	12/2020	-	3/4
781	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	199.35	05/2016 -	12/2020	-	3/4
782	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021	59(O) 0	2/4
783	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	304.42	09/2016 -	09/2020	-	3/4
784	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	264.97	08/2017 -	08/2020	-	3/4
785	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021	44(O) 0	0/4
786	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	288.92	01/2018 -	12/2020	-	1/4
787	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/0
788	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH , EPC	09/2018	597.67 -	597.67	.00	01/2020 -	01/2020	-	0/0
789	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH , EPC	09/2018	617.41 -	617.41	.00	02/2019 -	02/2019	-	0/0
790	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2019	1,226.88 -	1,226.88	.00	02/2021 -	02/2021	0(O) -	0/0
791	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	1,601.10 -	1,601.10	.00	02/2021 -	02/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
792	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	.00	02/2012 -	-	-	0/0
793	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
794	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	389.45	349.94	05/2012 06/2018	-	-	0/0
795	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 197.16	197.16	91.25	10/2018 09/2015	09/2018	-	2/4
796	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	394.53	06/2018 -	-	-	2/3
797	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	178.10	- -	-	-	2/4
798	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	184.62	10/2016 -	-	-	3/4
799	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	172.89	- -	-	-	2/4
800	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	-	2/4
801	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60(O) -	1/4
802	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	139.47	04/2017 03/2018	03/2021	47(O) 0	1/4
803	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	252.79	97.07	04/2017 -	-	-	2/4
804	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	263.31	110.34	04/2017 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
805	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	104.37	04/2017 -	-	-	2/4
806	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	50.17	04/2017 -	02/2021	46(O) -	0/4
807	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	22.06	04/2017 -	02/2021	46(O) -	1/4
808	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	104.36	04/2017 -	-	-	2/4
809	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
810	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	115.89	- -	-	-	0/0
811	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	376.69	- -	-	-	0/0
812	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	260.57	- -	-	-	0/0
813	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	91.23	- -	-	-	0/0
814	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	71.60	- -	04/2022	-	0/4
815	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	61.55	- -	04/2022	-	0/4
816	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	140.98	- 01/2016	01/2019	-	0/4
817	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	133.95	- -	-	-	3/4
818	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
819	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,217.25	- 03/2020	-	-	0/0
820	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	160.09	- -	09/2020	-	0/0
821	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	301.06 -	301.06	.00	04/2022 -	04/2022	0(O) -	0/4
822	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH , EPC	09/2020	353.90 -	353.90	.00	05/2022 -	05/2022	0(O) -	0/4
823	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	403.68 -	403.68	25.52	02/2020 -	-	-	0/0
824	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	342.55 -	342.55	104.06	02/2020 -	-	-	0/0
825	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	421.48 -	421.48	104.06	11/2020 -	-	-	0/0
826	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	543.05 -	543.05	104.06	11/2020 -	-	-	0/0
827	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	486.70 -	486.70	15.49	10/2020 -	-	-	0/0
828	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	560.39 -	560.39	33.61	02/2020 -	-	-	0/0
829	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	347.78 -	347.78	33.58	09/2020 -	-	-	0/0
830	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	394.27 -	394.27	.00	10/2020 -	-	-	0/0
831	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	450.65 -	450.65	.00	11/2020 -	-	-	0/0
832	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	520.00	612.58	02/2009 -	-	-	0/0
833	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	340.14	325.28	04/2009 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
834	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	435.78	427.96	11/2008 -	-	-	0/0
835	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	255.23	251.39	11/2008 -	-	-	0/0
836	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	236.86	03/2008 -	08/2020	-	0/0
837	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	352.28	06/2008 -	09/2019	-	0/0
838	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	360.99	04/2008 -	12/2020	-	0/0
839	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019	-	0/0
840	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	655.17	655.17	07/2009 -	-	-	0/0
841	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	-	0/0
842	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	273.38	05/2018 -	12/2020	-	2/4
843	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	407.30	102.90	06/2018 -	12/2021	42(O) -	0/4
844	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	398.06	126.86	06/2018 -	12/2021	42(O) -	0/4
845	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	350.14	01/2019 -	-	-	2/4
846	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	117.35	11/2018 -	-	-	4/4
847	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	474.44	11/2018 -	-	-	3/4
848	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 390.73	390.73	267.46	05/2017 -	-	-	0/0
849	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	386.98	02/2011 -	-	-	0/0
850	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	111.16	06/2018 -	-	-	3/4
851	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	303.49	153.44	- -	-	-	2/4
852	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	64.28	12/2018 -	-	-	1/4
853	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	190.47	01/2016 -	04/2021	63(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
854	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	223.50	103.73	01/2016 -	-	-	0/4
855	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	399.65	01/2016 -	-	-	2/3
856	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	887.68	228.44	- -	-	-	1/4
857	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/2018	160.00 -	160.00	70.46	09/2021 -	09/2021	0(O) -	0/0
858	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	-	-	0/0
859	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	273.40	127.57	- -	-	-	0/0
860	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM ,	03/2020	166.94 -	166.94	.00	12/2020 -	-	-	0/0
861	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL,ASSAM , EPC	03/2020	220.20 -	220.20	.00	12/2022 -	12/2022	0(O) -	0/4
862	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM , EPC	08/2020	208.84 -	208.84	.00	04/2022 -	04/2022	0(O) -	0/4
863	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM , EPC	08/2020	278.46 -	278.46	.00	03/2022 -	03/2022	0(O) -	0/4
864	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]NHIDCL,ASSAM , EPC	03/2020	216.49 -	216.49	12.40	03/2022 -	03/2022	0(O) -	0/4
865	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,360.63	02/2013 -	-	-	3/4
866	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
867	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
868	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	555.63	07/2013 -	-	-	2/3
869	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 585.00	591.00	575.64	11/2013 12/2020	01/2021	-	0/0
870	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 -	675.00	253.10	- -	-	-	0/0
871	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	318.64	08/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
872	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	343.70	10/2016 -	-	-	0/0
873	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	-	-	-	0/0
874	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	301.48	04/2019 -	-	-	0/0
875	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	512.04	-	10/2021	-	2/4
876	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	-	0/0
877	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	400.60	-	-	-	1/4
878	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,182.94	186.70	-	-	-	0/0
879	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	297.27	271.39	04/2019 -	-	-	3/4
880	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR ,	01/1991	478.35 -	478.35	446.60	-	-	-	0/0
881	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	1,038.56	1,160.00	-	-	-	3/4
882	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	649.27	712.15	04/2018 -	-	-	4/4
883	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR , EPC	01/1991	154.62 -	154.62	.00	-	-	-	0/0
884	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	238.01	-	-	-	0/0
885	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
886	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 -	560.70	657.38	07/2016 -	-	-	0/0
887	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
888	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	87.02	05/2016 -	-	-	0/0
889	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
890	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	289.14	05/2016 -	-	-	0/0
891	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 -	925.87	699.76	10/2016 -	-	-	0/0
892	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
893	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR ,	08/2015	288.24 -	288.24	303.16	11/2015 -	-	-	0/0
894	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	89.69	05/2017 -	-	-	0/0
895	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,467.08	12/2016 -	-	-	0/0
896	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	26.78	03/2020 -	-	-	0/0
897	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14(O) -	0/0
898	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54(O) -	0/0
899	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
900	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	23.19	- -	-	-	0/0
901	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
902	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	38.11	- -	-	-	0/0
903	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	3.59	- -	-	-	0/0
904	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR ,	11/2016	230.34 -	230.34	205.97	10/2019 -	-	-	0/0
905	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	39.82	- -	-	-	0/0
906	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR ,	05/2014	199.98 -	199.98	174.35	08/2016 -	12/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
907	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	14.94	- -	-	-	0/0
908	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR , EPC	10/2013	649.90 -	649.90	.00	12/2020 -	12/2020	-	0/0
909	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR , EPC	10/2013	446.97 -	446.97	.00	11/2020 -	11/2020	-	0/0
910	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR , EPC	10/2013	464.09 -	464.09	.00	11/2020 -	11/2020	-	0/0
911	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH ,	03/2010	179.89 271.00	271.00	270.91	03/2013 05/2019	-	-	0/0
912	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH ,	12/2010	169.26 299.00	299.00	.00	01/2019 -	-	-	0/0
913	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	200.71	- 03/2021	03/2021	- 5	0/0
914	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.13	12/2015 -	-	-	0/0
915	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	439.27	05/2018 -	-	-	0/0
916	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
917	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	299.11	- -	03/2021	- -	0/0
918	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 572.66	572.66	255.42	08/2016 06/2021	06/2021	58(O) 3	0/0
919	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	264.26	06/2017 06/2021	06/2021	48(O) 3	0/0
920	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 543.73	544.00	397.33	09/2016 06/2021	06/2021	57(O) 3	0/0
921	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH ,	03/2016	491.52 512.77	491.52	474.52	09/2016 10/2020	10/2020	-	0/0
922	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 731.50	731.50	399.36	10/2016 06/2021	06/2021	56(O) 3	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
923	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 435.61	435.61	85.00	07/2016 06/2021	06/2021	59(O) 3	0/0
924	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	264.67	01/2018 03/2021	03/2021	38(O) 0	0/0
925	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	239.88	03/2015 06/2021	06/2021	75(O) 3	0/0
926	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	75.05	05/2019 03/2021	03/2021	22(O) 0	0/0
927	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	256.32	11/2017 03/2021	03/2021	40(O) 0	0/0
928	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	-	-	0/0
929	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
930	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	310.72	- -	-	-	0/4
931	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	91.39	- -	-	-	2/4
932	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	219.47	- -	-	-	3/4
933	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	478.46	- -	-	-	0/0
934	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	336.25	- -	-	-	0/0
935	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	205.20	- -	-	-	0/0
936	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	278.30	05/2020 -	-	-	1/4
937	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 -	852.67	138.14	12/2019 -	-	-	1/4
938	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.89	09/2012 -	-	-	2/3
939	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	11/2020	-	0/0
940	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-	-	3/3
941	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
942	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	715.10	- -	-	-	2/2
943	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	203.40	- -	-	-	1/1
944	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	503.45	- -	-	-	2/2
945	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	450.54	- -	-	-	2/2
946	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	134.77	- -	-	-	0/0
947	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	392.00	353.42	- -	02/2021	-	0/0
948	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	248.88	- -	-	-	0/0
949	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	303.96	- -	-	-	0/3
950	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	-	-	0/0
951	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	8(O) -	3/3
952	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
953	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 -	1,449.00	394.36	- -	01/2021	-	0/0
954	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
955	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 -	1,437.64	584.17	- -	07/2021	-	0/0
956	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	37.17	- -	-	-	0/0
957	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	444.86	11/2018 -	-	-	2/4
958	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	276.20	11/2018 -	-	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
959	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	130.53	05/2019 -	-	-	2/4
960	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	235.12	03/2018 -	-	-	1/4
961	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	109.64	06/2021 -	06/2021	0(O) -	2/4
962	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
963	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-	-	0/0
964	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	507.70	496.22	06/2016 -	-	-	0/0
965	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	537.16	516.32	07/2018 -	-	-	0/0
966	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29(O) -	0/0
967	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	270.65	05/2019 -	-	-	0/0
968	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	813.45	577.21	05/2019 -	-	-	0/0
969	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	597.77	03/2020 03/2021	03/2021	12(O) 0	0/0
970	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	444.49	- 06/2021	12/2020	-	0/0
971	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	169.48	- -	-	-	0/0
972	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	197.30	- -	-	-	0/0
973	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	931.21	268.17	- -	07/2021	- -	0/0
974	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	213.17	- -	07/2021	- -	0/0
975	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	117.51	- -	-	-	0/0
976	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	129.12	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
977	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	306.06	- -	-	-	0/0
978	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	178.64	03/2019 -	02/2021	23(O) -	0/0
979	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 -	-	-	0/0
980	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	526.09	- 02/2020	-	-	0/0
981	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	501.73	- -	-	-	0/0
982	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	690.88	- -	-	-	0/0
983	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	604.45	- -	-	-	0/0
984	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	659.79	- 01/2020	-	-	0/0
985	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	438.38	- 06/2020	-	-	0/0
986	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	468.24	- 02/2020	-	-	0/0
987	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	567.52	- -	-	-	0/0
988	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-	-	0/0
989	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	697.33	03/2018 -	-	-	0/0
990	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	667.10	02/2019 -	-	-	0/0
991	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	271.06	- -	09/2020	-	0/0
992	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	663.25	- -	-	-	0/0
993	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,160.74	- -	08/2020	-	0/0
994	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15(O) -	0/0
995	FOUR LANING OF SOLAN-KAITHLIGHT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	127.42	- -	05/2021	-	0/0
996	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,106.27	07/2015 -	09/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
997	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,709.06	06/2015 -	-	-	0/0
998	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,651.59	07/2013 -	-	-	0/0
999	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,922.52	06/2014 -	10/2020	-	0/0
1000	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	815.94	06/2019 -	12/2020	-	0/0
1001	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,602.69	12/2018 -	-	-	0/0
1002	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	817.59	- -	01/2021	-	2/3
1003	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	137.56	08/2018 -	-	-	2/4
1004	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	74.42	11/2018 -	-	-	1/4
1005	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	29.28	07/2019 -	-	-	0/0
1006	CONSTRUCTION OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]NHIDCL,JAMMU AND KASHMIR ,	12/2019	2,680.42 -	2,680.42	29.22	12/2023 -	12/2023	0(O) -	0/4
1007	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]NHIDCL,JAMMU AND KASHMIR , EPC	08/2020	6,808.69 -	6,808.69	38.33	09/2026 -	09/2026	0(O) -	0/6
1008	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	228.39 -	228.39	.00	04/2022 -	04/2022	0(O) -	0/4
1009	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	210.79 -	210.79	.00	04/2022 -	04/2022	0(O) -	0/4
1010	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
1011	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 1,115.95	1,115.95	975.08	03/2019 10/2019	10/2019	-	0/0
1012	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 486.00	486.00	432.16	- -	-	-	0/0
1013	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	336.60	312.79	08/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1014	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	64.77	- -	-	-	0/0
1015	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	350.78	- -	-	-	0/0
1016	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- -	03/2021	- -	0/0
1017	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSI PUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND ,	03/2018	212.99 -	212.99	155.29	06/2020 -	01/2021	-	0/0
1018	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021	0(O) -	0/4
1019	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	-	-	3/3
1020	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
1021	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
1022	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
1023	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	-	0/0
1024	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,287.50	08/2018 -	-	-	0/0
1025	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	119.00	03/2019 03/2022	03/2022	36(O) 0	0/0
1026	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	-	0/0
1027	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	936.78	04/2020 -	12/2020	-	0/0
1028	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	870.00	336.58	03/2019 01/2021	12/2021	33(O) 0	0/0
1029	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-	-	0/0
1030	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	905.81	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1031	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,085.47	03/2020 -	-	-	0/0
1032	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	273.86	- -	-	-	0/0
1033	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	-	0/0
1034	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,244.98	- -	-	-	0/0
1035	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
1036	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
1037	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0
1038	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
1039	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
1040	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0
1041	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
1042	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
1043	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	325.86	326.88	10/2018 -	-	-	0/0
1044	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
1045	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1046	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
1047	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
1048	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
1049	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	-	-	0/0
1050	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
1051	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	-	-	0/0
1052	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
1053	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	-	-	0/0
1054	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	-	0/0
1055	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	889.83	- 01/2020	01/2020	-	0/0
1056	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	522.80	06/2018 10/2020	03/2021	33(O) 0	0/0
1057	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	492.81	09/2017 -	05/2021	44(O) -	0/0
1058	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1059	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1060	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
1061	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1062	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	- 0	0/0
1063	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1064	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1065	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73(O) -	0/0
1066	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71(O) -	0/0
1067	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 686.13	686.13	669.94	- -	05/2020	-	0/0
1068	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 679.94	691.38	669.35	- -	05/2020	-	0/0
1069	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	418.09	01/2020 01/2021	03/2021	14(O) 0	0/0
1070	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	735.81	02/2020 04/2021	04/2021	14(O) 0	0/0
1071	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	824.83	- -	06/2015	-	0/0
1072	FOUR LANING OF GWALIOR-SHIPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1073	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1074	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	771.23	- 06/2015	06/2015	-	0/0
1075	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	366.24	08/2017 06/2021	06/2021	46(O) 0	0/0
1076	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	195.73	01/2019 -	-	-	4/4
1077	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	473.85	10/2017 -	02/2021	40(O) -	3/4
1078	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	221.79	09/2017 -	12/2020	-	3/4
1079	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	648.40	09/2017 -	01/2021	-	3/4
1080	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	224.81	- -	08/2021	- -	3/4
1081	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	738.74	- -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1082	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	326.08	- -	07/2018	-	0/0
1083	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	129.98	03/2018 02/2021	02/2021	35(O) 0	0/0
1084	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 173.41	173.41	139.19	08/2018 03/2021	03/2021	31(O) 0	0/0
1085	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	38.45	03/2018 04/2021	04/2021	37(O) 0	0/0
1086	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH ,	11/2017	235.91 -	235.91	173.80	02/2018 02/2021	02/2021	36(O) 0	0/0
1087	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	115.57	02/2018 02/2021	02/2021	36(O) 0	0/0
1088	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH ,	03/2018	191.21 -	191.21	117.80	11/2019 01/2021	02/2021	15(O) 1	0/0
1089	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	116.58	03/2017 06/2021	06/2021	51(O) 0	0/0
1090	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	59.72	03/2018 09/2021	09/2021	42(O) 0	0/0
1091	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 226.88	226.88	170.05	08/2018 03/2021	03/2021	31(O) 0	0/0
1092	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	151.12	03/2018 01/2021	03/2021	36(O) 0	0/0
1093	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	191.67	07/2018 03/2021	03/2021	32(O) 0	0/0
1094	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	03/2021	37(O) 0	0/0
1095	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	03/2021	36(O) 0	0/0
1096	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH ,	09/2016	287.34 -	287.34	194.85	01/2019 09/2020	11/2020	-	0/0
1097	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	186.74	09/2019 06/2021	06/2021	21(O) 0	0/0
1098	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	512.17	07/2018 05/2021	05/2021	34(O) 0	0/0
1099	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	877.79	668.14	06/2019 04/2021	04/2021	22(O) 0	0/0
1100	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH ,	09/2016	178.23 -	178.23	122.99	09/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1101	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	296.24	06/2019 -	-	-	0/4
1102	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	345.46	03/2018 06/2021	06/2021	39(O) 0	0/0
1103	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	78.54	03/2021 -	03/2021	0(O) -	0/0
1104	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	231.66	- -	12/2021	- -	1/3
1105	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	35.00	- -	-	-	0/4
1106	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	425.85	- -	02/2022	- -	1/4
1107	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	164.95	- -	-	-	0/4
1108	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	496.65	12/2019 -	12/2021	24(O) -	2/3
1109	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	312.73	03/2020 -	04/2022	25(O) -	1/3
1110	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	296.06	05/2020 -	05/2022	24(O) -	1/3
1111	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	313.00	03/2020 -	-	-	1/3
1112	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,540.00	03/2013 -	03/2021	96(O) -	0/0
1113	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1114	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	80.00	- -	-	-	0/4
1115	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1116	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	300.50	- -	-	-	3/4
1117	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1118	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1119	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	89.93	- -	-	-	0/0
1120	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1121	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	408.90	05/2018 11/2020	11/2020	-	0/1
1122	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	730.97	630.68	05/2018 06/2021	06/2021	37(O) 0	0/0
1123	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1124	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	690.17	585.57	05/2018 06/2021	06/2021	37(O) 0	0/1
1125	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	199.44	03/2019 12/2021	12/2021	33(O) 0	0/0
1126	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	361.58	05/2018 04/2019	06/2021	37(O) 0	0/1
1127	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0
1128	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	857.08	11/2016 -	-	-	0/0
1129	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	3,443.43	01/2018 -	09/2020	-	0/0
1130	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1131	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	151.11	07/2018 -	-	-	0/0
1132	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	302.83	07/2019 06/2021	12/2021	29(O) 0	0/0
1133	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	317.73	07/2019 06/2021	12/2021	29(O) 0	0/0
1134	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	585.85	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1135	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MORTH, MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	324.00	- -	-	-	0/0
1136	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	887.07	- -	07/2021	-	3/4
1137	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	271.89	- -	07/2021	-	1/4
1138	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA ,	11/2016	400.25 -	400.25	105.20	03/2019 -	02/2021	23(O) -	0/0
1139	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA ,	11/2016	446.17 -	446.17	70.85	03/2019 -	03/2021	24(O) -	0/0
1140	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA ,	11/2016	290.73 -	315.00	309.40	- -	-	-	0/0
1141	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA ,	01/2017	244.90 -	244.90	251.87	05/2019 -	-	-	0/0
1142	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA ,	02/2017	904.16 -	904.16	855.25	02/2020 -	-	-	0/0
1143	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA ,	03/2017	247.02 -	157.49	63.76	03/2020 -	-	-	0/0
1144	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	-	-	0/0
1145	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	-	0/3
1146	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-	-	3/3
1147	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	11/2020	-	0/0
1148	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	-	-	0/0
1149	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	-	-	0/3
1150	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA ,	12/2017	404.94 -	448.18	407.94	- -	10/2020	-	0/0
1151	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA ,	01/2018	607.00 -	607.00	411.79	- -	08/2021	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1152	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA ,	01/2018	621.00 -	621.00	591.21	- -	04/2021	- -	2/3
1153	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI, MAHARASHTRA , EPC	03/2018	291.53 -	291.53	127.37	- 08/2021	02/2022	- 3	0/0
1154	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI, MAHARASHTRA , EPC	03/2018	289.21 -	289.21	162.72	- 02/2021	08/2021	- 0	0/0
1155	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	72.87	- -	07/2021	- -	0/0
1156	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA ,	03/2018	642.13 -	807.00	628.87	- -	-	-	0/0
1157	SARSAM TO KOTHARI - [N24001002]MoRTH, MAHARASHTRA ,	02/2016	545.64 -	545.64	151.62	07/2019 -	-	-	0/4
1158	AKOLA TO AKOT - [N24001003]MoRTH, MAHARASHTRA ,	01/2017	313.95 -	313.95	49.38	06/2019 -	-	-	0/4
1159	AKOT TO ANJANGAON - [N24001006]MoRTH, MAHARASHTRA ,	01/2017	245.77 246.00	245.77	186.28	06/2019 -	-	-	0/4
1160	KHAMGAON TO SHEGAON - [N24001009]MoRTH, MAHARASHTRA ,	02/2017	203.21 203.00	203.21	173.79	05/2019 -	-	-	0/0
1161	SHEGAON TO DEORI PHATA - [N24001010]MoRTH, MAHARASHTRA ,	02/2017	373.10 373.00	373.10	311.24	05/2019 -	-	-	0/4
1162	MEHKAR TO CHIKALI - [N24001011]MoRTH, MAHARASHTRA ,	02/2017	322.48 322.00	322.48	230.03	05/2019 -	-	-	0/4
1163	CHIKALI TO KHAMGAON - [N24001012]MoRTH, MAHARASHTRA ,	02/2017	548.03 548.00	548.03	353.00	06/2019 -	-	-	0/4
1164	DIGRAS DARWAH KARANJA - [N24001013]MoRTH, MAHARASHTRA ,	01/2017	391.06 391.00	391.06	204.91	06/2019 -	-	-	0/0
1165	NANDGAON TO MORSHI - [N24001014]MoRTH, MAHARASHTRA ,	01/2017	385.87 386.00	385.87	254.89	06/2019 -	-	-	0/0
1166	MORSHI TO ACHALPUR - [N24001015]MoRTH, MAHARASHTRA ,	01/2017	341.16 341.00	341.16	222.94	06/2019 -	-	-	0/0
1167	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH, MAHARASHTRA ,	01/2017	471.61 472.00	471.61	317.05	06/2019 -	-	-	0/0
1168	DAHEGAON TO KUHI - [N24001017]MoRTH, MAHARASHTRA ,	01/2017	228.89 229.00	228.89	152.57	06/2019 -	-	-	3/4
1169	BHANDARA TO GHOTITOK - [N24001018]MoRTH, MAHARASHTRA ,	01/2017	392.83 393.00	392.83	271.60	06/2019 -	-	-	0/0
1170	KATOL TO WARUD - [N24001019]MoRTH, MAHARASHTRA ,	01/2017	463.62 664.00	463.62	253.23	06/2019 -	-	-	0/4
1171	AMDHI TO SAONER - [N24001021]MoRTH, MAHARASHTRA ,	01/2017	396.91 397.00	396.91	280.56	06/2019 -	-	-	3/4
1172	WADI TO ASOLA - [N24001022]MoRTH, MAHARASHTRA ,	01/2017	363.82 364.00	363.82	26.75	09/2019 -	-	-	1/4
1173	NAGAJ TO VAJJAPUR - [N24001023]MoRTH, MAHARASHTRA ,	01/2017	376.72 377.00	376.72	224.81	06/2019 -	-	-	0/4
1174	MANGAON TO DIGHI PORT - [N24001024]MoRTH, MAHARASHTRA ,	01/2017	457.52 -	457.52	352.94	07/2019 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1175	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	268.87	07/2019 -	-	-	3/4
1176	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	47.76	05/2019 -	-	-	1/4
1177	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	46.26	12/2019 -	-	-	1/4
1178	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	92.84	12/2019 -	-	-	0/4
1179	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	218.78	08/2019 -	-	-	2/4
1180	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	264.93	08/2019 -	-	-	2/4
1181	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	162.30	08/2019 -	-	-	2/4
1182	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	227.76	05/2019 -	-	-	0/4
1183	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	293.39	07/2019 -	-	-	2/4
1184	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	252.78	07/2019 -	-	-	2/4
1185	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	270.13	12/2019 -	-	-	0/4
1186	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.10	07/2019 -	-	-	0/0
1187	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	252.45	07/2019 -	-	-	2/4
1188	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	8.34	05/2020 -	-	-	0/4
1189	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	98.05	- -	-	-	0/4
1190	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	178.43	11/2019 -	-	-	2/4
1191	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	112.83	07/2019 -	-	-	2/4
1192	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	203.63	12/2019 -	-	-	0/4
1193	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	112.39	05/2020 -	-	-	0/4
1194	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	317.91	06/2019 -	-	-	0/4
1195	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	198.65	11/2019 -	-	-	0/4
1196	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	125.69	07/2019 -	-	-	0/4
1197	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	202.34	11/2019 -	-	-	0/0
1198	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	148.53	07/2019 -	-	-	0/0
1199	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	181.55	12/2019 -	-	-	0/4
1200	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	86.72	12/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1201	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	146.39	12/2019 -	-	-	0/4
1202	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	155.57	12/2019 -	-	-	0/4
1203	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	148.25	06/2019 -	-	-	0/4
1204	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	116.30	11/2019 -	-	-	0/4
1205	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	208.63	07/2019 -	-	-	0/4
1206	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	278.82	07/2019 -	-	-	0/0
1207	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	108.68	06/2019 -	-	-	0/4
1208	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	255.47	12/2019 -	-	-	0/4
1209	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	97.86	12/2019 -	-	-	0/4
1210	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	125.23	12/2019 -	-	-	0/4
1211	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	97.66	12/2019 -	-	-	0/4
1212	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	142.66	12/2019 -	-	-	0/4
1213	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	93.23	02/2020 -	-	-	0/4
1214	DHANGRIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	131.55	02/2020 -	-	-	0/4
1215	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	126.00	12/2019 -	-	-	0/4
1216	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	186.18	12/2019 -	-	-	0/4
1217	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	186.24	12/2019 -	-	-	0/4
1218	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	149.54	12/2019 -	-	-	1/4
1219	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	158.00	09/2019 -	-	-	1/4
1220	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	132.40	12/2019 -	-	-	2/4
1221	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	66.25	08/2020 -	-	-	0/4
1222	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	138.50	12/2019 -	-	-	0/4
1223	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	152.42	08/2020 -	-	-	0/0
1224	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	155.48	12/2019 -	-	-	0/0
1225	OSMANNAGAR TO KUNDRA - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	97.52	08/2020 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1226	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	123.76	12/2019 -	-	-	0/0
1227	KUNDRA TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	254.75	12/2019 -	-	-	2/4
1228	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	73.50	12/2019 -	-	-	0/0
1229	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	149.80	06/2020 -	-	-	1/4
1230	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	84.00	12/2019 -	-	-	0/0
1231	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	68.30	12/2019 -	-	-	1/4
1232	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	26.85	12/2019 -	-	-	0/0
1233	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	222.37	12/2019 -	-	-	2/4
1234	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	123.23	05/2020 -	-	-	0/4
1235	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	199.01	06/2019 -	-	-	0/4
1236	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	124.95	07/2019 -	-	-	0/4
1237	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	153.84	11/2019 -	-	-	0/4
1238	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	-	-	0/0
1239	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	223.97	12/2019 -	-	-	0/4
1240	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	261.97	07/2019 -	-	-	0/4
1241	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKAALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 634.30	536.65	539.22	12/2019 03/2021	03/2021	15(O) 0	0/0
1242	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	246.97	07/2019 -	-	-	0/4
1243	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	181.32	12/2019 -	-	-	0/0
1244	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	136.95	03/2019 -	-	-	0/0
1245	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	187.77	- -	-	-	0/0
1246	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	165.67	03/2019 -	-	-	0/0
1247	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	22.40	05/2020 -	-	-	0/4
1248	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	131.92	12/2019 -	-	-	1/4
1249	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	221.81	07/2019 -	-	-	0/4
1250	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	409.50	08/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1251	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	190.69	07/2019 -	-	-	0/4
1252	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4
1253	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	137.63	07/2019 -	-	-	0/4
1254	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	189.91	06/2019 -	-	-	2/4
1255	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	164.90	03/2019 -	-	-	0/4
1256	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	32.52	03/2018 -	-	-	0/4
1257	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	7.03	05/2020 -	-	-	0/4
1258	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	135.41	12/2019 -	-	-	0/4
1259	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	140.20	12/2019 -	-	-	0/4
1260	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	149.29	04/2020 -	-	-	1/4
1261	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	362.73	04/2019 -	-	-	0/4
1262	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	163.36	09/2019 -	-	-	2/4
1263	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	61.53	09/2018 -	04/2021	31(O) -	0/4
1264	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	648.90	12/2019 -	-	-	1/4
1265	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	889.21	11/2019 -	-	-	1/4
1266	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	279.80	06/2019 -	-	-	2/4
1267	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	53.94	07/2019 -	-	-	1/4
1268	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	74.91	06/2019 -	-	-	0/4
1269	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.60	07/2019 -	-	-	0/4
1270	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	136.85	02/2019 -	-	-	0/4
1271	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	213.10	11/2018 -	-	-	0/4
1272	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	128.89	06/2019 -	-	-	0/4
1273	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	177.79	06/2019 -	-	-	0/4
1274	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	116.75	06/2019 -	-	-	0/4
1275	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	94.22	06/2019 -	-	-	0/4
1276	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	185.74	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1277	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.69	06/2019 -	-	-	0/0
1278	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	188.64	07/2019 -	-	-	0/4
1279	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	137.87	06/2021 -	06/2021	0(O) -	1/4
1280	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	709.06	12/2019 -	-	-	1/4
1281	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	627.00	11/2019 -	-	-	1/4
1282	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	797.60	02/2019 -	-	-	0/0
1283	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	630.05	03/2020 -	-	-	2/4
1284	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	961.51	03/2020 -	-	-	3/5
1285	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	31.81	06/2019 -	-	-	1/4
1286	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	233.77	12/2019 -	-	-	0/0
1287	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 -	313.58	98.04	04/2020 -	-	-	0/4
1288	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	160.06	10/2018 -	10/2021	36(O) -	3/4
1289	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR ,	10/2016	235.31 -	235.31	170.53	11/2020 -	11/2020	-	0/0
1290	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL,MANIPUR , EPC	03/2019	471.00 -	471.00	101.20	07/2022 -	07/2022	0(O) -	0/4
1291	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL,MANIPUR , EPC	03/2020	292.24 -	292.24	8.60	06/2022 -	06/2022	0(O) -	0/4
1292	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL,MANIPUR , EPC	06/2020	365.53 -	365.53	14.15	08/2022 -	08/2022	0(O) -	0/4
1293	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL,MANIPUR , EPC	03/2020	167.95 -	167.95	18.22	06/2022 -	06/2022	0(O) -	0/4
1294	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL,MANIPUR , EPC	07/2020	177.76 -	177.76	17.84	08/2022 -	08/2022	0(O) -	0/4
1295	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL,MANIPUR , EPC	08/2020	379.39 -	379.39	.00	04/2022 -	04/2022	0(O) -	0/4
1296	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL,MANIPUR , EPC	08/2020	268.98 -	268.98	.00	04/2022 -	04/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1297	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL,MANIPUR , EPC	08/2020	228.97 -	228.97	.00	04/2022 -	04/2022	0(O) -	0/4
1298	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 -	-	-	0/0
1299	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	119.35	- -	09/2021	- -	2/4
1300	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	84.67	05/2019 -	-	-	1/4
1301	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	-	0/0
1302	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021	128(O) 0	0/0
1303	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021	128(O) 0	0/0
1304	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	65.01	09/2019 -	04/2023	43(O) -	0/0
1305	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	18.08	09/2019 -	07/2023	46(O) -	0/0
1306	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	33.18	09/2019 -	06/2023	45(O) -	0/0
1307	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	47.39	09/2019 -	04/2023	43(O) -	0/0
1308	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	58.49	09/2019 -	04/2023	43(O) -	0/0
1309	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	72.44	09/2019 -	06/2023	45(O) -	0/0
1310	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	50.49	09/2019 -	04/2024	55(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1311	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	59.92	09/2019 -	09/2023	48(O) -	0/0
1312	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	292.10	09/2014 12/2020	-	-	0/0
1313	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM , EPC	09/2020	275.02 -	275.02	4.72	10/2022 -	10/2022	0(O) -	0/4
1314	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM , EPC	03/2020	206.88 -	206.88	.00	07/2022 -	07/2022	0(O) -	0/4
1315	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM , EPC	03/2020	216.49 -	216.49	.00	07/2022 -	07/2022	0(O) -	0/4
1316	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM , EPC	03/2020	292.24 -	292.24	.00	07/2022 -	07/2022	0(O) -	0/4
1317	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM , EPC	03/2020	281.78 -	281.78	.00	07/2022 -	07/2022	0(O) -	0/4
1318	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	364.59	334.71	12/2009 -	-	-	0/0
1319	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1320	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1321	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105(O) -	0/0
1322	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	11/2020	-	0/0
1323	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71(O) -	3/4
1324	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,565.00	- -	05/2021	- -	0/0
1325	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	-	-	0/0
1326	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0
1327	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1328	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	290.94	08/2016 -	05/2021	57(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1329	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	339.55	276.01	08/2016 -	05/2021	57(O) -	2/4
1330	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	340.00	234.97	08/2016 -	05/2021	57(O) -	2/4
1331	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	129.13	04/2017 -	-	-	1/4
1332	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	260.08	09/2018 -	09/2020	-	2/4
1333	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 336.49	336.49	71.11	09/2018 -	11/2022	50(O) -	0/0
1334	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	114.91	09/2018 -	07/2022	46(O) -	0/0
1335	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	85.02	09/2018 -	05/2022	44(O) -	0/4
1336	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	68.70	09/2018 -	09/2022	48(O) -	0/4
1337	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	80.78	09/2018 -	12/2021	39(O) -	0/4
1338	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	95.34	09/2018 -	12/2021	39(O) -	0/4
1339	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	95.97	09/2018 -	-	-	1/2
1340	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	111.04	09/2018 -	-	-	0/2
1341	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	192.60	114.76	09/2018 -	-	-	0/2
1342	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	83.20	09/2018 -	11/2021	38(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1343	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	60.55	09/2018 -	12/2021	39(O) -	1/4
1344	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	36.80	09/2018 -	10/2022	49(O) -	0/4
1345	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	42.55	09/2018 -	11/2022	50(O) -	0/4
1346	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	98.42	12/2020 -	12/2020	-	0/0
1347	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	123.44	12/2020 -	12/2020	-	0/0
1348	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 369.96	336.25	301.49	09/2019 09/2020	-	-	0/0
1349	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	87.30	11/2020 05/2021	11/2020	-	0/0
1350	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	50.27	12/2022 -	12/2022	0(O) -	0/0
1351	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND , EPC	09/2020	277.44 -	277.44	.00	10/2022 -	10/2022	0(O) -	0/4
1352	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257]NHIDCL,NAGALAND , EPC	08/2020	159.85 -	159.85	.00	10/2022 -	10/2022	0(O) -	0/4
1353	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND , EPC	08/2020	202.36 -	202.36	.00	04/2022 -	04/2022	0(O) -	0/4
1354	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND , EPC	09/2020	315.63 -	315.63	.00	04/2022 -	04/2022	0(O) -	0/4
1355	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND , EPC	09/2020	257.15 -	257.15	5.29	04/2022 -	04/2022	0(O) -	0/4
1356	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND , EPC	03/2020	320.97 -	320.97	8.86	06/2022 -	06/2022	0(O) -	0/4
1357	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND , EPC	03/2020	355.79 -	355.79	12.99	06/2022 -	06/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1358	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND , EPC	03/2020	361.53 -	361.53	3.66	06/2022 -	06/2022	0(O) -	0/4
1359	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND , EPC	03/2020	330.78 -	330.78	11.24	12/2021 -	12/2021	0(O) -	0/4
1360	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND , EPC	03/2020	278.95 -	278.95	41.64	06/2022 -	06/2022	0(O) -	0/4
1361	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND , EPC	04/2020	330.80 -	330.80	1.50	12/2021 -	12/2021	0(O) -	0/4
1362	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288]NHIDCL,NAGALAND , EPC	08/2020	232.29 -	232.29	.00	04/2022 -	04/2022	0(O) -	0/4
1363	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1364	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021	81(O) 0	0/0
1365	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1366	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1367	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1368	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	- -	0/0
1369	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	213.52	- -	03/2022	- -	0/1
1370	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	-	-	0/0
1371	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	-	-	0/0
1372	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	611.71	- -	01/2021	-	0/0
1373	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	555.68	08/2019 -	03/2021	19(O) -	0/0
1374	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	- -	0/0
1375	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1376	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1377	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1378	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1379	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	-	0/0
1380	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1381	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15(O) -	0/0
1382	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47(O) -	0/0
1383	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	227.63	- -	06/2021	- -	0/0
1384	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	127.61	- -	06/2021	- -	0/0
1385	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	332.04	- -	03/2022	- -	0/0
1386	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	276.59	- -	06/2021	- -	0/0
1387	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	63.98	- -	-	-	0/1
1388	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	217.40	- -	08/2021	- -	0/0
1389	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	240.00	- -	08/2021	- -	0/1
1390	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	261.74	- -	06/2021	- -	0/0
1391	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	- -	0/0
1392	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	102.70	- -	06/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1393	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	25.40	- -	06/2021	- -	0/0
1394	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	189.70	- -	04/2021	- -	0/0
1395	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1396	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1397	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1398	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1399	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1400	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1401	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1402	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB , EPC	12/2015	766.36 -	766.36	685.36	- -	-	-	0/0
1403	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB , EPC	11/2015	847.02 -	847.02	795.00	- -	-	-	0/0
1404	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 -	904.82	754.06	- -	12/2020	-	0/0
1405	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	456.80	- -	07/2021	-	0/0
1406	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	746.43	676.33	12/2017 -	-	-	0/0
1407	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- -	-	-	0/0
1408	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	-	0/0
1409	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	2,280.00	1,282.04	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1410	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	352.32	03/2020 -	09/2021	18(O) -	0/0
1411	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	193.26	- -	07/2021	- -	0/0
1412	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	- -	-	-	0/0
1413	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	- -	-	-	0/0
1414	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB ,	03/2018	322.48 -	322.48	261.72	07/2020 -	08/2021	13(O) -	0/0
1415	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB ,	03/2018	173.24 -	173.24	114.55	06/2020 -	-	-	0/0
1416	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	155.65	08/2020 -	-	-	0/0
1417	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	678.17	10/2019 -	12/2020	-	0/0
1418	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 -	170.57	44.68	11/2020 -	05/2021	6(O) -	0/0
1419	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	-	-	0/0
1420	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	237.13	08/2020 -	-	-	0/0
1421	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1422	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1423	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1424	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1425	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH, RAJASTHAN , EPC	02/2015	383.40 -	383.40	244.68	03/2015 -	-	-	0/0
1426	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH, RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.22	06/2018 -	-	-	0/4
1427	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 -	-	-	0/0
1428	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN ,	10/2015	597.00 -	597.00	587.64	10/2017 -	-	-	3/4
1429	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1430	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	1,688.16	04/2018 -	-	-	0/0
1431	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1432	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	-	-	0/4
1433	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1434	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	-	-	-	0/0
1435	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1436	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	191.80	06/2019 -	-	-	1/1
1437	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN ,	06/2016	649.00 -	649.00	546.54	06/2019 -	-	-	0/0
1438	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN ,	07/2016	688.70 -	688.70	880.00	-	-	-	0/0
1439	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1440	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,727.66	1,674.80	-	01/2021	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1441	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,304.00	- -	03/2021	- -	0/0
1442	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	- -	0/0
1443	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15(O) -	0/0
1444	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	773.03	10/2017 -	11/2020	-	0/0
1445	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	330.46	- -	-	-	0/0
1446	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	673.70	- -	09/2020	-	0/0
1447	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	119.02	- -	-	-	0/0
1448	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	610.56	- -	-	-	0/0
1449	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	886.59	- -	-	-	0/0
1450	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	611.28	- -	-	-	0/0
1451	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	131.74	04/2018 -	03/2021	35(O) -	2/4
1452	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35(O) -	3/4
1453	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34(O) -	1/4
1454	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37(O) -	1/4
1455	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	139.26	- -	03/2021	- -	0/0
1456	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	90.45	08/2022 -	08/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1457	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24(O) -	0/0
1458	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	.00	11/2020 -	08/2022	21(O) -	0/0
1459	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM ,	04/2013	151.59 370.01	151.59	282.36	08/2013 12/2020	-	-	0/0
1460	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM , ITEM RATE	04/2013	166.27 359.92	166.27	243.59	08/2013 12/2020	-	-	0/0
1461	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM , ITEM RATE	01/2013	182.28 369.64	269.14	274.07	02/2013 12/2020	-	-	0/0
1462	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	255.15	10/2017 -	-	-	3/4
1463	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	66.63	11/2017 -	-	-	2/4
1464	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	107.98	- -	-	-	1/4
1465	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	24.70	11/2017 -	-	-	1/4
1466	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	11.03	06/2018 -	-	-	0/4
1467	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM , EPC	03/2019	402.94 -	402.94	.78	04/2022 -	04/2022	0(O) -	0/4
1468	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL,SIKKIM , EPC	08/2020	295.97 -	295.97	.00	04/2023 -	04/2023	0(O) -	0/4
1469	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM , EPC	03/2020	242.97 -	242.97	.00	06/2022 -	06/2022	0(O) -	0/4
1470	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001261]NHIDCL,SIKKIM , EPC	08/2020	311.00 -	311.00	.00	04/2023 -	04/2023	0(O) -	0/4
1471	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001262]NHIDCL,SIKKIM , EPC	07/2020	345.38 -	345.38	.00	04/2023 -	04/2023	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1472	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,337.06	12/2013 -	-	-	0/0
1473	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	1.65	06/2013 -	10/2020	-	0/0
1474	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	49.53	05/2013 -	08/2021	99(O) -	0/0
1475	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	8.56	04/2014 -	-	-	0/0
1476	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	223.10	08/2015 -	-	-	0/0
1477	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	-	0/0
1478	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	140.64	08/2015 -	-	-	0/0
1479	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	-	-	0/0
1480	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	-	-	0/0
1481	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1482	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1483	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	419.77	08/2018 -	03/2021	31(O) -	0/0
1484	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	394.32	07/2018 -	02/2021	31(O) -	0/0
1485	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 932.23	848.45	219.00	03/2020 -	12/2021	21(O) -	0/0
1486	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	394.32	07/2016 -	02/2021	55(O) -	0/0
1487	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	453.70	08/2017 -	07/2022	59(O) -	0/0
1488	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	182.00	09/2017 -	-	-	0/0
1489	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	561.03	09/2017 -	07/2022	58(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1490	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	187.16	- -	-	-	0/0
1491	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	220.78	- -	07/2021	- -	0/0
1492	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	240.60	- -	05/2021	- -	0/0
1493	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	303.46	- -	09/2021	- -	0/0
1494	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	-	0/0
1495	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	196.87	- -	07/2021	- -	0/0
1496	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	-	-	0/0
1497	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU ,	03/2019	297.55 -	297.55	45.52	11/2019 -	-	-	0/0
1498	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU ,	01/2016	162.72 -	162.72	136.46	09/2016 -	-	-	0/0
1499	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]MoRTH,TAMIL NADU ,	05/2016	307.70 -	307.70	312.82	01/2017 -	-	-	0/0
1500	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 -	240.38	74.56	06/2019 -	-	-	0/0
1501	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU , EPC	07/2020	3,426.00 -	3,426.00	.00	12/2021 -	12/2021	0(O) -	0/0
1502	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0
1503	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1504	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1505	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,056.08	970.12	11/2018 07/2019	03/2021	28(O) 2	0/0
1506	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1507	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	380.39	- -	-	-	0/0
1508	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	462.38	- -	-	-	0/0
1509	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	144.31	- -	-	-	0/0
1510	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1511	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	112.37	02/2019 -	-	-	0/0
1512	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	113.83	03/2019 -	-	-	0/0
1513	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	162.42	05/2019 -	-	-	0/0
1514	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	106.43	10/2019 -	-	-	0/0
1515	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	222.84	12/2019 -	-	-	0/0
1516	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	293.94	05/2019 -	-	-	0/0
1517	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	168.63	05/2019 -	-	-	0/0
1518	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	97.89	05/2020 -	-	-	0/0
1519	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	171.39	12/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1520	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA ,	02/2018	206.13 -	206.13	171.39	06/2020 -	-	-	0/0
1521	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA ,	02/2018	294.13 -	294.13	109.06	11/2019 -	-	-	0/0
1522	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA ,	02/2018	220.28 -	220.28	118.67	11/2019 -	-	-	0/0
1523	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA ,	02/2018	426.52 -	426.52	385.12	04/2020 -	-	-	0/0
1524	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA ,	03/2018	322.81 -	322.81	77.17	09/2020 -	-	-	0/0
1525	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA ,	03/2018	626.76 -	626.76	170.17	07/2020 -	-	-	0/0
1526	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA ,	01/2017	605.08 -	605.08	394.25	10/2019 -	-	-	0/0
1527	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA ,	03/2018	192.67 -	192.67	146.55	07/2019 -	-	-	0/0
1528	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA ,	01/2019	193.19 -	193.19	91.71	- -	-	-	0/0
1529	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00	357.19	03/2018 -	-	-	3/4
1530	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH, TRIPURA ,	10/2016	171.90 -	171.90	110.19	08/2020 07/2021	07/2021	11(O) 0	0/0
1531	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL, TRIPURA , EPC	03/2020	247.76 -	247.76	.00	01/2022 -	01/2022	0(O) -	0/4
1532	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL, TRIPURA , EPC	06/2020	347.36 -	347.36	.00	01/2022 -	01/2022	0(O) -	0/4
1533	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL, TRIPURA , EPC	06/2020	277.50 -	277.50	.00	01/2022 -	01/2022	0(O) -	0/4
1534	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265]NHIDCL, TRIPURA , EPC	03/2020	154.51 -	154.51	.00	07/2022 -	07/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1535	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL, TRIPURA , EPC	03/2020	178.43 -	178.43	.00	07/2022 -	07/2022	0(O) -	0/4
1536	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH, TRIPURA , EPC	01/2017	197.67 -	197.67	5.75	12/2022 -	12/2022	0(O) -	0/0
1537	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1538	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)	07/2012	291.36 469.31	469.31	459.07	01/2014 12/2020	12/2020	-	0/0
1539	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-	-	0/0
1540	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH, UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1541	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1542	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH ,	04/2014	351.34 417.68	417.68	433.68	01/2016 12/2020	12/2020	-	0/0
1543	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH ,	09/2015	368.73 -	368.73	239.04	09/2016 -	-	-	0/0
1544	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH ,	04/2014	495.78 627.93	627.93	633.24	01/2016 01/2020	01/2020	-	0/0
1545	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH, UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	-	-	0/0
1546	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH, UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1547	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1548	4-LANING OF GHAGHRA BRIDGE TO VARANASI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1549	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1550	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1551	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1552	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1553	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH, UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	128.54	08/2015 -	-	-	0/0
1554	MEERUT-BULANDSHAHAH - [N24000539]NHAI, UTTAR PRADESH ,	01/2016	683.24 -	987.94	867.27	- -	-	-	0/2
1555	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH ,	01/2016	1,081.57 -	1,057.60	549.07	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1556	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	977.26	04/2019 -	-	-	0/0
1557	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	- -	-	-	0/0
1558	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1559	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1560	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	641.51	04/2019 -	-	-	0/0
1561	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	08/2020	-	0/0
1562	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	-	-	0/0
1563	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	-	-	0/0
1564	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1565	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	-	-	0/0
1566	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1567	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	974.57	03/2020 -	-	-	2/4
1568	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,039.23	03/2020 -	-	-	3/4
1569	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	756.92	03/2020 -	-	-	0/0
1570	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1571	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	812.83	- -	-	-	0/0
1572	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	43.23	- -	-	-	0/0
1573	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1574	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1575	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	263.74	- -	-	-	0/0
1576	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	517.66	- -	-	-	0/0
1577	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	1,011.70	- -	-	-	0/0
1578	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	-	0/0
1579	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,344.09	- -	-	-	0/0
1580	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,118.92	- -	-	-	0/0
1581	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	461.52	- -	-	-	0/0
1582	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	623.03	- -	-	-	0/0
1583	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0
1584	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	74.00	- -	09/2021	-	0/0
1585	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH ,	03/2016	208.50 -	208.50	165.82	11/2019 -	02/2021	15(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1586	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	120.69	03/2020 -	-	-	0/0
1587	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	160.61	09/2019 -	-	-	0/0
1588	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	14(O) -	0/0
1589	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	141.11	10/2018 -	-	-	0/0
1590	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.29	469.64	03/2017 -	-	-	0/0
1591	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	141.33	08/2015 -	01/2021	-	0/0
1592	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	205.40	05/2019 -	02/2021	21(O) -	0/0
1593	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH ,	10/2016	239.63 -	239.63	212.53	02/2019 -	-	-	0/0
1594	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH ,	03/2016	599.34 -	599.34	492.15	01/2020 -	-	-	0/0
1595	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	1,363.84	01/2019 -	-	-	0/0
1596	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH ,	03/2016	388.83 -	388.83	304.70	12/2019 -	-	-	0/0
1597	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	129.75	03/2020 -	02/2021	11(O) -	0/0
1598	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	168.68	10/2019 -	02/2021	16(O) -	0/0
1599	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH ,	12/2016	209.10 -	209.10	201.46	10/2019 -	06/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1600	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	181.21	04/2020 -	04/2021	12(O) -	0/0
1601	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	124.43	02/2020 -	01/2021	-	0/0
1602	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	120.37	08/2020 -	03/2021	7(O) -	0/0
1603	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	172.63	09/2020 -	03/2021	6(O) -	0/0
1604	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	.00	- -	-	-	0/0
1605	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	- -	-	-	0/0
1606	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6(O) -	0/0
1607	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH , EPC	10/2020	724.60 -	724.60	.00	03/2023 -	03/2023	0(O) -	0/0
1608	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	12/2020	-	0/0
1609	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	348.16	- -	-	-	0/0
1610	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	- -	08/2020	-	0/0
1611	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 -	-	-	0/0
1612	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	55.50	05/2018 -	-	-	2/4
1613	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	124.74	06/2018 -	-	-	2/4
1614	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	144.90	05/2018 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1615	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	-	-	0/0
1616	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	-	-	0/0
1617	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	-	-	0/0
1618	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	-	-	0/0
1619	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	-	-	0/0
1620	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	-	-	0/0
1621	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	-	-	0/0
1622	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	-	-	0/0
1623	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	- -	-	-	0/0
1624	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	-	-	0/0
1625	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1626	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	196.35	07/2018 -	-	-	1/5
1627	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	-	-	0/0
1628	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,239.99	08/2013 -	05/2021	93(O) -	3/4
1629	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,858.57	08/2013 -	03/2022	103(O) -	3/4
1630	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1631	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1632	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	363.93	272.98	- -	-	-	0/0
1633	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	-	0/0
1634	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	2,360.65	4,472.01	- -	-	-	0/0
1635	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	130.72	11/2018 -	-	-	0/0
1636	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	604.65	08/2018 -	-	-	0/0
1637	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
1638	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]MoRTH, WEST BENGAL ,	08/2014	600.87 720.97	720.97	682.36	11/2017 05/2019	05/2019	-	0/0
1639	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]MoRTH, WEST BENGAL ,	08/2014	823.20 937.76	937.76	807.99	11/2017 06/2019	06/2019	-	0/0
1640	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	242.95	09/2019 11/2020	05/2021	20(O) 0	0/0
1641	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH, WEST BENGAL ,	03/2017	202.69 202.69	202.69	144.89	11/2019 -	-	-	0/0
1642	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15(O) -	0/0
1643	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	103.81	11/2020 04/2020	04/2021	5(O) 0	0/0
1644	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 254.30	254.30	79.69	10/2020 -	03/2021	5(O) -	0/0
1645	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 213.97	213.97	24.14	08/2019 -	11/2022	39(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1646	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28(O) -	0/0
1647	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL ,	04/2014	279.70 398.52	398.52	330.94	08/2017 01/2020	02/2020	-	0/0
	Total		5,40,947.36 -	5,60,277.95	3,48,803.37				338/1239
	SHIPPING AND PORTS								
1648	JAL MARG VIKAS PROJECT - [N25000072]IWAI, MULTI STATE ,	01/2018	5,369.18 4,633.81	4,633.81	1,814.28	03/2023 -	03/2023	0(O) -	0/0
	Total		5,369.18 -	4,633.81	1,814.28				0/0
	TELECOMMUNICATIONS								
1649	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE (NICF) AT GHIT - [N28000115]CPWD, DELHI ,	10/2016	248.20 -	248.20	80.10	03/2018 -	-	-	0/0
1650	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE ,	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	71(O) -	0/0
1651	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL, MULTI STATE , Central Sector Projects	03/2020	431.16 431.00	431.16	.00	06/2021 -	11/2021	5(O) -	0/0
	Total		14,013.36 -	25,343.36	16,674.10				0/0
	URBAN DEVELOPMENT								
1652	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1653	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL, BIHAR ,	02/2019	13,365.77 -	13,365.77	231.90	06/2024 -	06/2024	0(O) -	0/0
1654	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE VI-5) SHOPS CO - [N28000149]CPWD, CHHATISGARH ,	05/2019	299.97 -	299.97	.29	09/2020 -	-	-	0/0
1655	DELHI MRTS PHASE-III - [N28000056]DMRC, DELHI ,	09/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021	66(O) -	0/0
1656	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI ,	07/2012	884.30 -	884.30	812.00	12/2015 -	-	-	0/0
1657	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI ,	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	-	3/7
1658	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD, DELHI ,	06/2015	197.33 -	197.33	102.34	04/2019 06/2021	10/2021	30(O) 0	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1659	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	651.85	- -	07/2022	- -	0/9
1660	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	157.67	05/2020 -	02/2021	9(O) -	1/2
1661	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	55.38	03/2021 07/2021	07/2021	4(O) 0	0/0
1662	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19(O) -	0/0
1663	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	126.16	11/2020 -	-	-	0/2
1664	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41(O) -	0/0
1665	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022	0(O) -	0/0
1666	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	1,248.28	03/2025 -	03/2025	0(O) -	0/0
1667	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	511.60	12/2020 -	09/2021	9(O) -	0/0
1668	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI ,	02/2020	532.00 -	532.00	150.00	11/2020 02/2021	11/2020	-	0/0
1669	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	8,446.13	12/2018 -	08/2022	44(O) -	0/0
1670	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	56.76	03/2024 -	03/2024	0(O) -	0/0
1671	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	16.58	03/2024 -	03/2024	0(O) -	0/0
1672	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 30,695.00	26,405.14	16,349.18	02/2019 03/2021	06/2024	64(O) 0	97/249
1673	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 6,218.14	6,218.14	6,059.17	07/2017 09/2020	09/2020	-	0/0
1674	BHOPAL METRO RAIL - [N28000124]MPMRL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	126.50	02/2023 -	02/2023	0(O) -	0/0
1675	INDORE METRO RAIL - [N28000125]MPMRL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	117.53	02/2023 -	02/2023	0(O) -	0/0
1676	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	7,068.52	03/2018 -	-	-	0/0
1677	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 09/2022	03/2023	98(O) 0	0/0
1678	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	5,696.05	11/2021 -	11/2021	0(O) -	0/0
1679	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	2,987.00	06/2025 -	06/2025	0(O) -	0/0
1680	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-	-	12/24
1681	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	2,932.59	03/2018 -	03/2021	36(O) -	5/21

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1682	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1683	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	.00	03/2024 -	03/2024	0(O) -	0/0
1684	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	.00	03/2024 -	03/2024	0(O) -	0/0
1685	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0
	Total		2,82,747.18 -	3,01,054.80	1,34,498.88				119/316
	<u>WATER RESOURCES</u>								
1686	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	16,995.57	03/2020 11/2021	04/2022	25(O) 0	0/19
1687	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	721.37	712.37	03/2015 -	03/2021	72(O) -	5/7
1688	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	55.02	07/2021 -	07/2021	0(O) -	0/0
1689	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	254.13	.05	09/2020 -	-	-	0/0
1690	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	22.69	12/2020 06/2021	06/2021	6(O) 0	0/0
1691	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	.00	08/2021 -	12/2021	4(O) -	0/0
1692	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1693	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	225.77	263.72	03/2020 -	03/2021	12(O) -	0/0
1694	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR ,	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14(O) -	0/0
1695	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	274.08	01/2021 -	-	-	0/0
1696	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	88.45	04/2021 -	04/2021	0(O) -	0/0
1697	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR ,	05/2017	184.86 -	184.86	152.78	05/2021 -	05/2021	0(O) -	0/0
1698	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	44.97	11/2020 03/2021	03/2021	4(O) 0	0/0
1699	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	125.66	05/2021 -	05/2021	0(O) -	0/0
1700	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	.29	06/2022 -	06/2022	0(O) -	0/0
1701	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	.42	06/2022 -	06/2022	0(O) -	0/0
1702	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	665.78	149.78	12/2022 -	12/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1703	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	60.47	12/2021 -	12/2022	12(O) -	0/0
1704	REHABILITATION AND UPGADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	118.82	02/2022 -	12/2022	10(O) -	0/0
1705	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	297.33	01/2021 -	06/2021	5(O) -	0/0
1706	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1707	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	-	-	0/0
1708	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	32.47	09/2021 -	09/2021	0(O) -	0/0
1709	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH ,	03/2018	904.00 -	904.00	56.74	09/2021 -	09/2021	0(O) -	0/0
1710	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 -	213.62	.00	03/2022 -	03/2022	0(O) -	0/0
1711	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH ,	10/2016	370.40 -	370.40	361.93	08/2020 03/2021	03/2021	7(O) 0	0/0
1712	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	54.21	09/2021 -	09/2021	0(O) -	0/0
1713	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH ,	02/2017	161.31 -	161.31	50.65	11/2019 -	03/2021	16(O) -	0/0
1714	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	0(O) -	0/0
1715	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	106.27	12/2020 -	05/2021	5(O) -	0/0
1716	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 -	279.91	222.79	12/2019 -	01/2021	-	0/0
1717	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	.00	12/2021 -	12/2021	0(O) -	0/0
1718	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	21.10	10/2021 -	10/2021	0(O) -	0/0
1719	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	681.78	.00	06/2022 -	06/2022	0(O) -	0/0
1720	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 -	298.12	.00	07/2021 -	06/2022	11(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1721	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND ,	03/2017	273.37 -	273.37	71.53	08/2019 -	-	-	0/0
1722	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	77.81	11/2019 03/2021	03/2021	16(O) 0	0/0
1723	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(O) -	0/0
1724	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(O) -	0/0
1725	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(O) -	0/0
1726	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 -	198.43	.00	02/2022 -	02/2022	0(O) -	0/0
1727	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(O) -	0/0
1728	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(O) -	0/0
1729	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 -	160.00	.00	02/2022 -	02/2022	0(O) -	0/0
1730	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	.00	12/2021 -	12/2021	0(O) -	0/0
1731	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	198.28	12/2019 05/2021	05/2021	17(O) 0	0/0
1732	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	210.94	04/2020 -	03/2021	11(O) -	0/0
1733	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	.00	12/2021 -	12/2021	0(O) -	0/0
1734	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	.00	12/2021 -	12/2021	0(O) -	0/0
	Total		26,781.06 -	71,946.50	21,022.75				5/26
	<u>DEFENCE PRODUCTION</u>								
1735	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD, KARNATAKA ,	12/2016	246.31 -	246.31	115.20	02/2020 -	06/2021	16(O) -	6/10
	Total		246.31 -	246.31	115.20				6/10
	<u>COMMERCE</u>								
1736	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC, DELHI ,	06/2018	302.64 -	302.64	60.00	10/2020 -	-	-	0/0
	Total		302.64 -	302.64	60.00				0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Grand Total		22,32,019.72	26,61,205.74	12,78,270.71				2955/5799


Summary of projects in the Flash Report for the month of February, 2021

Project Implementation - Current Status:

Number of Projects in Previous Month	1739
Number of Projects completed/dropped/frozen in Current Month	18
	0
Number of Projects Added in Current Month	15
Number of Projects in Current Month	1736

Brief Analysis


Project Status with respect to Original Schedule: Out of 1736 projects, 12 projects are ahead of schedule, 247 projects are on schedule 547 projects are delayed. 815 projects do not have fixed dates of commissioning. 115 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

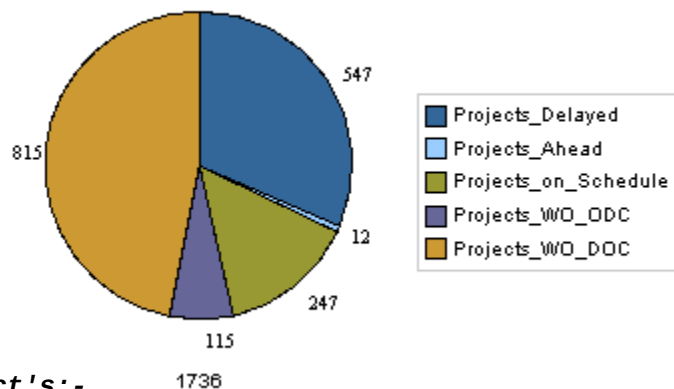

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1736 projects when sanctioned, was of the order of Rs. 2232019.72 crore but this was subsequently revised to Rs. 2661205.74 crore implying a cost overrun of 19.2%. The expenditure incurred on these projects till February, 2021 is Rs. 1278270.71 crore, which is 48% of the anticipated cost of the projects.

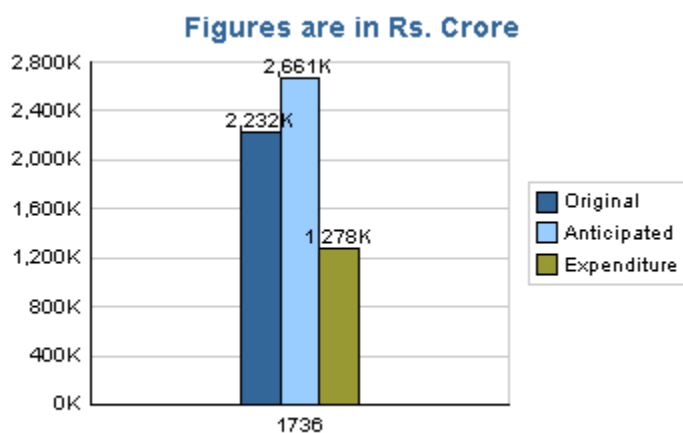

Sector wise current status of projects on the Flash Report


RURAL DEVELOPMENT

Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 3 projects are delayed.

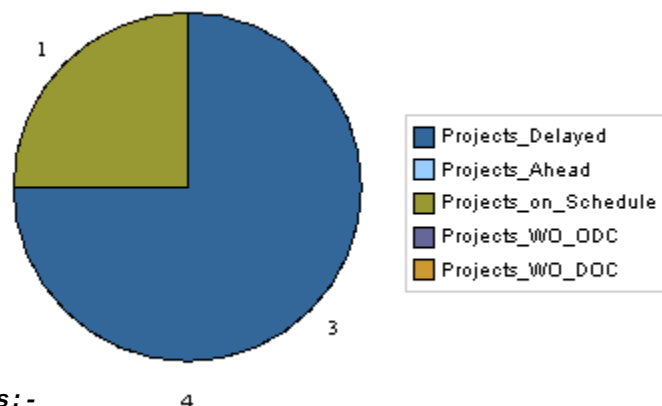


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 889.43 crore but this was subsequently anticipated to Rs. 899.87 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till February, 2021 is Rs. 472.48 crore, which is 52.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

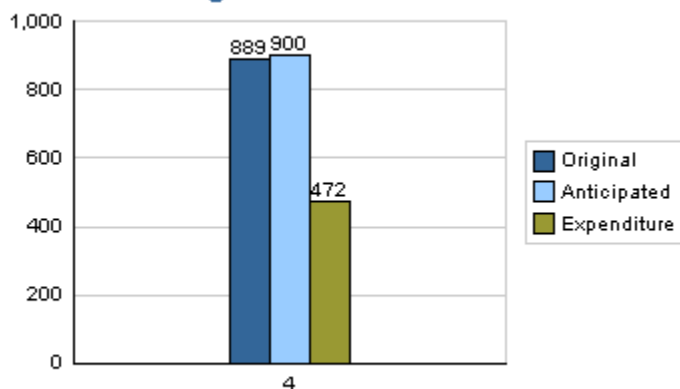

Sector wise current status of projects on the Flash Report


HOME AFFAIRS

Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule 2 projects are delayed.

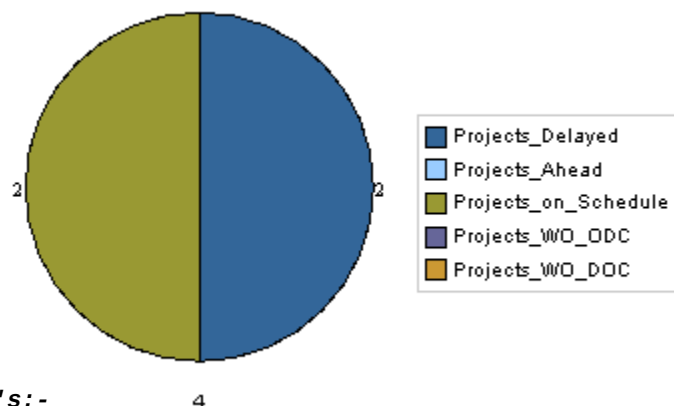


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1716.05 crore but this was subsequently anticipated to Rs. 2571.96 crore implying a cost overrun of 49.9%. The expenditure incurred on these projects till February, 2021 is Rs. 1044.88 crore, which is 40.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

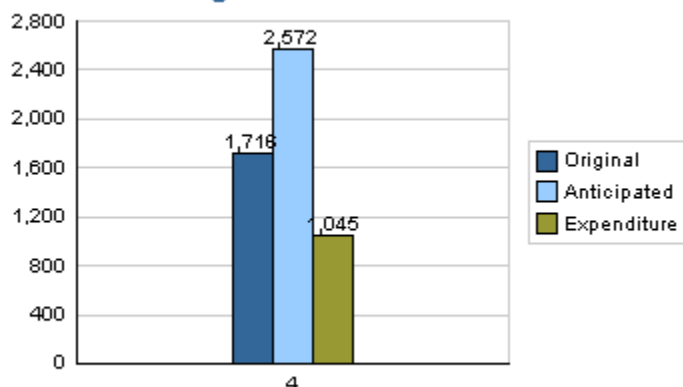

Sector wise current status of projects on the Flash Report

HUMAN RESOURCE DEVELOPMENT


Current Status:

Number of Projects	26
Number of Projects On Schedule	4
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	8
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 26 projects, 4 projects are on schedule 14 projects are delayed. 8 projects do not have fixed dates of commissioning.

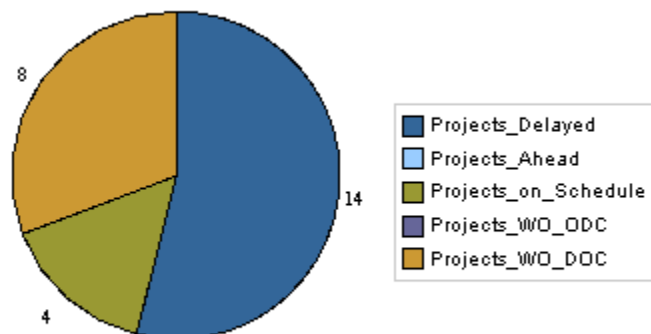


Total No Of Project's:-

26

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 11077.4 crore but this was subsequently anticipated to Rs. 11265.83 crore implying a cost overrun of 1.7%. The expenditure incurred on these projects till February, 2021 is Rs. 2413.56 crore, which is 21.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

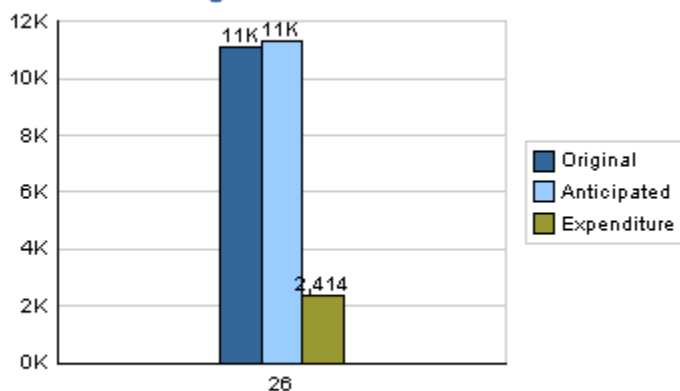

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	49
Number of Projects On Schedule	26
Number of Projects Delayed	17

Number of Projects Without Date Of Commissioning	6
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 49 projects, 26 projects are on schedule 17 projects are delayed. 6 projects do not have fixed dates of commissioning.

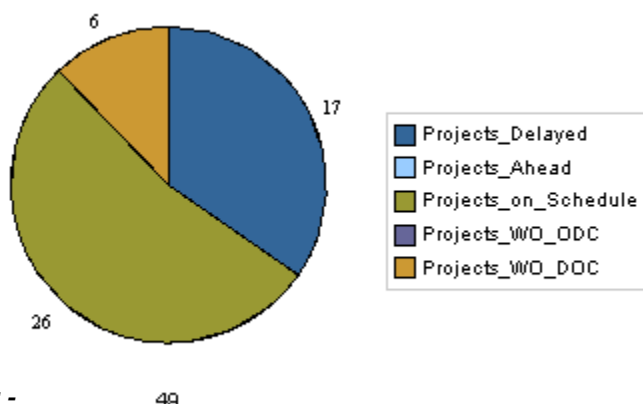


Total No Of Project's:-

49

Investment Scenario

Total original cost of implementation of 49 projects when sanctioned, was of the order of Rs. 26781.06 crore but this was subsequently anticipated to Rs. 71946.5 crore implying a cost overrun of 168.6%. The expenditure incurred on these projects till February, 2021 is Rs. 21022.75 crore, which is 29.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

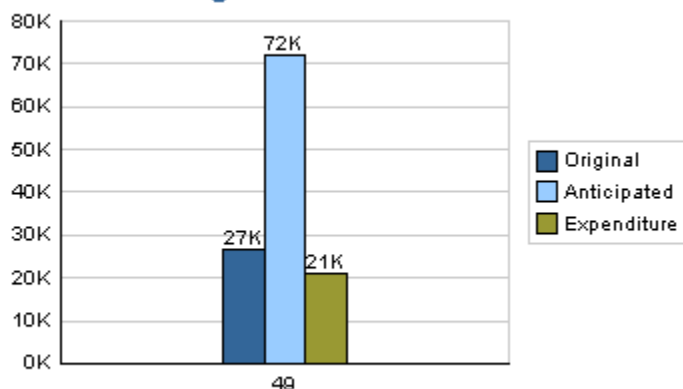

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	34
Number of Projects On Schedule	11
Number of Projects Delayed	11
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 34 projects, 11 projects are on schedule 11 projects are delayed. 11 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

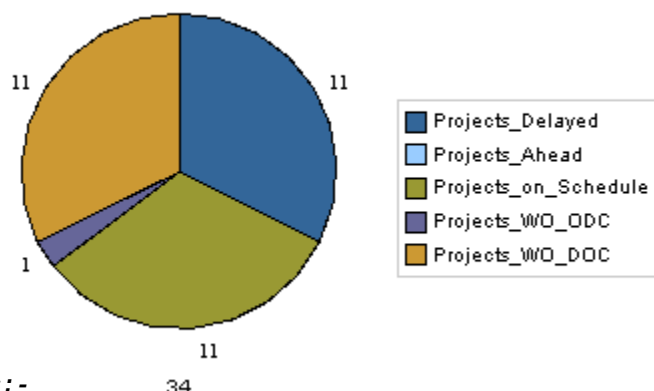


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 34 projects when sanctioned, was of the order of Rs. 282747.18 crore but this was subsequently anticipated to Rs. 301054.8 crore implying a cost overrun of 6.5%. The expenditure incurred on these projects till February, 2021 is Rs. 134498.88 crore, which is 44.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

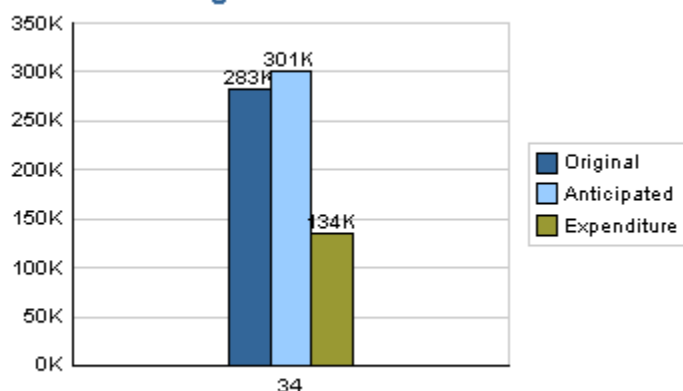

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed. 1 project does not have fixed dates of commissioning.

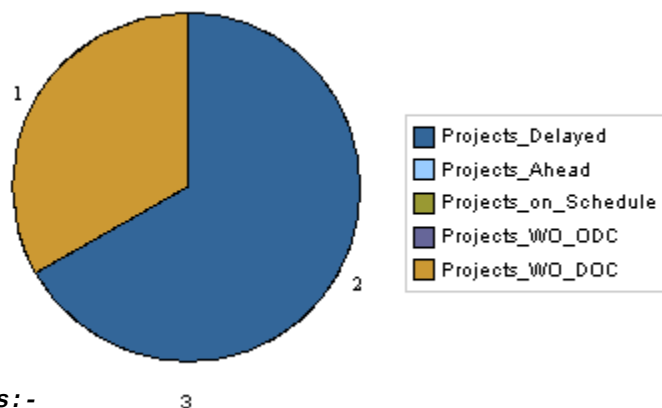


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14013.36 crore but this was subsequently anticipated to Rs. 25343.36 crore implying a cost overrun of 80.9%. The expenditure incurred on these projects till February, 2021 is Rs. 16674.1 crore, which is 65.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

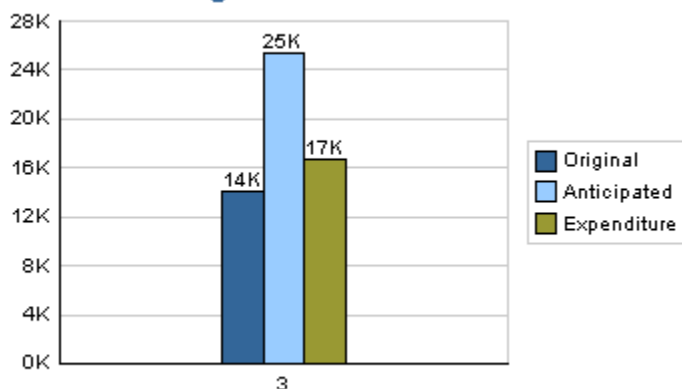

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	908
Number of Projects On Schedule	57
Number of Projects Delayed	139

Number of Projects Without Original Date of Commissioning	57
Number of Projects Without Date Of Commissioning	655

Brief Analysis

Project Status with respect to Original Schedule: Out of 908 projects, 57 projects are on schedule 139 projects are delayed. 655 projects do not have fixed dates of commissioning. 57 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

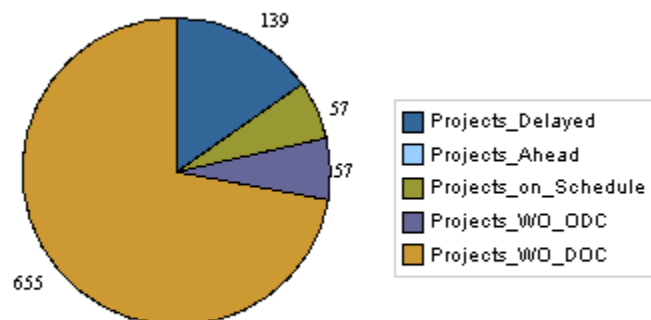


Total No Of Project's:-

908

Investment Scenario

Total original cost of implementation of 908 projects when sanctioned, was of the order of Rs. 540947.36 crore but this was subsequently anticipated to Rs. 560277.95 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till February, 2021 is Rs. 348803.37 crore, which is 62.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

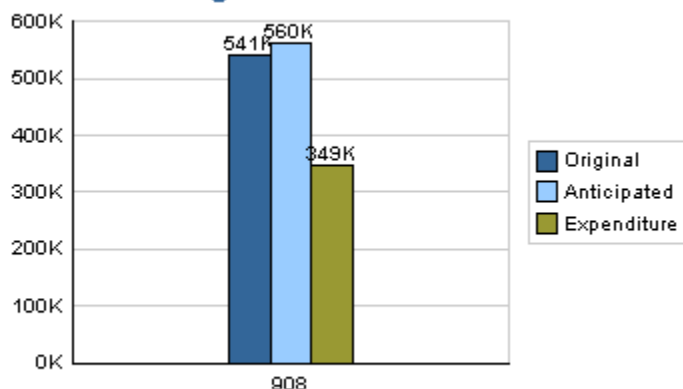

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	312
Number of Projects On Schedule	18
Number of Projects Delayed	157
Number of Projects Ahead	6
Number of Projects Without Original Date of Commissioning	49
Number of Projects Without Date Of Commissioning	82

Brief Analysis

Project Status with respect to Original Schedule: Out of 312 projects, 6 projects are ahead of schedule, 18 projects are on schedule 157 projects are delayed. 82 projects do not have fixed dates of commissioning. 49 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

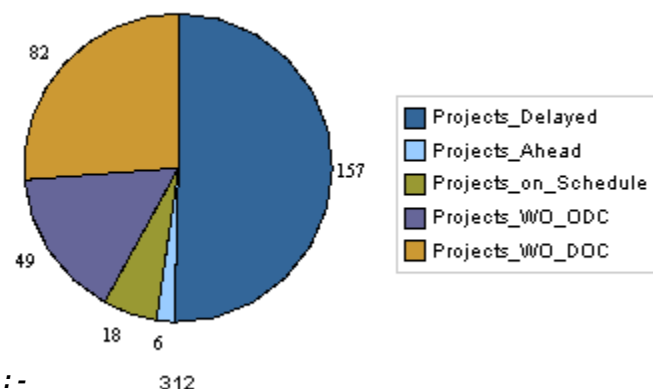


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 312 projects when sanctioned, was of the order of Rs. 462095.03 crore but this was subsequently anticipated to Rs. 698959.98 crore implying a cost overrun of 51.3%. The expenditure incurred on these projects till February, 2021 is Rs. 244559.04 crore, which is 35% of the anticipated cost of the projects.

Figures are in Rs. Crore

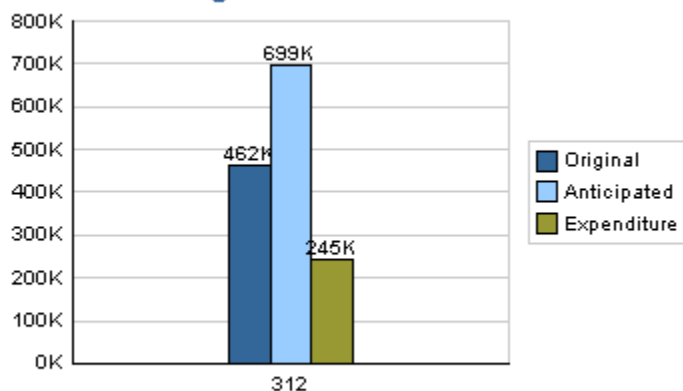

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	29
Number of Projects On Schedule	3
Number of Projects Delayed	13
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 1 project is ahead of schedule, 3 projects are on schedule 13 projects are delayed. 7 projects do not have fixed dates of commissioning. 5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

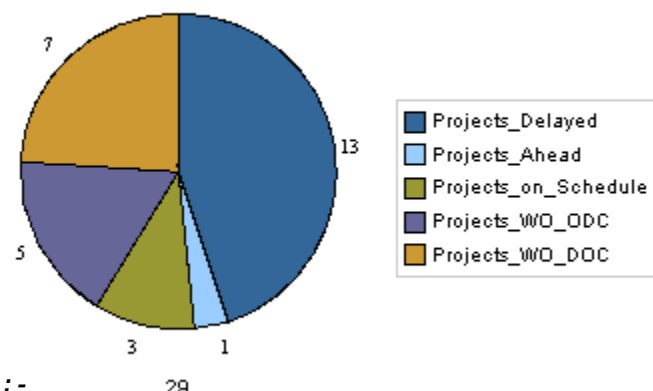


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 15273.26 crore but this was subsequently anticipated to Rs. 15594.81 crore implying a cost overrun of 2.1%. The expenditure incurred on these projects till February, 2021 is Rs. 7459.26 crore, which is 47.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

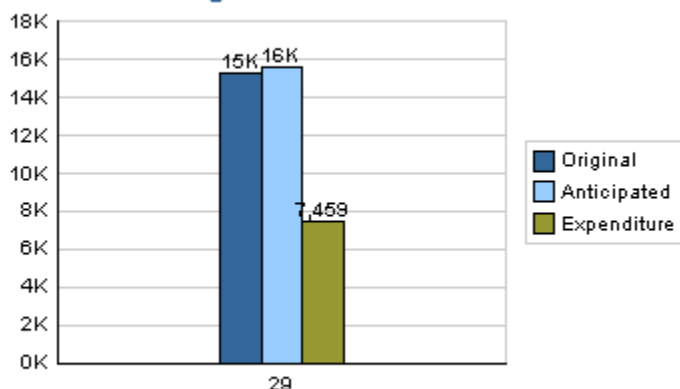

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	78
Number of Projects On Schedule	11
Number of Projects Delayed	45

Number of Projects Without Date Of Commissioning	22
--	----

Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 11 projects are on schedule 45 projects are delayed. 22 projects do not have fixed dates of commissioning.

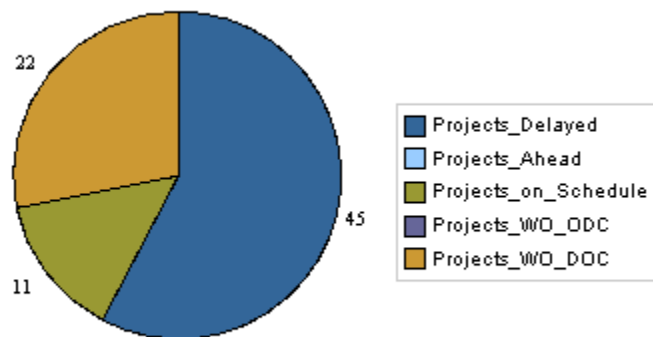


Total No Of Project's:-

78

Investment Scenario

Total original cost of implementation of 78 projects when sanctioned, was of the order of Rs. 295137.42 crore but this was subsequently anticipated to Rs. 366945.59 crore implying a cost overrun of 24.3%. The expenditure incurred on these projects till February, 2021 is Rs. 251832.37 crore, which is 68.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

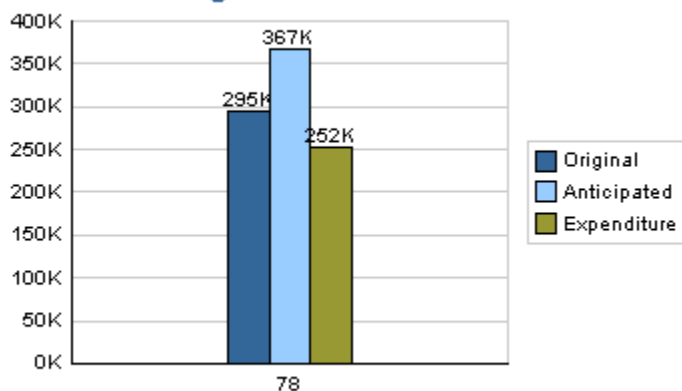

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	138
Number of Projects On Schedule	59
Number of Projects Delayed	68
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 138 projects, 5 projects are ahead of schedule, 59 projects are on schedule 68 projects are delayed. 4 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

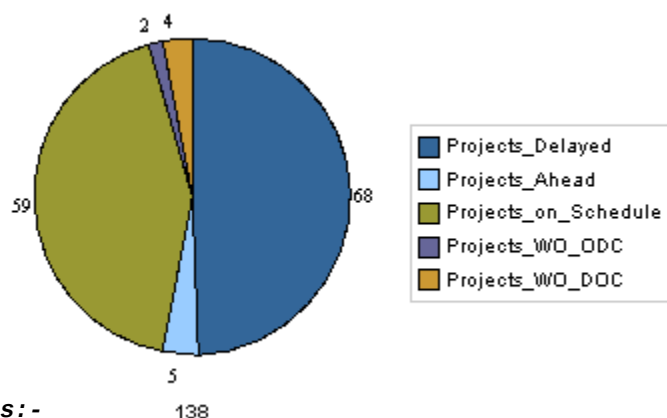


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 138 projects when sanctioned, was of the order of Rs. 295617.09 crore but this was subsequently anticipated to Rs. 302198.67 crore implying a cost overrun of 2.2%. The expenditure incurred on these projects till February, 2021 is Rs. 104628.98 crore, which is 34.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

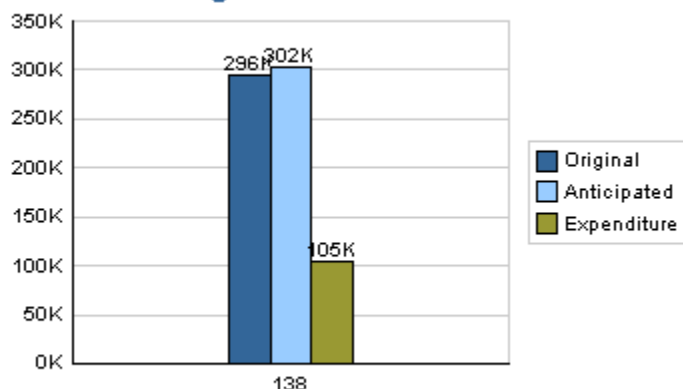

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	9
Number of Projects On Schedule	3
Number of Projects Delayed	5

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 3 projects are on schedule 5 projects are delayed. 1 project does not have fixed dates of commissioning.

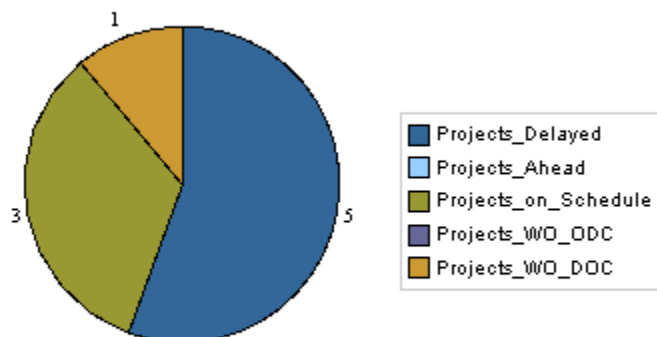


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 25452.51 crore but this was subsequently anticipated to Rs. 31567.51 crore implying a cost overrun of 24%. The expenditure incurred on these projects till February, 2021 is Rs. 22119.24 crore, which is 70.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

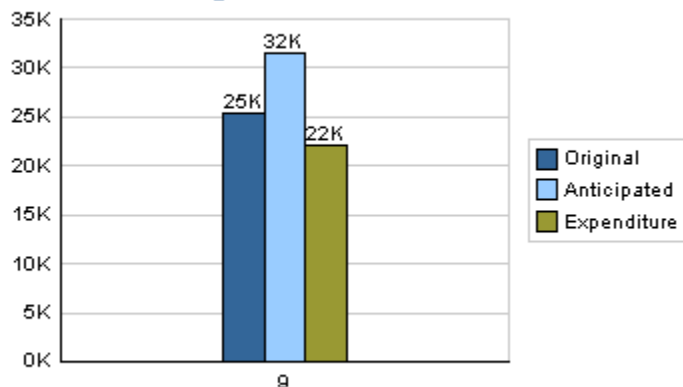

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 1 project is on schedule 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

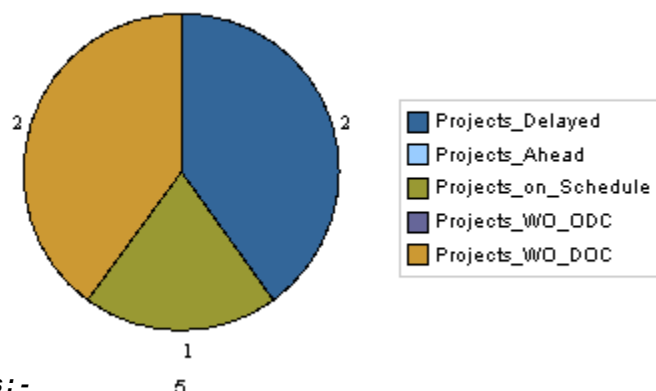


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore. The expenditure incurred on these projects till February, 2021 is Rs. 1260.44 crore, which is 17.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

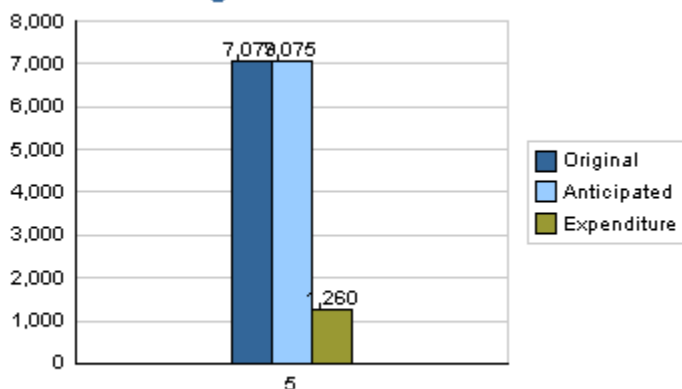

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

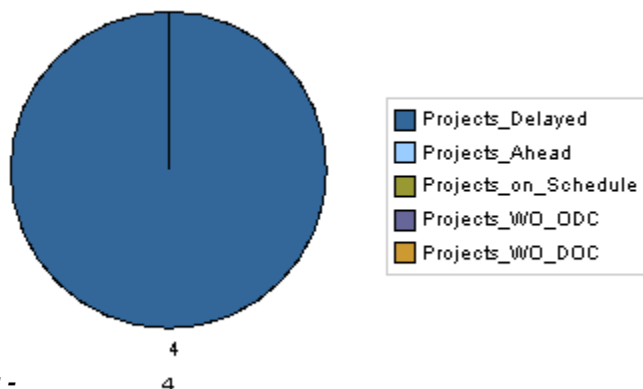

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till February, 2021 is Rs. 842.45 crore, which is 76.5% of the anticipated cost of the projects.

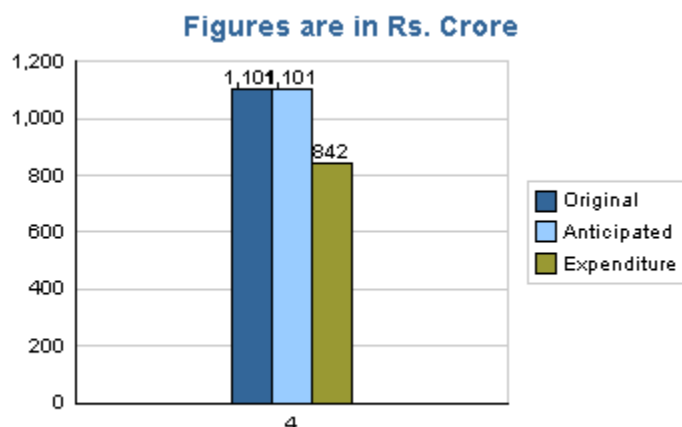

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	101
Number of Projects On Schedule	43
Number of Projects Delayed	44

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	13

Brief Analysis

Project Status with respect to Original Schedule: Out of 101 projects, 43 projects are on schedule 44 projects are delayed. 13 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

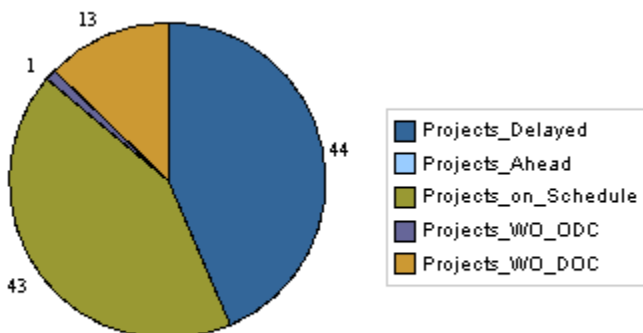


Total No Of Project's:-

101

Investment Scenario

Total original cost of implementation of 101 projects when sanctioned, was of the order of Rs. 145653.01 crore but this was subsequently anticipated to Rs. 144237.84 cr The expenditure incurred on these projects till February, 2021 is Rs. 45301.73 crore, which is 31.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

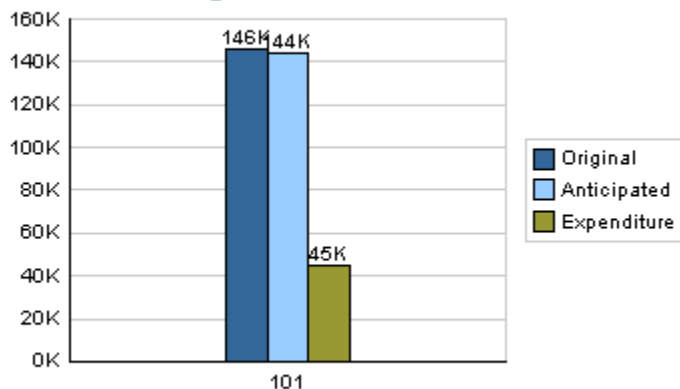

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	19
Number of Projects On Schedule	6
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 6 projects are on schedule 12 projects are delayed. 1 project does not have fixed dates of commissioning.

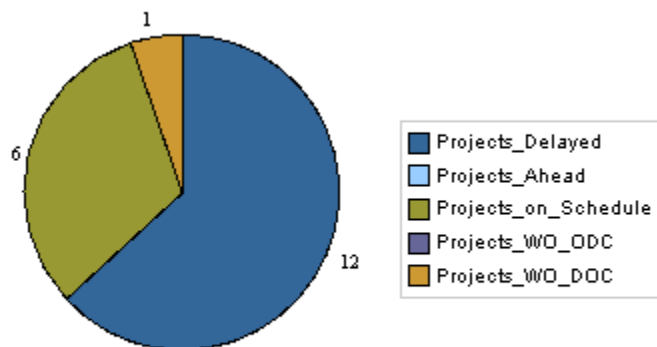


Total No Of Project's:-

19

Investment Scenario

Total original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 13786.34 crore but this was subsequently anticipated to Rs. 14034.5 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till February, 2021 is Rs. 2597.3 crore, which is 18.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

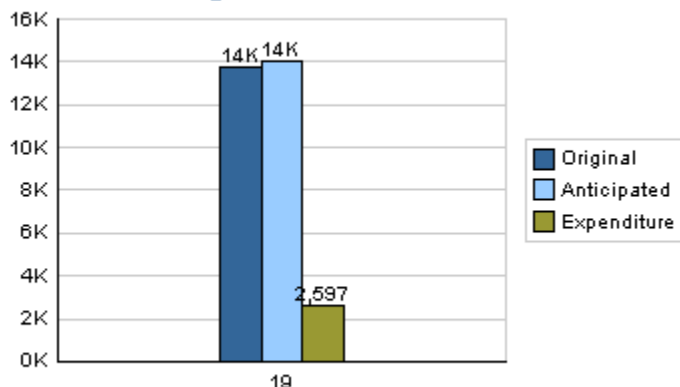

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

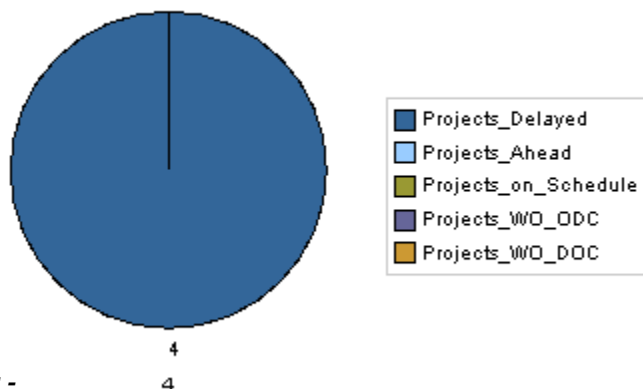

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till February, 2021 is Rs. 58335.8 crore, which is 72.6% of the anticipated cost of the projects.

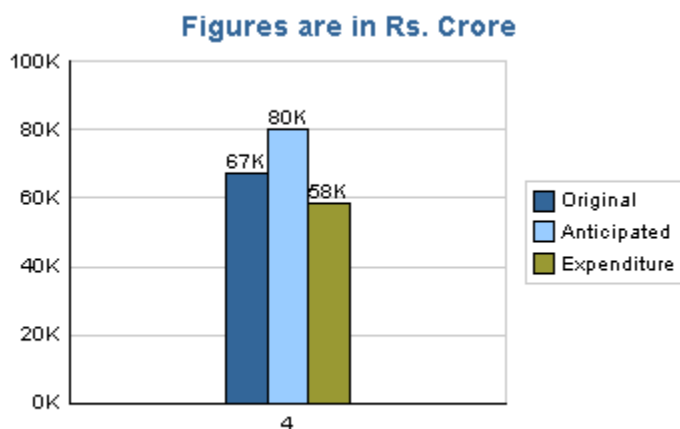

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (FEBRUARY 2021)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	2,893.59	816.45
2	ANDHRA PRADESH	78	1,23,127.88	1,70,658.55	73,361.08
3	ARUNACHAL PRADESH	42	24,624.65	44,255.46	26,876.75
4	ASSAM	47	42,046.33	45,719.63	14,197.94
5	BIHAR	109	1,23,051.26	1,59,414.14	74,567.97
6	CHANDIGARH	2	349.15	570	270.91
7	CHHATISGARH	48	91,239.04	1,02,416.44	53,713.88
8	DELHI	35	90,445.77	91,842.87	55,571.92
9	GOA	11	5,629.77	5,640.26	2,593.94
10	GUJARAT	58	1,04,455.6	1,15,668.59	55,837.26
11	HARYANA	43	30,316.35	32,837.14	18,650.17
12	HIMACHAL PRADESH	15	20,365.24	30,249.67	17,299.27
13	JAMMU AND KASHMIR	22	40,412.13	66,473.44	41,654.34
14	JHARKHAND	42	70,673.4	69,045.14	32,735.2
15	KARNATAKA	60	71,320.53	76,413.21	41,346.74
16	KERALA	22	37,466.85	42,063.18	18,880.73
17	MADHYA PRADESH	84	91,161.4	1,04,937.48	54,575.27
18	MAHARASHTRA	241	2,16,637.38	2,39,566.06	1,29,253.38
19	MANIPUR	12	8,137.49	15,887.67	11,268.12
20	MEGHALAYA	7	3,245.09	6,563.59	1,560.31
21	MIZORAM	18	9,030.03	12,978.73	6,030.14
22	MULTI STATE	128	3,66,425.54	4,80,969.26	1,85,534.67
23	NAGALAND	38	18,265.97	22,463.91	4,123.23
24	ODISHA	89	1,29,891.78	1,34,147.04	55,242.13
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	29	15,325.05	18,249.98	10,916.08
27	RAJASTHAN	60	53,090.5	61,077.72	38,856.69
28	SIKKIM	14	5,074.99	12,481.74	1,885.47
29	TAMIL NADU	71	1,19,185.26	1,38,236.09	79,929
30	TELANGANA	47	36,326.25	38,960.97	19,087.09
31	TRIPURA	13	3,479.87	3,662.68	1,469.03
32	UTTAR PRADESH	134	1,78,012.58	1,85,558.75	90,665.55
33	UTTARAKHAND	32	34,539.29	46,026.02	15,018.9
34	WEST BENGAL	75	65,583.67	83,081.74	44,464.69
TOTAL		1,736	22,32,019.72	26,61,205.74	12,78,270.71

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
1	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	-	09/2025	05/2024
	Total		1,828.00	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
2	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00	2,433.00	2,018.90	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
3	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26	249.26	121.72	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
4	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00	315.00	196.27	12/2021	06/2021
5	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	1,793.18	09/2022	03/2022
6	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00	1,378.00	21.66	12/2022	09/2022
	Total		8,087.26	8,071.26	4,151.73		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
7	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63	808.63	639.30	01/2018 04/2021	03/2021
8	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37	14,733.37	11,441.18	11/2019 04/2021	03/2021
	Total		15,542.00	15,542.00	12,080.48		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
9	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,204.21	03/2024	03/2023
	<u>North East Frontier Railway</u>						
10	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27	760.00	801.53	12/2021	04/2021
	<u>North Western Railway</u>						

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
11	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	167.74	08/2022 -	06/2022
	<u>Rail Vikas Nigam Ltd.</u>						
12	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	875.99	12/2026 -	12/2025
13	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00	3,000.00	2,181.62	03/2023 -	12/2022
14	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	.19	12/2025 -	03/2025
	<u>South Central Railway</u>						
15	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	521.91	03/2020 03/2022	06/2021
	<u>Southern Railway</u>						
16	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	600.30	355.13	- 10/2021	09/2021
	Total		11,725.08 -	17,201.76	6,108.32		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
17	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]	3/2018	289.67 -	289.67	177.78	08/2018 06/2021	02/2021
18	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09 -	995.09	476.77	05/2016 08/2021	04/2021
	<u>National Highways Authority Of India</u>						
19	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	2,499.00	1,539.65	03/2021 10/2021	04/2021
	Total		2,817.38 -	3,783.76	2,194.20		
	Grand Total		39,999.72	46,426.78	24,534.73		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24 -	412.24	-	06/2021 -	06/2021
2	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	-	05/2022 -	05/2022
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	51.11	09/2021 -	09/2021
4	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	-	03/2023 -	03/2023
5	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	475.39 -	475.39	88.11	04/2021 -	04/2021
	Total		3,416.21 -	3,550.27	261.41		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.54	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
8	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	238.83	03/2023 -	03/2023
9	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
10	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	0.50	03/2027 -	03/2027
11	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	163.16	03/2022 -	03/2022
12	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	-	03/2025 -	03/2025
13	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.39	03/2026 -	03/2026
14	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	97.54	03/2024 -	03/2024
15	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	0.03	03/2027 -	03/2027
16	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	10.11	03/2029 -	03/2029
	<u>Mahanadi Coal Fields Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
17	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029
18	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027
19	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026
	<u>Northern Coal Fields Limited</u>						
20	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
21	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
22	NIGAHI EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
23	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
	<u>South-Eastern Coal Fields Limited</u>						
24	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.40	03/2021 -	03/2021
25	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	9.71	03/2023 -	03/2023
26	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
27	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	0.85	03/2022 -	03/2022
28	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	-	03/2029 -	03/2029
29	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	4,219.60	03/2023 03/2016	03/2023
30	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	8.28	03/2023 -	03/2023
31	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	142.84	03/2022 -	03/2022
32	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
33	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	24.44	03/2026 -	03/2026
34	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
35	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
36	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	-	03/2029 -	03/2029
37	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	-	03/2024 -	03/2024
38	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,587.18	03/2023 -	03/2023
39	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.95	03/2026 -	03/2026
	<u>Western Coal Fields Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
40	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
41	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	0.87	03/2026 -	03/2026
42	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	211.41	03/2021 -	03/2021
43	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	274.95	03/2021 -	03/2021
44	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	99.77	03/2021 -	03/2021
45	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	7/2016	281.25 -	409.87	20.99	03/2022 -	03/2022
46	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	85.82	03/2023 -	03/2023
47	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	251.34	03/2021 -	03/2021
48	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	226.81	03/2022 -	03/2022
49	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	281.92	03/2025 -	03/2025
	Total		60,434.16 -	60,784.52	12,647.06		
	<u>FINANCE</u>						
	<u>Central Public Works Department</u>						
50	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	113.99	11/2021 -	11/2021
	Total		348.77 -	348.77	113.99		
	<u>HEALTH AND FAMILY WELFARE</u>						
51	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	124.80	09/2023 -	09/2023
52	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
53	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	648.37	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	773.17		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
54	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	0.29	05/2022 -	05/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
55	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE - - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
	Total		333.96 -	333.96	.29		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
56	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	35.88	06/2022 -	06/2022
57	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
58	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
59	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
	Total		2,206.13 -	2,206.13	93.30		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
60	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	0.74	04/2021 04/2021	04/2021
	Total		483.00 -	483.00	.74		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
61	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	73.00	06/2022 -	06/2022
62	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	302.82	03/2023 -	03/2023
63	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	688.49	12/2021 -	12/2021
64	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	189.36	08/2022 -	08/2022
65	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	96.63	03/2021 -	03/2021
66	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	297.39	12/2021 -	12/2021
	<u>Gas Authority Of India Limited</u>						
67	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	94.56	10/2022 -	10/2022
68	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	32.60	11/2022 -	11/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
69	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	76.84	10/2022 -	10/2022
70	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]	8/2018	217.92 -	217.92	76.80	04/2021 -	04/2021
71	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	196.18	04/2022 -	04/2022
72	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	98.03	07/2022 -	07/2022
73	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	837.00	05/2023 -	05/2023
74	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	132.60	10/2022 -	10/2022
75	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	205.30	07/2022 -	07/2022
76	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	74.18	07/2022 -	07/2022
77	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,096.40	12/2021 -	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
78	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	185.40	11/2021 -	11/2021
79	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	91.57	09/2026 -	09/2026
80	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	14.63	03/2031 -	03/2031
81	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	103.91	11/2022 -	11/2022
82	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	-	08/2021 -	08/2021
83	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	-	11/2022 -	11/2022
84	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	763.33	06/2022 -	06/2022
85	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	131.02	12/2022 -	12/2022
86	220 KV GRID SUPPLY - [N16000407]	10/2020	303.40 -	303.40	-	03/2021 -	03/2021
87	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	153.20	03/2029 -	03/2029
88	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,244.50	54.49	02/2023 -	02/2023
	<u>Indian Oil Corporation Limited</u>						
89	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,561.15	10/2021 -	10/2021
90	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	77.55	01/2024 -	01/2024
91	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	54.61	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
92	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00 -	18,936.00	-	09/2024 -	09/2024
93	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	125.61	11/2021 -	11/2021
94	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	1.73	07/2022 -	07/2022
95	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00 -	1,398.00	75.59	12/2023 -	12/2023
96	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	1,568.98	08/2021 -	08/2021
97	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	6.63	09/2021 -	09/2021
98	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	65.53	10/2021 -	10/2021
99	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	722.25	04/2023 -	04/2023
100	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	13.16	07/2021 -	07/2021
101	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	151.68	10/2021 -	10/2021
102	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	398.94	08/2022 -	08/2022
103	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	1.93	09/2022 -	09/2022
104	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	55.17	01/2023 -	01/2023
105	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00 -	921.00	3.05	09/2023 -	09/2023
106	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	84.15	05/2023 -	05/2023
107	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	8.49	07/2022 -	07/2022
108	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	429.94	12/2022 -	12/2022
109	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,468.42	02/2022 -	02/2022
110	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	1.76	08/2022 -	08/2022
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
111	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	1.46	06/2023 -	06/2023
	<u>Numaligarh Refinery Limited</u>						
112	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024
113	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Oil & Natural Gas Corporation Limited</u>						
114	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	773.52	03/2026 -	03/2026
115	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	1,565.69	05/2021 -	05/2021
116	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	79.65	08/2022 -	08/2022
117	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	2,305.03	05/2021 -	05/2021
118	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,238.26	03/2022 -	03/2022
119	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	3,596.00	3,494.45	05/2021 05/2021	05/2021
	Total		1,59,066.99 -	1,57,947.23	24,686.27		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
120	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71 -	1,522.71	-	09/2021 -	09/2021
121	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	261.80	-	10/2021 -	10/2021
122	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	-	09/2021 -	09/2021
123	JETSAR SOLAR 160 MW - [N18000287]	12/2019	702.28 -	702.28	-	03/2021 -	03/2021
124	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]	3/2020	1,782.00 -	1,782.00	-	09/2021 -	09/2021
125	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	-	09/2021 -	09/2021
126	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	-	04/2021 -	04/2021
127	KAYAMKULAM SOLAR 70 MW - [N18000288]	9/2019	403.62 -	403.62	-	06/2021 -	06/2021
	<u>SatluJ Jal Vidyut Nigam Limited</u>						
128	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	1,479.16	01/2024 -	01/2024
129	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	524.12	12/2021 -	12/2021
130	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	286.90	01/2026 -	01/2026
	Total		21,037.82 -	21,037.82	2,290.18		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
131	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
132	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023
133	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
134	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023
135	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>North Central Railway</u>						
136	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021
137	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
138	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	4,083.02	263.68	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
139	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	112.02	12/2021 -	12/2021
140	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
141	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	929.79	03/2022 -	03/2022
	<u>National High Speed Rail Corporation Limited</u>						
142	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	11,158.98	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
143	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	535.71	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
144	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023
145	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
146	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,438.76	12/2021 -	12/2021
147	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021
148	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	705.50	12/2024 -	12/2024
	Total		1,47,147.85 -	1,55,917.22	21,533.15		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
149	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	137.87	06/2021 -	06/2021
150	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	197.67	5.75	12/2022 -	12/2022
151	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]	3/2018	351.00 -	351.00	109.64	06/2021 -	06/2021
152	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021
153	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]	3/2020	370.36 -	370.36	90.45	08/2022 -	08/2022
154	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	78.54	03/2021 -	03/2021
155	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH - [N24001180]	3/2019	237.51 -	237.51	50.27	12/2022 -	12/2022
156	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	70.46	09/2021 -	09/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
157	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR- SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	29.22	12/2023 -	12/2023
158	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]	8/2020	278.46 -	278.46	-	03/2022 -	03/2022
159	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]	3/2020	292.24 -	292.24	8.60	06/2022 -	06/2022
160	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	-	05/2022 -	05/2022
161	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]	6/2020	365.53 -	365.53	14.15	08/2022 -	08/2022
162	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	-	07/2022 -	07/2022
163	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]	3/2020	178.43 -	178.43	-	07/2022 -	07/2022
164	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	-	04/2022 -	04/2022
165	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	-	04/2022 -	04/2022
166	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4- LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
167	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244	8/2020	301.06 -	301.06	-	04/2022 -	04/2022
168	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001261	8/2020	311.00 -	311.00	-	04/2023 -	04/2023
169	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260	9/2020	257.15 -	257.15	5.29	04/2022 -	04/2022
170	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	-	06/2022 -	06/2022
171	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAPOKPI TO SEKMAI SECTI - [N24001276	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
172	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	101.20	07/2022 -	07/2022
173	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	-	10/2022 -	10/2022
174	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	-	12/2022 -	12/2022
175	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280	3/2020	320.97 -	320.97	8.86	06/2022 -	06/2022
176	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	41.64	06/2022 -	06/2022
177	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285	3/2020	330.78 -	330.78	11.24	12/2021 -	12/2021
178	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265	3/2020	154.51 -	154.51	-	07/2022 -	07/2022
179	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282	3/2020	355.79 -	355.79	12.99	06/2022 -	06/2022
180	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279	3/2020	216.49 -	216.49	-	07/2022 -	07/2022
181	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	12.40	03/2022 -	03/2022
182	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283	3/2020	281.78 -	281.78	-	07/2022 -	07/2022
183	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247	3/2020	247.76 -	247.76	-	01/2022 -	01/2022
184	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001262	7/2020	345.38 -	345.38	-	04/2023 -	04/2023
185	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	18.22	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
186	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288	8/2020	232.29 -	232.29	-	04/2022 -	04/2022
187	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277	9/2020	275.02 -	275.02	4.72	10/2022 -	10/2022
188	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	-	04/2022 -	04/2022
189	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	38.33	09/2026 -	09/2026
190	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273	7/2020	177.76 -	177.76	17.84	08/2022 -	08/2022
191	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249	6/2020	347.36 -	347.36	-	01/2022 -	01/2022
192	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284	3/2020	361.53 -	361.53	3.66	06/2022 -	06/2022
193	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251	3/2019	402.94 -	402.94	0.78	04/2022 -	04/2022
194	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	-	04/2023 -	04/2023
195	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274	8/2020	379.39 -	379.39	-	04/2022 -	04/2022
196	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287	4/2020	330.80 -	330.80	1.50	12/2021 -	12/2021
197	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257	8/2020	159.85 -	159.85	-	10/2022 -	10/2022
198	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	9/2020	315.63 -	315.63	-	04/2022 -	04/2022
199	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263	6/2020	277.50 -	277.50	-	01/2022 -	01/2022
200	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
201	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281	3/2020	292.24 -	292.24	-	07/2022 -	07/2022
	<u>National Highways Authority Of India</u>						
202	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 -	1,226.88	-	02/2021 -	02/2021
203	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
204	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
205	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301	11/2019	1,601.10 -	1,601.10	-	02/2021 -	02/2021
	Total		30,857.66 -	30,857.66	921.57		
	<u>RURAL DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
206	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021
	Total		361.60 -	361.60	12.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
207	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,814.28	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,814.28		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
208	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124	11/2015	2,907.00 -	2,907.00	185.08	06/2023 -	06/2023
	<u>Steel Authority Of India Limited (Sail)</u>						
209	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	17.50	12/2023 -	12/2023
210	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	0.63	05/2023 -	05/2023
	Total		3,826.42 -	3,826.42	203.21		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
211	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	16.58	03/2024 -	03/2024
212	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	56.76	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
213	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022
	<u>Delhi Metro Rail Corporation</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
214	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	1,248.28	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
215	KANPUR METRO RAIL PROJECT - [N28000144]	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
216	AGRA METRO RAIL PROJECT - [N28000145]	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
217	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	5,696.05	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
218	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	126.50	02/2023 -	02/2023
219	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	117.53	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
220	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	2,987.00	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
221	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,365.77	231.90	06/2024 -	06/2024
	Total		1,32,439.21 -	1,32,439.21	10,502.60		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
222	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	0.42	06/2022 -	06/2022
223	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	88.45	04/2021 -	04/2021
224	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	125.66	05/2021 -	05/2021
225	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
226	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	0.29	06/2022 -	06/2022
227	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	152.78	05/2021 -	05/2021
228	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	55.02	07/2021 -	07/2021
	<u>Delhi Jal Board</u>						
229	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	149.78	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
230	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
231	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
232	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
233	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
234	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
235	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
236	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
237	INTERCEPTION AND DIVERSION WITH STP AT HUGHLI-CHINSURAH - [N30000042]	5/2018	160.00 -	160.00	-	02/2022 -	02/2022
238	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
239	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	5/2018	198.43 -	198.43	-	02/2022 -	02/2022
	<u>Uttar Pradesh Jal Nigam</u>						
240	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
241	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
242	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	681.78	-	06/2022 -	06/2022
243	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23 -	967.23	54.21	09/2021 -	09/2021
244	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00 -	904.00	56.74	09/2021 -	09/2021
245	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	213.62	-	03/2022 -	03/2022
246	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	21.10	10/2021 -	10/2021
247	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	32.47	09/2021 -	09/2021
	Total		9,914.61 -	9,916.85	736.92		
	Grand Total		5,81,575.57	5,89,347.47	76,590.58		

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044] BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,915.80	09/2010 09/2016	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010] NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	16,297.00	12/2015 -	02/2022	74	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027] NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	12,992.00	12/2016 -	03/2023	75	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028] NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	23,131.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	58,335.80					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076] AAI, DELHI	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13	0	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073] AAI, A & N ISLANDS	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	33	5.78	
7	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080] AAI, WEST BENGAL	01/2016	458.00 -	458.00	105.12	03/2020 -	06/2021	15	0	
8	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089] AAI, ANDHRA PRADESH	08/2017	177.10 -	177.10	-	02/2020 -	06/2021	16	0	
9	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085] AAI, UTTARAKHAND	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5	0	
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	12	7.88	
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7	0	
13	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12	0	
14	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	389.71	37.38	11/2021 -	10/2022	11	0	
15	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	1,405.00	-	08/2022 -	03/2023	7	0	
16	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	-	03/2022 -	03/2023	12	0	
	Total		9,931.85 -	10,045.95	2,000.31					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
17	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	280.46	05/2014 -	06/2021	85	0	
18	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	30.15	03/2017 -	10/2021	55	12.2	
19	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	18.35	04/2018 -	12/2021	44	37.56	
20	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	457.98	04/2015 -	03/2022	83	0	
21	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	20.22	04/2014 -	04/2023	108	0	
	<u>Central Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
22	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.63	03/2011 -	03/2022	132	0	
23	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	401.87	03/2016 -	03/2022	72	0	
24	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	96.86	03/2014 -	03/2022	96	0	
25	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND	02/2012	4,983.58 5,136.15	4,983.58	244.12	03/2020 03/2024	03/2024	48	0	
26	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND	08/2008	6,964.33 7,254.37	706.40	639.01	07/2012 03/2025	03/2025	152	-89.86	
	<u>Eastern Coal Fields Limited</u>									
27	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	641.54	03/2018 -	03/2021	36	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2.Expediting the work of tree felling for hand over of 32.65 Ha forest land.
28	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL,WEST BENGAL	11/2015	1,210.12 -	1,210.12	20.92	03/2022 03/2029	03/2029	84	0	
	<u>Mahanadi Coal Fields Limited</u>									
29	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	168.13	03/2012 -	03/2021	108	0	
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108	0	
31	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60	0	
32	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36	0	
33	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL,ODISHA	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028	180	0	
34	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL,ODISHA	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029	228	0	
35	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168	0	
	<u>Neyveli Lignite Corporation</u>									
36	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	7,980.79	7,404.29	12/2015 -	02/2021	62	35.1	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
37	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	11,135.69	11/2021 07/2022	07/2022	8	0	
38	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	32.27	08/2022 -	09/2023	13	0	
	<u>Northern Coal Fields Limited</u>									
39	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	558.53	03/2021 -	03/2022	12	0	
40	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	144.51	03/2022 -	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
41	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	193.33	03/2016 -	03/2021	60	-3.5	
42	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	129.58	03/2015 -	03/2022	84	-32.3	
43	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	292.49	03/2015 -	03/2022	84	114.6	
44	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	21.17	03/2015 -	03/2022	84	5.85	
45	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	124.04	07/2016 -	03/2022	68	-7.91	
46	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	106.68	03/2019 -	03/2022	36	11.42	
47	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	169.95	03/2019 -	03/2022	36	0	
48	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	16.86	
	<u>South-Eastern Coal Fields Limited</u>									
49	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.32	03/2014 -	03/2021	84	0	
50	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	187.31	03/2015 03/2020	03/2022	84	201.44	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
51	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	4.43	03/2014 -	03/2022	96	0	
52	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	120.77	03/2021 -	03/2022	12	0	
53	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	0	
54	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	124.35	03/2020 -	03/2023	36	0	
55	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	60.14	03/2021 -	03/2024	36	0	
	<u>Western Coal Fields Limited</u>									
56	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	12	15.41	
57	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	141.08	03/2021 -	03/2024	36	0	
58	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	36	0	
59	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 -	851.60	194.28	03/2020 -	03/2026	72	0	
60	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA	11/2014	1,184.33 -	1,184.33	368.56	03/2020 -	03/2027	84	0	
	Total		71,443.37 -	67,942.20	28,842.61					
	<u>FINANCE</u>									
	<u>Central Public Works Department</u>									
61	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	208.96	205.40	10/2019 -	04/2021	18	-0.2	
	Total		209.00 -	208.96	205.40					
	<u>FERTILISERS</u>									
	<u>National Fertiliser Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
62	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	218.83	174.61	11/2019 -	02/2021	15	0	
63	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	166.34	11/2019 -	03/2021	16	0	
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	239.81	185.55	11/2019 -	03/2021	16	0	
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
65	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72 -	426.72	315.95	04/2020 03/2021	04/2021	12	0	
	Total		1,101.28 -	1,101.28	842.45					
	<u>MINES</u>									
	<u>National Aluminum Company Limited (Nalco)</u>									
66	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	355.00	93.85	11/2020 -	02/2021	3	0	
67	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	5,540.00 6,435.90	5,540.00	698.73	04/2021 12/2022	12/2022	20	0	
	Total		5,895.00 -	5,895.00	792.58					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
68	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	17,691.25	05/2015 07/2021	07/2021	74	41.32	
	<u>Rastriya Ispat Nigam Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
69	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,552.60	09/2018 03/2021	03/2021	30	0	No
	<u>Steel Authority Of India Limited (SAIL)</u>									
70	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	172.15	06/2019 05/2021	05/2021	23	0	
71	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL	12/2018	263.36 -	263.36	177.74	09/2020 03/2021	05/2021	8	0	
72	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	513.54	10/2017 12/2021	12/2021	50	0	
	Total		18,768.09 -	25,183.09	20,107.28					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
73	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	5,245.96	4,852.63	08/2018 11/2019	03/2021	31	14.33	
74	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	449.58	365.05	12/2019 03/2021	03/2021	15	0	
75	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	3,288.96	2,726.00	02/2020 03/2021	03/2021	13	-73	
76	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA	08/2016	282.64 -	282.64	241.79	08/2020 -	03/2021	7	0	
77	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	151.16	02/2021 -	03/2021	1	0	
78	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	711.00	06/2019 -	02/2022	32	35.54	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
79	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	17.80	02/2017 08/2022	08/2022	66	117.11	
	<u>Chennai Petroleum Corporation Limited</u>									
80	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13	-28.74	
	<u>Gas Authority Of India Limited</u>									
81	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	187.00	04/2018 -	04/2021	36	-38.98	
82	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,556.70	12/2020 -	05/2021	5	-30.59	
83	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	166.90	08/2020 05/2021	05/2021	9	14.17	
84	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00 -	2,433.00	2,018.90	12/2020 12/2021	06/2021	6	0	
85	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 -	1,933.00	1,231.50	12/2020 12/2021	12/2021	12	0	
86	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00 3,048.00	3,048.00	1,718.70	12/2020 12/2021	12/2021	12	-11.32	
87	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	778.20	12/2020 12/2021	12/2021	12	0	
88	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	225.54	39.50	02/2021 -	12/2021	10	0	
89	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,483.60	12/2012 02/2022	02/2022	110	102.71	
	<u>Hindustan Petroleum Corporation Limited</u>									
90	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA	11/2017	255.00 300.00	300.00	253.92	11/2020 06/2021	06/2021	7	17.65	
91	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	84.63	07/2020 -	07/2021	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
92	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	121.72	06/2020 12/2021	09/2021	15	0	
93	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	67.53	06/2020 09/2021	09/2021	15	0	
94	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	13,352.70	07/2020 07/2022	07/2022	24	25.5	
95	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 3,072.00	3,072.00	1,825.04	06/2021 08/2022	08/2022	14	14.76	
	<u>Indian Oil Corporation Limited</u>									
96	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	138.76	01/2021 -	04/2021	3	0	
97	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	147.12	01/2021 -	04/2021	3	0	
98	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	508.53	07/2018 02/2021	05/2021	34	0	
99	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	3,338.00	2,750.24	12/2020 -	06/2021	6	43.82	
100	DEVELOPMENT OF FACILITIES AT MOINARABAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	502.00	403.62	08/2019 06/2021	06/2021	22	18.68	
101	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	85.89	02/2020 06/2021	06/2021	16	0	
102	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	126.15	01/2021 06/2021	06/2021	5	0	
103	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	471.42	02/2020 06/2021	06/2021	16	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
104	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342] IOCL, ANDHRA PRADESH	08/2018	466.00 -	466.00	232.67	04/2021 -	07/2021	3	0	
105	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193] IOCL, MULTI STATE	01/2015	1,823.00 -	3,027.90	1,755.66	03/2021 -	08/2021	5	66.09	
106	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305] IOCL, TAMIL NADU	12/2017	466.43 -	466.43	185.01	10/2020 -	08/2021	10	0	
107	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321] IOCL, HARYANA	04/2018	206.63 -	206.63	75.17	02/2020 08/2021	08/2021	18	0	
108	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304] IOCL, MADHYA PRADESH	08/2017	236.00 293.00	293.00	162.96	06/2020 09/2021	09/2021	15	24.15	
109	LPG BP PROJECT MOTIHARI - [N16000317] IOCL, BIHAR	05/2018	206.50 -	206.50	115.92	03/2021 09/2021	09/2021	6	0	
110	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268] IOCL, MAHARASHTRA	05/2016	348.00 -	348.00	132.88	01/2021 -	10/2021	9	0	
111	KHARAGPUR LPG BOTTLING PLANT - [N16000300] IOCL, WEST BENGAL	04/2017	163.02 -	163.02	88.03	04/2020 10/2021	10/2021	18	0	
112	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326] IOCL, GUJARAT	10/2017	906.00 -	906.00	259.40	02/2020 10/2021	10/2021	20	0	
113	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303] IOCL, UTTAR PRADESH	08/2017	318.80 -	318.80	136.81	08/2021 -	11/2021	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	17.21	08/2020 11/2021	11/2021	15	0	
115	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	301.57	03/2021 12/2021	12/2021	9	0	
116	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	589.44	10/2021 -	12/2021	2	0	
117	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	6,025.00	3,409.77	12/2018 -	02/2022	38	33.98	
118	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	29.92	10/2020 02/2022	02/2022	16	0	
119	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	240.52	02/2020 02/2022	02/2022	24	0	
120	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	385.53	10/2017 03/2022	03/2022	53	17.66	
121	LPG BP PROJECT KHANDUA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	46.92	12/2019 03/2022	03/2022	27	0	
122	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	222.31	01/2021 03/2022	03/2022	14	0	
123	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	587.98	08/2020 -	04/2022	20	0	
124	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	25.82	06/2021 07/2022	07/2022	13	0	
125	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	92.80	04/2022 -	02/2023	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
126	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	65.87	04/2022 -	08/2023	16	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
127	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	443.62	03/2020 11/2020	06/2021	15	9.64	
128	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,556.82	12/2019 04/2021	10/2021	22	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
129	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	1,846.46	1,546.02	05/2013 12/2020	03/2021	94	114.26	
130	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,685.92	04/2018 05/2021	05/2021	37	5.8	
131	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	624.35	446.46	03/2019 05/2021	05/2021	26	-4.07	
132	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	180.83	05/2020 05/2021	05/2021	12	21.57	
133	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	619.17	12/2020 05/2021	05/2021	5	-3.93	
134	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	25,090.00	10,477.71	06/2020 06/2022	06/2022	24	-26.23	
135	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	974.84	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									
136	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021	48	39.05	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
137	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	187.00	10/2020 -	03/2021	5	0	
138	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	457.91	12/2019 -	04/2021	16	0	
139	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 638.60	652.10	136.05	02/2020 -	04/2021	14	19.89	
140	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	222.21	144.80	08/2020 -	04/2021	8	-1.13	
	Total		1,21,399.61 -	1,27,799.43	70,297.03					
	<u>POWER</u>									
	<u>Central Public Works Department</u>									
141	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	201.69	11/2019 -	05/2021	18	0	
	<u>Chenab Valley Power Projects [P] Limited</u>									
142	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,664.74	04/2020 -	07/2025	63	0	
	<u>National Hydro-Electric Power Corporation</u>									
143	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	8,825.13	09/2009 03/2022	03/2022	150	152.52	
144	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	13,233.01	09/2010 08/2023	08/2023	155	218.08	
	<u>National Thermal Power Corporation</u>									
145	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 15,105.22	15,105.22	13,657.43	01/2018 10/2020	02/2021	37	29.79	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
146	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	10,016.10	7,966.63	07/2019 03/2021	03/2021	20	9	
147	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	1,746.41	12/2018 -	03/2021	27	0	
148	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 13,140.91	13,140.91	11,641.13	12/2018 02/2021	04/2021	28	4.86	Support of State Govt. of Odisha is required for following: •Balance RoW for 132 kV transmission line for Make Up Water pump house. Acquisition/possession of balance land for Railway siding.
149	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,680.05	07/2012 06/2020	04/2021	105	97.38	
150	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	349.00	226.00	11/2020 04/2021	04/2021	5	0	
151	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	410.98	11/2018 -	05/2021	30	0	
152	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,463.61	05/2018 06/2021	07/2021	38	33.47	
153	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	501.29	49.76	09/2021 01/2022	01/2022	4	0	
154	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	798.24	31.64	09/2021 01/2022	01/2022	4	0	
155	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	1,722.14	103.85	09/2021 01/2022	01/2022	4	0	
156	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	8,125.04	11/2020 03/2022	03/2022	16	0	
157	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	18,308.58	10/2011 04/2022	04/2022	126	145.16	•Support required for early completion of Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur rail route, which is critical to ease transportation of coal for Barh Project.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
158	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,389.42	11,612.82	06/2019 10/2022	10/2022	40	7.12	Support of State Govt of Jharkhand is required for following: 1.Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. 2.Acquisition of Land by CCL for external CHP. 3.Early completion of Road Widening and strengthening of SH-7 from Hazaribagh to Bijupara. It is being done on deposit basis by RCD. The road diversion in project area needs to be completed on priority. 4.Repair of damaged bridge over Garhi River is critical for transportation of material for project. 5.Forest clearance in ATS lines.
159	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,841.21	03/2013 12/2021	12/2022	117	96.99	
160	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,112.00	4,060.28	03/2023 -	09/2024	18	-8.34	Support requested for resolving inter-ministerial issues.
161	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,381.54	649.64	09/2019 11/2022	12/2024	63	-02	•All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSERC. State Govt is not ready to finalize power evacuation line in absence of PPA. •Shifting of balance Homesteads from Project area. (13 Nos + 01 School)
	<u>North East Electric Power Corporation</u>									
162	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	7,927.34	8,154.49	12/2009 02/2021	02/2021	134	217.49	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Power Grid Corporation Of India Limited</u>									
163	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,630.84	10/2012 06/2020	03/2021	101	5.14	
164	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	639.30	01/2018 04/2021	03/2021	38	0	
165	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	343.03	04/2018 03/2021	03/2021	35	0	
166	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	11,441.18	11/2019 04/2021	03/2021	16	0	
167	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	5,070.13	4,041.83	04/2020 -	03/2021	11	0	
168	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	456.53	02/2019 05/2020	03/2021	25	0	
169	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,644.55	02/2020 09/2020	03/2021	13	0	
170	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	239.65	05/2020 -	03/2021	10	0	
171	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	148.03	06/2019 09/2020	04/2021	22	0	
172	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	2,825.43	07/2020 -	04/2021	9	14.11	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
173	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	157.07	07/2019 04/2021	04/2021	21	17.99	
174	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	477.66	11/2016 06/2020	05/2021	54	4.61	
175	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	241.55	04/2016 12/2017	06/2021	62	0	
176	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	89.36	03/2018 -	06/2021	39	0	
177	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	519.78	05/2017 07/2020	06/2021	49	0	
178	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	200.36	02/2019 06/2021	06/2021	28	0	
179	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	224.72	12/2019 06/2020	06/2021	18	0	
180	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	2,002.54	12/2018 -	12/2021	36	92.02	
181	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	2,541.14	12/2018 -	12/2021	36	31.08	
182	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,869.26	08/2013 03/2022	03/2022	103	32.24	
	Thdc India Limited									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
183	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21	1,587.16	464.00	09/2020	08/2022	23	-24.57	1. Tenancy/Private land (337.35 Ha): Title dispute of land of approx. 400 land holders pending in court of Collector, Singrauli due to which distribution of Compensation to beneficiaries is delayed. 2. Govt. land for R&R (53.13 Ha): Declaration of the land as "Abadi Land" is pending at GoMP. 3. Govt. land of Coal Block (178.13 Ha): Collector, Singrauli informed that permission under section 247 shall be accorded after grant of Mining Lease which is pending with Director (Mining), GoMP.
184	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	3,860.35	2,161.90	06/2013	12/2023	126	54.94	Environment Clearance of Gadi Quarry is still pending. In the meeting of SEIAA held in Nov19 it was informed that Environmental Clearance for Gadi Quarry shall be given to the owner THDCIL in place of HCC. In this context THDCIL has written letter to District Magistrate Chamoli on 13.12.19 to consider the transfer of name of applicant from Ms HCC to THDC India Limited in the application of EC DM.
185	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42	11,089.42	1,432.11	09/2023	08/2024	11	0	• Continuous help of District administration is required for expeditious land acquisition. • Continuous help of District administration is required for expeditious shifting of Nagla residents to newly identified land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		2,07,656.15	2,73,404.51	1,89,445.94					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Central Public Works Department</u>									
186	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84	209.84	123.92	03/2020	05/2021	14	0	
187	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA	09/2017	150.29	150.29	36.14	03/2020	12/2021	21	0	
188	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00	195.00	16.41	09/2020	04/2022	19	0	
189	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00	260.00	25.38	06/2021	05/2022	11	0	
	<u>HII Infra Tech Services Limited</u>									
190	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00	715.06	524.06	04/2020	07/2021	15	-8.91	
191	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00	557.48	449.74	06/2020	07/2021	13	-20.7	
192	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00	747.80	296.84	05/2021	07/2022	14	-14.54	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
193	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11	499.23	481.52	11/2013	03/2021	88	20.55	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
194	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	250.00	229.39	05/2017 -	03/2021	46	22.29	
195	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	24	.13	
196	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	280.39	03/2019 -	03/2021	24	0	
197	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	161.29	02/2018 -	04/2021	38	16.33	
198	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	234.12	05/2018 -	12/2021	43	0	
	Total		4,940.96 -	4,754.30	3,117.71					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
199	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24	98.88	
200	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24	73.73	
201	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12	.89	
202	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24	0	
203	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12	0	
204	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24	0	
205	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
206	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	36	25.65	
207	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	346.32	316.04	03/2019 -	03/2021	24	0	
	<u>East Central Railways</u>									
208	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	678.54 678.54	929.86	738.84	03/2019 -	05/2021	26	37.04	
209	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	477.88 283.95	751.55	687.20	03/2012 -	07/2021	112	57.27	
210	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	217.40	03/2019 -	03/2022	36	0	
211	GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND	03/2015	348.23 -	348.23	316.23	03/2021 -	03/2022	12	0	
212	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]ECR, BIHAR	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	15	62.06	
213	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	128	229.5	
214	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	36	49.45	
215	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR, BIHAR	12/2015	1,200.20 1,200.20	1,200.20	862.71	03/2020 -	03/2023	36	0	
216	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR, BIHAR	12/2015	1,491.47 -	1,491.47	471.48	03/2020 -	03/2023	36	0	
217	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,111.96	03/2020 -	03/2024	48	0	
218	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR, BIHAR	04/2016	744.04 -	1,215.54	309.44	03/2021 -	03/2024	36	63.37	
	<u>East Coast Railway</u>									
219	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	1,111.99 1,539.28	1,539.28	1,109.06	02/2019 12/2021	12/2021	34	38.43	
220	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 238.03	238.03	219.74	03/2020 03/2021	03/2022	24	52.77	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
221	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	902.85	03/2020 03/2023	03/2023	36	.07	
222	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR, ODISHA	04/2015	1,547.38 1,547.38	1,547.38	603.73	03/2022 03/2023	03/2023	12	0	
223	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	843.04 843.04	843.04	208.46	10/2020 03/2024	03/2024	41	0	
224	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	604.03	03/2022 03/2024	03/2024	24	0	
225	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR, ODISHA	04/2015	701.61 810.02	810.02	171.45	11/2018 03/2024	03/2024	64	15.45	
226	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR, ODISHA	04/2015	1,172.92 1,172.92	1,172.92	596.91	12/2018 03/2024	03/2024	63	0	
227	TALCHER- BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 1,928.07	1,928.07	845.24	06/2021 03/2025	03/2025	45	137.8	
228	KHURDA ROAD- BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,413.99	03/2009 03/2026	03/2026	204	29.71	
229	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 2,361.74	2,361.74	380.90	03/2022 03/2026	03/2026	48	0	
	<u>Eastern Railways</u>									
230	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28	0	
231	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	542.18 -	663.13	516.55	03/2020 -	03/2021	12	22.31	State Govt. is requested to deposit. for their balance share of cost for the project. But still deposition is awaited.
232	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	133	134.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
233	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	903.03	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30 KM between Kamarpukur and Jairambati is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.
234	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	970.10	12/2010 -	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 238.75 Cr. for their balance share of cost towards project Katwa-Bardhaman G.C.
235	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
236	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98	2,137.81	355.79	03/2022	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
237	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52	995.10	640.17	03/2016	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to 41 nos. of un authorized crossings Amghata to Nabadwipghat work is dropped vide Bd's letter No. 2020/W- I/Compliance in Bd Mtg, dated 09.10.2020
238	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51	769.40	103.78	03/2017	03/2025	96	29.2	Suri – Prantik New Line (33.90 Km).- The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
239	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28	266.32	185.36	03/2016	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
240	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	374.08	03/2017 -	03/2025	96	20.3	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non-availability of land.
241	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahat (9.75 Km) New line-- Work could not be started due to non availability of land
242	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	163.26	02/2012 -	03/2025	157	36.15	Sangrapur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
243	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	106.31	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
244	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
245	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42	0	1-Agitation by Land losers.
246	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21	117.23	
247	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-81.5	
	<u>Metropolitan Rapid Transport Projects</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
248	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-82.67	
249	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
250	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102	48.06	
251	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216	501.57	
	<u>North Central Railway</u>									
252	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	32.02	
	<u>North East Frontier Railway</u>									
253	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 486.96	800.00	795.88	03/2019 -	03/2021	24	154.78	
254	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,645.92	12/2008 -	04/2021	148	284.8	
255	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,133.64	03/2021 -	05/2021	2	115.07	
256	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	30.26	
257	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,105.00	787.79	03/2019 -	03/2023	48	186.86	
258	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	3,816.20	03/2014 -	03/2023	108	130.69	
259	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,478.05	03/2022 -	03/2023	12	32.15	
260	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	10,777.52	03/2011 -	12/2023	153	175.34	
261	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,084.69	8,600.00	619.18	12/2015 12/2023	12/2023	96	542.04	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
262	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	968.95	03/2019 -	03/2024	60	302.54	
263	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	69.92	03/2019 -	03/2024	60	13.6	
264	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,911.00	1,125.27	03/2015 -	12/2024	117	197.05	
	<u>North Eastern Railway</u>									
265	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	476.60	04/2017 -	03/2021	47	-31.45	
266	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	80.76	12/2019 -	04/2021	16	-12.65	
267	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	68	.16	
268	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	37	61.8	
269	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	199.70	01/2022 -	03/2022	2	-38.88	
270	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
271	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
272	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-32.79	
	<u>North Western Railway</u>									
273	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	395.00	324.37	12/2019 -	02/2021	14	60.52	
274	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	375.00	337.30	11/2019 -	03/2021	16	75.73	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
275	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	307.78	03/2020 -	06/2021	15	0	
276	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	691.34	02/2019 -	11/2021	33	109.82	
277	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	172.41	03/2020 -	04/2022	25	16.97	
	<u>Northern Railway</u>									
278	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	893.45	658.97	12/2011 -	06/2021	114	211.31	
279	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	859.00	852.73	03/2016 -	06/2021	63	37.44	
280	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	22,879.22	11/2002 -	12/2022	241	1017.96	
281	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	388.89	
282	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	1,540.13	242.12	03/2023 03/2025	03/2025	24	369.35	
283	MANSABHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108	0	
	<u>Rail India Technical And Economic Service</u>									
284	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15	0	
	<u>Rail Vikas Nigam Ltd.</u>									
285	MULTI MODAL TRANSPORT SYSTEM(MMST) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	799.01	03/2016 -	12/2021	69	50.15	
286	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,531.51	03/2020 -	12/2021	21	281.93	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
287	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	21	111.91	
288	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,282.18	03/2020 -	12/2021	21	-7.28	
289	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,546.20	12/2020 -	12/2021	12	23.55	
290	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	1,868.89	1,795.61	12/2021 -	03/2022	3	20.68	
291	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24	124.58	
292	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	102.92	
293	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,302.29	03/2019 -	06/2022	39	51.02	
294	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	62.89	
295	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	54.24	
296	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	5.98	
297	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	833.10	03/2023 -	12/2024	21	0	
298	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,676.61	03/2016 -	03/2025	108	7.78	
299	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,072.08	03/2016 -	03/2025	108	59.22	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
300	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,768.76	12/2024 -	03/2025	3	40.08	
301	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	18.95	
302	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	3,327.72	1,225.51	12/2024 -	12/2026	24	42.47	
	<u>South Central Railway</u>									
303	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	704.31 -	927.94	521.91	03/2020 03/2022	06/2021	15	31.75	
304	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	275.34	
305	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	1,847.08	03/2000 -	03/2023	276	98.57	
306	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	850.07	03/2009 -	03/2024	180	102.85	
307	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	478.70	03/2010 -	03/2024	168	0	
308	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	543.07	03/2023 -	03/2024	12	5.16	
309	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,214.20	03/2021 -	03/2024	36	15.49	
310	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,370.71	03/2021 -	03/2024	36	0	
311	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,165.50	03/2022 -	03/2024	24	7.06	
312	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	350.55	03/2014 -	03/2027	156	42.44	
	<u>South East Central Railway</u>									
313	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12	291.76	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
314	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34	116.46	
315	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 2,753.05	3,524.81	982.38	03/2023 12/2023	12/2023	9	84.69	
316	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33	8.23	
317	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24	.07	
318	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36	378.6	
	<u>South Eastern Railway</u>									
319	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	297.17	12/2018 12/2018	06/2021	30	38.92	
320	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	857.47	03/2020 03/2020	12/2021	21	35.38	
321	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	704.10	03/2021 03/2021	12/2023	33	15.6	
322	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	54.99	
323	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324	130.97	
	<u>South Western Railway</u>									
324	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00 -	783.00	613.57	03/2020 03/2021	03/2021	12	35.47	
325	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	1,528.14	03/2019 -	03/2021	24	15.84	
326	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,147.00	881.92	03/2020 06/2021	06/2021	15	33.31	
327	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,656.00	1,119.96	03/2020 11/2021	11/2021	20	43.14	
328	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	307.78	03/2016 -	12/2023	93	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
329	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	35.01	03/2016 -	12/2023	93	0	
330	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	
331	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
332	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	277.39	12/2018 06/2025	06/2025	78	0	
	<u>Southern Railway</u>									
333	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	253.33	
334	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-23.24	
335	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	102.11	
336	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	60	465.83	
337	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	73	301.67	
338	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
339	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	105	1699.64	
	<u>West Central Railway</u>									
340	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	24	585.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
341	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93	1,762.94	1,084.58	03/2020	03/2023	36	-06	Work is suffering badly on this Critical project due pending forest land clearance. The detail position is as under: ¿ Niwas Road to Deoragram: Forest land 46.067 Ha from Railway Km 1261 to 1301 under DFO Singrauli in isolated patches. Application has been uploaded on Sep'2018. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 2055 Nos. trees cutting have been submitted on 18.06.2020 and 21.07.2020. However, APCCF/Bhopal vide letter dated 31.07.2020 has sought clarifications from MOEF. MOEF vide letter dated 24.09.2020 has clarified that case need to be processed further in FCA. GM/WCR vide letter dated 09.10.2020 has requested Railway Board to intervene in this matter. A meeting was held in Collector Singrauli office on 12.12.20. This meeting was chaired by Hon'ble MP/ Sidhi Smt Riti Pathak. Collector Singrauli has been requested to expedite this proposal. ¿ Vijaysota to Beohari: Forest Land 66.69 Ha under DFO Shahdol from Rly Km 1162 to 1189 in isolated patches. Application has been uploaded in Feb'2019. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 17454 Nos trees cutting have been submitted on 18.08.2020

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
342	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	0	
343	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	254.64	03/2022 -	03/2023	12	114.32	
344	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	3230.57	
	<u>Western Railway</u>									
345	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	1,017.91	650.65	03/2020 02/2021	02/2021	11	47.13	
346	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 890.76	890.76	745.11	03/2019 10/2021	10/2021	31	61.51	
347	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	1,389.05	1,103.31	03/2021 12/2021	12/2021	9	33.93	
348	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	1,002.39	642.89	03/2021 12/2022	12/2022	21	0	
349	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 411.62	411.62	126.05	03/2012 03/2023	03/2023	132	29.34	
350	CHOTTADEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	1,347.26	897.00	03/2022 03/2023	03/2023	12	0	
351	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48	329.77	
352	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	249.28	06/2020 03/2023	03/2023	33	-13.76	
353	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	1,959.74	1,784.02	03/2020 12/2023	12/2023	45	136.19	
354	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	5,912.40	2,143.20	03/2022 03/2024	03/2024	24	68.75	
355	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	866.05	03/2022 03/2025	03/2025	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		2,02,568.46	3,31,130.18	1,57,476.15					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
356	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56	162.56	129.98	03/2018 02/2021	02/2021	35	0	
357	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91	235.91	173.80	02/2018 02/2021	02/2021	36	0	
358	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62	184.62	115.57	02/2018 02/2021	02/2021	36	0	
359	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21	191.21	117.80	11/2019 01/2021	02/2021	15	0	
360	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25	247.25	178.64	03/2019	02/2021	23	0	
361	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	177.78	08/2018 06/2021	02/2021	30	0	
362	REHABILITATION AND UPGRADATION OF HARPALPUR-SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50	208.50	165.82	11/2019	02/2021	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
363	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	205.40	05/2019 -	02/2021	21	0	
364	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	218.90	129.75	03/2020 -	02/2021	11	0	
365	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	168.68	10/2019 -	02/2021	16	0	
366	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	271.45	225.81	10/2015 03/2021	03/2021	65	0	
367	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71	0	
368	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	418.09	01/2020 01/2021	03/2021	14	0	
369	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 173.41	173.41	139.19	08/2018 03/2021	03/2021	31	4.33	
370	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	254.30	79.69	10/2020 -	03/2021	5	0	
371	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 226.88	226.88	170.05	08/2018 03/2021	03/2021	31	4.45	
372	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	151.12	03/2018 01/2021	03/2021	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
373	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	191.67	07/2018 03/2021	03/2021	32	0	
374	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	03/2021	37	0	
375	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	03/2021	36	0	
376	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	105.72	08/2018 03/2021	03/2021	31	0	
377	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	187.82	131.74	04/2018 -	03/2021	35	0	
378	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35	0	
379	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 634.30	536.65	539.22	12/2019 03/2021	03/2021	15	0	
380	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	14	0	
381	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	120.37	08/2020 -	03/2021	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
382	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	172.63	09/2020 -	03/2021	6	0	
383	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	264.67	01/2018 03/2021	03/2021	38	0	
384	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	75.05	05/2019 03/2021	03/2021	22	0	
385	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	256.32	11/2017 03/2021	03/2021	40	0	
386	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47	77.26	
387	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	735.81	02/2020 04/2021	04/2021	14	0	
388	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	38.45	03/2018 04/2021	04/2021	37	0	
389	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	218.70	103.81	11/2020 04/2020	04/2021	5	0	
390	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	668.14	06/2019 04/2021	04/2021	22	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
391	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	476.77	05/2016 08/2021	04/2021	59	0	
392	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34	0	
393	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	61.53	09/2018 -	04/2021	31	0	
394	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	181.21	04/2020 -	04/2021	12	-8.28	
395	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	242.95	09/2019 11/2020	05/2021	20	0	
396	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	512.17	07/2018 05/2021	05/2021	34	0	
397	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	170.57	44.68	11/2020 -	05/2021	6	0	
398	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021	44	0	
399	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
400	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021	128	69.3	
401	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021	128	93.8	
402	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	366.24	08/2017 06/2021	06/2021	46	0	
403	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	116.58	03/2017 06/2021	06/2021	51	0	
404	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	186.74	09/2019 06/2021	06/2021	21	0	
405	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37	0	
406	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	345.46	03/2018 06/2021	06/2021	39	9.23	
407	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	572.66	255.42	08/2016 06/2021	06/2021	58	15.19	
408	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	264.26	06/2017 06/2021	06/2021	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
409	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	544.00	397.33	09/2016 06/2021	06/2021	57	14.24	
410	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	731.50	399.36	10/2016 06/2021	06/2021	56	17.04	
411	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	435.61	85.00	07/2016 06/2021	06/2021	59	-3.83	
412	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	239.88	03/2015 06/2021	06/2021	75	0	
413	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6	0	
414	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021	59	0	
415	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	110.19	08/2020 07/2021	07/2021	11	0	
416	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	322.48	261.72	07/2020 -	08/2021	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
417	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	59.72	03/2018 09/2021	09/2021	42	0	
418	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	24.84	
419	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15	0	
420	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28	11.18	
421	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24	0	
422	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	-	11/2020 -	08/2022	21	-12	
423	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	24.14	08/2019 -	11/2022	39	33.51	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
424	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	180.57	50.17	04/2017 -	02/2021	46	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
425	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	167.28	22.06	04/2017 -	02/2021	46	0	
426	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	139.47	04/2017 03/2018	03/2021	47	0	
427	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	190.47	01/2016 -	04/2021	63	0	
428	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	387.00	290.94	08/2016 -	05/2021	57	3.73	
429	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	339.55	276.01	08/2016 -	05/2021	57	-14.37	
430	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	340.00	234.97	08/2016 -	05/2021	57	-20.84	
431	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	457.77	160.06	10/2018 -	10/2021	36	-11.55	
432	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL, NAGALAND	03/2018	215.12 -	215.12	83.20	09/2018 -	11/2021	38	0	
433	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	407.30	102.90	06/2018 -	12/2021	42	-6.88	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
434	FOUR LANE OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM)	06/2015	463.49 -	398.06	126.86	06/2018 -	12/2021	42	-14.12	
435	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	315.03	80.78	09/2018 -	12/2021	39	0	
436	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	240.64	95.34	09/2018 -	12/2021	39	0	
437	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	60.55	09/2018 -	12/2021	39	0	
438	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	0	
439	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	85.02	09/2018 -	05/2022	44	0	
440	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57 -	339.57	114.91	09/2018 -	07/2022	46	0	
441	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL, NAGALAND	03/2018	285.68 -	285.68	68.70	09/2018 -	09/2022	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
442	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	36.80	09/2018 -	10/2022	49	0	
443	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	336.49	71.11	09/2018 -	11/2022	50	-32.71	
444	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	42.55	09/2018 -	11/2022	50	0	
445	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	65.01	09/2019 -	04/2023	43	0	
446	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	47.39	09/2019 -	04/2023	43	0	
447	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	58.49	09/2019 -	04/2023	43	0	
448	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	33.18	09/2019 -	06/2023	45	0	
449	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	72.44	09/2019 -	06/2023	45	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
450	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	18.08	09/2019 -	07/2023	46	0	
451	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	59.92	09/2019 -	09/2023	48	0	
452	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	50.49	09/2019 -	04/2024	55	0	
	<u>National Highways Authority Of India</u>									
453	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	473.85	10/2017 -	02/2021	40	0	
454	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	394.32	07/2018 -	02/2021	31	0	
455	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	105.20	03/2019 -	02/2021	23	0	-
456	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	8	1.78	
457	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	394.32	07/2016 -	02/2021	55	0	
458	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,540.00	03/2013 -	03/2021	96	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
459	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021	81	0	
460	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71	52.73	
461	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	1,056.08	970.12	11/2018 07/2019	03/2021	28	-25.83	
462	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	707.82	419.77	08/2018 -	03/2021	31	0	
463	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	804.97	522.80	06/2018 10/2020	03/2021	33	0	
464	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	2,510.04	555.68	08/2019 -	03/2021	19	0	
465	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	446.17	70.85	03/2019 -	03/2021	24	0	
466	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA	03/2017	639.79 -	552.90	597.77	03/2020 03/2021	03/2021	12	-13.58	
467	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI, ANDHRA PRADESH	03/2018	1,532.62 -	2,499.00	1,539.65	03/2021 10/2021	04/2021	1	63.05	
468	4-LANNING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,239.99	08/2013 -	05/2021	93	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
469	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-3.27	
470	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI, KERALA	09/2017	1,124.11 -	1,232.76	492.81	09/2017 -	05/2021	44	9.67	Additional land acquisition
471	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	730.97	630.68	05/2018 06/2021	06/2021	37	37.63	
472	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	690.17	585.57	05/2018 06/2021	06/2021	37	16.34	
473	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	504.00	361.58	05/2018 04/2019	06/2021	37	-2	
474	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15	10.24	
475	REHABILITATION AND UPGRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	0	
476	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15	3.95	
477	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	166.90	49.53	05/2013 -	08/2021	99	-55.37	
478	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
479	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	352.32	03/2020 -	09/2021	18	.23	
480	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15	0	
481	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	199.44	03/2019 12/2021	12/2021	33	0	
482	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	302.83	07/2019 06/2021	12/2021	29	0	
483	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	317.73	07/2019 06/2021	12/2021	29	0	
484	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	336.58	03/2019 01/2021	12/2021	33	-25.48	
485	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	848.45	219.00	03/2020 -	12/2021	21	0	
486	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	496.65	12/2019 -	12/2021	24	0	
487	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54	0	
488	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,858.57	08/2013 -	03/2022	103	0	
489	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	119.00	03/2019 03/2022	03/2022	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
490	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	312.73	03/2020 -	04/2022	25	0	
491	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	296.06	05/2020 -	05/2022	24	0	
492	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	453.70	08/2017 -	07/2022	59	0	
493	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	561.03	09/2017 -	07/2022	58	0	
494	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105	18.66	
	Total		79,212.04 -	82,198.44	48,503.25					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
495	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	431.16	-	06/2021 -	11/2021	5	0	
	<u>Department Of Telecommunication</u>									
496	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	71	84.97	
	Total		13,765.16 -	25,095.16	16,594.00					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
497	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	8,446.13	12/2018 -	08/2022	44	18.69	
	<u>Bangalore Metro Rail Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
498	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 30,695.00	26,405.14	16,349.18	02/2019 03/2021	06/2024	64	0	
	<u>Central Public Works Department</u>									
499	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	238.56	157.67	05/2020 -	02/2021	9	0	
500	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	55.38	03/2021 07/2021	07/2021	4	0	
501	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	102.34	04/2019 06/2021	10/2021	30	0	
502	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19	0	
503	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41	-6.71	
	<u>Chennai Metro Rail Ltd</u>									
504	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	3,770.00	2,932.59	03/2018 -	03/2021	36	0	
	<u>Delhi Metro Rail Corporation</u>									
505	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021	66	0	
506	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	511.60	12/2020 -	09/2021	9	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
507	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 09/2022	03/2023	98	44.39	
	Total		1,05,664.03 -	1,17,868.83	85,542.57					
	<u>WATER RESOURCES</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
508	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR	12/2014	225.77 -	225.77	263.72	03/2020 -	03/2021	12	0	
509	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR	05/2017	191.62 -	191.62	44.97	11/2020 03/2021	03/2021	4	0	
510	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO, BIHAR	11/2018	236.15 -	236.15	22.69	12/2020 06/2021	06/2021	6	0	
511	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO, BIHAR	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14	0	
512	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19 -	305.19	-	08/2021 -	12/2021	4	0	
	<u>Delhi Jal Board</u>									
513	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB, DELHI	12/2018	515.07 -	515.07	297.33	01/2021 -	06/2021	5	0	
514	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI	05/2016	211.79 -	211.79	60.47	12/2021 -	12/2022	12	0	
515	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI	05/2016	239.11 -	239.11	118.82	02/2022 -	12/2022	10	0	
	<u>Hindustan Steelwork Construction Limited</u>									
516	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	721.37	712.37	03/2015 -	03/2021	72	-24.54	
	<u>Kolkata Metropolitan Development Authority</u>									
517	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	272.32	210.94	04/2020 -	03/2021	11	0	
518	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	274.76	198.28	12/2019 05/2021	05/2021	17	0	
	<u>Polavaram Project Authority</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
519	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	16,995.57	03/2020 11/2021	04/2022	25	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									
520	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UP JalNigam,UTTAR PRADESH	10/2016	370.40 -	370.40	361.93	08/2020 03/2021	03/2021	7	0	
521	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UP JalNigam,UTTAR PRADESH	02/2017	161.31 -	161.31	50.65	11/2019 -	03/2021	16	0	
522	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam,UTTAR PRADESH	12/2017	460.45 -	460.45	106.27	12/2020 -	05/2021	5	0	
523	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam,UTTAR PRADESH	03/2019	298.12 -	298.12	-	07/2021 -	06/2022	11	0	
	<u>Uttarakhand Pey Jal Nigam</u>									
524	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UK JalNigam,UTTARA KHAND	03/2017	158.00 -	158.00	77.81	11/2019 03/2021	03/2021	16	0	
	Total		15,212.03 -	60,375.23	19,685.18					
	<u>DEFENCE PRODUCTION</u>									
	<u>Central Public Works Department</u>									
525	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	115.20	02/2020 -	06/2021	16	0	
	Total		246.31 -	246.31	115.20					
	<u>HUMAN RESOURCE DEVELOPMENT</u>									
526	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	20	1.85	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
527	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6	10.22	
528	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	350.69	265.91	04/2019 -	04/2021	24	19.28	
529	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	0	
530	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15	0	
531	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	0	
532	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52	.57	
533	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	387.83	180.63	05/2020 -	02/2022	21	-9.81	
534	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	149.00	03/2022 -	06/2022	3	0	
535	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	0	
536	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD,PUNJAB	10/2019	348.24 -	348.24	15.20	05/2022 -	08/2022	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
537	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	0	
538	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 375.00	375.00	48.46	09/2020 -	11/2022	26	0	
539	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	0	
	Total		6,229.82 -	6,276.31	1,798.74					
	<u>HOME AFFAIRS</u>									
540	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	874.24	10/2019 -	12/2021	26	64.04	
541	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 238.00	238.00	170.35	04/2018 12/2021	12/2021	44	46.12	
	Total		1,382.09 -	2,238.00	1,044.59					
	<u>RURAL DEVELOPMENT</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
542	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	03/2021	63	3.96	
543	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2021	51	2.23	
544	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	03/2021	51	0	
	Total		527.83 -	538.27	460.04					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>CULTURE DEVELOPMENT</u>									
545	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	145.60	09/2017 -	03/2021	42	0	Non receipt of payment from Client
	Total		151.33 -	151.33	145.60					
	<u>DPIIT</u>									
	<u>Delhi Mumbai Industrial Corridor</u>									
546	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC, MULTI STATE	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 01/2014	07/2021	22	9.8	
	<u>India International Convention And Expo Centre</u>									
547	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC, DELHI	11/2017	4,773.00 -	5,178.00	2,419.54	12/2019 -	10/2021	22	8.49	
	Total		17,352.09 -	18,990.30	11,134.61					
	Grand Total		9,50,776.50	12,41,791.08	7,16,487.04					

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,915.80	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,297.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12,992.00	12/2016 -	03/2023	38.63
	Total		27,271.00 -	40,499.00	35,204.80			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	5.78
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	51.11	09/2021 -	09/2021	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	7.88
	Total		1,905.50 -	2,153.66	666.76			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
7	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	18.35	04/2018 -	12/2021	37.56
8	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	30.15	03/2017 -	10/2021	12.20
	<u>Eastern Coal Fields Limited</u>							
9	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	591.17	08/2019 -	-	93.35
	<u>Neyveli Lignite Corporation</u>							
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,404.29	12/2015 -	02/2021	35.10
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11,135.69	11/2021 -	07/2022	.00
	<u>Singareni Colliers Company Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86
13	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	106.68	03/2019 -	03/2022	11.42
14	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	21.17	03/2015 -	03/2022	5.85
15	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	292.49	03/2015 -	03/2022	114.60
	<u>South-Eastern Coal Fields Limited</u>							
16	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	187.31	03/2015 -	03/2022	201.44
	<u>Western Coal Fields Limited</u>							
17	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	85.82	03/2023 -	03/2023	117.98
18	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	15.41
19	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	07/2016	281.25 -	409.87	20.99	03/2022 -	03/2022	45.73
20	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	.00
	Total		28,978.66 -	34,696.87	20,467.10			
	<u>DPIIT</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
21	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>							
22	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,419.54	12/2019 -	10/2021	8.49
	Total		17,352.09 -	18,990.30	11,134.61			
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
23	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>							
24	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	481.52	11/2013 -	03/2021	20.55
25	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	229.39	05/2017 -	03/2021	22.29
26	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
27	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
28	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71
29	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	161.29	02/2018 -	04/2021	16.33
30	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
31	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	.13
32	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.64	128.08	-	03/2021	.05
33	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	228.87	-	12/2020	.02
	<u>National Building Construcion Corporation Ltd</u>							
34	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	648.37	09/2021 -	09/2021	8.88
	Total		5,589.39 -	6,253.60	3,417.18			
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
35	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	874.24	10/2019 -	12/2021	64.04
36	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	170.35	04/2018 -	12/2021	46.12
	Total		1,382.09 -	2,238.00	1,044.59			
	<u>HUMAN RESOURCE DEVELOPMENT</u>							
37	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	.57
38	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	265.91	04/2019 -	04/2021	19.28
39	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	1.85
40	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	10.22
	<u>Rail India Technical And Economic Service</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
41	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	-	09/2014 -	-	29.31
	Total		2,009.81 -	2,240.41	1,079.50			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
42	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	4,852.63	08/2018 -	03/2021	14.33
43	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	17.80	02/2017 -	08/2022	117.11
44	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	711.00	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							
45	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,483.60	12/2012 -	02/2022	102.71
46	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	04/2017	287.49 -	345.15	196.18	04/2022 -	04/2022	20.06
47	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	166.90	08/2020 -	05/2021	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
48	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	13,352.70	07/2020 -	07/2022	25.50
49	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	09/2015	4,199.00 -	5,060.00	4,338.40	03/2020 -	-	20.50
50	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	1,825.04	06/2021 -	08/2022	14.76
51	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312	11/2017	255.00 -	300.00	253.92	11/2020 -	06/2021	17.65
	<u>Indian Oil Corporation Limited</u>							
52	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	385.53	10/2017 -	03/2022	17.66
53	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00 -	3,027.90	1,755.66	03/2021 -	08/2021	66.09
54	PARADIP HYDERABAD PIPELINE - [N16000194	01/2015	2,321.00 -	3,338.00	2,750.24	12/2020 -	06/2021	43.82
55	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 -	502.00	403.62	08/2019 -	06/2021	18.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
56	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	3,409.77	12/2018 -	02/2022	33.98
57	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	293.00	162.96	06/2020 -	09/2021	24.15
58	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	03/2018	588.20 -	730.20	65.94	- -	05/2023	24.14
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
59	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	443.62	03/2020 -	06/2021	9.64
	<u>Oil & Natural Gas Corporation Limited</u>							
60	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,846.46	1,546.02	05/2013 -	03/2021	114.26
61	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,685.92	04/2018 -	05/2021	5.80
62	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	634.60	03/2023 -	03/2022	38.20
63	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	180.83	05/2020 -	05/2021	21.57
64	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	974.84	03/2022 -	05/2023	23.16
65	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	2,305.03	05/2021 -	05/2021	2.17
	<u>Oil India Limited</u>							
66	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	455.00	03/2017 -	03/2021	39.05
67	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	136.05	02/2020 -	04/2021	19.89
	Total		61,914.04 -	80,292.67	47,493.80			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
68	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	8,825.13	09/2009 -	03/2022	152.52
69	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	13,233.01	09/2010 -	08/2023	218.08
	<u>National Thermal Power Corporation</u>							
70	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	15,105.22	13,657.43	01/2018 -	02/2021	29.79

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
71	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,841.21	03/2013 -	12/2022	96.99
72	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	10,016.10	7,966.63	07/2019 -	03/2021	9.00
73	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,140.91	11,641.13	12/2018 -	04/2021	4.86
74	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	11,612.82	06/2019 -	10/2022	7.12
75	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,680.05	07/2012 -	04/2021	97.38
76	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	15,463.61	05/2018 -	07/2021	33.47
77	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	11,130.00	02/2017 -	01/2021	24.87
78	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	18,308.58	10/2011 -	04/2022	145.16
79	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	7.55
80	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	17.95
81	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	12.95
82	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,380.97	10/2017 -	-	7.41
<u>North East Electric Power Corporation</u>								
83	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	8,154.49	12/2009 06/2016	-	217.49
<u>Power Grid Corporation Of India Limited</u>								
84	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,630.84	10/2012 -	03/2021	5.14
85	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,869.26	08/2013 -	03/2022	32.24
86	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,320.63	04/2016 -	07/2020	38.61
87	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	477.66	11/2016 -	05/2021	4.61
88	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	01/2015	871.62 -	902.49	644.11	10/2017 -	01/2021	3.54
89	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	200.16	07/2017 -	-	27.92
90	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	-	31.17
91	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	516.12	415.85	01/2019 -	04/2020	26.36

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
92	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,002.54	12/2018 -	12/2021	92.02
93	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	2,541.14	12/2018 -	12/2021	31.08
94	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	2,825.43	07/2020 -	04/2021	14.11
95	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	157.07	07/2019 -	04/2021	17.99
	<u>Thdc India Limited</u>							
96	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,161.90	06/2013 -	12/2023	54.94
	Total		1,63,505.25 -	2,37,386.77	191,667.25			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
97	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	73.73
98	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	315.00	312.62	03/2019 -	03/2020	71.14
99	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	98.88
100	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
101	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024	25.04
102	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89
103	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							
104	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	25.65
105	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
106	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	- -	-	143.17
107	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
108	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [N220100222	03/1999	1,033.07 -	3,550.00	3,528.48	- -	03/2022	243.64
109	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [N220100303	04/2003	528.65 -	2,066.78	1,529.08	- -	03/2023	290.95
110	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	751.55	687.20	03/2012 -	07/2021	57.27
111	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [N220100240	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	229.50
112	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [N220100257	04/1997	162.87 -	614.45	340.21	- -	12/2023	277.26
113	KOSI BRIDGE (NL), ECR - [N220100304	04/2002	499.41 -	516.02	436.36	03/2020 -	-	3.33
114	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00 -	519.33	266.24	- -	03/2025	36.67
115	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	738.84	03/2019 -	05/2021	37.04
116	KODERMA-TILAIYA (NL), ECR - [N220100305	04/2002	459.91 -	1,625.87	767.07	- -	03/2023	253.52
117	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 -	549.75	15.55	- -	-	32.26
118	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	818.15
119	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00 -	735.20	379.57	- -	03/2021	126.22
120	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	385.87	- -	03/2023	391.01
121	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	24.74	- -	-	376.78
122	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14 -	1,470.50	1,123.21	- -	03/2023	295.15
123	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	49.45
124	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01 -	480.00	477.72	- -	-	125.34
125	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15 -	546.71	541.83	07/2014 -	-	64.60
126	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	309.44	03/2021 -	03/2024	63.37
127	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	62.06
128	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	04/1998	180.82 -	726.31	543.57	- -	-	301.68
129	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	1,194.00	- -	03/2022	350.27

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>East Coast Railway</u>							
130	TALCHER-BIMALAGARH(NL)(ECOR) - [N220100328	04/2005	810.78 -	1,928.07	845.24	06/2021 -	03/2025	137.80
131	KHURDA ROAD-BOLANGIR(NL)ECOR - [N220100284	04/1994	2,923.13 -	3,791.66	1,413.99	03/2009 -	03/2026	29.71
132	SAMBALPUR-TALCHER DOUBLING - [N220000315	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	38.43
133	KIRANDUL - JAGDALPUR DOUBLING - [N220000318	12/2012	1,160.00 -	1,160.83	902.85	03/2020 -	03/2023	.07
134	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N220000319	03/2012	155.81 -	238.03	219.74	03/2020 -	03/2022	52.77
135	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N220000380	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	15.45
	<u>Eastern Railways</u>							
136	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [N220100272	04/2000	1,188.91 -	1,619.48	903.03	03/2019 12/2009	03/2025	36.22
137	DEOGHAR - SULTANGANJ (INL), ER - [N220100273	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	134.80
138	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N220000229	04/2010	365.17 -	439.30	374.08	03/2017 -	03/2025	20.30
139	TARAKESHWAR-MAGRA NEW BG LINE - [N220000235	04/2010	365.17 -	527.54	1.76	- -	03/2025	44.46
140	HANSDIHA-GODDA NL - [N220000236	04/2011	542.18 -	663.13	516.55	03/2020 -	03/2021	22.31
141	BOINCHI-SHAKTIGARH 3RD LINE - [N220000238	04/2011	175.80 -	495.10	283.97	- -	03/2022	181.63
142	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N220000239	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02
143	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N220000240	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01
144	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N220000241	04/2000	297.47 -	298.22	52.09	- -	03/2025	.25
145	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N220000243	04/2009	499.96 -	680.68	163.26	02/2012 -	03/2025	36.15
146	MONIGRAM- NIMTITA - [N220000301	04/2012	250.93 -	310.70	356.54	- -	03/2024	23.82
147	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N220000302	04/2012	255.64 -	272.20	239.06	- -	03/2022	6.48
148	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N220000216	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	34.08

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
149	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	-	-	03/2025	180.30
150	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	11.32	-	03/2025	51.19
151	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	355.79	03/2022 -	03/2025	133.39
152	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	422.81	-	03/2021	74.26
153	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	565.00	538.28	-	05/2019	116.16
154	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	640.17	03/2016 -	03/2025	7.75
155	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225]	04/2005	595.51 -	769.40	103.78	03/2017 -	03/2025	29.20
	<u>Indian Railway Construction Company Limited</u>							
156	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	117.23
157	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489]	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	.00
	<u>Metropolitan Rapid Transport Projects</u>							
158	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37
159	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	501.57
160	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N220000028]	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	48.06
161	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>							
162	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	345.51	12/2008 -	-	188.33
163	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02
164	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	1.69
	<u>North East Frontier Railway</u>							
165	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	275.07	03/2019 -	-	106.51
166	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	3,816.20	03/2014 -	03/2023	130.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
167	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266	04/2000	1,180.19 -	4,541.38	3,645.92	12/2008 -	04/2021	284.80
168	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288	04/2003	4,454.17 -	12,264.15	10,777.52	03/2011 -	12/2023	175.34
169	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,105.00	787.79	03/2019 -	03/2023	186.86
170	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	532.87 -	2,145.00	968.95	03/2019 -	03/2024	302.54
171	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 -	6,911.00	1,125.27	03/2015 -	12/2024	197.05
172	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	6.74	- -	-	7.86
173	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	12/2023	542.04
174	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,042.51	69.92	03/2019 -	03/2024	13.60
175	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	38.20	- -	-	71.62
176	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26
177	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	263.68	03/2021 -	03/2021	350.44
178	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	73.97	03/2020 -	-	94.45
179	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	287.09	- -	12/2021	54.80
180	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	1,040.00	154.52	03/2020 -	-	150.70
181	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	1,082.01	- -	-	128.39
182	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	800.00	795.88	03/2019 -	03/2021	154.78
183	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32 -	2,950.00	1,478.05	03/2022 -	03/2023	32.15
184	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	1,873.21	1,133.64	03/2021 -	05/2021	115.07
185	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390	04/2016	602.27 -	760.00	801.53	12/2021 -	04/2021	26.19
186	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499	02/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-	186.55
	<u>North Eastern Railway</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
187	KICHHA-KHATIMA (NL) - NER - [N220100317]	04/2003	142.45 -	228.40	0.15	- -	-	60.34
188	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	- -	-	8.10
189	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	- -	-	358.99
190	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	112.02	12/2021 -	12/2021	267.13
191	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	61.80
192	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	- -	-	.16
193	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	.16
194	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	-	01/2018 -	-	9.91
195	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	63.70	- -	12/2023	18.56
	<u>North Western Railway</u>							
196	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	02/1997	410.08 -	860.41	691.34	02/2019 -	11/2021	109.82
197	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	172.41	03/2020 -	04/2022	16.97
198	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	4.60	- -	-	126.64
199	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	324.37	12/2019 -	02/2021	60.52
200	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	186.12	- -	-	104.65
201	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	251.41	10/2018 -	-	47.91
202	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	-	- -	-	33.70
203	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	- -	-	33.81
204	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	337.30	11/2019 -	03/2021	75.73
205	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	459.43	02/2019 -	02/2020	116.86
	<u>Northern Railway</u>							
206	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	111.51	- -	03/2024	129.17
207	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	658.97	12/2011 -	06/2021	211.31

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
208	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	572.99	- -	03/2023	134.90
209	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	127.91	- -	09/2023	41.71
210	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	204.53	- -	-	57.68
211	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	2.93
212	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	1.73	- -	03/2024	310.24
213	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	388.89
214	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	22,879.22	11/2002 -	12/2022	1,017.96
215	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.12	03/2023 -	03/2025	369.35
216	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>							
217	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	55.57
218	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92
219	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	196.83
220	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	1,072.08	03/2016 -	03/2025	59.22
221	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	875.99	12/2026 -	12/2025	127.62
222	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	2,181.62	03/2023 -	12/2022	41.04
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	2,676.61	03/2016 -	03/2025	7.78
224	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95
225	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	124.58
226	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	1,438.76	12/2021 -	12/2021	53.75
227	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	35.42
228	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	1,795.61	12/2021 -	03/2022	20.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
229	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	799.01	03/2016 -	12/2021	50.15
230	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023	9.32
231	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	5.98
232	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	705.50	12/2024 -	12/2024	9.83
233	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	1,302.29	03/2019 -	06/2022	51.02
234	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	2,768.76	12/2024 -	03/2025	40.08
235	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,531.51	03/2020 -	12/2021	281.93
236	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	1,225.51	12/2024 -	12/2026	42.47
237	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	111.91
238	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	62.89
239	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	54.24
240	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	1,546.20	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>							
241	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
242	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	850.07	03/2009 -	03/2024	102.85
243	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	-	-	161.86
244	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	543.07	03/2023 -	03/2024	5.16
245	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,214.20	03/2021 -	03/2024	15.49
246	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	521.91	03/2020 -	06/2021	31.75
247	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	350.55	03/2014 -	03/2027	42.44
248	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	538.84
249	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	1,847.08	03/2000 -	03/2023	98.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
250	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,165.50	03/2022 -	03/2024	7.06
251	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	275.34
	<u>South East Central Railway</u>							
252	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	1,416.77	- -	-	268.37
253	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	291.76
254	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	84.69
255	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	116.46
256	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	378.60
257	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	1,131.91	12/2019 -	-	40.65
258	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	8.23
259	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>							
260	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
261	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	195.52	12/2016 -	08/2020	153.41
262	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	40.99	- -	03/2025	131.89
263	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
264	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
265	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	297.17	12/2018 -	06/2021	38.92
266	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	857.47	03/2020 -	12/2021	35.38
267	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	704.10	03/2021 -	12/2023	15.60
268	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>							
269	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	74.87	- -	12/2023	9.22

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
270	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	296.10	0.01	- -	12/2023	.03
271	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	1,111.69	- -	03/2025	17.95
272	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	0.34	- -	12/2023	14.14
273	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	68.97
274	HUBLI- CHIKKAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	1,119.96	03/2020 -	11/2021	43.14
275	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	881.92	03/2020 -	06/2021	33.31
276	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	613.57	03/2020 -	03/2021	35.47
277	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,528.14	03/2019 -	03/2021	15.84
278	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	998.00	463.35	03/2017 -	-	54.78
	<u>Southern Railway</u>							
279	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	301.67
280	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	465.83
281	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	262.68	- -	-	79.80
282	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	3.34	02/2019 -	-	247.32
283	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	130.17
284	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	0.62	- -	-	78.78
285	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	319.22	- -	03/2024	181.84
286	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	439.49	- -	12/2021	69.20
287	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	8.50	- -	-	46.09
288	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	1.63	- -	-	295.05
289	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	600.30	355.13	- -	09/2021	265.12
290	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,121.00	906.57	- -	04/2021	20.28

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
291	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	6.73	- -	-	45.43
292	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	1,699.64
293	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	332.00	265.41	04/2014 -	12/2020	77.29
294	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,246.00	0.81	- -	-	24.60
295	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	253.33
296	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11
	<u>West Central Railway</u>							
297	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	585.35
298	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57
299	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	254.64	03/2022 -	03/2023	114.32
	<u>Western Railway</u>							
300	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	5,912.40	2,143.20	03/2022 -	03/2024	68.75
301	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	72.42
302	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	411.62	126.05	03/2012 -	03/2023	29.34
303	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,959.74	1,784.02	03/2020 -	12/2023	136.19
304	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77
305	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,389.05	1,103.31	03/2021 -	12/2021	33.93
306	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	890.76	745.11	03/2019 -	10/2021	61.51
307	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494]	04/2017	691.84 -	1,017.91	650.65	03/2020 -	02/2021	47.13
	Total		2,30,736.04 -	4,78,634.95	205,245.45			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
308	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	175.00	- -	-	58.68
309	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	58.98
310	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	-	02/2012 -	-	76.21
311	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	295.96	10/2010 -	06/2021	69.30
312	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 -	389.45	349.94	05/2012 -	-	88.11
313	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	274.07	02/2013 -	-	47.65
314	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	223.10	08/2015 -	-	3.84
315	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	3.07
316	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	219.47	- -	-	3.72
317	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	36.24
318	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	-	46.51
319	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	77.26
320	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	267.46	05/2017 -	-	45.75
321	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	754.06	- -	12/2020	1.75
322	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	386.98	02/2011 -	-	34.06
323	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	318.64	08/2016 -	-	14.02

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
324	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84
325	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	343.70	10/2016 -	-	5.42
326	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	256.11	11/2015 -	-	6.21
327	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	325.42	10/2010 -	06/2021	93.80
328	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	238.01	- -	-	15.67
329	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	.26
330	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	.02
331	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	-	- -	-	.06
332	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	7.48	11/2019 -	-	.08
333	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871	08/2014	600.87 720.97	720.97	682.36	11/2017 -	05/2019	19.99
334	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	807.99	11/2017 -	06/2019	13.92
335	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	173.41	139.19	08/2018 -	03/2021	4.33
336	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	24.14	08/2019 -	11/2022	33.51
337	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	12/2021	11.18
338	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	330.94	08/2017 -	02/2020	42.48
339	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	170.05	08/2018 -	03/2021	4.45
340	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	315.57	12/2015 -	-	6.81

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
341	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	188.64	07/2019 -	-	.31
342	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	469.64	03/2017 -	-	46.51
343	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	345.46	03/2018 -	06/2021	9.23
344	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	322.24	292.10	09/2014 -	-	72.36
345	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	1,217.25	- -	-	2.93
346	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	255.42	08/2016 -	06/2021	15.19
347	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	397.33	09/2016 -	06/2021	14.24
348	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	399.36	10/2016 -	06/2021	17.04
349	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]	03/2010	179.89 271.00	271.00	270.91	03/2013 -	-	50.65
350	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]	12/2010	169.26 299.00	299.00	-	01/2019 -	-	76.65
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
351	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	11.57
352	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 -	252.79	97.07	04/2017 -	-	29.48
353	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 -	263.31	110.34	04/2017 -	-	29.48
354	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	290.94	08/2016 -	05/2021	3.73
355	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	255.15	10/2017 -	-	15.30
356	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]	10/2017	818.00 -	887.68	228.44	- -	-	8.52
	<u>National Highways Authority Of India</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
357	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	520.00	612.58	02/2009 -	-	85.71
358	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	325.28	04/2009 -	-	70.23
359	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	427.96	11/2008 -	-	159.95
360	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	251.39	11/2008 -	-	64.62
361	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019	4.99
362	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	-	234.27
363	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-	167.82
364	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
365	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	65.82
366	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	360.99	04/2008 -	12/2020	10.58
367	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
368	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	4,709.06	06/2015 -	-	16.67
369	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66
370	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	575.64	11/2013 -	01/2021	15.53
371	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	07/2012	291.36 -	469.31	459.07	01/2014 -	12/2020	61.08
372	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	52.73
373	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 [N24000360	04/2014	351.34 -	417.68	433.68	01/2016 -	12/2020	18.88
374	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367	04/2014	495.78 -	627.93	633.24	01/2016 -	01/2020	26.66
375	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	730.97	630.68	05/2018 -	06/2021	37.63
376	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437	10/2015	361.15 -	363.93	272.98	- -	-	.77
377	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 [N24000441	10/2015	593.26 -	690.17	585.57	05/2018 -	06/2021	16.34
378	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	889.83	- -	01/2020	11.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
379	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	68.71
380	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	512.04	-	10/2021	1.37
381	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
382	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	676.33	12/2017 -	-	66.88
383	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	400.60	-	-	6.11
384	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	186.70	-	-	1.33
385	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,472.01	-	-	41.78
386	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,160.00	-	-	21.50
387	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	712.15	04/2018 -	-	25.80
388	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 -	987.94	867.27	-	-	44.60
389	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	02/2016	997.15 -	1,115.95	975.08	03/2019 -	10/2019	11.91
390	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84
391	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	353.42	-	02/2021	7.53
392	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]	07/2016	458.03 -	486.00	432.16	-	-	6.11
393	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	86.37
394	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,282.04	-	-	94.94
395	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	312.79	08/2018 -	-	3.98
396	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82 -	1,727.66	1,674.80	-	01/2021	39.35
397	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-	16.55
398	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	1,304.00	-	03/2021	4.10

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
399	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	309.40	- -	-	8.35
400	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	-	19.25
401	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	1,039.23	03/2020 -	-	10.58
402	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	-	03/2020 -	-	31.88
403	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	3.40
404	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-	5.56
405	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	11/2020	1.06
406	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	-	5.70
407	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	352.32	03/2020 -	09/2021	.23
408	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	26.78	03/2020 -	-	9.38
409	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	951.13	03/2020 -	-	13.97
410	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	10.24
411	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	18.50
412	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	905.81	03/2020 -	-	41.54
413	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	1,085.47	03/2020 -	-	44.39
414	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	3.95
415	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78
416	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	492.81	09/2017 -	05/2021	9.67
417	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	407.94	- -	10/2020	10.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
418	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 -	276.17	64.77	-	-	.99
419	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 -	1,853.42	14.19	-	-	30.09
420	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 -	2,400.00	3,088.59	-	11/2021	20.28
421	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 -	2,450.00	2,244.98	-	-	12.50
422	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]	03/2018	1,261.98 -	1,952.20	934.06	-	07/2021	54.69
423	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 -	1,197.00	1,011.70	-	-	29.35
424	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 -	1,332.00	1,118.92	-	-	18.87
425	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 -	1,449.00	394.36	-	01/2021	37.71
426	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	2,499.00	1,539.65	03/2021	04/2021	63.05
427	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 -	537.17	38.11	-	-	8.26
428	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 -	1,261.05	299.11	-	03/2021	22.44
429	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,071.00	196.87	-	07/2021	5.32
430	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96 -	2,169.00	-	-	-	4.99
431	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 -	1,296.00	-	-	-	.12
432	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	931.21	268.17	-	07/2021	46.72
433	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 -	799.30	213.17	-	07/2021	.48

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
434	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	628.87	- -	-	25.68
435	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	231.66	- -	12/2021	.00
436	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	35.00	- -	-	27.86
437	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	164.95	- -	-	305.58
	Total		92,826.35 -	1,18,797.47	88,406.30			
	<u>RURAL DEVELOPMENT</u>							
	<u>Hindustan Steelwork Construction Limited</u>							
438	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2021	2.23
439	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	155.66	144.95	12/2015 -	03/2021	3.96
	Total		352.34 -	362.78	335.17			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
440	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	17,691.25	05/2015 -	07/2021	41.32
	Total		15,525.00 -	21,940.00	17,691.25			
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
441	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	84.97
	Total		13,334.00 -	24,664.00	16,594.00			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
442	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	8,446.13	12/2018 -	08/2022	18.69
	<u>Central Public Works Department</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
443	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	-	12/2013 -	-	132.80
	<u>Chennai Metro Rail Ltd</u>							
444	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-	30.53
	<u>Kochi Metro Rail Corporation Ltd</u>							
445	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	09/2020	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>							
446	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	44.39
	<u>National Building Construcion Corporation Ltd</u>							
447	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	10.71
	Total		58,069.05 -	76,455.87	52,593.61			
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
448	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	16,995.57	03/2020 -	04/2022	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
449	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	-	12/2021 -	12/2021	.97
	Total		10,382.83 -	55,782.90	16,995.57			
	Grand Total		7,31,133.44	12,01,389.25	710,036.94			

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(February 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,915.80	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,297.00	12/2015 -	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00 -	17,079.00	12,992.00	12/2016 -	03/2023	38.63	75
	Total		27,271.00 -	40,499.00	35,204.80				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	5.78	33
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	7.88	12
	Total		1,559.23 -	1,673.33	615.65				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	18.35	04/2018 -	12/2021	37.56	44
7	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	30.15	03/2017 -	10/2021	12.20	55
	<u>Neyveli Lignite Corporation</u>								
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,404.29	12/2015 -	02/2021	35.10	62
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00 -	17,237.80	11,135.69	11/2021 -	07/2022	.00	8
	<u>Singareni Colliers Company Limited</u>								
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	292.49	03/2015 -	03/2022	114.60	84
11	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	106.68	03/2019 -	03/2022	11.42	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
12	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	21.17	03/2015 -	03/2022	5.85	84
13	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>								
14	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	187.31	03/2015 -	03/2022	201.44	84
	<u>Western Coal Fields Limited</u>								
15	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	.00	36
16	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	15.41	12
	Total		25,847.74 -	28,730.84	19,769.12				
	<u>DPIIT</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>								
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,419.54	12/2019 -	10/2021	8.49	22
	Total		17,352.09 -	18,990.30	11,134.61				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
19	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	161.29	02/2018 -	04/2021	16.33	38
20	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	229.39	05/2017 -	03/2021	22.29	46
21	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	.13	24
22	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	481.52	11/2013 -	03/2021	20.55	88
	Total		1,043.69 -	1,199.69	1,130.71				
	<u>HOME AFFAIRS</u>								
	<u>Central Public Works Department</u>								
23	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	170.35	04/2018 -	12/2021	46.12	44

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
24	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	874.24	10/2019 -	12/2021	64.04	26
	Total		1,382.09 -	2,238.00	1,044.59				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
25	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	10.22	6
26	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	265.91	04/2019 -	04/2021	19.28	24
27	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	.57	52
28	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	1.85	20
	Total		1,525.49 -	1,614.15	1,079.50				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
29	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	17.80	02/2017 -	08/2022	117.11	66
30	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	711.00	06/2019 -	02/2022	35.54	32
31	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,852.63	08/2018 -	03/2021	14.33	31
	<u>Gas Authority Of India Limited</u>								
32	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	166.90	08/2020 -	05/2021	14.17	9
33	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,483.60	12/2012 -	02/2022	102.71	110
	<u>Hindustan Petroleum Corporation Limited</u>								
34	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	253.92	11/2020 -	06/2021	17.65	7
35	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	1,825.04	06/2021 -	08/2022	14.76	14
36	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	13,352.70	07/2020 -	07/2022	25.50	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Indian Oil Corporation Limited</u>								
37	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	08/2017	236.00 -	293.00	162.96	06/2020 -	09/2021	24.15	15
38	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 -	502.00	403.62	08/2019 -	06/2021	18.68	22
39	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	385.53	10/2017 -	03/2022	17.66	53
40	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00 -	3,027.90	1,755.66	03/2021 -	08/2021	66.09	5
41	PARADIP HYDERABAD PIPELINE - [N16000194	01/2015	2,321.00 -	3,338.00	2,750.24	12/2020 -	06/2021	43.82	6
42	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	3,409.77	12/2018 -	02/2022	33.98	38
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
43	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	637.00	443.62	03/2020 -	06/2021	9.64	15
	<u>Oil & Natural Gas Corporation Limited</u>								
44	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	07/2016	249.85 250.00	303.75	180.83	05/2020 -	05/2021	21.57	12
45	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,846.46	1,546.02	05/2013 -	03/2021	114.26	94
46	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,375.90	2,685.92	04/2018 -	05/2021	5.80	37
47	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	04/2019	3,228.80 -	3,976.67	974.84	03/2022 -	05/2023	23.16	14
	<u>Oil India Limited</u>								
48	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	490.24	455.00	03/2017 -	03/2021	39.05	48
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	652.10	136.05	02/2020 -	04/2021	19.89	14
	Total		52,355.37 -	69,279.48	39,953.65				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
50	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	9,897.59	8,825.13	09/2009 -	03/2022	152.52	150
51	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	19,992.43	13,233.01	09/2010 -	08/2023	218.08	155

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>National Thermal Power Corporation</u>								
52	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,841.21	03/2013 -	12/2022	96.99	117
53	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	10,016.10	7,966.63	07/2019 -	03/2021	9.00	20
54	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,680.05	07/2012 -	04/2021	97.38	105
55	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,140.91	11,641.13	12/2018 -	04/2021	4.86	28
56	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	15,105.22	13,657.43	01/2018 -	02/2021	29.79	37
57	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	11,612.82	06/2019 -	10/2022	7.12	40
58	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	15,463.61	05/2018 -	07/2021	33.47	38
59	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	18,308.58	10/2011 -	04/2022	145.16	126
	<u>North East Electric Power Corporation</u>								
60	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	8,154.49	12/2009 06/2016	-	217.49	134
	<u>Power Grid Corporation Of India Limited</u>								
61	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	157.07	07/2019 -	04/2021	17.99	21
62	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	477.66	11/2016 -	05/2021	4.61	54
63	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	2,825.43	07/2020 -	04/2021	14.11	9
64	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,630.84	10/2012 -	03/2021	5.14	101
65	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	2,541.14	12/2018 -	12/2021	31.08	36
66	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,002.54	12/2018 -	12/2021	92.02	36
67	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,869.26	08/2013 -	03/2022	32.24	103
	<u>Thdc India Limited</u>								
68	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,161.90	06/2013 -	12/2023	54.94	126
	Total		1,22,937.52 -	1,90,759.23	150,049.93				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
69	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89	12
70	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	73.73	24
71	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	98.88	24
	<u>Container Corporation Of India</u>								
72	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	25.65	36
	<u>East Central Railways</u>								
73	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	687.20	03/2012 -	07/2021	57.27	112
74	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	49.45	36
75	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	738.84	03/2019 -	05/2021	37.04	26
76	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	229.50	128
77	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	62.06	15
78	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	309.44	03/2021 -	03/2024	63.37	36
	<u>East Coast Railway</u>								
79	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	219.74	03/2020 -	03/2022	52.77	24
80	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	15.45	64
81	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	902.85	03/2020 -	03/2023	.07	36
82	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	38.43	34
83	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	845.24	06/2021 -	03/2025	137.80	45
84	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,413.99	03/2009 -	03/2026	29.71	204
	<u>Eastern Railways</u>								
85	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
86	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	374.08	03/2017 -	03/2025	20.30	96
87	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01	240
88	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	34.08	228
89	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	516.55	03/2020 -	03/2021	22.31	12
90	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	163.26	02/2012 -	03/2025	36.15	157
91	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	103.78	03/2017 -	03/2025	29.20	96
92	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	640.17	03/2016 -	03/2025	7.75	108
93	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	134.80	133
94	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	903.03	03/2019 12/2009	03/2025	36.22	72
95	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	355.79	03/2022 -	03/2025	133.39	36
<u>Indian Railway Construction Company Limited</u>									
96	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	.00	42
97	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	117.23	21
<u>Metropolitan Rapid Transport Projects</u>									
98	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	48.06	102
99	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	501.57	216
100	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91	63
<u>North Central Railway</u>									
101	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02	33
<u>North East Frontier Railway</u>									
102	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
103	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	800.00	795.88	03/2019 -	03/2021	154.78	24
104	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,105.00	787.79	03/2019 -	03/2023	186.86	48
105	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,133.64	03/2021 -	05/2021	115.07	2
106	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING [N22000183]	04/2013	1,798.00 -	2,042.51	69.92	03/2019 -	03/2024	13.60	60
107	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	968.95	03/2019 -	03/2024	302.54	60
108	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,478.05	03/2022 -	03/2023	32.15	12
109	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,645.92	12/2008 -	04/2021	284.80	148
110	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	3,816.20	03/2014 -	03/2023	130.69	108
111	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,911.00	1,125.27	03/2015 -	12/2024	197.05	117
112	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	12/2023	542.04	96
113	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	10,777.52	03/2011 -	12/2023	175.34	153
	<u>North Eastern Railway</u>								
114	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	.16	68
115	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	61.80	37
	<u>North Western Railway</u>								
116	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	337.30	11/2019 -	03/2021	75.73	16
117	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	324.37	12/2019 -	02/2021	60.52	14
118	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	172.41	03/2020 -	04/2022	16.97	25
119	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	691.34	02/2019 -	11/2021	109.82	33
	<u>Northern Railway</u>								
120	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	37.44	63
121	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	658.97	12/2011 -	06/2021	211.31	114
122	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.12	03/2023 -	03/2025	369.35	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
123	NANGALDAM-TALWARA(NL),NR - [N220100188	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	388.89	140
124	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [N220100133	03/1995	2,500.00 -	27,949.00	22,879.22	11/2002 -	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>								
125	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213	04/2012	632.68 -	950.00	799.01	03/2016 -	12/2021	50.15	69
126	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	5.98	33
127	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,400.00	1,302.29	03/2019 -	06/2022	51.02	39
128	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	62.89	39
129	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	54.24	24
130	BINA - KOTA DOUBLING WITH RE - [N22000414	04/2011	1,485.85 -	1,835.83	1,546.20	12/2020 -	12/2021	23.55	12
131	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,548.66 -	1,868.89	1,795.61	12/2021 -	03/2022	20.68	3
132	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	111.91	21
133	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N220100325	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92	88
134	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,725.00	2,531.51	03/2020 -	12/2021	281.93	21
135	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95	141
136	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	3,327.72	1,225.51	12/2024 -	12/2026	42.47	24
137	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	124.58	24
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	2,676.61	03/2016 -	03/2025	7.78	108
139	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	1,072.08	03/2016 -	03/2025	59.22	108
140	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	22,716.11	2,768.76	12/2024 -	03/2025	40.08	3
	<u>South Central Railway</u>								
141	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	275.34	9

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
142	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	521.91	03/2020 -	06/2021	31.75	15
143	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	543.07	03/2023 -	03/2024	5.16	12
144	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	850.07	03/2009 -	03/2024	102.85	180
145	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,214.20	03/2021 -	03/2024	15.49	36
146	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	350.55	03/2014 -	03/2027	42.44	156
147	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	1,847.08	03/2000 -	03/2023	98.57	276
148	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,165.50	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>								
149	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	378.60	36
150	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	116.46	34
151	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	.07	24
152	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	291.76	12
153	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	8.23	33
154	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	84.69	9
	<u>South Eastern Railway</u>								
155	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	297.17	12/2018 -	06/2021	38.92	30
156	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99	120
157	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	857.47	03/2020 -	12/2021	35.38	21
158	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	704.10	03/2021 -	12/2023	15.60	33
159	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>								
160	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	613.57	03/2020 -	03/2021	35.47	12
161	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	881.92	03/2020 -	06/2021	33.31	15

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
162	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	1,119.96	03/2020 -	11/2021	43.14	20
163	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,528.14	03/2019 -	03/2021	15.84	24
	<u>Southern Railway</u>								
164	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	253.33	198
165	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11	27
166	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	465.83	60
167	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	1,699.64	105
168	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	301.67	73
	<u>West Central Railway</u>								
169	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	254.64	03/2022 -	03/2023	114.32	12
170	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	585.35	24
171	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
172	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	411.62	126.05	03/2012 -	03/2023	29.34	132
173	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	890.76	745.11	03/2019 -	10/2021	61.51	31
174	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	04/2017	691.84 -	1,017.91	650.65	03/2020 -	02/2021	47.13	11
175	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77	48
176	VIRAMGAM-SAMAKHALI (DL) - [N22000145]	04/2011	1,037.15 -	1,389.05	1,103.31	03/2021 -	12/2021	33.93	9
177	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,959.74	1,784.02	03/2020 -	12/2023	136.19	45
178	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	5,912.40	2,143.20	03/2022 -	03/2024	68.75	24
	Total		1,39,971.62 -	2,78,974.12	137,892.54				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
179	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	173.41	139.19	08/2018 -	03/2021	4.33	31
180	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	24.14	08/2019 -	11/2022	33.51	39
181	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	170.05	08/2018 -	03/2021	4.45	31
182	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	59.92	08/2019 -	12/2021	11.18	28
183	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	295.96	10/2010 -	06/2021	69.30	128
184	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	325.42	10/2010 -	06/2021	93.80	128
185	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	345.46	03/2018 -	06/2021	9.23	39
186	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	397.33	09/2016 -	06/2021	14.24	57
187	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	255.42	08/2016 -	06/2021	15.19	58
188	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	399.36	10/2016 -	06/2021	17.04	56
189	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	77.26	47
190	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84	73
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
191	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	290.94	08/2016 -	05/2021	3.73	57
	<u>National Highways Authority Of India</u>								
192	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	585.57	05/2018 -	06/2021	16.34	37
193	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	630.68	05/2018 -	06/2021	37.63	37

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
194	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	352.32	03/2020 -	09/2021	.23	18
195	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	3.95	15
196	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	492.81	09/2017 -	05/2021	9.67	44
197	REHABILITATION AND UPGRADE BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	10.24	15
198	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78	8
199	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	1,539.65	03/2021 -	04/2021	63.05	1
200	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	52.73	71
201	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66	105
	Total		18,437.24 -	22,896.45	15,431.39				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
202	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	155.66	144.95	12/2015 -	03/2021	3.96	63
203	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2021	2.23	51
	Total		352.34 -	362.78	335.17				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
204	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	17,691.25	05/2015 -	07/2021	41.32	74
	Total		15,525.00 -	21,940.00	17,691.25				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
205	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	84.97	71

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		13,334.00 -	24,664.00	16,594.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
206	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	8,446.13	12/2018 -	08/2022	18.69	44
	<u>Mumbai Metro Rail Corporation Ltd</u>								
207	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	44.39	98
	Total		33,909.00 -	46,193.00	25,485.49				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
208	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	16,995.57	03/2020 -	04/2022	447.22	25
	Total		10,151.04 -	55,548.87	16,995.57				
	Grand Total		4,82,954.46	8,05,563.24	490,407.97				

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75				2/6
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
2	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80	229.80	80.21	-	05/2022	0(R3)	16/26
3	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20	730.20	65.94	-	05/2023	0(R3)	12/17
	Total		818.00	960.00	146.15				28/43
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
4	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	156.64	128.08	-	03/2021	-	0/0
5	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84	268.84	239.89	-	03/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	358.42	-	06/2021	-	0/0
7	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	460.56	-	06/2021	-	0/0
8	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	455.70	-	06/2021	-	0/0
	Total		2,261.40	2,261.48	1,642.65				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
9	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00	735.20	379.57	-	03/2021	-	0/0
10	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07	3,550.00	3,528.48	-	03/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
11	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	1,483.14	1,194.00	- -	03/2022	-	0/0
12	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	2,066.78	1,529.08	- -	03/2023	-	0/0
13	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	1,625.87	767.07	- -	03/2023	-	0/0
14	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,858.75	385.87	- -	03/2023	-	0/0
15	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	24.31	- -	03/2023	-	0/0
16	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	1,470.50	1,123.21	- -	03/2023	-	0/0
17	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	614.45	340.21	- -	12/2023	-	0/0
18	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	-	0/0
19	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
20	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	519.33	266.24	- -	03/2025	-	0/0
	<u>Eastern Railways</u>								
21	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	502.48	422.81	- -	03/2021	-	0/0
22	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	283.97	- -	03/2022	-	0/0
23	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	272.20	239.06	- -	03/2022	-	0/0
24	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	356.54	- -	03/2024	-	0/0
25	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
26	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	11.32	- -	03/2025	-	0/0
27	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
28	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.11	- -	03/2025	-	0/0
29	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
30	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
31	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	- -	03/2025	-	0/0
32	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
33	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
34	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	287.09	- -	12/2021	-	0/0
35	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.74	- -	03/2022	-	0/0
	<u>North Eastern Railway</u>								
36	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	714.34	63.70	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
37	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	791.39	572.99	- -	03/2023	-	0/0
38	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
39	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	127.91	- -	09/2023	-	0/0
40	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	359.00	111.51	- -	03/2024	-	0/0
41	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	<u>South Eastern Railway</u>								
42	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
43	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,967.00	74.87	- -	12/2023	-	0/0
44	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	558.00	-	- -	12/2023	-	0/0
45	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	296.10	.01	- -	12/2023	-	0/0
46	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	- -	12/2023	-	0/0
47	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
48	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	-	12/2023	-	0/0
49	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	3,911.65	157.01	-	12/2024	-	0/0
50	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,432.50	1,111.69	-	03/2025	-	2/2
	<u>Southern Railway</u>								
51	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,121.00	906.57	-	02/2021	2(R3)	0/0
52	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	600.30	355.13	-	10/2021	-1(R3)	0/0
53	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	457.08	439.49	-	12/2021	-	0/0
54	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,205.00	2.28	-	03/2024	0(R3)	0/0
55	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	559.95	319.22	-	03/2024	-	0/0
56	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	582.83	239.11	-	12/2025	-	0/0
	<u>Western Railway</u>								
57	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	179.19	-	03/2024	0(R3)	0/0
	Total		25,127.57 -	45,001.02	16,172.60				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
58	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	291.05	200.71	-	03/2021	0(R3)	0/0
59	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	178.13	139.26	-	03/2021	-	0/0
60	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	257.01	-	03/2021	3(R3)	0/0
61	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	74.00	-	09/2021	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	119.35	- -	09/2021	-	2/4
63	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	71.60	- -	04/2022	-	0/4
64	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	61.55	- -	04/2022	-	0/4
National Highways Authority Of India									
65	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	353.42	- -	02/2021	-	0/0
66	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	565.09	550.75	- -	02/2021	-	0/0
67	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	-	0/0
68	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,145.31	1,304.00	- -	03/2021	-	0/0
69	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	1,261.05	299.11	- -	03/2021	-	0/0
70	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	1,005.08	-	- -	03/2021	-	0/0
71	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	621.00	591.21	- -	04/2021	-	2/3
72	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	189.70	- -	04/2021	-	0/0
73	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,565.00	- -	05/2021	-	0/0
74	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	240.60	- -	05/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
75	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	478.74	127.42	- -	05/2021	-	0/0
76	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	-	0/0
77	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	227.63	- -	06/2021	-	0/0
78	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	127.61	- -	06/2021	-	0/0
79	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	276.59	- -	06/2021	-	0/0
80	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	261.74	- -	06/2021	-	0/0
81	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0
82	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	102.70	- -	06/2021	-	0/0
83	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	25.40	- -	06/2021	-	0/0
84	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	86.83	- -	06/2021	-	0/0
85	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
86	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	456.80	- -	07/2021	-	0/0
87	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	887.07	- -	07/2021	-	3/4
88	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	271.89	- -	07/2021	-	1/4

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
89	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0
90	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,166.26	220.78	- -	07/2021	-	0/0
91	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
92	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	193.26	- -	07/2021	-	0/0
93	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	196.87	- -	07/2021	-	0/0
94	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	584.17	- -	07/2021	-	0/0
95	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	931.21	268.17	- -	07/2021	-	0/0
96	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	213.17	- -	07/2021	-	0/0
97	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	72.87	- -	07/2021	-	0/0
98	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	224.81	- -	08/2021	-	3/4
99	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	411.79	- -	08/2021	-	0/1
100	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0
101	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
102	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	162.72	- 02/2021	08/2021	6(R3)	0/0
103	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
104	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,337.98	- -	09/2021	-	0/0
105	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	303.46	- -	09/2021	-	0/0
106	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
107	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
108	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	-	0/0
109	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
110	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	231.66	- -	12/2021	-	0/3
111	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	127.37	- 08/2021	02/2022	6(R3)	0/0
112	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	425.85	- -	02/2022	-	1/4
113	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	213.52	- -	03/2022	-	0/1
114	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	332.04	- -	03/2022	-	0/0
	Total		48,240.03 -	49,222.89	24,783.76				14/41

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								
115	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	651.85	- -	07/2022	-	0/9
	Total		2,694.00 -	2,694.00	651.85				0/9
	Grand Total		79,413.73	1,00,412.12	43,550.76				46/101

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 -	-
	Total		438.28 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TALABIRA II AND III OCP - [N06000189]NLC, ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
5	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	06/2015 03/2025	-
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Western Coal Fields Limited</u>				
10	SINGHORI OC MINE - [N06000130]WCL, MAHARASHTRA	06/2015	205.49 -	03/2020 -	03/2020
11	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020
12	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
13	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL, MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
14	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
	Total		13,502.75 -		
	<u>MINES</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Aluminum Company Limited (Nalco)</u>				
15	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 06/2021	12/2020
16	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		700.62 -		
	<u>STEEL</u>				
	<u>Rastriya Ispat Nigam Limited</u>				
17	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 12/2020	12/2020
	Total		2,858.00 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
18	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	01/2021
	<u>Hindustan Petroleum Corporation Limited</u>				
19	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
20	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
21	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	10/2019 11/2020	-
	Total		7,719.64 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	02/2017 06/2020	01/2021
24	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 01/2021	01/2021
25	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
26	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-
27	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
28	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
29	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
30	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
	<u>Power Grid Corporation Of India Limited</u>				
31	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 516.12	01/2019 04/2020	04/2020
32	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 04/2020	05/2020
33	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 04/2020	07/2020
34	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 06/2020	09/2020
35	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 06/2020	09/2020
36	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 902.49	10/2017 12/2020	01/2021
37	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
38	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
39	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	-
40	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
41	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-
42	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-
43	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
	Total		66,443.45 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
44	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 12/2020	-
	Total		1,554.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
45	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
46	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
47	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
48	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
49	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
50	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	12/2020
51	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
	Total		1,910.90 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
52	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 03/2020	03/2020
	<u>Container Corporation Of India</u>				
53	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 12/2020	12/2020
54	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-
55	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
56	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
57	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
58	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
59	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
60	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
61	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	-
62	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
63	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-
64	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
65	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
66	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
67	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
68	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
69	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
70	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
71	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
72	HAJIPUR-RAMDALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
73	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
74	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-
	<u>Eastern Railways</u>				
75	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				
76	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
77	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
78	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
79	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
80	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
81	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
	<u>North East Frontier Railway</u>				
82	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
83	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
84	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-
85	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
87	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
88	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
89	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
90	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
91	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
92	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
93	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
94	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
95	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
96	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-
97	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
98	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
99	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
100	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
101	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
102	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-
103	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
	<u>Railway Electrification</u>				
104	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
105	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00 -	- -	-
107	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	761.37 -	- -	-
108	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH	04/2013	829.00 -	- -	-
109	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
110	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	08/2020
111	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR, CHHATISGARH	04/2008	872.00 -	12/2019 -	10/2020
	<u>South Eastern Railway</u>				
112	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
113	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
114	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>South Western Railway</u>				
115	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 -	03/2017 -	-
	<u>Southern Railway</u>				
116	OMALUR-METTURDAM- DOUBLING WITH ELCTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU	10/2013	187.26 -	04/2014 03/2021	12/2020
117	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	1,566.00 -	- -	-
118	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	227.40 -	- -	-
119	ATTIPPATTU PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	151.84 -	02/2019 -	-
120	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-
121	KUMBALAM-TURAVUR - [N22000191]SR, KERALA	04/2011	252.96 -	- -	-
122	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 -	- -	-
123	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	- -	-
124	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR, KERALA	02/2015	1,431.90 -	- -	-
125	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR, KERALA	02/2015	1,000.00 -	- -	-
126	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR, KERALA	02/2012	550.00 -	03/2016 -	-
127	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR, TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
128	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
129	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
130	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
131	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
132	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
133	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		76,394.79 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
134	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
135	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 -	08/2020
136	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 -	09/2020
137	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 -	12/2020
138	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	01/2018 -	12/2020
139	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 -	02/2017 06/2021	02/2019
140	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
141	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 07/2021	05/2019
142	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
143	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 05/2021	08/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
144	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933])MoRTH,ANDHRA PRADESH	02/2017	429.43 -	11/2017 04/2021	11/2019
145	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020
146	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	06/2020
147	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 -	08/2018 05/2021	08/2020
148	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
149	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020
150	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
151	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
152	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020
153	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020
154	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020
155	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	12/2020
156	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2020	12/2020
157	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020
158	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020
159	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020
160	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 04/2021	01/2021
161	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
162	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021
163	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
164	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
165	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
166	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
167	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
168	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
169	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
170	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
171	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
172	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
173	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
174	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
175	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
176	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
177	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
178	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
179	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
180	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
181	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
182	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
183	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
184	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
185	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
186	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
187	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
188	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 12/2020	-
189	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 12/2020	-
190	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 12/2020	-
191	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
192	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
193	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
194	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
195	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
196	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
197	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
198	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
199	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
200	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
201	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
202	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
203	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
205	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
206	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
207	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
208	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 390.73	05/2017 -	-
209	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
210	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
214	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
215	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
216	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
217	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
218	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
219	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
220	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
221	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
222	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
223	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
224	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
225	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
226	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIK 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
229	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
230	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
233	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
234	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
235	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
236	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
237	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-
238	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
239	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
240	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
241	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
242	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
243	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
244	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
245	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
246	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
247	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
248	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
249	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
250	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
251	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
252	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
253	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
254	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-
255	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
256	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
257	REHABILITATION AND UPGADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
258	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
259	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
260	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
261	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-
262	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
263	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-
264	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
265	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
266	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
267	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
268	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
269	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
270	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
271	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
272	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
273	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
274	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
275	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
276	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
277	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-
278	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-
279	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	-
280	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
281	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
282	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-
283	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
284	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
285	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
286	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
287	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
288	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
289	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
290	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
291	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
292	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
293	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
294	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
295	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
296	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
297	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
298	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
299	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
300	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
301	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-
302	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
303	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
304	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
305	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
306	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
307	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
308	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
309	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
310	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
311	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
312	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
313	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
314	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
315	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
316	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
317	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
318	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
319	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
320	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
321	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
322	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
323	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
324	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
325	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
326	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
327	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
328	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
329	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
330	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
331	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
332	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
333	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
334	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
335	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
336	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
337	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
338	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
339	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
340	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
341	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
342	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
343	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
344	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
345	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
346	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
347	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
348	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
349	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
350	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
351	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
352	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
353	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
354	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
355	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
356	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
357	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
358	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
359	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
360	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
361	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
362	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
363	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
364	DHANGRIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
365	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
366	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
367	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
368	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
369	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
370	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
371	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
372	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
373	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
374	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
375	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
376	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
377	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
378	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
379	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
380	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
381	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
382	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
383	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
384	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
385	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
386	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
387	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
388	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
389	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
390	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
391	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
392	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
393	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
394	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
395	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
396	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
397	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
398	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
399	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
400	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
401	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
402	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
403	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
404	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
405	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
406	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
407	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
408	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
409	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
410	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
411	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
412	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
413	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
414	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
415	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
416	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
417	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
418	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-
419	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
420	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
421	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
422	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
423	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
424	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
425	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
426	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
427	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
428	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
429	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
430	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
431	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
432	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
433	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
434	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
435	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-
436	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-
437	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	-
438	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
439	REHABILITATION AND UPGRADATION OF PRATAPGARH- ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-
440	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
441	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
442	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-
443	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
444	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
445	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
446	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
447	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
448	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGECHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
449	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
450	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
451	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
452	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
453	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
454	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.90 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
455	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
456	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
457	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
458	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
459	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
460	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-
461	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2020	-
462	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
463	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
464	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
465	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-
466	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
467	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-
468	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
469	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
470	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-
471	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
472	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-
473	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
474	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
475	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
476	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
477	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
478	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
479	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
480	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
481	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
482	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
483	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
484	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
485	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2020
486	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	12/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
487	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
488	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
489	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
490	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
491	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
492	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
493	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
494	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
495	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
496	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
497	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
498	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
499	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-
500	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
501	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
502	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
503	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
504	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
505	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
506	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
507	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
508	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
509	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
510	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
511	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
512	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
513	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
514	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
515	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
516	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
517	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
518	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
519	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
520	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
521	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
522	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
523	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
524	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
525	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
526	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
527	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
528	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
529	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
530	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
531	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
532	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
533	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
534	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
535	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
National Highways Authority Of India					
536	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	01/2020
537	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	02/2019
538	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	08/2020
539	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	08/2020
540	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	09/2020
541	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
542	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	11/2020
543	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	11/2020
544	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI, BIHAR	10/2013	446.97 -	11/2020 -	11/2020
545	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI, BIHAR	10/2013	464.09 -	11/2020 -	11/2020
546	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2020
547	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI, MADHYA PRADESH	09/2017	374.40 -	09/2017 -	12/2020
548	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI, BIHAR	10/2013	649.90 -	12/2020 -	12/2020
549	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
550	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
551	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI, MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
552	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 -	06/2019
553	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	04/2010 -	07/2019
554	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	06/2008 -	09/2019
555	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
556	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 1,115.95	03/2019 10/2019	10/2019
557	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020
558	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- 01/2020	01/2020
559	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
560	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
561	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
562	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	03/2008 -	08/2020
563	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
564	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
565	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	09/2020
566	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
567	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
568	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA	12/2017	404.94 -	- -	10/2020
569	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
570	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
571	4-LANNING OF WARANGA-MAHAGAON SECTION (KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020
572	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI, RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020
573	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	04/2008 -	12/2020
574	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020
575	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020
576	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
577	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020
578	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020
579	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
580	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
581	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021
582	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	01/2021
583	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN	09/2016	1,239.82 -	- -	01/2021
584	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI, MADHYA PRADESH	09/2017	990.61 -	09/2017 -	01/2021
585	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
586	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- -	01/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
587	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
588	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
589	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
590	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
591	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
592	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
593	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
594	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
595	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
596	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
597	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
598	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
599	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
600	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
601	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
602	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
603	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
604	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
605	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
606	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
607	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
608	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
609	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
610	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
611	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
612	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
613	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	-
614	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
615	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
616	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
617	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
618	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
619	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	-
620	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	-
621	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
622	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	-
623	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
624	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
625	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
626	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
627	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	-
628	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
629	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	-	-
630	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
631	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	-
632	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	-
633	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	-
634	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
635	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
636	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
637	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
638	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-
639	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
640	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
641	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
642	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
643	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
644	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
645	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
646	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
647	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
648	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
649	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
650	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
651	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
652	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
653	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-
654	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
655	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
656	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
657	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
658	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-
659	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
660	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
661	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
662	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-
663	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
664	MEERUT-BULANDSHAHAH - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-
665	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
666	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
667	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
668	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
669	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
670	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-
671	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-
672	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
673	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
674	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
675	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-
676	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	- -	-
677	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 -	- -	-
678	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-
679	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-
680	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
681	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
682	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
683	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
684	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
685	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
686	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
687	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
688	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
689	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 486.00	- -	-
690	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
691	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
692	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
693	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
694	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
695	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-
696	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
697	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
698	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-
699	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-
700	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
701	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
702	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
703	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
704	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
705	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
706	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
707	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
708	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
709	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	-
710	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
711	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
712	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
713	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
714	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
715	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
716	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
717	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
718	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
719	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
720	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
721	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
722	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
723	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
724	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
725	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
726	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
727	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
728	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
729	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
730	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
731	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
732	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
733	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
734	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
735	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
736	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
737	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
738	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
739	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
740	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
741	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
742	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
743	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
744	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
745	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
746	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
747	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
748	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
749	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
750	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
751	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
752	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
753	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
754	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
755	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
756	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
757	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
758	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
759	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
760	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
761	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
762	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-
763	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-
764	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-
765	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
766	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-
767	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI, HARYANA	03/2018	307.79 -	- -	-
768	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-
769	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
770	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-
771	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	- -	-
772	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA	03/2018	198.05 -	- -	-
773	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA	03/2018	181.78 -	- -	-
774	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI, HARYANA	03/2018	551.58 -	- -	-
775	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA	03/2018	642.13 -	- -	-
776	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
777	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- 02/2020	-
778	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
779	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
780	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
781	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-
782	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-
783	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-
784	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
785	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-
786	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
787	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
788	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
	Total		3,82,637.63 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Central Public Works Department</u>				
789	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	03/2018 -	-
	Total		248.20 -		
	<u>URBAN DEVELOPMENT</u>				
790	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 02/2021	11/2020
791	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
792	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
793	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	11/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
794	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO - [N28000149]CPWD, CHHATISGARH	05/2019	299.97 -	09/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
795	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
796	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
797	KOCHI METRO RAIL PROJECT - [N28000081]KMRL, KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
798	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
799	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-
	<u>National Building Construction Corporation Ltd</u>				
800	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI	06/2012	4,264.00 -	11/2019 -	-
	Total		41,949.94 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
801	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB, MAHARASHTRA	03/2017	233.57 -	12/2019 -	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
802	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 -	09/2020 -	-
803	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR	04/2015	268.63 -	01/2021 -	-
	<u>Delhi Jal Board</u>				
804	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB, DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Uttar Pradesh Jal Nigam</u>				
805	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP Jal Nigam, UTTAR PRADESH	02/2011	279.91 -	12/2019 -	01/2021
	<u>Uttarakhand Pey Jal Nigam</u>				
806	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UK Jal Nigam, UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
	Total		1,654.42 -		
	<u>COMMERCE</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Building Construcion Corporation Ltd</u>				
807	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
808	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
809	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
810	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
811	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
812	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				
813	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
814	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	<u>Rail India Technical And Economic Service</u>				
815	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		2,641.45 -		
	Grand Total		6,00,956.71		

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	166.90	05/2013 -	08/2021	-55.37	99
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	364.59	12/2009 -	-	-39.64	0
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	469.31	01/2014 -	12/2020	61.08	83
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
5	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	-	.00	0
6	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
7	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	06/2020	.00	46
8	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
9	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
10	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	-	.00	0
11	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	591.00	11/2013 -	01/2021	15.53	86
12	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	-	.00	0
13	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
14	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
15	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	-	.00	0
16	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	-	.00	92
17	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (February 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	-	.00	0
19	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	-	.00	0
20	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	88
21	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	-	.00	0
22	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2022	.00	103
23	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2021	.00	81
24	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	05/2021	.00	93
25	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	10/2020	.00	76
26	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
27	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
28	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88 -	1,226.88	02/2021 -	-	.00	0
29	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	-	.00	0
30	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	0
31	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	-	.00	0
32	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	-	.00	0
33	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	-	.00	0
34	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
35	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	-	.00	0
36	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	-	.00	0
37	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	-	.00	0
39	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10 -	1,601.10	02/2021 -	-	.00	0
40	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
41	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	12/2020	.00	52
42	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	01/2019 -	-	.00	0
43	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	-	.00	0
44	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	-	.00	0
45	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	03/2021	.00	96
46	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	-	.00	0
47	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	-	.00	32
48	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	-	.00	0
49	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	09/2020	.00	62
50	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	-	.00	0
51	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	04/2019 -	09/2021	.00	29
52	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00 -	2,159.00	01/2019 -	-	.00	0
53	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	-	.00	0
54	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	2,360.65	- -	-	41.78	0
55	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
56	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
57	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	03/2021	52.73	71
58	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	-	167.82	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (February 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		74,577.61 -	79,826.06				
	Grand Total		74,577.61	79,826.06				

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,915.80	09/2010 09/2016	10/2022
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,297.00	12/2015 -	02/2022
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12,992.00	12/2016 -	03/2023
	Total		27,271.00 -	40,499.00	35,204.80		
	<u>COAL</u>						
	<u>Singareni Colliers Company Limited</u>						
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	292.49	03/2015 -	03/2022
	<u>Western Coal Fields Limited</u>						
5	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	246.55	03/2019 -	-
	Total		361.44 -	547.96	539.04		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
6	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	499.23	481.52	11/2013 -	03/2021
7	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
8	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	161.29	02/2018 -	04/2021
9	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
10	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	229.39	05/2017 -	03/2021
11	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
	Total		1,739.63 -	2,028.35	1,928.43		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,852.63	08/2018 11/2019	03/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Indian Oil Corporation Limited</u>						
13	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	3,338.00	2,750.24	12/2020 -	06/2021
	<u>Oil India Limited</u>						
14	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN [N16000167]	7/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021
	Total		7,261.85 -	9,074.20	8,057.87		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
15	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	11,130.00	02/2017 06/2020	01/2021
16	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-
17	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-
	<u>North East Electric Power Corporation</u>						
18	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	8,154.49	12/2009 02/2021	02/2021
	<u>Power Grid Corporation Of India Limited</u>						
19	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	-
20	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	456.53	02/2019 05/2020	03/2021
	Total		34,897.68 -	45,077.65	44,117.41		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
21	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	315.00	312.62	03/2019 03/2020	03/2020
22	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023
	<u>Container Corporation Of India</u>						
23	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	487.13	434.63	03/2018 -	03/2021
	<u>East Central Railways</u>						
24	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,550.00	3,528.48	- -	03/2022
25	KODERMA-TILAIYA (NL), ECR - [220100305]	4/2002	459.91 -	1,625.87	767.07	- -	03/2023
26	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,194.00	- -	03/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
27	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	4/1998	180.82 -	726.31	543.57	- -	-
28	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	546.71	541.83	07/2014 -	-
29	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	480.00	477.72	- -	-
30	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	4/2004	372.14 -	1,470.50	1,123.21	- -	03/2023
31	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	4/2006	378.56 -	1,858.75	385.87	- -	03/2023
32	SAKRI-HASANPUR ROAD (NL) - [N22000171]	4/1999	325.00 -	735.20	379.57	- -	03/2021
33	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	738.84	03/2019 -	05/2021
34	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	4/2003	528.65 -	2,066.78	1,529.08	- -	03/2023
35	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	4/1997	162.87 -	614.45	340.21	- -	12/2023
36	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022
37	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	4/1996	477.88 283.95	751.55	687.20	03/2012 -	07/2021
	<u>Eastern Railways</u>						
38	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	4/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024
39	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	4/2010	365.17 -	439.30	374.08	03/2017 -	03/2025
40	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	495.10	283.97	- -	03/2022
41	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	565.00	538.28	- -	05/2019
42	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	502.48	422.81	- -	03/2021
43	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	356.54	- -	03/2024
	<u>Metropolitan Rapid Transport Projects</u>						
44	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
45	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022
46	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	<u>North Central Railway</u>						
47	ETAWAH-MAINPURI (NL),NCR - [220100318]	4/1997	120.00 -	346.00	345.51	12/2008 -	-
	<u>North East Frontier Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	4/2000	1,180.19 -	4,541.38	3,645.92	12/2008 -	04/2021
49	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,105.00	787.79	03/2019 -	03/2023
50	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	12,264.15	10,777.52	03/2011 -	12/2023
51	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	2/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-
52	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	760.00	801.53	12/2021 -	04/2021
53	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	1,873.21	1,133.64	03/2021 -	05/2021
54	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	800.00	795.88	03/2019 -	03/2021
55	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,871.00	1,082.01	- -	-
56	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	373.87	287.09	- -	12/2021
<u>North Eastern Railway</u>							
57	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
58	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	506.99	01/2019 -	02/2022
<u>North Western Railway</u>							
59	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	860.41	691.34	02/2019 -	11/2021
60	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	395.00	324.37	12/2019 -	02/2021
61	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	350.45	251.41	10/2018 -	-
62	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	525.00	459.43	02/2019 -	02/2020
63	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	375.00	337.30	11/2019 -	03/2021
<u>Northern Railway</u>							
64	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	658.97	12/2011 -	06/2021
65	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	859.00	852.73	03/2016 -	06/2021
66	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024
<u>Rail Vikas Nigam Ltd.</u>							
67	HARIDASPUR-PARADEEP(NL) - [220100285]	4/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-
68	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
69	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-
70	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,835.83	1,546.20	12/2020 -	12/2021
71	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022
72	BANASPAANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022
73	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021
74	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	2,725.00	2,531.51	03/2020 -	12/2021
75	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,400.00	1,302.29	03/2019 -	06/2022
76	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	950.00	799.01	03/2016 -	12/2021
77	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,868.89	1,795.61	12/2021 -	03/2022
78	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021
79	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,438.76	12/2021 -	12/2021
80	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	3/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022
81	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,181.62	03/2023 -	12/2022
	<u>South Central Railway</u>						
82	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
83	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	4/1997	1,723.00 1.00	3,421.35	1,847.08	03/2000 -	03/2023
	<u>South East Central Railway</u>						
84	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	4/2005	383.79 -	1,413.76	1,416.77	- -	08/2020
85	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021
86	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021
87	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,226.51	1,131.91	12/2019 -	10/2020
	<u>South Eastern Railway</u>						
88	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	377.00	195.52	12/2016 -	08/2020
	<u>South Western Railway</u>						
89	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	1,147.00	881.92	03/2020 06/2021	06/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
90	ARSIKERE-TUMKUR - [N22000332 <u>Southern Railway</u>	3/2015	578.00 -	783.00	613.57	03/2020 03/2021	03/2021
91	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'- AGASTIYAMPALLI - [N22000079	9/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025
92	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	9/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025
93	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	2/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022
94	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	2/1996	268.87 -	950.00	928.36	03/2005 -	09/2021
95	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	332.00	265.41	04/2014 03/2021	12/2020
96	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	4/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027
97	MADURAI-BODINAYAKKANUR - [N22000201	4/2008	164.41 -	600.30	355.13	- 10/2021	09/2021
98	KURUPPANTHARA-CHINGAVANAM - [N22000190	4/2007	270.14 -	457.08	439.49	- -	12/2021
99	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	4/1999	198.68 -	559.95	319.22	- -	03/2024
	<u>West Central Railway</u>						
100	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023
101	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	9/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025
	<u>Western Railway</u>						
102	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	202.35	809.40	03/2011 -	-
	Total		55,383.02 -	1,36,989.65	99,536.48		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
103	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020
104	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238	5/2016	307.70 -	307.70	312.82	01/2017 -	-
105	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	322.24	292.10	09/2014 12/2020	-
106	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	3/2018	325.86 -	325.86	326.88	10/2018 -	-
107	KOLHA TO NASRATPUR - [N24001111	4/2016	281.78 282.00	281.78	362.73	04/2019 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	KUNDRA TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	254.75	12/2019 -	-
109	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	3/2018	297.12 294.00	294.12	373.98	07/2018 -	-
110	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]	8/2015	288.24 -	288.24	303.16	11/2015 -	-
111	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	210.29	11/2017 -	-
112	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
113	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	8/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021
114	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]	3/2015	298.33 -	298.33	310.72	- -	-
115	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	8/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021
116	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	-
117	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	322.01	318.64	08/2016 -	-
118	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021
119	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	3/2012	207.03 -	389.45	349.94	05/2012 06/2018	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
120	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	394.53	06/2018 -	-
	<u>National Highways Authority Of India</u>						
121	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	520.00	612.58	02/2009 -	-
122	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]	3/2018	874.25 -	874.25	886.59	- -	-
123	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	2,499.00	1,539.65	03/2021 10/2021	04/2021
124	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	3/2018	925.40 -	1,197.00	1,011.70	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
125	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	2/2018	2,177.80 -	2,450.00	2,244.98	- -	-
126	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	2/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021
127	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	407.94	- -	10/2020
128	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	1,085.47	03/2020 -	-
129	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	905.81	03/2020 -	-
130	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-
131	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-
132	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650	1/2017	244.90 -	244.90	251.87	05/2019 -	-
133	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	-
134	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634	10/2016	447.75 -	447.75	1,160.74	- -	08/2020
135	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	309.40	- -	-
136	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,565.00	- -	05/2021
137	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	9/2016	1,100.19 -	1,145.31	1,304.00	- -	03/2021
138	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-
139	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	9/2016	1,239.82 -	1,727.66	1,674.80	- -	01/2021
140	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608	8/2016	248.97 -	248.97	270.65	05/2019 -	-
141	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	8/2016	1,169.61 -	2,280.00	1,282.04	- -	-
142	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-
143	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591	7/2016	688.70 -	688.70	880.00	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
144	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]	3/2016	1,404.50 -	1,404.50	2,977.58	- -	-
145	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	667.10	02/2019 -	-
146	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]	1/2016	1,134.97 -	1,134.97	1,634.05	11/2018 -	-
147	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	977.26	04/2019 -	-
148	MEERUT-BULANDSHAHR - [N24000539]	1/2016	683.24 -	987.94	867.27	- -	-
149	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	886.96	07/2008 -	-
150	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	8/2015	516.13 -	649.27	712.15	04/2018 -	-
151	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	8/2015	854.80 -	1,038.56	1,160.00	- -	-
152	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	627.93	633.24	01/2016 01/2020	01/2020
153	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	417.68	433.68	01/2016 12/2020	12/2020
154	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021
155	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-
156	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-
157	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	-
158	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021
159	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,858.57	08/2013 -	03/2022
160	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,239.99	08/2013 -	05/2021
161	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,364.18	03/2013 -	11/2020
162	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-
163	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,922.52	06/2014 -	10/2020
164	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
165	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.73	03/2014 -	-
166	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-
167	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
168	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	352.28	06/2008 -	09/2019
169	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	360.99	04/2008 -	12/2020
170	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019
171	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-
172	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,540.00	03/2013 -	03/2021
173	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
174	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]	2/2010	617.00 -	617.00	943.17	08/2012 -	-
175	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
176	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
177	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	6/2015	845.24 -	941.00	889.83	- 01/2020	01/2020
178	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 -	-
179	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
180	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	1,688.16	04/2018 -	-
181	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	630.68	05/2018 06/2021	06/2021
182	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020
183	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,275.58	05/2014 -	-
184	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]	8/2015	275.90 -	275.90	289.13	- -	-
185	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]	12/2015	479.20 -	479.20	712.89	05/2018 -	-
186	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	2,360.65	4,472.01	- -	-
187	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS [N24000509]	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
188	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	3,443.43	01/2018 -	09/2020
189	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	676.33	12/2017 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
190	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
191	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
192	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-
193	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022
194	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.53	10/2013 -	-
195	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	976.79	07/2013 -	11/2020
196	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,337.06	12/2013 -	-
197	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
198	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	1,360.63	02/2013 -	-
199	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163	7/2010	1,813.76 -	1,813.76	2,651.59	07/2013 -	-
200	NASHRI- CHANANI - [N24000162	5/2011	2,159.00 -	2,519.00	4,709.06	06/2015 -	-
201	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	3,106.27	07/2015 -	09/2020
202	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131	2/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-
203	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
204	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	3/2010	1,509.10 -	1,509.10	3,684.89	09/2012 -	-
205	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
206	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	-
207	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	5/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-
208	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019
209	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	325.28	04/2009 -	-
210	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	427.96	11/2008 -	-
211	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	251.39	11/2008 -	-
	Total		98,665.40 -	1,15,596.11	1,51,073.05		
	TELECOMMUNICATIONS						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Department Of Telecommunication</u>						
212	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021
	Total		13,334.00 -	24,664.00	16,594.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Chennai Metro Rail Ltd</u>						
213	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	2/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-
	<u>Delhi Metro Rail Corporation</u>						
214	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021
	<u>National Building Construcion Corporation Ltd</u>						
215	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-
	Total		57,449.00 -	62,363.73	60,887.85		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
216	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	225.77	263.72	03/2020 -	03/2021
217	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	274.08	01/2021 -	-
	Total		494.40 -	494.40	537.80		
	Grand Total		2,96,857.42	4,37,335.05	4,18,476.73		

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39 -	04/2021 -	04/2021	0/0
2	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 -	04/2020 -	05/2021	0/0
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	417.23 -	09/2018 -	06/2021	0/0
4	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	458.00 -	03/2020 -	06/2021	0/0
5	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24 -	06/2021 -	06/2021	0/0
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	02/2020 -	06/2021	0/0
7	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	09/2020 -	07/2021	0/0
8	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR	07/2018	346.27 -	09/2021 -	09/2021	0/0
9	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	10/2021 -	03/2022	0/0
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	03/2021 -	03/2022	0/0
11	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]AAI,TELANGANA	05/2020	353.61 -	05/2022 -	05/2022	0/0
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	02/2022 -	09/2022	0/0
13	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2022	0/0
14	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	11/2021 -	10/2022	0/0
15	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	10/2022 -	10/2022	0/0
16	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	08/2022 -	03/2023	0/0
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	03/2022 -	03/2023	0/0
18	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH	04/2020	611.80 -	03/2023 -	03/2023	0/0
19	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	438.28 -	06/2019 -	-	0/0
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
20	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	03/2017 -	10/2021	0/0
21	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	04/2018 -	12/2021	0/0
	<u>Central Coal Fields Limited</u>					
22	TETARIAKHAR EXPANSION OCP - [N06000186]CCL, JHARKHAND	11/2019	243.52 -	03/2023 -	03/2023	0/0
	<u>Eastern Coal Fields Limited</u>					
23	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL, WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
	<u>Neyveli Lignite Corporation</u>					
24	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
25	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
26	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
27	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>South-Eastern Coal Fields Limited</u>					
28	JAMPALI OCP RCE - [N06000198]SECL, CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0
29	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL, CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
30	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]SECL, CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
31	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL, CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>Western Coal Fields Limited</u>					
32	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
33	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL, MADHYA PRADESH	07/2016	281.25 -	03/2022 -	03/2022	0/0
	<u>STEEL</u>					
	<u>National Mineral Development Corporation (NmDC)</u>					
34	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC, CHHATISGARH	11/2015	2,907.00 -	06/2023 -	06/2023	0/0
	<u>Steel Authority Of India Limited (SAIL)</u>					
35	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL, ODISHA	11/2020	377.18 -	05/2023 -	05/2023	0/0
36	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL, CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0
	<u>PETROLEUM</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	Bharat Petroleum Corporation Limited					
37	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	12/2021 -	12/2021	0/0
38	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
39	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
40	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	08/2022	0/0
41	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL, KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
	Chennai Petroleum Corporation Limited					
42	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU	09/2017	1,858.00 -	12/2019 -	01/2021	0/0
43	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	08/2020 -	09/2021	0/0
	Hindustan Petroleum Corporation Limited					
44	220 KV GRID SUPPLY - [N16000407]HPCL, ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	03/2021	0/0
45	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL, ANDHRA PRADESH	10/2020	210.94 -	08/2021 -	08/2021	0/0
46	RUF PITCH LOADING GANTRY - [N16000406]HPCL, ANDHRA PRADESH	10/2020	332.61 -	11/2022 -	11/2022	0/0
47	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL, HARYANA	09/2018	520.00 -	09/2026 -	09/2026	0/0
48	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL, UTTAR PRADESH	03/2019	3,450.20 -	03/2029 -	03/2029	0/0
49	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL	03/2019	5,830.20 -	03/2031 -	03/2031	0/0
	Indian Oil Corporation Limited					
50	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021	0/0
51	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
52	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL, MAHARASHTRA	05/2016	261.00 -	01/2021 -	04/2021	0/0
53	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
54	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL, HARYANA	09/2019	164.69 -	07/2021 -	07/2021	0/0
55	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
56	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 293.00	06/2020 09/2021	09/2021	0/0
57	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
58	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
59	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	10/2021 -	10/2021	0/0
60	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
61	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 12/2021	12/2021	0/0
62	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	07/2022	0/0
63	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	07/2022 -	07/2022	0/0
64	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0
65	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	09/2022	0/0
66	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	12/2022 -	12/2022	0/0
67	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00 -	01/2023 -	01/2023	0/0
68	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
69	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0
70	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	09/2023	0/0
71	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	12/2023	0/0
72	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	01/2024 -	01/2024	0/0
73	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT	09/2020	18,936.00 -	09/2024 -	09/2024	0/0
74	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
<u>Numaligarh Refinery Limited</u>						
75	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINERY - [N16000379]NRL,ASSAM	01/2019	12,366.00 -	10/2024 -	10/2024	0/0
76	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM	01/2019	10,228.00 -	10/2024 -	10/2024	0/0
<u>Oil & Natural Gas Corporation Limited</u>						
77	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT	02/2020	444.87 -	08/2022 -	08/2022	0/0
<u>Oil India Limited</u>						
78	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	04/2021	0/0
<u>POWER</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Central Public Works Department</u>					
79	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	05/2021	0/0
	<u>Chenab Valley Power Projects [P] Limited</u>					
80	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	07/2025	0/0
	<u>National Hydro-Electric Power Corporation</u>					
81	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
82	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
83	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 01/2021	01/2021	0/0
84	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	12/2018 -	03/2021	0/0
85	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	03/2021 -	03/2021	0/0
86	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 04/2021	04/2021	0/0
87	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	04/2021 -	04/2021	0/0
88	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	11/2018 -	05/2021	0/0
89	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	06/2021 -	06/2021	0/0
90	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	09/2021 -	09/2021	0/0
91	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	09/2021 -	09/2021	0/0
92	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN	03/2020	1,749.31 -	09/2021 -	09/2021	0/0
93	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	09/2021 -	09/2021	0/0
94	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	10/2021 -	10/2021	0/0
95	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	09/2021 01/2022	01/2022	0/0
96	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	09/2021 01/2022	01/2022	0/0
97	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	09/2021 01/2022	01/2022	0/0
98	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
99	TALAIPELLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 516.12	01/2019 04/2020	04/2020	0/0
101	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 04/2020	05/2020	0/0
102	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 06/2020	09/2020	0/0
103	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 06/2020	09/2020	0/0
104	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 04/2021	03/2021	0/0
105	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	03/2021	0/0
106	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 04/2021	03/2021	0/0
107	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	03/2021	0/0
108	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 05/2020	03/2021	0/0
109	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 09/2020	03/2021	0/0
110	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	03/2021	0/0
111	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 09/2020	04/2021	0/0
112	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	04/2021	0/0
113	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	07/2019 04/2021	04/2021	0/0
114	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	06/2021	0/0
115	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	06/2021	0/0
116	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 06/2021	06/2021	0/0
117	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 06/2020	06/2021	0/0
118	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2021	0/0
119	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	12/2018 -	12/2021	0/0
120	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-	0/0
121	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-	0/0
122	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-	0/0
123	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Satluj Jal Vidyut Nigam Limited</u>					
124	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH	11/2020	1,810.56 -	01/2026 -	01/2026	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
125	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 12/2020	-	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Central Public Works Department</u>					
126	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
127	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
128	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
129	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>HII Infra Tech Services Limited</u>					
130	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	07/2021	0/0
131	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	07/2021	0/0
132	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	07/2022	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
133	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
134	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
135	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	12/2020	0/0
136	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARAstra - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
137	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	03/2021	0/0
138	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
139	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2021	0/0
140	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	03/2021	0/0
141	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
142	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	06/2021	0/0
143	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	06/2021	0/0
144	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	06/2021	0/0
145	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	12/2021	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
146	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 03/2020	03/2020	0/0
147	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2023	0/0
148	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
149	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2023	0/0
150	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
151	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
152	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
153	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
154	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
155	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
156	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
157	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
158	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
159	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
	<u>Container Corporation Of India</u>					
160	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 12/2020	12/2020	0/0
161	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2021	0/0
162	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
163	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-	0/0
164	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
165	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-	0/0
166	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-	0/0
167	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
168	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
169	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
	<u>East Central Railways</u>					
170	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
171	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	477.88 283.95	03/2012 -	07/2021	0/0
172	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]JECR,JHARKHAND	03/1999	1,033.07 -	- -	03/2022	0/0
173	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2022	0/0
174	GARHWA ROAD-RAMNA - [N22000465]JECR,JHARKHAND	03/2015	348.23 -	03/2021 -	03/2022	0/0
175	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]JECR,BIHAR	04/1991	329.39 -	- -	03/2022	0/0
176	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]JECR,BIHAR	04/2016	731.64 -	03/2021 -	06/2022	0/0
177	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]JECR,BIHAR	04/1997	324.73 -	03/2012 -	11/2022	0/0
178	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]JECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
179	KODERMA-TILAIYA (NL), ECR - [220100305]JECR,JHARKHAND	04/2002	459.91 -	- -	03/2023	0/0
180	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]JECR,BIHAR	04/2006	378.56 -	- -	03/2023	0/0
181	ARARIA-SUPAUL (NL) - [N22000177]JECR,BIHAR	04/2008	1,605.17 -	- -	03/2023	0/0
182	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]JECR,BIHAR	04/2004	372.14 -	- -	03/2023	0/0
183	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]JECR,BIHAR	04/2009	548.00 -	03/2020 -	03/2023	0/0
184	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]JECR,BIHAR	04/1997	162.87 -	- -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
185	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
186	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
187	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2024	0/0
188	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2024	0/0
189	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	03/2025	0/0
190	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	-	0/0
191	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
192	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-	0/0
193	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
194	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-	0/0
195	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
196	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
197	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
198	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
199	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
200	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
201	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
202	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-	0/0
	<u>East Coast Railway</u>					
203	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 12/2021	12/2021	0/0
204	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	03/2020 03/2021	03/2022	0/0
205	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
206	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2024	03/2024	0/0
207	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2024	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 810.02	11/2018 03/2024	03/2024	0/0
209	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2024	03/2024	0/0
210	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 03/2025	03/2025	0/0
211	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 03/2026	03/2026	0/0
212	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
	<u>Eastern Railways</u>					
213	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
214	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021	0/0
215	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
216	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
217	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0
218	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	03/2022	0/0
219	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
220	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
221	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
222	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
223	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
224	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
225	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
226	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR -CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
227	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
228	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
229	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
230	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
231	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
232	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
233	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
234	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
235	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
236	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
237	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
238	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
239	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
	<u>Indian Railway Construction Company Limited</u>					
240	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2024	0/0
	<u>Kolkata Metro Rail Corporation Limited</u>					
241	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
242	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2021	0/0
243	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
244	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	03/2004 -	03/2022	0/0
245	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
246	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
247	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
248	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
249	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
250	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
251	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
252	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 486.96	03/2019 -	03/2021	0/0
253	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	04/2021	0/0
254	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	602.27 -	12/2021 -	04/2021	0/0
255	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	05/2021	0/0
256	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	12/2021	0/0
257	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	03/2019 -	03/2023	0/0
258	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	03/2014 -	03/2023	0/0
259	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
260	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	03/2011 -	12/2023	0/0
261	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,084.69	12/2015 12/2023	12/2023	0/0
262	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2024	0/0
263	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	03/2019 -	03/2024	0/0
264	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	12/2024	0/0
265	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-	0/0
266	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
267	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
268	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-	0/0
269	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
270	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
271	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	03/2022	0/0
272	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-	0/0
<u>North Eastern Railway</u>						
273	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021	0/0
274	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
275	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
276	INDARA - DOHRGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0
277	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0
278	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
279	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022	0/0
280	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
281	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
282	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
283	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
284	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	03/2025	0/0
285	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
286	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
287	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
288	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
289	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
<u>North Western Railway</u>						
290	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020	0/0
291	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021	0/0
292	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	03/2021	0/0
293	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2021	0/0
294	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	11/2021	0/0
295	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
296	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	06/2022	0/0
297	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
298	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
299	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
300	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021	0/0
301	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	03/2016 -	06/2021	0/0
302	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	12/2022	0/0
303	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	- -	03/2023	0/0
304	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
305	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0
306	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0
307	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
308	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
309	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	03/2023 03/2025	03/2025	0/0
310	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	08/2016 -	08/2025	0/0
311	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
312	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
313	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
314	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
315	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
316	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2021	0/0
317	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	12/2021	0/0
318	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
319	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	03/2020 -	12/2021	0/0
320	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2021	0/0
321	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
322	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
323	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	02/2015 -	06/2022	0/0
324	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	03/2019 -	06/2022	0/0
325	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
326	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
327	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
328	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL, UTTAR PRADESH	06/2016	3,677.76 -	12/2023 -	12/2023	0/0
329	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
330	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
331	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
332	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
333	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
334	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
335	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
336	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
337	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
338	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	12/2024 -	12/2026	0/0
339	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	1,185.64 -	12/2017 -	-	0/0
<u>Railway Electrification</u>						
340	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
341	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	12/2022	0/0
342	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2023	0/0
343	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2024	0/0
344	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
345	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
346	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2024	0/0
347	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
348	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
349	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
350	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	08/2020	0/0
351	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	10/2020	0/0
352	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 -	12/2023	0/0
<u>South Eastern Railway</u>						
353	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020	0/0
354	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	12/2018 12/2018	06/2021	0/0
355	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 03/2020	12/2021	0/0
356	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 03/2021	12/2023	0/0
357	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	03/2025	0/0
358	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
359	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 -	03/2030	0/0
360	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
361	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
<u>South Western Railway</u>						
362	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
363	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 06/2021	06/2021	0/0
364	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
365	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
366	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
367	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
368	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
369	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
370	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
371	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
372	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
373	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
374	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 06/2025	06/2025	0/0
375	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	-	0/0
	<u>Southern Railway</u>					
376	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 03/2021	12/2020	0/0
377	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- 02/2021	04/2021	0/0
378	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- 10/2021	09/2021	0/0
379	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021	0/0
380	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	12/2021	0/0
381	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	06/2022	0/0
382	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2022	0/0
383	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- 03/2024	03/2024	0/0
384	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	03/2024	0/0
385	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
386	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
387	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
388	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
389	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0
390	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
391	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
392	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
393	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
394	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
395	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
396	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
397	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
398	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
399	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
400	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
Western Railway						
401	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 02/2021	02/2021	0/0
402	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 890.76	03/2019 10/2021	10/2021	0/0
403	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	03/2021 12/2021	12/2021	0/0
404	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 12/2022	12/2022	0/0
405	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 411.62	03/2012 03/2023	03/2023	0/0
406	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2023	03/2023	0/0
407	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	03/2019 03/2023	03/2023	0/0
408	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 03/2023	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
409	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	03/2020 12/2023	12/2023	0/0
410	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	03/2022 03/2024	03/2024	0/0
411	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2024	03/2024	0/0
412	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2025	03/2025	0/0
413	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
414	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
415	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
416	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
417	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
418	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Central Public Works Department</u>					
419	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-	0/0
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
420	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH, WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
421	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH, WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0
422	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020	0/0
423	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH, UTTAR PRADESH	12/2016	209.10 -	10/2019 -	06/2020	0/0
424	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH, ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020	0/0
425	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH, CHHATTISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020	0/0
426	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH, MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020	0/0
427	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH, MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
428	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH, NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020	0/0
429	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH, MIZORAM	11/2010	624.41 -	03/2011 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
430	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	-	12/2020	0/0
431	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019	12/2020	0/0
432	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016	12/2020	0/0
433	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020	12/2020	0/0
434	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020	12/2020	0/0
435	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020	01/2021	0/0
436	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015	01/2021	0/0
437	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020	01/2021	0/0
438	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 02/2021	02/2021	0/0
439	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021	0/0
440	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 02/2021	02/2021	0/0
441	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 01/2021	02/2021	0/0
442	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019	02/2021	0/0
443	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019	02/2021	0/0
444	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019	02/2021	0/0
445	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020	02/2021	0/0
446	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019	02/2021	0/0
447	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 03/2021	03/2021	0/0
448	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015	03/2021	0/0
449	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 01/2021	03/2021	0/0
450	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 173.41	08/2018 03/2021	03/2021	0/0
451	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020	03/2021	0/0
452	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 226.88	08/2018 03/2021	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
453	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 01/2021	03/2021	0/0
454	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 03/2021	03/2021	0/0
455	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2021	03/2021	0/0
456	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 12/2020	03/2021	0/0
457	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 634.30	12/2019 03/2021	03/2021	0/0
458	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021	0/0
459	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 -	03/2021	0/0
460	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	03/2021	0/0
461	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2021	0/0
462	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	03/2021	0/0
463	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 03/2021	03/2021	0/0
464	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 03/2021	03/2021	0/0
465	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 03/2021	03/2021	0/0
466	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	04/2021	0/0
467	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 04/2021	04/2021	0/0
468	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 04/2021	04/2021	0/0
469	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2020	04/2021	0/0
470	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 04/2021	04/2021	0/0
471	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	04/2021	0/0
472	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAL-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2020	05/2021	0/0
473	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	05/2021	0/0
474	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	05/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
475	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
476	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 06/2021	06/2021	0/0
477	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- 03/2021	06/2021	0/0
478	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 06/2021	06/2021	0/0
479	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	06/2021	0/0
480	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 06/2021	06/2021	0/0
481	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 06/2021	06/2021	0/0
482	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	03/2018 06/2021	06/2021	0/0
483	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	08/2016 06/2021	06/2021	0/0
484	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 06/2021	06/2021	0/0
485	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	09/2016 06/2021	06/2021	0/0
486	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	10/2016 06/2021	06/2021	0/0
487	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	07/2016 06/2021	06/2021	0/0
488	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 06/2021	06/2021	0/0
489	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	12/2020 -	06/2021	0/0
490	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 07/2021	07/2021	0/0
491	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	07/2020 -	08/2021	0/0
492	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	09/2021	0/0
493	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 09/2021	09/2021	0/0
494	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
495	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	10/2021	0/0
496	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	12/2021	0/0
497	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	08/2019 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
498	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN	03/2020	370.36 -	08/2022 -	08/2022	0/0
499	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	08/2022	0/0
500	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	08/2022	0/0
501	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	11/2022	0/0
502	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
503	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
504	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
505	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
506	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
507	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
508	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
509	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
510	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
511	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
512	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
513	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
514	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
515	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
516	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-	0/0
517	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 12/2020	-	0/0
518	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 12/2020	-	0/0
519	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 12/2020	-	0/0
520	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
521	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
522	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
523	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
524	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
525	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
526	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
527	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
528	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
529	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
530	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
531	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
532	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
533	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-	0/0
534	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-	0/0
535	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-	0/0
536	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 390.73	05/2017 -	-	0/0
537	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
538	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
539	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
540	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
541	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
542	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
543	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
544	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
545	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-	0/0
546	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
547	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
548	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-	0/0
549	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-	0/0
550	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-	0/0
551	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
552	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-	0/0
553	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
554	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-	0/0
555	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-	0/0
556	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
557	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
558	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
559	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
560	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
561	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
562	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
563	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
564	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
565	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
566	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
567	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
568	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
569	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
570	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
571	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
572	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
573	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
574	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-	0/0
575	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-	0/0
576	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-	0/0
577	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-	0/0
578	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-	0/0
579	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-	0/0
580	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-	0/0
581	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-	0/0
582	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
583	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-	0/0
584	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
585	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-	0/0
586	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-	0/0
587	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-	0/0
588	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
589	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-	0/0
590	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-	0/0
591	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
592	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
593	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
594	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
595	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
596	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
597	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
598	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
599	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
600	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
601	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-	0/0
602	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0
603	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0
604	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
605	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
606	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
607	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
608	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
609	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
610	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
611	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
612	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
613	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
614	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0
615	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
616	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
617	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
618	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
619	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
620	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-	0/0
621	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-	0/0
622	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-	0/0
623	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-	0/0
624	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-	0/0
625	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
626	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
627	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
628	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-	0/0
629	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-	0/0
630	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
631	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
632	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-	0/0
633	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-	0/0
634	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
635	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-	0/0
636	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
637	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-	0/0
638	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-	0/0
639	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-	0/0
640	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-	0/0
641	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
642	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-	0/0
643	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
644	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-	0/0
645	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
646	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-	0/0
647	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-	0/0
648	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-	0/0
649	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	-	0/0
650	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-	0/0
651	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-	0/0
652	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-	0/0
653	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-	0/0
654	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
655	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
656	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
657	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
658	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
659	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHAARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
660	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
661	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
662	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
663	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
664	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
665	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
666	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
667	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
668	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0
669	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
670	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
671	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-	0/0
672	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2020	-	0/0
673	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-	0/0
674	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
675	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-	0/0
676	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0
677	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
678	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-	0/0
679	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-	0/0
680	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ - [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-	0/0
681	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-	0/0
682	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-	0/0
683	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-	0/0
684	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
685	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-	0/0
686	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-	0/0
687	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-	0/0
688	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-	0/0
689	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-	0/0
690	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-	0/0
691	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-	0/0
692	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-	0/0
693	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
694	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	07/2022	0/0
695	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	09/2018 -	11/2022	0/0
696	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	04/2023	0/0
697	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	04/2023	0/0
698	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	04/2023	0/0
699	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	06/2023	0/0
700	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	06/2023	0/0
701	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	07/2023	0/0
702	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2023	0/0
703	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	04/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
704	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-	0/0
705	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
706	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
707	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
708	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
709	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-	0/0
710	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0
National Highways Authority Of India						
711	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	01/2020	0/0
712	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	02/2019	0/0
713	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	02/2021	0/0
714	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	02/2021	0/0
715	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	08/2020	0/0
716	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	08/2020	0/0
717	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	09/2020	0/0
718	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
719	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	11/2020	0/0
720	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2020	0/0
721	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	11/2020	0/0
722	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	11/2020	0/0
723	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2020	0/0
724	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	12/2020	0/0
725	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
726	FOUR LANNING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
727	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018	0/0
728	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
729	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
730	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019	0/0
731	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
732	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 1,115.95	03/2019 10/2019	10/2019	0/0
733	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020	0/0
734	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020	0/0
735	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020	0/0
736	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020	0/0
737	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
738	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
739	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020	0/0
740	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020	0/0
741	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
742	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020	0/0
743	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020	0/0
744	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020	0/0
745	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
746	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
747	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
748	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2020	0/0
749	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
750	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020	0/0
751	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
752	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
753	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020	0/0
754	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020	0/0
755	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020	0/0
756	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021	0/0
757	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021	0/0
758	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021	0/0
759	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	02/2021	0/0
760	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	02/2021	0/0
761	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
762	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	02/2021	0/0
763	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
764	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2021	0/0
765	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 03/2021	03/2021	0/0
766	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021	0/0
767	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 07/2019	03/2021	0/0
768	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2021	0/0
769	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 10/2020	03/2021	0/0
770	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021	0/0
771	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	03/2021	0/0
772	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
773	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 03/2021	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
774	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021	0/0
775	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	03/2021	0/0
776	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
777	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	05/2021	0/0
778	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
779	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	05/2021	0/0
780	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	05/2021	0/0
781	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	05/2021	0/0
782	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 06/2021	06/2021	0/0
783	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	06/2021	0/0
784	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	06/2021	0/0
785	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	06/2021	0/0
786	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	06/2021	0/0
787	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	06/2021	0/0
788	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	06/2021	0/0
789	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	06/2021	0/0
790	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	06/2021	0/0
791	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	06/2021	0/0
792	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
793	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2021	0/0
794	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2021	0/0
795	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	07/2021	0/0
796	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	07/2021	0/0
797	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
798	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	07/2021	0/0
799	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 -	- -	07/2021	0/0
800	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	07/2021	0/0
801	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	07/2021	0/0
802	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
803	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	07/2021	0/0
804	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
805	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
806	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	08/2021	0/0
807	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
808	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- 02/2021	08/2021	0/0
809	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021	0/0
810	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	09/2021	0/0
811	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	09/2021	0/0
812	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
813	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
814	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	09/2021	0/0
815	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
816	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
817	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 12/2021	12/2021	0/0
818	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 06/2021	12/2021	0/0
819	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 06/2021	12/2021	0/0
820	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 01/2021	12/2021	0/0
821	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	03/2020 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
822	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	-	12/2021	0/0
823	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021	12/2021	0/0
824	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017	02/2022	0/0
825	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	-	02/2022	0/0
826	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019	03/2022	0/0
827	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	-	03/2022	0/0
828	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017	07/2022	0/0
829	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017	07/2022	0/0
830	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014	12/2022	0/0
831	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 -	03/2023	03/2023	0/0
832	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009	-	0/0
833	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009	-	0/0
834	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008	-	0/0
835	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008	-	0/0
836	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009	-	0/0
837	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009	-	0/0
838	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010	-	0/0
839	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011	-	0/0
840	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012	-	0/0
841	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014	-	0/0
842	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015	-	0/0
843	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013	-	0/0
844	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013	-	0/0
845	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
846	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
847	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
848	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
849	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
850	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
851	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
852	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
853	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
854	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
855	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
856	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
857	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-	0/0
858	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
859	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
860	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
861	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
862	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
863	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
864	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	-	0/0
865	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
866	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-	0/0
867	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
868	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-	0/0
869	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
870	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
871	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
872	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
873	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-	0/0
874	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
875	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
876	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-	0/0
877	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
878	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
879	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
880	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
881	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
882	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
883	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
884	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
885	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
886	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
887	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
888	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-	0/0
889	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
890	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
891	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
892	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
893	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
894	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
895	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-	0/0
896	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
897	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
898	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
899	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-	0/0
900	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
901	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
902	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
903	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-	0/0
904	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-	0/0
905	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
906	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
907	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
908	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
909	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-	0/0
910	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
911	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
912	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
913	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
914	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 486.00	- -	-	0/0
915	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-	0/0
916	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-	0/0
917	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
918	FOUR LANNING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-	0/0
919	CONSTRUCTION OF FOUR LANNING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-	0/0
920	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
921	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-	0/0
922	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-	0/0
923	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-	0/0
924	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
925	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
926	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
927	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-	0/0
928	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
929	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
930	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-	0/0
931	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-	0/0
932	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
933	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-	0/0
934	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-	0/0
935	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-	0/0
936	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-	0/0
937	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
938	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
939	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
940	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0
941	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
942	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
943	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-	0/0
944	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
945	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
946	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
947	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
948	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
949	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
950	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
951	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
952	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
953	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
954	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
955	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
956	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
957	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
958	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
959	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
960	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
961	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
962	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
963	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
964	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
965	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
966	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
967	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
968	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
969	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
970	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
971	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
972	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
973	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
974	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
975	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
976	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
977	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
978	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
979	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
980	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
981	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
982	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0
983	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-	0/0
984	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
985	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
986	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
987	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-	0/0
988	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
989	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
990	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-	0/0
991	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
992	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
993	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- 02/2020	-	0/0
994	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
995	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
996	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
997	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-	0/0
998	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-	0/0
999	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-	0/0
1000	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
1001	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Inland Waterways Authority Of India</u>					
1002	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	5,369.18 4,633.81	03/2023 -	03/2023	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
1003	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	06/2021 -	11/2021	0/0
	<u>Central Public Works Department</u>					
1004	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	03/2018 -	-	0/0
	<u>Department Of Telecommunication</u>					
1005	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	06/2021	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1006	AHMEDABAD METRO RAIL PROJECT PHASE I - [N28000122]MEGA,GUJARAT	11/2014	10,773.00	12/2018	08/2022	0/0
1007	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT	03/2019	5,384.17	03/2024	03/2024	0/0
1008	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32	03/2024	03/2024	0/0
<u>Central Public Works Department</u>						
1009	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00	11/2020	11/2020	0/0
1010	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00	03/2021	07/2021	0/0
1011	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00	08/2020	03/2022	0/0
1012	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00	03/2022	03/2022	0/0
1013	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00	07/2021	12/2024	0/0
1014	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	12/2015	-	0/0
1015	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26	12/2013	-	0/0
1016	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112,TYPE V-68, TYPE-VI-5), SHOPS,CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97	09/2020	-	0/0
<u>Delhi Metro Rail Corporation</u>						
1017	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00	03/2016	09/2021	0/0
1018	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00	12/2020	09/2021	0/0
1019	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65	03/2025	03/2025	0/0
<u>Jawahar Lal Nehru National Urban Renewal Mission</u>						
1020	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90	-	-	0/0
<u>Kochi Metro Rail Corporation Ltd</u>						
1021	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79	07/2017	09/2020	0/0
<u>Lucknow Metro Rail Corporation Limited</u>						
1022	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48	03/2024	03/2024	0/0
1023	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62	03/2024	03/2024	0/0
1024	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00	03/2019	-	0/0
<u>Maharashtra Metro Rail Corporation Ltd.</u>						
1025	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00	11/2021	11/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1026	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 09/2022	03/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1027	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1028	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1029	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-	0/0
	<u>National Capital Region Transport Corp</u>					
1030	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE	03/2019	30,274.00 -	06/2025 -	06/2025	0/0
	<u>Patna Metro Rail Corporation</u>					
1031	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1032	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					
1033	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021	0/0
1034	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	03/2021	0/0
1035	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
1036	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021	0/0
1037	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0
1038	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	06/2021	0/0
1039	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	04/2020 -	06/2021	0/0
1040	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
1041	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
1042	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	12/2021	0/0
1043	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1044	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
1045	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-	0/0
1046	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-	0/0
	<u>Delhi Jal Board</u>					
1047	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021	0/0
1048	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
1049	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
1050	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
1051	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-	0/0
	<u>Kolkata Metropolitan Development Authority</u>					
1052	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021	0/0
1053	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	05/2021	0/0
1054	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA,WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0
1055	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA,WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
1056	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA,WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
1057	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA,WEST BENGAL	05/2018	198.43 -	02/2022 -	02/2022	0/0
1058	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA,WEST BENGAL	05/2018	160.00 -	02/2022 -	02/2022	0/0
1059	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA,WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
1060	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA,WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
1061	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA,WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0
1062	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA,WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
1063	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA,WEST BENGAL	08/2017	307.12 -	09/2022 -	09/2022	0/0
	<u>Uttar Pradesh Jal Nigam</u>					
1064	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 -	12/2019 -	01/2021	0/0
1065	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH	10/2016	370.40 -	08/2020 03/2021	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1066	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021	0/0
1067	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021	0/0
1068	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
1069	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
1070	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH	03/2018	904.00 -	09/2021 -	09/2021	0/0
1071	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
1072	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0
1073	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
1074	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH	10/2017	213.62 -	03/2022 -	03/2022	0/0
1075	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
1076	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 -	07/2021 -	06/2022	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
1077	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	03/2021	0/0
1078	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-	0/0
	<u>COMMERCE</u>					
	<u>National Building Construcion Corporation Ltd</u>					
1079	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	-	0/0
	<u>HUMAN RESOURCE DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
1080	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	06/2021	0/0
1081	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	03/2021 -	06/2022	0/0
1082	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH	09/2018	392.51 -	06/2022 -	06/2022	0/0
1083	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	07/2022 -	07/2022	0/0
1084	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD,CHHATTISGARH	03/2020	808.62 -	07/2022 -	07/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1085	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	03/2022 -	09/2022	0/0
1086	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 375.00	09/2020 -	11/2022	0/0
1087	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	09/2022 -	01/2023	0/0
1088	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	04/2023 -	04/2023	0/0
1089	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-	0/0
	<u>Edcil(India) Limited</u>					
1090	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-	0/0
	<u>Indian Institute Of Technology, Kharagpur</u>					
1091	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
1092	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-	0/0
	<u>HOME AFFAIRS</u>					
	<u>Central Public Works Department</u>					
1093	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE-C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]CPWD,HARYANA	01/2020	166.98 -	05/2022 -	05/2022	0/0
1094	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD,HARYANA	01/2020	166.98 167.00	10/2023 -	10/2023	0/0
	<u>DPIIT</u>					
	<u>Delhi Mumbai Industrial Corridor</u>					
1095	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021	0/0
	<u>India International Convention And Expo Centre</u>					
1096	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	12/2019 -	10/2021	0/0
	Total		13,18,323.00 -			0/0
	Grand Total		13,18,323.00			0/0

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(FEBRUARY 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
7	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
8	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
9	RPR FOR JAMUNIA UG (0.90 MTY)	WCL	07/2016	03/2022	281.25	409.87	128.62
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	12579.09	13812.3	1233.21
12	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
13	AIIMS BILASPUR	NBCC	04/2018	09/2021	1351	1471	120
14	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD	03/2019	09/2025	1577	1828	251

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
16	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	484.32	626.26	141.94

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
17	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	352.56	490.24	137.68
18	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
19	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
20	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3072	395
21	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
22	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
23	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
24	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
25	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
26	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
27	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
28	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
29	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
30	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
31	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	652.1	108.19
32	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1846.46	984.67
34	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
35	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
36	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
37	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
38	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	15105.22	3466.67
39	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
40	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
41	EASTERN REGION STRENGTHENING SCHEME- XVIII	PGCIL	03/2017	07/2020	3500	3994	494
42	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
43	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
44	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	408.46	516.12	107.66
45	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
46	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
47	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
48	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
49	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
50	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
51	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
52	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
53	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
54	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	10566	5213
55	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15389.42	1022.84
56	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13140.91	608.47
57	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	9188.98	10016.1	827.12
58	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
59	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
60	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
61	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3550	2516.93
62	KOTLIPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
63	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
64	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
65	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
66	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
67	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
68	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
69	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5521.45	3127.98
70	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
71	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2910.84	2186.15
72	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
73	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	396	262.59
74	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83
75	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2432.5	370.2
76	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
77	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
78	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
79	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
80	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
81	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	1967	165.99
82	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	315	130.94
83	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
84	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1105	719.8
85	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTPT	04/2006	06/2013	495.74	734.01	238.27
86	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12264.15	7809.98
87	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
88	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	4541.38	3361.19
89	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
90	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1070	745.27
91	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
92	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTPT	03/1996	03/2004	495.44	2980.41	2484.97
93	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
94	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3377	1873.29
95	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1959.74	1130
96	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	1720	1416.02
97	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	2315	3911.65	1596.65
98	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
99	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	2005.25	1493.39
100	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
101	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
102	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
103	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
104	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
105	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	187.26	332	144.74
106	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
107	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
108	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
109	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
110	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
111	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
112	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
113	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	565	303.62
114	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	502.48	214.13
115	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
116	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
117	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
118	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2172.16	2051.46
119	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
120	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	800	486
121	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJBHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
122	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	1040	625.16
123	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
124	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
125	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
126	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	931.98	1121	189.02
127	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	600.3	435.89
128	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
129	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	742	172.37
130	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
131	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	369.55	116.59
132	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
133	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	559.95	361.27
134	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
135	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1205	681.48
136	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	527.37	375.53
137	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2042.51	244.51
138	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	480	266.99
139	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
140	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
141	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
142	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
143	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
144	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
145	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
146	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
147	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
148	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
149	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	525	282.91
150	AJMER-BANGURGRAM	NWR	04/2011	11/2019	213.39	375	161.61
151	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
152	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099	277
153	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	236.93	350.45	113.52
154	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
155	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
156	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1389.05	351.9
157	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	1868.89	320.23
158	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
159	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	872.65	228.27
160	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1500	524.38
161	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	395	148.92
162	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
163	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
164	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
165	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
166	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	929.86	251.32
167	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
168	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	783	205
169	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
170	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
171	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1147	286.57
172	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
173	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1656	499.06
174	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
175	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	NFR	02/1999	04/2010	380.6	1090.6	710
176	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	691.84	1017.91	326.07
177	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	859	234
178	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
179	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	890.76	339.25
180	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	998	353.22
181	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
182	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
183	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
184	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
185	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
186	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
187	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
188	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
189	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
190	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
191	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
192	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1536	776
193	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
194	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
195	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	449.39	329.66
196	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3524.81	1616.3
197	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
198	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
199	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	1825	641.75
200	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1536	593.05
201	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96
202	VIZIANAGARAM -SAMBALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
203	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2725	2011.52
204	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	22716.11	6500.11
205	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1400	472.99
206	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
207	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1246	246
208	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	1724.2	1993.24	269.04
209	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
210	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	12/2021	602.27	760	157.73
211	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25
212	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
213	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
214	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
215	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
216	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
217	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2200	1750
218	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
219	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
220	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6911	4584.48
221	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
222	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4517.49	2245.99
223	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3000	873
224	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
225	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
226	KADAPA-BANGALORE (NL), KADAPA- PENDLIMARRI PH-I	SCR	04/2008	03/2014	2132.77	3037.95	905.18
227	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
228	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	2643.25	354.55
229	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
230	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
231	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	663.13	120.95
232	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
233	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59
234	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	5912.4	2408.71
235	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
236	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	346	226
237	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
238	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	520	240
240	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
241	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
242	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	MORTH	12/2011	02/2012	156.63	276	119.37
243	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MORTH	03/2012	05/2012	207.03	389.45	182.42
244	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
245	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
246	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	MORTH	12/2010	01/2019	169.26	299	129.74
247	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	624.98	731.5	106.52
248	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
249	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
250	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
251	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
252	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
253	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
254	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
255	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	1952.2	690.22
256	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
257	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
258	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
259	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
260	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
261	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
262	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
263	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
264	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
265	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
266	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1827.15	744.15
267	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	730.97	199.84
268	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
269	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MORTH	11/2011	09/2015	954.43	1191.51	237.08
270	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	MORTH	11/2010	02/2011	470.2	630.36	160.16
271	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	268.08	390.73	122.65
272	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
273	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	NHAI	02/2016	03/2019	997.15	1115.95	118.8
274	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
275	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
276	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
277	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MORTH	11/2013	05/2017	497.05	881.05	384
278	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	MORTH	10/2013	03/2017	445.89	653.29	207.4
279	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
280	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
281	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
282	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
283	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
284	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
285	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	186.96	322.24	135.28
286	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653.29	207.4
287	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MORTH	04/2014	08/2017	279.7	398.52	118.82
288	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	MORTH	08/2014	11/2017	823.2	937.76	114.56
289	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	MORTH	08/2014	11/2017	600.87	720.97	120.1
290	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
291	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
292	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
293	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
294	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
295	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
296	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
297	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
298	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
299	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	NHAI	09/2016	N.A.	1239.82	1727.66	487.84
300	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
301	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2587.5	1199.16
302	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
303	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
304	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
305	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
306	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2021)

STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
307	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
308	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
309	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4720.73	456.73
310	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
311	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
312	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	23136	33406	10270
313	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
314	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
WATER RESOURCES							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
315	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	12320	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	11459	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	03/2023	380.87	12
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	06/2021	177.1	16
7	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	AAI	01/2018	08/2022	03/2023	1405	7
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2022	1142	12
9	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	09/2022	1383	12
10	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	06/2021	458	15
11	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	10/2022	389.71	11
12	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	07/2021	456.86	10
13	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	05/2021	303.8	13
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2021	417.23	33
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	09/2022	2467	7

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
16	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	10/2021	304.13	55
17	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	12/2021	243	44
18	PACHWARA SOUTH COAL BLOCK	NLC	07/2013	08/2022	09/2023	1795.01	13
19	RECAST PR FOR DHANKASA UG (1.00 MTY)	WCL	09/2016	03/2022	03/2025	289.29	36
20	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2022	869.44	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2021	430.45	60
22	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	84
23	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
24	BHUBANESWARI EXPENSION OCP(40.0 MTY)	MCL	12/2007	03/2017	03/2031	3145.45	168
25	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
26	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2022	479.53	108
27	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	MCL	12/2007	03/2010	03/2029	3504.21	228
28	MURADIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	04/2023	339.88	108
29	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	03/2022	1230.27	83
30	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	02/2021	5907.11	62
31	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2022	447.06	84
32	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	WCL	11/2015	03/2021	03/2024	313.34	36
33	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	WCL	11/2015	03/2020	03/2026	851.6	72
34	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2021	1055.05	36
35	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
36	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2024	1375.38	36
37	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	WCL	11/2014	03/2020	03/2027	1184.33	84
38	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
39	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
40	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	06/2021	289.45	85
41	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2022	397.09	36
42	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
43	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2022	510.85	72
45	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	MCL	12/2007	03/2013	03/2028	8416.19	180
46	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2022	1783.09	12
47	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	84
48	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2025	6964.33	152
49	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
50	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2022	163.51	132
51	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2022	162.46	96
52	EXPANSION PR OF JHANJRA UG(5.00 MTY)	ECL	11/2015	03/2022	03/2029	1210.12	84
53	KISTARAM OCP	SCCL	11/2010	03/2015	03/2022	242.29	84
54	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2022	178.44	96
55	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2022	417.33	68
56	RECAST EPR AMRAPALI OC	CCL	02/2012	03/2020	03/2024	4983.58	48
57	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	07/2022	17237	8
58	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12
59	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36

CULTURE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	03/2021	151.33	42

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
61	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	06/2021	246.31	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
62	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	10/2021	4773	22
63	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	12579.09	22

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
64	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	04/2021	426.72	12
65	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	NFL	01/2018	11/2019	03/2021	239.81	16
66	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	NFL	01/2018	11/2019	03/2021	215.92	16
67	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	NFL	01/2018	11/2019	02/2021	218.83	15

FINANCE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
68	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD	12/2015	10/2019	04/2021	209	18

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
69	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD	03/2018	09/2020	04/2022	195	19
70	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
71	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	04/2021	152.95	38
72	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	03/2021	204.44	46
73	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	03/2021	272.19	24
74	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	03/2021	355.15	24
75	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	03/2021	414.11	88
76	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	12/2021	363.99	43
77	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	HITES	07/2016	06/2020	07/2021	703	13
78	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	HITES	07/2016	04/2020	07/2021	785	15
79	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	CPWD	09/2017	03/2020	12/2021	150.29	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
80	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD	12/2018	06/2021	05/2022	260	11
81	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	HITES	05/2017	05/2021	07/2022	875	14

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
82	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	12/2021	1219.21	26
83	NSG AT KOLKATA	CPWD	10/2014	04/2018	12/2021	162.88	44

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
84	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD	09/2018	09/2020	11/2022	375	26
85	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD	07/2019	03/2021	06/2022	753.63	15
86	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD	07/2019	03/2022	09/2022	851	6
87	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	06/2021	171.86	63
88	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2021	496.18	52
89	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	04/2021	294	24
90	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	CPWD	11/2017	03/2020	06/2021	171.72	15
91	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	CPWD	01/2018	07/2020	06/2021	223.37	11
92	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	CPWD	12/2016	07/2019	03/2021	549.31	20
93	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	02/2022	430	21
94	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	CPWD	02/2019	09/2020	03/2021	186	6

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
95	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	12/2022	5540	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
96	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	07/2021	196.26	12
97	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	07/2022	278.6	13
98	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	04/2021	224.75	8
99	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	02/2022	598	24
100	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
101	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	12/2021	522	9
102	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2021	861.79	94
103	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	10/2021	163.02	18
104	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	09/2021	421	13
105	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	IOCL	08/2017	06/2020	09/2021	236	15
106	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
107	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	HPCL	11/2017	11/2020	06/2021	255	7
108	PUNE POL STORAGE DEPOT	BPCL	08/2016	08/2020	03/2021	282.64	7
109	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
110	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15
111	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
112	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	09/2021	206.5	6
113	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	08/2021	206.63	18
114	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	11/2021	255.4	15
115	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	02/2022	199.36	16
116	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2021	906	20
117	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	04/2021	543.91	14
118	BS VI PROJECT AT GUWAHATI REFINERY	IOCL	08/2018	02/2020	06/2021	557	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
119	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	04/2022	1636	20
120	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2021	3190.69	37
121	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	06/2021	160.1	16
122	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	03/2022	161.59	27
123	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
124	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	06/2021	581	15
125	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2021	352.56	48
126	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	53
127	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	06/2021	2321	6
128	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	05/2021	690	34
129	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	IOCL	06/2016	08/2019	06/2021	423	22
130	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2021	650.82	26
131	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	06/2022	34012	24
132	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497	38
133	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	10/2021	1810	22
134	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	04/2021	571.66	16
135	MMPL PIPELINE REROUTING PROJECT	BPCL	04/2013	12/2019	03/2021	449.58	15
136	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	03/2021	3313	13
137	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
138	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1933	12
139	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2021	2433	6
140	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	3437	12
141	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1740	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
142	PIPELINE NETWORK PROJECT GELEKI, ASSAM	ONGC	07/2016	05/2020	05/2021	249.85	12
143	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677	14
144	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	03/2021	4588.29	31
145	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	04/2021	327.78	36
146	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
147	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
148	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
149	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	12/2021	225.54	10
150	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	03/2022	909	14
151	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	05/2021	286.42	9
152	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
153	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	05/2021	529.68	30
154	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	09/2024	18668	18
155	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	03/2021	1885.13	27
156	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
157	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	04/2021	3500	9
158	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	04/2021	186.17	21
159	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	03/2021	445.89	25
160	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	03/2021	1931.39	13
161	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	07/2021	12964.6	38
162	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2022	3919.59	150

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
163	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
164	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2021	4824.12	101
165	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	02/2021	11638.55	37
166	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
167	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	06/2021	374.63	62
168	EASTERN REGION STRENGTHENING SCHEME- XII	PGCIL	05/2014	11/2016	05/2021	522.29	54
169	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	117
170	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
171	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	03/2021	9188.98	20
172	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	04/2021	12532.44	28
173	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	14366.58	40
174	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	63
175	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	06/2021	197.4	39
176	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2021	1394.52	49
177	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	04/2021	5353	105
178	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	126
179	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	02/2021	2496.9	134
180	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	04/2022	8692.97	126
181	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	03/2022	10598.98	16
182	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	PGCIL	05/2016	11/2019	03/2021	14733.37	16
183	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	06/2021	322.3	28
184	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	04/2021	235.53	22
185	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	06/2021	379.95	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
186	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	PGCIL	02/2017	04/2020	03/2021	5070.13	11
187	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2021	4754.42	36
188	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	36
189	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	03/2021	358.83	10
190	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	CPWD	10/2017	11/2019	05/2021	271.9	18
191	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2021	808.63	38
192	EASTERN REGION STRENGTHENING SCHEME- XV	PGCIL	04/2016	04/2018	03/2021	454.11	35
193	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
194	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108
195	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
196	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	02/2021	691.84	11
197	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	RITES	02/2016	03/2020	06/2021	393.98	15
198	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625	63
199	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2023	2288	21
200	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
201	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
202	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	12
203	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
204	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	03/2024	5200	48
205	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2022	528.57	36
206	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
207	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	CCOI	01/2013	03/2018	03/2021	387.7	36
208	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2021	346.32	24
209	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	03/2021	622.5	47
210	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	39
211	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
212	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	21
213	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
214	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	21
215	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2021	1402.02	21
216	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
217	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
218	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	12
219	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
220	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
221	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
222	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
223	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631	24
224	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
225	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	2499.71	24
226	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
227	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	64
228	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	NWR	04/2013	03/2020	06/2021	420.18	15
229	AJMER-BANGURGRAM	NWR	04/2011	11/2019	03/2021	213.39	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
230	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
231	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2021	258.2	30
232	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548	36
233	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2024	1798	60
234	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	24
235	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2021	314	24
236	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	69
237	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
238	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	04/2021	511.86	12
239	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
240	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60
241	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2023	318.24	132
242	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	12/2023	829.74	45
243	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
244	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	34
245	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
246	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.2	180
247	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
248	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
249	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.6	24
250	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
251	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
252	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
253	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
254	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2023	2393.47	108
255	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	07/2021	477.88	112
256	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	168
257	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
258	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	24
259	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
260	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
261	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28
262	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
263	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	12
264	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
265	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
266	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
267	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
268	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
269	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
270	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
271	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287	114
272	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
273	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
274	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
275	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	156
276	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
277	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
278	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
279	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	216
280	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
281	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	128
282	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	04/2021	1180.19	148
283	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	204
284	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
285	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2021	495.74	102
286	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.2	48
287	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
288	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2024	2326.52	117
289	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2021	5300	84
290	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	96
291	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	11/2021	410.08	33
292	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140
293	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500	241
294	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
295	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
296	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
297	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2022	155.81	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
298	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	11/2021	1156.94	20
299	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
300	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	15
301	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	03/2021	578	12
302	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
303	HAIJIPUR - BACHAWARA	ECR	05/2015	03/2019	05/2021	678.54	26
304	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
305	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	63
306	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	02/2021	246.08	14
307	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	12
308	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2025	1640.04	36
309	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	48
310	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2021	1037.15	9
311	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
312	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
313	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
314	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
315	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
316	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
317	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36
318	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	03/2023	1491.47	36
319	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2023	1763.93	36
320	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
321	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
322	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
323	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
324	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	21
325	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33
326	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
327	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
328	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
329	GARHWA ROAD-RAMNA	ECR	03/2015	03/2021	03/2022	348.23	12
330	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	24
331	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
332	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	36
333	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	15
334	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
335	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
336	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	9
337	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	34
338	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	198
339	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
340	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760	27
341	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	12/2021	213	68
342	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
343	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
344	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	31
345	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	03/2022	3055	42

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
346	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	MORTH	08/2020	11/2020	08/2022	196.23	21
347	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	04/2022	847	25
348	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	12/2021	990.97	24
349	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	MORTH	11/2018	12/2020	06/2021	281.45	6
350	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE	NHAI	03/2019	05/2020	05/2022	1047	24
351	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO	MORTH	03/2020	08/2020	08/2022	255.23	24
352	REHABILITATION UPGRADE OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MORTH	01/2016	08/2016	07/2021	348.95	59
353	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MORTH	01/2017	09/2017	05/2021	263.45	44
354	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIKAALA TO RENGAPALI ODISHA	MORTH	03/2016	12/2019	03/2021	536.65	15
355	BARASGAON TO RAHATEE	MORTH	07/2016	09/2018	04/2021	289.11	31
356	REHABILITATION AND UPGRADE OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	MORTH	03/2016	01/2020	03/2021	240.3	14
357	REHABILITATION AND UPGRADE OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	MORTH	03/2016	05/2019	02/2021	249.5	21
358	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MORTH	11/2017	03/2018	06/2021	392.33	39
359	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	MORTH	02/2017	05/2019	05/2021	157.32	24
360	REHABILITATION AND UPGRADE OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MORTH	01/2016	08/2016	06/2021	497.14	58
361	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	06/2021	193.69	128
362	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAUNGTLAI)	MORTH	08/2010	10/2010	06/2021	195.04	128
363	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND	NHAI	03/2016	07/2016	02/2021	641.17	55

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NAGERCOIL TO KAVALKINARU OF NH						
364	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
365	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	07/2022	1176.37	59
366	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
367	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	02/2021	639.97	40
368	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	44
369	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	07/2022	1227.87	58
370	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH	MoRTH	03/2015	10/2015	03/2021	271.45	65
371	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
372	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
373	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	04/2021	497.05	47
374	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	03/2021	628.45	14
375	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	04/2021	957.54	14
376	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	06/2021	511.83	46
377	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	04/2021	294.17	63
378	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	73
379	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	MoRTH	01/2012	04/2015	03/2021	410.72	71
380	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	08/2021	374	99
381	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	03/2021	1724.55	96
382	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105
383	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	05/2021	1078.84	93
384	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	03/2022	998.79	103
385	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2021	1047	81
386	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	03/2021	1928.22	71

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
387	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	09/2021	2128.72	29
388	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2021	531.13	37
389	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2021	593.26	37
390	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	12/2021	649.5	33
391	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	06/2021	505	37
392	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	03/2021	1423.96	28
393	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36
394	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2021	707.82	31
395	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	02/2021	641.17	31
396	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2021	546	29
397	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2021	591.66	29
398	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	03/2021	804.97	33
399	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	12/2021	1167.42	33
400	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	03/2021	2510.04	19
401	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	02/2021	400.25	23
402	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	03/2021	446.17	24
403	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	12/2021	848.45	21
404	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	09/2021	754.54	18
405	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	NHAI	03/2017	03/2020	03/2021	639.79	12
406	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
407	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	15
408	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
409	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
410	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
411	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46
412	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	05/2021	373.07	57
413	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	05/2021	396.52	57
414	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	05/2021	429.52	57
415	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	07/2021	894	15
416	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
417	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	NHAI	06/2017	06/2020	02/2021	1958.88	8
418	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
419	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	07/2022	339.57	46
420	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
421	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
422	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	NHIDCL	03/2018	09/2018	12/2021	315.03	39
423	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	NHIDCL	03/2018	09/2018	12/2021	240.64	39
424	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	11/2021	215.12	38
425	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2021	215.79	39
426	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
427	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	NHIDCL	03/2018	09/2018	11/2022	323.98	50
428	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	03/2021	249.05	32
429	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2021	254.17	37
430	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	03/2021	279.44	36
431	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	06/2021	373.82	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
432	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	05/2021	809.16	34
433	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	04/2021	877.79	22
434	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	MoRTH	01/2017	03/2019	02/2021	247.25	23
435	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	MoRTH	03/2018	07/2020	08/2021	322.48	13
436	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	05/2021	170.57	6
437	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
438	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	09/2023	428.11	48
439	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
440	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	02/2021	162.56	35
441	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2021	166.21	31
442	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	04/2021	169.63	37
443	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	MoRTH	01/2017	09/2019	05/2021	396.86	20
444	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	MoRTH	11/2017	02/2018	02/2021	235.91	36
445	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	12/2021	426.18	15
446	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
447	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	07/2023	640.07	46
448	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
449	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
450	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
451	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
452	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	02/2021	184.62	36
453	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	MoRTH	03/2018	11/2019	02/2021	191.21	15
454	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL	MoRTH	03/2016	08/2019	11/2022	160.27	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	CROSSING AT KM 303.9 ON NH-60 (PAND						
455	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	12/2021	236.78	28
456	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	06/2021	205.05	51
457	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	09/2021	214.69	42
458	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2021	217.22	31
459	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	03/2021	233.04	36
460	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MoRTH	03/2018	08/2018	03/2021	228.32	31
461	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MoRTH	03/2018	08/2018	02/2021	289.67	30
462	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	MoRTH	03/2016	05/2016	04/2021	995.09	59
463	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	MoRTH	03/2016	11/2019	02/2021	208.5	15
464	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	MoRTH	11/2017	04/2018	03/2021	187.82	35
465	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	MoRTH	11/2017	04/2018	03/2021	163.95	35
466	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	06/2018	04/2021	370.3	34
467	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	05/2018	06/2021	341.79	37
468	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MoRTH	11/2015	06/2017	06/2021	335.32	48
469	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MoRTH	01/2016	09/2016	06/2021	476.2	57
470	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2021	624.98	56
471	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	06/2021	452.94	59
472	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	MoRTH	03/2017	01/2018	03/2021	423.79	38
473	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	06/2021	496.02	75
474	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	03/2021	188.8	22
475	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	03/2021	379.16	40
476	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	MoRTH	10/2016	08/2020	07/2021	171.9	11
477	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM	MoRTH	10/2016	03/2020	02/2021	218.9	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	450.000 TO KM 486.770 (EXCEPT						
478	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	MoRTH	07/2016	10/2019	02/2021	208.88	16
479	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MoRTH	03/2018	04/2020	04/2021	263.89	12
480	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	MoRTH	03/2018	08/2020	03/2021	288.3	7
481	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	MoRTH	03/2016	09/2020	03/2021	296.5	6

RURAL DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
482	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSC	03/2007	12/2015	03/2021	149.73	63
483	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSC	10/2011	12/2016	03/2021	175.49	51
484	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSC	12/2007	12/2016	03/2021	202.61	51

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
485	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	SAIL	12/2018	09/2020	05/2021	263.36	8
486	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	05/2021	262.87	23
487	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2021	1034.01	50
488	FORGED WHEEL PLANT	RINL	04/2014	09/2018	03/2021	1682.85	30
489	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2021	15525	74

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
490	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2021	13334	71

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
491	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	DMRC	05/2017	12/2020	09/2021	565	9
492	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	12/2024	1180	41

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
493	BANGALORE METRO RAIL PROJECT PHASE-2	BMRC	02/2014	02/2019	06/2024	26405.14	64
494	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	10/2021	197.33	30
495	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	03/2023	23136	98
496	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	09/2021	38585	66
497	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	CMRL	06/2016	03/2018	03/2021	3770	36
498	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	CPWD	11/2017	05/2020	02/2021	238.56	9
499	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	CPWD	10/2016	08/2020	03/2022	392	19
500	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	10773	44

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
501	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	KMDA	12/2014	04/2020	03/2021	272.32	11
502	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	KMDA	02/2014	12/2019	05/2021	274.76	17
503	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	BUIDCO	04/2015	04/2020	06/2021	184.93	14
504	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	03/2021	225.77	12
505	I AND D AND STP AT CHAPRA	BUIDCO	11/2018	12/2020	06/2021	236.15	6
506	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	06/2022	298.12	11
507	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
508	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12
509	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
510	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
511	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	UPJalNigam	02/2017	11/2019	03/2021	161.31	16
512	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	UPJalNigam	10/2016	08/2020	03/2021	370.4	7
513	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	UKJalNigam	03/2017	11/2019	03/2021	158	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	1,2320.00	1,7079.00	4759	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	1,1459.00	1,6580.00	5121	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	349.28	186.52	84
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	459.49	307.06	84
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	02/2021	5907.11	7980.79	2073.68	62

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	10/2021	4773.00	5178.00	405	22
8	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	1,2579.09	1,3812.30	1233.21	22

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	12/2021	1219.21	2000.00	780.79	26

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14
11	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
12	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497.00	6025.00	1528	38

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

474

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	04/2021	543.91	652.10	108.19	14
14	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677.00	3072.00	395	14
15	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
16	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	03/2021	4588.29	5245.96	657.67	31
17	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2021	3190.69	3375.90	185.21	37
18	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	5909.00	2994	110
19	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2021	352.56	490.24	137.68	48
20	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	714.25	107.19	53
21	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	06/2021	2321.00	3338.00	1017	6
22	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2021	861.79	1846.46	984.67	94
23	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678.00	1472.00	794	66

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
24	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	6700.00	1588.67	36
25	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	04/2022	8692.97	2,1312.11	12619.1	126
26	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2021	4754.42	9129.32	4374.9	36
27	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	3860.35	1368.77	126
28	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	04/2021	1,2532.44	1,3140.91	608.47	28

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

475

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	04/2021	3500.00	3994.00	494	9
30	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	07/2021	1,2964.60	1,7304.00	4339.4	38
31	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2022	3919.59	9897.59	5978	150
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
33	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2021	4824.12	5071.94	247.82	101
34	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	02/2021	1,1638.55	1,5105.22	3466.67	37
35	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,4719.10	3588.91	103
36	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	5867.38	2888.9	117
37	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	03/2021	9188.98	1,0016.10	827.12	20
38	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	1,4366.58	1,5389.42	1022.84	40
39	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	04/2021	5353.00	1,0566.00	5213	105
40	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	02/2021	2496.90	7927.34	5430.44	134

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
41	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	02/2021	691.84	1017.91	326.07	11
42	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2023	2288.00	4970.11	2682.11	21
43	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33
44	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	1185.73	454.09	15

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

476

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760.00	1536.00	776	27
46	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1536.00	593.05	39
47	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	1825.00	641.75	24
48	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	1835.83	349.98	12
49	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	1247.64	665.51	12
50	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3524.81	1616.3	9
51	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	449.39	329.66	9
52	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	1268.32	682.39	34
53	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	950.00	681.13	198
54	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	1540.13	1211.99	24
55	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	742.00	172.37	24
56	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2021	314.00	800.00	486	24
57	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	950.00	317.32	69
58	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2172.16	2051.46	105
59	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
60	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
61	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

477

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
62	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631.00	3887.48	256.48	24
63	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	810.02	108.41	64
64	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2021	495.74	734.01	238.27	102
65	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.20	1105.00	719.8	48
66	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60
67	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2024	2326.52	6911.00	4584.48	117
68	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	8600.00	7260.52	96
69	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	11/2021	410.08	860.41	450.33	33
70	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450.00	2200.00	1750	140
71	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2022	2500.00	2,7949.00	25449	241
72	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
73	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	07/2021	477.88	751.55	273.67	112
74	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
75	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	5912.40	2408.71	24
76	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	1377.48	584.59	24
77	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	663.13	120.95	12
78	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
79	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287.00	893.45	606.45	114

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

478

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
80	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.70	2643.25	354.55	36
81	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	927.94	223.63	15
82	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.20	2120.16	1074.96	180
83	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
84	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
85	RAMGANJMUINDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
86	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
87	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
88	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	2910.84	2186.15	73
89	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2023	2393.47	5521.45	3127.98	108
90	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	3037.95	905.18	156
91	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4517.49	2245.99	24
92	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	2980.41	2484.97	216
93	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
94	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	1070.00	745.27	128
95	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	04/2021	1180.19	4541.38	3361.19	148
96	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	3791.66	868.53	204

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

479

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
97	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,2264.15	7809.98	153
98	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
99	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
100	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	04/2020	04/2021	511.86	2005.25	1493.39	12
101	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	1720.00	1416.02	60
102	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	12/2023	829.74	1959.74	1130	45
103	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	3377.00	1873.29	24
104	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	1539.28	427.29	34
105	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	11/2021	1156.94	1656.00	499.06	20
106	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600.00	701.81	101.81	25
107	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	1147.00	286.57	15
108	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	03/2021	578.00	783.00	205	12
109	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
110	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	05/2021	678.54	929.86	251.32	26
111	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	477.31	182.31	37
112	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
113	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	02/2021	246.08	395.00	148.92	14

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

480

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
114	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	1378.11	1057.45	48
115	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2021	1037.15	1389.05	351.9	9
116	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
117	AJMER-BANGURGRAM	NWR	04/2011	11/2019	03/2021	213.39	375.00	161.61	16
118	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
119	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2021	258.20	358.68	100.48	30
120	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548.00	819.01	271.01	36
121	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2024	1798.00	2042.51	244.51	60
122	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
123	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	1312.96	343.13	21
124	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.20	1993.24	269.04	33
125	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
126	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	1400.00	472.99	39
127	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	2725.00	2011.52	21
128	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
129	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	2009.00	1060.96	21
130	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	1215.54	471.5	36

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

481

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
131	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
132	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	890.76	339.25	31
133	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625.00	859.00	234	63

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
134	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2021	624.98	731.50	106.52	56
135	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	1420.00	131.93	15
136	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105
137	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	04/2021	497.05	881.05	384	47
138	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	06/2021	193.69	327.92	134.23	128
139	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2021	195.04	377.99	182.95	128
140	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	1232.76	108.65	44
141	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	1191.51	237.08	73
142	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	03/2021	1928.22	2945.00	1016.78	71
143	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2021	531.13	730.97	199.84	37

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
144	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2021	1,5525.00	2,1940.00	6415	74

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

482

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2021)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
145	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2021	1,3334.00	2,4664.00	11330	71

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
146	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	1,0773.00	1,2787.00	2014	44
147	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	03/2023	2,3136.00	3,3406.00	10270	98

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
148	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
1	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	-	09/2025	05/2024
	Total		1,828.00	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
2	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00	2,433.00	2,018.90	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
3	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26	249.26	121.72	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
4	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00	315.00	196.27	12/2021	06/2021
5	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	1,793.18	09/2022	03/2022
6	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00	1,378.00	21.66	12/2022	09/2022
	Total		8,087.26	8,071.26	4,151.73		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
7	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63	808.63	639.30	01/2018 04/2021	03/2021
8	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37	14,733.37	11,441.18	11/2019 04/2021	03/2021
	Total		15,542.00	15,542.00	12,080.48		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
9	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,204.21	03/2024	03/2023

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North East Frontier Railway</u>						
10	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	760.00	801.53	12/2021 -	04/2021
	<u>North Western Railway</u>						
11	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	167.74	08/2022 -	06/2022
	<u>Rail Vikas Nigam Ltd.</u>						
12	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	875.99	12/2026 -	12/2025
13	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00	3,000.00	2,181.62	03/2023 -	12/2022
14	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	0.19	12/2025 -	03/2025
	<u>South Central Railway</u>						
15	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	521.91	03/2020 03/2022	06/2021
	<u>Southern Railway</u>						
16	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	600.30	355.13	- 10/2021	09/2021
	Total		11,725.08 -	17,201.76	6,108.32		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
17	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]	3/2018	289.67 -	289.67	177.78	08/2018 06/2021	02/2021
18	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09 -	995.09	476.77	05/2016 08/2021	04/2021
	<u>National Highways Authority Of India</u>						
19	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	2,499.00	1,539.65	03/2021 10/2021	04/2021
	Total		2,817.38 -	3,783.76	2,194.20		
	Grand Total		39,999.72	46,426.78	24,534.73		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	51.11	09/2021 -	09/2021
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	475.39 -	475.39	88.11	04/2021 -	04/2021
3	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022
4	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	-	03/2023 -	03/2023
5	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24 -	412.24	-	06/2021 -	06/2021
6	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	-	05/2022 -	05/2022
	Total		3,416.21 -	3,550.27	261.41		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.54	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
8	MAGADH EXPANSION OC(51 MTY) - [N06000015]	8/2008	6,964.33 6,964.33	706.40	639.01	07/2012 03/2025	03/2025
9	RECAST EPR AMRAPALI OC - [N06000103]	2/2012	4,983.58 4,983.58	4,983.58	244.12	03/2020 03/2024	03/2024
10	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023
11	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	238.83	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
12	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]	11/2015	1,210.12 -	1,210.12	20.92	03/2022 03/2029	03/2029
13	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	10.11	03/2029 -	03/2029
14	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	.50	03/2027 -	03/2027

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
15	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	97.54	03/2024 -	03/2024
16	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	-	03/2025 -	03/2025
17	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	.03	03/2027 -	03/2027
18	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.39	03/2026 -	03/2026
19	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	163.16	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
20	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026
21	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029
22	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027
23	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029
24	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028
	<u>Neyveli Lignite Corporation</u>						
25	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	11,135.69	11/2021 07/2022	07/2022
	<u>Northern Coal Fields Limited</u>						
26	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
27	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
28	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
29	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
30	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	8.28	03/2023 -	03/2023
31	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	142.84	03/2022 -	03/2022
32	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
33	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.40	03/2021 -	03/2021
34	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	-	03/2029 -	03/2029
35	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	-	03/2024 -	03/2024
37	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	-	03/2029 -	03/2029
38	JHIRIA WEST OPENCASE PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
39	MAHAMAYA OPENCASE PROJECT - [N06000164]	5/2018	410.26 -	410.26	24.44	03/2026 -	03/2026
40	VIJAY WEST OPENCASE PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.95	03/2026 -	03/2026
41	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,587.18	03/2023 -	03/2023
42	DURGAPUR OPENCASE PROJECT - [N06000136]	2/2015	916.24 -	916.24	9.71	03/2023 -	03/2023
43	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	.85	03/2022 -	03/2022
44	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
45	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	85.82	03/2023 -	03/2023
46	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	281.92	03/2025 -	03/2025
47	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	7/2016	281.25 -	409.87	20.99	03/2022 -	03/2022
48	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	274.95	03/2021 -	03/2021
49	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	.87	03/2026 -	03/2026
50	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	99.77	03/2021 -	03/2021
51	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	211.41	03/2021 -	03/2021
52	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
53	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	226.81	03/2022 -	03/2022
54	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	251.34	03/2021 -	03/2021
	Total		90,933.19 -	85,026.42	21,965.81		
	<u>FINANCE</u>						
	<u>Central Public Works Department</u>						
55	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	113.99	11/2021 -	11/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		348.77 -	348.77	113.99		
	<u>HEALTH AND FAMILY WELFARE</u>						
56	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	124.80	09/2023 -	09/2023
57	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
58	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	648.37	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	773.17		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
59	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	170.35	04/2018 12/2021	12/2021
60	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
61	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	.29	05/2022 -	05/2022
	Total		496.84 -	571.96	170.64		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
62	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
63	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
64	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
65	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	35.88	06/2022 -	06/2022
	Total		2,206.13 -	2,206.13	93.30		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
66	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	698.73	04/2021 12/2022	12/2022
67	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	.74	04/2021 04/2021	04/2021
	Total		6,023.00 -	6,023.00	699.47		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
68	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	17.80	02/2017 08/2022	08/2022
69	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	2,726.00	02/2020 03/2021	03/2021
70	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	365.05	12/2019 03/2021	03/2021
71	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	297.39	12/2021 -	12/2021
72	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	189.36	08/2022 -	08/2022
73	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	73.00	06/2022 -	06/2022
74	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	688.49	12/2021 -	12/2021
75	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	96.63	03/2021 -	03/2021
76	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	302.82	03/2023 -	03/2023
	<u>Gas Authority Of India Limited</u>						
77	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,231.50	12/2020 12/2021	12/2021
78	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,048.00	1,718.70	12/2020 12/2021	12/2021
79	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,483.60	12/2012 02/2022	02/2022
80	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	196.18	04/2022 -	04/2022
81	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	98.03	07/2022 -	07/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
82	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	132.60	10/2022 -	10/2022
83	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	94.56	10/2022 -	10/2022
84	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	837.00	05/2023 -	05/2023
85	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	32.60	11/2022 -	11/2022
86	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]	8/2018	217.92 -	217.92	76.80	04/2021 -	04/2021
87	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	76.84	10/2022 -	10/2022
88	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	205.30	07/2022 -	07/2022
89	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	327.01	166.90	08/2020 05/2021	05/2021
90	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,096.40	12/2021 -	12/2021
91	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	74.18	07/2022 -	07/2022
92	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	778.20	12/2020 12/2021	12/2021
<u>Hindustan Petroleum Corporation Limited</u>							
93	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	26,264.00	13,352.70	07/2020 07/2022	07/2022
94	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	185.40	11/2021 -	11/2021
95	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	91.57	09/2026 -	09/2026
96	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	-	08/2021 -	08/2021
97	220 KV GRID SUPPLY - [N16000407]	10/2020	303.40 -	303.40	-	03/2021 -	03/2021
98	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	-	11/2022 -	11/2022
99	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB [N16000402]	5/2020	1,421.46 -	1,244.50	54.49	02/2023 -	02/2023
100	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	14.63	03/2031 -	03/2031
101	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	153.20	03/2029 -	03/2029
102	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	103.91	11/2022 -	11/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
103	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	131.02	12/2022 -	12/2022
104	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	253.92	11/2020 06/2021	06/2021
105	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	67.53	06/2020 09/2021	09/2021
106	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	763.33	06/2022 -	06/2022
107	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	3,072.00	1,825.04	06/2021 08/2022	08/2022
	<u>Indian Oil Corporation Limited</u>						
108	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	385.53	10/2017 03/2022	03/2022
109	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	301.57	03/2021 12/2021	12/2021
110	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	471.42	02/2020 06/2021	06/2021
111	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,561.15	10/2021 -	10/2021
112	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	126.15	01/2021 06/2021	06/2021
113	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	65.94	- 05/2023	05/2023
114	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	398.94	08/2022 -	08/2022
115	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	259.40	02/2020 10/2021	10/2021
116	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	29.92	10/2020 02/2022	02/2022
117	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	17.21	08/2020 11/2021	11/2021
118	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	75.17	02/2020 08/2021	08/2021
119	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY [N16000409]	9/2020	18,936.00 -	18,936.00	-	09/2024 -	09/2024
120	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00 -	1,398.00	75.59	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
121	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00 -	921.00	3.05	09/2023 -	09/2023
122	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	1.76	08/2022 -	08/2022
123	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	77.55	01/2024 -	01/2024
124	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	1.73	07/2022 -	07/2022
125	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	55.17	01/2023 -	01/2023
126	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	151.68	10/2021 -	10/2021
127	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	429.94	12/2022 -	12/2022
128	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	1.93	09/2022 -	09/2022
129	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	25.82	06/2021 07/2022	07/2022
130	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	1,568.98	08/2021 -	08/2021
131	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	6.63	09/2021 -	09/2021
132	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	240.52	02/2020 02/2022	02/2022
133	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	222.31	01/2021 03/2022	03/2022
134	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	65.53	10/2021 -	10/2021
135	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	722.25	04/2023 -	04/2023
136	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	13.16	07/2021 -	07/2021
137	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	84.15	05/2023 -	05/2023
138	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	8.49	07/2022 -	07/2022
139	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	54.61	12/2021 -	12/2021
140	LPG BP PROJECT JODHPUR - [N16000318]	3/2018	229.80 -	229.80	80.21	- 05/2022	05/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	115.92	03/2021 09/2021	09/2021
142	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	293.00	162.96	06/2020 09/2021	09/2021
143	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	267.12	04/2021 03/2021	03/2021
144	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	88.03	04/2020 10/2021	10/2021
145	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	125.61	11/2021 -	11/2021
146	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	46.92	12/2019 03/2022	03/2022
147	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	85.89	02/2020 06/2021	06/2021
148	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,468.42	02/2022 -	02/2022
149	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	502.00	403.62	08/2019 06/2021	06/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
150	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	1.46	06/2023 -	06/2023
	<u>Numaligarh Refinery Limited</u>						
151	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024
152	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
153	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,685.92	04/2018 05/2021	05/2021
154	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	303.75	180.83	05/2020 05/2021	05/2021
155	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]	11/2015	650.82 -	624.35	446.46	03/2019 05/2021	05/2021
156	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	25,090.00	10,477.71	06/2020 06/2022	06/2022
157	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	634.60	03/2023 03/2022	03/2022
158	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	773.52	03/2026 -	03/2026
159	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	79.65	08/2022 -	08/2022
160	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	619.17	12/2020 05/2021	05/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
161	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,238.26	03/2022 -	03/2022
162	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	2,305.03	05/2021 -	05/2021
163	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	974.84	03/2022 05/2023	05/2023
164	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	1,565.69	05/2021 -	05/2021
165	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	3,596.00	3,494.45	05/2021 05/2021	05/2021
	Total		2,48,540.68 -	2,49,320.63	70,164.37		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
166	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	9,897.59	8,825.13	09/2009 03/2022	03/2022
167	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	19,992.43	13,233.01	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
168	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	10,016.10	7,966.63	07/2019 03/2021	03/2021
169	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	8,125.04	11/2020 03/2022	03/2022
170	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	18,308.58	10/2011 04/2022	04/2022
171	DEVIKOT SOLAR 90MW - [N18000280]	3/2020	501.29 -	501.29	49.76	09/2021 01/2022	01/2022
172	NOKHRA - [N18000282]	3/2020	1,722.14 -	1,722.14	103.85	09/2021 01/2022	01/2022
173	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	-	04/2021 -	04/2021
174	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]	3/2020	1,782.00 -	1,782.00	-	09/2021 -	09/2021
175	KAYAMKULAM SOLAR 70 MW - [N18000288]	9/2019	403.62 -	403.62	-	06/2021 -	06/2021
176	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	-	09/2021 -	09/2021
177	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	-	09/2021 -	09/2021
178	JETSAR SOLAR 160 MW - [N18000287]	12/2019	702.28 -	702.28	-	03/2021 -	03/2021
179	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71 -	1,522.71	-	09/2021 -	09/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
180	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	261.80	-	10/2021 -	10/2021
181	DEVIKOT SOLAR 150MW - [N18000281]	1/2020	798.24 -	798.24	31.64	09/2021 01/2022	01/2022
182	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	226.00	11/2020 04/2021	04/2021
183	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,389.42	11,612.82	06/2019 10/2022	10/2022
	<u>North East Electric Power Corporation</u>						
184	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	8,154.49	12/2009 02/2021	02/2021
	<u>Power Grid Corporation Of India Limited</u>						
185	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,869.26	08/2013 03/2022	03/2022
186	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	219.66	157.07	07/2019 04/2021	04/2021
187	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	200.36	02/2019 06/2021	06/2021
188	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	343.03	04/2018 03/2021	03/2021
	<u>Satluj Jal Vidyut Nigam Limited</u>						
189	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	1,479.16	01/2024 -	01/2024
190	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	524.12	12/2021 -	12/2021
191	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	286.90	01/2026 -	01/2026
	Total		92,050.59 -	1,35,257.63	92,496.85		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
192	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023
193	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
194	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023
195	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
196	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>East Coast Railway</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
197	TALCHER-BIMALAGARH(NL)(ECOR) - [N220100328	4/2005	810.78 -	1,928.07	845.24	06/2021 03/2025	03/2025
198	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	2,499.71	604.03	03/2022 03/2024	03/2024
199	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	596.91	12/2018 03/2024	03/2024
200	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	4/2015	701.61 -	810.02	171.45	11/2018 03/2024	03/2024
201	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379	4/2015	2,361.74 -	2,361.74	380.90	03/2022 03/2026	03/2026
202	JAGADALPUR-KORAPUT DOUBLING - [N22000376	4/2015	1,547.38 -	1,547.38	603.73	03/2022 03/2023	03/2023
203	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	4/1994	2,923.13 -	3,791.66	1,413.99	03/2009 03/2026	03/2026
204	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	902.85	03/2020 03/2023	03/2023
205	BHADRAK - NERGUNDI 3RD LINE - [N22000316	3/2013	843.04 -	843.04	208.46	10/2020 03/2024	03/2024
206	SAMBALPUR-TALCHER DOUBLING - [N22000315	3/2011	1,111.99 -	1,539.28	1,109.06	02/2019 12/2021	12/2021
	<u>North Central Railway</u>						
207	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495	3/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023
208	JHANSI BINA DOUBLING - [N22000496	9/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021
	<u>North East Frontier Railway</u>						
209	SEVOK RANGPO, NEFR - [N22000102	4/2008	1,339.48 -	8,600.00	619.18	12/2015 12/2023	12/2023
210	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	4/2010	906.46 -	4,083.02	263.68	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
211	HATHUA-BHATNI (N L) (NER) - [220100319	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
212	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42 -	1,295.42	929.79	03/2022 -	03/2022
213	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	3/2007	243.78 -	895.00	112.02	12/2021 -	12/2021
	<u>Northern Railway</u>						
214	CHANDIGARH-BADDI - [N22000467	4/2007	328.14 -	1,540.13	242.12	03/2023 03/2025	03/2025
	<u>National High Speed Rail Corporation Limited</u>						
215	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463	12/2015	1,08,000.00 -	1,08,000.00	11,158.98	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
216	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	535.71	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
217	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,438.76	12/2021 -	12/2021
218	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021
219	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
220	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	705.50	12/2024 -	12/2024
221	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023
	<u>South East Central Railway</u>						
222	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	3,524.81	982.38	03/2023 12/2023	12/2023
	<u>South Western Railway</u>						
223	GADAG-WADI NL - [N22000299]	4/2013	2,841.84 -	2,841.84	277.39	12/2018 06/2025	06/2025
224	HUBLI- CHIKJAJUR - [N22000325]	3/2015	1,156.94 -	1,656.00	1,119.96	03/2020 11/2021	11/2021
225	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	783.00	613.57	03/2020 03/2021	03/2021
226	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	1,147.00	881.92	03/2020 06/2021	06/2021
	<u>Southern Railway</u>						
227	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	4/2008	523.52 -	1,205.00	2.28	- 03/2024	03/2024
	<u>Western Railway</u>						
228	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	5,912.40	2,143.20	03/2022 03/2024	03/2024
229	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	897.00	03/2022 03/2023	03/2023
230	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	1,017.91	650.65	03/2020 02/2021	02/2021
231	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	249.28	06/2020 03/2023	03/2023
232	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	890.76	745.11	03/2019 10/2021	10/2021
233	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	642.89	03/2021 12/2022	12/2022
234	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,389.05	1,103.31	03/2021 12/2021	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
235	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	1,378.11	540.09	03/2019 03/2023	03/2023
236	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	179.19	- 03/2024	03/2024
237	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	866.05	03/2022 03/2025	03/2025
238	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	411.62	126.05	03/2012 03/2023	03/2023
239	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,959.74	1,784.02	03/2020 12/2023	12/2023
	Total		1,84,603.63 -	2,13,266.72	43,035.41		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
240	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]	12/2015	291.05 -	291.05	200.71	- 03/2021	03/2021
241	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	957.54 -	957.54	735.81	02/2020 04/2021	04/2021
242	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]	12/2014	379.16 -	379.16	256.32	11/2017 03/2021	03/2021
243	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]	11/2017	188.80 -	188.80	75.05	05/2019 03/2021	03/2021
244	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]	12/2014	496.02 -	496.02	239.88	03/2015 06/2021	06/2021
245	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]	3/2017	423.79 -	423.79	264.67	01/2018 03/2021	03/2021
246	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]	3/2016	452.94 -	435.61	85.00	07/2016 06/2021	06/2021
247	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	1/2016	624.98 -	731.50	399.36	10/2016 06/2021	06/2021
248	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	1/2016	476.20 544.00	544.00	397.33	09/2016 06/2021	06/2021
249	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]	11/2015	335.32 -	335.32	264.26	06/2017 06/2021	06/2021
250	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	1/2016	497.14 -	572.66	255.42	08/2016 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
251	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021
252	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198	1/2019	264.50 -	264.50	78.54	03/2021 -	03/2021
253	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881	11/2017	184.62 -	184.62	115.57	02/2018 02/2021	02/2021
254	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	197.67	5.75	12/2022 -	12/2022
255	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878	11/2017	235.91 -	235.91	173.80	02/2018 02/2021	02/2021
256	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875	2/2018	169.63 -	169.63	38.45	03/2018 04/2021	04/2021
257	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	3/2018	166.21 -	173.41	139.19	08/2018 03/2021	03/2021
258	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870	3/2018	162.56 -	162.56	129.98	03/2018 02/2021	02/2021
259	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	366.24	08/2017 06/2021	06/2021
260	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301	3/2015	271.45 -	271.45	225.81	10/2015 03/2021	03/2021
261	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	8/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021
262	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021
263	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240	3/2020	370.36 -	370.36	90.45	08/2022 -	08/2022
264	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	105.72	08/2018 03/2021	03/2021
265	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	3/2016	877.79 -	877.79	668.14	06/2019 04/2021	04/2021
266	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898	1/2016	809.16 -	809.16	512.17	07/2018 05/2021	05/2021
267	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896	1/2017	373.82 -	373.82	186.74	09/2019 06/2021	06/2021
268	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
269	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892	11/2017	249.05 -	249.05	191.67	07/2018 03/2021	03/2021
270	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	3/2018	217.22 -	226.88	170.05	08/2018 03/2021	03/2021
271	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888	3/2018	214.69 -	214.69	59.72	03/2018 09/2021	09/2021
272	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886	1/2017	205.05 -	205.05	116.58	03/2017 06/2021	06/2021
273	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	109.64	06/2021 -	06/2021
274	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	50.27	12/2022 -	12/2022
275	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177	10/2016	171.90 -	171.90	110.19	08/2020 07/2021	07/2021
276	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	70.46	09/2021 -	09/2021
277	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	345.46	03/2018 06/2021	06/2021
278	BHOGAN KHURD TO KASHEDI - [N24001132	9/2017	743.21 743.00	743.21	137.87	06/2021 -	06/2021
279	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	539.22	12/2019 03/2021	03/2021
280	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021
281	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966	1/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
282	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244	8/2020	301.06 -	301.06	-	04/2022 -	04/2022
283	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245	9/2020	353.90 -	353.90	-	05/2022 -	05/2022
284	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	-	12/2022 -	12/2022
285	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	-	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
286	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	-	04/2023 -	04/2023
287	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]	3/2020	242.97 -	242.97	-	06/2022 -	06/2022
288	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]	9/2020	277.44 -	277.44	-	10/2022 -	10/2022
289	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258]	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
290	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]	3/2020	178.43 -	178.43	-	07/2022 -	07/2022
291	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]	7/2020	210.79 -	210.79	-	04/2022 -	04/2022
292	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265]	3/2020	154.51 -	154.51	-	07/2022 -	07/2022
293	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	-	04/2022 -	04/2022
294	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]	6/2020	277.50 -	277.50	-	01/2022 -	01/2022
295	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24001262]	7/2020	345.38 -	345.38	-	04/2023 -	04/2023
296	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24001261]	8/2020	311.00 -	311.00	-	04/2023 -	04/2023
297	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]	9/2020	257.15 -	257.15	5.29	04/2022 -	04/2022
298	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	-	04/2022 -	04/2022
299	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
300	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
301	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	-	04/2022 -	04/2022
302	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	17.84	08/2022 -	08/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
303	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	18.22	06/2022 -	06/2022
304	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	14.15	08/2022 -	08/2022
305	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270	3/2020	292.24 -	292.24	8.60	06/2022 -	06/2022
306	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	12.40	03/2022 -	03/2022
307	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	101.20	07/2022 -	07/2022
308	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	41.64	06/2022 -	06/2022
309	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284	3/2020	361.53 -	361.53	3.66	06/2022 -	06/2022
310	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283	3/2020	281.78 -	281.78	-	07/2022 -	07/2022
311	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282	3/2020	355.79 -	355.79	12.99	06/2022 -	06/2022
312	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281	3/2020	292.24 -	292.24	-	07/2022 -	07/2022
313	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280	3/2020	320.97 -	320.97	8.86	06/2022 -	06/2022
314	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279	3/2020	216.49 -	216.49	-	07/2022 -	07/2022
315	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278	3/2020	206.88 -	206.88	-	07/2022 -	07/2022
316	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277	9/2020	275.02 -	275.02	4.72	10/2022 -	10/2022
317	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288	8/2020	232.29 -	232.29	-	04/2022 -	04/2022
318	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287	4/2020	330.80 -	330.80	1.50	12/2021 -	12/2021
319	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285	3/2020	330.78 -	330.78	11.24	12/2021 -	12/2021
320	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257	8/2020	159.85 -	159.85	-	10/2022 -	10/2022
321	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	38.33	09/2026 -	09/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
322	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	29.22	12/2023 -	12/2023
323	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]	3/2019	402.94 -	402.94	.78	04/2022 -	04/2022
324	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]	6/2020	347.36 -	347.36	-	01/2022 -	01/2022
325	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	-	04/2022 -	04/2022
326	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]	3/2020	247.76 -	247.76	-	01/2022 -	01/2022
	<u>National Highways Authority Of India</u>						
327	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021
328	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
329	PREPARATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
330	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]	11/2019	1,601.10 -	1,601.10	-	02/2021 -	02/2021
331	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]	11/2019	1,226.88 -	1,226.88	-	02/2021 -	02/2021
332	4-LANING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	597.77	03/2020 03/2021	03/2021
333	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	199.44	03/2019 12/2021	12/2021
334	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	630.68	05/2018 06/2021	06/2021
335	4-LANING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]	3/2016	701.40 -	701.40	119.00	03/2019 03/2022	03/2022
336	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	585.57	05/2018 06/2021	06/2021
	Total		47,376.17 -	48,188.80	13,381.05		
	<u>RURAL DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
337	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021
	Total		361.60 -	361.60	12.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
338	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,814.28	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,814.28		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
339	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	21,940.00	17,691.25	05/2015 07/2021	07/2021
340	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124	11/2015	2,907.00 -	2,907.00	185.08	06/2023 -	06/2023
	<u>Rastrya Ispat Nigam Limited</u>						
341	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	1,552.60	09/2018 03/2021	03/2021
	<u>Steel Authority Of India Limited (Sail)</u>						
342	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	513.54	10/2017 12/2021	12/2021
343	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	172.15	06/2019 05/2021	05/2021
344	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	17.50	12/2023 -	12/2023
345	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	.63	05/2023 -	05/2023
	Total		22,331.15 -	28,746.15	20,132.75		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
346	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	56.76	03/2024 -	03/2024
347	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	16.58	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
348	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110	10/2016	422.00 -	422.00	55.38	03/2021 07/2021	07/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
349	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022
	<u>Delhi Metro Rail Corporation</u>						
350	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS [N28000135]	7/2019	24,948.65 -	24,948.65	1,248.28	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
351	KANPUR METRO RAIL PROJECT - [N28000144]	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
352	AGRA METRO RAIL PROJECT - [N28000145]	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
353	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	5,696.05	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
354	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	126.50	02/2023 -	02/2023
355	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	117.53	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
356	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	2,987.00	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
357	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,365.77	231.90	06/2024 -	06/2024
	Total		1,32,861.21 -	1,32,861.21	10,557.98		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
358	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	55.02	07/2021 -	07/2021
359	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	88.45	04/2021 -	04/2021
360	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]	5/2017	191.62 -	191.62	44.97	11/2020 03/2021	03/2021
361	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	.29	06/2022 -	06/2022
362	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	.42	06/2022 -	06/2022
363	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK [N30000044]	3/2017	277.42 -	277.42	125.66	05/2021 -	05/2021
364	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	152.78	05/2021 -	05/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
365	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
366	I AND D AND STP AT CHAPPRA - [N30000028]	11/2018	236.15 -	236.15	22.69	12/2020 06/2021	06/2021
	<u>Delhi Jal Board</u>						
367	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	149.78	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
368	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
369	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
370	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
371	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]	2/2014	274.76 -	274.76	198.28	12/2019 05/2021	05/2021
372	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
373	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH [N30000042]	5/2018	160.00 -	160.00	-	02/2022 -	02/2022
374	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
375	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
376	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
377	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
378	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA [N30000032]	5/2018	198.43 -	198.43	-	02/2022 -	02/2022
	<u>Uttar Pradesh Jal Nigam</u>						
379	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	32.47	09/2021 -	09/2021
380	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]	10/2016	370.40 -	370.40	361.93	08/2020 03/2021	03/2021
381	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH [N30000021]	1/2019	231.79 -	234.03	-	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
382	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	2/2019	681.78 -	681.78	-	06/2022 -	06/2022
383	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022	1/2019	206.05 -	206.05	21.10	10/2021 -	10/2021
384	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
385	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010	3/2018	967.23 -	967.23	54.21	09/2021 -	09/2021
386	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008	10/2017	213.62 -	213.62	-	03/2022 -	03/2022
387	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007	3/2018	904.00 -	904.00	56.74	09/2021 -	09/2021
	<u>Uttarakhand Pey Jal Nigam</u>						
388	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004	3/2017	158.00 -	158.00	77.81	11/2019 03/2021	03/2021
	Total		11,145.54 -	11,147.78	1,442.60		
	Grand Total		8,52,395.89	9,26,213.88	2,77,115.52		

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2021)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,915.80	09/2010 09/2016	10/2022	145	73
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	16,297.00	12/2015 -	02/2022	74	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	12,992.00	12/2016 -	03/2023	75	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	23,131.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	58,335.80				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	33	-
7	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	458.00 -	458.00	105.12	03/2020 -	06/2021	15	-
8	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	-	02/2020 -	06/2021	16	-
9	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10	-
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5	-
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	12	-
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7	-
13	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12	-
14	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	389.71	37.38	11/2021 -	10/2022	11	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI, GUJARAT	01/2018	1,405.00 -	1,405.00	-	08/2022 -	03/2023	7	-
16	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI, TAMIL NADU	06/2019	380.87 -	380.87	-	03/2022 -	03/2023	12	-
	Total		9,931.85 -	10,045.95	2,000.31				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
17	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	280.46	05/2014 -	06/2021	85	-
18	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	341.22	30.15	03/2017 -	10/2021	55	-
19	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	334.27	18.35	04/2018 -	12/2021	44	-
20	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	457.98	04/2015 -	03/2022	83	-
21	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	20.22	04/2014 -	04/2023	108	-
	<u>Central Coal Fields Limited</u>								
22	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	106.63	03/2011 -	03/2022	132	-
23	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	401.87	03/2016 -	03/2022	72	-
24	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	96.86	03/2014 -	03/2022	96	-
	<u>Eastern Coal Fields Limited</u>								
25	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	641.54	03/2018 -	03/2021	36	-
	<u>Mahanadi Coal Fields Limited</u>								
26	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	168.13	03/2012 -	03/2021	108	-
27	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108	-
28	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60	-
29	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36	-
30	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL, ODISHA	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168	-
	<u>Neyveli Lignite Corporation</u>								
31	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,980.79	7,980.79	7,404.29	12/2015 -	02/2021	62	-
32	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC, JHARKHAND	07/2013	1,795.01 -	1,795.01	32.27	08/2022 -	09/2023	13	-
	<u>Northern Coal Fields Limited</u>								
33	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	558.53	03/2021 -	03/2022	12	-
34	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL, MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	144.51	03/2022 -	03/2023	12	-

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Singareni Colliers Company Limited</u>								
35	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	193.33	03/2016 -	03/2021	60	-
36	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	129.58	03/2015 -	03/2022	84	-
37	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	292.49	03/2015 -	03/2022	84	-
38	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	473.22	21.17	03/2015 -	03/2022	84	-
39	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	384.32	124.04	07/2016 -	03/2022	68	-
40	KAKATIYAKHANI OPENCASST-2 PROJECT - [N06000129]SCCL, TELANGANA	05/2015	397.09 -	442.42	106.68	03/2019 -	03/2022	36	-
41	KAKATIYAKHANI OPENCASST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	169.95	03/2019 -	03/2022	36	-
42	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	-
	<u>South-Eastern Coal Fields Limited</u>								
43	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	211.32	03/2014 -	03/2021	84	-
44	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 459.49	459.49	187.31	03/2015 03/2020	03/2022	84	24
45	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	4.43	03/2014 -	03/2022	96	-
46	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL, MADHYA PRADESH	03/2016	869.44 -	869.44	120.77	03/2021 -	03/2022	12	-
47	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATISGARH	06/2010	11,816.40 -	11,816.40	4,219.60	03/2023 03/2016	03/2023	0	84
48	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	-
49	AMGAON OPENCASST PROJECT RCE - [N06000135]SECL, CHHATISGARH	07/2015	316.10 -	316.10	124.35	03/2020 -	03/2023	36	-
50	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	60.14	03/2021 -	03/2024	36	-
	<u>Western Coal Fields Limited</u>								
51	ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	12	-
52	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL, MAHARASHTRA	11/2015	313.34 -	313.34	141.08	03/2021 -	03/2024	36	-
53	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL, MULTI STATE	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	36	-
54	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL, MAHARASHTRA	11/2015	851.60 -	851.60	194.28	03/2020 -	03/2026	72	-
55	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL, MAHARASHTRA	11/2014	1,184.33 -	1,184.33	368.56	03/2020 -	03/2027	84	-
	Total		40,944.34 -	43,700.30	19,523.86				
	<u>FINANCE</u>								

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Central Public Works Department</u>								
56	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD, TAMIL NADU	12/2015	209.00 -	208.96	205.40	10/2019 -	04/2021	18	-
	Total		209.00 -	208.96	205.40				
	<u>FERTILISERS</u>								
	<u>National Fertiliser Limited</u>								
57	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL, PUNJAB	01/2018	218.83 -	218.83	174.61	11/2019 -	02/2021	15	-
58	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL, HARYANA	01/2018	215.92 -	215.92	166.34	11/2019 -	03/2021	16	-
59	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL, PUNJAB	01/2018	239.81 -	239.81	185.55	11/2019 -	03/2021	16	-
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
60	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF, MAHARASHTRA	04/2018	426.72 -	426.72	315.95	04/2020 03/2021	04/2021	12	1
	Total		1,101.28 -	1,101.28	842.45				
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
61	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO, ODISHA	12/2015	355.00 -	355.00	93.85	11/2020 -	02/2021	3	-
	Total		355.00 -	355.00	93.85				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (Sail)</u>								
62	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL	12/2018	263.36 -	263.36	177.74	09/2020 03/2021	05/2021	8	2
	Total		263.36 -	263.36	177.74				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
63	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA	11/2014	4,588.29 -	5,245.96	4,852.63	08/2018 11/2019	03/2021	31	16
64	PUNE POL STORAGE DEPOT - [N16000313]BPCL, MAHARASHTRA	08/2016	282.64 -	282.64	241.79	08/2020 -	03/2021	7	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
65	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	151.16	02/2021 -	03/2021	1	-
66	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	711.00	06/2019 -	02/2022	32	-
	<u>Chennai Petroleum Corporation Limited</u>								
67	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13	-
	<u>Gas Authority Of India Limited</u>								
68	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	187.00	04/2018 -	04/2021	36	-
69	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,556.70	12/2020 -	05/2021	5	-
70	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	225.54	39.50	02/2021 -	12/2021	10	-
	<u>Hindustan Petroleum Corporation Limited</u>								
71	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	84.63	07/2020 -	07/2021	12	-
	<u>Indian Oil Corporation Limited</u>								
72	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	138.76	01/2021 -	04/2021	3	-
73	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	147.12	01/2021 -	04/2021	3	-
74	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	508.53	07/2018 02/2021	05/2021	34	3
75	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	3,338.00	2,750.24	12/2020 -	06/2021	6	-
76	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	232.67	04/2021 -	07/2021	3	-
77	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	3,027.90	1,755.66	03/2021 -	08/2021	5	-
78	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	185.01	10/2020 -	08/2021	10	-
79	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	132.88	01/2021 -	10/2021	9	-
80	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	136.81	08/2021 -	11/2021	3	-

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
81	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	589.44	10/2021 -	12/2021	2	-
82	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	6,025.00	3,409.77	12/2018 -	02/2022	38	-
83	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	587.98	08/2020 -	04/2022	20	-
84	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	92.80	04/2022 -	02/2023	10	-
85	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	65.87	04/2022 -	08/2023	16	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
86	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	443.62	03/2020 11/2020	06/2021	15	7
87	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,556.82	12/2019 04/2021	10/2021	22	6
	<u>Oil & Natural Gas Corporation Limited</u>								
88	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	1,846.46	1,546.02	05/2013 12/2020	03/2021	94	3
	<u>Oil India Limited</u>								
89	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021	48	2
90	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	187.00	10/2020 -	03/2021	5	-
91	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	457.91	12/2019 -	04/2021	16	-
92	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 638.60	652.10	136.05	02/2020 -	04/2021	14	-
93	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	222.21	144.80	08/2020 -	04/2021	8	-
	Total		31,269.51 -	36,226.14	23,726.18				
	<u>POWER</u>								
	<u>Central Public Works Department</u>								
94	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	201.69	11/2019 -	05/2021	18	-
	<u>Chenab Valley Power Projects [P] Limited</u>								
95	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,664.74	04/2020 -	07/2025	63	-
	<u>National Thermal Power Corporation</u>								

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
96	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 15,105.22	15,105.22	13,657.43	01/2018 10/2020	02/2021	37	4
97	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	1,746.41	12/2018 -	03/2021	27	-
98	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 13,140.91	13,140.91	11,641.13	12/2018 02/2021	04/2021	28	2
99	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,680.05	07/2012 06/2020	04/2021	105	10
100	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	410.98	11/2018 -	05/2021	30	-
101	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,463.61	05/2018 06/2021	07/2021	38	1
102	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,841.21	03/2013 12/2021	12/2022	117	12
103	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,112.00	4,060.28	03/2023 -	09/2024	18	-
104	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,381.54	649.64	09/2019 11/2022	12/2024	63	25
	<u>Power Grid Corporation Of India Limited</u>								
105	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,630.84	10/2012 06/2020	03/2021	101	9
106	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	5,070.13	4,041.83	04/2020 -	03/2021	11	-
107	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	456.53	02/2019 05/2020	03/2021	25	10
108	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,644.55	02/2020 09/2020	03/2021	13	6
109	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	239.65	05/2020 -	03/2021	10	-
110	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	148.03	06/2019 09/2020	04/2021	22	7
111	EASTERN REGION STRENGTHENING SCHEME- XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	2,825.43	07/2020 -	04/2021	9	-
112	EASTERN REGION STRENGTHENING SCHEME- XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	477.66	11/2016 06/2020	05/2021	54	11
113	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	241.55	04/2016 12/2017	06/2021	62	42
114	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	89.36	03/2018 -	06/2021	39	-
115	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	519.78	05/2017 07/2020	06/2021	49	11

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
116	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	224.72	12/2019 06/2020	06/2021	18	12
117	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	2,002.54	12/2018 -	12/2021	36	-
118	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	2,541.14	12/2018 -	12/2021	36	-
	<u>Thdc India Limited</u>								
119	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 -	1,587.16	464.00	09/2020 -	08/2022	23	-
120	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,860.35	2,161.90	06/2013 -	12/2023	126	-
121	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	1,432.11	09/2023 -	08/2024	11	-
	Total		1,21,101.38 -	1,43,642.70	87,158.79				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Central Public Works Department</u>								
122	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	123.92	03/2020 -	05/2021	14	-
123	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	36.14	03/2020 -	12/2021	21	-
124	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
125	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>Hll Infra Tech Services Limited</u>								
126	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	524.06	04/2020 -	07/2021	15	-
127	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	449.74	06/2020 -	07/2021	13	-
128	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	296.84	05/2021 -	07/2022	14	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
129	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	481.52	11/2013 -	03/2021	88	-
130	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	250.00	229.39	05/2017 -	03/2021	46	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	24	-
132	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	280.39	03/2019 -	03/2021	24	-
133	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	161.29	02/2018 -	04/2021	38	-
134	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	234.12	05/2018 -	12/2021	43	-
	Total		4,940.96 -	4,754.30	3,117.71				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
135	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24	-
136	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24	-
137	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12	-
138	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24	-
139	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12	-
140	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24	-
141	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
142	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	36	-
143	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	316.04	03/2019 -	03/2021	24	-
	<u>East Central Railways</u>								
144	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	929.86	738.84	03/2019 -	05/2021	26	-
145	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	751.55	687.20	03/2012 -	07/2021	112	-
146	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	217.40	03/2019 -	03/2022	36	-
147	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	348.23	316.23	03/2021 -	03/2022	12	-
148	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	15	-
149	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	128	-
150	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	36	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	862.71	03/2020 -	03/2023	36	-
152	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	471.48	03/2020 -	03/2023	36	-
153	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,111.96	03/2020 -	03/2024	48	-
154	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	309.44	03/2021 -	03/2024	36	-
	<u>East Coast Railway</u>								
155	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	219.74	03/2020 03/2021	03/2022	24	12
	<u>Eastern Railways</u>								
156	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28	-
157	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	663.13	516.55	03/2020 -	03/2021	12	-
158	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.87	02/2013 -	03/2024	133	-
159	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	903.03	03/2019 12/2009	03/2025	72	183
160	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,091.59	970.10	12/2010 -	03/2025	171	-
161	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228	-
162	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	355.79	03/2022 -	03/2025	36	-
163	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	640.17	03/2016 -	03/2025	108	-
164	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.78	03/2017 -	03/2025	96	-
165	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	185.36	03/2016 -	03/2025	108	-
166	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	374.08	03/2017 -	03/2025	96	-
167	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
168	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	163.26	02/2012 -	03/2025	157	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
169	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]JER,MULTI STATE	04/2009	257.42 -	257.42	106.31	03/2014 -	03/2025	132	-
170	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]JER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
171	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42	-
172	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21	-
173	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-
	<u>Metropolitan Rapid Transport Projects</u>								
174	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-
175	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
176	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102	-
177	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216	-
	<u>North Central Railway</u>								
178	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
179	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 486.96	800.00	795.88	03/2019 -	03/2021	24	-
180	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,645.92	12/2008 -	04/2021	148	-
181	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,133.64	03/2021 -	05/2021	2	-
182	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	-
183	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,105.00	787.79	03/2019 -	03/2023	48	-
184	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	3,816.20	03/2014 -	03/2023	108	-
185	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,478.05	03/2022 -	03/2023	12	-
186	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	10,777.52	03/2011 -	12/2023	153	-
187	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	968.95	03/2019 -	03/2024	60	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
188	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	69.92	03/2019 -	03/2024	60	-
189	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,911.00	1,125.27	03/2015 -	12/2024	117	-
	<u>North Eastern Railway</u>								
190	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	476.60	04/2017 -	03/2021	47	-
191	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	80.76	12/2019 -	04/2021	16	-
192	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	68	-
193	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	37	-
194	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	199.70	01/2022 -	03/2022	2	-
195	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
196	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
197	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
	<u>North Western Railway</u>								
198	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	395.00	324.37	12/2019 -	02/2021	14	-
199	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	375.00	337.30	11/2019 -	03/2021	16	-
200	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	307.78	03/2020 -	06/2021	15	-
201	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	691.34	02/2019 -	11/2021	33	-
202	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	172.41	03/2020 -	04/2022	25	-
	<u>Northern Railway</u>								
203	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	893.45	658.97	12/2011 -	06/2021	114	-
204	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	859.00	852.73	03/2016 -	06/2021	63	-
205	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	22,879.22	11/2002 -	12/2022	241	-
206	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	-
207	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108	-
	<u>Rail India Technical And Economic Service</u>								

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
208	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES, CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15	-
	<u>Rail Vikas Nigam Ltd.</u>								
209	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	950.00	799.01	03/2016 -	12/2021	69	-
210	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL, MAHARASHTRA	03/2009	713.48 -	2,725.00	2,531.51	03/2020 -	12/2021	21	-
211	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	2,009.00	1,764.93	03/2020 -	12/2021	21	-
212	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,282.18	03/2020 -	12/2021	21	-
213	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,546.20	12/2020 -	12/2021	12	-
214	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	1,868.89	1,795.61	12/2021 -	03/2022	3	-
215	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24	-
216	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	-
217	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,302.29	03/2019 -	06/2022	39	-
218	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	-
219	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	-
220	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	-
221	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	833.10	03/2023 -	12/2024	21	-
222	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,676.61	03/2016 -	03/2025	108	-
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,072.08	03/2016 -	03/2025	108	-
224	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,768.76	12/2024 -	03/2025	3	-
225	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-
226	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	3,327.72	1,225.51	12/2024 -	12/2026	24	-
	<u>South Central Railway</u>								

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
227	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	-
228	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	1,847.08	03/2000 -	03/2023	276	-
229	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	850.07	03/2009 -	03/2024	180	-
230	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	478.70	03/2010 -	03/2024	168	-
231	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	543.07	03/2023 -	03/2024	12	-
232	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,214.20	03/2021 -	03/2024	36	-
233	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,370.71	03/2021 -	03/2024	36	-
234	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,165.50	03/2022 -	03/2024	24	-
235	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	350.55	03/2014 -	03/2027	156	-
	<u>South East Central Railway</u>								
236	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12	-
237	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34	-
238	JHARSUGUDA-BILASPU 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33	-
239	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24	-
240	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36	-
	<u>South Eastern Railway</u>								
241	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	297.17	12/2018 12/2018	06/2021	30	30
242	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	857.47	03/2020 03/2020	12/2021	21	21
243	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	704.10	03/2021 03/2021	12/2023	33	33
244	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
245	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
246	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	1,528.14	03/2019 -	03/2021	24	-
247	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	307.78	03/2016 -	12/2023	93	-
248	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	35.01	03/2016 -	12/2023	93	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
249	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-
250	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
	<u>Southern Railway</u>								
251	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,121.00	906.57	- 02/2021	04/2021	-	2
252	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	-
253	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-
254	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	-
255	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	60	-
256	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	73	-
257	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
258	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	105	-
	<u>West Central Railway</u>								
259	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,132.38	03/2021 -	03/2023	24	-
260	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,762.94	1,084.58	03/2020 -	03/2023	36	-
261	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	-
262	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	254.64	03/2022 -	03/2023	12	-
263	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	-
	Total		1,66,707.97 -	2,76,022.84	1,36,540.02				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
264	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	191.21	117.80	11/2019 01/2021	02/2021	15	1
265	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	178.64	03/2019 -	02/2021	23	-

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
266	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	208.50	165.82	11/2019 -	02/2021	15	-
267	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	205.40	05/2019 -	02/2021	21	-
268	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	218.90	129.75	03/2020 -	02/2021	11	-
269	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	168.68	10/2019 -	02/2021	16	-
270	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71	-
271	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	418.09	01/2020 01/2021	03/2021	14	2
272	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	254.30	79.69	10/2020 -	03/2021	5	-
273	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	151.12	03/2018 01/2021	03/2021	36	2
274	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	03/2021	36	3
275	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	187.82	131.74	04/2018 -	03/2021	35	-
276	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35	-
277	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	14	-
278	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	120.37	08/2020 -	03/2021	7	-
279	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	172.63	09/2020 -	03/2021	6	-
280	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
281	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 218.70	218.70	103.81	11/2020 04/2020	04/2021	5	12
282	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH, RAJASTHAN	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34	-
283	BARASGAON TO RAHATEE - [N24001113]MoRTH, MAHARASHTRA	07/2016	289.11 290.00	289.11	61.53	09/2018 -	04/2021	31	-
284	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH, UTTAR PRADESH	03/2018	263.89 -	242.05	181.21	04/2020 -	04/2021	12	-
285	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAINCHAN - [N24000876]MoRTH, WEST BENGAL	01/2017	396.86 396.86	396.86	242.95	09/2019 11/2020	05/2021	20	6
286	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH, PUNJAB	03/2018	170.57 -	170.57	44.68	11/2020 -	05/2021	6	-
287	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH, KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
288	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH, MADHYA PRADESH	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	-	3
289	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH, RAJASTHAN	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37	-
290	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH, UTTAR PRADESH	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6	-
291	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH, PUNJAB	03/2018	322.48 -	322.48	261.72	07/2020 -	08/2021	13	-
292	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH, MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	-
293	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15	-
294	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28	-
295	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH, RAJASTHAN	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24	-

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
296	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	-	11/2020 -	08/2022	21	-
297	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	24.14	08/2019 -	11/2022	39	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
298	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	180.57	50.17	04/2017 -	02/2021	46	-
299	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	167.28	22.06	04/2017 -	02/2021	46	-
300	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	139.47	04/2017 03/2018	03/2021	47	36
301	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	190.47	01/2016 -	04/2021	63	-
302	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	387.00	290.94	08/2016 -	05/2021	57	-
303	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	339.55	276.01	08/2016 -	05/2021	57	-
304	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	340.00	234.97	08/2016 -	05/2021	57	-
305	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	160.06	10/2018 -	10/2021	36	-
306	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	83.20	09/2018 -	11/2021	38	-
307	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	407.30	102.90	06/2018 -	12/2021	42	-
308	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	398.06	126.86	06/2018 -	12/2021	42	-

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	315.03	80.78	09/2018 -	12/2021	39	-
310	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	240.64	95.34	09/2018 -	12/2021	39	-
311	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	60.55	09/2018 -	12/2021	39	-
312	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	-
313	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	239.30	85.02	09/2018 -	05/2022	44	-
314	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	114.91	09/2018 -	07/2022	46	-
315	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	68.70	09/2018 -	09/2022	48	-
316	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	36.80	09/2018 -	10/2022	49	-
317	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	336.49	71.11	09/2018 -	11/2022	50	-
318	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	42.55	09/2018 -	11/2022	50	-
319	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	65.01	09/2019 -	04/2023	43	-
320	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	47.39	09/2019 -	04/2023	43	-
321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	58.49	09/2019 -	04/2023	43	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	33.18	09/2019 -	06/2023	45	-
323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	72.44	09/2019 -	06/2023	45	-
324	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	18.08	09/2019 -	07/2023	46	-
325	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	59.92	09/2019 -	09/2023	48	-
326	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	50.49	09/2019 -	04/2024	55	-
National Highways Authority Of India									
327	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	473.85	10/2017 -	02/2021	40	-
328	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	394.32	07/2018 -	02/2021	31	-
329	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	105.20	03/2019 -	02/2021	23	-
330	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	8	-
331	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	394.32	07/2016 -	02/2021	55	-
332	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,540.00	03/2013 -	03/2021	96	-
333	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71	-
334	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	970.12	11/2018 07/2019	03/2021	28	20
335	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	419.77	08/2018 -	03/2021	31	-
336	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	522.80	06/2018 10/2020	03/2021	33	5

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
337	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	555.68	08/2019 -	03/2021	19	-
338	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	70.85	03/2019 -	03/2021	24	-
339	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,239.99	08/2013 -	05/2021	93	-
340	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-
341	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	492.81	09/2017 -	05/2021	44	-
342	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	361.58	05/2018 04/2019	06/2021	37	26
343	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15	-
344	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	-
345	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15	-
346	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	49.53	05/2013 -	08/2021	99	-
347	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	162.72	- 02/2021	08/2021	-	6
348	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	-
349	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	352.32	03/2020 -	09/2021	18	-
350	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15	-
351	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	302.83	07/2019 06/2021	12/2021	29	6
352	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	317.73	07/2019 06/2021	12/2021	29	6
353	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	336.58	03/2019 01/2021	12/2021	33	11
354	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	848.45	219.00	03/2020 -	12/2021	21	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	496.65	12/2019 -	12/2021	24	-
356	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54	-
357	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	127.37	- 08/2021	02/2022	-	6
358	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,858.57	08/2013 -	03/2022	103	-
359	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	312.73	03/2020 -	04/2022	25	-
360	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	296.06	05/2020 -	05/2022	24	-
361	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	453.70	08/2017 -	07/2022	59	-
362	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	561.03	09/2017 -	07/2022	58	-
363	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105	-
	Total		61,138.45 -	62,345.84	34,597.38				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
364	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	431.16	-	06/2021 -	11/2021	5	-
	<u>Department Of Telecommunication</u>								
365	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	71	-
	Total		13,765.16 -	25,095.16	16,594.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
366	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	8,446.13	12/2018 -	08/2022	44	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
367	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCCL,KARNATAKA	02/2014	26,405.14 30,695.00	26,405.14	16,349.18	02/2019 03/2021	06/2024	64	39
	<u>Central Public Works Department</u>								
368	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	238.56	157.67	05/2020 -	02/2021	9	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
369	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	102.34	04/2019 06/2021	10/2021	30	4
370	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19	-
371	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41	-
	<u>Chennai Metro Rail Ltd</u>								
372	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	3,770.00	2,932.59	03/2018 -	03/2021	36	-
	<u>Delhi Metro Rail Corporation</u>								
373	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021	66	-
374	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	511.60	12/2020 -	09/2021	9	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
375	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 09/2022	03/2023	98	6
	Total		1,05,242.03 -	1,17,446.83	85,487.19				
	<u>WATER RESOURCES</u>								
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
376	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	225.77	263.72	03/2020 -	03/2021	12	-
377	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14	-
378	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	-	08/2021 -	12/2021	4	-
	<u>Delhi Jal Board</u>								
379	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	515.07	297.33	01/2021 -	06/2021	5	-
380	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	60.47	12/2021 -	12/2022	12	-
381	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	118.82	02/2022 -	12/2022	10	-
	<u>Hindustan Steelwork Construction Limited</u>								
382	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	721.37	712.37	03/2015 -	03/2021	72	-
	<u>Kolkata Metropolitan Development Authority</u>								
383	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	272.32	210.94	04/2020 -	03/2021	11	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Polavaram Project Authority</u>								
384	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	16,995.57	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								
385	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	161.31	50.65	11/2019 -	03/2021	16	-
386	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	460.45	106.27	12/2020 -	05/2021	5	-
387	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 -	298.12	-	07/2021 -	06/2022	11	-
	Total		13,981.10 -	59,144.30	18,979.50				
	<u>DEFENCE PRODUCTION</u>								
	<u>Central Public Works Department</u>								
388	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	115.20	02/2020 -	06/2021	16	-
	Total		246.31 -	246.31	115.20				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
389	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	20	-
390	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6	-
391	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	350.69	265.91	04/2019 -	04/2021	24	-
392	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	-
393	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15	-
394	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	-
395	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52	-
396	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	387.83	180.63	05/2020 -	02/2022	21	-
397	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	149.00	03/2022 -	06/2022	3	-

Costing Rs. 150 Crore and above

(February 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
398	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD, KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	-
399	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD, PUNJAB	10/2019	348.24 -	348.24	15.20	05/2022 -	08/2022	3	-
400	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD, KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	-
401	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD, BIHAR	09/2018	375.00 375.00	375.00	48.46	09/2020 -	11/2022	26	-
402	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD, ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	-
	Total		6,229.82 -	6,276.31	1,798.74				
	<u>HOME AFFAIRS</u>								
403	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES (CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	2,000.00	874.24	10/2019 -	12/2021	26	-
	Total		1,219.21 -	2,000.00	874.24				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
404	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	03/2021	63	-
405	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2021	51	-
406	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	03/2021	51	-
	Total		527.83 -	538.27	460.04				
	<u>CULTURE DEVELOPMENT</u>								
407	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	145.60	09/2017 -	03/2021	42	-
	Total		151.33 -	151.33	145.60				
	<u>DPIIT</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								

Costing Rs. 150 Crore and above

(February 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
408	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 01/2014	07/2021	22	90
	<u>India International Convention And Expo Centre</u>								
409	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	5,178.00	2,419.54	12/2019 -	10/2021	22	-
	Total		17,352.09 -	18,990.30	11,134.61				
	Grand Total		6,63,797.98	8,88,903.48	5,01,908.61				

List of projects original without Date of Commissioning

Costing Rs.		150 Crore and above				(February 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1	<u>COAL</u> <u>Singareni Colliers Company Limited</u>								
	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75	-			2/6
2	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u>								
	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	156.64	128.08	-	03/2021	-	0/0
	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84	268.84	239.89	-	03/2021	-	0/0
4	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	358.42	-	06/2021	-	0/0
5	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	460.56	-	06/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	455.70	-	06/2021	-	0/0
	Total		2,261.40	2,261.48	1,642.65				0/0
7	<u>RAILWAYS</u> <u>East Central Railways</u>								
	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00	735.20	379.57	-	03/2021	-	0/0
	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07	3,550.00	3,528.48	-	03/2022	-	0/0
9	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39	1,483.14	1,194.00	-	03/2022	-	0/0
10	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65	2,066.78	1,529.08	-	03/2023	-	0/0
11	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91	1,625.87	767.07	-	03/2023	-	0/0
12	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56	1,858.75	385.87	-	03/2023	-	0/0
13	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	1,605.17	1,605.17	24.31	-	03/2023	-	0/0

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14	1,470.50	1,123.21	-	03/2023	-	0/0
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87	614.45	340.21	-	12/2023	-	0/0
16	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20	2,995.01	2.04	-	03/2024	-	0/0
17	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
18	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00	519.33	266.24	-	03/2025	-	0/0
<u>Eastern Railways</u>									
19	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35	502.48	422.81	-	03/2021	-	0/0
20	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80	495.10	283.97	-	03/2022	-	0/0
21	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64	272.20	239.06	-	03/2022	-	0/0
22	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93	310.70	356.54	-	03/2024	-	0/0
23	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00	1,261.34	-	-	03/2025	-	0/0
24	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	260.10	11.32	-	03/2025	-	0/0
25	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	71.43	-	03/2025	-	0/0
26	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	250.55	20.11	-	03/2025	-	0/0
27	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17	527.54	1.76	-	03/2025	-	0/0
28	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47	298.22	52.09	-	03/2025	-	0/0
29	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96	336.96	70.20	-	03/2025	-	0/0
30	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
<u>Metropolitan Rapid Transport Projects</u>									
31	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
<u>North East Frontier Railway</u>									

Costing Rs. 150 Crore and above (February 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
32	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	287.09	- -	12/2021	-	0/0
33	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.74	- -	03/2022	-	0/0
	<u>North Eastern Railway</u>								
34	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	714.34	63.70	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
35	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	791.39	572.99	- -	03/2023	-	0/0
36	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
37	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	127.91	- -	09/2023	-	0/0
38	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	359.00	111.51	- -	03/2024	-	0/0
39	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	<u>South Eastern Railway</u>								
40	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
41	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,967.00	74.87	- -	12/2023	-	0/0
42	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	558.00	-	- -	12/2023	-	0/0
43	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	296.10	.01	- -	12/2023	-	0/0
44	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	- -	12/2023	-	0/0
45	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
46	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	- -	12/2023	-	0/0
47	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	-	0/0
48	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,432.50	1,111.69	- -	03/2025	-	2/2
	<u>Southern Railway</u>								
49	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	457.08	439.49	- -	12/2021	-	0/0
50	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	559.95	319.22	- -	03/2024	-	0/0
51	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	582.83	239.11	- -	12/2025	-	0/0
	Total		22,663.56 -	41,230.62	14,729.43				2/2

Costing Rs. 150 Crore and above (February 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ROAD TRANSPORT AND HIGHWAYS</u> <u>Ministry Of Road Transport And Highways</u> <u>(State Pwds)</u>								
52	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13	178.13	139.26	-	03/2021	-	0/0
53	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	74.00	-	09/2021	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>		327.00			-			
54	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51	553.51	119.35	-	09/2021	-	2/4
55	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06	175.06	71.60	-	04/2022	-	0/4
56	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12	176.12	61.55	-	04/2022	-	0/4
	<u>National Highways Authority Of India</u>								
57	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56	392.00	353.42	-	02/2021	-	0/0
58	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09	565.09	550.75	-	02/2021	-	0/0
59	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94	1,282.94	468.69	-	03/2021	-	0/0
60	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19	1,145.31	1,304.00	-	03/2021	-	0/0
61	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96	1,261.05	299.11	-	03/2021	-	0/0
62	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08	1,005.08	-	-	03/2021	-	0/0
63	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00	621.00	591.21	-	04/2021	-	2/3
64	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11	806.11	189.70	-	04/2021	-	0/0

Costing Rs. 150 Crore and above (February 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
65	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT (APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,565.00	- -	05/2021	-	0/0
66	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	240.60	- -	05/2021	-	0/0
67	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	478.74	127.42	- -	05/2021	-	0/0
68	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	-	0/0
69	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	227.63	- -	06/2021	-	0/0
70	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	127.61	- -	06/2021	-	0/0
71	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	276.59	- -	06/2021	-	0/0
72	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	261.74	- -	06/2021	-	0/0
73	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0
74	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	102.70	- -	06/2021	-	0/0
75	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	25.40	- -	06/2021	-	0/0
76	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	86.83	- -	06/2021	-	0/0
77	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
78	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	456.80	- -	07/2021	-	0/0

Costing Rs. 150 Crore and above (February 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
79	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	887.07	- -	07/2021	-	3/4
80	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	271.89	- -	07/2021	-	1/4
81	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0
82	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,166.26	220.78	- -	07/2021	-	0/0
83	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
84	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	193.26	- -	07/2021	-	0/0
85	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	196.87	- -	07/2021	-	0/0
86	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	584.17	- -	07/2021	-	0/0
87	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	931.21	268.17	- -	07/2021	-	0/0
88	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	213.17	- -	07/2021	-	0/0
89	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	72.87	- -	07/2021	-	0/0
90	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	224.81	- -	08/2021	-	3/4
91	4-LANNING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	411.79	- -	08/2021	-	0/1
92	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
93	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1
94	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
95	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,337.98	- -	09/2021	-	0/0
96	FOUR LANING OF MADURAI-CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	303.46	- -	09/2021	-	0/0
97	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
98	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
99	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	-	0/0
100	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
101	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	231.66	- -	12/2021	-	0/3
102	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	425.85	- -	02/2022	-	1/4
103	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	213.52	- -	03/2022	-	0/1
104	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	332.04	- -	03/2022	-	0/0
	Total		46,977.73 -	47,960.59	24,035.95				14/41
	URBAN DEVELOPMENT								
	National Building Construcion Corporation Ltd								

Costing Rs. 150 Crore and above (February 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
105	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	651.85	- -	07/2022	-	0/9
	Total		2,694.00 -	2,694.00	651.85				0/9
	Grand Total		74,869.42	94,419.42	41,213.63				18/58

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 -	-
	Total		438.28 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TALABIRA II AND III OCP - [N06000189]NLC, ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	06/2015 03/2025	-
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Western Coal Fields Limited</u>				
10	SINGHORI OC MINE - [N06000130]WCL, MAHARASHTRA	06/2015	205.49 -	03/2020 -	03/2020
11	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020
12	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
13	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL, MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
14	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
	Total		13,502.75 -		
	<u>MINES</u>				

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Aluminum Company Limited (Nalco)</u>				
15	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 06/2021	12/2020
16	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		700.62 -		
	<u>STEEL</u>				
	<u>Rastriya Ispat Nigam Limited</u>				
17	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 12/2020	12/2020
	Total		2,858.00 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
18	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	01/2021
	<u>Hindustan Petroleum Corporation Limited</u>				
19	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
20	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
21	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	10/2019 11/2020	-
	Total		7,719.64 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	02/2017 06/2020	01/2021
24	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 01/2021	01/2021
25	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
26	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-
27	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
28	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
29	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
30	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
	<u>Power Grid Corporation Of India Limited</u>				
31	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 516.12	01/2019 04/2020	04/2020
32	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 04/2020	05/2020
33	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 04/2020	07/2020
34	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 06/2020	09/2020
35	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 06/2020	09/2020
36	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 902.49	10/2017 12/2020	01/2021
37	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
38	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
39	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	-
40	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
41	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-
42	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-
43	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
	Total		66,443.45 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
44	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 12/2020	-
	Total		1,554.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
45	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
46	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
47	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
48	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	03/2018 -	09/2019
49	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	05/2017 -	01/2020
50	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	- -	12/2020
51	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
	Total		1,910.90 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
52	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 199.12	03/2019 03/2020	03/2020
	<u>Container Corporation Of India</u>				
53	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 12/2020	12/2020
54	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	-
55	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
56	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
57	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
58	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
59	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
60	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
61	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 -	03/2020 -	-
62	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
63	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR	04/2008	633.87 -	- -	-
64	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
65	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR, BIHAR	04/2008	445.25 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
66	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
67	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
68	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
69	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
70	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
71	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
72	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
73	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
74	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-
	<u>Eastern Railways</u>				
75	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				
76	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
77	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
78	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
79	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
80	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
81	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
	<u>North East Frontier Railway</u>				
82	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
83	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
84	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-
85	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-
86	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
88	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
89	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
90	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
91	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
92	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
93	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
94	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
95	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
96	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	10/2018 -	-
97	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
98	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
99	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
100	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
101	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES, MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
102	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	1,185.64 -	12/2017 -	-
103	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
	<u>Railway Electrification</u>				
104	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
105	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
106	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
107	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	761.37 -	- -	-
108	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH	04/2013	829.00 -	- -	-
109	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
110	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	08/2020
111	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR, CHHATISGARH	04/2008	872.00 -	12/2019 -	10/2020
	<u>South Eastern Railway</u>				
112	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
113	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
114	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>South Western Railway</u>				
115	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 -	03/2017 -	-
	<u>Southern Railway</u>				
116	OMALUR-METTURDAM- DOUBLING WITH ELCTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU	10/2013	187.26 -	04/2014 03/2021	12/2020
117	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	1,566.00 -	- -	-
118	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	227.40 -	- -	-
119	ATTIPPATTU PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	151.84 -	02/2019 -	-
120	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-
121	KUMBALAM-TURAVUR - [N22000191]SR, KERALA	04/2011	252.96 -	- -	-
122	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 -	- -	-
123	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	- -	-
124	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR, KERALA	02/2015	1,431.90 -	- -	-
125	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR, KERALA	02/2015	1,000.00 -	- -	-
126	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR, KERALA	02/2012	550.00 -	03/2016 -	-
127	ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR, TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
128	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
129	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
130	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
131	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
132	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
133	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		76,394.79 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
134	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
135	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 -	08/2020
136	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 -	09/2020
137	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 -	12/2020
138	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	01/2018 -	12/2020
139	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 -	02/2017 06/2021	02/2019
140	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
141	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 07/2021	05/2019
142	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
143	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 05/2021	08/2019

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
144	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933])MoRTH,ANDHRA PRADESH	02/2017	429.43 -	11/2017 04/2021	11/2019
145	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020
146	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205])MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	06/2020
147	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963])MoRTH,ANDHRA PRADESH	01/2018	418.03 -	08/2018 05/2021	08/2020
148	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
149	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020
150	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
151	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
152	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020
153	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020
154	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020
155	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	12/2020
156	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2020	12/2020
157	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020
158	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020
159	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020
160	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 04/2021	01/2021
161	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021
162	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
163	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
164	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
165	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
166	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
167	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
168	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
169	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
170	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
171	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
172	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
173	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
174	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
175	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
176	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
177	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
178	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
179	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
180	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
181	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
182	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
183	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
184	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
185	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
186	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
187	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
188	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 12/2020	-
189	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 12/2020	-
190	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 12/2020	-
191	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
192	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
193	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
194	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
195	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
196	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
197	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
198	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
199	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
200	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
201	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
202	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
203	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
205	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
206	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
207	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
208	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 390.73	05/2017 -	-
209	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
210	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
214	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
215	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
216	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
217	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
218	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
219	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
220	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
221	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
222	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
223	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
224	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
225	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
226	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
229	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
230	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
233	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
234	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
235	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
236	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
237	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-
238	4-LANING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
239	4-LANING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
240	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH, BIHAR	08/2016	1,742.01 -	12/2016 -	-
241	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH, ODISHA	03/2014	191.50 192.00	05/2016 -	-
242	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH, ODISHA	01/2015	326.63 327.00	04/2018 -	-
243	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH, ODISHA	02/2015	239.91 240.00	10/2017 -	-
244	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH, ODISHA	07/2014	342.05 342.00	01/2017 -	-
245	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH, ODISHA	08/2013	171.96 172.00	06/2016 -	-
246	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH, ODISHA	06/2016	157.30 157.00	06/2018 -	-
247	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH, UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
248	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH, UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
249	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH, UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
250	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH, UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
251	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH, UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
252	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH, UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
253	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH, UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
254	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH, UTTARAKHAND	02/2018	418.88 -	02/2020 -	-
255	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH, UTTARAKHAND	02/2018	293.68 -	- -	-
256	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH, UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
257	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH, UTTARAKHAND	03/2018	460.73 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
259	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
260	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH, WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
261	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-
262	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
263	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-
264	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
265	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
266	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
267	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
268	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
269	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
270	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
271	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
272	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
273	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
274	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
275	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
276	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
277	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
278	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-
279	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	-
280	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
281	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
282	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-
283	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
284	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
285	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
286	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
287	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
288	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
289	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
290	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
291	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
292	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
293	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
294	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
295	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
296	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
297	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
298	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
299	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
300	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
301	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-
302	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
303	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
304	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
305	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
306	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
307	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
308	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
309	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
310	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
311	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
312	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
313	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
314	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
315	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
316	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
317	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
318	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
319	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
320	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
321	AMD I TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
322	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
323	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
324	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
325	INDAPPAUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
326	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
327	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
328	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
329	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
330	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
331	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
332	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
333	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
334	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
335	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
336	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
337	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
338	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
339	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
340	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
341	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
342	SALAIKHURD TO TIJORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
343	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
344	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
345	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
346	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
347	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
348	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
349	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
350	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
351	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
352	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
353	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
354	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
355	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
356	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
357	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
358	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
359	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
360	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
361	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
362	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
363	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
364	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
365	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
366	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
367	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
368	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
369	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
370	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
371	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
372	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
373	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
374	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
375	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
376	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
377	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
378	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
379	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
380	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
381	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
382	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
383	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
384	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
385	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
386	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
387	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
388	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
389	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
390	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
391	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
392	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
393	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
394	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
395	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
396	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
397	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
398	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
399	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
400	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
401	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
402	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
403	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
404	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
405	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
406	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
407	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
408	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
409	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
410	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
411	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
412	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
413	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
414	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
415	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
416	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
417	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
418	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-
419	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
420	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
421	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
422	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
423	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
424	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
425	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
426	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
427	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
428	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
429	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
430	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
431	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
432	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
433	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
434	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
435	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-
436	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-
437	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	-
438	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
439	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
440	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
441	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
442	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-
443	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
444	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
445	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
446	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
447	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
448	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
449	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
450	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
451	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
452	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
453	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
454	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
455	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
456	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
457	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
458	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
459	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
460	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-
461	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2020	-
462	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
463	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
464	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
465	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-
466	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
467	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-
468	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
469	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-
470	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-
471	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
472	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-
473	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
474	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
475	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
476	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
477	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
478	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
479	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
480	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAGE - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
481	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
482	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
483	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
484	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
485	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2020
486	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	12/2020
487	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
488	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
489	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
490	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
491	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
492	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
493	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
494	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
495	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
496	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
497	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
498	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
499	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-
500	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
501	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
502	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
503	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
504	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
505	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
506	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
507	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
508	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
509	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
510	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
511	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
512	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
513	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
514	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
515	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
516	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
517	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
518	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
519	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
520	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
521	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
522	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
523	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
524	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
525	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
526	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
527	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
528	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
529	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
530	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
531	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
532	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
533	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
534	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
535	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
<u>National Highways Authority Of India</u>					
536	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	01/2020
537	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	02/2019
538	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	08/2020
539	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	08/2020
540	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	09/2020
541	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020
542	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	11/2020
543	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2020
544	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	11/2020
545	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	11/2020
546	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2020
547	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	12/2020
548	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	12/2020
549	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
550	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
551	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
552	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
553	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
554	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
555	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
556	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 1,115.95	03/2019 10/2019	10/2019
557	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020
558	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
559	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
560	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
561	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
562	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020
563	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
564	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
565	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020
566	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENMORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
567	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
568	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020
569	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
570	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
571	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020
572	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020
573	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2020

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
574	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020
575	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020
576	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
577	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020
578	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020
579	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
580	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
581	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021
582	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	01/2021
583	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN	09/2016	1,239.82 -	- -	01/2021
584	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI, MADHYA PRADESH	09/2017	990.61 -	09/2017 -	01/2021
585	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
586	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- -	01/2021
587	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	02/2009 -	-
588	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	04/2009 -	-
589	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	11/2008 -	-
590	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	11/2008 -	-
591	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	-
592	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	-
593	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	-
594	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
595	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
596	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	11/2011 -	-
597	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
598	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
599	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
600	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
601	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
602	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
603	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
604	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
605	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
606	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
607	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
608	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
609	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
610	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
611	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
612	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
613	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
614	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
615	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
616	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
617	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
618	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
619	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
620	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
621	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
622	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
623	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
624	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
625	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
626	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
627	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
628	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
629	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	-
630	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
631	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
632	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
633	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
634	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
635	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
636	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
637	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
638	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-
639	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
640	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
641	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
642	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
643	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
644	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
645	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
646	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
647	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
648	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
649	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
650	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
651	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
652	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
653	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-
654	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
655	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
656	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
657	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
658	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-
659	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	-
660	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
661	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
662	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
663	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
664	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
665	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
666	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
667	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
668	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
669	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
670	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
671	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
672	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
673	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
674	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
675	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
676	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
677	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
678	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
679	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
680	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
681	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
682	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
683	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
684	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
685	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
686	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
687	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
688	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
689	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 486.00	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
690	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
691	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
692	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
693	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
694	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
695	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-
696	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
697	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
698	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-
699	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-
700	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
701	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
702	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
703	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
704	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
705	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
706	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
707	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
708	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
709	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
710	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
711	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
712	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
713	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
714	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
715	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
716	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
717	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
718	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
719	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
720	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
721	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
722	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
723	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
724	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
725	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
726	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
727	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
728	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
729	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
730	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI, ANDHRA PRADESH	12/2017	357.00 -	- -	-
731	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	-
732	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	-
733	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	- -	-
734	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	- -	-
735	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND	01/2018	273.46 -	- -	-
736	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND	01/2018	1,155.16 -	- -	-
737	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI, MADHYA PRADESH	01/2018	960.24 -	- -	-
738	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA	01/2018	633.68 -	- -	-
739	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 -	- -	-
740	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-
741	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-
742	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA	02/2018	1,424.77 -	- -	-
743	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH	02/2018	670.50 -	- -	-
744	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI, KARNATAKA	02/2018	2,177.80 -	- -	-
745	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI, UTTAR PRADESH	03/2018	809.07 -	- -	-
746	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI, UTTAR PRADESH	03/2018	925.40 -	- -	-
747	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
748	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN	02/2018	716.76 -	- -	-
749	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
750	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
751	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
752	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
753	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
754	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
755	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
756	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
757	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
758	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
759	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
760	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
761	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
762	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
763	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
764	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
765	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
766	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
767	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
768	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
769	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
770	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
771	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
772	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
773	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
774	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
775	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
776	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
777	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- 02/2020	-
778	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
779	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
780	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
781	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-
782	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-
783	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-
784	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
785	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-
786	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
787	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
788	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
	Total		3,82,637.63 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Central Public Works Department</u>				
789	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	03/2018 -	-
	Total		248.20 -		
	<u>URBAN DEVELOPMENT</u>				
790	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 02/2021	11/2020
791	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
792	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
793	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	11/2020 -	-
794	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE-VI-5), SHOPS,CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	09/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
795	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
796	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
797	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
798	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
799	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-
	<u>National Building Construcion Corporation Ltd</u>				

Costing Rs. 150 Crore and above				(February 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
800	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	11/2019 -	-
	Total		41,949.94 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
801	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
802	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
803	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-
	<u>Delhi Jal Board</u>				
804	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Uttar Pradesh Jal Nigam</u>				
805	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 -	12/2019 -	01/2021
	<u>Uttarakhand Pey Jal Nigam</u>				
806	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
	Total		1,654.42 -		
	<u>COMMERCE</u>				
	<u>National Building Construcion Corporation Ltd</u>				
807	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
808	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
809	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
810	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
811	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
812	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-

Costing Rs. 150 Crore and above					(February 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Edcil(India) Limited</u>				
813	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
814	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	<u>Rail India Technical And Economic Service</u>				
815	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		2,641.45 -		
	Grand Total		6,00,956.71		

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	03/2023	38.63	75
	Total		27,271.00 -	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	441.33	09/2018 -	06/2021	5.78	33
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	09/2021 -	09/2021	38.72	0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	03/2021 -	03/2022	7.88	12
	Total		1,905.50 -	2,153.66				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
7	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	08/2019 -	-	93.35	0
	<u>Neyveli Lignite Corporation</u>							
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	07/2022	.00	8
	<u>Singareni Colliers Company Limited</u>							
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2022	114.60	84
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2022	11.42	36
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2022	5.85	84

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>Western Coal Fields Limited</u>							
13	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	03/2022 -	03/2025	.00	36
14	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
15	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98	0
16	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	07/2016	281.25 -	409.87	03/2022 -	03/2022	45.73	0
	Total		22,371.99 -	25,581.10				
	<u>DPIIT</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>							
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	10/2021	8.49	22
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	09/2025 -	09/2025	15.92	0
	<u>Hospital Services Consultancy Corporation Ltd</u>							
20	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.64	- -	03/2021	.05	0
21	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	04/2021	16.33	38
22	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20	26
23	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64	8
24	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	12/2020	.02	0
25	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29	46
26	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13	24
27	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
28	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	11/2013 -	03/2021	20.55	88
29	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR [N21000011	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71	18
	<u>National Building Construcion Corporation Ltd</u>							
30	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	09/2021 -	09/2021	8.88	0
	Total		5,589.39 -	6,253.60				
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	10/2019 -	12/2021	64.04	26
	Total		1,219.21 -	2,000.00				
	<u>HUMAN RESOURCE DEVELOPMENT</u>							
32	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	02/2019	186.00 199.00	205.00	09/2020 -	03/2021	10.22	6
33	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102	08/2016	294.00 -	350.69	04/2019 -	04/2021	19.28	24
34	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	10/2021	.57	52
35	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	559.47	07/2019 -	03/2021	1.85	20
	<u>Rail India Technical And Economic Service</u>							
36	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	09/2014 -	-	29.31	0
	Total		2,009.81 -	2,240.41				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
37	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	03/2021	14.33	31
	<u>Indian Oil Corporation Limited</u>							
38	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 -	502.00	08/2019 -	06/2021	18.68	22

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	03/2021 -	08/2021	66.09	5
40	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	06/2021	43.82	6
41	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2022	33.98	38
	<u>Oil India Limited</u>							
42	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	03/2017 -	03/2021	39.05	48
43	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	02/2020 -	04/2021	19.89	14
	Total		14,548.76 -	19,281.20				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							
44	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95	0
45	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41	0
46	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	10,016.10	07/2019 -	03/2021	9.00	20
47	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	-	12.95	0
48	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	01/2021	24.87	47
49	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	-	7.55	0
50	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	06/2019 -	10/2022	7.12	40
	<u>Power Grid Corporation Of India Limited</u>							
51	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	-	27.92	0
52	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	-	31.17	0
53	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	07/2020 -	04/2021	14.11	9
54	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	12/2018 -	12/2021	92.02	36
	<u>Thdc India Limited</u>							
55	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	06/2013 -	12/2023	54.94	126

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		72,224.69	85,706.71				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
56	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	184.06	315.00	03/2019	03/2020	71.14	12
57	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356	02/2015	1,272.19	1,283.49	03/2022	03/2023	.89	12
58	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	792.89	1,377.48	03/2021	03/2023	73.73	24
59	DAUND - MANMAD (236 KM) - [N22000360	02/2016	1,876.00	2,081.27	03/2023	03/2023	10.94	0
60	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	02/2016	2,750.00	3,438.51	03/2024	03/2024	25.04	0
61	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	02/2015	3,627.47	3,627.47	03/2024	03/2023	.00	-12
62	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181	02/1997	2,271.50	4,517.49	03/2021	03/2023	98.88	24
63	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00	5,341.68	03/2024	03/2024	120.28	0
	<u>Container Corporation Of India</u>							
64	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50	235.00	03/2019	-	.21	0
65	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	01/2013	387.70	487.13	03/2018	03/2021	25.65	36
	<u>East Central Railways</u>							
66	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01	480.00	-	-	125.34	0
67	KOSI BRIDGE (NL), ECR - [220100304	04/2002	499.41	516.02	03/2020	-	3.33	0
68	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00	519.33	-	03/2025	36.67	0
69	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15	546.71	07/2014	-	64.60	0
70	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67	549.75	-	-	32.26	0
71	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87	614.45	-	12/2023	277.26	0
72	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR [N22000475	04/1998	180.82	726.31	-	-	301.68	0
73	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00	735.20	-	03/2021	126.22	0
74	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88	751.55	03/2012	07/2021	57.27	112

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
75	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	03/2020 -	03/2023	49.45	36
76	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	03/2019 -	05/2021	37.04	26
77	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	- -	-	376.78	0
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,070.00	03/2012 -	11/2022	229.50	128
79	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	03/2021 -	06/2022	62.06	15
80	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	03/2021 -	03/2024	63.37	36
81	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14 -	1,470.50	- -	03/2023	295.15	0
82	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	- -	03/2022	350.27	0
83	KODERMA-TILAIYA (NL), ECR - [220100305	04/2002	459.91 -	1,625.87	- -	03/2023	253.52	0
84	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	- -	03/2023	391.01	0
85	HAJIPUR-SUGAU LI VIA VAISHALI (NL), ECR - [220100303	04/2003	528.65 -	2,066.78	- -	03/2023	290.95	0
86	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	- -	03/2024	818.15	0
87	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	03/1999	1,033.07 -	3,550.00	- -	03/2022	243.64	0
	<u>Eastern Railways</u>							
88	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	- -	03/2025	51.19	0
89	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	03/2022	6.48	0
90	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 -	298.22	- -	03/2025	.25	0
91	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	- -	03/2024	23.82	0
92	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
93	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	03/2017 -	03/2025	20.30	96
94	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
95	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	- -	03/2022	181.63	0

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
96	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	- -	03/2021	74.26	0
97	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46	0
98	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
99	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	565.00	- -	05/2019	116.16	0
100	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	03/2020 -	03/2021	22.31	12
101	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
102	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
103	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
104	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30	0
105	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
106	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
107	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
<u>Indian Railway Construction Company Limited</u>								
108	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	09/2018 -	03/2022	.00	42
109	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2023	117.23	21
<u>Metropolitan Rapid Transport Projects</u>								
110	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	12/2021	48.06	102
111	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2022	501.57	216
112	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37	0
113	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91	63
<u>North Central Railway</u>								
114	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	-	188.33	0

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
115	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	-	1.69	0
116	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
117	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	-	7.86	0
118	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	- -	12/2021	54.80	0
119	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62	0
120	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
121	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	-	106.51	0
122	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	03/2020 -	03/2022	30.26	24
123	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	760.00	12/2021 -	04/2021	26.19	-8
124	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	800.00	03/2019 -	03/2021	154.78	24
125	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	1,040.00	03/2020 -	-	150.70	0
126	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	04/2010 -	-	186.55	0
127	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,105.00	03/2019 -	03/2023	186.86	48
128	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39	0
129	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	03/2021 -	05/2021	115.07	2
130	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2024	302.54	60
131	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15	12
132	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	4,083.02	03/2021 -	03/2021	350.44	0
133	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	12/2008 -	04/2021	284.80	148
134	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	03/2014 -	03/2023	130.69	108
135	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,911.00	03/2015 -	12/2024	197.05	117

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
136	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	12/2015 -	12/2023	542.04	96
137	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	03/2011 -	12/2023	175.34	153
	<u>North Eastern Railway</u>							
138	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10	0
139	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	12/2021	.16	68
140	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34	0
141	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	02/2022	61.80	37
142	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP [N22000136]	03/2013	643.00 -	644.00	- -	-	.16	0
143	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	12/2023	18.56	0
144	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13	0
145	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99	0
146	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91	0
	<u>North Western Railway</u>							
147	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	10/2018 -	-	47.91	0
148	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	11/2019 -	03/2021	75.73	16
149	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	12/2019 -	02/2021	60.52	14
150	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81	0
151	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	02/2019 -	02/2020	116.86	12
152	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	03/2020 -	04/2022	16.97	25
153	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	11/2021	109.82	33
154	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	- -	-	33.70	0
155	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64	0
156	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	- -	-	104.65	0
	<u>Northern Railway</u>							
157	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68	0

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
158	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
159	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
160	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	- -	03/2024	310.24	0
161	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	03/2016 -	06/2021	37.44	63
162	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	06/2021	211.31	114
163	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	- -	03/2023	2.93	0
164	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	07/2012 -	03/2024	388.89	140
	<u>Rail Vikas Nigam Ltd.</u>							
165	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	03/2009 03/2009	-	196.83	0
166	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
167	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	03/2021	35.42	0
168	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15	69
169	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98	33
170	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2022	51.02	39
171	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	12/2021 -	12/2021	53.75	0
172	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	03/2019 -	06/2022	62.89	39
173	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413]	03/2012	1,183.25 -	1,825.00	12/2020 -	12/2022	54.24	24
174	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	12/2020 -	12/2021	23.55	12
175	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	-	55.57	0
176	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68	3
177	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	03/2020 -	12/2021	111.91	21
178	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
179	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	03/2020 -	12/2021	281.93	21

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
181	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04	-3
182	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
183	VIJAYAWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58	24
184	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
185	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22	108
187	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62	-12
188	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08	3
	<u>Railway Electrification</u>							
189	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77	0
	<u>South Central Railway</u>							
190	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	03/2022 -	12/2022	275.34	9
191	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	03/2020 -	06/2021	31.75	15
192	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84	0
193	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
194	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2024	102.85	180
195	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	03/2021 -	03/2024	15.49	36
196	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86	0
197	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	03/2014 -	03/2027	42.44	156
198	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
199	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>							

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
200	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
201	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	12/2019 -	-	40.65	10
202	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	02/2019 -	12/2021	116.46	34
203	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	12/2021 -	12/2023	.07	24
204	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	- -	-	268.37	0
205	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	04/2020 -	04/2021	291.76	12
206	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	03/2021 -	12/2023	8.23	33
207	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	03/2023 -	12/2023	84.69	9
<u>South Eastern Railway</u>								
208	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44	0
209	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323]	04/2012	148.77 -	377.00	12/2016 -	08/2020	153.41	44
210	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89	0
211	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
212	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76	0
213	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	03/2021 -	12/2023	15.60	33
214	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
<u>South Western Railway</u>								
215	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14	0
216	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	296.10	- -	12/2023	.03	0
217	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	03/2020 -	03/2021	35.47	12
218	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	998.00	03/2017 -	-	54.78	0
219	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	03/2020 -	06/2021	33.31	15
220	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	03/2020 -	11/2021	43.14	20
221	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84	24

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
222	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	- -	12/2023	9.22	0
223	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	- -	03/2025	17.95	0
224	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	- -	12/2024	68.97	0
	<u>Southern Railway</u>							
225	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	- -	-	45.43	0
226	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	332.00	04/2014 -	12/2020	77.29	80
227	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	- -	-	46.09	0
228	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	12/2021	69.20	0
229	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	02/2019 -	-	247.32	0
230	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	- -	03/2024	181.84	0
231	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	600.30	- -	09/2021	265.12	0
232	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	09/2021	253.33	198
233	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,121.00	- -	04/2021	20.28	0
234	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05	0
235	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	- -	03/2024	130.17	0
236	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,246.00	- -	-	24.60	0
237	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78	0
238	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	03/2020 -	06/2022	102.11	27
239	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	03/2020 -	03/2025	465.83	60
240	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	03/2019 -	12/2027	1,699.64	105
241	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80	0
242	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,910.84	02/2019 -	03/2025	301.67	73
	<u>West Central Railway</u>							

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
243	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
244	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>							
245	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	03/2011 -	-	72.42	0
	Total		1,85,293.15 -	3,45,310.63				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
246	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00	157.30	06/2018 -	-	.00	0
247	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	-	.00	0
248	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	-	.00	0
249	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	-	.00	0
250	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	-	.00	0
251	REHABILITATION AND UPGRADE OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	-	.00	0
252	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	-	.00	0
253	MANGRUPHIR TO MAHAN - [N24001087	03/2018	222.13 222.00	222.13	11/2019 -	-	.00	0
254	KUNDRAI TO WAZAR - [N24001077	01/2018	225.25 225.00	225.25	12/2019 -	-	.00	0
255	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	-	.00	0
256	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	-	.08	0
257	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	-	.00	0
258	REHABILITATION AND UPGRADE OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	03/2021	.00	14
259	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00	244.04	03/2019 -	-	.00	0
260	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	- -	-	58.68	0

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
261	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00	257.38	12/2019 -	-	.00	0
262	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00	264.41	03/2019 -	-	.00	0
263	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84	0
264	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00	272.04	12/2019 -	-	.00	0
265	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	- -	-	3.72	0
266	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	03/2018	297.12 294.00	294.12	07/2018 -	-	-1.01	0
267	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	07/2019 -	-	.31	0
268	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00	301.38	08/2020 -	-	.00	0
269	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00	303.24	12/2019 -	-	.00	0
270	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	08/2016 -	-	14.02	0
271	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	322.24	09/2014 -	-	72.36	0
272	MEHKAR TO CHIKALI - [N24001011]	02/2017	322.48 322.00	322.48	05/2019 -	-	.00	0
273	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	10/2010 -	06/2021	69.30	128
274	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00	336.21	12/2019 -	-	.00	0
275	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00	336.47	12/2019 -	-	.00	0
276	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00	341.16	06/2019 -	-	.00	0
277	OSMANNAGAR TO KUNDRAI - [N24001075]	09/2017	344.25 344.00	344.25	08/2020 -	-	.00	0
278	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00	344.85	12/2019 -	-	.00	0
279	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	0
280	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 -	353.89	11/2015 -	-	6.21	0
281	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]	10/2015	333.21 -	355.89	12/2015 -	-	6.81	0

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
282	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67	0
283	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	-	.00	0
284	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42	0
285	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2021	93.80	128
286	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00	381.08	05/2020 -	-	.00	0
287	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	05/2012 -	-	88.11	0
288	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	-	.00	0
289	CHIKLI TO TAKARKHED - [N24001083	03/2018	393.10 393.00	393.10	12/2019 -	-	.00	0
290	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00	404.33	05/2020 -	-	.00	0
291	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	-	.00	0
292	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00	0
293	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	06/2020 -	-	.00	0
294	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06	0
295	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	01/2021	.00	26
296	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	09/2016 -	06/2021	14.24	57
297	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	-	.00	0
298	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06	0
299	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	-	46.51	0
300	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	03/2017 -	-	46.51	0
301	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00	743.21	06/2021 -	06/2021	.00	0

Costing Rs. 150 Crore and above							(February 2021)	
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Antici Pated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
302	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	04/2021	77.26	47
303	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	12/2020	1.75	0
304	PARSHURAM GHAT TO ARAWALI - [N24001133	04/2016	983.14 983.00	983.14	12/2019 -	-	.00	0
305	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2020	58.98	117
306	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	04/2021	.00	59
307	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401	11/2011	954.43 -	1,191.51	09/2015 -	10/2021	24.84	73
308	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00	0
309	KALMATH TO ZARAP - [N24001137	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	-	.00	0
310	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	-	.00	0
311	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	- -	-	2.93	0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
312	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	04/2017 -	-	29.48	0
313	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	04/2017 -	-	29.48	0
314	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	08/2016 -	05/2021	3.73	57
315	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30	0
316	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902	10/2017	818.00 -	887.68	- -	-	8.52	0
	<u>National Highways Authority Of India</u>							
317	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99	133
318	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	12/2020	10.58	152
319	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	-	64.62	0
320	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	- -	-	.99	0

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
321	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	- -	-	8.35	0
322	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501	08/2015	322.09 -	322.09	04/2018 -	12/2020	.00	32
323	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 -	336.60	08/2018 -	-	3.98	0
324	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	04/2009 -	-	70.23	0
325	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82	111
326	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437	10/2015	361.15 -	363.93	- -	-	.77	0
327	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56 -	392.00	- -	02/2021	7.53	0
328	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	11/2008 -	-	159.95	0
329	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	- -	10/2020	10.68	0
330	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
331	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	520.00	02/2009 -	-	85.71	0
332	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	- -	-	8.26	0
333	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	11/2013 -	01/2021	15.53	86
334	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	08/2015	516.13 -	649.27	04/2018 -	-	25.80	0
335	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	07/2009 -	-	234.27	0
336	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	- -	-	6.11	0
337	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	690.17	05/2018 -	06/2021	16.34	37
338	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469	03/2015	794.30 -	691.38	- -	05/2020	-12.96	0
339	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	07/2018 -	-	19.25	0
340	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	730.97	05/2018 -	06/2021	37.63	37
341	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	-	9.38	0

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
342	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]	10/2019	743.88 -	743.89	- -	12/2021	.00	0
343	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	12/2017 -	-	66.88	0
344	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	09/2021	.23	18
345	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 -	799.30	- -	07/2021	.48	0
346	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	03/2018	642.13 -	807.00	- -	-	25.68	0
347	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	- -	10/2021	1.37	0
348	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]	12/2017	656.98 -	840.00	- -	-	27.86	0
349	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]	12/2017	217.96 -	884.00	- -	-	305.58	0
350	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	04/2020 -	07/2021	3.95	15
351	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	931.21	- -	07/2021	46.72	0
352	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	- -	01/2020	11.33	0
353	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	-	31.88	0
354	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 -	987.94	- -	-	44.60	0
355	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	- -	-	21.50	0
356	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	-	5.56	0
357	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	-	3.40	0
358	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,071.00	- -	07/2021	5.32	0
359	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
360	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	08/2019 -	-	16.55	0
361	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 -	1,145.31	- -	03/2021	4.10	0
362	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	-	5.70	0
363	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	-	41.54	0
364	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507	12/2015	1,167.45 -	1,182.94	- -	-	1.33	0
365	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	-	13.97	0
366	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	- -	-	29.35	0
367	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	05/2021	9.67	44
368	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44	0
369	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12	0
370	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	0
371	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
372	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	06/2021	10.24	15
373	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
374	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	- -	01/2021	37.71	0
375	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
376	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
377	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	09/2016	1,239.82 -	1,727.66	- -	01/2021	39.35	0

Costing Rs. 150 Crore and above					(February 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
378	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,827.15	06/2018 -	-	68.71	0
379	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09	0
380	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	- -	07/2021	54.69	0
381	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	06/2020 -	02/2021	1.78	8
382	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	-	4.99	0
383	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 -	2,280.00	- -	-	94.94	0
384	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 -	2,360.65	- -	-	41.78	0
385	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28	0
386	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	-	18.50	0
387	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50	0
388	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05	1
389	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
390	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	09/2019 -	-	86.37	0
391	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	03/2021	52.73	71
392	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	11/2011 -	-	167.82	0
393	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84	0
394	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		1,03,345.32 -	1,27,447.37				
	TELECOMMUNICATIONS							
	Bharat Sanchar Nigam Limited							

Costing Rs. 150 Crore and above

(February 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
395	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00	431.16	06/2021 -	11/2021	.00	5
	<u>Department Of Telecommunication</u>							
396	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2021	84.97	71
	Total		13,765.16 -	25,095.16				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
397	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	12/2018 -	08/2022	18.69	44
	<u>Chennai Metro Rail Ltd</u>							
398	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53	0
	<u>Mumbai Metro Rail Corporation Ltd</u>							
399	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	33,406.00	01/2015 -	03/2023	44.39	98
	<u>National Building Construcion Corporation Ltd</u>							
400	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,720.73	11/2019 -	-	10.71	0
	Total		52,773.00 -	69,971.73				
	<u>WATER RESOURCES</u>							
	<u>Uttar Pradesh Jal Nigam</u>							
401	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 -	234.03	12/2021 -	12/2021	.97	0
	Total		231.79 -	234.03				
	Grand Total		5,19,900.86	7,70,764.90				

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost
Annexure - XIII

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 5,677.00	6,840.00	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 - 12,320.00	17,079.00	12/2016 -	03/2023	38.63
	Total		27,271.00 .00 29,456.00	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 - 417.23	441.33	09/2018 -	06/2021	5.78
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	09/2021	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2022	7.88
	Total		1,905.50 .00 1,905.50	2,153.66			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
7	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	-	93.35
	<u>Neyveli Lignite Corporation</u>						
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	07/2022	.00
	<u>Singareni Colliers Company Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2022	11.42
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 - 447.06	473.22	03/2015 -	03/2022	5.85
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2022	114.60
	<u>Western Coal Fields Limited</u>						
13	BHANEGAON OC - [N06000121]	02/2015	187.94 - 187.94	409.68	03/2023 -	03/2023	117.98
14	ADASA UG TO OC - [N06000133]	08/2015	288.90 - 288.90	333.43	03/2023 -	03/2024	15.41
15	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	07/2016	281.25 - 281.25	409.87	03/2022 -	03/2022	45.73
16	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 - 289.29	289.30	03/2022 -	03/2025	.00
	Total		22,371.99 .00 22,371.99	25,581.10			
	<u>DPIIT</u>						
	<u>Delhi Mumbai Industrial Corridor</u>						
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>						
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	10/2021	8.49
	Total		17,352.09 .00 17,352.09	18,990.30			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 - 1,577.00	1,828.00	09/2025 -	09/2025	15.92

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Hospital Services Consultancy Corporation Ltd</u>						
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 - 414.11	499.23	11/2013 -	03/2021	20.55
21	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 - 204.44	250.00	05/2017 -	03/2021	22.29
22	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
23	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 - 168.90	191.20	05/2017 -	07/2019	13.20
24	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 - 505.58	585.00	03/2018 -	09/2019	15.71
25	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 - 152.95	177.92	02/2018 -	04/2021	16.33
26	CNCI KOLKATA WEST BENGAL - [N21000015	08/2016	244.00 - 244.00	248.00	09/2018 -	05/2019	1.64
27	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 - 272.19	272.54	03/2019 -	03/2021	.13
28	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 - 156.56	156.64	- -	03/2021	.05
29	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022	01/2018	249.01 - 249.01	249.07	- -	12/2020	.02
	<u>National Building Construcion Corporation Ltd</u>						
30	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 - 1,351.00	1,471.00	09/2021 -	09/2021	8.88
	Total		5,589.39 .00 5,589.39	6,253.60			
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	12/2021	64.04
	Total		1,219.21 .00 1,219.21	2,000.00			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
32	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00 496.00	498.99	06/2017 -	10/2021	.60
33	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 - 294.00	350.69	04/2019 -	04/2021	19.28
34	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 - 549.31	559.47	07/2019 -	03/2021	1.85
35	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00 199.00	205.00	09/2020 -	03/2021	3.02
	<u>Rail India Technical And Economic Service</u>						
36	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 - 484.32	626.26	09/2014 -	-	29.31
	Total		2,009.81 695.00 2,022.63	2,240.41			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
37	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 - 4,588.29	5,245.96	08/2018 -	03/2021	14.33
	<u>Indian Oil Corporation Limited</u>						
38	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 - 1,823.00	3,027.90	03/2021 -	08/2021	66.09
39	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 - 2,321.00	3,338.00	12/2020 -	06/2021	43.82
40	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 - 423.00	502.00	08/2019 -	06/2021	18.68
41	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 - 4,497.00	6,025.00	12/2018 -	02/2022	33.98
	<u>Oil India Limited</u>						
42	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 - 352.56	490.24	03/2017 -	03/2021	39.05
43	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 - 638.60	652.10	02/2020 -	04/2021	19.89

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		14,548.76 - 14,643.45	19,281.20			
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
44	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 - 9,188.98	10,016.10	07/2019 -	03/2021	9.00
45	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 - 14,366.58	15,389.42	06/2019 -	10/2022	7.12
46	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 - 9,750.89	12,176.28	02/2017 -	01/2021	24.87
47	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 - 11,846.00	12,739.82	10/2017 -	-	7.55
48	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
49	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 - 9,870.51	11,148.86	01/2020 -	-	12.95
50	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
51	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 - 203.28	260.03	07/2017 -	-	27.92
52	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 - 487.49	639.46	06/2014 -	-	31.17
53	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 - 4,754.42	9,129.32	12/2018 -	12/2021	92.02
54	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	04/2021	14.11
	<u>Thdc India Limited</u>						
55	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 - 2,491.58	3,860.35	06/2013 -	12/2023	54.94
	Total		72,224.69 7,738.00 72,224.73	85,706.71			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
56	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	1,377.48	03/2021 -	03/2023	73.73
57	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 - 199.12	315.00	03/2019 -	03/2020	71.14
58	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,517.49	03/2021 -	03/2023	98.88
59	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 - 2,425.00	5,341.68	03/2024 -	03/2024	120.28
60	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 - 2,750.00	3,438.51	03/2024 -	03/2024	25.04
61	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,283.49	03/2022 -	03/2023	.89
62	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
63	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
64	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 - 387.70	487.13	03/2018 -	03/2021	25.65
65	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	-	.21
	<u>East Central Railways</u>						
66	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 - 1,033.07	3,550.00	- -	03/2022	243.64
67	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 - 528.65	2,066.78	- -	03/2023	290.95
68	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95 283.95	751.55	03/2012 -	07/2021	164.68
69	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 - 324.73	1,070.00	03/2012 -	11/2022	229.50

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
70	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 - 162.87	614.45	- -	12/2023	277.26
71	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 - 499.41	516.02	03/2020 -	-	3.33
72	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 - 380.00	519.33	- -	03/2025	36.67
73	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 - 678.54	929.86	03/2019 -	05/2021	37.04
74	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 - 459.91	1,625.87	- -	03/2023	253.52
75	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 - 415.67	549.75	- -	-	32.26
76	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 - 326.20	2,995.01	- -	03/2024	818.15
77	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 - 325.00	735.20	- -	03/2021	126.22
78	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 - 378.56	1,858.75	- -	03/2023	391.01
79	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 - 211.00	1,006.00	- -	-	376.78
80	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 - 372.14	1,470.50	- -	03/2023	295.15
81	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 - 548.00	819.01	03/2020 -	03/2023	49.45
82	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 - 213.01	480.00	- -	-	125.34
83	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 - 332.15	546.71	07/2014 -	-	64.60
84	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 - 744.04	1,215.54	03/2021 -	03/2024	63.37
85	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 - 731.64	1,185.73	03/2021 -	06/2022	62.06

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
86	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 - 180.82	726.31	- -	-	301.68
87	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 - 329.39	1,483.14	- -	03/2022	350.27
	<u>Eastern Railways</u>						
88	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
89	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
90	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 - 365.17	439.30	03/2017 -	03/2025	20.30
91	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46
92	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 - 542.18	663.13	03/2020 -	03/2021	22.31
93	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 - 175.80	495.10	- -	03/2022	181.63
94	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
95	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01
96	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25
97	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 - 499.96	680.68	02/2012 -	03/2025	36.15
98	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
99	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
100	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08
101	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
102	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
103	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
104	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 - 288.35	502.48	- -	03/2021	74.26
105	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 - 261.38	565.00	- -	05/2019	116.16
106	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
107	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225]	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
108	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	12/2023	117.23
109	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489]	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	03/2022	.00
<u>Metropolitan Rapid Transport Projects</u>							
110	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37
111	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 - 495.44	2,980.41	03/2004 -	03/2022	501.57
112	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	734.01	06/2013 -	12/2021	48.06
113	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	06/2021	75.91
<u>North Central Railway</u>							
114	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 - 120.00	346.00	12/2008 -	-	188.33
115	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
116	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00 668.00	680.00	03/2020 -	-	1.80

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>North East Frontier Railway</u>						
117	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 - 200.34	614.00	03/2019 -	-	106.51
118	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 5,021.45	5,521.45	03/2014 -	03/2023	130.69
119	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 - 2,531.34	4,541.38	12/2008 -	04/2021	284.80
120	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 4,454.17	12,264.15	03/2011 -	12/2023	175.34
121	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,105.00	03/2019 -	03/2023	186.86
122	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 - 2,132.03	2,145.00	03/2019 -	03/2024	302.54
123	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 - 2,326.52	6,911.00	03/2015 -	12/2024	197.05
124	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 - 333.76	360.00	- -	-	7.86
125	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 4,084.69	8,600.00	12/2015 -	12/2023	542.04
126	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 - 221.42	380.00	- -	-	71.62
127	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 569.63	742.00	03/2020 -	03/2022	30.26
128	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	4,083.02	03/2021 -	03/2021	350.44
129	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
130	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	373.87	- -	12/2021	54.80
131	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	1,040.00	03/2020 -	-	150.70
132	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 - 819.23	1,871.00	- -	-	128.39

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
133	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 - 486.96	800.00	03/2019 -	03/2021	154.78
134	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	2,950.00	03/2022 -	03/2023	32.15
135	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	1,873.21	03/2021 -	05/2021	115.07
136	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 - 602.27	760.00	12/2021 -	04/2021	26.19
137	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 - 380.60	1,090.60	04/2010 -	-	186.55
<u>North Eastern Railway</u>							
138	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 - 142.45	228.40	- -	-	60.34
139	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 - 182.92	197.73	- -	-	8.10
140	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
141	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 - 243.78	895.00	12/2021 -	12/2021	267.13
142	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	477.31	01/2019 -	02/2022	61.80
143	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
144	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	12/2021	.16
145	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,476.15	01/2018 -	-	9.91
146	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	714.34	- -	12/2023	18.56
<u>North Western Railway</u>							
147	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	11/2021	109.82

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
148	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	04/2022	16.97
149	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 - 873.71	1,980.21	- -	-	126.64
150	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 - 246.08	395.00	12/2019 -	02/2021	60.52
151	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
152	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 - 236.93	350.45	10/2018 -	-	47.91
153	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 - 822.00	1,099.00	- -	-	33.70
154	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 - 323.00	432.22	- -	-	33.81
155	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 - 213.39	375.00	11/2019 -	03/2021	75.73
156	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 - 242.09	525.00	02/2019 -	02/2020	116.86
	<u>Northern Railway</u>						
157	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	359.00	- -	03/2024	129.17
158	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	06/2021	211.31
159	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
160	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 - 219.83	346.63	- -	-	57.68
161	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 - 1,229.00	1,265.00	- -	03/2023	2.93
162	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
163	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,200.00	07/2012 -	03/2024	388.89

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
164	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 781.00	859.00	03/2016 -	06/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>						
165	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 - 1,185.64	1,844.47	12/2017 -	-	55.57
166	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
167	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	396.00	03/2009 03/2009	-	91.30
168	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,639.00	03/2016 -	03/2025	59.22
169	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	12/2025	127.62
170	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,000.00	03/2023 -	12/2022	41.04
171	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,259.48	03/2016 -	03/2025	7.78
172	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
173	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	3,377.00	03/2020 -	03/2022	124.58
174	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 - 975.62	1,500.00	12/2021 -	12/2021	53.75
175	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 - 644.38	872.65	03/2021 -	03/2021	35.42
176	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 - 1,548.66	1,868.89	12/2021 -	03/2022	20.68
177	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	950.00	03/2016 -	12/2021	50.15
178	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32
179	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,000.00	03/2022 -	12/2024	5.98

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
180	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 - 773.94	850.00	12/2024 -	12/2024	9.83
181	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,400.00	03/2019 -	06/2022	51.02
182	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	22,716.11	12/2024 -	03/2025	40.08
183	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,725.00	03/2020 -	12/2021	281.93
184	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
185	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	12/2021	111.91
186	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,536.00	03/2019 -	06/2022	62.89
187	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	1,825.00	12/2020 -	12/2022	54.24
188	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>						
189	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
190	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2024	102.85
191	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86
192	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
193	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 - 2,288.70	2,643.25	03/2021 -	03/2024	15.49
194	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 - 704.31	927.94	03/2020 -	06/2021	31.75

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
195	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288	04/2008	2,132.77 - 2,132.77	3,037.95	03/2014 -	03/2027	42.44
196	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	164.36 - 164.36	1,050.00	02/2009 -	-	538.84
197	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
198	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2024	7.06
199	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00 185.00	449.39	03/2022 -	12/2022	142.91
<u>South East Central Railway</u>							
200	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 - 383.79	1,413.76	- -	-	268.37
201	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 - 511.86	2,005.25	04/2020 -	04/2021	291.76
202	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 - 2,753.05	3,524.81	03/2023 -	12/2023	84.69
203	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438	04/2010	585.93 - 585.93	1,268.32	02/2019 -	12/2021	116.46
204	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 - 229.00	1,096.00	12/2021 -	12/2024	378.60
205	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 - 872.00	1,226.51	12/2019 -	-	40.65
206	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	04/2015	1,973.00 - 1,973.00	2,135.34	03/2021 -	12/2023	8.23
207	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 - 1,370.00	1,370.94	12/2021 -	12/2023	.07
<u>South Eastern Railway</u>							
208	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
209	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 - 148.77	377.00	12/2016 -	08/2020	153.41

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
210	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
211	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
212	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 - 149.90	230.00	03/2015 -	-	53.44
213	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 - 1,724.20	1,993.24	03/2021 -	12/2023	15.60
214	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 - 1,966.70	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
215	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 - 1,801.01	1,967.00	- -	12/2023	9.22
216	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	296.10	- -	12/2023	.03
217	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,432.50	- -	03/2025	17.95
218	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 - 146.75	167.50	- -	12/2023	14.14
219	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	3,911.65	- -	12/2024	68.97
220	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,656.00	03/2020 -	11/2021	43.14
221	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,147.00	03/2020 -	06/2021	33.31
222	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	783.00	03/2020 -	03/2021	35.47
223	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,614.59	1,870.41	03/2019 -	03/2021	15.84
224	KADUR CHIKMAGALUR SAKLLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 - 644.78	998.00	03/2017 -	-	54.78
	<u>Southern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
225	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 - 724.69	2,910.84	02/2019 -	03/2025	301.67
226	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,720.00	03/2020 -	03/2025	465.83
227	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
228	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	527.37	02/2019 -	-	247.32
229	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	1,205.00	- -	03/2024	130.17
230	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	1,500.00	- -	-	78.78
231	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 - 198.68	559.95	- -	03/2024	181.84
232	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 270.14	457.08	- -	12/2021	69.20
233	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 252.96	369.55	- -	-	46.09
234	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	1,140.00	- -	-	295.05
235	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	600.30	- -	09/2021	265.12
236	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	1,121.00	- -	04/2021	20.28
237	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 189.24	275.21	- -	-	45.43
238	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,172.16	03/2019 -	12/2027	1,699.64
239	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 - 187.26	332.00	04/2014 -	12/2020	77.29
240	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,000.00	1,246.00	- -	-	24.60

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
241	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	950.00	03/2005 -	09/2021	253.33
242	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	06/2022	102.11
	<u>West Central Railway</u>						
243	RAMGANJIMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2023	585.35
244	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
	<u>Western Railway</u>						
245	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95 196.95	202.35	03/2011 -	-	2.74
	Total		1,85,293.15 5,323.20 1,94,005.59	3,45,310.63			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
246	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00 227.00	247.95	- - -	-	9.23
247	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 - 624.41	992.67	03/2011 -	12/2020	58.98
248	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 - 193.69	327.92	10/2010 -	06/2021	69.30
249	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 - 207.03	389.45	05/2012 -	-	88.11
250	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 - 258.97	268.92	08/2015 -	-	3.84
251	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 - 280.16	290.59	- - -	-	3.72
252	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00 348.00	348.43	09/2017 - -	-	.12
253	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 [N24000371]	10/2013	445.89 - 445.89	653.29	03/2017 -	-	46.51

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
254	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 - 497.05	881.05	05/2017 -	04/2021	77.26
255	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 - 889.24	904.82	- -	12/2020	1.75
256	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 - 470.20	630.36	02/2011 -	-	34.06
257	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 - 282.41	322.01	08/2016 -	-	14.02
258	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 - 954.43	1,191.51	09/2015 -	10/2021	24.84
259	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 - 358.22	377.64	10/2016 -	-	5.42
260	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 - 333.21	353.89	11/2015 -	-	6.21
261	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 - 195.04	377.99	10/2010 -	06/2021	93.80
262	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 - 319.68	369.77	- -	-	15.67
263	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]	06/2016	157.30 157.00 157.00	157.30	06/2018 -	-	.19
264	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 - 460.73	461.00	- -	-	.06
265	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 - 237.80	238.00	11/2019 -	-	.08
266	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]	10/2015	333.21 - 333.21	355.89	12/2015 -	-	6.81
267	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	03/2018	297.12 294.00 294.00	294.12	07/2018 -	-	.04
268	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	03/2018	504.19 504.00 504.00	504.19	11/2018 -	01/2021	.04
269	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00 995.00	995.09	05/2016 -	04/2021	.01

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
270	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00 203.00	203.21	05/2019 -	-	.10
271	SHEGAON TO DEORI PHATA - [N24001010]	02/2017	373.10 373.00 373.00	373.10	05/2019 -	-	.03
272	MEHKAR TO CHIKALI - [N24001011]	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15
273	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00 548.00	548.03	06/2019 -	-	.01
274	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00 391.00	391.06	06/2019 -	-	.02
275	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
276	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	-	40.76
277	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00 257.00	257.38	12/2019 -	-	.15
278	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
279	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	-	.05
280	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	-	.08
281	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	-	.24
282	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	-	.06
283	WADIGODRI TO DHANGRIPIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	-	.12
284	DHANGRIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	-	.06
285	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	-	.08

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
286	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	-	.14
287	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	-	.01
288	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	-	.13
289	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	-	.07
290	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	-	.11
291	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	-	.01
292	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	-	.03
293	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	-	.06
294	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	-	.47
295	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	-	.08
296	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	-	.02
297	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	-	.16
298	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	-	.08
299	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	-	26.19
300	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	-	2.47
301	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
302	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	06/2021	.03
303	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01
304	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00
305	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	-	.01
306	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00 215.00	215.16	09/2019 -	-	.07
307	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	03/2021	.13
308	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00 653.00	653.29	03/2017 -	-	.04
309	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 - 186.96	322.24	09/2014 -	-	72.36
310	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 - 1,979.00	2,036.90	- -	-	2.93
311	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00 543.73	544.00	09/2016 -	06/2021	.00
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
312	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 - 195.23	252.79	04/2017 -	-	29.48
313	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 - 203.36	263.31	04/2017 -	-	29.48
314	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 - 373.07	387.00	08/2016 -	05/2021	3.73
315	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
316	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]	10/2017	818.00 - 818.00	887.68	- -	-	8.52
	<u>National Highways Authority Of India</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
317	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 - 280.00	520.00	02/2009 -	-	85.71
318	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23
319	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95
320	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
321	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 - 160.00	167.98	05/2008 -	06/2019	4.99
322	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 - 196.00	655.17	07/2009 -	-	234.27
323	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 - 1,108.00	2,967.50	11/2011 -	-	167.82
324	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
325	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 - 217.61	360.84	04/2010 -	07/2019	65.82
326	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 - 208.00	230.00	04/2008 -	12/2020	10.58
327	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
328	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
329	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
330	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 - 585.00	591.00	11/2013 -	01/2021	15.53
331	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 - 1,928.22	2,945.00	04/2015 -	03/2021	52.73
332	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 - 531.13	730.97	05/2018 -	06/2021	37.63

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
333	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 - 361.15	363.93	- -	-	.77
334	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 - 593.26	690.17	05/2018 -	06/2021	16.34
335	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
336	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 - 1,083.00	1,827.15	06/2018 -	-	68.71
337	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]	03/2015	794.30 - 679.94	691.38	- -	05/2020	-12.96
338	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	10/2021	1.37
339	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
340	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]	08/2015	322.09 - 247.00	322.09	04/2018 -	12/2020	.00
341	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 - 447.29	746.43	12/2017 -	-	66.88
342	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	-	6.11
343	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	-	1.33
344	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	-	41.78
345	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	-	21.50
346	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	-	25.80
347	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	-	44.60
348	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH- 29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
349	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	02/2021	7.53
350	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	2,587.50	09/2019 -	-	86.37
351	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 - 1,169.61	2,280.00	- -	-	94.94
352	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 - 323.72	336.60	08/2018 -	-	3.98
353	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82 - 1,239.82	1,727.66	- -	01/2021	39.35
354	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 - 950.69	1,108.00	08/2019 -	-	16.55
355	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 - 1,100.19	1,145.31	- -	03/2021	4.10
356	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 - 290.73	315.00	- -	-	8.35
357	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 - 605.84	722.46	07/2018 -	-	19.25
358	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
359	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 - 744.64	982.00	03/2020 -	-	31.88
360	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	-	3.40
361	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 - 988.34	1,043.28	03/2020 -	-	5.56
362	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	11/2020	1.06
363	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	-	5.70
364	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 - 754.54	756.27	03/2020 -	09/2021	.23

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
365	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 - 672.89	736.01	03/2020 -	-	9.38
366	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
367	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	06/2021	10.24
368	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
369	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54
370	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
371	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	07/2021	3.95
372	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	02/2021	1.78
373	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 - 1,124.11	1,232.76	09/2017 -	05/2021	9.67
374	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 - 404.94	448.18	- -	10/2020	10.68
375	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 - 273.46	276.17	- -	-	.99
376	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
377	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 - 1,995.34	2,400.00	- -	11/2021	20.28
378	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
379	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 - 1,261.98	1,952.20	- -	07/2021	54.69
380	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
381	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
382	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 - 1,052.21	1,449.00	- -	01/2021	37.71
383	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 - 1,532.62	2,499.00	03/2021 -	04/2021	63.05
384	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 - 496.20	537.17	- -	-	8.26
385	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
386	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	07/2021	5.32
387	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	-	4.99
388	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
389	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 - 634.70	931.21	- -	07/2021	46.72
390	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 795.50	799.30	- -	07/2021	.48
391	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	-	25.68
392	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 - 743.88	743.89	- -	12/2021	.00
393	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	-	27.86
394	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 - 217.96	884.00	- -	-	305.58
	Total		1,03,345.32 19,154.00 1,03,438.31	1,27,447.37			
	TELECOMMUNICATIONS						
	Bharat Sanchar Nigam Limited						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
395	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00 431.00	431.16	06/2021 -	11/2021	.04
	<u>Department Of Telecommunication</u>						
396	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 - 13,334.00	24,664.00	07/2015 -	06/2021	84.97
	Total		13,765.16 431.00 13,765.00	25,095.16			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
397	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 - 10,773.00	12,787.00	12/2018 -	08/2022	18.69
	<u>Chennai Metro Rail Ltd</u>						
398	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 - 14,600.00	19,058.00	12/2015 -	-	30.53
	<u>Mumbai Metro Rail Corporation Ltd</u>						
399	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 - 23,136.00	33,406.00	01/2015 -	03/2023	44.39
	<u>National Building Construcion Corporation Ltd</u>						
400	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 - 4,264.00	4,720.73	11/2019 -	-	10.71
	Total		52,773.00 .00 52,773.00	69,971.73			
	<u>WATER RESOURCES</u>						
	<u>Uttar Pradesh Jal Nigam</u>						
401	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 - 231.79	234.03	12/2021 -	12/2021	.97
	Total		231.79 .00 231.79	234.03			
	Grand Total		5,19,900.86 33,341.20 5,30,998.68	7,70,764.90			

Details of State wise Projects Costing Rs.150 crore and above (as on					28.02.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2021]	417.23 (-) [441.33]	291.75 (24.10) [33]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	47.28 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	164.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	172.78 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	26.44 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	39.86 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	24.96 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [0/0]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [3/2023]	611.80 (-) [611.80]	0.00 (0.00) [0]
11	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (-) [6/2021]	177.10 (-) [177.10]	0.00 (0.00) [16]
	<u>Health And Family Welfare</u>				
12	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [6/2021]	601.02 (-) [601.02]	358.42 (0.00) [-]
13	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2021]	272.19 (-) [272.54]	258.51 (0.35) [24]
	<u>Human Resource Development</u>				
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-)	186.00 (199.00)	130.63 (19.00)

			[3/2021]	[205.00]	[6]
15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	9/2019	9/2022 (-) [1/2023]	588.72 (-) [588.72]	14.80 (0.00) [4]
16	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [0/0]	655.34 (-) [655.34]	49.89 (0.00) [0]
	<u>Petroleum</u>				
17	220 KV GRID SUPPLY	10/2020	3/2021 (-) [3/2021]	303.40 (-) [303.40]	0.00 (0.00) [0]
18	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	232.67 (0.00) [3]
19	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (3/2021) [3/2021]	384.58 (-) [384.58]	267.12 (0.00) [-1]
20	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [3/2021]	580.20 (-) [580.20]	151.16 (0.00) [1]
21	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (6/2022) [6/2022]	34,012.00 (-) [25,090.00]	10,477.71 (-8,922.00) [24]
22	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [7/2022]	167.00 (-) [167.00]	8.49 (0.00) [0]
23	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	92.80 (0.00) [10]
24	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	65.53 (0.00) [0]
25	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [11/2022]	332.61 (-) [332.61]	0.00 (0.00) [0]
26	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [8/2021]	210.94 (-) [210.94]	0.00 (0.00) [0]
27	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [7/2021]	196.26 (-) [196.26]	84.63 (0.00) [12]
28	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	13,352.70 (5,336.00) [24]
	<u>Railways</u>				
29	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [829.00]	0.94 (0.00) [0]
30	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
31	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
32	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2024]	3,631.00 (-) [3,887.48]	1,165.50 (256.48) [24]
33	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2024]	1,045.20 (-) [2,120.16]	850.07 (1,074.96) [180]
34	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022	2,499.71	604.03

			(3/2024) [3/2024]	(-) [2,499.71]	(0.00) [24]
35	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [0/0]	234.50 (-) [235.00]	14.14 (0.50) [0]
36	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [3/2021]	387.70 (-) [487.13]	434.63 (99.43) [36]
37	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,643.25]	1,214.20 (354.55) [36]
38	NANDYAL-YERRAGUNTLA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
39	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	2,224.17 (302.42) [0]
40	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [3,377.00]	2,683.67 (1,873.29) [24]
Road Transport And Highways					
41	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	234.49 (0.00) [0]
42	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (-) [2/2021]	1,226.88 (-) [1,226.88]	0.00 (0.00) [0]
43	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021 (-) [2/2021]	1,601.10 (-) [1,601.10]	0.00 (0.00) [0]
44	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
45	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	351.02 (0.00) [0]
46	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (5/2021) [5/2021]	263.45 (-) [263.45]	97.45 (0.00) [44]
47	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (4/2021) [11/2019]	429.43 (-) [429.43]	293.60 (0.00) [0]
48	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [6/2021]	314.43 (-) [314.43]	86.83 (0.00) [-]
49	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (12/2020) [12/2020]	350.61 (-) [350.61]	323.06 (0.00) [0]
50	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
51	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]
52	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
53	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (-) [0/0]	333.21 (-) [355.89]	315.57 (22.68) [0]
54	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-	3/2018	3/2021	1,532.62	1,539.65

	KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)		(10/2021) [4/2021]	(-) [2,499.00]	(966.38) [1]
55	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	1,634.05 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (-) [12/2020]	576.48 (-) [576.48]	288.92 (0.00) [0]
57	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (7/2021) [7/2021]	348.95 (-) [348.95]	200.57 (0.00) [59]
58	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (-) [12/2020]	386.09 (-) [386.09]	199.35 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (7/2021) [5/2019]	290.15 (-) [290.15]	214.00 (0.00) [0]
61	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	550.75 (0.00) [-]
63	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (8/2021) [4/2021]	995.09 (995.00) [995.09]	476.77 (0.00) [59]
64	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (-) [9/2020]	444.84 (-) [444.84]	304.42 (0.00) [0]
65	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (-) [8/2020]	376.25 (-) [376.25]	264.97 (0.00) [0]
66	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (-) [0/0]	297.12 (294.00) [294.12]	373.98 (-3.00) [0]
67	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (6/2021) [2/2021]	289.67 (290.00) [289.67]	177.78 (0.00) [30]
68	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (4/2021) [1/2021]	504.19 (504.00) [504.19]	427.08 (0.00) [0]
69	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (3/2021) [3/2021]	271.45 (-) [271.45]	225.81 (0.00) [65]
70	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (5/2021) [8/2019]	319.28 (-) [319.28]	214.00 (0.00) [0]
71	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (-) [0/0]	244.95 (245.00) [244.95]	136.22 (0.00) [0]
72	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (6/2021) [2/2019]	372.68 (-) [372.68]	214.00 (0.00) [0]
73	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2021) [3/2021]	228.32 (-) [228.32]	105.72 (0.00) [31]
74	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM	1/2018	8/2018 (5/2021)	418.03 (-)	279.86 (0.00)

	420.800(P		[8/2020]	[418.03]	[0]
75	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (-) [0/0]	378.24 (-) [378.24]	315.42 (0.00) [0]
76	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [10/2021]	1,959.00 (-) [1,959.00]	1,211.72 (0.00) [-]
77	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (-) [1/2020]	597.67 (-) [597.67]	0.00 (0.00) [0]
78	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN	9/2018	2/2019 (-) [2/2019]	617.41 (-) [617.41]	0.00 (0.00) [0]
79	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [7/2021]	1,323.15 (-) [1,323.15]	785.33 (0.00) [-]
80	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [9/2021]	1,550.98 (-) [1,550.98]	1,337.98 (0.00) [-]
81	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,275.58 (0.00) [0]
82	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	951.13 (145.48) [0]
83	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
84	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
85	COKE OVEN BATTERY-5	12/2011	12/2017 (12/2020) [12/2020]	2,858.00 (-) [2,558.00]	1,808.75 (-300.00) [0]
	<u>Urban Development</u>				
86	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>Water Resources</u>				
87	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2021) [4/2022]	10,151.04 (55,548.87) [55,548.87]	16,995.57 (45,397.83) [25]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
88	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (2/2021) [2/2021]	2,496.90 (7,927.34) [7,927.34]	8,154.49 (5,430.44) [134]
89	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	13,233.01 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
90	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	133.95 (0.00) [0]
91	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	394.53 (0.00) [0]
92	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	140.98 (0.00) [0]

93	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	160.09 (0.00) [0]
94	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	25.52 (0.00) [0]
95	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	104.06 (0.00) [0]
96	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	0.00 (0.00) [0]
97	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	15.49 (0.00) [0]
98	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	33.61 (0.00) [0]
99	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	33.58 (0.00) [0]
100	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	0.00 (0.00) [0]
101	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	104.06 (0.00) [0]
102	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	104.06 (0.00) [0]
103	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	115.89 (0.00) [0]
104	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	260.57 (0.00) [0]
105	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	91.23 (0.00) [0]
106	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]
107	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	178.10 (0.00) [0]
108	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	184.62 (0.00) [0]
109	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	91.25 (0.00) [0]
110	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	376.69 (0.00) [0]
111	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	0.00 (0.00) [0]
112	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	0.00 (0.00) [0]
113	CONSTRUCTION OF MEKA ROING HUNLI FROM	1/2017	3/2017	1,253.10	204.77

	EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN		(-) [3/2022]	(-) [1,253.10]	(0.00) [60]
114	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [2/2021]	167.28 (-) [167.28]	22.06 (0.00) [46]
115	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
116	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	(-) [0/0]	(-) [434.06]	(0.00) [0]
117	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	139.47 (0.00) [47]
118	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [252.79]	97.07 (57.56) [0]
119	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [263.31]	110.34 (59.95) [0]
120	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	104.37 (0.00) [0]
121	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	104.36 (0.00) [0]
122	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (-) [389.45]	349.94 (182.42) [0]
123	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	50.17 (0.00) [46]
124	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	0.00 (119.37) [0]
125	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
126	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/	256.66	24.14
127	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	(-) [4/2022]	(-) [175.06]	(0.00) [-]
128	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/	176.12	61.55
129	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	(-) [4/2022]	(-) [176.12]	(0.00) [-]
	ASSAM		/	1,979.00	1,217.25
			(3/2020) [0/0]	(-) [2,036.90]	(57.90) [0]
	ASSAM				
	Civil Aviation				
130	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2022]	1,142.00 (-) [1,232.00]	323.90 (90.00) [12]
	Health And Family Welfare				
131	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [7/2022]	875.00 (-) [747.80]	296.84 (-127.20) [14]
132	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-)	175.57 (-)	163.37 (0.00)

			[3/2018]	[175.57]	[0]
	<u>Petroleum</u>				
133	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [6/2021]	557.00 (-) [557.00]	471.42 (0.00) [16]
134	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [4/2021]	224.75 (-) [222.21]	144.80 (-2.54) [8]
135	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [6/2021]	423.00 (-) [502.00]	403.62 (79.00) [22]
136	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [4/2021]	543.91 (638.60) [652.10]	136.05 (108.19) [14]
137	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [12,366.00]	168.82 (0.00) [0]
138	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	117.34 (0.00) [0]
139	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2021) [5/2021]	249.85 (303.75) [303.75]	180.83 (53.90) [12]
	<u>Railways</u>				
140	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2021]	314.00 (486.96) [800.00]	795.88 (486.00) [24]
141	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,478.05 (717.68) [12]
142	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [5/2021]	870.96 (-) [1,873.21]	1,133.64 (1,002.25) [2]
143	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,105.00]	787.79 (719.80) [48]
	<u>Road Transport And Highways</u>				
144	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (390.73) [390.73]	267.46 (122.65) [0]
145	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
146	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	12.40 (0.00) [0]
147	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
148	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [303.49]	153.44 (-216.52) [0]
149	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	474.44 (0.00) [0]
150	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	64.28 (0.00) [0]
151	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	103.73 (-28.50) [0]

152	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.30]	102.90 (-30.09) [42]
153	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [4/2021]	294.17 (-) [294.17]	190.47 (0.00) [63]
154	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	0.00 (0.00) [0]
155	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (-) [0/0]	166.94 (-) [166.94]	0.00 (0.00) [0]
156	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	489.84 (143.23) [0]
157	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [0/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
158	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	233.27 (7.98) [0]
159	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
160	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	117.35 (0.00) [0]
161	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/	818.00 (-) [0/0]	228.44 (69.68) [0]
162	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	126.86 (-65.43) [42]
163	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	399.65 (0.00) [0]
164	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	273.38 (0.00) [0]
165	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
166	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
167	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
168	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
169	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
170	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2020]	208.00 (-) [230.00]	360.99 (22.00) [0]
171	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	352.28 (0.00) [0]
172	OUR LANNING OF DOLABARI TO JAMUGURI SECTION	3/2017	/	1,049.51	127.57

	FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST		(-) [0/0]	(-) [273.40]	(-776.11) [0]
173	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	236.86 (-70.66) [0]
174	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	70.46 (0.00) [0]
175	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	0.00 (0.00) [0]
176	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	0.00 (0.00) [0]
	BIHAR				
	Civil Aviation				
177	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	1,216.90 (-) [1,216.90]	122.19 (0.00) [0]
	Human Resource Development				
178	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [10/2021]	496.18 (496.00) [498.99]	224.58 (2.81) [52]
179	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (375.00) [375.00]	48.46 (0.00) [26]
	Petroleum				
180	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [4/2023]	14,810.00 (-) [14,810.00]	722.25 (0.00) [0]
181	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	132.60 (0.00) [0]
182	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (12/2021) [12/2021]	522.00 (-) [522.00]	301.57 (0.00) [9]
183	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (2/2022) [2/2022]	199.36 (-) [199.36]	29.92 (0.00) [16]
184	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (11/2020) [0/0]	951.64 (-) [951.64]	708.43 (0.00) [0]
185	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021) [6/2021]	189.00 (-) [189.00]	126.15 (0.00) [5]
186	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (9/2021) [9/2021]	206.50 (-) [206.50]	115.92 (0.00) [6]
187	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	1.76 (0.00) [0]
	Power				
188	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (4/2022) [4/2022]	8,692.97 (21,312.11) [21,312.11]	18,308.58 (12,619.14) [126]
189	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (6/2020) [4/2021]	5,353.00 (10,566.00) [10,566.00]	8,680.05 (5,213.00) [105]
190	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	1,479.16 (0.00) [0]

191	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (6/2021) [7/2021]	12,964.60 (17,304.00) [17,304.00]	15,463.61 (4,339.40) [38]
	<u>Railways</u>				
192	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]
193	ARARIA-SUPAUL (NL)	4/2008	/ (-) [3/2023]	1,605.17 (-) [1,605.17]	24.31 (0.00) [-]
194	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	2.04 (2,668.81) [-]
195	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2023]	378.56 (-) [1,858.75]	385.87 (1,480.19) [-]
196	DANIYAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
197	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [0/0]	205.00 (-) [205.00]	5.21 (0.00) [0]
198	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [3/2022]	329.39 (-) [1,483.14]	1,194.00 (1,153.75) [-]
199	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [0/0]	445.25 (-) [445.25]	1.15 (0.00) [0]
200	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (-) [0/0]	213.01 (-) [480.00]	477.72 (266.99) [0]
201	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [3/2023]	528.65 (-) [2,066.78]	1,529.08 (1,538.13) [-]
202	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [11/2022]	324.73 (-) [1,070.00]	1,062.07 (745.27) [128]
203	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (-) [3/2023]	548.00 (-) [819.01]	530.12 (271.01) [36]
204	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [12/2023]	162.87 (-) [614.45]	340.21 (451.58) [-]
205	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/ (-) [3/2022]	333.76 (-) [360.00]	6.74 (26.24) [-]
206	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	862.71 (0.00) [36]
207	KOSI BRIDGE (NL), ECR	4/2002	3/2020 (-) [0/0]	499.41 (-) [516.02]	436.36 (16.61) [0]
208	KURSELA-BIHARIGANJ (NL)	4/2008	/ (-) [0/0]	192.56 (-) [192.56]	0.39 (0.00) [0]
209	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012 (-) [7/2021]	477.88 (283.95) [751.55]	687.20 (273.67) [112]
210	MOTIHARI-SITAMARHI (NL)	4/2006	/ (-) [0/0]	211.00 (-) [1,006.00]	24.74 (795.00) [0]

211	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	4/2016	3/2021 (-) [6/2022]	731.64 (-) [1,185.73]	165.55 (454.09) [15]
212	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.60
			(-) [0/0]	(-) [281.30]	(0.00) [0]
213	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.53
			(-) [3/2024]	(-) [228.05]	(0.00) [-]
214	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	541.83
			(-) [0/0]	(-) [546.71]	(214.56) [0]
215	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.31
			(-) [0/0]	(-) [620.57]	(0.00) [0]
216	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	968.95
			(-) [3/2024]	(2,132.03) [2,145.00]	(1,612.13) [60]
217	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/	180.82	543.57
			(-) [0/0]	(-) [726.31]	(545.49) [0]
218	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	471.48
			(-) [3/2023]	(-) [1,491.47]	(0.00) [36]
219	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	309.44
			(-) [3/2024]	(-) [1,215.54]	(471.50) [36]
220	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	379.57
			(-) [3/2021]	(-) [735.20]	(410.20) [-]
221	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	1,123.21
			(-) [3/2023]	(-) [1,470.50]	(1,098.36) [-]
222	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	266.24
			(-) [3/2025]	(-) [519.33]	(139.33) [-]
223	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.20
			(-) [0/0]	(-) [678.62]	(0.00) [0]
	<u>Road Transport And Highways</u>				
224	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (12/2020) [1/2021]	511.54 (585.00) [591.00]	575.64 (79.46) [0]
225	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
226	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [0/0]	575.00 (-) [575.00]	555.63 (0.00) [0]
227	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	89.69 (0.00) [0]
228	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [11/2020]	464.09 (-) [464.09]	0.00 (0.00) [0]
229	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [12/2020]	649.90 (-) [649.90]	0.00 (0.00) [0]
230	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [11/2020]	446.97 (-) [446.97]	0.00 (0.00) [0]

231	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/	2,926.42	14.94
			(-)	(-)	(0.00)
			[0/0]	[2,926.42]	[0]
232	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING REHABILITATION AND	9/2018	/	1,478.40	3.59
			(-)	(-)	(0.00)
			[0/0]	[1,478.40]	[0]
233	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015	288.24	303.16
			(-)	(-)	(0.00)
			[0/0]	[288.24]	[0]
234	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,598.00]	[0]
235	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020	235.48	36.08
			(-)	(-)	(-7.71)
			[5/2021]	[227.77]	[14]
236	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20	38.11
			(-)	(-)	(40.97)
			[0/0]	[537.17]	[0]
237	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016	683.83	657.38
			(-)	(-)	(-123.13)
			[0/0]	[560.70]	[0]
238	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	553.30	289.14
			(-)	(-)	(-74.95)
			[0/0]	[478.35]	[0]
239	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016	369.77	0.00
			(-)	(-)	(0.00)
			[0/0]	[369.77]	[0]
240	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	178.85	87.02
			(-)	(-)	(-26.23)
			[0/0]	[152.62]	[0]
241	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/	1,167.45	186.70
			(-)	(-)	(15.49)
			[0/0]	[1,182.94]	[0]
242	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/	642.41	400.60
			(-)	(-)	(39.26)
			[0/0]	[681.67]	[0]
243	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018	322.09	77.53
			(-)	(247.00)	(0.00)
			[12/2020]	[322.09]	[0]
244	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016	1,408.85	699.76
			(-)	(-)	(-482.98)
			[0/0]	[925.87]	[0]
245	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/	814.04	512.04
			(-)	(-)	(11.13)
			[10/2021]	[825.17]	[-]
246	FOUR LANING OF PATNA TO KOILWAR	8/2015	/	556.07	0.00
			(-)	(-)	(0.00)
			[0/0]	[556.07]	[0]
247	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019	1,041.10	301.48
			(-)	(-)	(0.00)
			[0/0]	[1,041.10]	[0]
248	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014	574.00	768.73
			(-)	(-)	(0.00)
			[0/0]	[574.00]	[0]
249	PATNA-MUZZAFFARPUR	8/2010	2/2013	671.30	1,360.63
			(-)	(-)	(0.00)
			[0/0]	[671.30]	[0]
250	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016	1,742.01	1,467.08
			(-)	(-)	(0.00)
			[0/0]	[1,742.01]	[0]
251	REHABILITATION AND UPGRADATION OF TWO LANING	1/2018	/	573.70	23.19

	OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I		(-) [0/0]	(-) [573.70]	(0.00) [0]
252	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
253	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	446.60 (0.00) [0]
254	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	238.01 (50.09) [0]
255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
256	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	318.64 (39.60) [0]
257	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	343.70 (19.42) [0]
258	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	253.10 (0.00) [0]
259	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
260	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
261	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	200.18 (0.00) [54]
262	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	39.82 (0.00) [0]
263	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
264	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [0/0]	399.54 (-) [297.27]	271.39 (-102.27) [0]
265	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [1,038.56]	1,160.00 (183.76) [0]
266	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [649.27]	712.15 (133.14) [0]
267	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [0/0]	672.89 (-) [736.01]	26.78 (63.12) [0]
268	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	174.35 (0.00) [0]
269	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [0/0]	230.34 (-) [230.34]	205.97 (0.00) [0]
	<u>Urban Development</u>				
270	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [6/2024]	13,365.77 (-) [13,365.77]	231.90 (0.00) [0]
	<u>Water Resources</u>				

271	I AND D AND STP AT CHAPPRA	11/2018	12/2020 (6/2021) [6/2021]	236.15 (-) [236.15]	22.69 (0.00) [6]
272	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [0/0]	254.13 (-) [254.13]	0.05 (0.00) [0]
273	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [721.37]	712.37 (-234.63) [72]
274	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [0/0]	268.63 (-) [268.63]	274.08 (0.00) [0]
275	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	4/2015	4/2020 (-) [6/2021]	184.93 (-) [184.93]	163.36 (0.00) [14]
276	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [7/2021]	230.06 (-) [230.06]	55.02 (0.00) [0]
277	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [12/2021]	305.19 (-) [305.19]	0.00 (0.00) [4]
278	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [10/2021]	294.02 (-) [294.02]	0.00 (0.00) [0]
279	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	5/2021 (-) [5/2021]	184.86 (-) [184.86]	152.78 (0.00) [0]
280	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [4/2021]	356.37 (-) [356.37]	88.45 (0.00) [0]
281	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [6/2022]	824.00 (-) [824.00]	0.42 (0.00) [0]
282	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [6/2022]	578.89 (-) [578.89]	0.29 (0.00) [0]
283	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [3/2021]	225.77 (-) [225.77]	263.72 (0.00) [12]
284	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [5/2021]	277.42 (-) [277.42]	125.66 (0.00) [0]
285	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (3/2021) [3/2021]	191.62 (-) [191.62]	44.97 (0.00) [4]
	<u>CHANDIGARH</u>				
	<u>Road Transport And Highways</u>				
286	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	3/2010	3/2013 (5/2019) [0/0]	179.89 (271.00) [271.00]	270.91 (91.11) [0]
287	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	1/2019 (-) [0/0]	169.26 (299.00) [299.00]	0.00 (129.74) [0]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
288	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	49.42 (0.00) [60]
289	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2023]	316.10 (-) [316.10]	124.35 (0.00) [36]

290	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	0.00 (0.00) [0]
291	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	142.84 (0.00) [0]
292	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	0.00 (0.00) [0]
293	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	9.71 (0.00) [0]
294	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	4,219.60 (0.00) [0]
295	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2022]	152.43 (459.49) [459.49]	187.31 (307.06) [84]
296	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	0.00 (0.00) [0]
297	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
298	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2022]	178.44 (-) [178.44]	4.43 (0.00) [96]
299	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,587.18 (0.00) [0]
300	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
301	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	24.44 (0.00) [0]
302	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	211.32 (0.00) [84]
303	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	8.28 (0.00) [0]
304	PORDA CHINTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
305	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.95 (0.00) [0]
	<u>Human Resource Development</u>				
306	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [7/2022]	808.62 (-) [808.62]	57.42 (0.00) [0]
	<u>Power</u>				
307	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (-) [0/0]	11,846.00 (-) [12,739.82]	13,766.78 (893.82) [0]
308	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [0/0]	3,004.00 (-) [3,004.00]	2,369.23 (0.00) [0]
	<u>Railways</u>				
309	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019	872.00	1,131.91

			(-) [10/2020]	(-) [1,226.51]	(354.51) [0]
310	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [6/2021]	393.98 (-) [393.98]	350.81 (0.00) [15]
311	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [12/2023]	2,288.00 (-) [4,970.11]	866.16 (2,682.11) [21]
312	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (-) [12/2023]	1,973.00 (-) [2,135.34]	351.35 (162.34) [33]
313	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [3/2022]	3,055.00 (-) [3,055.15]	2,431.72 (0.15) [42]
314	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2023]	1,160.00 (1,160.83) [1,160.83]	902.85 (0.83) [36]
315	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
316	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2021]	1,402.02 (-) [1,300.00]	1,282.18 (-102.02) [21]
	<u>Road Transport And Highways</u>				
317	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	299.11 (231.09) [-]
318	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
319	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	439.27 (0.00) [0]
320	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (3/2021) [3/2021]	291.05 (-) [291.05]	200.71 (0.00) [-]
321	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (6/2021) [6/2021]	335.32 (-) [335.32]	264.26 (0.00) [48]
322	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION	3/2016	9/2016 (10/2020) [10/2020]	491.52 (512.77) [491.52]	474.52 (0.00) [0]
323	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (6/2021) [6/2021]	476.20 (543.73) [544.00]	397.33 (67.80) [57]
324	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (6/2021) [6/2021]	496.02 (-) [496.02]	239.88 (0.00) [75]
325	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (6/2021) [6/2021]	497.14 (572.66) [572.66]	255.42 (75.52) [58]
326	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (6/2021) [6/2021]	624.98 (731.50) [731.50]	399.36 (106.52) [56]
327	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (6/2021) [6/2021]	452.94 (435.61) [435.61]	85.00 (-17.33) [59]
328	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (3/2021) [3/2021]	423.79 (-) [423.79]	264.67 (0.00) [38]
329	REHABILITATION AND UPGRADATION OF NH-111 FROM	11/2015	12/2015	485.44	447.13

	KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION)		(-) [0/0]	(-) [485.44]	(0.00) [0]
330	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (3/2021) [3/2021]	188.80 (-) [188.80]	75.05 (0.00) [22]
331	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (3/2021) [3/2021]	379.16 (-) [379.16]	256.32 (0.00) [40]
	<u>Steel</u>				
332	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2021) [7/2021]	15,525.00 (21,940.00) [21,940.00]	17,691.25 (6,415.00) [74]
333	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (-) [6/2023]	2,907.00 (-) [2,907.00]	185.08 (0.00) [0]
334	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	17.50 (0.00) [0]
	<u>Urban Development</u>				
335	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO	5/2019	9/2020 (-) [0/0]	299.97 (-) [299.97]	0.29 (0.00) [0]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
336	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [5/2021]	303.80 (-) [303.80]	115.88 (0.00) [13]
	<u>Commerce</u>				
337	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [0/0]	302.64 (-) [302.64]	60.00 (0.00) [0]
	<u>Dpiit</u>				
338	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [10/2021]	4,773.00 (-) [5,178.00]	2,419.54 (405.00) [22]
	<u>Health And Family Welfare</u>				
339	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [3/2021]	204.44 (-) [250.00]	229.39 (45.56) [46]
340	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
341	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [3/2021]	156.56 (-) [156.64]	128.08 (0.08) [-]
342	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [3/2021]	414.11 (-) [499.23]	481.52 (85.12) [88]
	<u>Heavy Industry</u>				
343	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (12/2020) [0/0]	1,554.00 (-) [900.00]	815.00 (-654.00) [0]
	<u>Home Affairs</u>				
344	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [12/2021]	1,219.21 (-) [2,000.00]	874.24 (780.79) [26]
	<u>Power</u>				
345	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [5/2021]	271.90 (-) [271.90]	201.69 (0.00) [18]
346	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF	3/2015	5/2017	1,394.52	519.78

	DELHI DURING 12TH PLAN PERIOD (PART-A)		(7/2020) [6/2021]	(-) [1,394.52]	(0.00) [49]
	<u>Railways</u>				
347	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	127.91 (123.32) [-]
348	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [359.00]	111.51 (202.35) [-]
	<u>Road Transport And Highways</u>				
349	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019 (-) [0/0]	269.69 (-) [269.69]	0.00 (0.00) [0]
	<u>Rural Development</u>				
350	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [7/2021]	361.60 (-) [361.60]	12.44 (0.00) [0]
	<u>Telecommunications</u>				
351	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	3/2018 (-) [0/0]	248.20 (-) [248.20]	80.10 (0.00) [0]
	<u>Urban Development</u>				
352	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG	2/2020	11/2020 (2/2021) [11/2020]	532.00 (-) [532.00]	150.00 (0.00) [0]
353	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2021) [10/2021]	197.33 (-) [197.33]	102.34 (0.00) [30]
354	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	11/2020 (-) [0/0]	218.72 (-) [218.72]	126.16 (0.00) [0]
355	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	812.00 (0.00) [0]
356	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	1,248.28 (0.00) [0]
357	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (-) [9/2021]	565.00 (-) [565.00]	511.60 (0.00) [9]
358	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [9/2021]	38,585.00 (-) [38,585.00]	39,838.90 (0.00) [66]
359	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [2/2021]	238.56 (-) [238.56]	157.67 (0.00) [9]
360	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [0/0]	4,264.00 (-) [4,720.73]	4,683.08 (456.73) [0]
361	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [12/2024]	1,180.00 (-) [1,100.80]	35.63 (-79.20) [41]
362	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (-) [3/2022]	392.00 (-) [392.00]	73.79 (0.00) [19]
363	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [3/2022]	1,128.00 (-) [1,128.00]	22.00 (0.00) [0]
364	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (7/2021) [7/2021]	422.00 (-) [422.00]	55.38 (0.00) [4]

365	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [7/2022]	2,694.00 (-) [2,694.00]	651.85 (0.00) [-]
	<u>Water Resources</u>				
366	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
367	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [6/2021]	515.07 (-) [515.07]	297.33 (0.00) [5]
368	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	149.78 (0.00) [0]
369	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	60.47 (0.00) [12]
370	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	118.82 (0.00) [10]
	<u>GOA</u>				
	<u>Health And Family Welfare</u>				
371	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [12/2020]	249.01 (-) [249.07]	228.87 (0.06) [0]
	<u>Human Resource Development</u>				
372	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [0/0]	303.90 (-) [303.90]	16.50 (0.00) [0]
	<u>Road Transport And Highways</u>				
373	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	219.47 (10.43) [0]
374	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	91.39 (0.00) [0]
375	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	478.46 (0.00) [0]
376	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	310.72 (0.00) [0]
377	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	290.64 (0.00) [0]
378	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [0/0]	852.67 (-) [852.67]	138.14 (0.00) [0]
379	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [0/0]	634.32 (-) [634.32]	278.30 (0.00) [0]
380	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	336.25 (0.00) [0]
381	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	205.20 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
382	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [2/2022]	11,459.00 (-) [16,580.00]	16,297.00 (5,121.00) [74]

	Civil Aviation				
383	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022 (-) [3/2023]	1,405.00 (-) [1,405.00]	0.00 (0.00) [7]
	Petroleum				
384	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	84.15 (0.00) [0]
385	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (5/2023) [5/2023]	588.20 (730.20) [730.20]	65.94 (142.00) [-]
386	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [4/2021]	327.78 (-) [200.00]	187.00 (-127.78) [36]
387	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2021) [10/2021]	906.00 (-) [906.00]	259.40 (0.00) [20]
388	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021 (-) [12/2021]	403.00 (-) [403.00]	54.61 (0.00) [0]
389	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024 (-) [9/2024]	18,936.00 (-) [18,936.00]	0.00 (0.00) [0]
390	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022 (-) [8/2022]	444.87 (-) [444.87]	79.65 (0.00) [0]
391	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [970.30]	773.52 (-192.26) [0]
392	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (-) [9/2022]	1,378.00 (-) [1,378.00]	21.66 (0.00) [-3]
393	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [12/2021]	225.54 (-) [225.54]	39.50 (0.00) [10]
	Power				
394	KAWAS SOLAR 56 MW	8/2020	10/2021 (-) [10/2021]	261.80 (-) [261.80]	0.00 (0.00) [0]
395	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (6/2020) [9/2020]	193.14 (-) [193.14]	119.53 (0.00) [0]
396	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (6/2020) [9/2020]	175.64 (-) [175.64]	122.40 (0.00) [0]
	Railways				
397	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,500.00]	1,438.76 (524.38) [0]
398	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (12/2023) [12/2023]	829.74 (1,959.74) [1,959.74]	1,784.02 (1,130.00) [45]
399	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
400	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (10/2021) [10/2021]	551.51 (890.76) [890.76]	745.11 (339.25) [31]
401	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2023) [3/2023]	318.24 (411.62) [411.62]	126.05 (93.38) [132]

402	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (2/2021) [2/2021]	691.84 (1,017.91) [1,017.91]	650.65 (326.07) [11]
403	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [872.65]	800.30 (228.27) [0]
404	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
405	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2024) [3/2024]	844.10 (844.10) [844.10]	179.19 (0.00) [-]
406	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
407	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
408	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,868.89]	1,795.61 (320.23) [3]
409	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2023) [3/2023]	320.66 (1,378.11) [1,378.11]	540.09 (1,057.45) [48]
410	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,002.39) [1,002.39]	642.89 (0.00) [21]
411	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (12/2021) [12/2021]	1,037.15 (1,389.05) [1,389.05]	1,103.31 (351.90) [9]
412	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
Road Transport And Highways					
413	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	303.96 (0.00) [0]
414	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	248.88 (0.00) [0]
415	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [2/2021]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [8]
416	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,669.71 (0.00) [0]
417	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [2/2021]	364.56 (-) [392.00]	353.42 (27.44) [-]
418	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	37.17 (0.00) [0]
419	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	584.17 (0.00) [-]
420	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [6/2021]	2,702.05 (-) [2,043.00]	1,327.65 (-659.05) [-]
421	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	130.53 (0.00) [0]

422	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (-) [962.43]	235.12 (0.00) [0]
423	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	444.86 (0.00) [0]
424	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	715.10 (0.00) [0]
425	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	503.45 (0.00) [0]
426	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	203.40 (0.00) [0]
427	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	450.54 (0.00) [0]
428	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.89 (0.00) [0]
429	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
430	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [11/2020]	953.88 (-) [953.88]	976.79 (0.00) [0]
431	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (-) [1,449.00]	394.36 (396.79) [0]
432	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [0]
433	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	134.77 (0.00) [0]
434	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	109.64 (0.00) [0]
435	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	276.20 (0.00) [0]
436	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
	<u>Urban Development</u>				
437	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [8/2022]	10,773.00 (-) [12,787.00]	8,446.13 (2,014.00) [44]
438	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	56.76 (0.00) [0]
439	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	16.58 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
440	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [3/2021]	215.92 (-) [215.92]	166.34 (0.00) [16]
	<u>Health And Family Welfare</u>				

441	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2019]	505.58 (-) [585.00]	586.96 (79.42) [0]
	<u>Home Affairs</u>				
442	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	1/2020	10/2023 (-) [10/2023]	166.98 (167.00) [166.98]	0.00 (0.00) [0]
443	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96	1/2020	5/2022 (-) [5/2022]	166.98 (-) [166.98]	0.29 (0.00) [0]
	<u>Petroleum</u>				
444	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [3/2022]	909.00 (-) [909.00]	222.31 (0.00) [14]
445	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (8/2021) [8/2021]	206.63 (-) [206.63]	75.17 (0.00) [18]
446	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (-) [9/2026]	520.00 (-) [520.00]	91.57 (0.00) [0]
447	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (-) [7/2021]	164.69 (-) [164.69]	13.16 (0.00) [0]
448	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (6/2021) [6/2021]	255.00 (300.00) [300.00]	253.92 (45.00) [7]
449	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (2/2022) [2/2022]	598.00 (-) [598.00]	240.52 (0.00) [24]
450	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [7/2022]	278.60 (-) [278.60]	25.82 (0.00) [13]
451	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [4/2022]	1,636.00 (-) [1,636.00]	587.98 (0.00) [20]
452	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [10/2021]	1,255.00 (-) [1,255.00]	151.68 (0.00) [0]
453	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (-) [12/2022]	2,281.94 (-) [2,281.94]	429.94 (0.00) [0]
454	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (5/2021) [5/2021]	286.42 (327.01) [327.01]	166.90 (40.59) [9]
	<u>Railways</u>				
455	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2021]	346.32 (-) [346.32]	316.04 (0.00) [24]
456	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [6/2021]	287.00 (-) [893.45]	658.97 (606.45) [114]
	<u>Road Transport And Highways</u>				
457	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [507.70]	496.22 (-95.25) [0]
458	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	516.32 (-37.12) [0]
459	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (3/2021) [3/2021]	639.79 (-) [552.90]	597.77 (-86.89) [12]

460	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [9/2021]	2,128.72 (-) [2,128.72]	1,070.00 (0.00) [29]
461	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (-) [0/0]	276.01 (-) [276.01]	187.39 (0.00) [0]
462	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [2/2021]	247.25 (-) [247.25]	178.64 (0.00) [23]
463	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [0/0]	248.97 (-) [248.97]	270.65 (0.00) [0]
464	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (6/2021) [12/2020]	1,484.30 (-) [1,484.30]	444.49 (0.00) [0]
465	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [0/0]	1,004.67 (-) [813.45]	577.21 (-191.22) [0]
466	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]
467	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	567.52 (0.00) [0]
468	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (1/2020) [0/0]	1,243.45 (-) [1,243.45]	659.79 (0.00) [0]
469	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (6/2020) [0/0]	889.36 (-) [889.36]	438.38 (0.00) [0]
470	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (2/2020) [0/0]	1,018.79 (-) [1,018.79]	468.24 (0.00) [0]
471	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (2/2020) [0/0]	1,051.91 (-) [1,051.91]	526.09 (0.00) [0]
472	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	501.73 (0.00) [0]
473	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (-) [0/0]	1,137.42 (-) [1,137.42]	690.88 (0.00) [0]
474	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (-) [0/0]	1,033.19 (-) [1,033.19]	604.45 (0.00) [0]
475	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [0/0]	1,108.00 (-) [2,967.50]	3,996.01 (1,859.50) [0]
476	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [0/0]	551.58 (-) [551.58]	306.06 (0.00) [0]
477	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [0/0]	275.12 (-) [275.12]	169.48 (0.00) [0]
478	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI	3/2018	/ (-) [0/0]	307.79 (-) [307.79]	197.30 (0.00) [0]
479	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.78 (-) [181.78]	129.12 (0.00) [0]
480	REHABILITATION AND UPGRADATION TO 2-LANE WITH	3/2018	/	198.05	117.51

	PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN		(-) [0/0]	(-) [198.05]	(0.00) [0]
481	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/	795.50	213.17
			(-) [7/2021]	(-) [799.30]	(3.80) [-]
482	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/	634.70	268.17
			(-) [7/2021]	(-) [931.21]	(296.51) [-]
	<u>HIMACHAL PRADESH</u>				
	<u>Health And Family Welfare</u>				
483	AIIMS BILASPUR	4/2018	9/2021	1,351.00	648.37
			(-) [9/2021]	(-) [1,471.00]	(120.00) [0]
484	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021	260.00	25.38
			(-) [5/2022]	(-) [260.00]	(0.00) [11]
	<u>Human Resource Development</u>				
485	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	270.83	226.16
			(-) [0/0]	(-) [270.83]	(0.00) [0]
486	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022	392.51	35.88
			(-) [6/2022]	(-) [392.51]	(0.00) [0]
	<u>Power</u>				
487	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026	1,810.56	286.90
			(-) [1/2026]	(-) [1,810.56]	(0.00) [0]
488	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009	3,919.59	8,825.13
			(3/2022) [3/2022]	(9,897.59) [9,897.59]	(5,978.00) [150]
	<u>Railways</u>				
489	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026	2,966.99	875.99
			(-) [12/2025]	(-) [6,753.42]	(3,786.43) [-12]
	<u>Road Transport And Highways</u>				
490	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019	273.20	667.10
			(-) [0/0]	(-) [273.20]	(0.00) [0]
491	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020	2,485.93	827.64
			(-) [9/2021]	(-) [2,485.93]	(0.00) [15]
492	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016	1,916.79	1,960.92
			(-) [0/0]	(-) [1,916.79]	(0.00) [0]
493	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018	934.46	697.33
			(-) [0/0]	(-) [934.46]	(0.00) [0]
494	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/	478.74	127.42
			(-) [5/2021]	(-) [478.74]	(0.00) [-]
495	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/	1,273.71	663.25
			(-) [0/0]	(-) [1,273.71]	(0.00) [0]
496	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/	447.75	1,160.74
			(-) [8/2020]	(-) [447.75]	(0.00) [0]
497	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/	1,583.18	271.06
			(-) [9/2020]	(-) [1,583.18]	(0.00) [0]
	<u>JAMMU AND KASHMIR</u>				
	<u>Civil Aviation</u>				

498	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [9/2021]	346.27 (-) [480.33]	51.11 (134.06) [0]
	<u>Health And Family Welfare</u>				
499	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	0.00 (0.00) [-16]
500	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
501	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	124.80 (0.00) [0]
	<u>Human Resource Development</u>				
502	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (-) [676.00]	0.00 (0.00) [0]
503	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (-) [7/2022]	329.00 (-) [329.00]	0.00 (0.00) [0]
	<u>Power</u>				
504	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [7/2025]	8,112.12 (-) [8,112.12]	1,664.74 (0.00) [63]
	<u>Railways</u>				
505	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2022]	2,500.00 (27,949.00) [27,949.00]	22,879.22 (25,449.00) [241]
	<u>Road Transport And Highways</u>				
506	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	38.33 (0.00) [0]
507	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	817.59 (-132.75) [0]
508	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	29.22 (0.00) [0]
509	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	815.94 (0.00) [0]
510	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,602.69 (0.00) [0]
511	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,651.59 (0.00) [0]
512	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,709.06 (360.00) [0]
513	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,106.27 (0.00) [0]
514	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [10/2020]	1,100.70 (-) [1,100.70]	2,922.52 (0.00) [0]
515	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [4/2022]	228.39 (-) [228.39]	0.00 (0.00) [0]
516	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON	7/2020	4/2022 (-)	210.79 (-)	0.00 (0.00)

	GOHA-K		[4/2022]	[210.79]	[0]
517	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	29.28 (0.00) [0]
518	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	137.56 (0.00) [0]
519	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	74.42 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
520	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	97.54 (0.00) [0]
521	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2022]	163.51 (-) [163.51]	106.63 (0.00) [132]
522	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	163.16 (0.00) [0]
523	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2022]	162.46 (-) [162.46]	96.86 (0.00) [96]
524	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [6/2021]	289.45 (-) [289.45]	280.46 (0.00) [85]
525	MAGADH EXPANSION OC(51 MTY)	8/2008	7/2012 (3/2025) [3/2025]	6,964.33 (7,254.37) [706.40]	639.01 (-6,257.93) [152]
526	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [3/2022]	1,230.27 (-) [1,230.27]	457.98 (0.00) [83]
527	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [4/2023]	339.88 (-) [339.88]	20.22 (0.00) [108]
528	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.54 (0.00) [0]
529	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	238.83 (0.00) [0]
530	PACHWARA SOUTH COAL BLOCK	7/2013	8/2022 (-) [9/2023]	1,795.01 (-) [1,795.01]	32.27 (0.00) [13]
531	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [12/2021]	243.00 (334.27) [334.27]	18.35 (91.27) [44]
532	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2020]	269.82 (-) [269.82]	207.34 (0.00) [0]
533	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2022]	510.85 (-) [510.85]	401.87 (0.00) [72]
534	RECAST EPR AMRAPALI OC	2/2012	3/2020 (3/2024) [3/2024]	4,983.58 (5,136.15) [4,983.58]	244.12 (0.00) [48]
535	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	39.79 (0.00) [0]
	<u>Human Resource Development</u>				

536	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [6/2021]	171.86 (-) [171.86]	111.29 (0.00) [63]
	<u>Petroleum</u>				
537	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (9/2021) [9/2021]	161.50 (-) [161.50]	67.53 (0.00) [15]
538	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	94.56 (0.00) [0]
539	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	76.84 (0.00) [0]
540	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	634.60 (314.52) [-12]
541	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	73.00 (0.00) [0]
	<u>Power</u>				
542	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [10/2022]	14,366.58 (-) [15,389.42]	11,612.82 (1,022.84) [40]
543	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,380.97 (314.04) [0]
544	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [9/2024]	18,668.00 (-) [17,112.00]	4,060.28 (-1,556.00) [18]
	<u>Railways</u>				
545	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2023]	1,724.20 (-) [1,993.24]	704.10 (269.04) [33]
546	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [3/2022]	348.23 (-) [348.23]	316.23 (0.00) [12]
547	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2022]	1,033.07 (-) [3,550.00]	3,528.48 (2,516.93) [-]
548	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2023]	459.91 (-) [1,625.87]	767.07 (1,165.96) [-]
549	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (12/2018) [6/2021]	258.20 (358.68) [358.68]	297.17 (100.48) [30]
550	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (-) [8/2020]	148.77 (-) [377.00]	195.52 (228.23) [0]
	<u>Road Transport And Highways</u>				
551	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [3/2021]	1,005.08 (-) [1,005.08]	0.00 (0.00) [-]
552	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (10/2019) [10/2019]	997.15 (1,115.95) [1,115.95]	975.08 (118.80) [0]
553	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	64.77 (2.71) [0]
554	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [0/0]	323.72 (-) [336.60]	312.79 (12.88) [0]

555	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
556	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [1/2021]	212.99 (-) [212.99]	155.29 (0.00) [0]
557	SIX LANE OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	350.78 (0.00) [0]
558	TWO/FOUR LANE WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (486.00) [486.00]	432.16 (27.97) [0]
559	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	47.95 (0.00) [0]
	<u>Steel</u>				
560	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [12/2021]	1,034.01 (-) [1,034.01]	513.54 (0.00) [50]
561	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (5/2021) [5/2021]	262.87 (-) [262.87]	172.15 (0.00) [23]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
562	RESIDENTIAL QUATERS FOR HAL, BANGLORE	12/2016	2/2020 (-) [6/2021]	246.31 (-) [246.31]	115.20 (0.00) [16]
	<u>Human Resource Development</u>				
563	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (-) [9/2022]	851.00 (851.00) [851.00]	26.10 (0.00) [6]
	<u>Petroleum</u>				
564	BSVI UPGRADATION	9/2016	12/2019 (4/2021) [10/2021]	1,810.00 (1,810.00) [1,810.00]	1,556.82 (0.00) [22]
565	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	131.02 (0.00) [0]
566	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (-) [6/2023]	200.00 (-) [200.00]	1.46 (0.00) [0]
567	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	763.33 (0.00) [0]
568	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	96.63 (0.00) [0]
569	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [6/2021]	581.00 (637.00) [637.00]	443.62 (56.00) [15]
570	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (-) [11/2021]	380.00 (-) [380.00]	185.40 (0.00) [0]
	<u>Power</u>				
571	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (5/2020) [3/2021]	445.89 (-) [445.89]	456.53 (0.00) [25]
	<u>Railways</u>				
572	ARSIKERE-TUMKUR	3/2015	3/2020 (3/2021) [3/2021]	578.00 (-) [783.00]	613.57 (205.00) [12]

573	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2023]	986.30 (-) [986.30]	307.78 (0.00) [93]
574	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
575	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [327.25]	0.00 (0.00) [-]
576	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [558.00]	0.00 (0.00) [-]
577	GADAG-WADI NL	4/2013	12/2018 (6/2025) [6/2025]	2,841.84 (-) [2,841.84]	277.39 (0.00) [78]
578	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [12/2022]	2,127.00 (-) [3,000.00]	2,181.62 (873.00) [-3]
579	HUBLI- CHIKJAJUR	3/2015	3/2020 (11/2021) [11/2021]	1,156.94 (-) [1,656.00]	1,119.96 (499.06) [20]
580	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [3,911.65]	157.01 (1,596.65) [-]
581	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [0/0]	644.78 (-) [998.00]	463.35 (353.22) [0]
582	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	35.01 (0.00) [93]
583	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
584	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
585	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [1,967.00]	74.87 (165.99) [-]
586	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (-) [348.85]	0.36 (0.00) [-]
<u>Road Transport And Highways</u>					
587	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (1/2021) [12/2021]	1,167.42 (-) [870.00]	336.58 (-297.42) [33]
588	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	273.86 (0.00) [0]
589	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [0]
590	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (3/2022) [3/2022]	701.40 (-) [701.40]	119.00 (0.00) [36]
591	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [0]
592	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]

593	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [0/0]	171.60 (-) [171.60]	0.86 (0.00) [0]
594	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [0/0]	1,388.00 (-) [1,388.00]	1,287.50 (0.00) [0]
595	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [12/2020]	1,664.20 (-) [1,664.20]	936.78 (0.00) [0]
596	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [0/0]	946.00 (-) [946.00]	818.53 (0.00) [0]
597	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	326.88 (0.00) [0]
598	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
599	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
600	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
601	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
602	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,434.00]	1,085.47 (440.84) [0]
603	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.58 (-) [1,177.00]	905.81 (345.42) [0]
604	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,244.98 (272.20) [0]
605	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,088.59 (404.66) [-]
606	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
607	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
608	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [0/0]	950.69 (-) [1,108.00]	1,429.25 (157.31) [0]
609	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
610	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
611	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
612	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
613	WIDENING TO TWO LANE WITH PAVED SHOULDER	9/2017	10/2018	191.60	26.24

	FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR		(-) [0/0]	(-) [191.60]	(0.00) [0]
614	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	130.00 (0.00) [0]
615	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
616	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
617	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
618	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
619	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
620	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	<u>Urban Development</u>				
621	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (3/2021) [6/2024]	26,405.14 (30,695.00) [26,405.14]	16,349.18 (0.00) [64]
	<u>KERALA</u>				
	<u>Health And Family Welfare</u>				
622	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	36.14 (0.00) [21]
	<u>Human Resource Development</u>				
623	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [6/2022]	753.63 (-) [753.63]	58.47 (0.00) [15]
624	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [0/0]	165.23 (-) [165.23]	118.52 (0.00) [0]
	<u>Petroleum</u>				
625	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	711.00 (395.24) [32]
626	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [3/2022]	607.06 (714.25) [714.25]	385.53 (107.19) [53]
627	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (3/2021) [3/2021]	3,313.00 (-) [3,288.96]	2,726.00 (-24.04) [13]
628	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [3/2021]	4,588.29 (-) [5,245.96]	4,852.63 (657.67) [31]
629	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	302.82 (0.00) [0]
	<u>Power</u>				
630	KAYAMKULAM SOLAR 70 MW	9/2019	6/2021 (-) [6/2021]	403.62 (-) [403.62]	0.00 (0.00) [0]
	<u>Railways</u>				
631	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/	1,566.00	262.68

			(-) [0/0]	(-) [2,815.62]	(1,249.62) [0]
632	ERNAKULAM-KUMBALAM	4/2010	/	189.24	6.73
			(-) [0/0]	(-) [275.21]	(85.97) [0]
633	KUMBALAM-TURAVUR	4/2011	/	252.96	8.50
			(-) [0/0]	(-) [369.55]	(116.59) [0]
634	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016	550.00	0.00
			(-) [0/0]	(-) [550.00]	(0.00) [0]
635	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/	1,431.90	198.81
			(-) [0/0]	(-) [1,431.90]	(0.00) [0]
636	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/	1,000.00	0.81
			(-) [0/0]	(-) [1,246.00]	(246.00) [0]
	<u>Road Transport And Highways</u>				
637	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/	845.24	889.83
			(1/2020) [1/2020]	(-) [941.00]	(95.76) [0]
638	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018	804.97	522.80
			(10/2020) [3/2021]	(-) [804.97]	(0.00) [33]
639	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017	1,124.11	492.81
			(-) [5/2021]	(-) [1,232.76]	(108.65) [44]
640	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/	1,424.77	14.19
			(-) [0/0]	(-) [1,853.42]	(428.65) [0]
641	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017	255.75	290.12
			(-) [0/0]	(348.00) [348.43]	(92.68) [0]
642	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012	617.00	943.17
			(-) [0/0]	(-) [617.00]	(0.00) [0]
	<u>Urban Development</u>				
643	KOCHI METRO RAIL PROJECT	7/2012	7/2017	5,181.79	6,059.17
			(9/2020) [9/2020]	(6,218.14) [6,218.14]	(1,036.35) [0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
644	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021	412.24	0.00
			(-) [6/2021]	(-) [412.24]	(0.00) [0]
	<u>Coal</u>				
645	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021	869.44	120.77
			(-) [3/2022]	(-) [869.44]	(0.00) [12]
646	AMRITDHARA OC PROJECT	2/2015	3/2023	481.60	0.00
			(-) [3/2023]	(-) [481.60]	(0.00) [0]
647	BATURA HIGHWALL PROJECT	7/2015	3/2022	231.92	0.85
			(-) [3/2022]	(-) [231.92]	(0.00) [0]
648	BLOCK-B EXPANSION OPENCASE PROJECT	7/2019	3/2023	998.71	0.00
			(-) [3/2023]	(-) [998.71]	(0.00) [0]
649	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022	1,255.17	144.51
			(-) [3/2023]	(-) [1,255.17]	(0.00) [12]

650	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	0.87 (0.00) [0]
651	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2022]	1,783.09 (-) [1,783.09]	558.53 (0.00) [12]
652	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	60.14 (0.00) [36]
653	NIGAHI EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
654	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	100.40 (0.00) [0]
655	RPR FOR JAMUNIA UG (0.90 MTY)	7/2016	3/2022 (-) [3/2022]	281.25 (-) [409.87]	20.99 (128.62) [0]
656	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
657	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
658	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (9/2021) [9/2021]	236.00 (293.00) [293.00]	162.96 (57.00) [15]
	<u>Power</u>				
659	AMELIA COAL MINE	1/2017	9/2020 (-) [8/2022]	2,104.21 (-) [1,587.16]	464.00 (-517.05) [23]
660	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (10/2020) [2/2021]	11,638.55 (15,105.22) [15,105.22]	13,657.43 (3,466.67) [37]
661	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [0/0]	9,870.51 (-) [11,148.86]	10,019.31 (1,278.35) [0]
	<u>Railways</u>				
662	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2023]	1,370.00 (-) [1,370.94]	470.49 (0.94) [24]
663	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2021]	1,485.85 (-) [1,835.83]	1,546.20 (349.98) [12]
664	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [8/2020]	383.79 (-) [1,413.76]	1,416.77 (1,029.97) [0]
665	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [12/2021]	585.93 (-) [1,268.32]	941.56 (682.39) [34]
666	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [603.69]	249.28 (-96.31) [33]
667	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,763.93 (-) [1,762.94]	1,084.58 (-0.99) [36]
668	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2023]	582.13 (1,247.64) [1,247.64]	254.64 (665.51) [12]
669	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022	2,478.23	477.93

			(-) [3/2023]	(-) [2,478.23]	(0.00) [12]
670	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [0/0]	174.00 (-) [174.00]	172.08 (0.00) [0]
671	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2023]	424.60 (-) [2,909.99]	1,132.38 (2,485.39) [24]
672	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2024) [3/2024]	3,503.69 (5,912.40) [5,912.40]	2,143.20 (2,408.71) [24]
Road Transport And Highways					
673	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (1/2021) [2/2021]	191.21 (-) [191.21]	117.80 (0.00) [15]
674	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (3/2021) [3/2021]	249.05 (-) [249.05]	191.67 (0.00) [32]
675	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	296.24 (0.00) [0]
676	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [8/2021]	950.27 (-) [950.27]	224.81 (0.00) [-]
677	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [6/2021]	392.33 (428.55) [428.55]	345.46 (36.22) [39]
678	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	195.73 (0.00) [0]
679	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [12/2020]	374.40 (-) [204.65]	221.79 (-169.75) [0]
680	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	648.40 (0.00) [0]
681	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
682	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (3/2021) [6/2021]	390.51 (-) [390.51]	257.01 (0.00) [-]
683	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [0/0]	656.98 (-) [840.00]	35.00 (183.02) [0]
684	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [12/2021]	743.88 (-) [743.89]	231.66 (0.01) [-]
685	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [2/2022]	1,094.97 (-) [1,094.97]	425.85 (0.00) [-]
686	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [0/0]	217.96 (-) [884.00]	164.95 (666.04) [0]
687	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (6/2021) [6/2021]	205.05 (-) [205.05]	116.58 (0.00) [51]
688	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (-) [3/2021]	264.50 (-) [264.50]	78.54 (0.00) [0]
689	FOUR LANING OF DELINKED STRETCH OF SEONI –	1/2018	/	960.24	738.74

	MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO		(-) [0/0]	(-) [960.24]	(0.00) [0]
690	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
691	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
692	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [6/2015]	928.83 (-) [928.83]	824.83 (0.00) [0]
693	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [5/2020]	794.30 (679.94) [691.38]	669.35 (-102.92) [0]
694	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [5/2020]	795.76 (686.13) [686.13]	669.94 (-109.63) [0]
695	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	771.23 (0.00) [0]
696	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [2/2021]	639.97 (-) [639.97]	473.85 (0.00) [40]
697	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [7/2018]	770.73 (-) [770.73]	326.08 (0.00) [0]
698	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (4/2021) [4/2021]	957.54 (-) [957.54]	735.81 (0.00) [14]
699	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [4/2021]	497.05 (-) [881.05]	754.27 (384.00) [47]
700	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
701	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
702	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (1/2021) [3/2021]	628.45 (-) [628.45]	418.09 (0.00) [14]
703	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [3/2021]	410.72 (-) [410.72]	390.00 (0.00) [71]
704	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [12/2021]	990.97 (-) [990.97]	496.65 (0.00) [24]
705	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [5/2022]	1,047.00 (-) [1,047.00]	296.06 (0.00) [24]
706	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [4/2022]	847.00 (-) [847.00]	312.73 (0.00) [25]
707	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [0/0]	996.27 (-) [996.27]	313.00 (0.00) [0]
708	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (4/2021) [4/2021]	169.63 (-) [169.63]	38.45 (0.00) [37]
709	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-)	178.23 (-)	122.99 (0.00)

			[0/0]	[178.23]	[0]
710	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (9/2020) [11/2020]	287.34 (-) [287.34]	194.85 (0.00) [0]
711	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (4/2021) [4/2021]	877.79 (-) [877.79]	668.14 (0.00) [22]
712	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (2/2021) [2/2021]	235.91 (-) [235.91]	173.80 (0.00) [36]
713	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (5/2021) [5/2021]	809.16 (-) [809.16]	512.17 (0.00) [34]
714	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
715	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [10/2021]	954.43 (-) [1,191.51]	235.61 (237.08) [73]
716	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (6/2021) [6/2021]	511.83 (-) [511.83]	366.24 (0.00) [46]
717	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (3/2021) [3/2021]	254.17 (-) [254.17]	164.68 (0.00) [37]
718	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (1/2021) [3/2021]	233.04 (-) [233.04]	151.12 (0.00) [36]
719	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (12/2020) [3/2021]	279.44 (-) [279.44]	156.14 (0.00) [36]
720	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (3/2021) [3/2021]	166.21 (173.41) [173.41]	139.19 (7.20) [31]
721	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (2/2021) [2/2021]	184.62 (-) [184.62]	115.57 (0.00) [36]
722	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (9/2021) [9/2021]	214.69 (-) [214.69]	59.72 (0.00) [42]
723	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (3/2021) [3/2021]	217.22 (226.88) [226.88]	170.05 (9.66) [31]
724	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (2/2021) [2/2021]	162.56 (-) [162.56]	129.98 (0.00) [35]
725	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (6/2021) [6/2021]	373.82 (-) [373.82]	186.74 (0.00) [21]
	<u>Urban Development</u>				
726	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	126.50 (0.00) [0]
727	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	117.53 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
728	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	475.39 (-) [475.39]	88.11 (0.00) [0]

	<u>Coal</u>				
729	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	121.25 (44.53) [12]
730	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	246.55 (0.00) [0]
731	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	251.34 (0.00) [0]
732	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	281.92 (0.00) [0]
733	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [3/2021]	252.71 (-) [252.71]	99.77 (0.00) [0]
734	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	85.82 (221.74) [0]
735	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [0/0]	304.52 (-) [304.52]	142.28 (0.00) [0]
736	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	330.34 (0.00) [0]
737	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [0/0]	295.56 (-) [295.56]	160.23 (0.00) [0]
738	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	3/2020 (-) [3/2027]	1,184.33 (-) [1,184.33]	368.56 (0.00) [84]
739	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	11/2015	3/2021 (-) [3/2024]	313.34 (-) [313.34]	141.08 (0.00) [36]
740	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	11/2015	3/2020 (-) [3/2026]	851.60 (-) [851.60]	194.28 (0.00) [72]
741	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	135.36 (0.00) [0]
742	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	318.14 (-) [318.14]	211.41 (0.00) [0]
	<u>Fertilisers</u>				
743	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (3/2021) [4/2021]	426.72 (-) [426.72]	315.95 (0.00) [12]
	<u>Health And Family Welfare</u>				
744	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [6/2021]	582.99 (-) [582.99]	460.56 (0.00) [-]
745	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	252.34 (0.00) [0]
	<u>Human Resource Development</u>				
746	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [6/2021]	223.37 (-) [223.37]	61.35 (0.00) [11]
	<u>Petroleum</u>				
747	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (12/2021)	249.26 (-)	121.72 (0.00)

			[9/2021]	[249.26]	[15]
748	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	261.00 (-) [261.00]	147.12 (0.00) [3]
749	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	138.76 (0.00) [3]
750	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	132.88 (0.00) [9]
751	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2020) [3/2021]	861.79 (1,846.46) [1,846.46]	1,546.02 (984.67) [94]
752	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,203.71]	1,565.69 (-88.75) [0]
753	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,475.92) [3,596.00]	3,494.45 (-410.83) [0]
754	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-) [12/2021]	640.00 (-) [640.00]	297.39 (0.00) [0]
755	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2022]	2,494.68 (-) [2,354.72]	1,238.26 (-139.96) [0]
756	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (-) [2/2022]	1,945.00 (-) [1,945.00]	1,468.42 (0.00) [0]
757	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2021) [5/2021]	3,190.69 (3,375.90) [3,375.90]	2,685.92 (185.21) [37]
758	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (3/2021) [3/2021]	449.58 (-) [449.58]	365.05 (0.00) [15]
759	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	974.84 (747.87) [14]
760	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (-) [5/2021]	3,660.71 (3,740.05) [3,740.05]	2,305.03 (79.34) [0]
761	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [0/0]	4,199.00 (5,060.00) [5,060.00]	4,338.40 (861.00) [0]
762	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (5/2021) [5/2021]	763.92 (-) [733.86]	619.17 (-30.06) [5]
763	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [3/2021]	282.64 (-) [282.64]	241.79 (0.00) [7]
	<u>Power</u>				
764	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
	<u>Railways</u>				
765	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (3/2020) [3/2020]	184.06 (199.12) [315.00]	312.62 (130.94) [0]
766	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2023]	2,271.50 (-) [4,517.49]	2,648.51 (2,245.99) [24]
767	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE	3/1996	3/2004	495.44	1,768.25

	LINE(MTP)		(-) [3/2022]	(-) [2,980.41]	(2,484.97) [216]
768	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	445.15 (205.27) [0]
769	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [12/2021]	713.48 (-) [2,725.00]	2,531.51 (2,011.52) [21]
770	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
771	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
772	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	332.19 (0.00) [12]
773	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [1,377.48]	335.23 (584.59) [24]
774	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	244.12 (0.00) [24]
775	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (12/2020) [12/2020]	305.00 (-) [305.00]	269.73 (0.00) [0]
776	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
777	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2021]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [84]
778	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	1,204.21 (0.00) [-12]
779	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
780	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (2,753.05) [3,524.81]	982.38 (1,616.30) [9]
781	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
782	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
783	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
784	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2024]	229.00 (-) [1,096.00]	39.79 (867.00) [36]
785	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	182.65 (0.00) [12]
786	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	408.70 (11.30) [12]
787	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-)	3,168.29 (-)	1,352.27 (0.00)

			[3/2023]	[3,168.29]	[0]
788	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	272.55 (0.00) [24]
	Road Transport And Highways				
789	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
790	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
791	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
792	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	411.79 (0.00) [-]
793	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [4/2021]	621.00 (-) [621.00]	591.21 (0.00) [-]
794	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	857.08 (0.00) [0]
795	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [0/0]	744.64 (-) [982.00]	0.00 (237.36) [0]
796	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,048.10]	887.07 (-23.51) [-]
797	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	70.85 (0.00) [24]
798	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [0/0]	1,098.06 (-) [1,160.64]	1,068.76 (62.58) [0]
799	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	585.85 (0.00) [0]
800	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	324.00 (0.00) [0]
801	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [2/2021]	400.25 (-) [400.25]	105.20 (0.00) [23]
802	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [7/2021]	1,064.88 (-) [1,021.00]	271.89 (-43.88) [-]
803	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [11/2020]	1,059.73 (-) [1,071.00]	610.87 (11.27) [0]
804	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [0/0]	1,030.44 (-) [1,065.51]	1,015.76 (35.07) [0]
805	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [0/0]	988.34 (-) [1,043.28]	1,035.00 (54.94) [0]
806	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [6/2021]	505.00 (-) [504.00]	361.58 (-1.00) [37]
807	AHMADPUR TO PIMPLA	1/2017	8/2019 (-)	422.38 (-)	218.78 (0.00)

			[0/0]	[422.38]	[0]
808	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [0/0]	955.40 (-) [955.40]	409.50 (0.00) [0]
809	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [0/0]	211.42 (-) [211.42]	136.85 (0.00) [0]
810	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	49.38 (0.00) [0]
811	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	186.28 (0.00) [0]
812	AMD I TO SAONER	1/2017	6/2019 (-) [0/0]	396.91 (397.00) [396.91]	280.56 (0.00) [0]
813	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [0/0]	426.06 (426.00) [426.06]	149.80 (0.00) [0]
814	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [0/0]	309.94 (310.00) [309.94]	181.32 (0.00) [0]
815	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	116.75 (0.00) [0]
816	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	151.11 (0.00) [0]
817	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [0/0]	241.69 (242.00) [241.69]	149.29 (0.00) [0]
818	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	61.53 (0.00) [31]
819	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [0/0]	259.55 (260.00) [259.55]	202.34 (0.00) [0]
820	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	271.60 (0.00) [0]
821	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2021]	743.21 (743.00) [743.21]	137.87 (0.00) [0]
822	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	188.64 (0.90) [0]
823	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	124.95 (0.00) [0]
824	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [0/0]	206.97 (207.00) [206.97]	135.41 (0.00) [0]
825	CHIKALI TO DHAD	3/2018	12/2019 (-) [0/0]	189.46 (189.00) [189.46]	97.66 (0.00) [0]
826	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [0/0]	548.03 (548.00) [548.03]	353.00 (0.00) [0]
827	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [0/0]	393.10 (393.00) [393.10]	222.37 (0.00) [0]

828	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	164.90 (0.00) [0]
829	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	72.87 (0.00) [-]
830	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2021) [12/2021]	649.50 (-) [649.50]	199.44 (0.00) [33]
831	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (8/2021) [2/2022]	291.53 (-) [291.53]	127.37 (0.00) [-]
832	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [0/0]	244.90 (-) [244.90]	251.87 (0.00) [0]
833	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (2/2021) [8/2021]	289.21 (-) [289.21]	162.72 (0.00) [-]
834	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2021) [6/2021]	593.26 (-) [690.17]	585.57 (96.91) [37]
835	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
836	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (6/2021) [6/2021]	531.13 (-) [730.97]	630.68 (199.84) [37]
837	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	80.00 (0.00) [0]
838	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
839	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	63.76 (-89.53) [0]
840	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (-) [414.00]	408.90 (-0.51) [0]
841	DAHEGAON TO KUIHI	1/2017	6/2019 (-) [0/0]	228.89 (229.00) [228.89]	152.57 (0.00) [0]
842	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [0/0]	182.63 (-) [182.63]	132.40 (0.00) [0]
843	DEORI TO AMGAON	1/2017	5/2019 (-) [0/0]	409.62 (410.00) [409.62]	227.76 (0.00) [0]
844	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [0/0]	219.91 (-) [219.91]	123.76 (0.00) [0]
845	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [0/0]	296.19 (-) [254.00]	254.85 (-42.19) [0]
846	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [0/0]	336.21 (336.00) [336.21]	142.66 (0.00) [0]
847	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [0/0]	217.14 (217.00) [217.14]	131.55 (0.00) [0]
848	DIGRAS DARWAH KARANJA	1/2017	6/2019	391.06	204.91

			(-) [0/0]	(391.00) [391.06]	(0.00) [0]
849	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	185.74 (0.00) [0]
850	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
851	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [807.00]	628.87 (164.87) [0]
852	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [9/2020]	1,871.34 (-) [1,871.34]	3,443.43 (0.00) [0]
853	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [0/0]	904.16 (-) [904.16]	855.25 (0.00) [0]
854	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	279.80 (0.00) [0]
855	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	208.63 (0.00) [0]
856	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [0/0]	294.87 (295.00) [294.87]	68.30 (0.00) [0]
857	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [0/0]	355.17 (-) [355.17]	268.87 (0.00) [0]
858	INDAPUR TO VADPALE	1/2017	12/2019 (-) [0/0]	1,202.52 (1,203.00) [1,202.52]	648.90 (0.00) [0]
859	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [0/0]	461.96 (-) [461.96]	178.43 (0.00) [0]
860	JALGAON TO BHADGAON	1/2018	11/2019 (-) [0/0]	307.54 (308.00) [307.54]	198.65 (0.00) [0]
861	JALGAON TO NANDURA	3/2018	12/2019 (-) [0/0]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
862	JALKOT TO TOGRI	7/2018	8/2020 (-) [0/0]	299.92 (300.00) [299.92]	66.25 (0.00) [0]
863	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (-) [356.66]	98.05 (0.00) [0]
864	KAIJ TO KUSALAM	1/2017	7/2019 (-) [0/0]	554.78 (-) [554.78]	252.45 (0.00) [0]
865	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	317.91 (0.00) [0]
866	KALMATH TO ZARAP	9/2016	3/2020 (-) [0/0]	1,338.13 (1,338.00) [1,338.13]	961.51 (0.00) [0]
867	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	627.00 (0.00) [0]
868	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-)	407.19 (407.00)	108.68 (0.00)

			[0/0]	[407.19]	[0]
869	KARAD TO TAGAON	1/2017	6/2019 (-) [0/0]	537.81 (538.00) [537.81]	148.25 (0.00) [0]
870	KARAD TO VITA	1/2018	12/2019 (-) [0/0]	344.85 (245.00) [344.85]	181.55 (0.00) [0]
871	KARWANDI TO RAJURI	3/2018	12/2019 (-) [0/0]	276.95 (277.00) [276.95]	255.47 (0.00) [0]
872	KATOL TO WARUD	1/2017	6/2019 (-) [0/0]	463.62 (664.00) [463.62]	253.23 (0.00) [0]
873	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [0/0]	249.29 (-) [249.29]	155.48 (0.00) [0]
874	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [0/0]	203.21 (203.00) [203.21]	173.79 (0.00) [0]
875	KHERDA TO NAGZARI	3/2018	12/2019 (-) [0/0]	181.30 (-) [181.30]	138.50 (0.00) [0]
876	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	261.97 (0.00) [0]
877	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [0/0]	281.78 (282.00) [281.78]	362.73 (0.00) [0]
878	KOTHARI TO DHANORA	9/2018	8/2020 (-) [0/0]	301.38 (301.00) [301.38]	152.42 (0.00) [0]
879	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	290.69 (0.00) [0]
880	KUNDRAI TO WAZAR	1/2018	12/2019 (-) [0/0]	225.25 (225.00) [225.25]	254.75 (0.00) [0]
881	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	190.69 (0.00) [0]
882	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [0/0]	243.45 (244.00) [243.45]	140.20 (0.00) [0]
883	LATUR TO PANGAON	3/2018	12/2019 (-) [0/0]	336.47 (336.00) [336.47]	186.18 (0.00) [0]
884	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [0/0]	237.40 (-) [237.40]	8.34 (0.00) [0]
885	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [0/0]	413.99 (-) [413.99]	299.10 (0.00) [0]
886	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [0/0]	256.15 (-) [256.15]	84.00 (0.00) [0]
887	MALEGAON TO RISOD	2/2018	12/2019 (-) [0/0]	303.24 (303.00) [303.24]	223.97 (0.00) [0]
888	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [0/0]	322.55 (-) [322.55]	189.91 (0.00) [0]

889	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [0/0]	457.52 (-) [457.52]	352.94 (0.00) [0]
890	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [0/0]	222.13 (222.00) [222.13]	153.84 (0.00) [0]
891	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [0/0]	228.54 (-) [228.54]	162.30 (0.00) [0]
892	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [0/0]	418.36 (-) [418.36]	270.13 (0.00) [0]
893	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [0/0]	486.19 (-) [486.19]	293.39 (0.00) [0]
894	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	148.53 (0.00) [0]
895	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	230.03 (0.00) [0]
896	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	221.81 (0.00) [0]
897	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	222.94 (0.00) [0]
898	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	317.05 (0.00) [0]
899	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [0/0]	162.34 (-) [162.34]	53.94 (0.00) [0]
900	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [0/0]	376.72 (377.00) [376.72]	224.81 (0.00) [0]
901	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	222.60 (0.00) [0]
902	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (6/2021) [12/2021]	546.00 (-) [546.00]	302.83 (0.00) [29]
903	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (6/2021) [12/2021]	591.66 (-) [591.66]	317.73 (0.00) [29]
904	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [0/0]	244.04 (244.00) [244.04]	136.95 (0.00) [0]
905	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [0/0]	274.50 (275.00) [274.50]	146.39 (0.00) [0]
906	NANDED TO JALKOT	12/2017	9/2019 (-) [0/0]	456.93 (457.00) [456.93]	158.00 (0.00) [0]
907	NANDGAON TO MORSHI	1/2017	6/2019 (-) [0/0]	385.87 (386.00) [385.87]	254.89 (0.00) [0]
908	NASHIK TO PETH	12/2015	11/2018 (-) [0/0]	289.60 (-) [289.60]	213.10 (0.00) [0]
909	NASRATPUR TO BARASGAON	7/2016	9/2019	406.54	163.36

			(-) [0/0]	(407.00) [406.54]	(0.00) [0]
910	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [0/0]	420.63 (421.00) [420.63]	112.39 (0.00) [0]
911	OMREGA TO AUSA	3/2018	12/2019 (-) [0/0]	272.04 (272.00) [272.04]	186.24 (0.00) [0]
912	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [0/0]	344.25 (344.00) [344.25]	97.52 (0.00) [0]
913	PAHUR TO BODHWAD	1/2017	5/2020 (-) [0/0]	244.93 (-) [244.93]	123.23 (0.00) [0]
914	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	128.89 (0.00) [0]
915	PALPHATA TO PHULAMBAR	3/2018	12/2019 (-) [0/0]	227.19 (227.00) [227.19]	125.23 (0.00) [0]
916	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [0/0]	381.08 (302.00) [381.08]	7.03 (0.00) [0]
917	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
918	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [0/0]	238.19 (238.00) [238.19]	126.00 (0.00) [0]
919	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [0/0]	205.72 (206.00) [205.72]	31.81 (0.00) [0]
920	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	709.06 (0.00) [0]
921	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [0/0]	420.57 (-) [420.57]	252.78 (0.00) [0]
922	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [0/0]	170.00 (-) [170.00]	92.84 (0.00) [0]
923	PEN TO KHOPOLI	3/2018	3/2018 (-) [0/0]	301.39 (302.00) [301.39]	32.52 (0.00) [0]
924	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [0/0]	595.77 (-) [595.77]	264.93 (0.00) [0]
925	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [0/0]	223.46 (-) [223.46]	26.85 (0.00) [0]
926	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [0/0]	228.31 (-) [228.31]	73.50 (0.00) [0]
927	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [3/2021]	1,724.55 (-) [1,724.55]	2,540.00 (0.00) [96]
928	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	125.69 (0.00) [0]
929	REHABILITATION AND UPGRADEMENT OF NH-222(61) FROM KM 342.00 TO 444.00	1/2014	/	446.77	300.50
			(-)	(-)	(0.00)

			[0/0]	[446.77]	[0]
930	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	89.93 (0.00) [0]
931	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (3/2021) [3/2021]	536.65 (634.30) [536.65]	539.22 (0.00) [15]
932	RISOD TO HINGOLI	2/2018	12/2019 (-) [0/0]	355.99 (-) [355.99]	233.77 (0.00) [0]
933	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [0/0]	362.96 (-) [362.96]	74.91 (0.00) [0]
934	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [0/0]	415.25 (415.25) [415.25]	203.63 (0.00) [0]
935	SANGOLA TO JATH	1/2018	12/2019 (-) [0/0]	257.38 (257.00) [257.38]	155.57 (0.00) [0]
936	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	137.63 (0.00) [0]
937	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	151.62 (0.00) [0]
938	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	187.77 (0.00) [0]
939	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	246.97 (0.00) [0]
940	SELDOH TO PANVAR	7/2018	5/2020 (-) [0/0]	404.33 (404.00) [404.33]	22.40 (0.00) [0]
941	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [0/0]	150.79 (-) [150.79]	46.26 (0.00) [0]
942	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [0/0]	373.10 (373.00) [373.10]	311.24 (0.00) [0]
943	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [0/0]	211.34 (-) [211.34]	112.83 (0.00) [0]
944	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	177.79 (0.00) [0]
945	SHIVUR TO YEOLA	3/2018	12/2019 (-) [0/0]	181.08 (-) [181.08]	97.86 (0.00) [0]
946	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	94.22 (0.00) [0]
947	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (-) [448.18]	407.94 (43.24) [0]
948	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [0/0]	290.73 (-) [315.00]	309.40 (24.27) [0]
949	TAKARKHED TO JALNA	9/2017	6/2019 (-) [0/0]	417.90 (418.00) [417.90]	199.01 (0.00) [0]

950	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [0/0]	264.41 (264.00) [264.41]	165.67 (0.00) [0]
951	TALGAON TO KALMATH	10/2016	3/2020 (-) [0/0]	904.70 (905.00) [904.70]	630.05 (0.00) [0]
952	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [0/0]	195.64 (196.00) [195.64]	116.30 (0.00) [0]
953	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	278.82 (0.00) [0]
954	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [0/0]	1,598.47 (1,560.00) [1,598.47]	889.21 (0.00) [0]
955	VITA TO NAGAJ	3/2018	12/2019 (-) [0/0]	304.58 (305.00) [304.58]	86.72 (0.00) [0]
956	WADI TO ASOLA	1/2017	9/2019 (-) [0/0]	363.82 (364.00) [363.82]	26.75 (0.00) [0]
957	WADIGODRI TO DHANGRIIMPRI	3/2018	2/2020 (-) [0/0]	194.23 (194.00) [194.23]	93.23 (0.00) [0]
958	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [0/0]	376.19 (-) [376.19]	47.76 (0.00) [0]
959	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	797.60 (0.00) [0]
960	WARDHA TO ARVI	2/2018	4/2020 (-) [0/0]	313.58 (-) [313.58]	98.04 (0.00) [0]
961	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [0/0]	216.90 (217.00) [216.90]	131.92 (0.00) [0]
962	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [0/0]	165.51 (-) [165.51]	149.54 (0.00) [0]
963	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
964	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Urban Development</u>				
965	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (9/2022) [3/2023]	23,136.00 (-) [33,406.00]	17,039.36 (10,270.00) [98]
966	NAGPUR METRO RAIL	8/2014	3/2018 (-) [0/0]	8,680.00 (-) [8,680.00]	7,068.52 (0.00) [0]
967	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (-) [11,420.00]	5,696.05 (0.00) [0]
	<u>Water Resources</u>				
968	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [0/0]	233.57 (-) [233.57]	32.20 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				

969	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
970	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	10,777.52 (7,809.98) [153]
	<u>Road Transport And Highways</u>				
971	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	8.60 (0.00) [0]
972	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	14.15 (0.00) [0]
973	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	18.22 (0.00) [0]
974	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	17.84 (0.00) [0]
975	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
976	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
977	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	0.00 (0.00) [0]
978	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	101.20 (0.00) [0]
979	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	170.53 (0.00) [0]
980	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	160.06 (-59.80) [36]
	<u>MEGHALAYA</u>				
	<u>Culture Development</u>				
981	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	145.60 (0.00) [42]
	<u>Health And Family Welfare</u>				
982	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	234.12 (0.00) [43]
	<u>Human Resource Development</u>				
983	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	<u>Railways</u>				
984	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [4,083.02]	263.68 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
985	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	84.67 (0.00) [0]
986	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-)	479.20 (-)	712.89 (0.00)

			[0/0]	[479.20]	[0]
987	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	119.35 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
988	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2023]	2,393.47 (5,021.45) [5,521.45]	3,816.20 (3,127.98) [108]
	<u>Road Transport And Highways</u>				
989	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2021) [6/2021]	195.04 (-) [377.99]	325.42 (182.95) [128]
990	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2020) [0/0]	186.96 (-) [322.24]	292.10 (135.28) [0]
991	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2021) [6/2021]	193.69 (-) [327.92]	295.96 (134.23) [128]
992	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	4.72 (0.00) [0]
993	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	0.00 (0.00) [0]
994	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	0.00 (0.00) [0]
995	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	0.00 (0.00) [0]
996	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	0.00 (0.00) [0]
997	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	65.01 (0.00) [43]
998	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	33.18 (0.00) [45]
999	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	47.39 (0.00) [43]
1000	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	18.08 (0.00) [46]
1001	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	58.49 (0.00) [43]
1002	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	50.49 (0.00) [55]
1003	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	59.92 (0.00) [48]
1004	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	72.44 (0.00) [45]
1005	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2020]	624.41 (-) [992.67]	890.74 (368.26) [0]

	<u>MULTI STATE</u>				
	<u>Coal</u>				
1006	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
1007	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	274.95 (0.00) [0]
1008	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	226.81 (0.00) [0]
1009	RECAST PR FOR DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2025]	289.29 (-) [289.30]	35.67 (0.01) [36]
	<u>Dpiit</u>				
1010	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (1/2014) [7/2021]	12,579.09 (-) [13,812.30]	8,715.07 (1,233.21) [22]
	<u>Human Resource Development</u>				
1011	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	8/2018	3/2019 (-) [0/0]	418.00 (-) [418.00]	110.00 (0.00) [0]
1012	STUDY IN INDIA	3/2018	4/2018 (-) [0/0]	150.00 (-) [150.00]	0.00 (0.00) [0]
	<u>Petroleum</u>				
1013	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	3/2021 (-) [8/2021]	1,823.00 (-) [3,027.90]	1,755.66 (1,204.90) [5]
1014	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [4/2021]	571.66 (-) [571.66]	457.91 (0.00) [16]
1015	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (3,060.00) [3,060.00]	2,096.40 (-248.00) [0]
1016	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	103.91 (0.00) [0]
1017	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	3,437.00 (3,048.00) [3,048.00]	1,718.70 (-389.00) [12]
1018	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	32.60 (0.00) [0]
1019	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2021]	2,433.00 (-) [2,433.00]	2,018.90 (0.00) [6]
1020	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (8/2022) [8/2022]	2,677.00 (3,072.00) [3,072.00]	1,825.04 (395.00) [14]
1021	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (5,909.00) [5,909.00]	3,483.60 (2,994.00) [110]
1022	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [5/2021]	2,881.40 (-) [2,000.00]	1,556.70 (-881.40) [5]
1023	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	837.00 (0.00) [0]
1024	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-)	2,321.00 (-)	2,750.24 (1,017.00)

			[6/2021]	[3,338.00]	[6]
1025	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (2/2021) [5/2021]	690.00 (-) [690.00]	508.53 (0.00) [34]
1026	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2021]	406.00 (-) [406.00]	187.00 (0.00) [5]
1027	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (1/2021) [3/2021]	352.56 (-) [490.24]	455.00 (137.68) [48]
1028	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	205.30 (0.00) [0]
	Power				
1029	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (4/2020) [5/2020]	198.49 (-) [198.49]	140.77 (0.00) [0]
1030	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2021]	4,754.42 (-) [9,129.32]	2,002.54 (4,374.90) [36]
1031	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [3/2021]	358.83 (-) [358.83]	239.65 (0.00) [10]
1032	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (4/2020) [7/2020]	1,364.52 (1,891.41) [1,891.41]	1,320.63 (526.89) [0]
1033	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2020) [5/2021]	522.29 (546.36) [546.36]	477.66 (24.07) [54]
1034	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [4/2021]	3,500.00 (3,500.00) [3,994.00]	2,825.43 (494.00) [9]
1035	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (9/2020) [4/2021]	235.53 (-) [235.53]	148.03 (0.00) [22]
1036	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (6/2021) [6/2021]	322.30 (-) [322.30]	200.36 (0.00) [28]
1037	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [6/2021]	197.40 (-) [197.40]	89.36 (0.00) [39]
1038	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [0/0]	3,519.59 (-) [3,519.59]	2,562.41 (0.00) [0]
1039	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [3/2021]	5,070.13 (-) [5,070.13]	4,041.83 (0.00) [11]
1040	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALAR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (4/2021) [3/2021]	14,733.37 (-) [14,733.37]	11,441.18 (0.00) [16]
1041	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALAR EN	8/2017	2/2020 (9/2020) [3/2021]	1,931.39 (-) [1,931.39]	1,644.55 (0.00) [13]
1042	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2021]	5,111.33 (6,700.00) [6,700.00]	2,541.14 (1,588.67) [36]
1043	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (14,719.10) [14,719.10]	12,869.26 (3,588.91) [103]
1044	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN	3/2017	11/2019 (-)	283.72 (-)	196.10 (0.00)

	REGION I.E WARO		[0/0]	[283.72]	[0]
1045	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [0/0]	3,654.00 (-) [3,654.00]	3,508.04 (0.00) [0]
1046	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [0/0]	608.24 (-) [608.24]	425.04 (0.00) [0]
1047	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [0/0]	203.28 (-) [260.03]	200.16 (56.75) [0]
1048	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (6/2020) [6/2021]	379.95 (-) [379.95]	224.72 (0.00) [18]
1049	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [0/0]	487.49 (-) [639.46]	590.30 (151.97) [0]
1050	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (6/2020) [3/2021]	4,824.12 (5,071.94) [5,071.94]	4,630.84 (247.82) [101]
1051	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (12/2020) [1/2021]	871.62 (902.49) [902.49]	644.11 (30.87) [0]
1052	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (4/2020) [4/2020]	408.46 (516.12) [516.12]	415.85 (107.66) [0]
1053	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [0/0]	5,151.37 (-) [5,151.37]	3,269.93 (0.00) [0]
1054	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (4/2021) [3/2021]	808.63 (-) [808.63]	639.30 (0.00) [38]
1055	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [6/2021]	374.63 (-) [374.63]	241.55 (0.00) [62]
	<u>Railways</u>				
1056	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	11,158.98 (0.00) [0]
1057	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2021]	288.35 (-) [502.48]	422.81 (214.13) [-]
1058	BARIARPUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.11 (-200.00) [-]
1059	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2022) [6/2021]	704.31 (-) [927.94]	521.91 (223.63) [15]
1060	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2022]	175.80 (-) [495.10]	283.97 (319.30) [-]
1061	CHANDIGARH-BADDI	4/2007	3/2023 (3/2025) [3/2025]	328.14 (1,540.13) [1,540.13]	242.12 (1,211.99) [24]
1062	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1063	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (3/2024) [3/2024]	523.52 (-) [1,205.00]	2.28 (681.48) [-]
1064	CHHAPRA-BALLIA UP	3/2013	1/2019 (-)	295.00 (-)	506.99 (182.31)

			[2/2022]	[477.31]	[37]
1065	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	112.02 (651.22) [0]
1066	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	103.78 (173.89) [96]
1067	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2023) [3/2023]	1,347.26 (1,347.26) [1,347.26]	897.00 (0.00) [12]
1068	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2025) [3/2025]	1,640.04 (1,640.04) [1,640.04]	866.05 (0.00) [36]
1069	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [439.30]	374.08 (74.13) [96]
1070	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2023]	336.91 (791.39) [791.39]	572.99 (454.48) [-]
1071	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	637.87 (818.35) [133]
1072	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1073	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1074	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1075	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.55 (134.08) [0]
1076	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (-) [4/2021]	511.86 (-) [2,005.25]	1,777.22 (1,493.39) [12]
1077	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1078	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	148.26 (932.64) [33]
1079	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [5/2021]	678.54 (678.54) [929.86]	738.84 (251.32) [26]
1080	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [663.13]	516.55 (120.95) [12]
1081	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	11.32 (88.07) [-]
1082	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1083	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2021]	1,614.59 (-) [1,870.41]	1,528.14 (255.82) [24]
1084	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.74 (0.00) [28]

1085	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [3/2025]	166.89 (-) [166.89]	0.02 (0.00) [-]
1086	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [6/2021]	625.00 (781.00) [859.00]	852.73 (234.00) [63]
1087	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2027]	2,132.77 (-) [3,037.95]	350.55 (905.18) [156]
1088	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	640.17 (71.58) [108]
1089	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [3/2025]	174.56 (-) [174.56]	71.43 (0.00) [-]
1090	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,370.71 (0.00) [36]
1091	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [1,952.68]	543.07 (95.73) [12]
1092	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [12/2021]	270.14 (-) [457.08]	439.49 (186.94) [-]
1093	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	149.30 (138.71) [228]
1094	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,131.17 (8,000.84) [202]
1095	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	106.31 (0.00) [132]
1096	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2027]	120.70 (-) [2,172.16]	243.01 (2,051.46) [105]
1097	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	163.26 (180.72) [157]
1098	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	356.54 (59.77) [-]
1099	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2023]	1,723.00 (1.00) [3,421.35]	1,847.08 (1,698.35) [276]
1100	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [0/0]	414.84 (-) [1,040.00]	154.52 (625.16) [0]
1101	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (-) [2,200.00]	714.78 (1,750.00) [140]
1102	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	32.00 (0.05) [240]
1103	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [0/0]	242.22 (-) [471.00]	73.97 (228.78) [0]
1104	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [12/2021]	241.52 (-) [373.87]	287.09 (132.35) [-]
1105	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019	1,798.00	69.92

			(-) [3/2024]	(2,042.51) [2,042.51]	(244.51) [60]
1106	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/	819.23	1,082.01
			(-) [0/0]	(-) [1,871.00]	(1,051.77) [0]
1107	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008	1,180.19	3,645.92
			(-) [4/2021]	(2,531.34) [4,541.38]	(3,361.19) [148]
1108	PHULERA - DIGANA DOUBLING	5/2015	3/2020	600.00	172.41
			(-) [4/2022]	(-) [701.81]	(101.81) [25]
1109	PIRPAINTI-BHAGALPUR	4/2011	/	261.38	538.28
			(-) [5/2019]	(-) [565.00]	(303.62) [0]
1110	PIRPAINTI-JASIDIH	4/2013	3/2022	915.98	355.79
			(-) [3/2025]	(-) [2,137.81]	(1,221.83) [36]
1111	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017	299.60	1.12
			(-) [3/2026]	(-) [335.62]	(36.02) [108]
1112	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/	2,082.75	186.12
			(-) [0/0]	(-) [4,262.36]	(2,179.61) [0]
1113	RAYADURGA-TUMKUR NL	4/2007	/	2,062.30	1,111.69
			(-) [3/2025]	(-) [2,432.50]	(370.20) [-]
1114	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/	297.47	52.09
			(-) [3/2025]	(-) [298.22]	(0.75) [-]
1115	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016	277.28	185.36
			(-) [3/2025]	(-) [266.32]	(-10.96) [108]
1116	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/	296.00	0.01
			(-) [12/2023]	(-) [296.10]	(0.10) [-]
1117	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/	450.00	0.00
			(-) [3/2025]	(-) [1,261.34]	(811.34) [-]
1118	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/	365.17	1.76
			(-) [3/2025]	(-) [527.54]	(162.37) [-]
1119	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020	16,592.00	22,485.00
			(-) [0/0]	(51,101.00) [51,101.00]	(34,509.00) [0]
1120	YELAHANKA-PENUKONDA	5/2015	3/2020	860.43	881.92
			(6/2021) [6/2021]	(-) [1,147.00]	(286.57) [15]
	<u>Road Transport And Highways</u>				
1121	4 LANING OF NAGPUR-BETUL	2/2011	8/2014	2,498.76	2,531.46
			(-) [0/0]	(-) [2,498.76]	(0.00) [0]
1122	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015	1,928.22	2,467.00
			(-) [3/2021]	(-) [2,945.00]	(1,016.78) [71]
1123	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/	1,294.47	0.00
			(-) [0/0]	(-) [1,296.00]	(1.53) [0]
1124	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/	998.70	0.00
			(-) [0/0]	(-) [962.00]	(-36.70) [0]
1125	GWALIOR-JHANSI, NH-75	12/2003	12/2009	604.00	334.71

			(-) [0/0]	(-) [364.59]	(-239.41) [0]
1126	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [11/2020]	754.00 (-) [754.00]	1,364.18 (0.00) [0]
1127	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [5/2021]	1,244.10 (-) [1,244.10]	1,565.00 (0.00) [-]
1128	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,848.49 (0.00) [0]
1129	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	2,901.20 (531.45) [105]
	<u>Shipping And Ports</u>				
1130	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	5,369.18 (4,633.81) [4,633.81]	1,814.28 (-735.37) [0]
	<u>Telecommunications</u>				
1131	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [6/2021]	13,334.00 (-) [24,664.00]	16,594.00 (11,330.00) [71]
1132	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021 (-) [11/2021]	431.16 (431.00) [431.16]	0.00 (0.00) [5]
	<u>Urban Development</u>				
1133	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	2,987.00 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1134	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1135	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [12/2024]	2,326.52 (-) [6,911.00]	1,125.27 (4,584.48) [117]
	<u>Road Transport And Highways</u>				
1136	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	85.02 (0.00) [44]
1137	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	68.70 (0.00) [48]
1138	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	114.76 (-90.38) [0]
1139	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2020]	387.00 (-) [387.00]	260.08 (0.00) [0]
1140	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (336.49) [336.49]	71.11 (-163.60) [50]
1141	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	8.86 (0.00) [0]
1142	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	12.99 (0.00) [0]
1143	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-)	361.53 (-)	3.66 (0.00)

			[6/2022]	[361.53]	[0]
1144	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	11.24 (0.00) [0]
1145	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	1.50 (0.00) [0]
1146	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	41.64 (0.00) [0]
1147	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	87.30 (0.00) [0]
1148	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	5.29 (0.00) [0]
1149	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
1150	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	0.00 (0.00) [0]
1151	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	0.00 (0.00) [0]
1152	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	0.00 (0.00) [0]
1153	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
1154	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	114.91 (0.00) [46]
1155	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	80.78 (0.00) [39]
1156	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	95.34 (0.00) [39]
1157	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	83.20 (0.00) [38]
1158	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	60.55 (0.00) [39]
1159	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	36.80 (0.00) [49]
1160	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	42.55 (0.00) [50]
1161	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	111.04 (0.00) [0]
1162	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	95.97 (0.00) [0]
1163	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	290.94 (13.93) [57]

1164	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [339.55]	276.01 (-56.97) [57]
1165	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [5/2021]	429.52 (-) [340.00]	234.97 (-89.52) [57]
1166	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (9/2020) [0/0]	336.25 (369.96) [336.25]	301.49 (0.00) [0]
1167	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	98.42 (0.00) [0]
1168	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	123.44 (0.00) [0]
1169	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	0.00 (0.00) [0]
1170	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1171	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	50.27 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1172	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	168.13 (0.00) [108]
1173	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	278.53 (0.00) [60]
1174	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3/2017 (-) [3/2031]	3,145.45 (-) [3,145.45]	612.55 (0.00) [168]
1175	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	3/2010 (3/2029) [3/2029]	3,504.21 (3,504.21) [3,504.21]	607.83 (0.00) [228]
1176	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	3/2013 (3/2028) [3/2028]	8,416.19 (8,416.19) [8,416.19]	890.78 (0.00) [180]
1177	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2024]	1,375.38 (-) [1,375.38]	504.36 (0.00) [36]
1178	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2022]	479.53 (-) [479.53]	475.14 (0.00) [108]
1179	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	181.04 (0.00) [0]
1180	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,236.90 (0.00) [0]
1181	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,986.09 (0.00) [0]
1182	TALABIRA II AND III OCP	7/2017	7/2020 (-) [4/2020]	2,401.07 (-) [2,401.07]	843.87 (0.00) [0]
	<u>Human Resource Development</u>				
1183	INDIAN INSTITUTE OF SCIENCE EDUCATION AND	1/2019	3/2022	790.79	149.00

	RESEARCH BERHAMPUR		(-) [6/2022]	(-) [790.79]	(0.00) [3]
	<u>Mines</u>				
1184	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (12/2022) [12/2022]	5,540.00 (6,435.90) [5,540.00]	698.73 (0.00) [20]
1185	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [2/2021]	355.00 (-) [355.00]	93.85 (0.00) [3]
1186	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.74 (0.00) [0]
1187	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [0/0]	534.00 (-) [534.00]	332.12 (0.00) [0]
	<u>Petroleum</u>				
1188	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [8/2022]	1,607.00 (-) [1,607.00]	189.36 (0.00) [0]
1189	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	6.63 (0.00) [0]
1190	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [6/2021]	315.00 (-) [315.00]	196.27 (0.00) [-6]
1191	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	98.03 (0.00) [0]
1192	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	74.18 (0.00) [0]
1193	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,933.00 (-) [1,933.00]	1,231.50 (0.00) [12]
1194	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	2,561.15 (0.00) [0]
1195	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	1,568.98 (0.00) [0]
1196	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	1.73 (0.00) [0]
1197	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (-) [9/2022]	371.00 (-) [371.00]	1.93 (0.00) [0]
1198	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	77.55 (0.00) [0]
1199	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [3/2022]	161.59 (-) [161.59]	46.92 (0.00) [27]
1200	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [12/2021]	1,297.50 (-) [1,297.50]	589.44 (0.00) [2]
	<u>Power</u>				
1201	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (2/2021) [4/2021]	12,532.44 (13,140.91) [13,140.91]	11,641.13 (608.47) [28]
1202	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-)	1,885.13 (-)	1,746.41 (0.00)

			[3/2021]	[1,885.13]	[27]
	<u>Railways</u>				
1203	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,536.00]	1,089.84 (593.05) [39]
1204	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2024) [3/2024]	843.04 (843.04) [843.04]	208.46 (0.00) [41]
1205	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2024) [3/2024]	1,172.92 (1,172.92) [1,172.92]	596.91 (0.00) [63]
1206	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1207	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2024]	5,200.00 (-) [962.00]	54.75 (-4,238.00) [48]
1208	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [0/0]	1,185.64 (-) [1,844.47]	1,883.44 (658.83) [0]
1209	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2023]	1,547.38 (1,547.38) [1,547.38]	603.73 (0.00) [12]
1210	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (3/2024) [3/2024]	701.61 (810.02) [810.02]	171.45 (108.41) [64]
1211	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [0/0]	133.41 (207.00) [396.00]	388.21 (262.59) [0]
1212	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (3/2026) [3/2026]	2,923.13 (3,791.66) [3,791.66]	1,413.99 (868.53) [204]
1213	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	380.90 (0.00) [48]
1214	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [12/2021]	969.83 (1,312.96) [1,312.96]	857.47 (343.13) [21]
1215	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (3/2021) [3/2022]	155.81 (238.03) [238.03]	219.74 (82.22) [24]
1216	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [12/2021]	948.04 (-) [2,009.00]	1,764.93 (1,060.96) [21]
1217	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (12/2021) [12/2021]	1,111.99 (1,539.28) [1,539.28]	1,109.06 (427.29) [34]
1218	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,337.54 (1,237.83) [88]
1219	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (3/2025) [3/2025]	810.78 (1,928.07) [1,928.07]	845.24 (1,117.29) [45]
1220	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	1,225.51 (992.05) [24]
	<u>Road Transport And Highways</u>				
1221	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [3/2021]	1,282.94 (-) [1,282.94]	468.69 (0.00) [-]
1222	DEVELOPMENT OF FOUR LANNING OF ANGUL-	9/2016	8/2019	2,510.04	555.68

	SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S		(-) [3/2021]	(-) [2,510.04]	(0.00) [19]
1223	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/	752.28	213.52
			(-) [3/2022]	(-) [752.28]	(0.00) [-]
1224	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/	1,069.65	611.71
			(-) [1/2021]	(-) [1,069.65]	(0.00) [0]
1225	PANIKHOLI-RIMOLI	3/2012	9/2014	1,410.00	1,935.14
			(-) [0/0]	(-) [1,410.00]	(0.00) [0]
1226	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/	1,008.96	930.39
			(-) [6/2021]	(-) [1,008.96]	(0.00) [-]
1227	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/	564.66	240.00
			(-) [8/2021]	(-) [564.66]	(0.00) [-]
1228	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017	476.56	52.19
			(-) [6/2021]	(-) [476.56]	(0.00) [47]
1229	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/	633.68	63.98
			(-) [0/0]	(-) [633.68]	(0.00) [0]
1230	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/	953.09	332.04
			(-) [3/2022]	(-) [953.09]	(0.00) [-]
1231	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/	668.86	276.59
			(-) [6/2021]	(-) [668.86]	(0.00) [-]
1232	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/	614.48	217.40
			(-) [8/2021]	(-) [614.48]	(0.00) [-]
1233	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017	342.05	258.91
			(-) [0/0]	(-) [342.05]	(0.00) [0]
1234	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/	503.88	25.40
			(-) [6/2021]	(-) [503.88]	(0.00) [-]
1235	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020	1,288.07	842.24
			(-) [6/2021]	(-) [1,420.00]	(131.93) [15]
1236	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/	686.65	227.63
			(-) [6/2021]	(-) [686.65]	(0.00) [-]
1237	REHABILITATION AND UPGRADATION OF CUTTACK- ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/	686.65	261.74
			(-) [6/2021]	(-) [686.65]	(0.00) [-]
1238	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/	417.51	127.61
			(-) [6/2021]	(-) [417.51]	(0.00) [-]
1239	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017	342.05	258.91
			(-) [0/0]	(342.00) [342.00]	(-0.05) [0]
1240	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/	999.00	102.70
			(-) [6/2021]	(-) [999.00]	(0.00) [-]
1241	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016	171.96	88.30
			(-) [0/0]	(172.00) [172.00]	(0.04) [0]
1242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	10/2017	218.63	29.27
			(-)	(-)	(0.00)

	BHOJPUR-CHHATAB		[0/0]	[218.63]	[0]
1243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1244	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (-) [6/2021]	1,522.00 (-) [1,522.00]	304.40 (0.00) [-]
1245	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (3/2021) [3/2021]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [81]
1246	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	189.70 (0.00) [-]
1247	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	136.19 (0.50) [0]
1248	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1249	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1250	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1251	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	210.29 (0.00) [0]
1252	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	99.98 (0.00) [0]
1253	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1254	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1255	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1256	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1257	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1258	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1259	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	<u>Steel</u>				
1260	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023 (-) [5/2023]	377.18 (-) [377.18]	0.63 (0.00) [0]
	<u>PONDICHERRY</u>				
	<u>Health And Family Welfare</u>				
1261	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020 (-) [4/2022]	195.00 (-) [195.00]	16.41 (0.00) [19]

	PUNJAB				
	Fertilisers				
1262	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [2/2021]	218.83 (-) [218.83]	174.61 (0.00) [15]
1263	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [3/2021]	239.81 (-) [239.81]	185.55 (0.00) [16]
	Health And Family Welfare				
1264	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [7/2021]	703.00 (-) [557.48]	449.74 (-145.52) [13]
1265	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [4/2021]	152.95 (-) [177.92]	161.29 (24.97) [38]
	Human Resource Development				
1266	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022 (-) [8/2022]	348.24 (-) [348.24]	15.20 (0.00) [3]
1267	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [2/2022]	430.00 (-) [387.83]	180.63 (-42.17) [21]
1268	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [4/2021]	294.00 (-) [350.69]	265.91 (56.69) [24]
	Petroleum				
1269	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,244.50]	54.49 (-176.96) [0]
	Railways				
1270	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	226.25 (0.00) [108]
1271	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	Road Transport And Highways				
1272	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (-) [2,280.00]	1,282.04 (1,110.39) [0]
1273	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	795.00 (0.00) [0]
1274	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [12/2020]	889.24 (-) [904.82]	754.06 (15.58) [0]
1275	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [0/0]	1,388.34 (-) [2,587.50]	1,569.38 (1,199.16) [0]
1276	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [9/2021]	754.54 (-) [756.27]	352.32 (1.73) [18]
1277	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (-) [0/0]	766.36 (-) [766.36]	685.36 (0.00) [0]
1278	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-) [0/0]	447.29 (-) [746.43]	676.33 (299.14) [0]
1279	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [7/2021]	261.76 (-) [207.00]	193.26 (-54.76) [-]

1280	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	456.80
			(-)	(-)	(0.00)
			[7/2021]	[479.00]	[-]
1281	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019	1,069.59	678.17
			(-)	(-)	(0.00)
			[12/2020]	[1,069.59]	[0]
1282	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/	196.05	143.03
			(-)	(-)	(0.00)
			[0/0]	[196.05]	[0]
1283	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/	199.90	124.52
			(-)	(-)	(0.00)
			[0/0]	[199.90]	[0]
1284	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020	170.57	44.68
			(-)	(-)	(0.00)
			[5/2021]	[170.57]	[6]
1285	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020	173.24	114.55
			(-)	(-)	(0.00)
			[0/0]	[173.24]	[0]
1286	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020	322.48	261.72
			(-)	(-)	(0.00)
			[8/2021]	[322.48]	[13]
1287	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	28.24
			(-)	(-)	(0.00)
			[0/0]	[293.64]	[0]
1288	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	237.13
			(-)	(-)	(0.00)
			[0/0]	[293.64]	[0]
1289	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020	293.10	155.65
			(-)	(-)	(0.00)
			[0/0]	[293.10]	[0]
1290	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/	892.17	648.44
			(-)	(-)	(0.00)
			[0/0]	[892.17]	[0]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1291	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12,320.00	12,992.00
			(-)	(-)	(4,759.00)
			[3/2023]	[17,079.00]	[75]
	<u>Coal</u>				
1292	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020	2,112.60	158.25
			(-)	(-)	(0.00)
			[0/0]	[2,112.60]	[0]
1293	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019	513.63	175.30
			(-)	(-)	(0.00)
			[0/0]	[513.63]	[0]
1294	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020	2,196.30	173.83
			(-)	(-)	(0.00)
			[0/0]	[2,196.30]	[0]
1295	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019	522.45	9.88
			(-)	(-)	(0.00)
			[0/0]	[522.45]	[0]
	<u>Human Resource Development</u>				
1296	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019	549.31	458.38
			(-)	(-)	(10.16)
			[3/2021]	[559.47]	[20]
	<u>Petroleum</u>				
1297	LPG BP PROJECT JODHPUR	3/2018	/	229.80	80.21
			(5/2022)	(-)	(0.00)
			[5/2022]	[229.80]	[-]
	<u>Power</u>				
1298	FATEHGARH SOLAR 296MW	3/2020	9/2021	1,749.31	0.00

			(-) [9/2021]	(-) [1,749.31]	(0.00) [0]
1299	JETSAR SOLAR 160 MW	12/2019	3/2021 (-) [3/2021]	702.28 (-) [702.28]	0.00 (0.00) [0]
1300	SAMBHU KI BHURJ SOLAR 250 MW	1/2020	9/2021 (-) [9/2021]	1,522.71 (-) [1,522.71]	0.00 (0.00) [0]
1301	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (-) [9/2021]	1,782.00 (-) [1,782.00]	0.00 (0.00) [0]
	<u>Railways</u>				
1302	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,980.21]	4.60 (1,106.50) [0]
1303	AJMER-BANGURGRAM	4/2011	11/2019 (-) [3/2021]	213.39 (-) [375.00]	337.30 (161.61) [16]
1304	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.00]	0.00 (277.00) [0]
1305	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [2/2020]	242.09 (-) [525.00]	459.43 (282.91) [0]
1306	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [2/2021]	246.08 (-) [395.00]	324.37 (148.92) [14]
1307	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [11/2021]	410.08 (-) [860.41]	691.34 (450.33) [33]
1308	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [6/2022]	808.85 (-) [808.85]	167.74 (0.00) [-2]
1309	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2021]	420.18 (-) [420.18]	307.78 (0.00) [15]
1310	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [0/0]	493.17 (-) [493.17]	464.53 (0.00) [0]
1311	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1312	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [0/0]	236.93 (-) [350.45]	251.41 (113.52) [0]
	<u>Road Transport And Highways</u>				
1313	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [8/2022]	370.36 (-) [370.36]	90.45 (0.00) [0]
1314	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	587.64 (0.00) [0]
1315	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [0]
1316	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [0/0]	688.70 (-) [688.70]	880.00 (0.00) [0]
1317	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [9/2021]	1,031.95 (-) [1,031.95]	374.05 (0.00) [-]

1318	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/	178.13	139.26
			(-)	(-)	(0.00)
			[3/2021]	[178.13]	[-]
1319	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018	822.90	1,688.16
			(-)	(-)	(0.00)
			[0/0]	[822.90]	[0]
1320	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/	1,158.35	611.28
			(-)	(-)	(0.00)
			[0/0]	[1,158.35]	[0]
1321	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018	163.95	116.47
			(-)	(-)	(0.00)
			[3/2021]	[163.95]	[35]
1322	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/	716.76	610.56
			(-)	(-)	(0.00)
			[0/0]	[716.76]	[0]
1323	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/	741.86	119.02
			(-)	(-)	(0.00)
			[0/0]	[741.86]	[0]
1324	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/	1,308.73	330.46
			(-)	(-)	(0.00)
			[0/0]	[1,308.73]	[0]
1325	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019	763.23	191.80
			(-)	(-)	(0.00)
			[0/0]	[763.23]	[0]
1326	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019	649.00	546.54
			(-)	(-)	(0.00)
			[0/0]	[649.00]	[0]
1327	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017	964.17	773.03
			(-)	(-)	(0.00)
			[11/2020]	[964.17]	[0]
1328	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011	1,673.70	3,326.93
			(-)	(-)	(0.00)
			[0/0]	[1,673.70]	[0]
1329	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013	511.00	492.00
			(-)	(-)	(0.00)
			[0/0]	[511.00]	[0]
1330	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013	511.00	2,323.04
			(-)	(-)	(0.00)
			[0/0]	[511.00]	[0]
1331	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020	196.23	0.00
			(-)	(-)	(-0.23)
			[8/2022]	[196.00]	[21]
1332	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014	278.87	0.00
			(-)	(-)	(0.00)
			[0/0]	[278.87]	[0]
1333	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014	376.52	0.00
			(-)	(-)	(0.00)
			[0/0]	[376.52]	[0]
1334	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/	1,100.19	1,304.00
			(-)	(-)	(45.12)
			[3/2021]	[1,145.31]	[-]
1335	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/	1,239.82	1,674.80
			(-)	(-)	(487.84)
			[1/2021]	[1,727.66]	[0]
1336	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020	894.00	810.00
			(-)	(-)	(35.32)
			[7/2021]	[929.32]	[15]
1337	TWO LANING WITH PAVED SHOULDER OF KARAU II - DHOLPUR	9/2014	9/2016	425.19	276.40
			(-)	(-)	(0.00)
			[0/0]	[425.19]	[0]
1338	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA	8/2015	/	275.90	289.13

	- ROPPAS -DHOLPUR		(-) [0/0]	(-) [275.90]	(0.00) [0]
1339	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1340	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	550.35 (0.00) [0]
1341	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO	3/2020	8/2020 (-) [8/2022]	255.23 (-) [255.23]	1.66 (0.00) [24]
1342	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	886.59 (0.00) [0]
1343	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [4/2021]	370.30 (-) [370.30]	290.00 (0.00) [34]
1344	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	673.70 (0.00) [0]
1345	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [6/2021]	341.79 (-) [341.79]	208.00 (0.00) [37]
1346	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1347	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	244.68 (0.00) [0]
1348	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1349	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	387.22 (0.00) [0]
1350	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [3/2021]	187.82 (-) [187.82]	131.74 (0.00) [35]
	SIKKIM				
	Railways				
1351	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [12/2023]	1,339.48 (4,084.69) [8,600.00]	619.18 (7,260.52) [96]
	Road Transport And Highways				
1352	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	0.00 (0.00) [0]
1353	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	0.00 (0.00) [0]
1354	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (12/2020) [0/0]	182.28 (369.64) [269.14]	274.07 (86.86) [0]
1355	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (12/2020) [0/0]	151.59 (370.01) [151.59]	282.36 (0.00) [0]
1356	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (12/2020) [0/0]	166.27 (359.92) [166.27]	243.59 (0.00) [0]
1357	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000	3/2017	/ (-)	375.80 (-)	107.98 (0.00)

	TO KM 16.00		[0/0]	[375.80]	[0]
1358	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	24.70 (0.00) [0]
1359	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
1360	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	11.03 (0.00) [0]
1361	CONSTUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	0.78 (0.00) [0]
1362	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	0.00 (0.00) [0]
1363	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	0.00 (0.00) [0]
1364	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	255.15 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1365	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	23,131.00 (0.00) [36]
1366	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [10/2022]	3,492.00 (5,677.00) [6,840.00]	5,915.80 (3,348.00) [145]
	<u>Civil Aviation</u>				
1367	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (-) [3/2023]	380.87 (-) [380.87]	0.00 (0.00) [12]
1368	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [9/2022]	2,467.00 (-) [2,467.00]	303.07 (0.00) [7]
1369	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [3/2022]	951.28 (-) [951.28]	249.79 (0.00) [5]
	<u>Coal</u>				
1370	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (3/2025) [0/0]	1,458.17 (709.06) [709.06]	483.91 (-749.11) [0]
1371	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (7,980.79) [7,980.79]	7,404.29 (2,073.68) [62]
	<u>Finance</u>				
1372	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [4/2021]	209.00 (-) [208.96]	205.40 (-0.04) [18]
1373	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	113.99 (0.00) [0]
	<u>Mines</u>				
1374	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (6/2021) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [0]
	<u>Petroleum</u>				
1375	AUGMENTATION OF CTMPL	12/2016	11/2021 (-)	228.00 (-)	125.61 (0.00)

			[11/2021]	[228.00]	[0]
1376	BS-VI PROJECTS	9/2017	12/2019 (-) [1/2021]	1,858.00 (-) [1,858.00]	1,528.75 (0.00) [0]
1377	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [9/2023]	921.00 (-) [921.00]	3.05 (0.00) [0]
1378	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	185.01 (0.00) [10]
1379	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2022]	4,497.00 (-) [6,025.00]	3,409.77 (1,528.00) [38]
1380	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1381	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2021) [5/2021]	650.82 (-) [624.35]	446.46 (-26.47) [26]
1382	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [8/2022]	678.00 (1,472.00) [1,472.00]	17.80 (794.00) [66]
1383	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [9/2021]	421.00 (-) [300.00]	241.01 (-121.00) [13]
1384	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [12/2023]	1,398.00 (-) [1,398.00]	75.59 (0.00) [0]
	<u>Power</u>				
1385	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (-) [9/2021]	1,316.22 (-) [1,316.22]	0.00 (0.00) [0]
1386	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (4/2021) [4/2021]	186.17 (219.66) [219.66]	157.07 (33.49) [21]
	<u>Railways</u>				
1387	ATTIPPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [238.00]	153.70 (-19.00) [0]
1388	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [527.37]	3.34 (375.53) [0]
1389	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (2/2021) [4/2021]	931.98 (-) [1,121.00]	906.57 (189.02) [-]
1390	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [3/2024]	198.68 (-) [559.95]	319.22 (361.27) [-]
1391	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1392	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [12/2021]	495.74 (-) [734.01]	481.29 (238.27) [102]
1393	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2022]	760.00 (-) [1,536.00]	1,233.08 (776.00) [27]
1394	MADURAI-BODINAYAKKANUR	4/2008	/ (10/2021) [9/2021]	164.41 (-) [600.30]	355.13 (435.89) [-]
1395	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022	1,700.00	756.45

			(-) [6/2022]	(-) [1,305.00]	(-395.00) [3]
1396	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [2,910.84]	1,597.41 (2,186.15) [73]
1397	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (3/2021) [12/2020]	187.26 (-) [332.00]	265.41 (144.74) [0]
1398	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]
1399	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [9/2021]	268.87 (-) [950.00]	928.36 (681.13) [198]
1400	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [12/2025]	582.83 (-) [582.83]	239.11 (0.00) [-]
1401	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [227.40]	63.90 (0.00) [0]
1402	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2025]	303.98 (-) [1,720.00]	697.29 (1,416.02) [60]
1403	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	<u>Road Transport And Highways</u>				
1404	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	8.56 (0.00) [0]
1405	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	182.00 (0.00) [0]
1406	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	561.03 (0.00) [58]
1407	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/	5/2016	1/2017 (-) [0/0]	307.70 (-) [307.70]	312.82 (0.00) [0]
1408	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	223.10 (9.95) [0]
1409	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	140.64 (0.00) [0]
1410	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [10/2020]	600.00 (-) [600.00]	1.65 (0.00) [0]
1411	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [7/2021]	1,016.92 (-) [1,071.00]	196.87 (54.08) [-]
1412	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [0/0]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1413	FOUR LANING OF MADURAI- CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [9/2021]	628.71 (-) [628.71]	303.46 (0.00) [-]
1414	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1415	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON	2/2018	/	1,166.26	220.78

	NH-227 IN THE STATE OF TAMIL NADU		(-) [7/2021]	(-) [1,166.26]	(0.00) [-]
1416	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [2/2021]	641.17 (-) [641.17]	394.32 (0.00) [55]
1417	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [5/2021]	505.35 (-) [505.35]	240.60 (0.00) [-]
1418	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	453.70 (0.00) [59]
1419	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2021]	707.82 (-) [707.82]	419.77 (0.00) [31]
1420	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [12/2021]	848.45 (932.23) [848.45]	219.00 (0.00) [21]
1421	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [2/2021]	641.17 (-) [641.17]	394.32 (0.00) [31]
1422	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	7/2020	12/2021 (-) [12/2021]	3,426.00 (-) [3,426.00]	0.00 (0.00) [0]
1423	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	146.79 (4.82) [0]
1424	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [0/0]	379.90 (-) [379.90]	187.16 (0.00) [0]
1425	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,337.06 (0.00) [0]
1426	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1427	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1428	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [8/2021]	374.00 (-) [166.90]	49.53 (-207.10) [99]
1429	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1430	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	93.53 (0.00) [0]
1431	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (-) [240.38]	74.56 (0.00) [0]
1432	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	45.52 (0.00) [0]
1433	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/	1/2016	9/2016 (-) [0/0]	162.72 (-) [162.72]	136.46 (0.00) [0]
	<u>Urban Development</u>				
1434	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [3/2021]	3,770.00 (-) [3,770.00]	2,932.59 (0.00) [36]
1435	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015	14,600.00	16,365.87

			(-) [0/0]	(-) [19,058.00]	(4,458.00) [0]
	<u>TELANGANA</u>				
	<u>Civil Aviation</u>				
1436	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (-) [5/2022]	353.61 (-) [353.61]	0.00 (0.00) [0]
	<u>Coal</u>				
1437	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2022]	447.06 (-) [473.22]	21.17 (26.16) [84]
1438	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	169.95 (0.00) [36]
1439	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2022]	397.09 (-) [442.42]	106.68 (45.33) [36]
1440	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2022]	417.33 (-) [384.32]	124.04 (-33.01) [68]
1441	KISTARAM OCP	11/2010	3/2015 (-) [3/2022]	242.29 (-) [164.04]	129.58 (-78.25) [84]
1442	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	416.07 (70.65) [132]
1443	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2022]	162.76 (-) [349.28]	292.49 (186.52) [84]
1444	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2021]	430.45 (-) [415.37]	193.33 (-15.08) [60]
1445	SRP OC-II EXPANSION PROJECT	11/2016	/ (-) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [-]
	<u>Health And Family Welfare</u>				
1446	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	123.92 (0.00) [14]
	<u>Petroleum</u>				
1447	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	65.87 (0.00) [16]
	<u>Power</u>				
1448	RAMAGUNDAM FLOATING SOLAR 100 MW	6/2019	4/2021 (-) [4/2021]	401.90 (-) [401.90]	0.00 (0.00) [0]
1449	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (3/2022) [3/2022]	10,598.98 (-) [10,598.98]	8,125.04 (0.00) [16]
	<u>Railways</u>				
1450	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2021]	632.68 (-) [950.00]	799.01 (317.32) [69]
1451	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	535.71 (0.00) [0]
1452	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [12/2022]	119.73 (185.00) [449.39]	7.09 (329.66) [9]
1453	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010	1,160.48	478.70

			(-) [3/2024]	(-) [1,160.48]	(0.00) [168]
1454	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92
			(-) [0/0]	(-) [2,911.84]	(1,799.84) [0]
1455	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [850.00]	705.50 (76.06) [0]
	<u>Road Transport And Highways</u>				
1456	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [0/0]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [0]
1457	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [0/0]	283.15 (-) [283.15]	97.89 (0.00) [0]
1458	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [0/0]	626.76 (-) [626.76]	170.17 (0.00) [0]
1459	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.95 (0.00) [0]
1460	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1461	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/	857.62	144.31
			(-) [0/0]	(-) [857.62]	(0.00) [0]
1462	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/	802.65	380.39
			(-) [0/0]	(-) [802.65]	(0.00) [0]
1463	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/	950.63	462.38
			(-) [0/0]	(-) [950.63]	(0.00) [0]
1464	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/	828.29	0.00
			(-) [0/0]	(-) [828.29]	(0.00) [0]
1465	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [3/2021]	1,423.96 (-) [1,056.08]	970.12 (-367.88) [28]
1466	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [0/0]	192.67 (-) [192.67]	146.55 (0.00) [0]
1467	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [0/0]	605.08 (-) [605.08]	394.25 (0.00) [0]
1468	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [0/0]	426.52 (-) [426.52]	385.12 (0.00) [0]
1469	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1470	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [0/0]	294.13 (-) [294.13]	109.06 (0.00) [0]
1471	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	118.67 (0.00) [0]
1472	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [0/0]	322.81 (-) [322.81]	77.17 (0.00) [0]
1473	WIDEINING TO TWO/FOUR LANE WITH PAVED	10/2016	3/2019	248.83	113.83

	SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ		(-) [0/0]	(-) [248.83]	(0.00) [0]
1474	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [0/0]	298.32 (-) [298.32]	112.37 (0.00) [0]
1475	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [0/0]	230.03 (-) [230.03]	171.39 (0.00) [0]
1476	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [0/0]	206.13 (-) [206.13]	171.39 (0.00) [0]
1477	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	91.71 (0.00) [0]
1478	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	106.43 (0.00) [0]
1479	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	222.84 (0.00) [0]
1480	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	162.42 (0.00) [0]
1481	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	293.94 (0.00) [0]
1482	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	168.63 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1483	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [0/0]	438.28 (-) [438.28]	335.58 (0.00) [0]
	<u>Railways</u>				
1484	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
1485	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	357.19 (0.00) [0]
1486	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	0.00 (0.00) [0]
1487	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	0.00 (0.00) [0]
1488	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	0.00 (0.00) [0]
1489	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	0.00 (0.00) [0]
1490	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	0.00 (0.00) [0]
1491	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [197.67]	5.75 (0.00) [0]
1492	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C.	10/2016	8/2020	171.90	110.19

	GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C		(7/2021) [7/2021]	(-) [171.90]	(0.00) [11]
	<u>Rural Development</u>				
1493	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [3/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [63]
1494	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [3/2021]	202.61 (227.00) [207.12]	190.22 (4.51) [51]
1495	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [3/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [51]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1496	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2022]	1,383.00 (-) [1,383.00]	369.66 (0.00) [12]
	<u>Coal</u>				
1497	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (7/2022) [7/2022]	17,237.00 (-) [17,237.80]	11,135.69 (0.80) [8]
	<u>Health And Family Welfare</u>				
1498	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [7/2021]	785.00 (-) [715.06]	524.06 (-69.94) [15]
1499	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [3/2021]	268.84 (-) [268.84]	239.89 (0.00) [-]
	<u>Human Resource Development</u>				
1500	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [6/2021]	171.72 (-) [171.72]	53.94 (0.00) [15]
	<u>Petroleum</u>				
1501	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	398.94 (0.00) [0]
1502	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (345.15) [345.15]	196.18 (57.66) [0]
1503	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (-) [3/2029]	3,450.20 (-) [3,450.20]	153.20 (0.00) [0]
1504	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (-) [4/2021]	217.92 (-) [217.92]	76.80 (0.00) [0]
1505	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (11/2021) [11/2021]	255.40 (-) [255.40]	17.21 (0.00) [15]
1506	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	688.49 (0.00) [0]
1507	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	136.81 (0.00) [3]
	<u>Power</u>				
1508	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (1/2021) [1/2021]	587.44 (-) [587.44]	463.48 (0.00) [0]
1509	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (4/2021) [4/2021]	349.00 (-) [349.00]	226.00 (0.00) [5]

1510	DEVIKOT SOLAR 150MW	1/2020	9/2021 (1/2022) [1/2022]	798.24 (-) [798.24]	31.64 (0.00) [4]
1511	DEVIKOT SOLAR 90MW	3/2020	9/2021 (1/2022) [1/2022]	501.29 (-) [501.29]	49.76 (0.00) [4]
1512	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	1,432.11 (0.00) [11]
1513	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [1/2021]	9,750.89 (-) [12,176.28]	11,130.00 (2,425.39) [0]
1514	NOKHRA	3/2020	9/2021 (1/2022) [1/2022]	1,722.14 (-) [1,722.14]	103.85 (0.00) [4]
1515	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (3/2021) [3/2021]	9,188.98 (-) [10,016.10]	7,966.63 (827.12) [20]
	<u>Railways</u>				
1516	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1517	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	199.70 (-233.29) [2]
1518	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1519	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,825.00]	1,411.49 (641.75) [24]
1520	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [12/2023]	602.50 (-) [714.34]	63.70 (111.84) [-]
1521	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1522	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1523	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1524	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1525	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	44.84 (0.35) [68]
1526	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	809.66 (0.00) [0]
1527	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	33.37 (0.00) [0]
1528	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1529	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2022]	528.57 (-) [528.57]	217.40 (0.00) [36]

1530	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [6/2022]	927.01 (-) [1,400.00]	1,302.29 (472.99) [39]
1531	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	446.65 (0.00) [0]
1532	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [0/0]	668.70 (668.00) [680.00]	330.00 (11.30) [0]
1533	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	833.10 (0.00) [21]
1534	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1535	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1536	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [3/2021]	622.50 (427.00) [426.74]	476.60 (-195.76) [47]
1537	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,111.96 (0.00) [48]
1538	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,295.42]	929.79 (0.00) [0]
1539	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	80.76 (-149.01) [16]
1540	UNCHAHAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,265.00]	103.72 (36.00) [-]
1541	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [1,000.00]	688.03 (56.40) [33]
Road Transport And Highways					
1542	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	239.04 (0.00) [0]
1543	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1544	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (12/2020) [12/2020]	351.34 (417.68) [417.68]	433.68 (66.34) [0]
1545	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (1/2020) [1/2020]	495.78 (627.93) [627.93]	633.24 (132.15) [0]
1546	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (12/2020) [12/2020]	291.36 (469.31) [469.31]	459.07 (177.95) [0]
1547	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1548	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,118.92 (211.43) [0]
1549	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [8/2020]	1,668.00 (-) [1,668.00]	946.08 (0.00) [0]

1550	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1551	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [0/0]	1,408.00 (-) [1,408.00]	442.70 (0.00) [0]
1552	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [0/0]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [0]
1553	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	2,977.58 (0.00) [0]
1554	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1555	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1556	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [0/0]	1,657.20 (-) [1,657.20]	2,345.00 (0.00) [0]
1557	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,357.84 (382.01) [0]
1558	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	43.23 (0.00) [0]
1559	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	977.26 (0.00) [0]
1560	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1561	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1562	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1563	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1564	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1565	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1566	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [0/0]	1,081.57 (-) [1,057.60]	549.07 (-23.97) [0]
1567	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,087.00]	812.83 (-145.21) [0]
1568	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [0/0]	1,989.00 (-) [1,989.00]	756.92 (0.00) [0]
1569	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]
1570	FOR REHABILITATION AND UPGRADATION FROM 2-LANE	2/2018	/	670.50	263.74

	TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP		(-) [0/0]	(-) [670.50]	(0.00) [0]
1571	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/	809.07	517.66
			(-) [0/0]	(-) [809.07]	(0.00) [0]
1572	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/	925.40	1,011.70
			(-) [0/0]	(-) [1,197.00]	(271.60) [0]
1573	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018	667.00	549.07
			(-) [0/0]	(-) [667.00]	(0.00) [0]
1574	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018	667.00	464.05
			(-) [0/0]	(-) [667.00]	(0.00) [0]
1575	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018	1,027.53	601.13
			(-) [0/0]	(-) [1,027.53]	(0.00) [0]
1576	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018	815.28	520.89
			(-) [0/0]	(-) [815.28]	(0.00) [0]
1577	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017	261.09	240.96
			(-) [0/0]	(-) [261.09]	(0.00) [0]
1578	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	3/2018	8/2020	288.30	120.37
			(-) [3/2021]	(-) [288.30]	(0.00) [7]
1579	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020	1,373.28	974.57
			(-) [0/0]	(-) [1,373.28]	(0.00) [0]
1580	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020	1,184.71	1,039.23
			(-) [0/0]	(-) [1,310.00]	(125.29) [0]
1581	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019	899.00	641.51
			(-) [0/0]	(-) [899.00]	(0.00) [0]
1582	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013	1,141.00	1,715.42
			(-) [0/0]	(-) [1,141.00]	(0.00) [0]
1583	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/	281.45	0.00
			(-) [0/0]	(-) [281.45]	(0.00) [0]
1584	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	11/2018	12/2020	281.45	72.05
			(-) [6/2021]	(-) [281.45]	(0.00) [6]
1585	MEERUT-BULANDSHAHR	1/2016	/	683.24	867.27
			(-) [0/0]	(-) [987.94]	(304.70) [0]
1586	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019	209.10	201.46
			(-) [6/2020]	(-) [209.10]	(0.00) [0]
1587	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/	326.99	74.00
			(-) [9/2021]	(327.00) [326.99]	(0.00) [-]
1588	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020	296.50	172.63
			(-) [3/2021]	(-) [296.50]	(0.00) [6]
1589	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/	1,025.80	461.52
			(-) [0/0]	(-) [677.07]	(-348.73) [0]
1590	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR	3/2018	/	1,115.28	623.03
			(-)	(-)	(-345.24)

	DAGAMAGPUR-LA		[0/0]	[770.04]	[0]
1591	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	2/2019 (-) [0/0]	239.63 (-) [239.63]	212.53 (0.00) [0]
1592	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [0/0]	388.83 (-) [388.83]	304.70 (0.00) [0]
1593	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2021]	263.89 (-) [242.05]	181.21 (-21.84) [12]
1594	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [2/2021]	208.50 (-) [208.50]	165.82 (0.00) [15]
1595	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [0/0]	445.89 (653.00) [653.29]	469.64 (207.40) [0]
1596	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [0/0]	599.34 (-) [599.34]	492.15 (0.00) [0]
1597	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [1/2021]	185.18 (-) [185.18]	124.43 (0.00) [0]
1598	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [2/2021]	249.50 (-) [249.50]	205.40 (0.00) [21]
1599	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [2/2021]	218.90 (-) [218.90]	129.75 (0.00) [11]
1600	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1601	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [0/0]	215.16 (215.00) [215.16]	160.61 (0.00) [0]
1602	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [3/2021]	240.30 (240.00) [240.30]	200.10 (0.00) [14]
1603	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [0/0]	218.94 (219.00) [218.94]	120.69 (0.00) [0]
1604	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [0/0]	176.94 (177.00) [176.94]	141.11 (0.00) [0]
1605	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [2/2021]	208.88 (-) [208.88]	168.68 (0.00) [16]
1606	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [653.29]	464.05 (207.40) [0]
1607	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	1,363.84 (0.00) [0]
1608	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,344.09 (0.00) [0]
1609	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [3/2023]	724.60 (-) [724.60]	0.00 (0.00) [0]
1610	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]

1611	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [1/2021]	164.54 (165.00) [164.54]	141.33 (0.00) [0]
1612	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	128.54 (0.00) [0]
	<u>Steel</u>				
1613	FORGED WHEEL PLANT	4/2014	9/2018 (3/2021) [3/2021]	1,682.85 (-) [1,682.85]	1,552.60 (0.00) [30]
	<u>Urban Development</u>				
1614	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	8,379.62 (-) [8,379.62]	0.00 (0.00) [0]
1615	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	11,076.48 (-) [11,076.48]	0.00 (0.00) [0]
1616	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>Water Resources</u>				
1617	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [3/2022]	213.62 (-) [213.62]	0.00 (0.00) [0]
1618	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS	3/2018	9/2021 (-) [9/2021]	904.00 (-) [904.00]	56.74 (0.00) [0]
1619	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	21.10 (0.00) [0]
1620	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [234.03]	0.00 (2.24) [0]
1621	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1622	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [6/2022]	298.12 (-) [298.12]	0.00 (0.00) [11]
1623	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	32.47 (0.00) [0]
1624	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [5/2021]	460.45 (-) [460.45]	106.27 (0.00) [5]
1625	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	2/2017	11/2019 (-) [3/2021]	161.31 (-) [161.31]	50.65 (0.00) [16]
1626	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [681.78]	0.00 (0.00) [0]
1627	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [1/2021]	279.91 (-) [279.91]	222.79 (0.00) [0]
1628	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	8/2020 (3/2021) [3/2021]	370.40 (-) [370.40]	361.93 (0.00) [7]
1629	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2021]	967.23 (-) [967.23]	54.21 (0.00) [0]
	<u>UTTARAKHAND</u>				

	Civil Aviation				
1630	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [7/2021]	456.86 (-) [456.86]	203.76 (0.00) [10]
	Petroleum				
1631	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [6/2021]	160.10 (-) [160.10]	85.89 (0.00) [16]
	Power				
1632	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.21 (274.07) [0]
1633	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	524.12 (0.00) [0]
1634	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [12/2022]	2,978.48 (5,867.38) [5,867.38]	4,841.21 (2,888.90) [117]
1635	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2023]	2,491.58 (-) [3,860.35]	2,161.90 (1,368.77) [126]
	Railways				
1636	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	204.53 (126.80) [0]
1637	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1638	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [22,716.11]	2,768.76 (6,500.11) [3]
	Road Transport And Highways				
1639	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	124.74 (0.00) [0]
1640	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	144.90 (0.00) [0]
1641	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [0/0]	605.84 (-) [722.46]	722.46 (116.62) [0]
1642	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [8/2020]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [0]
1643	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	55.50 (0.00) [0]
1644	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	196.35 (0.00) [0]
1645	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [0/0]	248.00 (-) [248.00]	0.00 (0.00) [0]
1646	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [0/0]	720.00 (-) [720.00]	348.16 (0.00) [0]
1647	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [12/2020]	478.51 (-) [478.00]	315.11 (-0.51) [0]
1648	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED	11/2017	11/2019 (-)	232.81 (-)	59.44 (0.00)

	SHOULDERS CONFIG		[0/0]	[232.81]	[0]
1649	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [0/0]	283.51 (-) [283.51]	126.38 (0.00) [0]
1650	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	257.34 (-) [257.34]	62.79 (0.00) [0]
1651	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [0/0]	282.08 (-) [282.08]	77.05 (0.00) [0]
1652	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	200.34 (-) [200.34]	31.00 (0.00) [0]
1653	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [0/0]	418.88 (-) [418.88]	88.00 (0.00) [0]
1654	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	266.52 (-) [266.52]	144.27 (0.00) [0]
1655	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [0/0]	234.88 (-) [208.89]	118.26 (-25.99) [0]
1656	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1657	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1658	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [0/0]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1659	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]
	<u>Water Resources</u>				
1660	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (3/2021) [3/2021]	158.00 (-) [158.00]	77.81 (0.00) [16]
1661	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	3/2017	8/2019 (-) [0/0]	273.37 (-) [273.37]	71.53 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1662	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (-) [10/2022]	389.71 (-) [389.71]	37.38 (0.00) [11]
1663	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (-) [6/2021]	458.00 (-) [458.00]	105.12 (0.00) [15]
	<u>Coal</u>				
1664	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [10/2021]	304.13 (341.22) [341.22]	30.15 (37.09) [55]
1665	EXPANSION PR OF JHANJRA UG(5.00 MTY)	11/2015	3/2022 (3/2029) [3/2029]	1,210.12 (-) [1,210.12]	20.92 (0.00) [84]
1666	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	10.11 (0.00) [0]
1667	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027	826.42	0.03

			(-) [3/2027]	(-) [826.42]	(0.00) [0]
1668	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [0/0]	2,661.73 (-) [5,146.48]	591.17 (2,484.75) [0]
1669	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	0.00 (0.00) [0]
1670	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	1.39 (0.00) [0]
1671	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2021]	1,055.05 (-) [1,055.05]	641.54 (0.00) [36]
1672	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.50 (0.00) [0]
	<u>Health And Family Welfare</u>				
1673	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1674	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1675	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [6/2021]	651.99 (-) [651.99]	455.70 (0.00) [-]
1676	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2021]	355.15 (-) [355.15]	280.39 (0.00) [24]
	<u>Home Affairs</u>				
1677	NSG AT KOLKATA	10/2014	4/2018 (12/2021) [12/2021]	162.88 (238.00) [238.00]	170.35 (75.12) [44]
	<u>Human Resource Development</u>				
1678	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [0/0]	193.83 (-) [193.83]	0.45 (0.00) [0]
	<u>Petroleum</u>				
1679	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [3/2022]	3,712.00 (-) [3,696.00]	1,793.18 (-16.00) [-6]
1680	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (-) [3/2031]	5,830.20 (-) [5,830.20]	14.63 (0.00) [0]
1681	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,740.00 (-) [1,740.00]	778.20 (0.00) [12]
1682	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	55.17 (0.00) [0]
1683	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [10/2021]	163.02 (-) [163.02]	88.03 (0.00) [18]
	<u>Power</u>				
1684	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [5/2021]	529.68 (-) [529.68]	410.98 (0.00) [30]
1685	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (3/2021) [3/2021]	454.11 (-) [454.11]	343.03 (0.00) [35]

1686	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (11/2022) [12/2024]	1,381.84 (-) [1,381.54]	649.64 (-0.30) [63]
	Railways				
1687	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (1,966.70) [2,373.00]	485.04 (1,345.60) [324]
1688	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [3/2025]	1,106.62 (-) [1,091.59]	970.10 (-15.03) [171]
1689	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	239.06 (16.56) [-]
1690	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1691	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1692	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1693	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1694	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [0/0]	221.42 (-) [380.00]	38.20 (158.58) [0]
1695	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [0/0]	297.32 (200.34) [614.00]	275.07 (316.68) [0]
1696	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,090.60]	1,087.60 (710.00) [0]
1697	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [4/2021]	602.27 (-) [760.00]	801.53 (157.73) [-8]
1698	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1699	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	1,072.08 (1,725.49) [108]
1700	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1701	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,676.61 (307.50) [108]
1702	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	903.03 (430.57) [72]
1703	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
	Road Transport And Highways				
1704	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (-) [1,827.15]	2,082.19 (744.15) [0]
1705	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-)	998.79 (-)	1,858.57 (0.00)

			[3/2022]	[998.79]	[103]
1706	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [5/2021]	1,078.84 (-) [1,078.84]	2,239.99 (0.00) [93]
1707	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [0]
1708	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [0/0]	361.15 (-) [363.93]	272.98 (2.78) [0]
1709	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [11/2022]	160.27 (213.97) [213.97]	24.14 (53.70) [39]
1710	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [0/0]	229.37 (-) [229.37]	130.72 (0.00) [0]
1711	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [12/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [28]
1712	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [3/2021]	254.30 (254.30) [254.30]	79.69 (0.00) [5]
1713	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [0/0]	767.03 (-) [767.03]	604.65 (0.00) [0]
1714	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	682.36 (120.10) [0]
1715	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	807.99 (114.56) [0]
1716	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [7/2021]	1,261.98 (-) [1,952.20]	934.06 (690.22) [-]
1717	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (1/2020) [2/2020]	279.70 (398.52) [398.52]	330.94 (118.82) [0]
1718	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (11/2020) [5/2021]	396.86 (396.86) [396.86]	242.95 (0.00) [20]
1719	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1720	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [2,360.65]	4,472.01 (695.65) [0]
1721	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [0/0]	202.69 (202.69) [202.69]	144.89 (0.00) [0]
1722	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (4/2020) [4/2021]	218.70 (218.70) [218.70]	103.81 (0.00) [5]
1723	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [12/2021]	426.18 (426.18) [426.18]	242.25 (0.00) [15]
	Steel				
1724	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (3/2021) [5/2021]	263.36 (-) [263.36]	177.74 (0.00) [8]
	Water Resources				
1725	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019	274.76	198.28

			(5/2021) [5/2021]	(-) [274.76]	(0.00) [17]
1726	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1727	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1728	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]
1729	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [2/2022]	160.00 (-) [160.00]	0.00 (0.00) [0]
1730	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1731	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	0.00 (0.00) [0]
1732	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [2/2022]	198.43 (-) [198.43]	0.00 (0.00) [0]
1733	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1734	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	0.00 (0.00) [0]
1735	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [12/2021]	185.22 (-) [185.22]	0.00 (0.00) [0]
1736	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [3/2021]	272.32 (-) [272.32]	210.94 (0.00) [11]
	Total			22,32,019.72 (6,57,105.54) [26,61,205.74]	12,78,270.71 (4,29,186.02)

Details of North East Projects Costing Rs.150 crore and above (as on					28.02.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	ARUNACHAL PRADESH				
	Power				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (2/2021) [2/2021]	2,496.90 (7,927.34) [7,927.34]	8,154.49 (5,430.44) [134]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	13,233.01 (13,707.10) [155]
	Road Transport And Highways				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	133.95 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	394.53 (0.00) [0]
5	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	140.98 (0.00) [0]
6	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	160.09 (0.00) [0]
7	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	25.52 (0.00) [0]
8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	104.06 (0.00) [0]
9	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	0.00 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	15.49 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	33.61 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	33.58 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	0.00 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	104.06 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	104.06 (0.00) [0]

16	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	115.89 (0.00) [0]
17	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	260.57 (0.00) [0]
18	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	91.23 (0.00) [0]
19	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]
20	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	178.10 (0.00) [0]
21	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	184.62 (0.00) [0]
22	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	91.25 (0.00) [0]
23	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	376.69 (0.00) [0]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	0.00 (0.00) [0]
25	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	0.00 (0.00) [0]
26	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	204.77 (0.00) [60]
27	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [2/2021]	167.28 (-) [167.28]	22.06 (0.00) [46]
28	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
29	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	172.89 (0.00) [0]
30	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	139.47 (0.00) [47]
31	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [252.79]	97.07 (57.56) [0]
32	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [263.31]	110.34 (59.95) [0]
33	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	104.37 (0.00) [0]
34	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	104.36 (0.00) [0]
35	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (-) [389.45]	349.94 (182.42) [0]
36	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON	2/2017	4/2017	180.57	50.17

	EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX		(-) [2/2021]	(-) [180.57]	(0.00) [46]
37	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	0.00 (119.37) [0]
38	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
39	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
40	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (-) [4/2022]	175.06 (-) [175.06]	71.60 (0.00) [-]
41	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (-) [4/2022]	176.12 (-) [176.12]	61.55 (0.00) [-]
42	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,217.25 (57.90) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
43	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2022]	1,142.00 (-) [1,232.00]	323.90 (90.00) [12]
	<u>Health And Family Welfare</u>				
44	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [7/2022]	875.00 (-) [747.80]	296.84 (-127.20) [14]
45	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
46	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [6/2021]	557.00 (-) [557.00]	471.42 (0.00) [16]
47	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [4/2021]	224.75 (-) [222.21]	144.80 (-2.54) [8]
48	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [6/2021]	423.00 (-) [502.00]	403.62 (79.00) [22]
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [4/2021]	543.91 (638.60) [652.10]	136.05 (108.19) [14]
50	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [12,366.00]	168.82 (0.00) [0]
51	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	117.34 (0.00) [0]
52	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2021) [5/2021]	249.85 (303.75) [303.75]	180.83 (53.90) [12]
	<u>Railways</u>				
53	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2021]	314.00 (486.96) [800.00]	795.88 (486.00) [24]
54	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,478.05 (717.68) [12]

55	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [5/2021]	870.96 (-) [1,873.21]	1,133.64 (1,002.25) [2]
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,105.00]	787.79 (719.80) [48]
	Road Transport And Highways				
57	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (390.73) [390.73]	267.46 (122.65) [0]
58	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
59	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	12.40 (0.00) [0]
60	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
61	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [303.49]	153.44 (-216.52) [0]
62	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	474.44 (0.00) [0]
63	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	64.28 (0.00) [0]
64	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	103.73 (-28.50) [0]
65	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.30]	102.90 (-30.09) [42]
66	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [4/2021]	294.17 (-) [294.17]	190.47 (0.00) [63]
67	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	0.00 (0.00) [0]
68	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (-) [0/0]	166.94 (-) [166.94]	0.00 (0.00) [0]
69	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	489.84 (143.23) [0]
70	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [0/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
71	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	233.27 (7.98) [0]
72	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
73	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	117.35 (0.00) [0]
74	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [887.68]	228.44 (69.68) [0]

75	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	126.86 (-65.43) [42]
76	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	399.65 (0.00) [0]
77	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	273.38 (0.00) [0]
78	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
79	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
80	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
81	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
82	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
83	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2020]	208.00 (-) [230.00]	360.99 (22.00) [0]
84	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	352.28 (0.00) [0]
85	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [273.40]	127.57 (-776.11) [0]
86	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	236.86 (-70.66) [0]
87	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	70.46 (0.00) [0]
88	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	0.00 (0.00) [0]
89	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	0.00 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
90	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
91	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	10,777.52 (7,809.98) [153]
	<u>Road Transport And Highways</u>				
92	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	8.60 (0.00) [0]
93	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	14.15 (0.00) [0]

94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	18.22 (0.00) [0]
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	17.84 (0.00) [0]
96	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
97	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
98	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	0.00 (0.00) [0]
99	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	101.20 (0.00) [0]
100	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	170.53 (0.00) [0]
101	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	160.06 (-59.80) [36]
	<u>MEGHALAYA</u>				
	<u>Culture Development</u>				
102	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	145.60 (0.00) [42]
	<u>Health And Family Welfare</u>				
103	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	234.12 (0.00) [43]
	<u>Human Resource Development</u>				
104	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	<u>Railways</u>				
105	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [4,083.02]	263.68 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
106	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	84.67 (0.00) [0]
107	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
108	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	119.35 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
109	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2023]	2,393.47 (5,021.45) [5,521.45]	3,816.20 (3,127.98) [108]
	<u>Road Transport And Highways</u>				
110	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2021) [6/2021]	195.04 (-) [377.99]	325.42 (182.95) [128]
111	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM	8/2010	9/2014	186.96	292.10

	38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD		(12/2020) [0/0]	(-) [322.24]	(135.28) [0]
112	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2021) [6/2021]	193.69 (-) [327.92]	295.96 (134.23) [128]
113	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	4.72 (0.00) [0]
114	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	0.00 (0.00) [0]
115	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	0.00 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	0.00 (0.00) [0]
117	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	0.00 (0.00) [0]
118	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	65.01 (0.00) [43]
119	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	59.92 (0.00) [48]
120	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	58.49 (0.00) [43]
121	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	50.49 (0.00) [55]
122	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	33.18 (0.00) [45]
123	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	72.44 (0.00) [45]
124	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	47.39 (0.00) [43]
125	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	18.08 (0.00) [46]
126	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2020]	624.41 (-) [992.67]	890.74 (368.26) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
127	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [12/2024]	2,326.52 (-) [6,911.00]	1,125.27 (4,584.48) [117]
	<u>Road Transport And Highways</u>				
129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	85.02 (0.00) [44]
130	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM	3/2018	9/2018 (-)	285.68 (-)	68.70 (0.00)

	EXISTING KM 52.370 TO		[9/2022]	[285.68]	[48]
131	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	114.76 (-90.38) [0]
132	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2020]	387.00 (-) [387.00]	260.08 (0.00) [0]
133	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (336.49) [336.49]	71.11 (-163.60) [50]
134	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	8.86 (0.00) [0]
135	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	12.99 (0.00) [0]
136	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	3.66 (0.00) [0]
137	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	11.24 (0.00) [0]
138	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	1.50 (0.00) [0]
139	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	41.64 (0.00) [0]
140	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	87.30 (0.00) [0]
141	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	5.29 (0.00) [0]
142	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
143	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	0.00 (0.00) [0]
144	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	0.00 (0.00) [0]
145	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	0.00 (0.00) [0]
146	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
147	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	114.91 (0.00) [46]
148	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	80.78 (0.00) [39]
149	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	95.34 (0.00) [39]
150	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	83.20 (0.00) [38]

151	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	60.55 (0.00) [39]
152	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	36.80 (0.00) [49]
153	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	42.55 (0.00) [50]
154	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	111.04 (0.00) [0]
155	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	95.97 (0.00) [0]
156	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	290.94 (13.93) [57]
157	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [339.55]	276.01 (-56.97) [57]
158	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [5/2021]	429.52 (-) [340.00]	234.97 (-89.52) [57]
159	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (9/2020) [0/0]	336.25 (369.96) [336.25]	301.49 (0.00) [0]
160	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	123.44 (0.00) [0]
161	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	98.42 (0.00) [0]
162	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	0.00 (0.00) [0]
163	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
164	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	50.27 (0.00) [0]
	SIKKIM				
	Railways				
165	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [12/2023]	1,339.48 (4,084.69) [8,600.00]	619.18 (7,260.52) [96]
	Road Transport And Highways				
166	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	0.00 (0.00) [0]
167	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	0.00 (0.00) [0]
168	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (12/2020) [0/0]	182.28 (369.64) [269.14]	274.07 (86.86) [0]
169	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (12/2020) [0/0]	151.59 (370.01) [151.59]	282.36 (0.00) [0]
170	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI	4/2013	8/2013	166.27	243.59

	ROAD IN SOUTH SIKKIM.		(12/2020) [0/0]	(359.92) [166.27]	(0.00) [0]
171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	107.98 (0.00) [0]
172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	24.70 (0.00) [0]
173	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
174	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	11.03 (0.00) [0]
175	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	0.78 (0.00) [0]
176	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	0.00 (0.00) [0]
177	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	0.00 (0.00) [0]
178	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	255.15 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
179	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [0/0]	438.28 (-) [438.28]	335.58 (0.00) [0]
	<u>Railways</u>				
180	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
181	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	357.19 (0.00) [0]
182	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	0.00 (0.00) [0]
183	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	0.00 (0.00) [0]
184	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	0.00 (0.00) [0]
185	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	0.00 (0.00) [0]
186	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	0.00 (0.00) [0]
187	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [197.67]	5.75 (0.00) [0]
188	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (7/2021) [7/2021]	171.90 (-) [171.90]	110.19 (0.00) [11]
	<u>Rural Development</u>				

189	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [3/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [63]
190	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [3/2021]	202.61 (227.00) [207.12]	190.22 (4.51) [51]
191	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [3/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [51]
	Total			1,13,904.42 (43,583.76) [1,64,013.41]	67,410.99 (50,108.99)
