

399th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
January 2019



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for January 2019 contains information on the status of the 1423 Central Sector Infrastructure Projects costing ₹150 crore and above. During January 2018, 6 projects (3 projects are in Power, 2 projects are in Railways and 1 project is in Telecommunication sectors) have reported completion.

2. During the reference month, out of 1423 projects, 378 projects are delayed with respect to their original schedules and 51 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 51 projects, 12 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	605	104	9	2
2	RAILWAYS	366	99	10	3
3	PETROLEUM	139	33	11	2
4	COAL	98	36	0	0
5	POWER	92	57	14	3
6	URBAN DEVELOPMENT	58	21	1	0
7	HEALTH AND FAMILY WELFARE	20	6	1	0
8	STEEL	13	10	3	1
9	SHIPPING AND PORTS	7	2	0	0
10	FERTILISERS	6	2	1	0
11	MINES	5	0	0	0
12	TELECOMMUNICATIONS	5	3	0	0
13	ATOMIC ENERGY	4	4	1	1
14	HEAVY INDUSTRY	2	0	0	0
15	DEFENCE PRODUCTION	2	0	0	0
16	CIVIL AVIATION	1	1	0	0
Total		1423	378	51	16

3. Total original cost of implementation of the 1423 projects was ₹18,25,733.41 crore and their anticipated completion cost is likely to be ₹21,44,298.86 crore, which reflects overall cost overruns of ₹3,18,565.45 crore (17.45% of original cost). The expenditure incurred on these projects till January 2019 is ₹8,24,847.36 crore, which is 38.47% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost
Overruns (as on 01-02-2019)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	74.68
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
	CIVIL AVIATION				
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
	COAL				
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	24.10
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.06
	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
	PETROLEUM				
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5751.00	97.29
3	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	83.01
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
5	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	330.35	62.78
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
2	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4401.90	165.65
3	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1078.31	156.12
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
5	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	139.69
	RAILWAYS				
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
2	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	1800.00	1391.30
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
4	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
5	MUNIRABAD (GINGERA) -RAICHUR NL	04/2007	179.65	1350.91	651.97
	ROAD TRANSPORT AND HIGHWAYS				
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	880.06
2	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	114.56
3	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
4	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27

5	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	271.56	11.07
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58
4	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	486.54	25.40

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-02-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	2608.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	BHANEAGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	99.78
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.09

4	HEAVY INDUSTRY				
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	2109.30
	PETROLEUM				
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5751.00	2836.00
2	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	03/2014	3076.00	4190.00	1114.00
3	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
4	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	715.36
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	5475.21
4	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9141.97	4387.55
5	BONGAIGAON THERMAL POWER PROJECT	01/2008	4375.35	8150.00	3774.65
	RAILWAYS				
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	13809.00	9354.83
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
	ROAD TRANSPORT AND HIGHWAYS				
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	6786.82
2	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	1728.77
3	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
4	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
5	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
	SHIPPING AND PORTS				
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	271.56	27.06
4	STEEL				
5	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
	URBAN DEVELOPMENT				
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
3	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46

4	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23
5	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	151.74

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1423 projects, 316 are on schedule, 378 are delayed, 345 projects reported cost overrun and 135 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 322 if delay is calculated on the basis of latest schedule of completion. Further, for 700 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 384 delayed projects, 121(32.01%) projects have overall delay in the range of 1 to 12 months, 58 (15.34%) projects have delay in the range of 13 to 24 months, 102 (26.98%) projects have delay in the range of 25 to 60 months and 97 (25.66%) projects have delay of 61 months and above. **The average time overrun in these 378 delayed projects is 43.11 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-02-2019)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
2	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
3	BALRAM OCP EXTENSION, MCL 8.00 MTY	12/2007	03/2010	03/2020	120
4	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2020	108
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	03/2012	03/2021	108
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	04/2019	29
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	02/2016	12/2017	02/2019	14
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	10/2020	83
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	07/2019	26
3	AIIMS - OPD(NEW)	08/2014	05/2017	03/2019	22
4	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	09/2019	16
5	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	06/2019	16
PETROLEUM					
1	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	12/2019	81

2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	06/2019	78
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
4	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	03/2019	70
5	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	03/2015	12/2019	57
POWER					
1	PARBATHI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	03/2019	124
3	BARH STPP(3X660MW) NTPC	02/2005	01/2011	04/2021	123
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	03/2019	111
5	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	09/2010	04/2019	103
RAILWAYS					
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
2	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
3	MANDHANA - BRAHMAWART NEW LINE PROJECT.	04/1997	04/1999	03/2019	239
4	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2019	228
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	03/2021	220
ROAD TRANSPORT AND HIGHWAYS					
1	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	02/2019	131
2	NALBARI T BIJNI (AS-7)	12/2003	04/2008	03/2019	131
3	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	04/2019	130
4	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	02/2019	129
5	GWALIOR-JHANSI, NH-75	12/2003	12/2009	08/2020	128
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	02/2019	155
2	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	12/2017	05/2020	29
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	06/2019	49
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	03/2020	41
3	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
4	COKE OVEN BATTERY-5	12/2011	12/2017	09/2019	21
5	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	06/2019	18
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
2	MADHYA PRADESH ACCESS (LOT1)	08/2017	05/2018	02/2019	9
3	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	02/2019	4
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2019	77
2	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
3	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70
4	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	05/2020	64
5	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	11/2019	56

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil

works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-02-2019)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	173.06	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	8.71	09/2019	09/2019
3	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	17.67	03/2022	03/2022
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	4524.70	11/2021	11/2021
5	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	258.23	03/2020	03/2020
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	147.00	11/2013	10/2020
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	272.00	06/2020	06/2020
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	39.35	04/2020	04/2020
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	247.47	09/2018	03/2019
HEAVY INDUSTRY							
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	335.03	09/2019	09/2019
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.12	02/2017	N.A.
4	MMPL PIPELINE REROUTING PROJECT	04/2013	449.58	449.58	122.99	12/2019	12/2019

5	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10448.57	09/2010	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3038.00	10/2017	N.A.
3	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	187.24	04/2016	03/2019
4	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1006.39	04/2020	10/2023
5	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9141.97	993.85	12/2018	12/2019
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	484.14	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	270.28	03/2019	03/2020
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	749.69	0.00	06/2005	N.A.
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	634.48	629.43	03/1994	N.A.
ROAD TRANSPORT AND HIGHWAYS							
1	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	520.01	520.01	0.00	N.A.	N.A.
2	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	20.12	N.A.	10/2020
3	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	319.68	0.00	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	550.78	03/2006	02/2019
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	413.91	12/2010	N.A.
4	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP	03/2016	600.00	257.90	1.45	12/2017	05/2020

	DRAFT						
5	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	05/2016	970.00	970.00	249.81	05/2020	05/2020
	STEEL						
1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	4749.00	4749.00	108.38	09/2017	N.A.
	TELECOMMUNICATIONS						
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.03	06/2017	N.A.
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	214.10	33.46	05/2018	02/2019
4	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	231.80	117.63	10/2018	02/2019
	URBAN DEVELOPMENT						
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-02-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5738.32
	COAL				
1	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	0.00	266.38
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	267.99

3	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	584.87
4	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	235.51
5	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	0.00	184.45
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	508.29
2	CNCI KOLKATA WEST BENGAL	08/2016	244.00	0.00	247.47
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	GAIL GAS LTD BENGALURU CGD PROJECT	02/2015	749.00	0.00	803.00
3	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	07/2015	822.66	0.00	868.92
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7164.11
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10448.57
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	6900.51
4	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	15441.10
5	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	0.00	3775.64
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	484.14
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	274.56	629.43
3	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	538.21
4	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	759.20
5	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	04/1994	320.66	0.00	550.16
ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	410.32
2	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	0.00	268.94
3	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	202.58
4	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	297.81
5	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	312.79
SHIPPING AND PORTS					
1	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	271.56
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.77
4	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	0.00	394.49

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on as on 01-02-2019)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	N.A.	03/2018
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	03/2012	N.A.	N.A.
3	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
4	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
5	MADHUBAND NLW WASHERY	08/2010	05/2014	N.A.	04/2018
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	N.A.	N.A.
3	PARADIP-RAIPUR- RANCHI PIPELINE	08/2009	12/2016	N.A.	N.A.
4	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
5	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
3	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
4	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	09/2011	09/2014	N.A.	N.A.
5	KUDGI STPP STAGE 1	01/2012	01/2017	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	N.A.	N.A.
4	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	N.A.	N.A.
5	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	03/2006	N.A.	01/2006
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	01/1991	05/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.

5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	01/1991	10/2016	N.A.	N.A.
SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	N.A.	N.A.
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	12/2017	03/2018	N.A.
STEEL					
1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	09/2017	N.A.	N.A.
2	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	04/2015	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
4	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 31.01.2019 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	605	9
2	RAILWAYS	366	10
3	PETROLEUM	139	11
4	COAL	98	0
5	POWER	92	14
6	URBAN DEVELOPMENT	58	1
7	HEALTH AND FAMILY WELFARE	20	1
8	STEEL	13	3
9	SHIPPING AND PORTS	7	0
10	FERTILISERS	6	1
11	MINES	5	0
12	TELECOMMUNICATIONS	5	0
13	ATOMIC ENERGY	4	1
14	HEAVY INDUSTRY	2	0
15	DEFENCE PRODUCTION	2	0
16	CIVIL AVIATION	1	0
	Total	1423	51

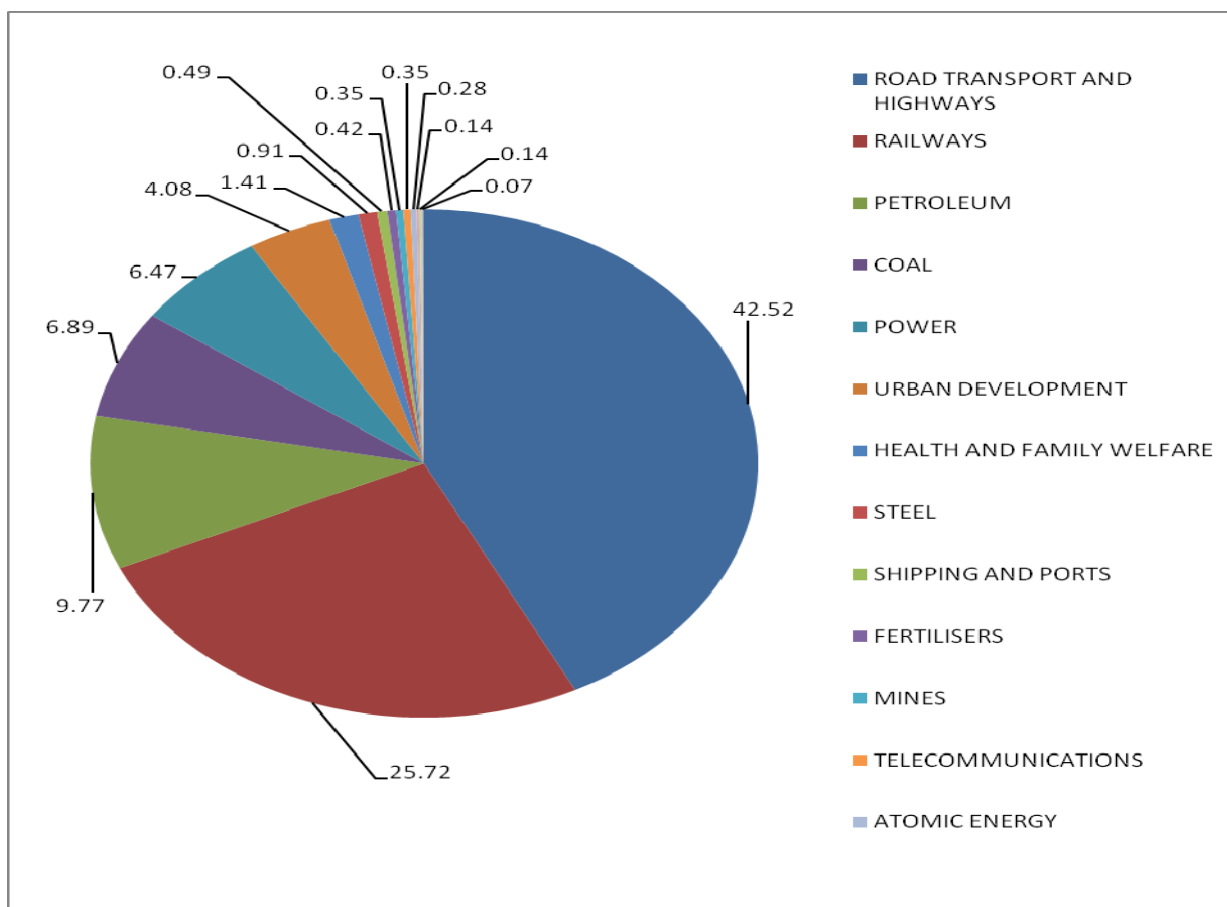


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2018-2019				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2018			
	<u>STEEL</u>			
1	ALTERNATE GAS NETWORK AT BSL (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000093]	255.19	03/2018	177.21
	<u>PETROLEUM</u>			
2	ENNORE TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000224]	393.00	04/2018	281.45
	<u>POWER</u>			
3	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000123]	198.63	09/2014	127.13
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000179]	6,517.36	04/2018	3,772.80
5	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000210]	207.88	07/2018	17.00
	<u>HEALTH AND FAMILY WELFARE</u>			
6	AIIMS-RAE BARELI-HOUSING (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000006]	159.50	11/2013	158.65
	<u>RAILWAYS</u>			
7	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION (RAIL VIKAS NIGAM LTD.) - [N22000189]	822.39	-	1,713.20
8	NEW COOCHBEHAR TO SAMUKTALA (NORTH EAST FRONTIER RAILWAY) - [N22000197]	209.77	-	620.04
9	DELANG-PURI DOUBLING (EAST COAST RAILWAY) - [N22000320]	165.16	03/2015	226.35
10	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) (RAIL VIKAS NIGAM LTD.) - [N22000322]	190.10	-	320.41
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	TALEGAON-AMRAVATI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000140]	567.00	11/2013	1,055.94
12	MURADABAD-BAREILY PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000154]	1,267.00	06/2013	2,667.96
	<u>SHIPPING AND PORTS</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED PPP (ANNUITY)(KAMARAJAR PORT LIMITED) - [N25000065]	198.94	06/2017	255.02
14	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000067]	274.85	04/2017	251.64
	<u>URBAN DEVELOPMENT</u>			
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN Central Sector Projects(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000091]	350.02	03/2015	452.35
	May,2018			
	<u>PETROLEUM</u>			
16	TWENTY NOS. FEEDER GAS LINES (OIL INDIA LIMITED) - [N16000192]	228.64	12/2016	149.73
17	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000201]	238.50	03/2017	203.98
18	SIX PIPELINE REPLACEMENT PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000214]	181.02	01/2017	174.88
19	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000245]	931.00	07/2017	684.74
	<u>POWER</u>			
20	PARE HYDRO ELECTRIC PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000045]	573.99	08/2013	1,637.60
	<u>RAILWAYS</u>			
21	GADWAL - RAICHUR (NL), SCR (SOUTH CENTRAL RAILWAY) - [220100270]	92.63	02/2011	319.43
22	JAGGAYYAPET - MELLACHERUVU (SOUTH CENTRAL RAILWAY) - [N22000304]	313.24	01/1999	578.00
	June,2018			
	<u>POWER</u>			
23	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000197]	1,479.30	04/2017	897.12
24	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000237]	167.75	04/2019	86.62
	<u>RAILWAYS</u>			
25	RANCHI-LOHARDAGA(GC),SER (SOUTH EASTERN RAILWAY) - [220100214]	194.07	06/2004	194.07
26	BHOPAL BINA 3D LINE DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000077]	687.20	03/2010	1,033.77

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	July,2018			
	<u>STEEL</u>			
27	EXPANSION OF BHILAI STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000057]	17,265.00	03/2013	19,855.23
	<u>PETROLEUM</u>			
28	DEVELOPMENT OF C-26 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000133]	2,592.17	05/2014	2,049.26
29	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000134]	200.69	07/2014	109.58
30	CONSTRUCTION OF THREE ETPS, MEHSANA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000135]	260.74	11/2014	83.44
31	PIPELINE REPLACEMENT PROJECT, AHMEDABAD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000159]	202.25	07/2016	130.21
32	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000172]	4,124.35	04/2016	5,347.49
33	MH NORTH REDEVELOPMENT PHASE III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000188]	5,706.47	05/2017	5,724.54
34	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000246]	215.38	06/2017	198.98
	<u>POWER</u>			
35	BOKARO THERMAL POWER STATION-A (DAMODAR VALLEY CORPORATION) - [N18000199]	2,313.00	12/2011	3,965.00
36	RAGHUNATHPUR THERMAL POWER STATION PHASE-I (DAMODAR VALLEY CORPORATION) - [N18000202]	4,122.00	02/2011	8,479.00
	September,2018			
	<u>PETROLEUM</u>			
37	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000199]	257.87	11/2016	243.30
38	NAWAGAM-KOYALI PIPELINE PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000211]	195.63	09/2018	174.68
39	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000264]	337.06	08/2018	167.16
	<u>POWER</u>			
40	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000143]	514.20	06/2015	605.50
41	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000169]	288.49	02/2017	276.10

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000220]	810.48	12/2018	528.50
43	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000254]	2,525.00	11/2017	2,015.38
44	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000255]	2,225.00	01/2018	1,655.02
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
45	CHAMBAL BRIDGE, NH-76 (RJ-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000068]	275.00	02/2010	252.25
46	DEOLI KOTA PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000148]	593.00	07/2013	1,073.73
47	2-LANNING WITH PS KHAGARIA-PURNEA PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000184]	664.00	02/2014	654.59
48	2-LANING WITH PS BHILWARA-LODPURA SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000240]	240.10	03/2016	194.69
49	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000337]	538.08	02/2018	335.24
50	JAISALMER - BARMER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000348]	482.27	02/2018	308.83
51	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000352]	455.60	07/2017	202.68
52	JODHPUR - BARMER SECTION OF PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000354]	264.72	04/2017	98.18
53	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 2) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000358]	562.34	04/2018	109.07
54	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000433]	768.56	03/2018	774.99
55	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000436]	664.53	03/2018	702.97
56	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000440]	789.31	03/2018	867.54
57	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000481]	1,232.00	08/2015	1,091.17
58	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000484]	239.23	12/2017	123.47
59	FOUR LANING OF KAITHAL - RAJASTHAN BORDER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000487]	1,393.00	-	1,917.40
60	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000500]	830.36	07/2018	326.23

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
61	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000597]	600.85	05/2018	109.84
	October,2018			
	<u>COAL</u>			
62	NEYVELI SOLAR POWER PROJECT 130 MW (NEYVELI LIGNITE CORPORATION) - [N06000151]	687.28	06/2017	758.30
	<u>PETROLEUM</u>			
63	DIESEL HYDROTREATOR Central Sector Projects(NUMALIGARH REFINERY LIMITED) - [N16000207]	1,031.37	01/2018	562.77
	<u>RAILWAYS</u>			
64	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) (WESTERN RAILWAY) - [N22000122]	1,389.62	03/2014	2,140.08
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
65	PADI - DAHOD (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000353]	279.14	05/2017	212.40
	<u>TELECOMMUNICATIONS</u>			
66	UP (EAST) ACCESS LOT1 (BHARAT SANCHAR NIGAM LIMITED) - [N26000112]	169.45	08/2018	78.34
	<u>URBAN DEVELOPMENT</u>			
67	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY EPC(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000095]	164.00	11/2018	123.90
	November,2018			
	<u>CIVIL AVIATION</u>			
68	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000050]	309.46	01/2011	546.69
	<u>PETROLEUM</u>			
69	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000262]	193.40	01/2019	106.79
	<u>RAILWAYS</u>			
70	GOELKERA-MANOHARPUR,(LD)(SER) (RAIL VIKAS NIGAM LTD.) - [N22000045]	261.70	02/2006	393.23
71	TINPAHAR - SAHIBGANJ (ER) (EASTERN RAILWAYS) - [N22000115]	167.73	03/2012	238.53

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
72	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) (EASTERN RAILWAYS) - [N22000119]	207.52	12/2012	335.35
73	VIRAMGAM-SURENDRANAGAR (DL) (WESTERN RAILWAY) - [N22000146]	279.40	-	334.93
74	PLASSEY-JIAGANJ DOUBLING (EASTERN RAILWAYS) - [N22000220]	248.07	03/2015	266.25
75	SAINTHIA-TARAPITH 3RD LINE (EASTERN RAILWAYS) - [N22000237]	193.44	-	280.68
76	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC (EASTERN RAILWAYS) - [N22000245]	423.66	03/2017	652.79
	<u>TELECOMMUNICATIONS</u>			
77	MAHARASHTRA ACCESS (LOT 1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000109]	212.70	05/2018	37.25
78	GUJARAT ACCESS (LOT 1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000111]	171.54	05/2018	72.46
	<u>URBAN DEVELOPMENT</u>			
79	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-43 G BLOCK BANDRA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000068]	241.33	03/2016	357.50
	December,2018			
	<u>COAL</u>			
80	RAJMAHAL OC EXP. (EASTERN COAL FIELDS LIMITED) - [N06000056]	153.82	03/2014	131.07
	<u>PETROLEUM</u>			
81	PARADIP HALDIA DURGAPUR LPG PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000148]	913.00	06/2018	1,323.53
82	PIPELINE REPLACEMENT PROJECT -4 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000203]	2,899.93	05/2017	2,183.66
83	ANKLESHWAR BARODA PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000232]	199.95	03/2018	156.83
	<u>POWER</u>			
84	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000080]	2,144.00	12/2012	2,669.96
85	EASTERN REGION STRENGTHENING SCHEME-III (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000100]	1,272.80	11/2012	1,473.05
86	INSTALLATION OF STATCOMS IN WESTERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000185]	1,071.24	09/2017	649.26
87	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000195]	780.33	10/2018	499.05

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
88	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000200]	2,247.37	07/2018	1,531.89
89	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000221]	287.99	06/2018	164.22
90	EASTERN REGION STRENGTHENING SCHEME XIV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000224]	167.01	11/2018	119.23
91	PROVISION OF SERIES REACTORS IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000232]	177.52	02/2019	87.48
92	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A Central Sector Projects (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000253]	955.00	12/2015	1,247.66
93	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V Central Sector Projects (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000256]	1,750.00	06/2018	1,335.04
	<u>HEALTH AND FAMILY WELFARE</u>			
94	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000014]	312.99	08/2018	318.00
	<u>RAILWAYS</u>			
95	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR (NORTH EAST FRONTIER RAILWAY) - [220100201]	3,230.02	04/2008	5,298.09
96	RANI-MARWAR JN. PATCH DOUBLING (NORTH WESTERN RAILWAY) - [N22000156]	288.97	11/2018	315.60
97	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000198]	283.55	03/2019	480.81
98	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. (SOUTH EASTERN RAILWAY) - [N22000491]	1,027.40	03/2022	195.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
99	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106281]	200.00	04/2009	248.60
100	JALANDHAR - AMRITSAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000351]	523.85	01/2016	170.68
	<u>TELECOMMUNICATIONS</u>			
101	MAHARASHTRA NODAL (LOT 1) Central Sector Projects (BHARAT SANCHAR NIGAM LIMITED) - [N26000107]	159.30	04/2018	60.27
	January, 2019			
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
102	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000215]	1,788.41	09/2017	1,727.37
103	WESTERN REGION STRENGTHENING SCHEME-XVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000229]	150.99	07/2018	97.16
104	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000270]	771.00	02/2013	1,577.20
	<u>RAILWAYS</u>			
105	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) (SOUTH CENTRAL RAILWAY) - [220100106]	124.43	-	1,022.21
106	GULBARGA-BIDAR, SCR(NL) (SOUTH CENTRAL RAILWAY) - [220100254]	242.42	-	1,172.64
	<u>TELECOMMUNICATIONS</u>			
107	MAHARASHTRA CORE (LOT1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000108]	167.68	04/2018	32.44

TABLE-3

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1424
No of Projects Completed/Dropped/Frozen in Current Month	6
No of Projects added in Current Month	5
No of Projects in Current Month	1423

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	378 (26.56%)	29 (2.04%)	316(22.21%)	79 (5.55%)	621(3.64%)	1423
Latest Approved (Date)	322 (22.63%)	29 (2.04%)	384(26.99%)	67 (4.71%)	621(3.64%)	1423

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1216	15,21,515.72	17,23,054.52	6,16,961.18	35.80	2,01,538.80	13.20
Project with Revision in Cost	207	4,52,193.97	4,21,244.34	2,07,886.18	49.40	-30,949.63	-6.80
Total	1,423	19,73,709.69	21,44,298.86	8,24,847.36	38.47	1,70,589.17	8.64
Original Cost of All Projects							
Original Cost	1,423	18,25,733.41	21,44,298.86	8,24,847.36	38.47	3,18,565.45	17.45

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	378	7,36,406.57	8,85,650.69	4,80,088.92	54.20	1,49,244.12	20.27
Latest Approved (RCE)	322	5,49,103.63	5,99,529.80	2,94,219.57	49.10	50,426.17	9.18

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	51	39,913.92	46,299.96	31,311.32	67.60	6,386.04	16.00
Total	51	39,913.92	46,299.96	31,311.32	67.63	6,386.04	16.00


Summary of projects in the Flash Report for the month of January, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1424
Number of Projects completed/dropped/frozen in Current Month	6
	0
Number of Projects Added in Current Month	5
Number of Projects in Current Month	1423

Brief Analysis

Project Status with respect to Original Schedule: Out of 1423 projects, 29 projects are ahead of schedule, 316 projects are on schedule 378 projects are delayed. 621 projects do not have fixed dates of commissioning. 79 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

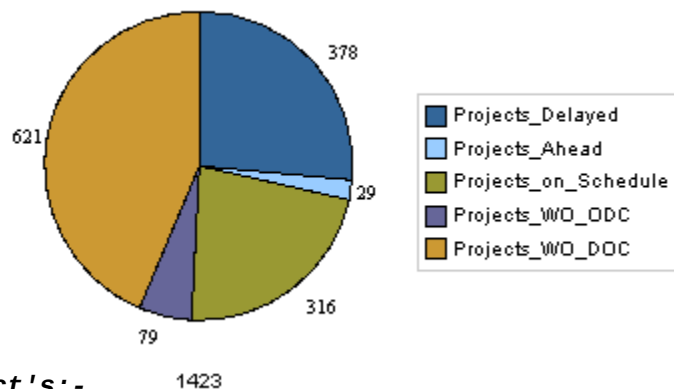

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1423 projects when sanctioned, was of the order of Rs. 1825733.41 crore but this was subsequently revised to Rs. 2144298.86 crore implying a cost overrun of 17.4%. The expenditure incurred on these projects till January, 2019 is Rs. 824847.36 crore, which is 38.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

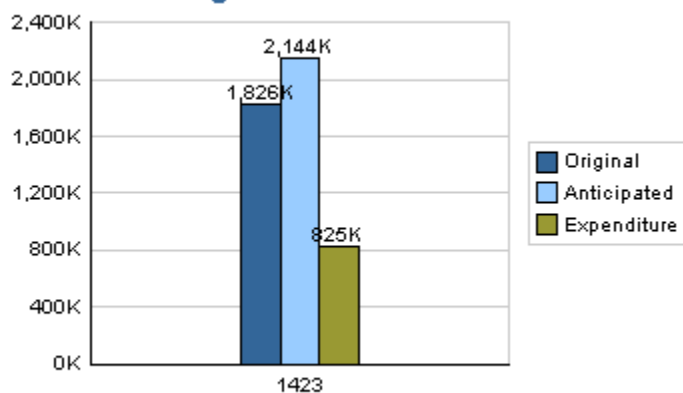


TABLE-4

<u>Extent of cost overrun in projects with respect to original schedule(Sector Wise) RS. 150 Crore and above</u> (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	98	97,468.86	96,940.36	-0.54	10	19,631.17	20,970.49	6.82
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	5.89
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	42.39
7	PETROLEUM	139	2,33,745.66	2,37,274.59	1.51	17	24,201.74	33,407.72	38.04
8	POWER	92	2,93,659.85	3,55,596.43	21.09	38	1,70,271.18	2,32,207.76	36.38
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
11	RAILWAYS	366	4,85,586.03	6,97,755.98	43.69	207	1,72,037.48	3,95,094.22	129.66
12	ROAD TRANSPORT AND HIGHWAYS	605	4,11,159.45	4,25,383.97	3.46	49	29,654.32	44,654.88	50.58
13	SHIPPING AND PORTS	7	6,557.29	6,995.32	6.68	3	760.89	1,541.02	102.53
14	TELECOMMUNICATIONS	5	16,310.53	27,539.33	68.84	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	58	1,60,566.07	1,66,251.85	3.54	11	22,711.08	28,405.75	25.07
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0.00
Total		1423	18,25,733.41	21,44,298.86	17.45	345	4,71,202.51	8,09,785.85	71.86

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-5

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	69	1,07,461.29	1,11,208.37	3.49	9	7,934.53	12,551.72	58.19
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	5	9,181.79	26,308.30	186.53
3	ASSAM	45	27,704.18	33,843.20	22.16	13	7,811.37	14,278.59	82.79
4	BIHAR	91	76,252.26	1,11,749.59	46.55	33	40,972.00	76,544.96	86.82
5	GOA	10	4,292.52	4,292.52	0.00	0	0.00	0.00	0.00
6	GUJARAT	49	51,576.03	57,483.90	11.45	6	14,699.98	22,283.77	51.59
7	HARYANA	29	21,083.41	22,987.06	9.03	4	2,139.14	4,176.00	95.22
8	HIMACHAL PRADESH	13	17,058.17	26,566.39	55.74	2	6,886.58	16,394.80	138.07
9	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	1017.96
10	KARNATAKA	47	82,362.96	88,262.78	7.16	13	23,620.24	29,732.82	25.88
11	KERALA	25	39,778.48	41,953.10	5.47	6	7,475.98	9,846.14	31.70
12	MADHYA PRADESH	60	67,550.02	72,708.48	7.64	10	26,531.45	35,146.93	32.47
13	MAHARASHTRA	128	1,85,529.12	1,97,693.64	6.56	25	31,645.68	45,825.52	44.81
14	MANIPUR	2	4,670.86	14,025.69	200.28	1	4,454.17	13,809.00	210.02
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	1	906.46	6,000.00	561.92
16	MIZORAM	4	3,406.61	5,981.14	75.57	1	2,393.47	4,968.00	107.56
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	28.95
18	ODISHA	84	97,034.62	1,02,058.71	5.18	20	25,790.34	31,662.01	22.77
19	PUNJAB	33	17,042.04	17,146.31	0.61	3	1,716.50	1,847.81	7.65
20	RAJASTHAN	56	46,045.92	48,245.10	4.78	11	5,160.21	7,368.28	42.79
21	SIKKIM	9	3,476.73	6,281.03	80.66	2	1,727.48	4,532.06	162.35
22	TAMIL NADU	76	1,19,890.58	1,37,033.24	14.30	26	29,413.59	47,647.46	61.99
23	TRIPURA	9	4,422.36	8,345.05	88.70	7	3,555.47	7,478.16	110.33
24	UTTAR PRADESH	110	1,34,449.08	1,36,016.30	1.17	18	25,563.98	29,809.84	16.61
25	WEST BENGAL	53	57,557.73	66,897.02	16.23	18	16,956.22	26,615.20	56.96
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	2	552.41	679.33	22.98
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	22	55,263.55	62,738.78	13.53	6	6,981.71	14,456.94	107.07
29	CHHATISGARH	45	78,684.04	82,285.57	4.58	7	17,333.75	22,308.14	28.70
30	JHARKHAND	48	47,744.98	52,545.65	10.05	9	22,304.03	27,108.48	21.54
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	9	9,874.84	15,740.60	59.40
32	TELANGANA	41	34,378.10	37,015.07	7.67	11	5,330.89	8,298.89	55.68
33	MULTI STATE	160	3,40,790.26	4,44,636.07	30.47	65	1,07,461.73	2,15,417.10	100.46
Total		1423	18,25,733.41	21,44,298.86	17.45	345	4,71,202.51	8,09,785.85	71.86

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

<u>Extent of time overrun in projects with respect to original schedule</u>						Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	98	97,468.86	96,940.36	-0.54	36	20,727.79	20,687.07	12 - 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	2	680.64	692.29	14 - 29
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	13	32,529.65	32,317.05	-0.65	10	26,773.72	26,561.12	9 - 49
7	PETROLEUM	139	2,33,745.66	2,37,274.59	1.51	33	87,238.71	92,111.65	1 - 81
8	POWER	92	2,93,659.85	3,55,596.43	21.09	57	1,95,058.30	2,38,053.57	1 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	6	1,673.14	1,772.92	6 - 83
11	RAILWAYS	366	4,85,586.03	6,97,755.98	43.69	99	1,23,852.80	2,02,478.25	1 - 324
12	ROAD TRANSPORT AND HIGHWAYS	605	4,11,159.45	4,25,383.97	3.46	104	90,619.80	93,602.74	1 - 131
13	SHIPPING AND PORTS	7	6,557.29	6,995.32	6.68	2	750.00	857.90	29 - 155
14	TELECOMMUNICATIONS	5	16,310.53	27,539.33	68.84	3	13,781.10	25,109.90	4 - 58
15	URBAN DEVELOPMENT	58	1,60,566.07	1,66,251.85	3.54	21	1,07,815.96	1,08,432.95	2 - 77
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	-
Total		1423	18,25,733.41	21,44,298.86	17.45	378	7,36,406.57	8,85,650.69	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-7

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	69	1,07,461.29	1,11,208.37	3.49	17	53,132.14	55,187.71	2 - 168
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	2	2,635.83	6,334.96	36 - 111
3	ASSAM	45	27,704.18	33,843.20	22.16	11	9,034.06	14,284.50	8 - 131
4	BIHAR	91	76,252.26	1,11,749.59	46.55	20	38,399.16	54,948.14	4 - 123
5	GOA	10	4,292.52	4,292.52	0.00	0	0.00	0.00	-
6	GUJARAT	49	51,576.03	57,483.90	11.45	10	15,727.28	21,262.18	2 - 84
7	HARYANA	29	21,083.41	22,987.06	9.03	4	2,534.20	3,714.20	3 - 91
8	HIMACHAL PRADESH	13	17,058.17	26,566.39	55.74	4	7,041.67	12,516.88	12 - 147
9	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	5	16,904.75	42,353.75	10 - 220
10	KARNATAKA	47	82,362.96	88,262.78	7.16	18	42,742.14	43,792.83	2 - 264
11	KERALA	25	39,778.48	41,953.10	5.47	8	16,401.45	17,142.27	8 - 79
12	MADHYA PRADESH	60	67,550.02	72,708.48	7.64	11	18,842.47	20,855.76	2 - 96
13	MAHARASHTRA	128	1,85,529.12	1,97,693.64	6.56	39	80,223.33	86,088.60	2 - 192
14	MANIPUR	2	4,670.86	14,025.69	200.28	2	4,670.86	14,025.69	56 - 108
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	3	1,379.19	1,379.19	10 - 60
16	MIZORAM	4	3,406.61	5,981.14	75.57	1	2,393.47	4,968.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	4	3,525.63	4,199.11	36 - 79
18	ODISHA	84	97,034.62	1,02,058.71	5.18	24	32,981.33	38,402.10	3 - 147
19	PUNJAB	33	17,042.04	17,146.31	0.61	5	2,036.78	2,137.05	1 - 22
20	RAJASTHAN	56	46,045.92	48,245.10	4.78	22	25,649.40	27,039.39	1 - 89
21	SIKKIM	9	3,476.73	6,281.03	80.66	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	76	1,19,890.58	1,37,033.24	14.30	18	64,780.71	67,438.21	1 - 155
23	TRIPURA	9	4,422.36	8,345.05	88.70	2	1,711.63	4,057.00	31 - 60
24	UTTAR PRADESH	110	1,34,449.08	1,36,016.30	1.17	24	41,292.86	41,964.05	2 - 239
25	WEST BENGAL	53	57,557.73	66,897.02	16.23	21	25,157.36	29,107.67	5 - 324
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	22	55,263.55	62,738.78	13.53	7	42,308.26	42,780.83	5 - 83
29	CHHATISGARH	45	78,684.04	82,285.57	4.58	11	30,819.18	32,754.74	13 - 117
30	JHARKHAND	48	47,744.98	52,545.65	10.05	17	23,839.56	25,977.03	9 - 108
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	6	23,935.83	29,313.50	15 - 102
32	TELANGANA	41	34,378.10	37,015.07	7.67	15	18,452.17	19,234.54	3 - 144
33	MULTI STATE	160	3,40,790.26	4,44,636.07	30.47	44	80,113.70	1,12,022.48	1 - 228
Total		1423	18,25,733.41	21,44,298.86	17.45	378	7,36,406.57	8,85,650.69	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	4	72,241.00	74,849.00	36 - 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	98	97,021.71	96,940.36	-0.08	35	19,426.09	20,054.26	0 - 144
4	FERTILISERS	6	1,793.57	1,793.57	0.00	1	482.85	482.85	14 - 14
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	13	32,529.65	32,317.05	-0.65	9	11,248.72	11,036.12	9 - 41
7	PETROLEUM	139	2,37,216.14	2,37,274.59	0.02	18	22,170.97	24,165.72	-9 - 78
8	POWER	92	3,68,110.40	3,55,596.43	-3.40	41	1,48,758.93	1,12,309.29	1 - 147
9	HEAVY INDUSTRY	2	5,281.30	5,381.30	1.89	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	4	895.04	895.04	6 - 26
11	RAILWAYS	366	5,47,419.86	6,97,755.98	27.46	86	1,08,807.33	1,75,705.14	0 - 239
12	ROAD TRANSPORT AND HIGHWAYS	605	4,11,729.58	4,25,383.97	3.32	104	90,565.21	93,602.74	1 - 131
13	SHIPPING AND PORTS	7	6,982.09	6,995.32	0.19	1	600.00	600.00	155 - 155
14	TELECOMMUNICATIONS	5	16,309.33	27,539.33	68.86	1	13,334.00	24,664.00	58 - 58
15	URBAN DEVELOPMENT	58	1,61,098.60	1,66,251.85	3.20	17	60,258.88	60,724.31	2 - 77
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	-
Total		1423	19,73,709.69	21,44,298.86	8.64	322	5,49,103.63	5,99,529.80	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of cost overrun in projects with respect to latest schedule RS. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	74.69
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	98	97,021.71	96,940.36	-0.08	7	18,876.68	19,914.04	5.50
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0.00
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	42.39
7	PETROLEUM	139	2,37,216.14	2,37,274.59	0.02	9	10,310.66	14,463.53	40.28
8	POWER	92	3,68,110.40	3,55,596.43	-3.40	21	1,33,335.16	1,75,289.01	31.47
9	HEAVY INDUSTRY	2	5,281.30	5,381.30	1.89	1	3,727.30	3,827.30	2.68
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
11	RAILWAYS	366	5,47,419.86	6,97,755.98	27.46	197	1,41,915.39	3,04,887.41	114.84
12	ROAD TRANSPORT AND HIGHWAYS	605	4,11,729.58	4,25,383.97	3.32	39	27,295.62	41,914.00	53.56
13	SHIPPING AND PORTS	7	6,982.09	6,995.32	0.19	1	258.33	271.56	5.12
14	TELECOMMUNICATIONS	5	16,309.33	27,539.33	68.86	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	58	1,61,098.60	1,66,251.85	3.20	8	22,543.90	27,706.04	22.90
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0.00
Total		1423	19,73,709.69	21,44,298.86	8.64	290	3,76,822.90	6,21,160.16	64.84

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-10

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	133- 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	98	97,021.71	96,940.36	-0.08	4	983.19	1,747.25	60- 144
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0- 0
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	41- 41
7	PETROLEUM	139	2,37,216.14	2,37,274.59	0.02	3	3,989.62	6,904.09	17- 78
8	POWER	92	3,68,110.40	3,55,596.43	-3.40	8	38,010.06	56,028.24	12- 147
9	HEAVY INDUSTRY	2	5,281.30	5,381.30	1.89	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	0	0.00	0.00	0- 0
11	RAILWAYS	366	5,47,419.86	6,97,755.98	27.46	53	53,274.64	1,21,512.19	3- 239
12	ROAD TRANSPORT AND HIGHWAYS	605	4,11,729.58	4,25,383.97	3.32	15	12,142.20	15,180.75	1- 131
13	SHIPPING AND PORTS	7	6,982.09	6,995.32	0.19	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	5	16,309.33	27,539.33	68.86	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	58	1,61,098.60	1,66,251.85	3.20	3	2,103.21	2,577.53	5- 36
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0- 0
Total		1423	19,73,709.69	21,44,298.86	8.64	90	1,27,986.53	2,35,643.78	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-11

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	98	97,468.86	96,940.36	-0.54	6	1,549.74	2,394.02	12- 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	29- 29
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	41- 41
7	PETROLEUM	139	2,33,745.66	2,37,274.59	1.51	11	18,298.77	25,054.49	2- 78
8	POWER	92	2,93,659.85	3,55,596.43	21.09	29	1,27,518.04	1,70,513.31	10- 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	1	414.11	513.89	83- 83
11	RAILWAYS	366	4,85,586.03	6,97,755.98	43.69	61	60,943.39	1,41,018.40	3- 324
12	ROAD TRANSPORT AND HIGHWAYS	605	4,11,159.45	4,25,383.97	3.46	16	12,281.13	15,335.75	1- 131
13	SHIPPING AND PORTS	7	6,557.29	6,995.32	6.68	1	150.00	600.00	155- 155
14	TELECOMMUNICATIONS	5	16,310.53	27,539.33	68.84	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	58	1,60,566.07	1,66,251.85	3.54	4	2,217.65	2,843.53	5- 70
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0- 0
Total		1423	18,25,733.41	21,44,298.86	17.45	135	2,52,513.23	4,06,756.56	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	69	1,07,461.29	1,11,208.37	3.49	5	3,397.13	6,023.66	2 - 168
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	2	2,635.83	6,334.96	36 - 111
3	ASSAM	45	27,704.18	33,843.20	22.16	7	5,748.91	11,156.30	12 - 131
4	BIHAR	91	76,252.26	1,11,749.59	46.55	11	31,379.06	47,928.04	12 - 123
5	GOA	10	4,292.52	4,292.52	0.00	0	0.00	0.00	-
6	GUJARAT	49	51,576.03	57,483.90	11.45	3	12,097.90	17,760.58	36 - 84
7	HARYANA	29	21,083.41	22,987.06	9.03	1	1,108.00	2,288.00	91 - 91
8	HIMACHAL PRADESH	13	17,058.17	26,566.39	55.74	1	3,919.59	9,394.80	147 - 147
9	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	220 - 220
10	KARNATAKA	47	82,362.96	88,262.78	7.16	4	2,604.52	3,671.22	2 - 36
11	KERALA	25	39,778.48	41,953.10	5.47	2	5,195.35	5,960.21	15 - 17
12	MADHYA PRADESH	60	67,550.02	72,708.48	7.64	2	12,195.09	14,208.38	21 - 96
13	MAHARASHTRA	128	1,85,529.12	1,97,693.64	6.56	13	17,326.15	23,193.13	2 - 192
14	MANIPUR	2	4,670.86	14,025.69	200.28	1	4,454.17	13,809.00	108 - 108
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	0	0.00	0.00	-
16	MIZORAM	4	3,406.61	5,981.14	75.57	1	2,393.47	4,968.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	79 - 79
18	ODISHA	84	97,034.62	1,02,058.71	5.18	10	21,836.21	27,256.98	3 - 147
19	PUNJAB	33	17,042.04	17,146.31	0.61	2	1,142.54	1,242.81	1 - 22
20	RAJASTHAN	56	46,045.92	48,245.10	4.78	5	2,372.03	3,770.91	3 - 67
21	SIKKIM	9	3,476.73	6,281.03	80.66	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	76	1,19,890.58	1,37,033.24	14.30	5	6,104.29	9,853.00	69 - 155
23	TRIPURA	9	4,422.36	8,345.05	88.70	2	1,711.63	4,057.00	31 - 60
24	UTTAR PRADESH	110	1,34,449.08	1,36,016.30	1.17	6	3,328.93	4,972.83	5 - 239
25	WEST BENGAL	53	57,557.73	66,897.02	16.23	6	11,840.03	15,790.35	12 - 324
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	22	55,263.55	62,738.78	13.53	2	1,633.32	2,105.89	5 - 83
29	CHHATISGARH	45	78,684.04	82,285.57	4.58	4	13,013.75	14,949.31	24 - 117
30	JHARKHAND	48	47,744.98	52,545.65	10.05	4	15,950.68	18,088.15	20 - 48
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	4	7,241.32	12,619.50	63 - 102
32	TELANGANA	41	34,378.10	37,015.07	7.67	5	2,730.04	3,648.31	33 - 144
33	MULTI STATE	160	3,40,790.26	4,44,636.07	30.47	23	52,672.68	86,230.22	11 - 178
Total		1423	18,25,733.41	21,44,298.86	17.45	135	2,52,513.23	4,06,756.56	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	166	3
2	ROAD TRANSPORT AND HIGHWAYS	136	2
3	PETROLEUM	50	2
4	POWER	48	3
5	COAL	15	0
6	URBAN DEVELOPMENT	13	0
7	STEEL	7	1
8	ATOMIC ENERGY	4	1
9	HEAVY INDUSTRY	2	0
10	SHIPPING AND PORTS	2	0
11	TELECOMMUNICATIONS	2	0
12	MINES	1	0
	Total	446	12

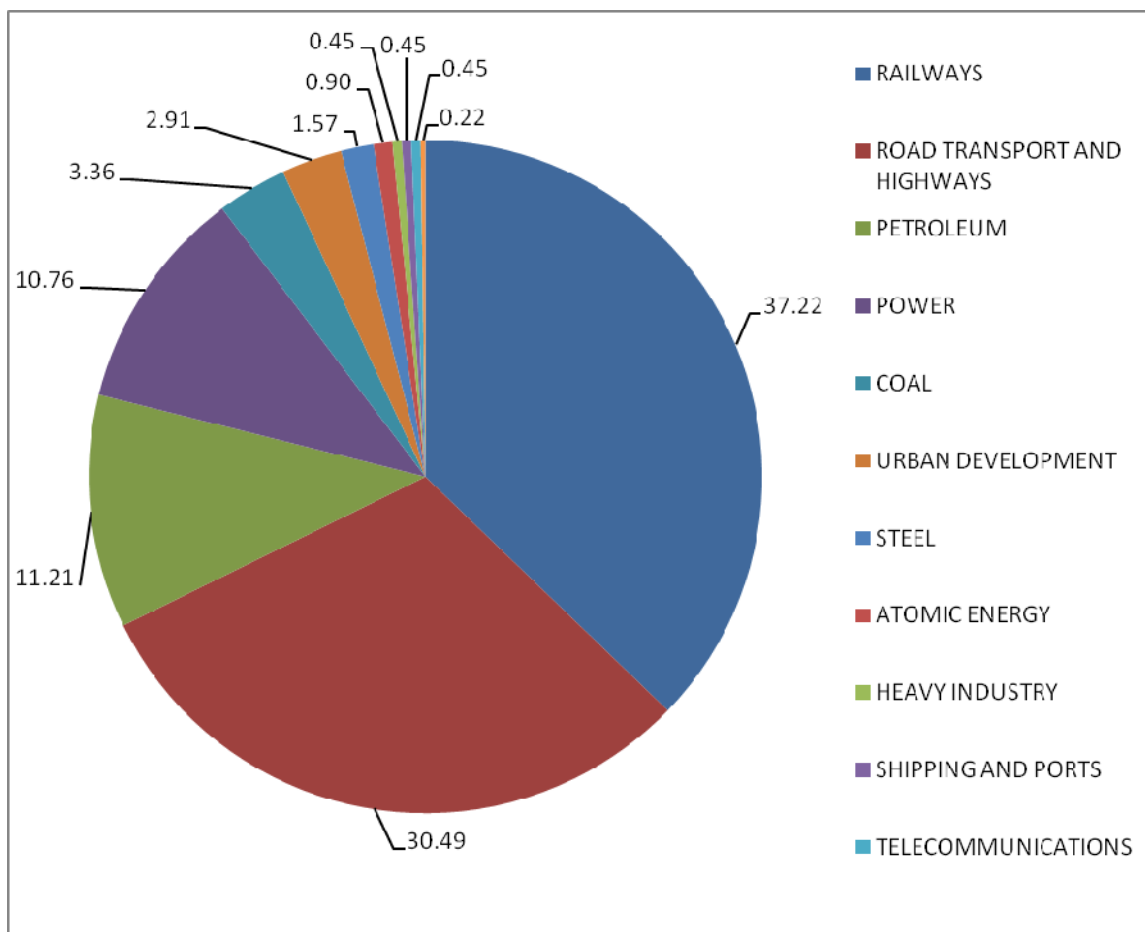


TABLE-14

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	444
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects added in Current Month	2
No of Projects in Current Month	446

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	160 (35.87%)	8 (1.79%)	121(27.13%)	30 (6.73%)	127(8.48%)	446
Latest Approved (Date)	125 (28.03%)	9 (2.02%)	159(35.65%)	26 (5.83%)	127(8.48%)	446

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	371	11,59,859.66	13,48,140.06	5,00,905.82	37.20	1,88,280.40	16.20
Project with Revision in Cost	75	3,44,733.72	3,66,054.75	1,79,851.99	49.10	21,321.03	6.20
Total	446	15,04,593.38	17,14,194.81	6,80,757.81	39.71	2,09,601.43	13.93
Original Cost of All Projects							
Original Cost	446	14,11,925.12	17,14,194.81	6,80,757.81	39.71	3,02,269.69	21.41

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	160	6,39,805.23	7,84,182.36	4,26,898.24	54.40	1,44,377.13	22.57
Latest Approved (RCE)	125	4,07,824.19	5,07,634.63	2,44,343.35	48.10	99,810.44	24.47

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	12	24,859.89	29,871.56	22,904.31	76.70	5,011.67	20.20
Total	12	24,859.89	29,871.56	22,904.31	76.68	5,011.67	20.16

TABLE-15

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	COAL	15	62,755.83	62,756.63	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0.00
5	PETROLEUM	50	1,95,340.65	1,99,957.56	2.36	9	20,876.75	28,907.95	38.47
6	POWER	48	2,76,605.54	3,37,391.29	21.98	27	1,66,239.92	2,27,025.67	36.57
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	166	4,03,504.69	6,01,007.67	48.95	101	1,39,218.39	3,41,976.69	145.64
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	17	20,393.80	33,696.27	65.23
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,002.50	3.62	4	20,852.09	26,202.57	25.66
Total		446	14,11,925.12	17,14,194.81	21.41	163	4,14,820.95	7,26,218.25	75.07

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-16

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	90,958.16	95,039.23	4.49	6	7,059.25	11,498.32	62.88
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	2	8,782.23	25,676.30	192.37
3	ASSAM	7	14,133.37	19,246.86	36.18	3	5,631.90	10,882.00	93.22
4	BIHAR	25	46,998.89	79,080.11	68.26	17	34,744.64	66,825.86	92.33
5	GUJARAT	15	34,067.85	41,024.32	20.42	3	13,943.72	20,900.19	49.89
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	2	6,886.58	16,394.80	138.07
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	1017.96
9	KARNATAKA	20	68,819.94	74,167.37	7.77	7	21,059.46	26,602.90	26.32
10	KERALA	10	32,670.86	34,554.11	5.76	2	6,154.29	8,061.58	30.99
11	MADHYA PRADESH	19	44,612.91	50,527.82	13.26	9	26,272.05	34,660.36	31.93
12	MAHARASHTRA	43	1,49,592.87	1,60,291.40	7.15	15	28,028.61	40,609.03	44.88
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	210.02
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	107.56
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	28.95
17	ODISHA	31	74,652.16	78,738.33	5.47	9	22,712.87	27,645.96	21.72
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	13	25,544.64	26,900.58	5.31	4	3,178.64	4,534.58	42.66
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	27	99,477.88	1,14,389.14	14.99	11	25,501.52	40,412.78	58.47
22	TRIPURA	3	2,458.01	6,218.51	152.99	3	2,458.01	6,218.51	152.99
23	UTTAR PRADESH	42	1,01,729.00	1,04,025.61	2.26	6	22,392.65	25,461.21	13.70
24	WEST BENGAL	24	46,282.76	53,304.29	15.17	8	13,999.31	21,035.27	50.26
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
26	DELHI	7	50,481.91	57,816.75	14.53	3	6,254.39	13,589.23	117.28
27	CHHATISGARH	14	64,313.38	68,809.25	6.99	5	16,797.78	21,293.65	26.76
28	JHARKHAND	12	34,294.40	38,289.18	11.65	4	20,763.50	24,758.28	19.24
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	4	8,654.06	14,154.57	63.56
30	TELANGANA	6	19,991.02	22,068.25	10.39	2	2,378.60	4,455.84	87.33
31	MULTI STATE	65	2,98,881.27	3,99,010.24	33.50	31	96,138.79	1,98,448.34	106.42
Total		446	14,11,925.12	17,14,194.81	21.41	163	4,14,820.95	7,26,218.25	75.07

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 133
2	COAL	15	62,755.83	62,756.63	0.00	4	9,323.71	9,323.71	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	29,772.34	-1.19	6	25,381.34	25,023.34	9 - 49
5	PETROLEUM	50	1,95,340.65	1,99,957.56	2.36	14	78,460.45	83,531.90	3 - 81
6	POWER	48	2,76,605.54	3,37,391.29	21.98	29	1,84,385.78	2,26,230.39	2 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	-
8	RAILWAYS	166	4,03,504.69	6,01,007.67	48.95	60	1,05,315.30	1,81,024.29	3 - 324
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	36	53,277.51	55,955.80	2 - 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,002.50	3.62	6	1,03,207.14	1,03,579.93	5 - 64
Total		446	14,11,925.12	17,14,194.81	21.41	160	6,39,805.23	7,84,182.36	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-18

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	95,039.23	4.49	10	50,233.04	52,355.67	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	7	14,133.37	19,246.86	36.18	3	7,225.70	12,060.86	12 - 88
4	BIHAR	25	46,998.89	79,080.11	68.26	10	32,659.99	48,769.28	12 - 123
5	GUJARAT	15	34,067.85	41,024.32	20.42	2	13,417.88	18,538.88	2 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	2	5,836.38	11,311.59	29 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	5	16,904.75	42,353.75	10 - 220
9	KARNATAKA	20	68,819.94	74,167.37	7.77	8	36,654.45	37,424.70	3 - 264
10	KERALA	10	32,670.86	34,554.11	5.76	4	14,207.19	14,840.82	8 - 33
11	MADHYA PRADESH	19	44,612.91	50,527.82	13.26	5	16,555.71	18,569.00	5 - 96
12	MAHARASHTRA	43	1,49,592.87	1,60,291.40	7.15	18	70,713.37	76,227.69	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	31	74,652.16	78,738.33	5.47	11	27,389.68	32,035.88	3 - 147
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	13	25,544.64	26,900.58	5.31	5	16,906.01	17,755.08	2 - 89
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	27	99,477.88	1,14,389.14	14.99	7	58,478.51	61,494.54	18 - 133
22	TRIPURA	3	2,458.01	6,218.51	152.99	1	1,142.00	3,407.00	60 - 60
23	UTTAR PRADESH	42	1,01,729.00	1,04,025.61	2.26	14	36,416.38	37,741.49	2 - 239
24	WEST BENGAL	24	46,282.76	53,304.29	15.17	11	20,451.13	24,084.76	11 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
26	DELHI	7	50,481.91	57,816.75	14.53	3	41,198.73	41,571.52	5 - 38
27	CHHATISGARH	14	64,313.38	68,809.25	6.99	3	28,002.78	29,459.82	24 - 111
28	JHARKHAND	12	34,294.40	38,289.18	11.65	6	20,635.13	22,328.00	9 - 48
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	4	23,343.06	28,569.50	15 - 102
30	TELANGANA	6	19,991.02	22,068.25	10.39	4	14,450.02	14,727.41	3 - 144
31	MULTI STATE	65	2,98,881.27	3,99,010.24	33.50	17	66,778.72	98,383.16	3 - 178
Total		446	14,11,925.12	17,14,194.81	21.41	160	6,39,805.23	7,84,182.36	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	4	72,241.00	74,849.00	36 - 133
2	COAL	15	62,755.83	62,756.63	0.00	4	9,323.71	9,323.71	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	29,772.34	-1.19	5	9,856.34	9,498.34	9 - 32
5	PETROLEUM	50	1,98,901.89	1,99,957.56	0.53	4	15,278.00	17,835.00	3 - 78
6	POWER	48	2,95,603.20	3,37,391.29	14.14	17	84,417.94	1,02,270.36	2 - 147
7	HEAVY INDUSTRY	2	5,281.30	5,381.30	1.89	0	0.00	0.00	-
8	RAILWAYS	166	4,66,181.66	6,01,007.67	28.92	50	94,153.55	1,56,923.49	3 - 239
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	36	53,277.51	55,955.80	2 - 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,002.50	3.41	4	55,942.14	56,314.93	5 - 64
Total		446	15,04,593.38	17,14,194.81	13.93	125	4,07,824.19	5,07,634.63	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of cost overrun in projects with respect to latest schedule RS. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	74.69
2	COAL	15	62,755.83	62,756.63	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0.00
5	PETROLEUM	50	1,98,901.89	1,99,957.56	0.53	4	8,085.04	11,891.19	47.08
6	POWER	48	2,95,603.20	3,37,391.29	14.14	20	1,32,898.48	1,74,686.57	31.44
7	HEAVY INDUSTRY	2	5,281.30	5,381.30	1.89	1	3,727.30	3,827.30	2.68
8	RAILWAYS	166	4,66,181.66	6,01,007.67	28.92	95	1,10,517.09	2,53,405.82	129.29
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	17	20,393.80	33,696.27	65.23
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,002.50	3.41	4	21,154.18	26,202.57	23.86
Total		446	15,04,593.38	17,14,194.81	13.93	144	3,30,838.89	5,51,711.52	66.76

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-21

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	133- 133
2	COAL	15	62,755.83	62,756.63	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0- 0
5	PETROLEUM	50	1,98,901.89	1,99,957.56	0.53	1	3,030.00	5,751.00	78- 78
6	POWER	48	2,95,603.20	3,37,391.29	14.14	7	37,573.38	55,425.80	12- 147
7	HEAVY INDUSTRY	2	5,281.30	5,381.30	1.89	0	0.00	0.00	0- 0
8	RAILWAYS	166	4,66,181.66	6,01,007.67	28.92	31	45,712.53	1,09,917.99	3- 239
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	10	10,602.24	13,280.53	2- 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,002.50	3.41	1	1,219.21	1,592.00	5- 5
Total		446	15,04,593.38	17,14,194.81	13.93	52	1,14,963.36	2,16,731.32	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-22

Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 133
2	COAL	15	62,755.83	62,756.63	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0- 0
5	PETROLEUM	50	1,95,340.65	1,99,957.56	2.36	6	16,691.40	22,676.95	13- 78
6	POWER	48	2,76,605.54	3,37,391.29	21.98	19	1,24,276.91	1,66,121.52	10- 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	166	4,03,504.69	6,01,007.67	48.95	38	52,366.65	1,28,240.68	3- 324
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	10	10,602.24	13,280.53	2- 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,002.50	3.62	1	1,219.21	1,592.00	5- 5
Total		446	14,11,925.12	17,14,194.81	21.41	77	2,33,441.41	3,79,255.68	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	95,039.23	4.49	3	2,819.63	5,300.26	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	7	14,133.37	19,246.86	36.18	2	4,760.55	9,682.00	12 - 88
4	BIHAR	25	46,998.89	79,080.11	68.26	8	29,968.32	46,077.61	12 - 123
5	GUJARAT	15	34,067.85	41,024.32	20.42	1	11,459.00	16,580.00	54 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	1	3,919.59	9,394.80	147 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	220 - 220
9	KARNATAKA	20	68,819.94	74,167.37	7.77	2	1,824.74	2,611.00	3 - 3
10	KERALA	10	32,670.86	34,554.11	5.76	1	4,588.29	5,245.96	15 - 15
11	MADHYA PRADESH	19	44,612.91	50,527.82	13.26	2	12,195.09	14,208.38	21 - 96
12	MAHARASHTRA	43	1,49,592.87	1,60,291.40	7.15	9	16,084.12	21,598.44	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	31	74,652.16	78,738.33	5.47	7	20,476.76	25,122.96	3 - 147
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	13	25,544.64	26,900.58	5.31	2	1,482.93	2,332.00	62 - 67
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	27	99,477.88	1,14,389.14	14.99	2	5,271.29	8,287.32	124 - 133
22	TRIPURA	3	2,458.01	6,218.51	152.99	1	1,142.00	3,407.00	60 - 60
23	UTTAR PRADESH	42	1,01,729.00	1,04,025.61	2.26	3	2,720.76	4,194.88	5 - 239
24	WEST BENGAL	24	46,282.76	53,304.29	15.17	5	11,542.71	15,176.35	18 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
26	DELHI	7	50,481.91	57,816.75	14.53	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	14	64,313.38	68,809.25	6.99	2	12,477.78	13,934.82	24 - 111
28	JHARKHAND	12	34,294.40	38,289.18	11.65	2	15,492.47	17,185.34	20 - 48
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	3	7,127.06	12,353.50	63 - 102
30	TELANGANA	6	19,991.02	22,068.25	10.39	1	1,266.60	1,544.00	33 - 33
31	MULTI STATE	65	2,98,881.27	3,99,010.24	33.50	12	48,983.97	81,148.41	12 - 178
Total		446	14,11,925.12	17,14,194.81	21.41	77	2,33,441.41	3,79,255.68	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>POWER</u>						
1	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT	01/2014	1,788.41	09/2017	2,333.71	01/2019	1,727.37
2	WESTERN REGION STRENGTHENING SCHEME-XVI	07/2016	150.99	07/2018	150.99	01/2019	97.16
3	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	08/2008	771.00	02/2013	1,624.00	02/2018	1,577.20
	<u>RAILWAYS</u>						
4	GULBARGA-BIDAR,SCR(NL)	02/1998	242.42	N.A.	369.70	01/2019	1,172.64
5	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	N.A.	1,025.00	03/2017	1,022.21
	<u>TELECOMMUNICATIONS</u>						
6	MAHARASHTRA CORE (LOT1) Central Sector Projects	08/2017	167.68	04/2018	167.68	01/2019	32.44

TABLE-25

List of projects added Rs.150 Crore and above					(January 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	CHITRA EAST (RCE) OCP	8/2018	513.98	3/2024	513.98	3/2024
	<u>PETROLEUM</u>					
2	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	11,130.00	3/2023	11,130.00	3/2023
3	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	206.26	3/2021	206.26	3/2021
	<u>SHIPPING AND PORTS</u>					
4	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA	7/2016	1,799.00	5/2021	1,799.00	5/2021
5	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	5/2016	970.00	5/2020	970.00	5/2020

TABLE-26

Milestones (Cumulative due & achieved) Rs.150 Crore and above	
Total	4506
Achieved up to month	2354

TABLE-27

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(January 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) BHAVNI	3,492.00	6,100.00	09/2010	03/2019	10/2021	31
	<u>FERTILISERS</u>						
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. RCF	482.85	482.85	12/2017	01/2019	02/2019	1
	<u>STEEL</u>						
3	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	03/2019	06/2019	3
4	CENTRAL DISPATCH YARD RINL	320.66	320.66	08/2018	02/2019	06/2019	4
5	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) RINL	465.85	465.85	07/2018	01/2019	06/2019	5
	<u>PETROLEUM</u>						
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP IOCL	356.00	356.00	05/2019	12/2018	01/2019	1
7	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE MANGALORE REFIN	135.00	170.70	03/2019	03/2019	05/2019	2
8	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE IOCL	212.00	212.00	01/2021	01/2021	04/2021	3
9	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR IOCL	318.80	318.80	08/2021	08/2021	11/2021	3
10	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU IOCL	466.43	466.43	10/2020	05/2021	08/2021	3
11	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH IOCL	466.00	466.00	04/2021	04/2021	07/2021	3
12	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY IOCL	822.66	822.66	11/2018	11/2018	03/2019	4
13	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND IOCL	236.00	236.00	06/2020	06/2020	10/2020	4

List of projects reporting additional delayed Rs.150 Crore and above							(January 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	ASSAM RENEWAL PROJECT FOR GROUP A ONGC	2,465.15	2,378.86	03/2013	03/2019	12/2019	9
15	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY IOCL	3,076.00	4,190.00	09/2017	06/2018	03/2019	9
16	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE IOCL	348.00	348.00	01/2021	01/2021	10/2021	9
	<u>POWER</u>						
17	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B PGCIL	307.18	307.18	11/2017	01/2019	02/2019	1
18	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) PGCIL	305.04	305.04	03/2017	01/2019	02/2019	1
19	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION PGCIL	431.89	431.89	02/2019	02/2019	03/2019	1
20	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ PGCIL	322.30	322.30	02/2019	02/2019	03/2019	1
21	WESTERN REGION STRENGTHENING SCHEME-V PGCIL	477.69	738.48	09/2010	02/2019	04/2019	2
22	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH PGCIL	5,151.37	5,151.37	03/2018	06/2019	08/2019	2
23	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	639.46	06/2014	03/2019	06/2019	3
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX PGCIL	539.82	539.82	06/2016	03/2019	06/2019	3
25	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	06/2019	09/2019	3
26	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT PGCIL Central Sector Projects	175.64	175.64	09/2018	06/2019	09/2019	3
27	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT PGCIL	193.14	193.14	06/2019	06/2019	09/2019	3
28	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,891.41	04/2016	02/2019	06/2019	4
29	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	550.18	11/2016	06/2019	12/2019	6
30	DHUKWAN SMALL HYDRO PROJECT THDCIL	195.42	294.60	02/2014	03/2019	10/2019	7


List of projects reporting additional delayed Rs.150 Crore and above							(January 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>HEALTH AND FAMILY WELFARE</u>						
31	CNCI KOLKATA WEST BENGAL HSCC	244.00	244.00	09/2018	09/2018	03/2019	6
	<u>RAILWAYS</u>						
32	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) NWR	808.85	808.85	08/2022	08/2022	09/2022	1
33	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) NWR	653.19	1,116.00	03/2014	03/2019	05/2019	2
34	ALWAR-BANDIKUI DOUBLING NWR	242.09	349.00	02/2019	03/2019	05/2019	2
35	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) NWR	829.74	1,216.00	03/2015	06/2020	10/2020	4
36	BANGURGRAM-GURIYA PATCH DOUBLING NWR	246.08	348.55	12/2019	06/2019	11/2019	5
37	THIYAT HAMIRA-SANU NWR	236.93	294.90	10/2018	10/2018	06/2019	8
38	DAUSA-GANGAPUR CITY(NL),NWR NWR	410.08	795.01	02/2019	02/2019	12/2019	10
39	ROSA-SITAPUR CANTT-BURHWAL DOUBLING NER	1,295.42	1,295.42	03/2022	02/2019	12/2019	10
40	CHHAPRA-BALLIA UP NER	295.00	477.31	01/2019	02/2019	01/2020	11
41	PHULERA - DIGANA DOUBLING NWR	600.00	685.99	03/2020	03/2020	04/2022	25
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
42	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	174.34	03/2008	01/2019	02/2019	1
43	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) NHAI	296.19	254.00	03/2020	05/2019	06/2019	1
44	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS NHAI	567.51	567.51	03/2018	01/2019	03/2019	2
45	FOUR LANING OF AURANGABAD - YEDISHI NHAI PPP (BOT)	1,871.34	1,871.34	01/2018	12/2018	02/2019	2
46	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION NHAI	227.49	227.49	01/2019	01/2019	03/2019	2
47	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST NHAI	244.90	244.90	05/2019	05/2019	07/2019	2

List of projects reporting additional delayed Rs.150 Crore and above							(January 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
48	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 NHAI	602.95	602.95	06/2016	12/2018	03/2019	3
49	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR NHAI PPP (BOT)	1,583.79	1,583.79	01/2019	01/2019	06/2019	5
50	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN NHAI	649.50	649.50	03/2019	03/2019	12/2019	9
	<u>URBAN DEVELOPMENT</u>						
51	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN CPWD	549.31	540.42	07/2019	10/2019	11/2019	1


TABLE-28

<u>Sector wise analysis of projects</u> Rs.150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	722,41.00	74,849.00	41,080.32
CIVIL AVIATION	1	314.61	3,14.61	441.33	85.79
COAL	98	97,468.86	970,21.71	96,940.36	29,719.04
FERTILISERS	6	1,781.92	17,93.57	1,793.57	715.65
MINES	5	7,078.62	70,78.62	7,078.62	565.50
STEEL	13	32,529.65	325,29.65	32,317.05	21,728.92
PETROLEUM	139	2,33,745.66	2,372,16.14	2,37,274.59	75,197.04
POWER	92	2,93,659.85	3,681,10.40	3,55,596.43	2,35,070.36
HEAVY INDUSTRY	2	3,272.00	52,81.30	5,381.30	3,268.26
HEALTH AND FAMILY WELFARE	20	8,129.23	81,29.23	8,246.52	2,946.15
RAILWAYS	366	4,85,586.03	5,474,19.86	6,97,755.98	1,69,590.53
ROAD TRANSPORT AND HIGHWAYS	605	4,11,159.45	4,117,29.58	4,25,383.97	1,59,378.55
SHIPPING AND PORTS	7	6,557.29	69,82.09	6,995.32	2,439.94
TELECOMMUNICATIONS	5	16,310.53	163,09.33	27,539.33	9,169.02
URBAN DEVELOPMENT	58	1,60,566.07	1,610,98.60	1,66,251.85	73,724.43
DEFENCE PRODUCTION	2	453.64	4,54.00	453.64	167.86
Grand total	1423	18,25,733.41	19,73,709.69	21,44,298.86	8,24,847.36

Graphical Presentation of All Projects w.r.t. Original Schedule

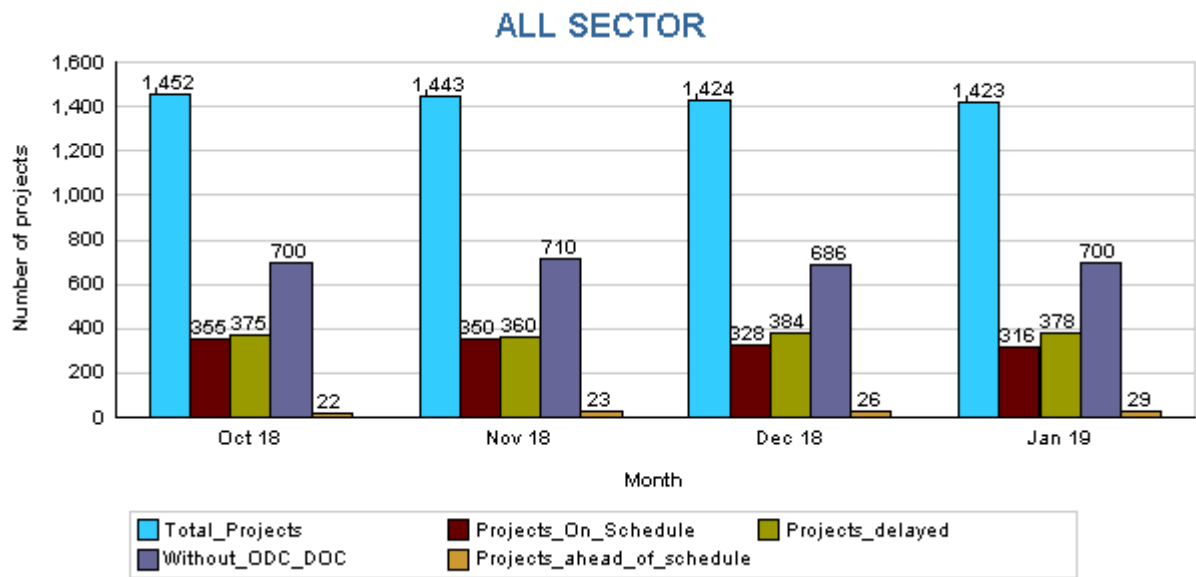


Break-up of 378 Delayed projects in January 2019

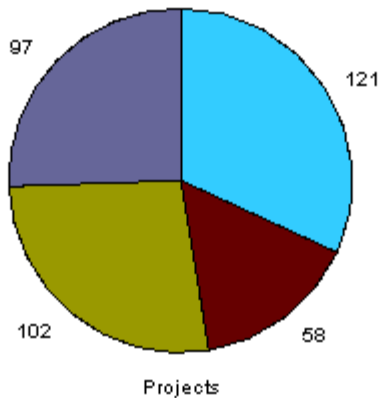


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

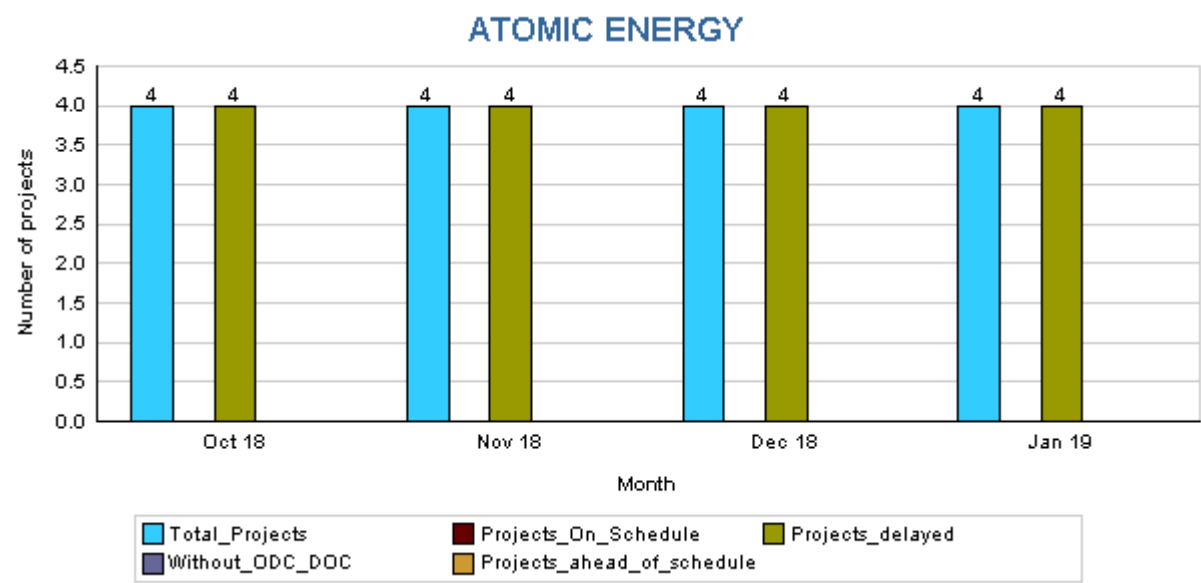


Break-up of 4 Delayed projects in January 2019

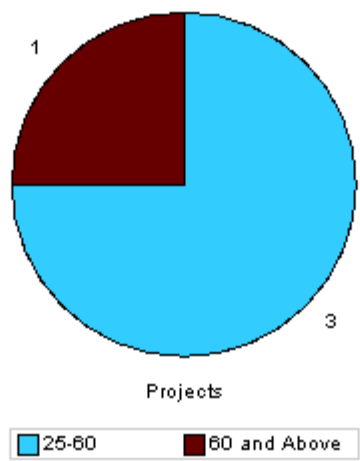


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

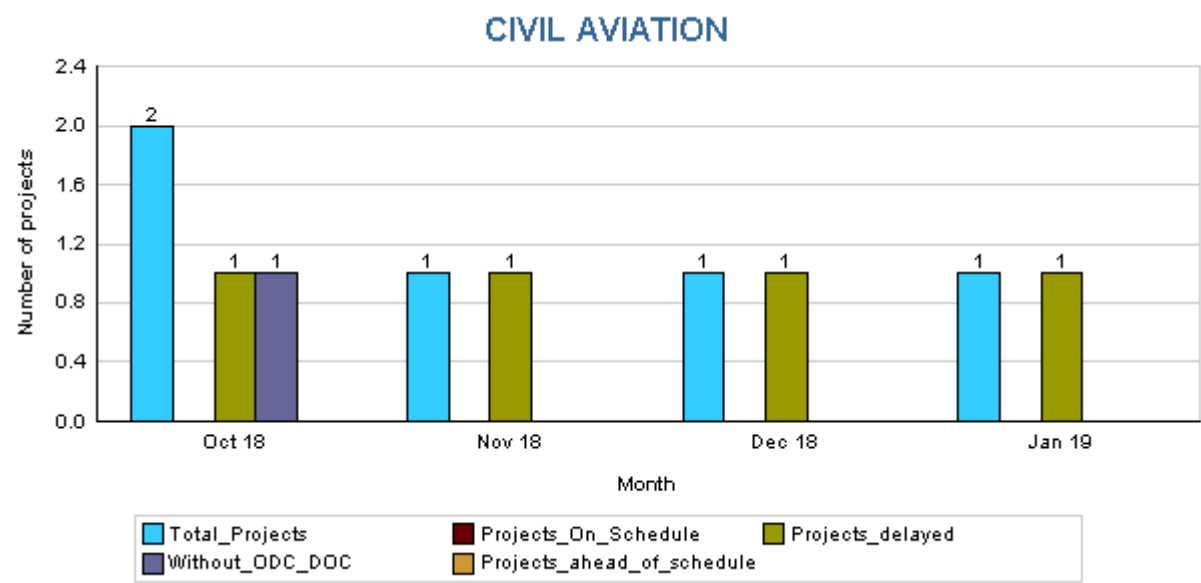


Break-up of 1 Delayed projects in January 2019




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

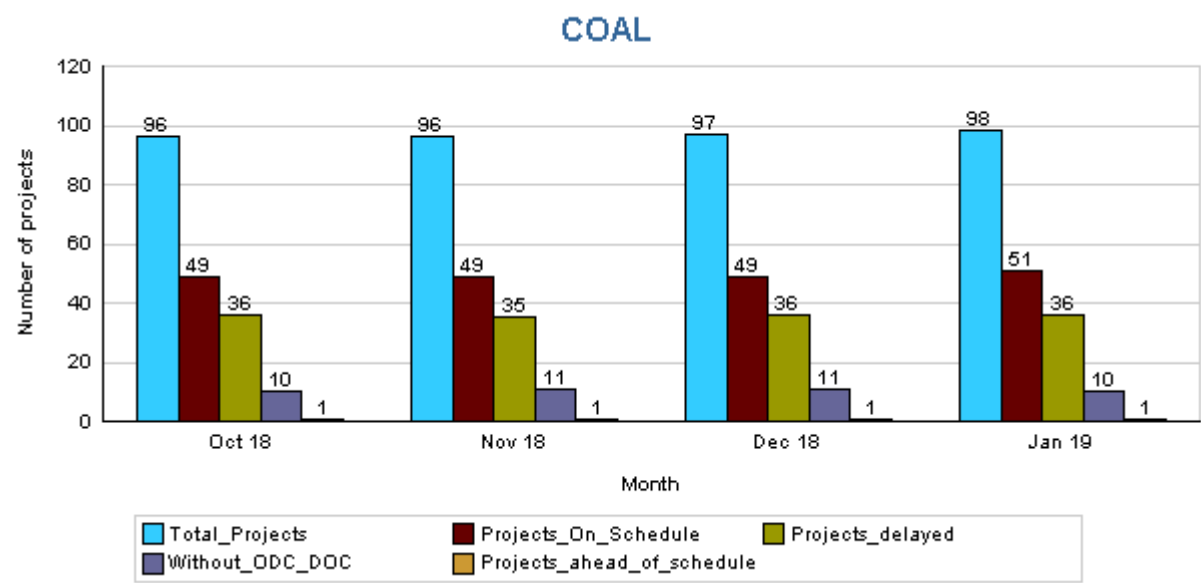


Break-up of 36 Delayed projects in January 2019

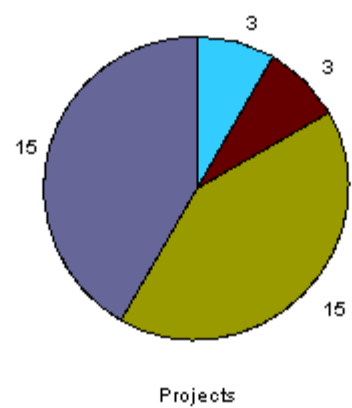


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

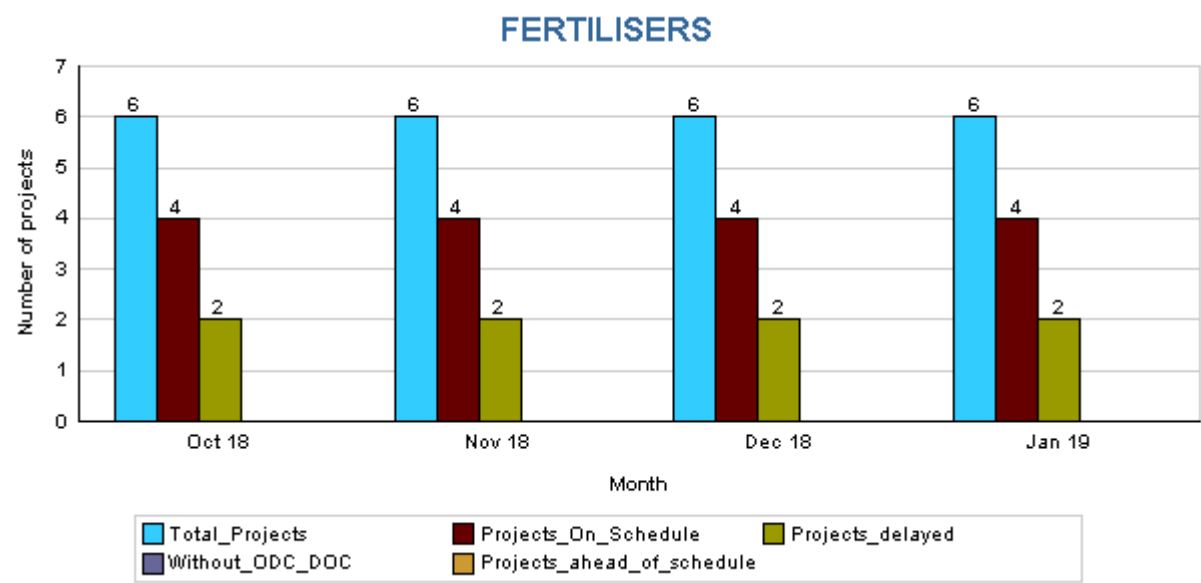


Break-up of 2 Delayed projects in January 2019

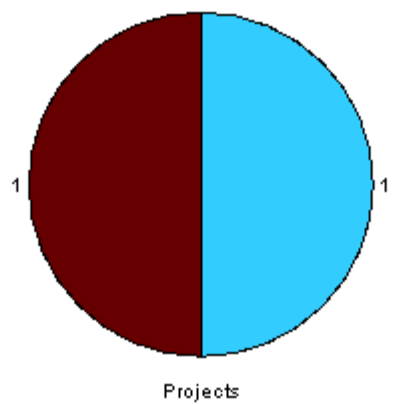

Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

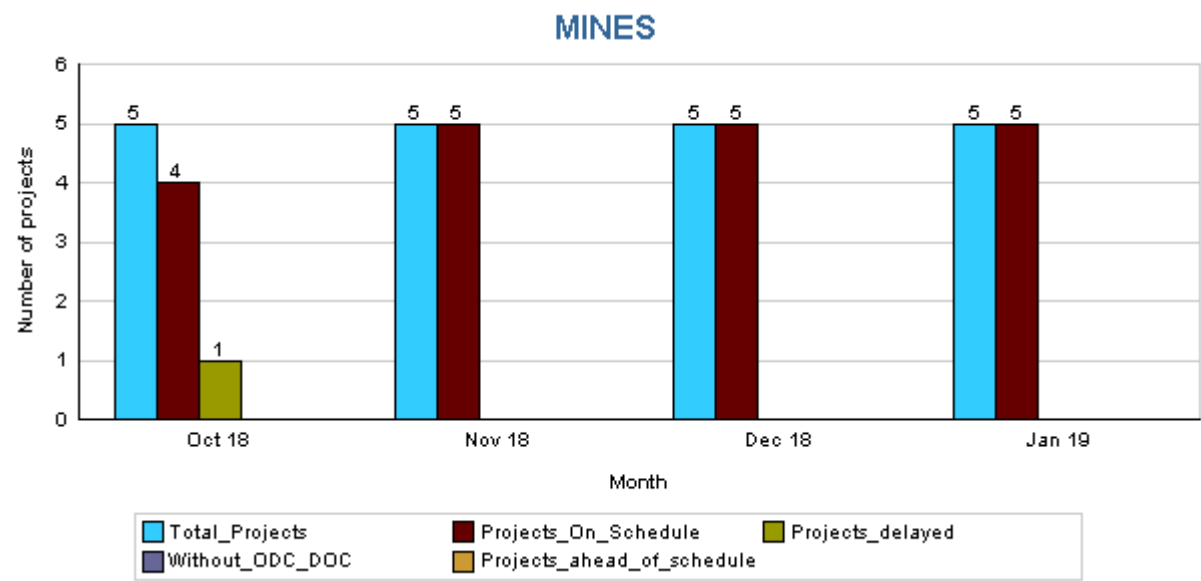


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

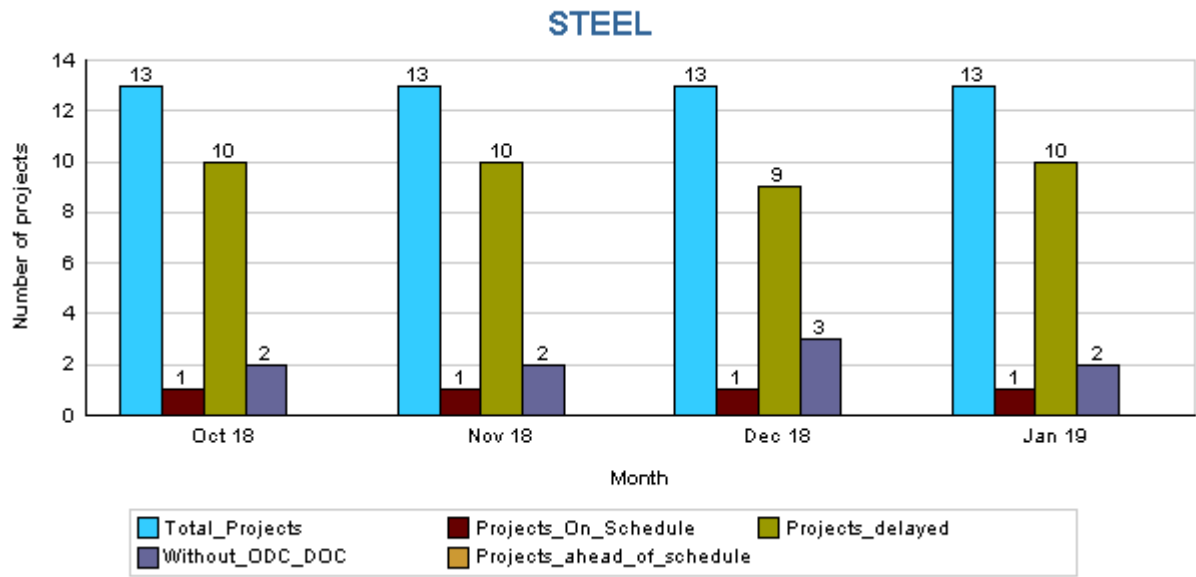


Break-up of 10 Delayed projects in January 2019

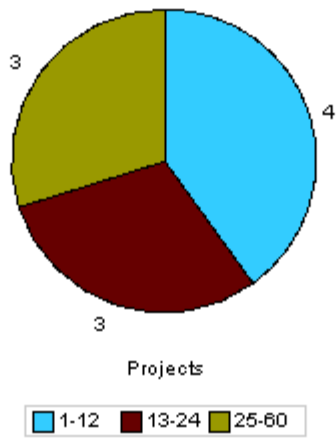


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

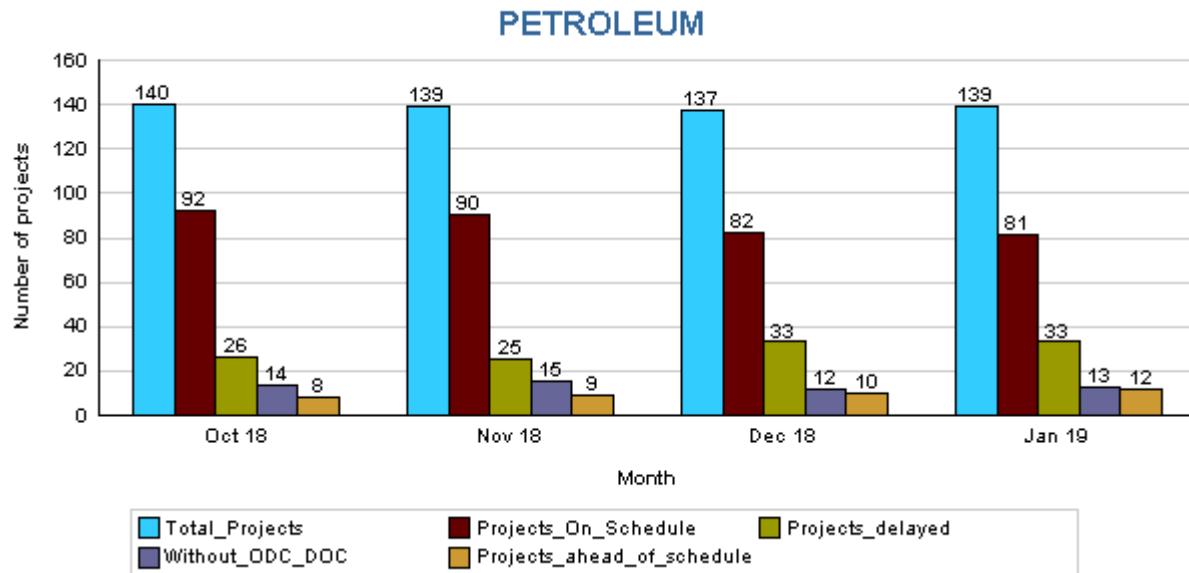


Break-up of 33 Delayed projects in January 2019

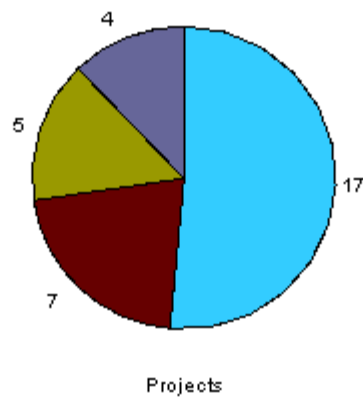


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

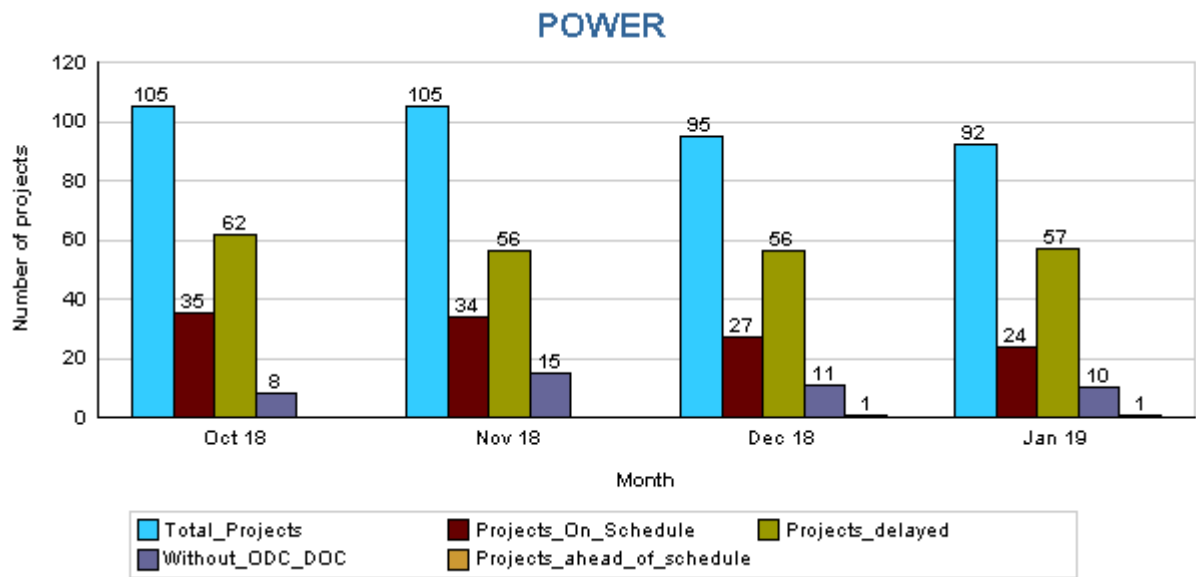


Break-up of 57 Delayed projects in January 2019

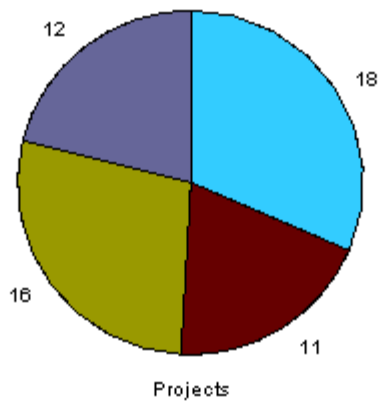


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

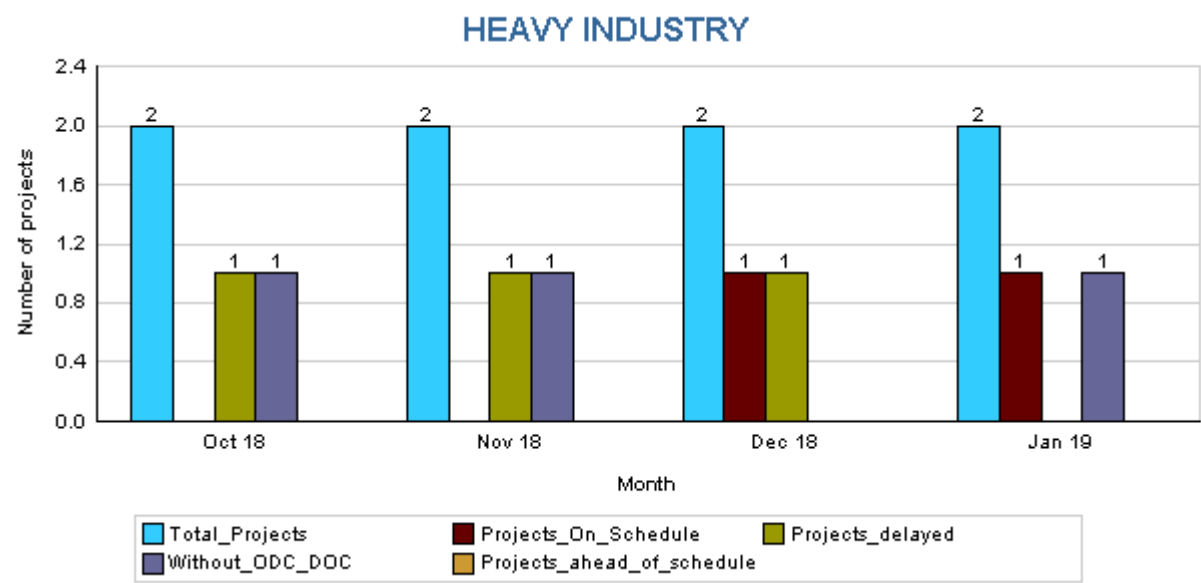


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

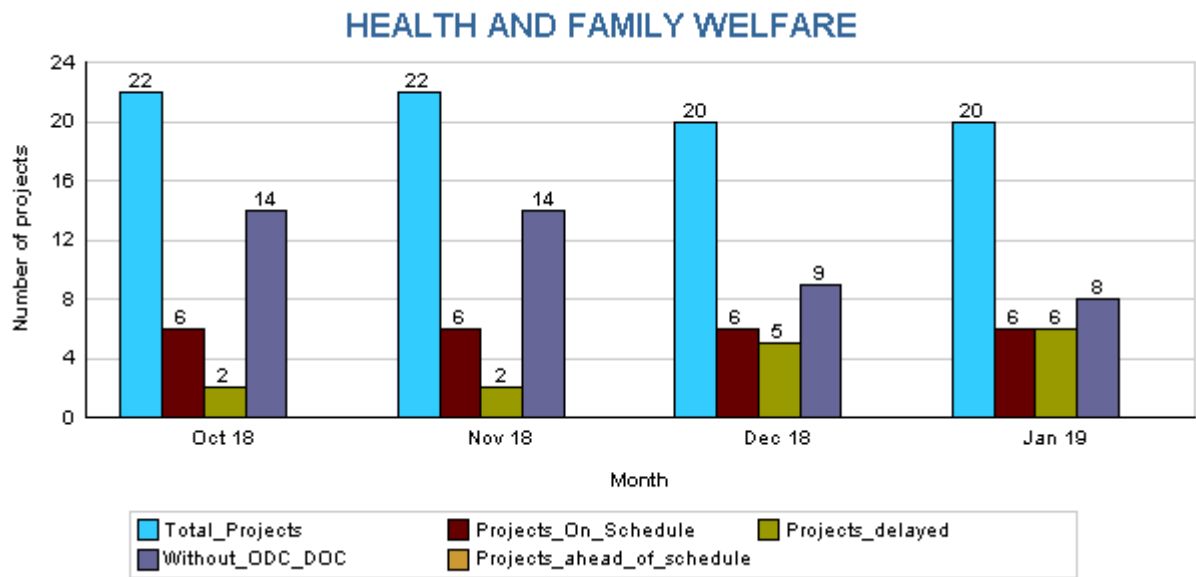


Break-up of 6 Delayed projects in January 2019

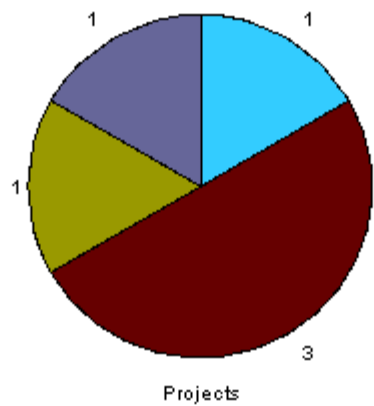

Graphical Presentation of All Projects w.r.t. Original Schedule

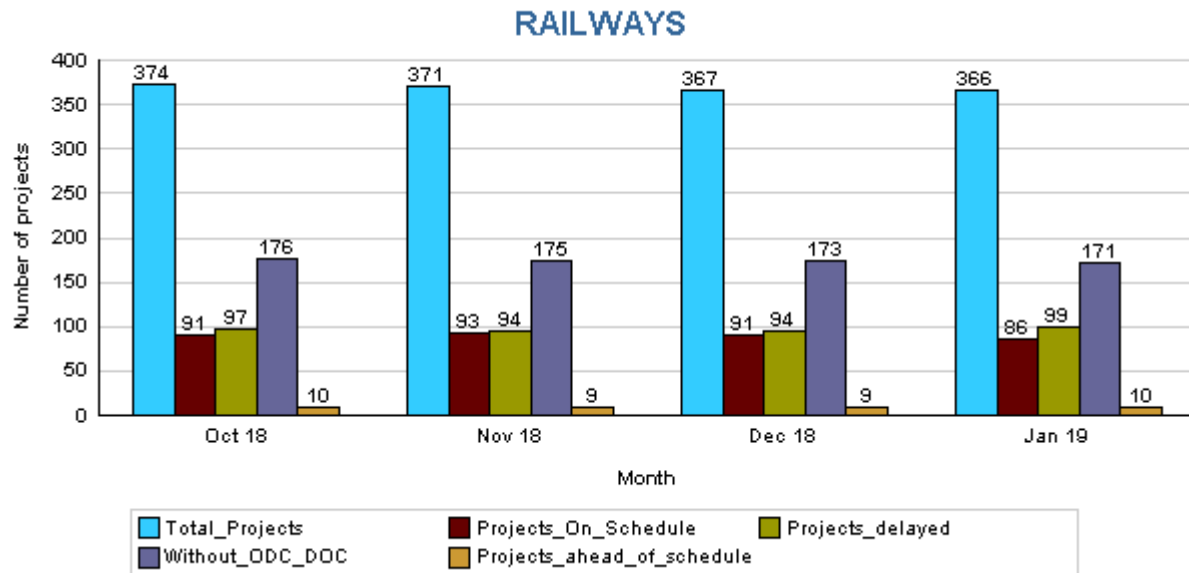


Break-up of 99 Delayed projects in January 2019

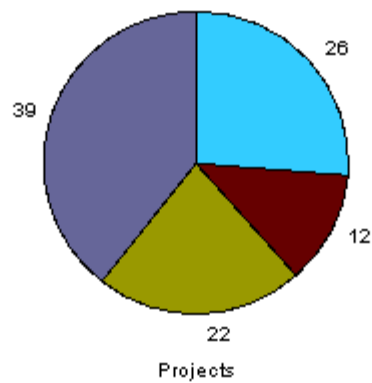


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

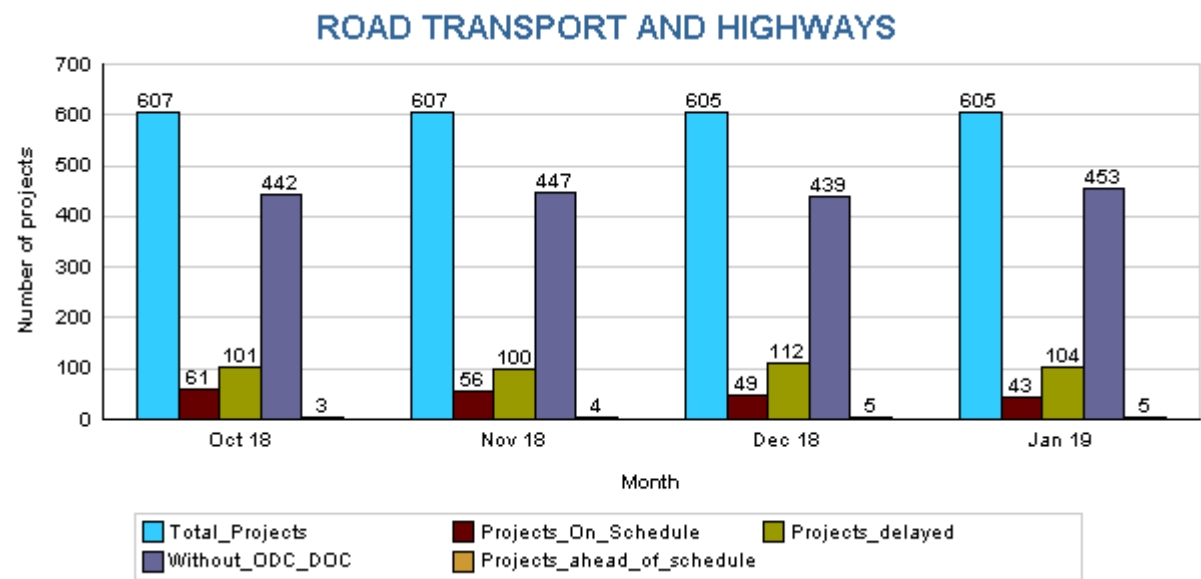


Break-up of 104 Delayed projects in January 2019

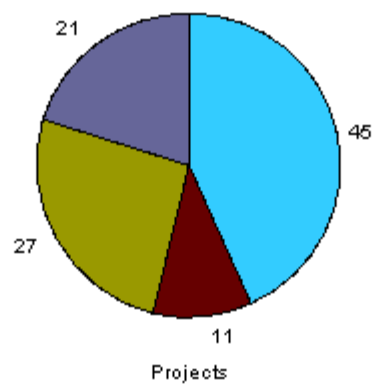


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

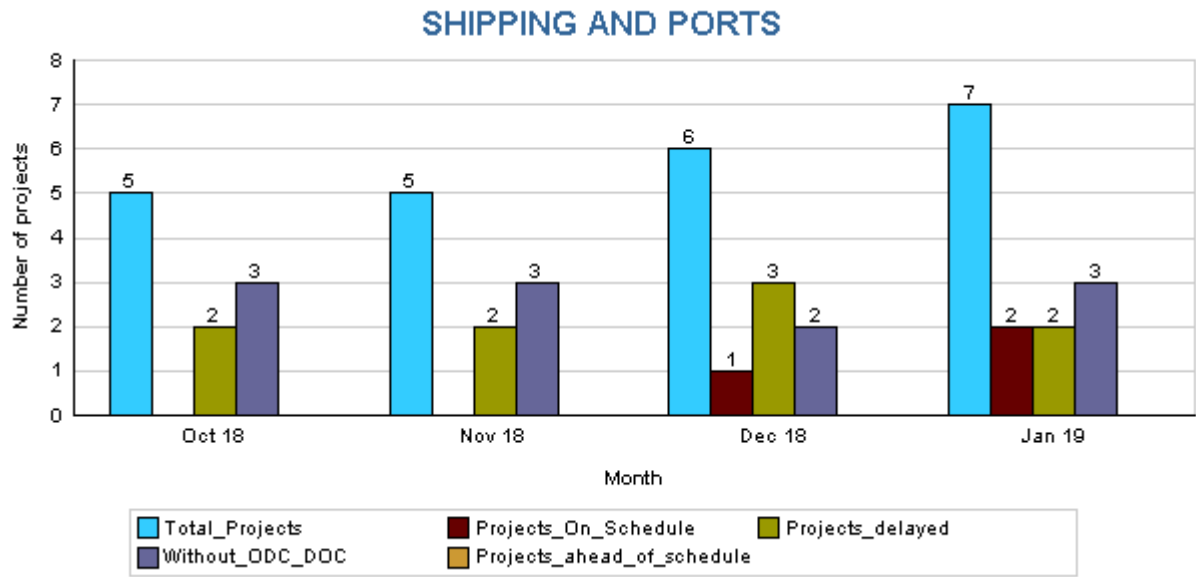


Break-up of 2 Delayed projects in January 2019

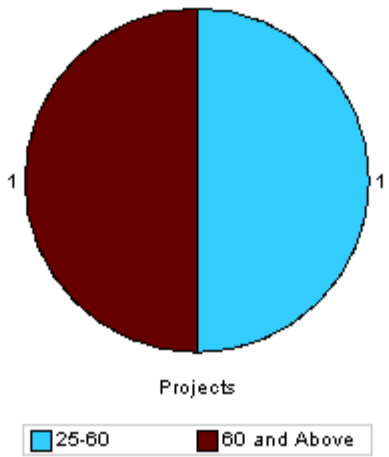


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

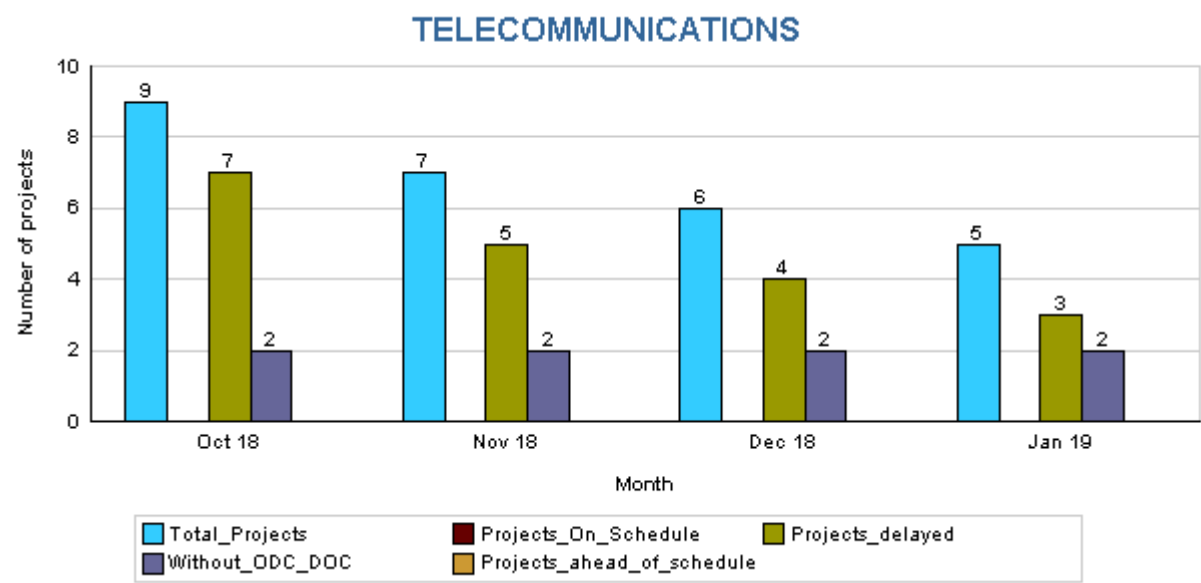


Break-up of 3 Delayed projects in January 2019

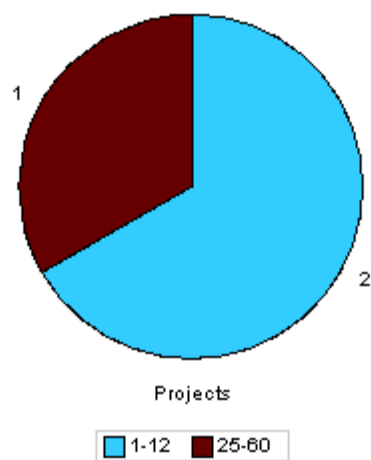


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

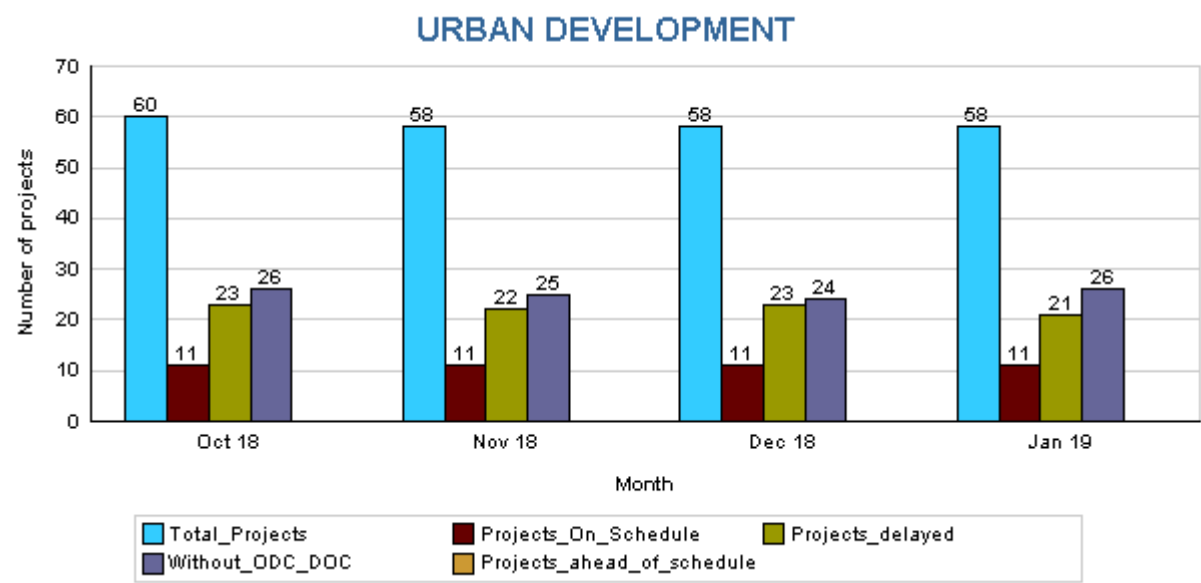


Break-up of 21 Delayed projects in January 2019

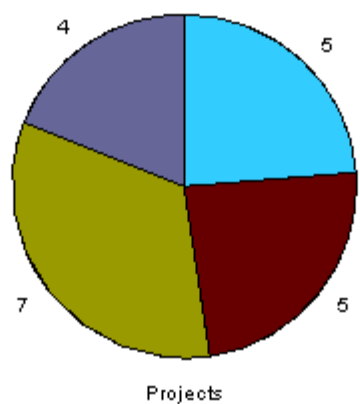

Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	5	5	7	4

Graphical Presentation of All Projects w.r.t. Original Schedule

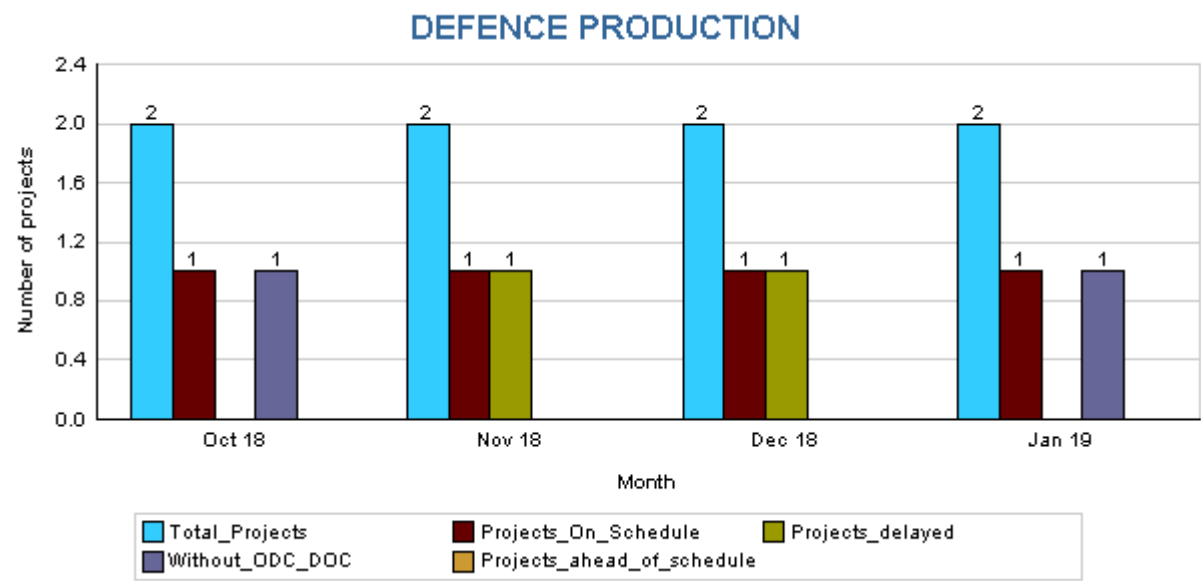

Delay in Months

TABLE-29

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	12,987.00	12/2015 11/2016	06/2020	54(O) 43(R)	51/70
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	10,285.00	12/2016 03/2017	12/2020	48(O) 45(R)	38/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,100.00	5,738.32	09/2010 -	10/2021	133(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	12,070.00	11/2020 -	11/2023	36(O) -	21/76
	Total		67,120.00 -	74,849.00	41,080.32				193/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
	Total		314.61 -	441.33	85.79				0/0
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,857.01	03/2023 -	03/2023	0(O) -	14/18
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	1,957.98	03/2023 -	03/2023	0(O) -	6/20
8	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.21	03/2023 -	03/2023	0(O) -	1/12
9	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 -	459.49	184.45	03/2015 -	03/2020	60(O) -	5/9
10	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	1/7
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	206.84	03/2014 -	03/2020	72(O) -	0/4
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.50	03/2016 -	03/2019	36(O) -	7/9
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	168.00	03/2016 -	03/2019	36(O) -	4/7
14	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	83.39	03/2022 -	03/2022	0(O) -	2/9
15	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	71.55	03/2020 -	03/2020	0(O) -	4/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97	335.97	51.70	03/2018	-	-	1/7
17	AMGAON OPENCASST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10	316.10	60.38	03/2020	03/2020	0(O)	0/6
18	DURGAPUR OPENCASST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24	916.24	3.88	03/2023	03/2023	0(O)	1/10
19	MADANNAGAR OPENCASST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32	1,875.32	.00	03/2024	03/2024	0(O)	1/4
20	VIJAY WEST OPENCASST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95	976.95	75.96	03/2026	03/2026	0(O)	0/1
21	MAHAMAYA OPENCASST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26	410.26	9.53	03/2026	03/2026	0(O)	0/0
22	JHIRIA WEST OPENCASST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97	389.97	.00	03/2026	03/2026	0(O)	0/0
23	MAGADH OC 20 MTY (CCL) - [N06000015]JCL,JHARKHAND ,	08/2008	706.40	706.40	185.62	07/2012	03/2021	104(O)	4/5
24	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND ,	08/2007	163.51	163.51	103.83	03/2011	03/2020	108(O)	3/5
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND ,	12/2007	179.87	179.87	175.17	03/2012	03/2019	84(O)	3/5
26	TAPIN OCP (2.5 MTY) - [N06000086]JCL,JHARKHAND ,	08/2008	264.68	264.68	178.37	03/2012	03/2019	84(O)	4/5
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCL,JHARKHAND ,	12/2009	510.85	510.85	340.33	03/2016	03/2019	36(O)	5/5
28	KARMA OCP (1.0MTY) - [N06000088]JCL,JHARKHAND ,	06/2009	162.46	162.46	89.21	03/2014	03/2019	60(O)	5/5
29	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88	339.88	12.08	04/2014	10/2018	-	4/7
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27	1,230.27	334.71	04/2015	04/2019	48(O)	2/6
31	AMRAPALI OC(12MTY) - [N06000103]JCL,JHARKHAND ,	02/2012	858.11	858.11	185.00	03/2020	03/2020	0(O)	6/6
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52	555.52	5.24	03/2021	03/2021	0(O)	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35	988.35	45.26	04/2017	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45	289.45	194.20	05/2014	04/2018	-	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82	269.82	179.95	04/2014	04/2018	-	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69	359.69	45.29	03/2022	03/2022	0(O)	1/22
37	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98	513.98	.00	03/2024	03/2024	0(O)	0/0
38	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40	486.57	266.38	03/2012	-	-	1/3
39	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64	203.82	106.07	03/2023	03/2021	-24(O)	3/10
40	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60	481.60	.00	03/2023	03/2023	0(O)	2/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
41	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	114.73	03/2021 -	03/2021	0(O) -	3/9
42	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	41.76	03/2021 -	03/2021	0(O) -	1/7
43	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/7
44	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	24.21	03/2023 -	03/2023	0(O) -	0/4
45	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	112.26	03/2021 -	03/2021	0(O) -	2/4
46	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	17.67	03/2022 -	03/2022	0(O) -	0/0
47	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	236.49	03/2021 -	03/2021	0(O) -	0/9
48	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022	0(O) -	0/9
49	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	191.97	03/2020 -	03/2020	0(O) -	7/11
50	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	397.95	03/2020 -	03/2020	0(O) -	3/8
51	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	143.29	03/2021 -	03/2021	0(O) -	12/12
52	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	208.09	03/2018 -	03/2018	-	7/7
53	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	97.41	03/2023 02/2017	03/2023	0(O) 73(R)	7/11
54	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	88.13	03/2019 -	03/2019	0(O) -	10/13
55	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	105.38	03/2020 -	03/2020	0(O) -	5/10
56	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	116.35	03/2021 -	03/2021	0(O) -	2/6
57	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	238.47	03/2025 -	03/2025	0(O) -	5/13
58	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 333.43	333.43	.07	03/2023 03/2024	03/2024	12(O) 0(R)	3/10
59	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 313.34	313.34	26.44	03/2021 09/2018	03/2024	36(O) 66(R)	3/6
60	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	67.18	03/2020 -	03/2020	0(O) -	2/6
61	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	254.72	03/2019 -	03/2019	0(O) -	2/9
62	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	129.79	03/2019 -	03/2019	0(O) -	2/8
63	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	258.23	03/2020 -	03/2020	0(O) -	0/0
64	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	58.04	03/2022 -	03/2022	0(O) -	0/3
65	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	16.00	03/2022 -	03/2022	0(O) -	1/12

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
66	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	91.22	03/2021 -	03/2021	0(O) -	1/6
67	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2018	-	10/10
68	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	421.62	03/2017 -	03/2020	36(O) -	11/12
69	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	584.87	03/2013 -	03/2020	84(O) -	8/9
70	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	267.99	03/2010 -	03/2020	120(O) -	3/4
71	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	235.51	03/2012 -	03/2021	108(O) -	5/5
72	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	397.41	03/2013 -	03/2020	84(O) -	6/9
73	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	123.19	03/2019 -	03/2024	60(O) -	2/9
74	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	690.11	03/2026 -	03/2026	0(O) -	6/15
75	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	65.58	03/2019 -	03/2021	24(O) -	5/6
76	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	30.04	03/2018 -	03/2020	24(O) -	3/5
77	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	425.28	03/2021 -	03/2021	0(O) -	5/9
78	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	.00	03/2027 -	03/2027	0(O) -	0/0
79	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	8.71	09/2019 -	09/2019	0(O) -	0/0
80	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	173.06	12/2019 -	12/2019	0(O) -	0/0
81	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	5,892.64	12/2015 12/2018	03/2019	39(O) 3(R)	28/35
82	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	400.53	06/2015 09/2019	09/2019	51(O) 0(R)	5/7
83	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	186.91	03/2012 -	03/2024	144(O) -	35/42
84	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
85	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132(O) -	0/2
86	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	154.21	03/2015 -	03/2019	48(O) -	30/31
87	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	159.87	03/2012 -	-	-	5/6
88	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	12.69	03/2015 -	03/2021	72(O) -	0/5
89	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2021	72(O) -	4/29
90	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	437.51	353.61	03/2015 -	03/2021	72(O) -	6/13

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
91	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	204.26	06/2015 -	03/2019	45(O) -	35/36
92	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	146.45	07/2016 -	03/2020	44(O) -	21/28
93	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	160.45	03/2016 -	03/2019	36(O) -	37/39
94	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	79.96	03/2019 -	03/2019	0(O) -	10/18
95	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.00	03/2018 -	03/2019	12(O) -	0/9
96	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	.00	03/2020 -	03/2020	0(O) -	1/17
97	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	.00	03/2019 -	03/2019	0(O) -	0/11
98	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA 6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 -	1,131.28	715.00	03/2018 -	03/2019	12(O) -	10/10
99	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	4,524.70	11/2021 -	11/2021	0(O) -	0/0
100	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	302.68	03/2022 -	03/2022	0(O) -	8/13
101	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	393.45	03/2018 -	03/2020	24(O) -	11/16
102	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	2,661.73	215.56	08/2019 -	08/2019	0(O) -	0/19
103	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/21
	Total		97,468.86 -	96,940.36	29,719.04				491/990
	<u>FERTILISERS</u>								
104	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	27.83	11/2019 -	11/2019	0(O) -	0/2
105	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	145.98	11/2016 04/2019	04/2019	29(O) 0(R)	1/13
106	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 482.85	482.85	430.86	12/2017 01/2019	02/2019	14(O) 1(R)	0/1
107	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	50.89	04/2020 -	04/2020	0(O) -	1/14
108	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	27.56	11/2019 -	11/2019	0(O) -	0/2
109	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	32.53	11/2019 -	11/2019	0(O) -	0/2
	Total		1,781.92 -	1,793.57	715.65				2/34

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>MINES</u>								
110	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N1000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	96.98	04/2021 04/2021	04/2021	0(O) 0(R)	3/3
111	UTKAL D AND E COAL BLOCK - [N1000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	302.60	01/2020 01/2020	01/2020	0(O) 0(R)	1/2
112	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N1000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020	0(O) -	2/2
113	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N1000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.00	04/2021 04/2021	04/2021	0(O) 0(R)	1/1
114	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N1000014]NALCO,TAMIL NADU ,	09/2017	166.62 166.62	166.62	134.00	06/2019 -	06/2019	0(O) -	0/1
	Total		7,078.62 -	7,078.62	565.50				7/9
	<u>STEEL</u>								
115	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	247.65	10/2016 -	03/2020	41(O) -	1/2
116	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,133.76	12/2017 -	09/2019	21(O) -	4/6
117	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	150.36	08/2018 -	06/2019	10(O) -	2/4
118	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	316.25	07/2018 -	06/2019	11(O) -	2/4
119	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	128.44	04/2015 -	-	-	4/5
120	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	14,659.90	05/2015 06/2019	06/2019	49(O) 0(R)	62/86
121	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	31.88	06/2020 -	06/2020	0(O) -	5/12
122	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	384.47	10/2017 -	06/2020	32(O) -	0/2
123	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	878.27	12/2017 -	06/2019	18(O) -	1/2
124	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	108.38	09/2017 -	-	-	0/0
125	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	78.83	06/2019 -	06/2020	12(O) -	0/1
126	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,638.63	04/2018 -	05/2019	13(O) -	3/3
127	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	972.10	09/2018 -	06/2019	9(O) -	3/5
	Total		32,529.65 -	32,317.05	21,728.92				87/132

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	PETROLEUM								
128	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	2,864.07	07/2020 -	07/2020	0(O) -	72/111
129	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	288.56	09/2019 -	09/2019	0(O) -	20/27
130	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	1,691.99	06/2020 08/2021	08/2021	14(O) 0(R)	0/20
131	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
132	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
133	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 207.80	207.80	32.71	09/2018 02/2019	02/2019	5(O) 0(R)	0/5
134	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	41.38	04/2021 -	04/2021	0(O) -	0/0
135	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	1.53	04/2021 -	07/2021	3(O) -	0/0
136	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	.00	04/2022 -	04/2022	0(O) -	0/0
137	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	148.35	02/2019 -	01/2019	-1(O) -	4/10
138	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.86	2,112.54	03/2013 12/2019	12/2019	81(O) 0(R)	6/15
139	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	330.35	89.48	01/2014 11/2019	11/2019	70(O) 0(R)	6/7
140	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	217.07	08/2019 -	08/2019	0(O) -	4/13
141	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,346.72	11/2019 -	11/2019	0(O) -	12/17
142	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 249.85	244.70	101.71	05/2020 05/2020	05/2020	0(O) 0(R)	0/5
143	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8(O) -	0/0
144	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	315.44	09/2019 -	09/2019	0(O) -	6/7
145	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	543.91	2.08	02/2020 -	02/2020	0(O) -	1/14
146	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	74.97	02/2020 -	02/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
147	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
148	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]OCL, BIHAR ,	07/2015	822.66 -	822.66	868.92	11/2018 -	03/2019	4(O) -	7/8
149	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]OCL, BIHAR ,	05/2016	664.00 -	664.00	455.62	12/2020 -	02/2020	-10(O) -	4/4
150	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]OCL, BIHAR ,	09/2015	324.00 -	324.00	107.15	06/2020 -	06/2020	0(O) -	3/3
151	LPG BP PROJECT MOTIHARI - [N16000317]OCL, BIHAR ,	05/2018	206.50 -	206.50	.00	03/2021 -	03/2021	0(O) -	7/26
152	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]OCL, BIHAR ,	12/2017	199.36 -	199.36	.00	10/2020 -	10/2020	0(O) -	0/0
153	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL, BIHAR ,	10/2017	359.25 -	359.25	38.20	10/2022 -	10/2022	0(O) -	0/0
154	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]OCL, BIHAR ,	07/2018	189.00 -	189.00	4.04	01/2021 -	01/2021	0(O) -	0/0
155	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]OCL, BIHAR ,	04/2018	522.00 -	522.00	2.56	03/2021 -	03/2021	0(O) -	0/0
156	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL, CHHATTISGARH ,	12/2016	300.00 -	300.00	.00	04/2021 -	04/2021	0(O) -	0/0
157	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,513.89	05/2019 10/2019	10/2019	5(O) 0(R)	0/14
158	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT ,	05/2015	1,671.22 567.22	567.22	457.84	11/2019 12/2018	02/2019	-9(O) 2(R)	0/5
159	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT ,	04/2016	327.78 -	200.00	134.00	04/2018 -	03/2019	11(O) -	18/20
160	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC, GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	307.27	03/2026 03/2026	03/2026	0(O) 0(R)	0/10
161	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]OCL, GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	69.50	07/2020 -	07/2020	0(O) -	0/0
162	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]OCL, GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	-	-	0/0
163	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]OCL, GUJARAT ,	08/2017	1,342.00 -	1,342.00	3.90	08/2020 -	08/2020	0(O) -	1/1
164	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]OCL, GUJARAT ,	03/2018	3,380.00 -	3,380.00	1,399.13	09/2019 -	09/2019	0(O) -	0/9
165	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]OCL, GUJARAT ,	10/2017	906.00 -	906.00	13.76	02/2020 -	02/2020	0(O) -	0/0
166	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]OCL, GUJARAT ,	03/2018	588.20 -	588.20	.00	-	-	-	3/17
167	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL, HARYANA ,	11/2017	255.00 -	255.00	15.68	11/2020 -	11/2020	0(O) -	0/46

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
168	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	2.76	02/2020 -	02/2020	0(O) -	0/0
169	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	1,068.35	07/2019 -	07/2019	0(O) -	0/9
170	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	128.87	08/2020 -	08/2020	0(O) -	0/0
171	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	205.41	05/2019 -	01/2019	-4(O) -	4/13
172	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	112.58	09/2019 -	02/2019	-7(O) -	3/3
173	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 -	-	-	8/12
174	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 910.23	910.23	115.49	03/2023 03/2022	03/2022	-12(O) 0(R)	0/10
175	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	06/2020	0(O) -	0/0
176	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	27.55	10/2022 -	10/2022	0(O) -	6/9
177	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	27.11	10/2022 -	10/2022	0(O) -	0/0
178	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
179	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	803.00	02/2020 -	02/2020	0(O) -	0/0
180	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019	0(O) -	6/8
181	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	129.95	03/2019 05/2019	05/2019	2(O) 0(R)	5/11
182	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019	0(O) -	7/9
183	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	581.00	.00	03/2020 -	03/2020	0(O) -	0/0
184	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	.00	03/2021 -	03/2021	0(O) -	0/0
185	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	352.66	10/2017 -	03/2019	17(O) -	39/52
186	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	2,627.83	08/2018 11/2019	11/2019	15(O) 0(R)	0/20
187	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	501.94	02/2020 10/2020	10/2020	8(O) 0(R)	0/20
188	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	.00	03/2023 -	03/2023	0(O) -	0/0
190	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	11.66	06/2020 -	10/2020	4(O) -	0/0
191	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,577.15	1,577.15	1,195.62	05/2013 03/2019	03/2019	70(O) 0(R)	1/8
192	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 12/2019	12/2019	57(O) 0(R)	0/17
193	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,597.60	04/2019 03/2019	03/2019	-1(O) 0(R)	0/9
194	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	1,888.28	03/2019 05/2020	05/2020	14(O) 0(R)	0/5
195	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 4,619.94	4,619.94	4,079.85	12/2017 03/2020	03/2020	27(O) 0(R)	4/5
196	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,123.52	04/2018 05/2019	05/2019	13(O) 0(R)	0/10
197	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	514.20	08/2021 -	08/2021	0(O) -	4/4
198	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	172.74	02/2020 -	02/2020	0(O) -	0/10
199	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	122.99	12/2019 -	12/2019	0(O) -	0/0
200	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	14.11	01/2021 -	04/2021	3(O) -	0/0
201	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	9.20	01/2021 -	10/2021	9(O) -	0/0
202	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	8.74	01/2021 -	01/2021	0(O) -	0/0
203	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	0/0
204	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	299.26	05/2019 05/2019	05/2019	0(O) 0(R)	0/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
205	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	249.63	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
206	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	219.96	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
207	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 968.61	968.61	668.42	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
208	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,006.83	4,006.83	1,671.49	05/2021 05/2021	05/2021	0(O) 0(R)	0/15
209	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	72.05	08/2020 -	08/2020	0(O) -	0/15
210	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	58.33	06/2020 -	06/2020	0(O) -	0/0
211	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	112.87	12/2019 -	12/2019	0(O) -	4/5
212	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,561.00	3,397.00	2,382.96	12/2018 -	03/2019	3(O) -	35/39
213	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	543.05	09/2011 -	-	-	0/3
214	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 -	-	-	8/8
215	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	610.73	10/2014 02/2019	02/2019	52(O) 0(R)	33/40
216	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	199.43	03/2017 -	06/2019	27(O) -	2/15
217	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	579.41	12/2020 -	12/2020	0(O) -	4/4
218	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	1,213.52	12/2020 -	08/2020	-4(O) -	4/4
219	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	579.18	10/2019 -	03/2019	-7(O) -	5/5
220	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	201.34	07/2018 10/2020	10/2020	27(O) 0(R)	21/36
221	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	1,048.00	06/2020 -	06/2020	0(O) -	16/24
222	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	122.05	02/2019 -	02/2019	0(O) -	12/13
223	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	26.81	10/2020 -	10/2020	0(O) -	6/12
224	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	44.43	12/2019 -	12/2019	0(O) -	6/22

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
225	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40	2,000.00	1,112.98	12/2019 12/2020	12/2019	0(O) -12(R)	16/24
226	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00	2,433.00	1,002.53	12/2020	12/2020	0(O)	14/24
227	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00	3,437.00	1,028.31	12/2020	12/2020	0(O)	14/24
228	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 3,030.00	5,751.00	2,038.08	12/2012 02/2019	06/2019	78(O) 4(R)	17/42
229	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00	2,677.00	60.42	03/2021	03/2021	0(O)	5/26
230	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00	500.00	.00	06/2017	-	-	0/0
231	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00	3,308.00	19.60	12/2021	12/2021	0(O)	0/20
232	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00	3,150.00	2,494.51	09/2017 12/2018	12/2018	-	5/6
233	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00	1,933.00	864.97	12/2020	12/2020	0(O)	16/24
234	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00	429.00	283.06	01/2019	01/2019	0(O)	6/6
235	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59	161.59	34.31	12/2019	12/2019	0(O)	17/26
236	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 243.53	243.53	34.34	07/2022	07/2022	0(O)	0/0
237	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00	315.00	3.37	12/2021	12/2021	0(O)	0/2
238	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	181.20	181.20	17.11	07/2022	07/2022	0(O)	0/0
239	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00	4,807.08	24.09	10/2021	07/2021	-3(O)	0/0
240	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00	750.00	26.58	12/2020	12/2020	0(O)	0/14
241	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50	1,297.50	.02	10/2021	10/2021	0(O)	0/0
242	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00	370.00	17.84	03/2013	-	-	0/24
243	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80	229.80	69.04	-	-	-	4/26
244	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00	711.00	11.12	06/2020	06/2020	0(O)	0/0
245	RESID UPGRADEATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36	3,110.36	2,915.42	11/2015	-	-	52/52
246	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00	678.00	5.12	02/2017	-	-	0/0
247	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 390.52	390.52	174.22	03/2019	04/2019	1(O)	0/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
248	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00	4,497.00	370.09	12/2018	12/2020	24(O)	4/4
249	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00	228.00	1.84	06/2020	06/2020	0(O)	4/4
250	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00	1,858.00	646.29	12/2019	12/2019	0(O)	0/0
251	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00	421.00	22.22	08/2020	08/2020	0(O)	0/0
252	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43	466.43	1.18	10/2020	08/2021	10(O)	0/0
253	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94	800.00	618.58	12/2018	03/2019	3(O)	17/20
254	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49	287.49	106.74	04/2022	04/2022	0(O)	29/33
255	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80	318.80	13.93	08/2021	11/2021	3(O)	0/0
256	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64	666.64	264.64	09/2019	09/2019	0(O)	0/6
257	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40	255.40	.10	08/2020	08/2020	0(O)	0/0
258	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00	676.00	7.46	12/2021	12/2021	0(O)	2/2
259	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10	160.10	28.75	02/2020	02/2020	0(O)	18/26
260	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL ,	03/2014	3,076.00	4,190.00	3,224.62	09/2017	03/2019	18(O)	6/7
261	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00	694.00	535.04	10/2018	06/2019	8(O)	0/15
262	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00	1,021.00	4.45	12/2020	12/2020	0(O)	0/0
263	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00	1,740.00	25.46	12/2020	12/2020	0(O)	11/24
264	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02	163.02	33.79	04/2020	04/2020	0(O)	17/26
265	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40	2,934.40	889.89	09/2019	09/2019	0(O)	0/11
266	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00	3,712.00	22.47	09/2022	06/2021	-15(O)	1/1
	Total		2,33,745.66	2,37,274.59	75,197.04				692/1467

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
267	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,448.57	09/2010 -	-	-	0/0
268	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	6,900.51	12/2009 03/2019	03/2019	111(O) 0(R)	30/30
269	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 8,150.00	8,150.00	7,220.84	09/2011 06/2018	01/2019	88(O) 7(R)	36/37
270	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	15,441.10	01/2011 04/2021	04/2021	123(O) 0(R)	26/47
271	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	7,998.00	7,511.72	05/2014 -	05/2019	60(O) -	3/18
272	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	12,593.00	01/2018 -	05/2020	28(O) -	31/34
273	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR ,	05/2015	436.68 -	602.44	540.02	12/2016 -	03/2019	27(O) -	14/19
274	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 790.30	790.30	527.54	06/2019 06/2019	06/2019	0(O) 0(R)	0/0
275	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	10,831.46	06/2017 06/2019	06/2019	24(O) 0(R)	35/40
276	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,388.93	11/2019 -	11/2019	0(O) -	0/0
277	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 1,394.52	1,394.52	293.99	05/2017 06/2019	09/2019	28(O) 3(R)	4/9
278	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 300.94	300.94	226.76	12/2018 12/2018	02/2019	2(O) 2(R)	0/0
279	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	311.17	11/2017 -	03/2019	16(O) -	1/4
280	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 175.64	175.64	80.24	09/2018 09/2018	09/2019	12(O) 12(R)	0/0
281	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPPT AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 193.14	193.14	4.80	06/2019 06/2019	09/2019	3(O) 3(R)	0/0
282	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,394.80	7,164.11	09/2009 -	12/2021	147(O) -	2/3
283	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,006.39	04/2020 -	10/2023	42(O) -	0/0
284	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	7,916.41	02/2019 10/2020	10/2020	20(O) 0(R)	22/23
285	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,038.00	10/2017 -	-	-	0/0
286	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 -	-	-	48/48
287	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 445.89	445.89	243.46	02/2019 02/2019	06/2019	4(O) 4(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
288	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	10,375.32	09/2017 06/2019	06/2019	21(O) 0(R)	36/41
289	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	6,693.90	09/2019 -	09/2019	0(O) -	27/32
290	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 305.04	305.04	237.11	03/2017 09/2018	02/2019	23(O) 5(R)	0/0
291	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	66.87	09/2020 -	09/2020	0(O) -	9/16
292	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	687.26	09/2010 12/2018	04/2019	103(O) 4(R)	5/8
293	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
294	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	9,026.43	11/2016 03/2019	03/2019	28(O) 0(R)	35/38
295	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,547.47	10/2012 12/2018	06/2019	80(O) 6(R)	8/11
296	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,727.30	08/2013 03/2022	03/2022	103(O) 0(R)	23/26
297	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	512.80	06/2014 12/2018	06/2019	60(O) 6(R)	10/12
298	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 534.02	534.02	441.88	08/2014 09/2018	02/2019	54(O) 5(R)	8/10
299	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 -	3,190.27	2,281.28	12/2015 -	-	-	15/18
300	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,221.08	04/2016 12/2018	06/2019	38(O) 6(R)	8/12
301	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 374.63	374.63	187.24	04/2016 12/2017	03/2019	35(O) 15(R)	0/0
302	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 539.82	539.82	424.53	06/2016 09/2018	06/2019	36(O) 9(R)	9/11
303	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 55,018.00	550.18	446.23	11/2016 06/2019	12/2019	37(O) 6(R)	8/12
304	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 206.42	206.42	145.82	03/2016 09/2018	02/2019	35(O) 5(R)	4/6
305	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 5,151.37	5,151.37	2,937.30	03/2018 03/2019	08/2019	17(O) 5(R)	9/12
306	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 225.28	225.28	151.02	02/2016 09/2018	03/2019	37(O) 6(R)	16/17
307	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	244.80	03/2018 09/2018	02/2019	11(O) 5(R)	1/3
308	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 871.62	871.62	462.92	10/2017 09/2019	09/2019	23(O) 0(R)	0/5
309	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	187.46	07/2017 06/2019	06/2019	23(O) 0(R)	3/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
310	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 197.40	197.40	74.71	03/2018 -	03/2019	12(O) -	0/0
311	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 3,705.61	3,705.61	2,572.10	04/2018 09/2018	02/2019	10(O) 5(R)	5/9
312	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	1,028.69	07/2018 -	-	-	0/0
313	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 808.63	808.63	416.66	01/2018 03/2019	09/2019	20(O) 6(R)	0/0
314	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 766.21	766.21	456.84	11/2018 11/2018	02/2019	3(O) 3(R)	0/0
315	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 3,519.59	3,519.59	2,129.90	05/2019 05/2019	05/2019	0(O) 0(R)	0/0
316	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 14,733.37	14,733.37	5,633.65	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
317	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 333.17	333.17	257.53	03/2019 03/2019	03/2019	0(O) 0(R)	0/0
318	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 431.89	431.89	231.96	02/2019 02/2019	03/2019	1(O) 1(R)	0/0
319	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 562.25	562.25	140.30	03/2019 03/2019	03/2019	0(O) 0(R)	0/0
320	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 251.60	251.60	152.51	06/2019 06/2019	06/2019	0(O) 0(R)	0/0
321	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 283.72	283.72	139.25	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
322	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 408.46	408.46	204.44	01/2019 01/2019	06/2019	5(O) 5(R)	0/0
323	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 608.24	608.24	382.10	04/2019 04/2019	04/2019	0(O) 0(R)	0/0
324	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 195.05	195.05	103.60	02/2020 02/2020	02/2020	0(O) 0(R)	0/0
325	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 322.30	322.30	127.38	02/2019 02/2019	03/2019	1(O) 1(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
326	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 162.31	162.31	92.40	03/2019 03/2019	03/2019	0(O) 0(R)	0/0
327	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 235.53	235.53	64.79	06/2019 06/2019	06/2019	0(O) 0(R)	0/0
328	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 379.95	379.95	22.22	12/2019 12/2019	12/2019	0(O) 0(R)	0/0
329	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 204.12	204.12	109.57	09/2019 09/2019	03/2019	-6(O) -6(R)	0/0
330	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 5,070.13	5,070.13	1,289.31	04/2020 04/2020	04/2020	0(O) 0(R)	0/0
331	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 337.75	337.75	31.80	06/2019 06/2019	06/2019	0(O) 0(R)	0/0
332	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 4,754.42	9,141.97	993.85	12/2018 12/2018	12/2019	12(O) 12(R)	0/0
333	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 5,111.33	6,652.57	1,035.32	12/2018 12/2018	12/2019	12(O) 12(R)	0/0
334	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	2,973.90	04/2019 -	04/2019	0(O) -	0/0
335	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	789.25	07/2020 -	07/2020	0(O) -	0/0
336	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 1,931.39	1,931.39	672.49	02/2020 02/2020	02/2020	0(O) 0(R)	0/0
337	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 198.49	198.49	22.80	09/2019 02/2020	02/2020	5(O) 0(R)	0/0
338	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 358.83	358.83	.70	05/2020 05/2020	05/2020	0(O) 0(R)	0/0
339	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	8,441.41	08/2018 06/2019	06/2019	10(O) 0(R)	30/37
340	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 844.64	844.64	326.60	04/2019 -	04/2019	0(O) -	0/0
341	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 307.18	307.18	211.31	11/2017 10/2018	02/2019	15(O) 4(R)	0/0
342	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 1,429.38	1,429.38	880.26	01/2019 01/2019	03/2019	2(O) 2(R)	0/0
343	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	2,106.62	11/2008 09/2018	03/2019	124(O) 6(R)	20/22

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
344	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 -	2,702.65	2,529.92	09/2014 -	-	-	11/13
345	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 186.17	186.17	64.27	07/2019 07/2019	07/2019	0(O) 0(R)	0/0
346	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	3,272.35	07/2020 10/2020	10/2020	3(O) 0(R)	21/23
347	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 -	1,078.31	963.23	07/2013 -	-	-	26/26
348	FGUTPP UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
349	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	5,433.65	03/2019 09/2019	09/2019	6(O) 0(R)	19/32
350	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	232.92	02/2014 02/2018	10/2019	68(O) 20(R)	7/8
351	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	8,798.00	12/2016 -	08/2019	32(O) -	33/34
352	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	4,401.90	2,731.61	02/2016 12/2020	05/2021	63(O) 5(R)	16/30
353	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,775.64	03/2013 12/2020	12/2020	93(O) 0(R)	6/15
354	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,105.30	1,593.51	06/2013 -	12/2021	102(O) -	9/13
355	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	151.99	08/2017 -	-	-	0/15
356	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	162.41	12/2021 -	12/2021	0(O) -	2/32
357	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	384.28	09/2019 02/2022	02/2022	29(O) 0(R)	5/9
358	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 454.11	454.11	255.32	04/2018 01/2020	01/2020	21(O) 0(R)	0/0
	Total		2,93,659.85 -	3,55,596.43	2,35,070.36				765/994
	<u>HEAVY INDUSTRY</u>								
359	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019	0(O) -	0/0
360	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 3,727.30	3,827.30	2,933.23	09/2011 06/2019	-	-	2/25
	Total		3,272.00 -	5,381.30	3,268.26				2/25
	<u>HEALTH AND FAMILY WELFARE</u>								

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
361	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS- MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	111.92	03/2019 -	03/2019	0(O) -	0/0
362	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	96.75	- -	02/2020	- -	0/0
363	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
364	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	174.00	05/2021 -	05/2021	0(O) -	0/0
365	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	513.89	147.00	11/2013 10/2020	10/2020	83(O) 0(R)	0/0
366	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	176.22	05/2017 06/2018	07/2019	26(O) 13(R)	2/2
367	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	282.43	05/2017 06/2018	03/2019	22(O) 9(R)	3/5
368	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.65	54.94	- -	02/2020	- -	0/0
369	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	46.28	- -	05/2020	- -	0/0
370	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	508.29	03/2018 -	-	-	1/2
371	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	125.36	03/2019 -	03/2019	0(O) -	0/0
372	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	61.17	- -	02/2020	- -	0/0
373	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	145.51	05/2018 09/2019	09/2019	16(O) 0(R)	0/0
374	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	95.16	02/2018 02/2018	06/2019	16(O) 16(R)	1/1
375	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	272.00	06/2020 -	06/2020	0(O) -	0/0
376	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	68.33	- -	04/2020	- -	0/0
377	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	39.35	04/2020 -	04/2020	0(O) -	0/0
378	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	247.47	09/2018 -	03/2019	6(O) -	0/0
379	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	122.43	03/2019 -	03/2019	0(O) -	0/0
380	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	58.04	- -	02/2020	- -	0/0
	Total		8,129.23 -	8,246.52	2,946.15				7/10

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	RAILWAYS								
381	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
382	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	289.91	03/2009 -	03/2023	168(O) -	0/0
383	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	732.81 -	1,993.00	2,017.37	03/2008 -	03/2020	144(O) -	0/0
384	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	-	-	-	0/0
385	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	-	-	-	0/1
386	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	393.16	03/2021 -	03/2022	12(O) -	0/1
387	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	1,005.66	03/2020 -	03/2022	24(O) -	0/0
388	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.07	-	-	-	0/0
389	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	177.18	03/2022 -	03/2023	12(O) -	0/0
390	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	378.12	12/2023 -	12/2023	0(O) -	0/0
391	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	183.68	03/2022 -	03/2022	0(O) -	0/0
392	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
393	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	4.98	03/2019 -	12/2020	21(O) -	0/0
394	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,532.00	575.61	03/2019 -	03/2020	12(O) -	0/0
395	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 486.96	551.00	615.94	03/2019 -	03/2019	0(O) -	0/0
396	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 614.81	398.93	339.81	03/2019 -	03/2019	0(O) -	0/0
397	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	288.01	03/2022 -	03/2020	-24(O) -	0/0
398	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	821.00	257.41	03/2021 -	03/2021	0(O) -	0/0
399	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96(O) -	0/0
400	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	792.46 724.31	1,320.00	929.63	12/2010 -	-	-	0/0
401	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	589.15	183.72	-	03/2022	-	0/0
402	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.77	330.82	-	03/2023	-	0/0
403	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	640.78	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
404	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
405	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	413.56	370.10	06/2018 -	10/2018	-	0/0
406	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96(O) -	0/0
407	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,132.03	2,145.00	930.20	03/2019 -	03/2020	12(O) -	0/0
408	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	4.98	-	03/2020	-	0/0
409	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	633.87 -	2,396.88	.39	-	-	-	0/0
410	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	2,626.98	.00	-	-	-	0/0
411	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,	04/2008	445.25 -	2,860.55	.00	-	-	-	0/0
412	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	2,995.01	1.68	-	-	-	0/0
413	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	325.00 -	729.92	253.10	-	03/2021	-	0/0
414	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	378.56 -	2,614.36	111.71	-	03/2022	-	0/0
415	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
416	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
417	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	-	-	-	0/0
418	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
419	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	.19	-	03/2023	-	0/0
420	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	-	-	-	0/0
421	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	-	-	-	0/0
422	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,474.47	338.44	-	03/2021	-	0/0
423	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	785.87	40.00	03/2020 -	03/2020	0(O) -	0/0
424	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	-	-	-	0/0
425	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	.00	-	-	-	0/0
426	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	.00	03/2020 -	10/2021	19(O) -	0/1
427	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	.00	03/2020 -	10/2021	19(O) -	1/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
428	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]JECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
429	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]JECR,BIHAR ,	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12(O) -	0/0
430	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]JECR,BIHAR ,	04/2016	731.64 -	1,185.73	.00	03/2021 -	03/2022	12(O) -	0/0
431	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]JECR,BIHAR ,	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61(O) -	0/0
432	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]JECR,BIHAR ,	04/1998	180.82 -	528.26	462.75	-	-	-	0/0
433	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]JECR,BIHAR ,	04/1991	329.39 -	566.41	759.20	-	12/2021	-	0/0
434	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR) NL RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	631.78 632.00	1,195.00	675.36	12/2012 -	03/2022	111(O) -	0/0
435	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	383.54 -	555.00	588.95	03/2010 -	12/2019	117(O) -	0/3
436	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]JECOR,CHHATISGARH ,	12/2012	1,160.00 -	1,160.83	571.51	03/2020 -	03/2020	0(O) -	1/1
437	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	958.09	887.59	03/2020 -	03/2020	0(O) -	0/0
438	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
439	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH ,	04/2011	1,471.93 -	543.00	.00	03/2022 -	03/2022	0(O) -	0/0
440	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,279.00	.00	12/2019 -	12/2019	0(O) -	0/0
441	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021	0(O) -	0/0
442	GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH ,	02/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022	0(O) -	0/0
443	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	600.00	09/2018 -	-	-	0/0
444	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	-	-	-	0/0
445	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	-	-	-	0/0
446	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 -	385.60	528.96	03/2020 -	03/2020	0(O) -	0/0
447	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	83.53	03/2012 -	03/2019	84(O) -	0/0
448	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
449	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	691.40	12/2021 -	12/2021	0(O) -	0/0
450	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	140.65	03/2021 -	03/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
451	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 -	844.10	62.58	-	03/2023	-	0/0
452	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 -	858.96	550.16	03/2019 -	03/2022	36(O) -	0/0
453	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	892.89	12/2021 -	12/2021	0(O) -	0/0
454	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	316.23	03/2021 -	03/2020	-12(O) -	0/0
455	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	291.62	03/2019 -	12/2019	9(O) -	0/0
456	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	-	-	-	0/0
457	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	-	-	-	0/0
458	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	-	-	-	0/0
459	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 -	551.51	257.05	03/2019 -	03/2019	0(O) -	0/0
460	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 -	691.84	43.44	03/2020 -	03/2020	0(O) -	0/0
461	JIND-SONEPAT (NL) NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
462	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	12/2011 -	-	-	0/0
463	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	.00	-	-	-	0/0
464	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	273.41	03/2019 -	03/2019	0(O) -	0/0
465	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	358.51	12/2026 -	12/2026	0(O) -	0/0
466	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	27,949.00	17,336.24	11/2002 -	03/2021	220(O) -	0/0
467	MANDARHILL-DUMKA-RAMPURHAT (NL) ER - [220100168]ER,JHARKHAND ,	04/1995	1,125.89 -	2,021.29	2,021.29	03/2016 -	03/2020	48(O) -	0/0
468	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 -	3,020.94	.00	-	03/2021	-	0/0
469	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	-	-	-	0/0
470	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	525.81	516.38	12/2015 12/2018	02/2019	38(O) 2(R)	0/0
471	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	198.49	- 12/2018	01/2020	- 13(R)	0/0
472	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	161.29	12/2016 08/2018	09/2019	33(O) 13(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
473	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 1,724.20	1,724.20	198.68	03/2021 03/2021	12/2021	9(O) 9(R)	0/0
474	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	109.68	03/2021 -	12/2020	-3(O) -	0/0
475	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	144.75	- 12/2024	12/2024	- 0(R)	0/0
476	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 03/2024	03/2024	264(O) 0(R)	0/0
477	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 1,801.01	1,801.01	14.24	- 12/2023	12/2023	- 0(R)	0/0
478	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	927.55	- -	12/2023	- -	0/1
479	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 986.30	986.30	288.01	03/2016 12/2023	12/2023	93(O) 0(R)	0/1
480	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	.00	- 12/2023	12/2023	- 0(R)	0/0
481	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024	96(O) 0(R)	0/0
482	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 348.85	348.85	.36	- 12/2023	12/2023	- 0(R)	0/0
483	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,255.49	03/2023 -	03/2023	0(O) -	0/1
484	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	- 0(R)	0/0
485	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 2,841.84	2,841.84	39.98	12/2018 12/2024	12/2024	72(O) 0(R)	0/0
486	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	- 0(R)	0/0
487	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 279.54	279.54	25.88	03/2016 12/2023	12/2023	93(O) 0(R)	0/0
488	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 1,140.93	1,140.93	714.14	03/2020 03/2020	03/2021	12(O) 12(R)	0/5
489	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 578.00	578.00	465.12	03/2020 03/2020	03/2020	0(O) 0(R)	0/2
490	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 889.52	889.52	433.71	03/2017 -	03/2020	36(O) -	0/0
491	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	254.53	- -	-	-	0/0
492	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	8.50	- -	-	-	0/0
493	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	369.83	432.50	- -	-	-	0/0
494	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.70	- -	-	-	0/0
495	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	23.84	- -	-	-	0/0
496	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	828.50	.08	- -	-	-	0/0
497	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
498	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA ,	02/2005	241.00 -	241.00	294.63	03/2014 -	-	-	0/0
499	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021	0(O) -	0/0
500	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	-	-	0/0
501	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 -	1,030.29	1,097.39	03/2022 -	03/2022	0(O) -	0/0
502	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,763.93	.00	03/2020 -	10/2021	19(O) -	1/1
503	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	903.15	12/2020 -	12/2020	0(O) -	0/0
504	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022	0(O) -	0/1
505	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,260.61	.00	03/2022 -	03/2022	0(O) -	0/1
506	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	140.94	03/2019 -	08/2019	5(O) -	0/0
507	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019	0(O) -	0/0
508	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH ,	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96(O) -	0/0
509	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021	0(O) -	0/0
510	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 -	700.00	1,055.19	06/2020 -	06/2020	0(O) -	0/0
511	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.96	716.90	06/1999 -	-	-	0/0
512	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	1,348.23	03/2004 -	03/2020	192(O) -	0/0
513	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 2,271.50	3,712.50	1,908.80	03/2021 -	03/2021	0(O) -	0/0
514	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60(O) -	0/0
515	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
516	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 3,168.29	3,168.29	1,011.99	03/2023 -	03/2023	0(O) -	0/0
517	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 792.89	792.89	277.94	03/2021 -	03/2021	0(O) -	0/0
518	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	298.70	245.23	03/2019 -	03/2019	0(O) -	0/0
519	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 540.02	540.02	175.86	03/2022 -	03/2022	0(O) -	0/0
520	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	8,857.98	.16	03/2024 -	03/2024	0(O) -	0/0
521	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
522	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
523	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 1,272.19	1,272.19	172.35	03/2022 -	03/2022	0(O) -	0/0
524	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 2,449.91	2,449.91	95.95	03/2023 -	03/2023	0(O) -	0/0
525	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.47	3,627.47	357.71	03/2024 -	03/2024	0(O) -	0/0
526	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	22.72	03/2023 -	03/2023	0(O) -	0/0
527	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 1,035.16	1,035.16	27.86	03/2022 -	03/2023	12(O) -	0/0
528	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 637.95	637.95	30.87	03/2023 -	03/2023	0(O) -	0/0
529	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	1,750.00	1,648.33	03/2020 -	03/2020	0(O) -	0/0
530	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.22	12/2025 -	03/2025	-9(O) -	0/0
531	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 -	2,686.63	.00	03/2023 -	03/2023	0(O) -	0/0
532	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	253.94	03/2019 -	03/2019	0(O) -	0/0
533	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
534	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
535	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	403.00	36.28	12/2021 -	12/2021	0(O) -	0/0
536	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	13,809.00	8,350.11	03/2011 -	03/2020	108(O) -	0/0
537	NEW BG LINE FROM BYRNIAH TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	6,000.00	260.10	03/2021 -	03/2021	0(O) -	0/0
538	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 2,393.48	4,968.00	2,541.80	03/2014 12/2020	12/2020	81(O) 0(R)	0/0
539	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
540	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	- -	-	-	0/0
541	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020	0(O) -	0/0
542	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
543	MUNEERABAD-MAHABOONAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	645.00	734.72	03/2000 -	03/2019	228(O) -	0/0
544	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
545	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 -	1,126.79	751.05	- -	-	-	1/1
546	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
547	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.87	- -	-	-	0/6
548	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	3,040.00	3,109.99	12/2008 -	03/2019	123(O) -	0/0
549	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	607.91	634.43	02/2013 -	-	-	0/0
550	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	770.08	231.72	12/2022 -	05/2019	-43(O) -	0/0
551	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	100.47	12/2021 -	12/2021	0(O) -	0/0
552	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	192.85	01/2019 -	01/2020	12(O) -	0/0
553	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	611.28	03/2022 -	03/2022	0(O) -	0/0
554	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	608.62	03/2022 -	03/2022	0(O) -	0/0
555	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,878.97	183.61	- -	-	-	0/1
556	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022	0(O) -	0/0
557	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	10.34	- -	12/2022	- -	0/0
558	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024	108(O) 0(R)	0/0
559	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
560	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	.00	03/2019 -	03/2019	0(O) -	0/0
561	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	- -	-	-	0/0
562	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	317.14	- -	-	-	0/0
563	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	65.88	03/2020 -	03/2020	0(O) -	0/0
564	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	148.33	- -	-	-	0/0
565	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	121.37	03/2020 -	03/2020	0(O) -	0/0
566	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
567	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	112.10	03/2019 -	03/2019	0(O) -	0/0
568	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	544.72	147.26	03/2006 -	01/2006	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
569	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	288.85	9.31	- -	-	-	0/0
570	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.84	- -	-	-	0/0
571	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	915.96	319.61	03/2022 -	03/2022	0(O) -	0/0
572	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	291.43	- -	-	-	0/0
573	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	378.90	- -	-	-	0/0
574	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	792.27	337.16	03/2016 02/2010	02/2010	-	0/0
575	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	538.37	109.04	03/2017 -	05/2010	-	0/0
576	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	175.99	57.52	- -	-	-	0/0
577	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.52	137.93	03/2016 -	03/2020	48(O) -	0/0
578	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	134.36	03/2017 -	-	-	0/0
579	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	50.69	11/2018 -	-	-	0/0
580	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	19.82	- -	-	-	0/0
581	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.73	- -	-	-	0/0
582	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	542.18	331.05	03/2020 -	03/2020	0(O) -	0/0
583	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	173.91	153.48	- -	-	-	0/0
584	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	299.60	1.12	03/2017 -	-	-	0/0
585	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	492.68	32.00	03/2005 -	-	-	0/0
586	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKUPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	299.03	53.11	- -	-	-	0/0
587	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	355.44	72.84	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
588	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]JER,MULTI STATE ,	04/2009	499.96 -	665.75	149.69	02/2012 12/2013	12/2013	-	0/0
589	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]JER,MULTI STATE ,	04/2009	257.42 -	258.73	113.58	03/2014 -	-	-	0/0
590	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]JER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
591	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]JER,MULTI STATE ,	04/2011	166.89 -	166.89	246.00	- -	-	-	0/0
592	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	2,200.00	229.44	03/2023 -	03/2024	12(O) -	0/0
593	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	1,787.00	2.46	- -	-	-	0/1
594	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	.00	- -	-	-	0/0
595	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
596	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- 12/2023	12/2023	- 0(R)	0/0
597	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 2,062.30	2,062.20	758.09	- -	03/2022	-	0/2
598	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 704.31	704.31	119.69	03/2020 03/2020	03/2020	0(O) 0(R)	0/1
599	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	2,132.77	217.64	03/2014 03/2023	03/2023	108(O) 0(R)	0/1
600	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
601	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
602	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	.00	- -	-	-	0/0
603	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
604	MONIGRAM- NIMTITA - [N22000301]JER,MULTI STATE ,	04/2012	250.93 -	259.23	208.85	- -	-	-	0/0
605	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	- 0(R)	0/0
606	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	3.58	03/2020 -	04/2022	25(O) -	0/0
607	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	207.68	- 03/2021	03/2021	- 0(R)	0/0
608	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 860.43	860.43	655.86	03/2020 03/2020	03/2020	0(O) 0(R)	0/0
609	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,870.41	1,870.41	787.72	03/2019 03/2021	03/2021	24(O) 0(R)	0/0
610	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 -	678.54	.00	03/2019 -	03/2020	12(O) -	0/38

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
611	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
612	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	401.52	03/2021 -	03/2021	0(O) -	0/0
613	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
614	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	1,425.36	12/2023 12/2023	12/2023	0(O) 0(R)	0/0
615	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
616	CHANDIGARH-BADDI - [N22000467]JNR,MULTI STATE ,	04/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023	0(O) -	0/0
617	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]JNR,MULTI STATE ,	03/2002	625.00 -	845.58	.00	03/2016 -	-	-	0/0
618	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 2,446.57	3,000.00	696.02	03/2015 10/2021	10/2021	79(O) 0(R)	0/0
619	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0(O) -	0/0
620	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147(O) -	0/0
621	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,458.49	12/2017 -	03/2020	27(O) -	0/0
622	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 245.00	1,202.70	706.84	02/2015 -	12/2021	82(O) -	0/0
623	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	377.10	03/2009 03/2009	02/2019	119(O) 119(R)	1/1
624	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 -	1,928.07	574.98	06/2021 -	03/2023	21(O) -	0/0
625	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
626	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	765.60	02/2019 -	03/2021	25(O) -	0/0
627	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 -	843.04	81.26	10/2020 -	03/2021	5(O) -	0/0
628	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	180.78	03/2020 -	03/2020	0(O) -	0/0
629	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 -	1,547.38	189.40	03/2022 -	03/2022	0(O) -	0/0
630	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 -	2,361.74	81.06	03/2022 -	03/2022	0(O) -	0/0
631	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28(O) -	0/0
632	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27(O) -	0/0
633	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	1,151.81	403.78	03/2020 03/2020	06/2020	3(O) 3(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
634	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	184.10	12/2021 12/2024	12/2024	36(O) 0(R)	0/0
635	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 2,335.67	2,335.67	355.05	12/2024 -	12/2024	0(O) -	0/0
636	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	1,103.00	1,009.91	03/2020 -	03/2020	0(O) -	0/0
637	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,120.00	910.97	03/2019 -	03/2021	24(O) -	0/0
638	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	.00	03/2020 -	03/2020	0(O) -	0/0
639	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
640	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	3.18	- -	-	-	0/0
641	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	795.01	467.29	02/2019 -	12/2019	10(O) -	0/0
642	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,216.00	741.81	03/2015 -	10/2020	67(O) -	0/0
643	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 -	1,116.00	840.30	03/2014 05/2019	05/2019	62(O) 0(R)	0/0
644	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	144.17	12/2019 -	11/2019	-1(O) -	0/0
645	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	167.81	10/2018 -	06/2019	8(O) -	0/0
646	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
647	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
648	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 295.02	420.18	96.91	03/2020 -	12/2019	-3(O) -	0/0
649	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	225.69	11/2019 -	11/2019	0(O) -	0/0
650	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	349.00	303.99	02/2019 -	05/2019	3(O) -	0/0
651	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,103.04	2.69	- -	-	-	0/0
652	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	415.31	03/2018 -	12/2019	21(O) -	0/0
653	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	.08	08/2022 -	09/2022	1(O) -	0/0
654	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0
655	KARUR-SALEM(NL) SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.94	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
656	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	445.91	06/2013 -	03/2019	69(O) -	1/4
657	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,169.07	02/2019 -	02/2019	0(O) -	0/0
658	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,049.68	- -	-	-	0/0
659	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	61.97	- -	-	-	0/0
660	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	237.73	- -	-	-	0/0
661	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019	0(O) -	0/0
662	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
663	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	303.72	- -	-	-	0/0
664	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	468.18	- -	-	-	0/0
665	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
666	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	83.15	- -	03/2020	- -	0/0
667	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71(O) -	0/0
668	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU ,	02/1997	458.63 -	458.63	.92	03/2015 -	-	-	0/0
669	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU ,	02/2000	200.84 -	200.84	394.26	03/2014 -	-	-	0/0
670	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	302.02	304.07	03/2005 -	-	-	0/0
671	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 -	257.00	.00	03/2018 -	03/2018	-	0/0
672	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
673	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU ,	02/2005	600.00 600.00	645.54	671.00	03/2010 -	-	-	0/0
674	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,700.00	.00	03/2022 -	03/2022	0(O) -	0/0
675	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU ,	02/2003	199.55 -	330.32	2.12	03/2009 -	-	-	0/0
676	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	.00	03/2020 -	03/2020	0(O) -	0/0
677	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION - [N22000453]SR,TAMIL NADU ,	02/2006	208.00 -	208.00	3.58	03/2012 -	-	-	0/0
678	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.26	3.69	- -	-	-	0/0
679	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.47	130.50	03/2010 -	03/2022	144(O) -	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
680	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	618.31	03/2016 03/2017	12/2020	57(O) 45(R)	0/0
681	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	0/1
682	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	723.00 -	616.08	.00	- -	-	-	0/1
683	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
684	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	250.05	12/2024 -	12/2024	0(O) -	0/0
685	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	.00	03/2022 -	03/2022	0(O) -	0/0
686	AGARTALA SABROOM NL NEFR - [N22000099]NFR,TRIPURA ,	04/2008	1,142.00 3,407.00	3,407.00	3,224.14	03/2014 12/2019	03/2019	60(O) -9(R)	0/0
687	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 984.97	1,733.20	1,553.74	03/2007 -	04/2016	-	0/0
688	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	650.00	.00	03/2020 -	10/2022	31(O) -	2/3
689	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
690	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
691	UTRATIA-ZAFRABAD NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	369.90 -	1,581.53	618.19	03/2010 -	-	-	0/0
692	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
693	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	308.00	.00	- -	-	-	0/0
694	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	435.00	457.93	- -	03/2018	-	0/0
695	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	270.00	267.76	08/2018 -	01/2019	5(O) -	0/0
696	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
697	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
698	FAIZABAD-LALGANJ VIA AKBARGANJ MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	.00	- -	-	-	0/0
699	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	380.00	4.12	- -	-	-	0/0
700	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
701	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	118.03	03/2022 -	12/2019	-27(O) -	0/0
702	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	668.00	.00	03/2020 -	03/2020	0(O) -	0/6

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
703	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	943.60	158.12	03/2022 -	12/2024	33(O) -	0/0
704	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,077.00	1,011.81	03/2019 -	03/2020	12(O) -	0/0
705	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	375.62	03/2023 -	12/2024	21(O) -	0/0
706	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	923.92	12/2020 -	03/2021	3(O) -	0/0
707	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	315.40	03/2020 -	03/2021	12(O) -	0/0
708	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	28.46	03/2019 -	12/2019	9(O) -	0/0
709	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH ,	04/1997	233.00 -	318.42	341.38	04/1999 -	-	-	0/0
710	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	.59	04/2016 -	02/2020	46(O) -	0/0
711	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
712	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH ,	04/1997	609.04 1,063.00	1,807.88	1,808.14	04/1999 -	03/2019	239(O) -	0/0
713	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
714	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,343.00	.00	01/2018 -	-	-	0/0
715	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	57.31	04/2017 -	01/2020	33(O) -	0/0
716	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
717	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	.00	- -	-	-	0/0
718	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	.46	01/2022 -	01/2020	-24(O) -	0/0
719	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	1.58	12/2019 -	04/2021	16(O) -	0/0
720	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	.00	03/2023 -	03/2023	0(O) -	0/0
721	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	.00	03/2021 -	03/2021	0(O) -	0/0
722	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
723	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0
724	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,235.71	12/2024 -	03/2026	15(O) -	0/0
725	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	270.28	03/2019 -	03/2020	12(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
726	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
727	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
728	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER, WEST BENGAL ,	04/2000	1,188.91 -	1,620.01	844.78	03/2019 12/2009	03/2022	36(O) 147(R)	0/0
729	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	1,106.62 -	1,092.20	634.34	12/2010 -	12/2017	-	7/7
730	TAMLUK DIGHA LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL ,	03/1984	293.97 -	749.69	.00	06/2005 -	-	-	0/0
731	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
732	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141(O) -	0/0
733	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	1,966.91	03/2016 -	03/2025	108(O) -	0/0
734	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 4,200.00	2,913.50	794.78	03/2016 -	03/2025	108(O) -	0/0
735	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL ,	04/2009	259.51 -	533.59	145.35	02/2012 -	09/2016	-	0/0
736	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL ,	04/2009	193.08 -	612.45	150.92	12/2011 -	09/2012	-	0/0
737	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	-	-	0/0
738	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	40.77	- 03/2025	03/2025	- 0(R)	0/0
739	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL ,	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
740	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	101.19	- -	03/2020	- -	0/0
741	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
742	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	89.78	- -	-	-	0/0
743	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL ,	04/2011	276.69 -	426.00	.00	- 03/2030	03/2030	- 0(R)	0/0
744	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	612.00	33.12	12/2021 -	03/2020	-21(O) -	0/0
745	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL ,	01/1991	1,013.45 1,013.45	1,428.00	484.58	12/2021 12/2021	12/2021	0(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
746	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	484.92	03/2003 03/2030	03/2030	324(O) 0(R)	0/0
	Total		4,85,586.03 -	6,97,755.98	1,69,590.53				18/104
	ROAD TRANSPORT AND HIGHWAYS								
747	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/0
748	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	.00	12/2017 -	-	-	0/4
749	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	.00	04/2017 -	-	-	0/4
750	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	.00	10/2018 -	-	-	0/4
751	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	.00	10/2018 -	-	-	0/4
752	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	29.43	11/2019 -	11/2019	0(O) -	0/0
753	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 12/2019	11/2019	0(O) -1(R)	0/0
754	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,177.45	05/2013 -	04/2019	71(O) -	0/0
755	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	-	0/0
756	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,003.77	05/2014 -	06/2019	61(O) -	0/0
757	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	.00	02/2015 -	-	-	0/4
758	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	-	-	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
759	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	.00	02/2017 -	-	-	0/0
760	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 -	207.40	44.08	07/2014 -	-	-	0/1
761	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	-	-	0/1
762	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/1
763	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	.00	- -	-	-	0/1
764	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	.00	- -	-	-	0/4
765	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	.00	- -	-	-	0/0
766	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	.00	12/2015 -	-	-	0/2
767	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
768	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	-	-	0/4
769	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	.00	- -	-	-	0/0
770	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	05/2015 -	-	-	2/4
771	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	.00	09/2015 -	-	-	0/4
772	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	.00	10/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
773	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	.00	12/2015 -	-	-	0/0
774	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	.00	06/2014 -	-	-	0/2
775	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	.00	11/2015 -	-	-	0/0
776	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	04/2015 -	-	-	0/0
777	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	51.81	11/2018 -	-	-	0/0
778	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
779	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	15.10	03/2020 -	03/2020	0(O) -	0/0
780	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	43.99	03/2020 -	05/2020	2(O) -	0/0
781	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	22.70	06/2017 -	11/2019	29(O) -	0/0
782	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	.00	- -	-	-	0/0
783	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	.00	- -	-	-	0/0
784	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
785	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	.00	- -	-	-	0/0
786	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	1,532.62	.00	03/2021 -	03/2021	0(O) -	0/0
787	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	.00	- -	12/2019	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
788	REHABILITATION AND UPGRADE OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	.00	- -	-	-	0/0
789	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	.00	- -	-	-	0/0
790	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	.00	- -	-	-	0/0
791	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
792	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2011 -	-	-	0/0
793	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	.00	05/2012 -	-	-	0/0
794	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	-	-	1/4
795	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
796	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	-	-	1/4
797	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	.00	06/2018 -	-	-	0/3
798	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	.00	- -	-	-	0/0
799	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	.00	09/2010 -	-	-	0/0
800	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	.00	09/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
801	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	-	-	1/4
802	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	.00	11/2016 -	-	-	0/0
803	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	.00	06/2016 -	-	-	0/4
804	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	.00	-	-	-	0/0
805	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	.00	10/2016 -	-	-	0/4
806	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	.00	-	-	-	0/0
807	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	.00	01/2017 -	01/2020	36(O) -	0/0
808	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	.00	03/2017 -	-	-	0/0
809	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	.00	04/2017 -	-	-	0/0
810	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	.00	04/2017 -	-	-	0/0
811	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	.00	04/2017 -	-	-	0/0
812	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	.00	04/2017 -	-	-	0/0
813	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	.00	04/2017 -	-	-	0/0
814	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	.00	04/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
815	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	.00	04/2017 -	-	-	0/0
816	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	.00	04/2017 -	-	-	0/0
817	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	.00	04/2017 -	-	-	0/0
818	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
819	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	410.32	02/2009 -	12/2018	-	0/0
820	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	209.80	04/2009 -	03/2019	119(O) -	0/0
821	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	-	0/0
822	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	-	-	0/0
823	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 174.34	174.34	214.88	03/2008 -	02/2019	131(O) -	0/0
824	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130(O) -	0/0
825	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	297.81	04/2008 -	03/2019	131(O) -	0/0
826	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	202.58	05/2008 -	02/2019	129(O) -	0/0
827	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0
828	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	390.71	04/2010 -	04/2019	108(O) -	0/0
829	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	-	-	0/4
830	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	-	-	0/4
831	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	-	-	0/4
832	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
833	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
834	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	-	-	0/4
835	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	.00	05/2017 -	-	-	0/0
836	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	.00	02/2011 -	-	-	0/0
837	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	.00	02/2018 -	-	-	0/0
838	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	.00	02/2018 -	-	-	0/0
839	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	.00	12/2018 -	-	-	0/4
840	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	.00	06/2018 -	-	-	0/0
841	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	.00	- -	-	-	0/0
842	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	.00	12/2018 -	-	-	0/0
843	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	.00	01/2016 -	-	-	0/4
844	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	.00	01/2016 -	-	-	0/4
845	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	.00	01/2016 -	-	-	0/0
846	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	884.58	02/2013 -	06/2019	76(O) -	0/0
847	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	-	-	0/0
848	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.65	03/2014 -	12/2018	-	0/0
849	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
850	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	832.77	07/2013 -	06/2019	71(O) -	0/0
851	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	564.70	11/2013 -	12/2018	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
852	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	.00	- -	-	-	0/0
853	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	-	-	0/0
854	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	-	-	0/0
855	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
856	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	175.85	04/2019 -	04/2019	0(O) -	0/0
857	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	279.13	- -	01/2020	-	0/0
858	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	71.28	04/2018 -	04/2020	24(O) -	0/0
859	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	20.12	- -	10/2020	-	0/0
860	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	38.33	- -	12/2019	-	0/0
861	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	158.10	04/2019 -	10/2019	6(O) -	0/0
862	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0
863	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	551.98	- -	03/2019	-	0/0
864	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	404.29	04/2018 -	12/2018	-	0/0
865	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
866	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	.00	- -	-	-	0/0
867	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	.00	03/2014 -	-	-	0/0
868	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
869	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	.00	08/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
870	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	.00	07/2016 -	-	-	0/0
871	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
872	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	.00	05/2016 -	-	-	0/0
873	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
874	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	.00	05/2016 -	-	-	0/0
875	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	.00	10/2016 -	-	-	0/0
876	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	.00	07/2016 -	-	-	0/0
877	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	.00	11/2015 -	-	-	0/0
878	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25(O) -	0/0
879	REHABILATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	.00	12/2016 -	-	-	0/0
880	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
881	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	03/2020	0(O) -	0/0
882	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	.00	08/2017 -	-	-	0/0
883	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
884	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
885	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
886	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
887	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	.00	03/2015 -	-	-	0/0
888	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	.00	03/2015 -	-	-	0/0
889	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	.00	03/2015 -	-	-	0/0
890	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	.00	- -	-	-	0/0
891	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	.00	12/2012 -	-	-	0/0
892	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIGMA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	.00	- -	-	-	0/0
893	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	.00	12/2015 -	-	-	0/0
894	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
895	FOUR LANING OF SIGMA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	284.92	05/2018 -	06/2019	13(O) -	0/0
896	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	7.21	04/2018 -	-	-	0/0
897	FOUR / SIX LANING OF RAIPUR - SIGMA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	323.95	04/2018 -	06/2019	14(O) -	0/0
898	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,029.96	.00	- -	-	-	0/0
899	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_ NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	-	-	0/0
900	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	04/2018 -	-	-	0/1
901	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
902	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
903	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
904	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	.00	- -	-	-	0/0
905	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	.00	- -	-	-	0/0
906	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	.00	- -	-	-	0/0
907	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	3,187.21	09/2012 -	08/2018	-	2/3
908	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.36	07/2013 -	12/2018	-	0/0
909	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-	-	0/3
910	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	346.60	08/2016 -	-	-	0/0
911	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	213.85	- -	08/2019	-	0/0
912	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	138.71	- -	10/2019	-	0/0
913	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	216.75	- -	09/2019	-	0/0
914	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	140.35	- -	08/2019	-	0/0
915	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	03/2019	-	0/0
916	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	364.56	64.61	- -	12/2019	-	0/0
917	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	72.69	- -	01/2020	-	0/0
918	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	100.75	- -	09/2019	-	0/0
919	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	.00	- -	-	-	0/0
920	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,958.88	549.02	06/2020 -	08/2020	2(O) -	0/0
921	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
922	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,052.21	.00	-	-	-	0/0
923	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	-	-	-	0/0
924	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	.00	-	-	-	0/0
925	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	-	-	-	0/0
926	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	10/2018	-	0/0
927	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,954.66	11/2011 -	06/2019	91(O) -	0/0
928	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	-	-	0/0
929	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
930	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 -	602.95	395.53	06/2016 -	03/2019	33(O) -	0/0
931	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 -	574.28	380.25	07/2018 -	03/2019	8(O) -	0/0
932	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	963.21	04/2019 -	04/2019	0(O) -	0/0
933	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
934	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA ,	08/2016	248.97 -	248.97	212.53	05/2019 -	08/2019	3(O) -	0/0
935	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	1,004.67	.00	05/2019 -	05/2019	0(O) -	0/0
936	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA ,	03/2017	639.79 -	552.90	422.78	03/2020 -	06/2019	-9(O) -	0/0
937	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA ,	03/2018	1,484.30 -	1,484.30	.00	-	-	-	0/0
938	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA ,	03/2018	275.12 -	275.12	.00	-	-	-	0/0
939	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI, HARYANA ,	03/2018	307.79 -	307.79	.00	-	-	-	0/0
940	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA ,	03/2018	634.70 -	634.70	.00	-	-	-	0/0
941	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI, HARYANA ,	03/2018	795.50 -	795.50	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
942	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	.00	- -	-	-	0/0
943	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	.00	- -	-	-	0/0
944	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	.00	- -	-	-	0/0
945	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	04/2019	29(O) -	0/0
946	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	330.04	03/2018 -	03/2019	12(O) -	0/0
947	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	230.61	02/2019 -	02/2019	0(O) -	0/0
948	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	- -	09/2020	-	0/0
949	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	07/2020	-	0/0
950	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	135.01	- -	11/2019	-	0/0
951	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	.00	06/2020 -	06/2020	0(O) -	0/0
952	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	.00	- -	-	-	0/0
953	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,403.47	07/2015 -	03/2019	44(O) -	0/0
954	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
955	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
956	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,288.68	06/2014 -	-	-	0/0
957	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	119.87	06/2019 -	12/2020	18(O) -	0/0
958	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,065.56	12/2018 -	10/2019	10(O) -	0/0
959	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	.00	- -	-	-	0/0
960	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
961	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	376.26	03/2019 -	03/2019	0(O) -	0/0
962	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	20.00	- -	12/2019	- -	0/0
963	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	37.20	08/2018 -	08/2019	12(O) -	0/0
964	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	24.21	03/2020 -	06/2019	-9(O) -	0/0
965	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	63.21	03/2020 -	06/2019	-9(O) -	0/0
966	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
967	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0
968	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- -	-	-	0/0
969	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9(O) -	3/3
970	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
971	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
972	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	380.95	09/2017 -	12/2018	-	0/0
973	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
974	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31(O) -	0/0
975	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	950.40	08/2018 -	04/2019	8(O) -	0/0
976	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	23.70	03/2019 -	07/2019	4(O) -	0/0
977	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	11.30	03/2019 -	11/2020	20(O) -	0/0
978	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
979	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	401.95	04/2020 -	04/2020	0(O) -	0/0
980	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	207.31	03/2019 -	03/2019	0(O) -	0/0
981	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	549.74	08/2019 -	08/2019	0(O) -	0/0
982	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	121.00	03/2020 -	06/2020	3(O) -	0/0
983	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	460.33	03/2020 -	06/2020	3(O) -	0/0
984	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	.00	- -	-	-	0/0
985	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	1,995.34	.00	- -	-	-	0/0
986	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,177.80	.00	- -	-	-	0/0
987	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	03/2019	79(O) -	0/0
988	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	231.56	09/2017 -	-	-	0/0
989	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	201.35	11/2017 -	-	-	0/0
990	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	727.93	- -	04/2019	- -	0/0
991	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	305.99	06/2018 -	04/2019	10(O) -	0/0
992	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	94.03	09/2017 -	06/2020	33(O) -	0/0
993	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,424.77	.00	- -	-	-	0/0
994	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	1,342.77	04/2013 -	11/2018	-	0/0
995	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/0
996	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
997	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
998	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	-	-	-	0/0
999	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	5.21	05/2015 -	01/2020	56(O) -	0/0
1000	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	-	-	0/0
1001	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	.00	05/2017 -	-	-	0/0
1002	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADHYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	-	-	0/0
1003	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	-	-	-	0/0
1004	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	-	-	0/0
1005	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	-	-	0/0
1006	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	-	-	0/0
1007	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	-	-	0/0
1008	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	464.01	-	03/2019	-	0/0
1009	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	398.49	-	05/2019	-	0/0
1010	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	-	-	0/0
1011	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	-	-	0/0
1012	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	-	-	0/0
1013	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	476.73	-	03/2019	-	0/0
1014	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	12/2018	-	0/0
1015	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	1,042.73	03/2016 -	03/2019	36(O) -	0/0
1016	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	454.51	-	03/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1017	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,469.10	01/2019 -	06/2019	5(O) -	0/0
1018	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	-	-	0/0
1019	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	78.39	01/2019 -	03/2019	2(O) -	0/0
1020	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	118.92	10/2017 -	01/2020	27(O) -	0/0
1021	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1022	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	.00	09/2017 -	-	-	0/0
1023	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	- -	-	-	0/0
1024	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	.00	- -	08/2020	- -	0/0
1025	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	- -	-	-	0/0
1026	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,264.75	03/2013 -	06/2019	75(O) -	0/0
1027	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	688.86	06/2014 -	06/2019	60(O) -	0/0
1028	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64(O) -	2/2
1029	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	-	-	0/2
1030	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	- -	-	-	0/4
1031	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	-	-	0/12
1032	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	- -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1033	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	-	-	0/4
1034	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	.00	- -	-	-	0/0
1035	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	65.16	- -	-	-	0/0
1036	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	205.97	- -	-	-	0/0
1037	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
1038	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	.00	05/2019 -	05/2019	0(O) -	0/0
1039	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	447.91	05/2018 -	03/2019	10(O) -	0/0
1040	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12(O) -	0/0
1041	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019	0(O) -	0/0
1042	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	45.11	05/2018 -	04/2019	11(O) -	0/0
1043	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	174.43	03/2019 -	12/2019	9(O) -	0/0
1044	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	331.17	05/2018 -	04/2019	11(O) -	0/0
1045	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,485.01	07/2017 -	12/2018	-	0/0
1046	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	662.12	11/2016 -	06/2019	31(O) -	0/0
1047	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	226.24	06/2006 -	-	-	0/0
1048	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	3,235.12	01/2018 -	02/2019	13(O) -	0/0
1049	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,047.41	06/2012 -	12/2018	-	0/0
1050	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1051	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA ,	03/2016	197.69 -	197.69	16.75	07/2018 -	-	-	0/0
1052	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA ,	03/2016	546.00 -	546.00	460.55	07/2019 -	07/2019	0(O) -	0/0
1053	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA ,	03/2016	591.66 -	591.66	608.89	07/2019 -	07/2019	0(O) -	0/0
1054	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA ,	03/2016	244.00 -	244.00	.00	07/2018 -	-	-	0/0
1055	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD, MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	.00	- -	-	-	0/0
1056	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD, MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	- -	-	-	0/0
1057	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	.00	- -	-	-	0/0
1058	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	-	-	0/0
1059	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6(O) -	0/0
1060	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA ,	11/2016	446.17 -	446.17	38.95	03/2019 -	07/2019	4(O) -	0/0
1061	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA ,	11/2016	290.73 -	290.73	101.84	- -	05/2019	- -	0/0
1062	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA ,	01/2017	244.90 -	244.90	175.56	05/2019 -	07/2019	2(O) -	0/0
1063	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA ,	02/2017	904.16 -	904.16	260.79	02/2020 -	05/2020	3(O) -	0/0
1064	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	03/2020	0(O) -	0/0
1065	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1066	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	420.38	03/2020 -	05/2020	2(O) -	0/0
1067	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA ,	03/2017	988.34 -	1,043.28	503.06	03/2020 -	08/2020	5(O) -	0/0
1068	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	197.98	03/2017 -	11/2020	44(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1069	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	202.79	03/2020 -	06/2019	-9(O) -	0/0
1070	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	469.50	03/2020 -	08/2020	5(O) -	0/0
1071	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	.00	- -	-	-	0/0
1072	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	.00	- -	-	-	0/0
1073	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	.00	- -	-	-	0/0
1074	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	.00	- -	-	-	0/0
1075	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	.00	- -	-	-	0/0
1076	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	.00	- -	-	-	0/0
1077	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	642.13	.00	- -	-	-	0/0
1078	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	839.86	01/2014 -	01/2019	60(O) -	0/0
1079	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	.00	02/2011 -	-	-	0/0
1080	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	470.59	05/2018 -	03/2019	10(O) -	0/0
1081	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	159.00	- -	-	-	0/0
1082	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	.00	03/2011 -	-	-	0/0
1083	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	.00	10/2010 -	-	-	0/0
1084	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1085	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00	604.00	423.83	12/2009	08/2020	128(O)	0/0
1086	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75	1,693.75	2,675.28	08/2011	-	-	2/2
1087	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76	2,498.76	2,531.46	08/2014	-	-	0/0
1088	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00	2,848.00	1,141.90	03/2014	12/2019	69(O)	0/0
1089	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00	754.00	1,363.43	03/2013	12/2019	81(O)	0/0
1090	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22	2,945.00	3,000.11	04/2015	-	-	0/0
1091	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83	789.83	109.77	-	-	-	0/0
1092	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51	788.51	103.37	03/2018	-	-	0/0
1093	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10	1,244.10	85.00	-	02/2020	-	0/0
1094	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47	1,294.47	.00	-	-	-	0/0
1095	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70	998.70	.00	-	-	-	0/0
1096	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00	1,296.00	.00	02/2011	-	-	0/0
1097	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07	373.07	.00	08/2016	08/2019	36(O)	0/0
1098	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52	396.52	.00	08/2016	08/2019	36(O)	0/0
1099	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52	429.52	.00	08/2016	08/2019	36(O)	0/0
1100	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68	507.68	.00	04/2017	-	-	0/0
1101	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00	387.00	.00	09/2018	-	-	0/0
1102	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09	500.09	.00	09/2018	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1103	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	.00	09/2018 -	-	-	0/0
1104	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 -	-	-	0/0
1105	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	-	-	0/0
1106	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	.00	09/2018 -	-	-	0/0
1107	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	.00	09/2018 -	-	-	0/0
1108	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	.00	09/2018 -	-	-	0/0
1109	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	.00	09/2018 -	-	-	0/0
1110	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	.00	09/2018 -	-	-	0/0
1111	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	.00	09/2018 -	-	-	0/0
1112	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	-	-	0/0
1113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/0
1114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/0
1115	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	03/2019	54(O) -	0/0
1116	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1117	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1118	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	.00	10/2016 -	-	-	0/0
1119	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1120	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	.00	01/2017 -	-	-	0/0
1121	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	.00	-	04/2020	-	0/0
1122	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	-	11/2019	-	0/0
1123	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	.00	11/2017 -	-	-	0/0
1124	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	.00	08/2015 -	-	-	0/0
1125	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	.00	-	06/2019	-	0/0
1126	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	.00	08/2019 -	08/2019	0(0)	0/0
1127	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	32.50	-	07/2020	-	0/0
1128	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	.00	05/2016 -	-	-	0/0
1129	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	.00	04/2018 -	-	-	0/0
1130	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	.00	10/2017 -	-	-	0/0
1131	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	.00	10/2017 -	-	-	0/0
1132	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	.00	05/2016 -	-	-	0/0
1133	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	.00	01/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1134	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	.00	06/2016 -	-	-	0/0
1135	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	.00	06/2018 -	-	-	0/0
1136	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	.00	05/2016 -	-	-	0/0
1137	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	.00	03/2020 -	03/2020	0(O) -	0/0
1138	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 -	11/2020	40(O) -	0/0
1139	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	.00	- -	-	-	0/0
1140	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	- -	-	-	0/0
1141	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	.00	- -	-	-	0/0
1142	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	.00	- -	-	-	0/0
1143	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1144	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	.00	- -	-	-	0/0
1145	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	-	-	0/0
1146	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	.00	- -	-	-	0/0
1147	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1148	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1149	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	-	-	0/0
1150	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1151	REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1152	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1153	4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1154	4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1155	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1156	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1157	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1158	CONST.OF 4 LANES WITH PAVED SHOULDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1159	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1160	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1161	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1162	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1163	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1164	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	161.79	- -	04/2019	- -	0/0
1165	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.09	- -	03/2019	-	0/0
1166	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	163.99	12/2017 -	04/2019	16(O) -	0/0
1167	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1168	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1169	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	670.70	09/2019 -	09/2019	0(O) -	0/0
1170	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	301.34	- -	04/2020	- -	0/0
1171	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	57.93	03/2020 -	04/2020	1(O) -	0/0
1172	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	261.76	.00	- -	-	-	0/0
1173	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	.00	- -	-	-	0/0
1174	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	108.91	- -	01/2020	- -	0/0
1175	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1176	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1177	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1178	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1179	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51(O) -	0/0
1180	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	.00	06/2018 -	-	-	0/0
1181	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30(O) -	0/0
1182	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	53.70	03/2018 -	03/2019	12(O) -	0/0
1183	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1184	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	206.78	05/2016 -	-	-	0/0
1185	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	604.80	10/2017 -	01/2019	15(O) -	0/0
1186	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	02/2019	30(O) -	0/0
1187	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	703.00	04/2018 -	03/2019	11(O) -	0/0
1188	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1189	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1190	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 09/2017	03/2019	89(O) 18(R)	0/0
1191	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	256.10	- -	03/2019	- -	0/0
1192	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	576.75	06/2019 -	09/2019	3(O) -	0/0
1193	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	155.03	06/2019 -	11/2019	5(O) -	0/0
1194	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	09/2019	3(O) -	0/0
1195	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	490.54	- -	11/2019	- -	0/0
1196	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	259.22	10/2018 -	11/2018	-	0/0
1197	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	193.54	01/2019 -	02/2019	1(O) -	0/0
1198	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	734.18	- -	05/2020	- -	0/0
1199	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	650.00	- -	12/2019	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1200	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1201	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	15.00	04/2020 -	11/2019	-5(O) -	0/0
1202	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	.00	10/2017 -	-	-	0/0
1203	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	-	-	0/0
1204	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	.00	- -	-	-	0/0
1205	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1206	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	.00	- -	-	-	0/0
1207	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	.00	- -	-	-	0/0
1208	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	.00	- -	-	-	0/0
1209	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	.00	08/2013 -	-	-	0/0
1210	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	.00	08/2013 -	-	-	0/0
1211	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1212	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	.00	10/2017 -	-	-	0/0
1213	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	7.50	11/2017 -	-	-	0/0
1214	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	.00	- -	-	-	0/0
1215	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	18.12	11/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1216	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/0
1217	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.49	12/2013 -	12/2018	-	0/0
1218	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	325.55	06/2013 -	-	-	0/0
1219	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	-	0/0
1220	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	-	0/0
1221	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1222	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1223	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 - 162.00	162.00	.00	07/2015 -	-	-	0/0
1224	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1225	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	926.73	11/2017 -	05/2019	18(O) -	0/0
1226	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18(O) -	0/0
1227	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1228	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	186.50	11/2016 -	-	-	0/0
1229	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	627.47	07/2008 -	-	-	0/0
1230	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	235.70	08/2018 -	06/2019	10(O) -	0/0
1231	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	289.10	07/2018 -	04/2019	9(O) -	0/0
1232	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	21.72	03/2020 -	03/2020	0(O) -	0/0
1233	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1234	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	.00	08/2017 -	-	-	0/0
1235	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	.00	09/2017 -	-	-	0/0
1236	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	.00	09/2017 -	-	-	0/0
1237	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	43.24	-	-	-	0/0
1238	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	-	-	-	0/0
1239	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	.00	-	-	-	0/0
1240	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	.00	-	-	-	0/0
1241	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	633.55	.00	-	-	-	0/0
1242	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,016.92	.00	-	-	-	0/0
1243	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,065.96	.00	-	-	-	0/0
1244	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,411.79	09/2016 -	06/2019	33(O) -	0/0
1245	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1246	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1247	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1248	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	.00	03/2016 -	-	-	0/2
1249	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1250	REHABILITATION AND UPGRADE OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	.00	12/2016 -	-	-	0/4
1251	REHABILITATION AND UPGRADE OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	.00	02/2017 -	-	-	0/1
1252	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	.00	01/2017 -	-	-	0/0
1253	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1254	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	544.89	11/2018 -	07/2019	8(O) -	0/0
1255	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1256	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	.00	- -	-	-	0/0
1257	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	.00	- -	-	-	0/0
1258	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	.00	- -	-	-	0/0
1259	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1260	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	261.24	03/2018 -	-	-	3/4
1261	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	-	-	0/4
1262	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	-	-	0/0
1263	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1264	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	442.51	01/2014 -	09/2018	-	0/0
1265	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-	-	0/0
1266	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1267	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	.00	03/2016 -	-	-	0/0
1268	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	.00	10/2016 -	-	-	0/0
1269	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1270	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	425.99	01/2016 -	-	-	0/0
1271	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	235.41	09/2016 -	-	-	0/0
1272	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	197.72	01/2016 -	-	-	0/0
1273	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	608.73	01/2016 -	-	-	0/0
1274	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	.00	03/2017 -	-	-	0/0
1275	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1276	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	.00	10/2016 -	-	-	0/0
1277	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	.00	03/2018 -	-	-	0/0
1278	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	-	-	0/0
1279	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	.00	10/2016 -	-	-	0/0
1280	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	.00	03/2017 -	-	-	0/0
1281	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	839.63	03/2018 -	-	-	0/0
1282	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,015.00	01/2019 -	01/2019	0(0) -	0/0
1283	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	701.24	06/2016 -	-	-	0/0
1284	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	396.67	06/2018 -	-	-	0/0
1285	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	492.20	06/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1286	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	404.76	07/2018 -	-	-	0/0
1287	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	441.14	06/2018 -	-	-	0/0
1288	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	.00	08/2015 -	-	-	0/0
1289	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1290	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1291	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	538.60	- -	-	-	0/0
1292	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	842.34	05/2019 -	05/2019	0(O) -	0/0
1293	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	827.52	06/2019 -	06/2019	0(O) -	0/0
1294	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	409.11	04/2019 -	04/2019	0(O) -	0/0
1295	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	301.48	- -	-	-	0/0
1296	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	169.51	- -	-	-	0/0
1297	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	201.46	04/2019 -	04/2019	0(O) -	0/0
1298	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	462.25	04/2019 -	04/2019	0(O) -	0/0
1299	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	349.13	- -	02/2020	- -	0/0
1300	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	5.71	- -	07/2020	- -	0/0
1301	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	50.71	- -	04/2020	- -	0/0
1302	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,820.02	04/2019 -	11/2019	7(O) -	0/0
1303	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	304.89	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1304	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	350.99	- -	-	-	0/0
1305	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	.00	03/2020 -	11/2020	8(O) -	0/0
1306	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	.00	03/2020 -	08/2020	5(O) -	0/0
1307	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2(O) -	0/0
1308	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	1,066.41	03/2020 -	03/2020	0(O) -	0/0
1309	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	637.48	- -	05/2020	-	0/0
1310	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1311	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1312	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1313	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1314	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1315	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0
1316	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	-	-	0/0
1317	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0
1318	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1319	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	1,025.80	.00	- -	-	-	0/0
1320	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	1,115.28	.00	- -	-	-	0/0
1321	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	.00	- -	-	-	0/0
1322	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69(O) -	0/0
1323	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	181.70	- -	10/2019	- -	0/0
1324	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	147.72	- -	02/2020	- -	0/0
1325	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	722.46	07/2018 -	07/2018	-	0/0
1326	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	.00	05/2018 -	-	-	0/4
1327	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	.00	06/2018 -	-	-	0/4
1328	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	.00	05/2018 -	-	-	0/4
1329	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	.00	12/2019 -	12/2019	0(O) -	0/0
1330	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	43.14	12/2019 -	12/2019	0(O) -	0/0
1331	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019	0(O) -	0/0
1332	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	66.19	06/2019 -	06/2019	0(O) -	0/0
1333	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	48.23	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1334	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	284.00	94.50	11/2019 -	11/2019	0(O) -	0/0
1335	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	95.30	11/2019 -	11/2019	0(O) -	0/0
1336	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	92.42	02/2020 -	02/2020	0(O) -	0/0
1337	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	.26	- -	-	-	0/0
1338	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1339	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.74	- -	-	-	0/0
1340	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,315.36	08/2013 -	06/2019	70(O) -	0/0
1341	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,829.14	08/2013 -	06/2020	82(O) -	0/0
1342	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	05/2019	56(O) -	0/0
1343	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	461.13	07/2014 -	05/2019	58(O) -	0/0
1344	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1345	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	47.90	- -	01/2020	-	0/0
1346	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	185.52	06/2018 -	05/2019	11(O) -	0/0
1347	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,901.17	- -	03/2019	-	0/0
1348	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	18.26	11/2018 -	04/2019	5(O) -	0/0
1349	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	186.83	08/2018 -	09/2019	13(O) -	0/0
1350	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	.00	06/2018 -	-	-	0/0
1351	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		4,11,159.45 -	4,25,383.97	1,59,378.55				26/210
	<u>SHIPPING AND PORTS</u>								
1352	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL,KERALA ,	07/2016	1,799.00 -	1,799.00	121.22	05/2021 -	05/2021	0(O) -	0/0
1353	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL,KERALA ,	05/2016	970.00 -	970.00	249.81	05/2020 -	05/2020	0(O) -	0/0
1354	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 669.46	669.46	413.91	12/2010 -	-	-	0/0
1355	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1356	ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 600.00	600.00	550.78	03/2006 03/2016	02/2019	155(O) 35(R)	0/0
1357	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.33	271.56	271.56	12/2017 03/2018	-	-	1/1
1358	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU ,	03/2016	600.00 257.90	257.90	1.45	12/2017 05/2020	05/2020	29(O) 0(R)	0/0
	Total		6,557.29 -	6,995.32	2,439.94				1/1
	<u>TELECOMMUNICATIONS</u>								
1359	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	367.03	06/2017 -	-	-	0/0
1360	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30 214.10	214.10	33.46	05/2018 02/2019	02/2019	9(O) 0(R)	0/0
1361	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 231.80	231.80	117.63	10/2018 02/2019	02/2019	4(O) 0(R)	0/0
1362	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58(O) -	0/0
1363	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,310.53 -	27,539.33	9,169.02				0/70
	<u>URBAN DEVELOPMENT</u>								
1364	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1365	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	154.30	03/2017 -	-	-	4/5
1366	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1367	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	.02	03/2019 -	03/2019	0(O) -	0/7
1368	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1369	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	34.09	06/2017 -	06/2020	36(O) -	0/0
1370	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	37,044.70	03/2016 05/2019	05/2019	38(O) 0(R)	0/0
1371	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	377.51	10/2019 -	03/2020	5(O) -	0/7
1372	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	677.49	12/2015 -	-	-	0/0
1373	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,746.53	11/2019 -	11/2019	0(O) -	3/7
1374	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	14.99	04/2019 06/2020	06/2020	14(O) 0(R)	0/2
1375	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1376	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	20.59	05/2020 -	05/2020	0(O) -	0/0
1377	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	101.04	06/2019 -	06/2019	0(O) -	0/0
1378	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	.00	- -	-	-	0/0
1379	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	.00	- -	-	-	0/0
1380	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	1.21	04/2018 -	-	-	0/0
1381	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	4.44	11/2019 -	11/2019	0(O) -	0/0
1382	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1383	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	163.97	11/2014 -	02/2019	51(O) -	2/8
1384	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1385	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1386	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0
1387	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1388	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	41.28	03/2016 -	04/2020	49(O) -	1/6
1389	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1390	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1391	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1392	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	34.90	02/2020 09/2020	09/2020	7(O) 0(R)	0/0
1393	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77(O) -	1/6
1394	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,181.79	.00	07/2017 -	12/2019	29(O) -	0/0
1395	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 -	03/2020	0(O) -	2/7
1396	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 8,680.00	8,680.00	4,898.72	03/2018 12/2019	12/2019	21(O) 0(R)	0/0
1397	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1398	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	13.00	07/2020 09/2018	09/2020	2(O) 24(R)	1/14
1399	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	2,024.91	11/2021 -	11/2021	0(O) -	0/0
1400	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2019	56(O) -	0/10
1401	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0
1402	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	486.54	394.49	05/2017 02/2019	03/2019	22(O) 1(R)	8/12

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1403	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	146.37	04/2019 06/2019	09/2019	5(O) 3(R)	4/8
1404	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	39.43	09/2018 -	09/2018	-	0/5
1405	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1406	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	540.42	234.59	07/2019 -	11/2019	4(O) -	0/0
1407	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72 -	342.00	321.13	09/2016 -	-	-	0/0
1408	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-	-	12/24
1409	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	51.00	10/2019 -	10/2019	0(O) -	1/6
1410	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/0
1411	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	11.10	- -	-	-	0/0
1412	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	13.03	03/2020 -	03/2020	0(O) -	0/5
1413	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1414	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1415	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1416	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1417	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	.00	03/2020 -	03/2020	0(O) -	0/0
1418	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1419	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1420	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	148.80	08/2016 -	03/2019	31(O) -	9/16

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1421	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	101.71	04/2018 -	07/2019	15(O) -	4/6
	Total		1,60,566.07 -	1,66,251.85	73,724.43				52/161
	<u>DEFENCE PRODUCTION</u>								
1422	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA ,	12/2016	167.69 168.00	167.69	105.91	05/2018 01/2019	-	-	6/10
1423	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL, GOA ,	12/2016	285.95 286.00	285.95	61.95	08/2020 -	08/2020	0(O) -	5/8
	Total		453.64 -	453.64	167.86				11/18
	Grand Total		18,25,733.41	21,44,298.86	8,24,847.36				2354/4526


Summary of projects in the Flash Report for the month of January, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1424
Number of Projects completed/dropped/frozen in Current Month	6
	0
Number of Projects Added in Current Month	5
Number of Projects in Current Month	1423

Brief Analysis

Project Status with respect to Original Schedule: Out of 1423 projects, 29 projects are ahead of schedule, 316 projects are on schedule 378 projects are delayed. 621 projects do not have fixed dates of commissioning. 79 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

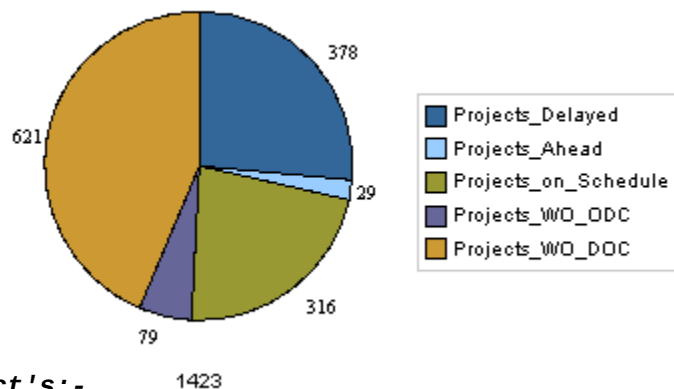


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1423 projects when sanctioned, was of the order of Rs. 1825733.41 crore but this was subsequently revised to Rs. 2144298.86 crore implying a cost overrun of 17.4%. The expenditure incurred on these projects till January, 2019 is Rs. 824847.36 crore, which is 38.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

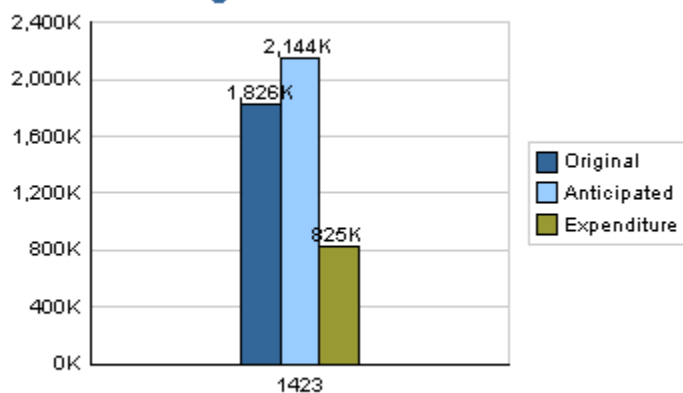

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

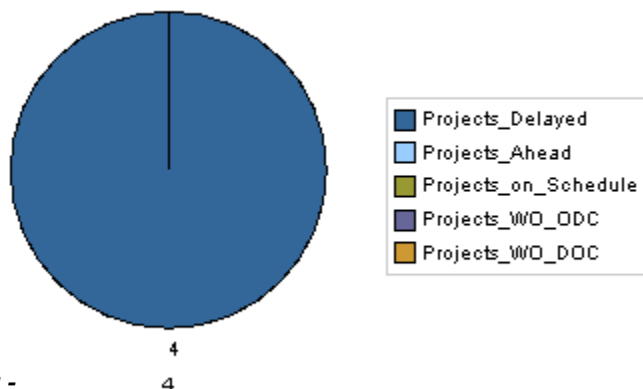


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 74849 crore implying a cost overrun of 11.5%. The expenditure incurred on these projects till January, 2019 is Rs. 41080.32 crore, which is 54.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

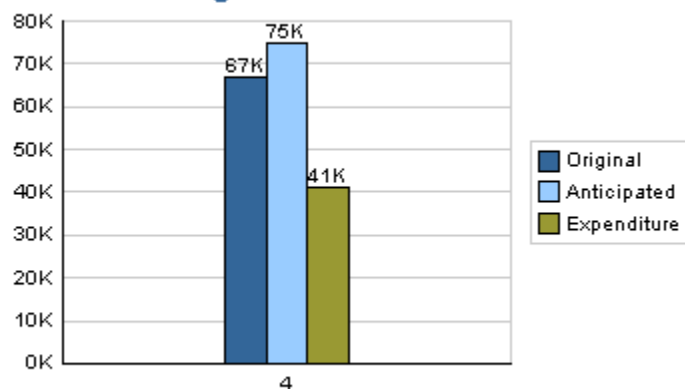

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

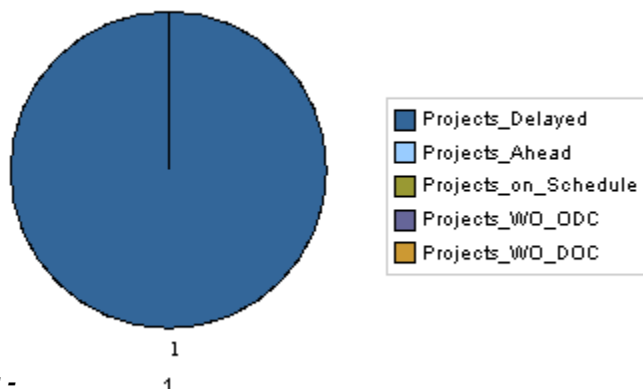


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 314.61 crore but this was subsequently anticipated to Rs. 441.33 crore implying a cost overrun of 40.3%. The expenditure incurred on these projects till January, 2019 is Rs. 85.79 crore, which is 19.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

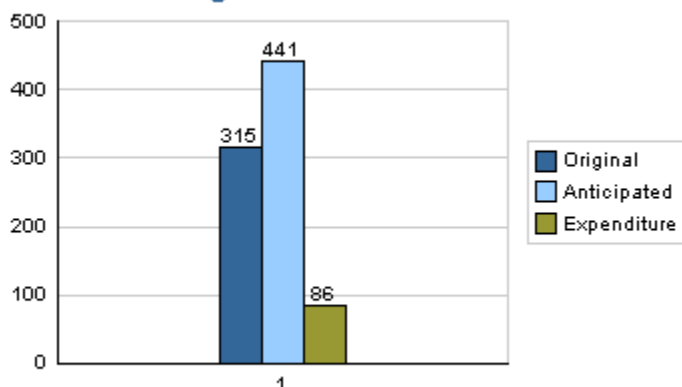

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	98
Number of Projects On Schedule	51
Number of Projects Delayed	36
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 98 projects, 1 project is ahead of schedule, 51 projects are on schedule 36 projects are delayed. 10 projects do not have fixed dates of commissioning.

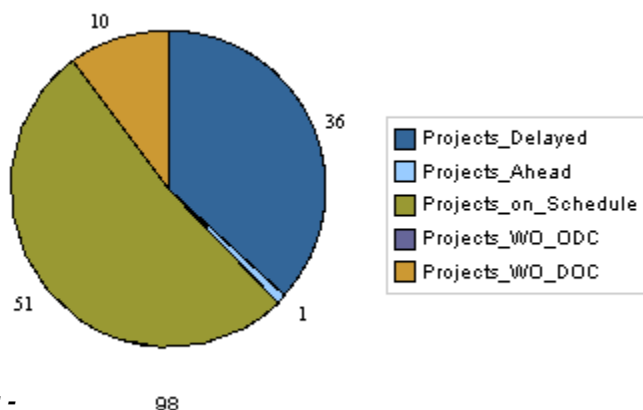


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 97468.86 crore but this was subsequently anticipated to Rs. 96940.36 cr The expenditure incurred on these projects till January, 2019 is Rs. 29719.04 crore, which is 30.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

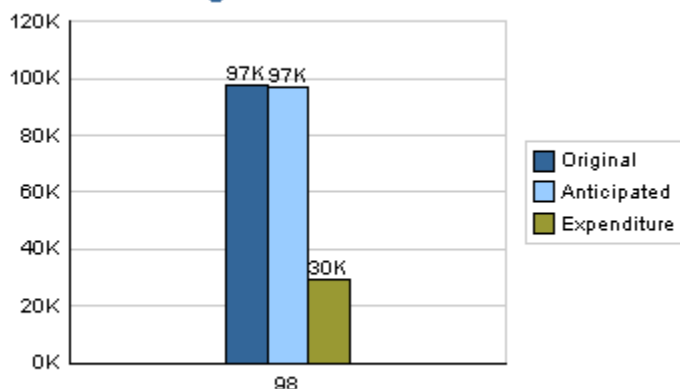

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule 2 projects are delayed.

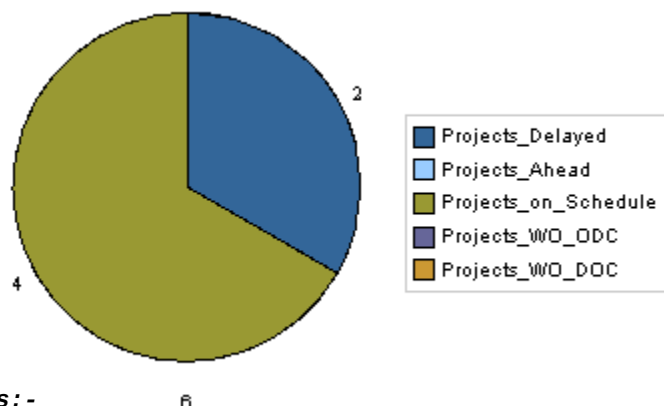


Total No Of Project's:-

6

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 1781.92 crore but this was subsequently anticipated to Rs. 1793.57 crore implying a cost overrun of .7%. The expenditure incurred on these projects till January, 2019 is Rs. 715.65 crore, which is 39.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

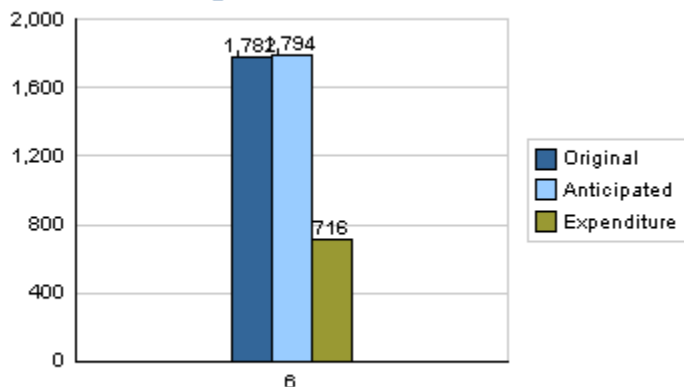

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	5
Number of Projects On Schedule	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 5 projects are on schedule

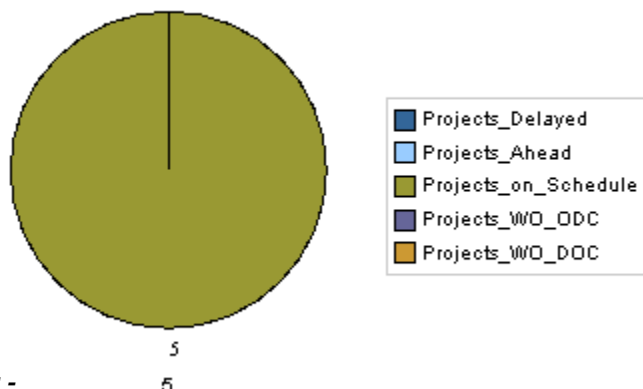


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore. The expenditure incurred on these projects till January, 2019 is Rs. 565.5 crore, which is 8% of the anticipated cost of the projects.

Figures are in Rs. Crore

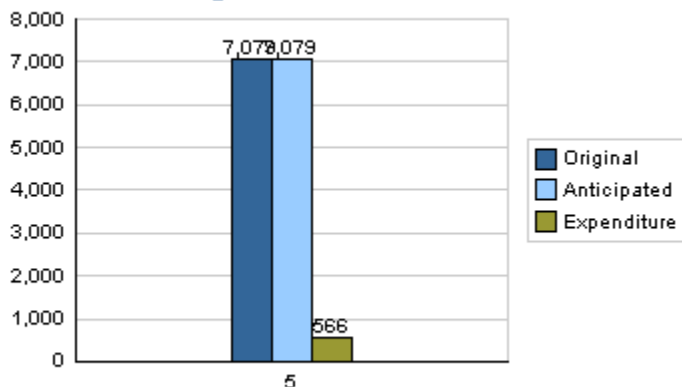

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	13
Number of Projects On Schedule	1
Number of Projects Delayed	10

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 1 project is on schedule 10 projects are delayed. 2 projects do not have fixed dates of commissioning.

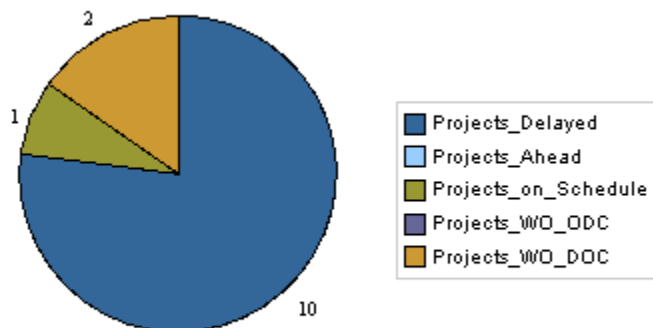


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 32529.65 crore but this was subsequently anticipated to Rs. 32317.05 cr The expenditure incurred on these projects till January, 2019 is Rs. 21728.92 crore, which is 67.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

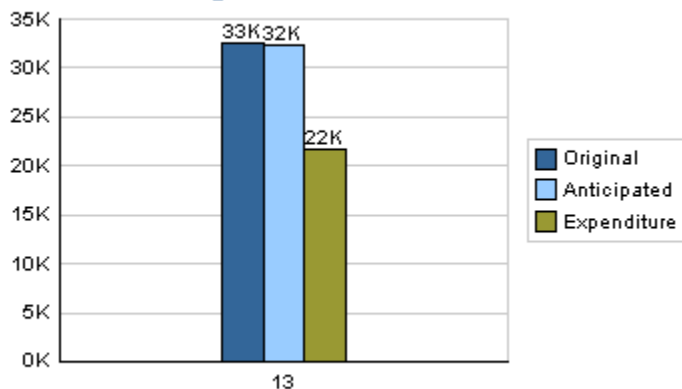

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	139
Number of Projects On Schedule	81
Number of Projects Delayed	33
Number of Projects Ahead	12
Number of Projects Without Date Of Commissioning	13

Brief Analysis

Project Status with respect to Original Schedule: Out of 139 projects, 12 projects are ahead of schedule, 81 projects are on schedule 33 projects are delayed. 13 projects do not have fixed dates of commissioning.

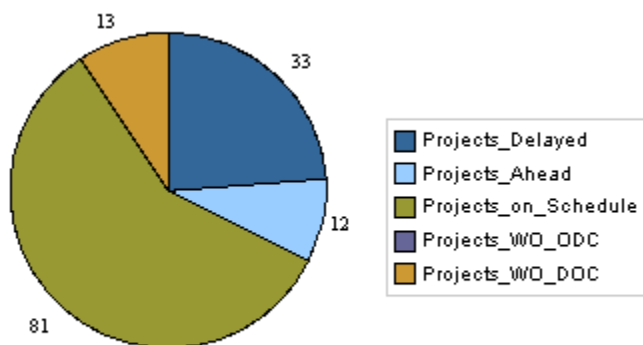


Total No Of Project's:-

139

Investment Scenario

Total original cost of implementation of 139 projects when sanctioned, was of the order of Rs. 233745.66 crore but this was subsequently anticipated to Rs. 237274.59 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till January, 2019 is Rs. 75197.04 crore, which is 31.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

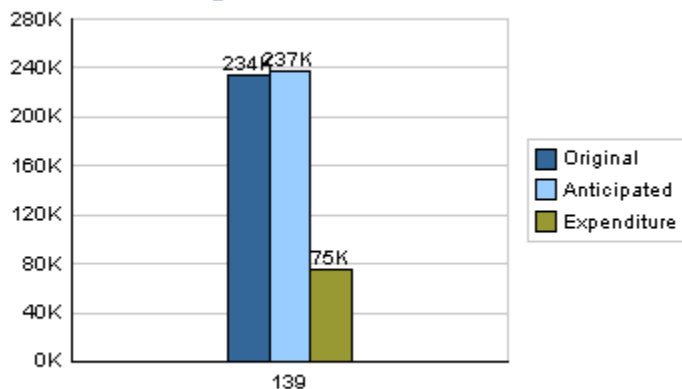

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	92
Number of Projects On Schedule	24
Number of Projects Delayed	57
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 92 projects, 1 project is ahead of schedule, 24 projects are on schedule 57 projects are delayed. 10 projects do not have fixed dates of commissioning.

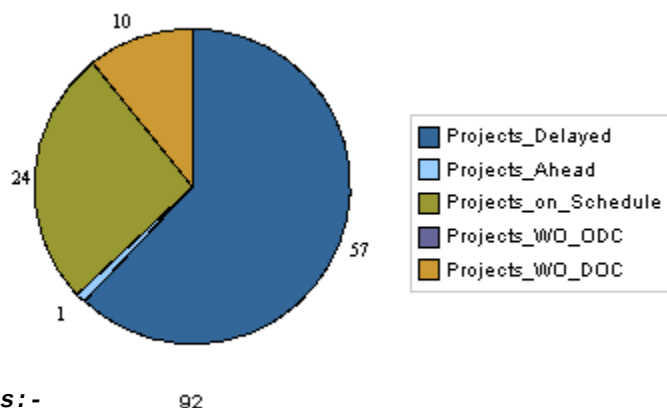


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 293659.85 crore but this was subsequently anticipated to Rs. 355596.43 crore implying a cost overrun of 21.1%. The expenditure incurred on these projects till January, 2019 is Rs. 235070.36 crore, which is 66.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

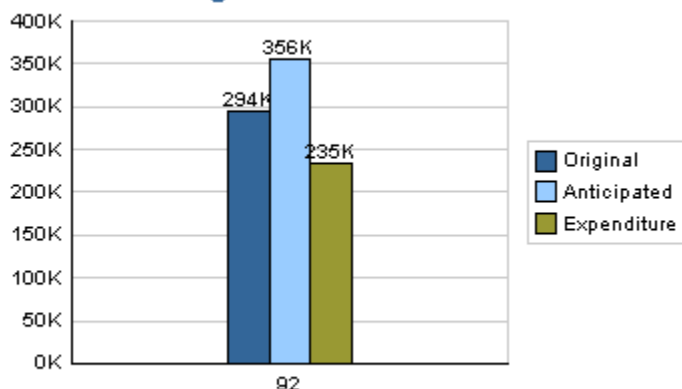

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.

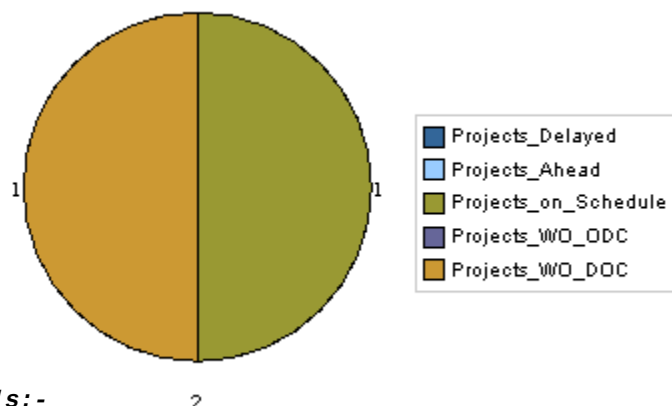


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 3272 crore but this was subsequently anticipated to Rs. 5381.3 crore implying a cost overrun of 64.5%. The expenditure incurred on these projects till January, 2019 is Rs. 3268.26 crore, which is 60.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

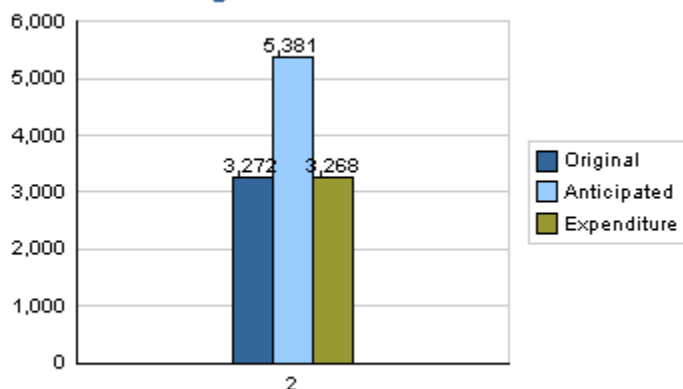

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	20
Number of Projects On Schedule	6
Number of Projects Delayed	6

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 6 projects are on schedule 6 projects are delayed. 2 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

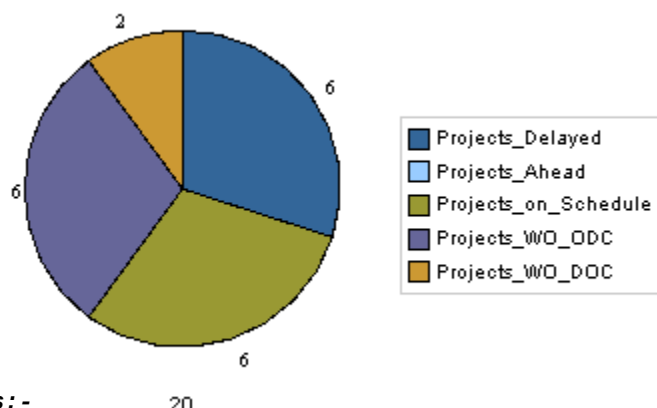


Total No Of Project's:-

20

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 8129.23 crore but this was subsequently anticipated to Rs. 8246.52 crore implying a cost overrun of 1.4%. The expenditure incurred on these projects till January, 2019 is Rs. 2946.15 crore, which is 35.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

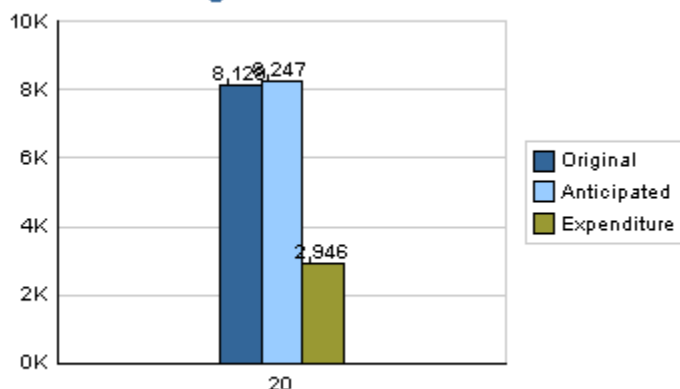

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	366
Number of Projects On Schedule	86
Number of Projects Delayed	99
Number of Projects Ahead	10
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	144

Brief Analysis

Project Status with respect to Original Schedule: Out of 366 projects, 10 projects are ahead of schedule, 86 projects are on schedule 99 projects are delayed. 144 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

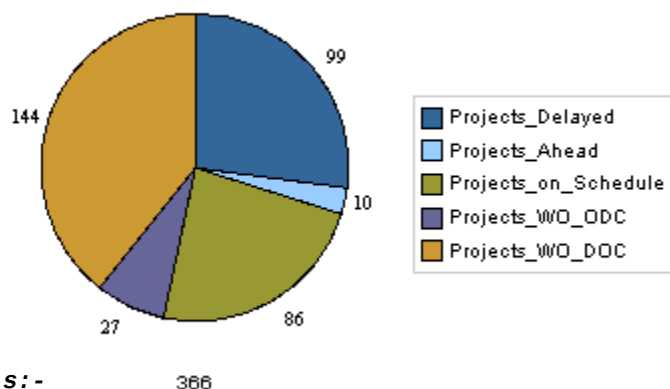


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 366 projects when sanctioned, was of the order of Rs. 485586.03 crore but this was subsequently anticipated to Rs. 697755.98 crore implying a cost overrun of 43.7%. The expenditure incurred on these projects till January, 2019 is Rs. 169590.53 crore, which is 24.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

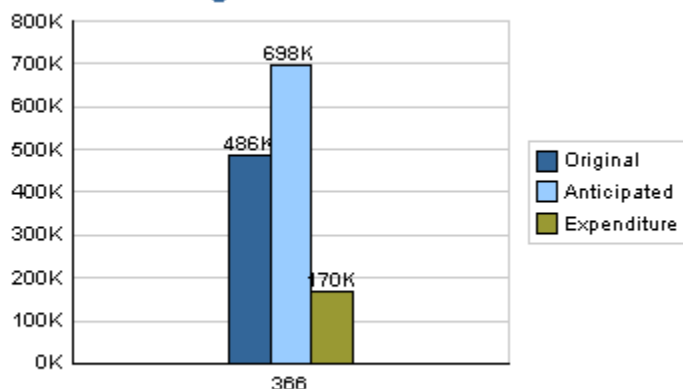

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	605
Number of Projects On Schedule	43
Number of Projects Delayed	104
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	46
Number of Projects Without Date Of Commissioning	407

Brief Analysis

Project Status with respect to Original Schedule: Out of 605 projects, 5 projects are ahead of schedule, 43 projects are on schedule 104 projects are delayed. 407 projects do not have fixed dates of commissioning. 46 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

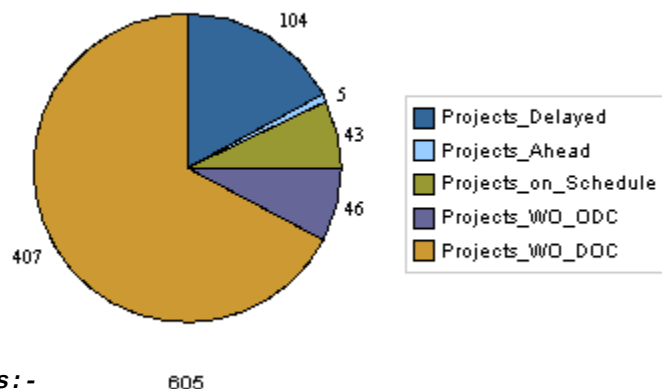


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 605 projects when sanctioned, was of the order of Rs. 411159.45 crore but this was subsequently anticipated to Rs. 425383.97 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till January, 2019 is Rs. 159378.55 crore, which is 37.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

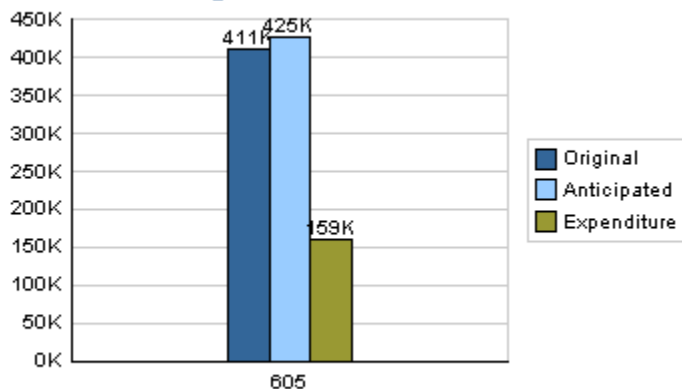

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	7
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 2 projects are on schedule 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

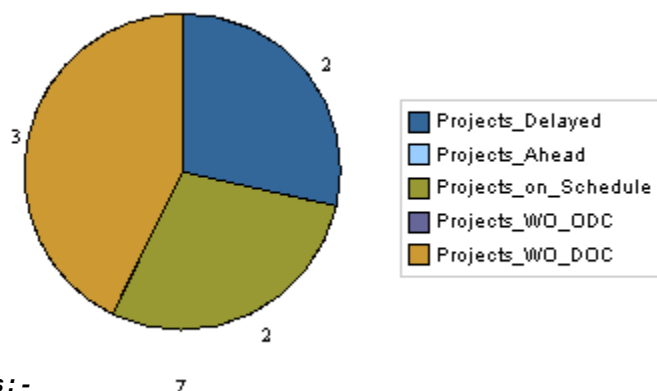


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 6557.29 crore but this was subsequently anticipated to Rs. 6995.32 crore implying a cost overrun of 6.7%. The expenditure incurred on these projects till January, 2019 is Rs. 2439.94 crore, which is 34.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

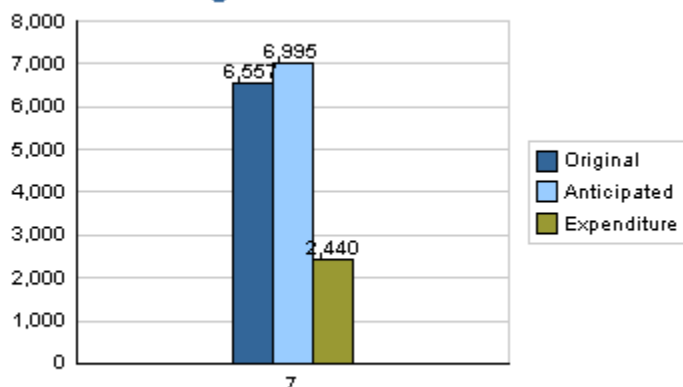

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	5
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed. 2 projects do not have fixed dates of commissioning.

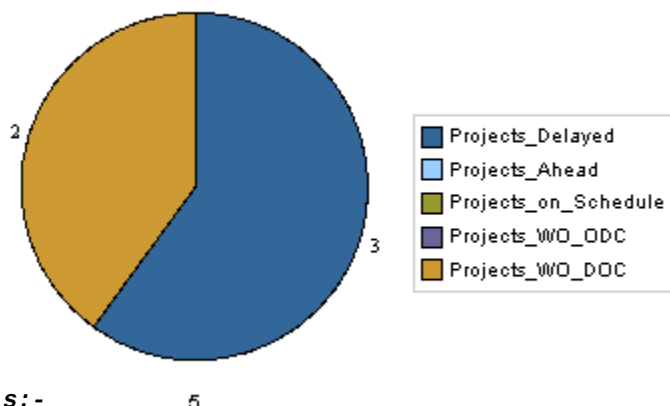


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 16310.53 crore but this was subsequently anticipated to Rs. 27539.33 crore implying a cost overrun of 68.8%. The expenditure incurred on these projects till January, 2019 is Rs. 9169.02 crore, which is 33.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

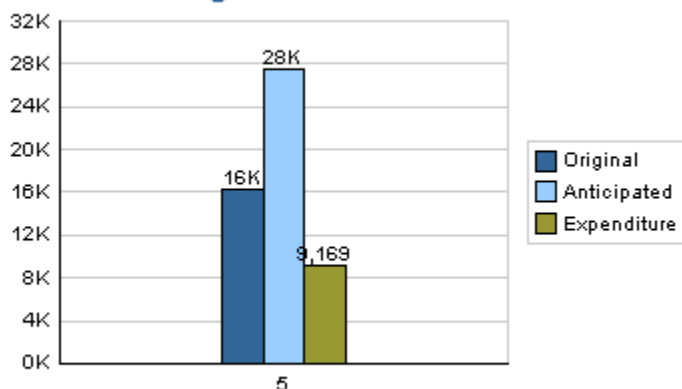

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	58
Number of Projects On Schedule	11
Number of Projects Delayed	21

Number of Projects Without Date Of Commissioning	26
--	----

Brief Analysis

Project Status with respect to Original Schedule: Out of 58 projects, 11 projects are on schedule 21 projects are delayed. 26 projects do not have fixed dates of commissioning.

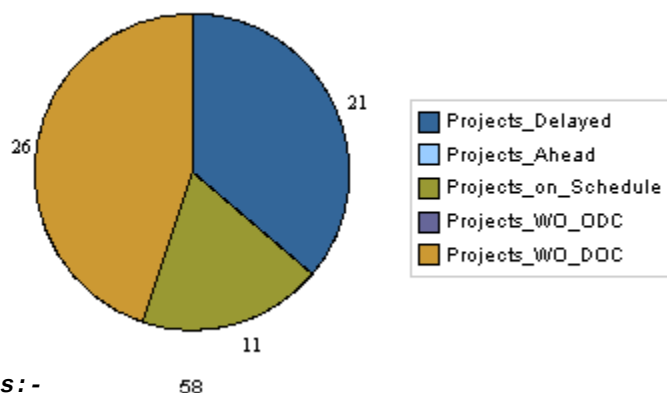


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 58 projects when sanctioned, was of the order of Rs. 160566.07 crore but this was subsequently anticipated to Rs. 166251.85 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till January, 2019 is Rs. 73724.43 crore, which is 44.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

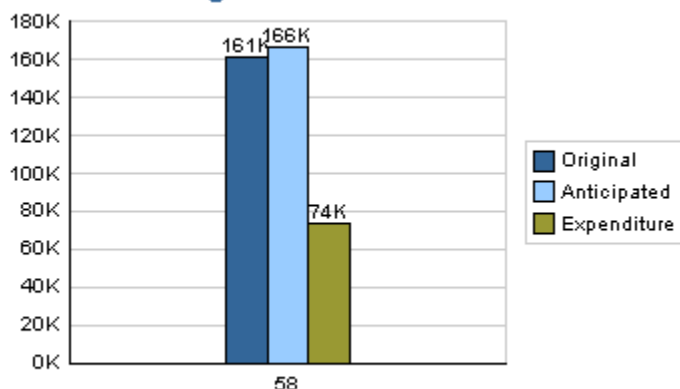

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.

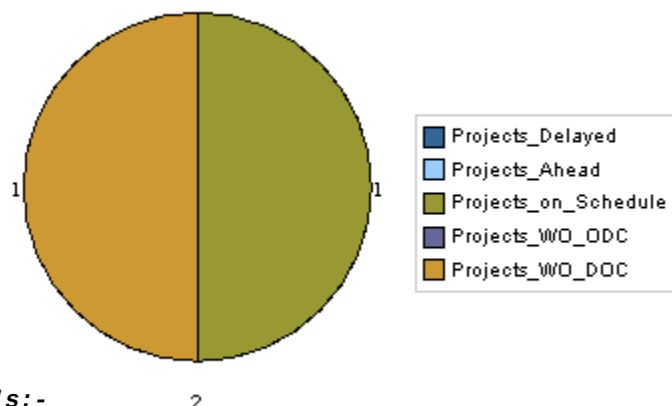


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 453.64 crore. The expenditure incurred on these projects till January, 2019 is Rs. 167.86 crore, which is 37% of the anticipated cost of the projects.

Figures are in Rs. Crore

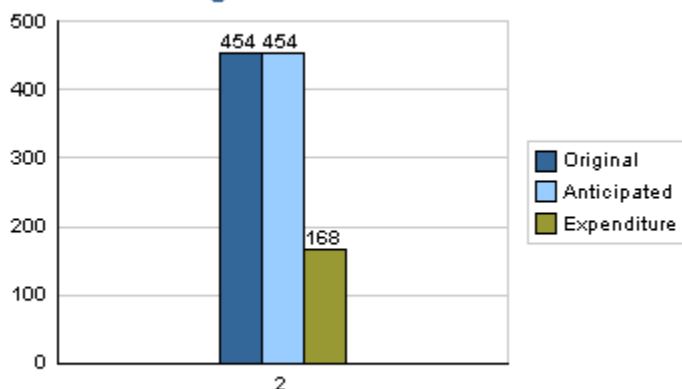

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (JANUARY 2019)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	8	2,385.01	2,492.59	156.31
2	ANDHRA PRADESH	69	1,07,461.29	1,11,208.37	18,939.58
3	ARUNACHAL PRADESH	31	16,421.02	33,547.53	17,755.48
4	ASSAM	45	27,704.18	33,843.2	17,466.67
5	BIHAR	91	76,252.26	1,11,749.59	52,313.67
6	CHHATISGARH	45	78,684.04	82,285.57	37,212.72
7	D & N HAVELI	1	6,086.08	5,842.31	4,513.89
8	DELHI	22	55,263.55	62,738.78	43,964.21
9	GOA	10	4,292.52	4,292.52	295.35
10	GUJARAT	49	51,576.03	57,483.9	30,924.66
11	HARYANA	29	21,083.41	22,987.06	11,417.18
12	HIMACHAL PRADESH	13	17,058.17	26,566.39	10,649.16
13	JAMMU AND KASHMIR	9	23,449.96	48,898.96	29,601.02
14	JHARKHAND	48	47,744.98	52,545.65	20,271.93
15	KARNATAKA	47	82,362.96	88,262.78	30,061.93
16	KERALA	25	39,778.48	41,953.1	7,548.49
17	MADHYA PRADESH	60	67,550.02	72,708.48	33,113.08
18	MAHARASHTRA	128	1,85,529.12	1,97,693.64	76,027.8
19	MANIPUR	2	4,670.86	14,025.69	8,402.11
20	MEGHALAYA	7	4,484.97	9,578.51	1,882.21
21	MIZORAM	4	3,406.61	5,981.14	2,672.62
22	MULTI STATE	160	3,40,790.26	4,44,636.07	1,32,690.43
23	NAGALAND	21	13,711.07	14,384.55	696.02
24	ODISHA	84	97,034.62	1,02,058.71	31,194.27
25	PUNJAB	33	17,042.04	17,146.31	5,074.63
26	RAJASTHAN	56	46,045.92	48,245.1	25,194.09
27	SIKKIM	9	3,476.73	6,281.03	433.9
28	TAMIL NADU	76	1,19,890.58	1,37,033.24	63,134.97
29	TELANGANA	41	34,378.1	37,015.07	8,884.51
30	TRIPURA	9	4,422.36	8,345.05	6,592.7
31	UTTAR PRADESH	110	1,34,449.08	1,36,016.3	55,436.22
32	UTTARAKHAND	28	33,689.4	39,554.65	11,676.94
33	WEST BENGAL	53	57,557.73	66,897.02	28,648.61
TOTAL		1,423	18,25,733.41	21,44,298.86	8,24,847.36

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

ATOMIC ENERGY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	3492	-	5738.32
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	259.4	-	266.38
3	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	457.77	-	584.87
4	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	267.99
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	235.51
6	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	152.43	-	184.45
7	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	418.97	-	477.74
8	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	198.68	-	254.72
HEALTH AND FAMILY WELFARE						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	505.58	-	508.29
10	CNCI KOLKATA WEST BENGAL	HSCC	08/2016	244	-	247.47
PETROLEUM						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1549.85
12	GAIL GAS LTD BENGALURU CGD PROJECT	GAIL	02/2015	749	-	803
13	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	IOCL	07/2015	822.66	-	868.92
POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
14	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	7164.11
15	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	10448.57
16	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	2496.9	6179.96	6900.51
17	BARH STPP(3X660MW) NTPC	NTPC	02/2005	8692.97	15095.67	15441.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
18	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3775.64
19	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	421.01	-	963.23
20	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	1940.13	-	2529.92
21	KUDGI STPP STAGE 1	NTPC	01/2012	15166.19	-	15364
22	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	5353	-	7511.72
23	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	-	540.02
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
24	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
25	AMRAVATI-NARKHER NL(CR)	CR	06/1994	663.01	668.34	716.9
26	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	2500	-	17336.24
27	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	631.78	632	675.36
28	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.3
29	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	1125.89	-	2021.29
30	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	511.86	-	967.96
31	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	484.14
32	KARUR-SALEM(NL), SR	SR	02/1997	155.55	-	856.94
33	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	164.36	-	999.64
34	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82
35	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	324.73	-	876.49
36	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
37	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	792.46	724.31	929.63
38	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	-	751.05

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
39	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72
40	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	03/2002	625.3	408.76	841.57
41	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.87
42	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	1180.19	2531.34	3109.99
43	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	1049.69	-	3544.3
44	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	607.09	-	634.43
45	JIND-SONEPAT (NL),NR	NR	01/2004	238.56	-	722.65
46	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	1185.64	-	1458.49
47	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	4454.17	-	8350.11
48	KOSI BRIDGE (NL), ECR	ECR	04/2002	499.41	-	640.78
49	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	424.6	-	898.83
50	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	370.1
51	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	120	-	210.67
52	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	231.72
53	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	377.1
54	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	477.88	283.95	495.4
55	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	732.81	-	2017.37
56	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	383.54	-	588.95
57	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	724.69	-	1169.07
58	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1049.68
59	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	385.2	-	575.61
60	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	369.9	-	618.19
61	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	2393.47	2393.48	2541.8

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
62	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	653.19	-	840.3
63	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29
64	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	457.93
65	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	267.76
66	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	320.66	-	550.16
67	AJMER-BANGURGRAM	NWR	04/2011	213.39	-	225.69
68	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	242.09	-	303.99
69	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	309.44	-	516.38
70	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	198.68	-	303.72
71	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	468.18
72	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	270.14	-	317.14
73	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	984.97	1553.74
74	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	432.5
75	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	819.23	-	1082.01
76	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	314	486.96	615.94
77	BANDEL-BOINCHI 3RD LINE	ER	04/2011	288.35	-	291.43
78	PIRPAINTI-BHAGALPUR	ER	04/2011	261.38	-	378.9
79	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	184.06	199.12	245.23
80	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	ER	04/2011	166.89	-	246
81	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	155.81	-	180.78
82	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	148.77	-	161.29
83	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21
84	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	927.01	-	1011.81

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
85	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	713.48	-	1648.33
86	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	948.04	-	1009.91
87	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	SR	02/2000	200.84	-	394.26
88	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	268.87	-	304.07
89	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	SR	02/2005	600	600	671
90	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	SR	02/2005	241	-	294.63
91	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	NER	04/1997	233	-	341.38
92	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	609.04	1063	1808.14
93	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	180.82	-	462.75
94	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	329.39	-	759.2
95	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	700	-	1055.19

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
96	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	280	-	410.32
97	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	199.81	-	209.8
98	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	167.64	-	268.94
99	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	155.04	-	195.35
100	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	225	-	312.79
101	NALBARI T BIJNI (AS-7)	NHAI	12/2003	208	-	297.81
102	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	160	-	202.58
103	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	340.12
104	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	217.61	-	390.71
105	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	1509.1	-	3187.21
106	SURAT- DAHISAR(SIX LANE) KM 263 TO KM	NHAI	02/2009	1693.75	-	2675.28

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
	502					
107	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	1108	-	3954.66
108	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	1175	-	1342.77
109	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2177.45
110	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	617	-	943.17
111	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	2498.76	-	2531.46
112	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	2264.75
113	INDORE-DEWAS(NH-3)	NHAI	11/2010	325	-	469.54
114	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	1987	-	2403.47
115	NASHRI- CHANANI	NHAI	05/2011	2159	-	3986.82
116	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	1813.76	-	2393.99
117	PATNA-MUZZAFFARPUR	NHAI	08/2010	671.3	-	884.58
118	ROHTAK-BAWAL	NHAI	05/2011	650	-	832.39
119	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1948.72
120	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1329.49
121	KANDLA - MUNDRA PORT	NHAI	01/2011	953.88	-	976.36
122	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	582.52
123	JORBAT - BARAPANI	NHAI	01/2011	536	-	839.86
124	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	3003.77
125	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	574	-	768.65
126	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	375.09	-	494.33
127	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	575	-	832.77
128	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	511.54	-	564.7

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
129	SRINAGAR TO BANIHAL	NHAI	06/2011	1100.7	-	1288.68
130	PANIKHOLI-RIMOLI	NHAI	03/2012	1410	-	1555.96
131	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1363.43
132	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2315.36
133	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	998.79	-	1829.14
134	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	1047	-	1613.62
135	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2614.84
136	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	442.51
137	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1998.25
138	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	2125.24	-	4659.71
139	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	1928.22	-	3000.11
140	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1792.9
141	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	NHAI	11/2013	1916.79	-	1948.92
142	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	1266.6	-	1411.79
143	2-LANING WITH PAVED SHOULDERS OF RAEARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	425.99
144	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEARELI	NHAI	04/2014	495.78	-	608.73
145	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	597	-	604.8
146	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	530.07	-	556.02
147	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	414.51	-	447.91
148	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	NHAI	09/2015	785.78	-	839.63
149	6 LANING OF AGRA - ETAWAH BYPASS	NHAI	07/2015	1657.2	-	2015
150	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1485.01
151	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	611.65	-	701.24

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
152	NAGPUR - KONDHALI	NHAI	09/2005	168	-	226.24
153	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	3326.93
154	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	1055	-	1393.4
155	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	1012.9	-	1042.73
156	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	3235.12
157	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2047.41
158	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	1901.17
159	TRICHY - KARUR	NHAI	03/2007	516	-	627.47
160	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	NHAI	01/2016	701.12	-	842.34
161	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	591.66	-	608.89
162	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	605.84	-	722.46

SHIPPING AND PORTS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
163	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	KPL	02/2015	244.5	258.33	271.56

URBAN DEVELOPMENT

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
164	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
165	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64
166	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	14600	-	16352.77
167	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	388	-	394.49

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	106.07	03/2023 -	03/2021
	Total		1,186.64 -	203.82	106.07		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
2	LAYING OF VIJAI PUR-AURAIYA PIPELINE SECTION OF VIJAI PUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,112.98	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
3	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
4	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,213.52	12/2020 -	08/2020
5	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	148.35	02/2019 -	01/2019
6	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	579.18	10/2019 -	03/2019
7	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	455.62	12/2020 -	02/2020
8	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	4,807.08	24.09	10/2021 -	07/2021
9	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,712.00	22.47	09/2022 -	06/2021
10	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	112.58	09/2019 -	02/2019
11	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	205.41	05/2019 -	01/2019
	Total		21,075.92 -	20,361.60	4,069.17		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
12	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 204.12	204.12	109.57	09/2019 09/2019	03/2019
	Total		204.12 -	204.12	109.57		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
13	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	109.68	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
14	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	1,142.00 3,407.00	3,407.00	3,224.14	03/2014 12/2019	03/2019
15	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	288.01	03/2022 -	03/2020
16	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	33.12	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
17	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	231.72	12/2022 -	05/2019
18	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42	1,295.42	118.03	03/2022 -	12/2019
19	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	366.71	.46	01/2022 -	01/2020
	<u>North Western Railway</u>						
20	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	144.17	12/2019 -	11/2019
21	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	4/2013	420.18 295.02	420.18	96.91	03/2020 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
22	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.22	12/2025 -	03/2025
	<u>Western Railway</u>						
23	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39	1,002.39	316.23	03/2021 -	03/2020
	Total		8,842.70 -	11,476.34	4,562.69		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
24	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 12/2019	11/2019
	<u>National Highways Authority Of India</u>						
25	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	202.79	03/2020 -	06/2019
26	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	422.78	03/2020 -	06/2019
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	24.21	03/2020 -	06/2019
28	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	63.21	03/2020 -	06/2019
29	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	15.00	04/2020 -	11/2019
	Total		2,492.50 -	2,346.96	769.08		

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		33,801.88	34,592.84	9,616.58		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	185.00	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	302.68	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	45.29	03/2022 -	03/2022
5	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	215.56	08/2019 -	08/2019
6	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	-	03/2024 -	03/2024
7	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
	<u>Mahanadi Coal Fields Limited</u>						
8	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	425.28	03/2021 -	03/2021
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	690.11	03/2026 -	03/2026
10	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	-	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	4,524.70	11/2021 -	11/2021
12	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	173.06	12/2019 -	12/2019
13	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	8.71	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
14	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022
15	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	236.49	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
16	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019
17	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
18	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	79.96	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>South-Eastern Coal Fields Limited</u>						
19	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.26	03/2021 -	03/2021
20	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
21	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.88	03/2023 -	03/2023
22	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
23	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
24	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,857.01	03/2023 -	03/2023
25	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.21	03/2023 -	03/2023
26	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	71.55	03/2020 -	03/2020
27	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	83.39	03/2022 -	03/2022
28	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
29	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
30	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	60.38	03/2020 -	03/2020
31	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,957.98	03/2023 -	03/2023
32	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
33	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	41.76	03/2021 -	03/2021
34	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.73	03/2021 -	03/2021
35	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	24.21	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
36	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	129.79	03/2019 -	03/2019
37	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	409.68	97.41	03/2023 02/2017	03/2023
38	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	116.35	03/2021 -	03/2021
39	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.29	03/2021 -	03/2021
40	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
41	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	67.18	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	105.38	03/2020 -	03/2020
43	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	191.97	03/2020 -	03/2020
44	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
45	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	238.47	03/2025 -	03/2025
46	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	91.22	03/2021 -	03/2021
47	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	397.95	03/2020 -	03/2020
48	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	258.23	03/2020 -	03/2020
49	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
50	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	03/2019
51	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	17.67	03/2022 -	03/2022
	Total		71,866.11 -	72,133.98	14,677.41		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
52	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	61.95	08/2020 -	08/2020
	Total		285.95 -	285.95	61.95		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
53	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	32.53	11/2019 -	11/2019
54	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	27.56	11/2019 -	11/2019
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	27.83	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
56	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	50.89	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	138.81		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
57	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
58	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
59	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
	<u>Hospital Services Consultancy Corporation</u>						
60	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	111.92	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
61	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	125.36	03/2019 -	03/2019
62	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	122.43	03/2019 -	03/2019
	Total		3,264.53 -	3,264.53	845.06		
	<u>HEAVY INDUSTRY</u>						
	<u>Indira Gandhi Centre For Atomic Research</u>						
63	DEVELOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
64	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	302.60	01/2020 01/2020	01/2020
65	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	96.98	04/2021 04/2021	04/2021
66	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
67	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]	9/2017	166.62 -	166.62	134.00	06/2019 -	06/2019
68	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
	Total		7,078.62 -	7,078.62	565.50		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
69	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	-	03/2021 -	03/2021
70	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
71	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	-	03/2023 -	03/2023
72	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	72.05	08/2020 -	08/2020
73	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	26.58	12/2020 -	12/2020
74	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	172.74	02/2020 -	02/2020
75	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	122.99	12/2019 -	12/2019
	<u>Chennai Petroleum Corporation Limited</u>						
76	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	646.29	12/2019 -	12/2019
77	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	22.22	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
78	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	27.55	10/2022 -	10/2022
79	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,002.53	12/2020 -	12/2020
80	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,112.98	12/2019 12/2020	12/2019
81	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,028.31	12/2020 -	12/2020
82	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	19.60	12/2021 -	12/2021
83	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	181.20 -	181.20	17.11	07/2022 -	07/2022
84	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	25.46	12/2020 -	12/2020
85	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	38.20	10/2022 -	10/2022
86	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	106.74	04/2022 -	04/2022
87	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	34.34	07/2022 -	07/2022
88	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	803.00	02/2020 -	02/2020
89	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	27.11	10/2022 -	10/2022
90	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	864.97	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Hindustan Petroleum Corporation Limited</u>						
91	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	122.05	02/2019 -	02/2019
92	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	2,864.07	07/2020 -	07/2020
93	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
94	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	15.68	11/2020 -	11/2020
95	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
96	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
97	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	288.56	09/2019 -	09/2019
98	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,048.00	06/2020 -	06/2020
99	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	60.42	03/2021 -	03/2021
	<u>Indian Oil Corporation Limited</u>						
100	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	1,068.35	07/2019 -	07/2019
101	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
102	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
103	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]	4/2018	355.00 -	355.00	-	04/2022 -	04/2022
104	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	2.76	02/2020 -	02/2020
105	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	0.02	10/2021 -	10/2021
106	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	315.44	09/2019 -	09/2019
107	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	8.74	01/2021 -	01/2021
108	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	41.38	04/2021 -	04/2021
109	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.90	08/2020 -	08/2020
110	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	264.64	09/2019 -	09/2019
111	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	0.10	08/2020 -	08/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
112	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	889.89	09/2019 -	09/2019
113	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	28.75	02/2020 -	02/2020
114	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	34.31	12/2019 -	12/2019
115	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	69.50	07/2020 -	07/2020
116	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	13.76	02/2020 -	02/2020
117	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
118	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	4.04	01/2021 -	01/2021
119	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	2.56	03/2021 -	03/2021
120	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,346.72	11/2019 -	11/2019
121	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
122	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
123	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	579.41	12/2020 -	12/2020
124	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	514.20	08/2021 -	08/2021
125	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	1.84	06/2020 -	06/2020
126	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
127	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	107.15	06/2020 -	06/2020
128	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	217.07	08/2019 -	08/2019
129	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	128.87	08/2020 -	08/2020
130	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	283.06	01/2019 -	01/2019
131	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	74.97	02/2020 -	02/2020
132	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,399.13	09/2019 -	09/2019
133	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	33.79	04/2020 -	04/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
134	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	3.37	12/2021 -	12/2021
135	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	7.46	12/2021 -	12/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
136	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
137	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
138	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
139	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	101.71	05/2020 05/2020	05/2020
140	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	307.27	03/2026 03/2026	03/2026
141	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	1,671.49	05/2021 05/2021	05/2021
142	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	112.87	12/2019 -	12/2019
143	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	668.42	11/2019 11/2019	11/2019
144	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	249.63	11/2019 11/2019	11/2019
145	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	219.96	11/2019 11/2019	11/2019
146	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	299.26	05/2019 05/2019	05/2019
	<u>Oil India Limited</u>						
147	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	44.43	12/2019 -	12/2019
148	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	26.81	10/2020 -	10/2020
149	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	2.08	02/2020 -	02/2020
	Total		1,06,482.47 -	1,05,672.17	22,149.91		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
150	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,388.93	11/2019 -	11/2019
151	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	6,693.90	09/2019 -	09/2019
	<u>Power Grid Corporation Of India Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
152	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	103.60	02/2020 02/2020	02/2020
153	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	672.49	02/2020 02/2020	02/2020
154	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	64.27	07/2019 07/2019	07/2019
155	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	2,973.90	04/2019 -	04/2019
156	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	789.25	07/2020 -	07/2020
157	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	152.51	06/2019 06/2019	06/2019
158	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	0.70	05/2020 05/2020	05/2020
159	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	140.30	03/2019 03/2019	03/2019
160	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	527.54	06/2019 06/2019	06/2019
161	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	31.80	06/2019 06/2019	06/2019
162	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	139.25	11/2019 11/2019	11/2019
163	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	2,129.90	05/2019 05/2019	05/2019
164	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]	3/2017	162.31 -	162.31	92.40	03/2019 03/2019	03/2019
165	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	382.10	04/2019 04/2019	04/2019
166	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	22.22	12/2019 12/2019	12/2019
167	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	64.79	06/2019 06/2019	06/2019
168	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	1,289.31	04/2020 04/2020	04/2020
169	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	326.60	04/2019 -	04/2019
170	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	5,633.65	11/2019 11/2019	11/2019
171	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	257.53	03/2019 03/2019	03/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
172	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	162.41	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
173	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	66.87	09/2020 -	09/2020
	Total		53,564.87 -	54,843.39	24,106.22		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
174	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	792.89 -	792.89	277.94	03/2021 -	03/2021
175	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	540.02 -	540.02	175.86	03/2022 -	03/2022
176	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
177	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	22.72	03/2023 -	03/2023
178	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	1,272.19 -	1,272.19	172.35	03/2022 -	03/2022
179	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,011.99	03/2023 -	03/2023
180	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	8,857.98	0.16	03/2024 -	03/2024
181	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
182	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	1,908.80	03/2021 -	03/2021
183	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	3,627.47	357.71	03/2024 -	03/2024
184	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	637.95 -	637.95	30.87	03/2023 -	03/2023
185	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	95.95	03/2023 -	03/2023
186	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	298.70	245.23	03/2019 -	03/2019
	<u>Container Corporation Of India</u>						
187	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	273.41	03/2019 -	03/2019
188	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	253.94	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
189	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
190	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
191	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
192	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
193	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
194	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	571.51	03/2020 -	03/2020
195	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	81.06	03/2022 -	03/2022
196	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	183.68	03/2022 -	03/2022
197	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	189.40	03/2022 -	03/2022
	<u>Eastern Railways</u>						
198	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	542.18	331.05	03/2020 -	03/2020
199	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	915.96	319.61	03/2022 -	03/2022
	<u>North Central Railway</u>						
200	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
201	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	-	03/2021 -	03/2021
202	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	-	03/2023 -	03/2023
203	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
	<u>North East Frontier Railway</u>						
204	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	257.41	03/2021 -	03/2021
205	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
206	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.37	03/2020 -	03/2020
207	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	339.81	03/2019 -	03/2019
208	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	65.88	03/2020 -	03/2020
209	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
210	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	551.00	615.94	03/2019 -	03/2019
211	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	260.10	03/2021 -	03/2021
	<u>North Eastern Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
212	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	100.47	12/2021 -	12/2021
213	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>North Western Railway</u>						
214	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	225.69	11/2019 -	11/2019
	<u>Northern Railway</u>						
215	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
216	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	1,425.36	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
217	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
218	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,255.49	03/2023 -	03/2023
219	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,750.00	1,648.33	03/2020 -	03/2020
220	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	691.40	12/2021 -	12/2021
221	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	358.51	12/2026 -	12/2026
222	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	892.89	12/2021 -	12/2021
223	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	355.05	12/2024 -	12/2024
224	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	958.09	887.59	03/2020 -	03/2020
225	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,103.00	1,009.91	03/2020 -	03/2020
226	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	140.65	03/2021 -	03/2021
227	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	378.12	12/2023 -	12/2023
228	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	903.15	12/2020 -	12/2020
229	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	250.05	12/2024 -	12/2024
	<u>South Central Railway</u>						
230	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	401.52	03/2021 -	03/2021
231	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
232	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	119.69	03/2020 03/2020	03/2020
	<u>South East Central Railway</u>						
233	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
234	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
235	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
236	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	1,471.93 -	543.00	-	03/2022 -	03/2022
237	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
238	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019
239	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
240	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
241	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
	<u>South Eastern Railway</u>						
242	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.58	12/2021 12/2021	12/2021
	<u>South Western Railway</u>						
243	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	465.12	03/2020 03/2020	03/2020
244	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	655.86	03/2020 03/2020	03/2020
	<u>Southern Railway</u>						
245	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
246	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,072.50	1,169.07	02/2019 -	02/2019
247	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	1,800.00	112.10	03/2019 -	03/2019
248	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
249	ATTIPPATTU PUTTUR - [N22000184]	4/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019
	<u>West Central Railway</u>						
250	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
251	RAMGANJMONDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
252	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
	<u>Western Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
253	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	700.00	1,055.19	06/2020 -	06/2020
254	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	691.84	43.44	03/2020 -	03/2020
255	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	551.51	257.05	03/2019 -	03/2019
256	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	385.60	528.96	03/2020 -	03/2020
257	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	1,030.29	1,097.39	03/2022 -	03/2022
258	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	611.28	03/2022 -	03/2022
259	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	608.62	03/2022 -	03/2022
	Total		2,46,860.60 -	3,10,062.22	52,412.45		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
260	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	94.50	11/2019 -	11/2019
261	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]	11/2017	232.81 -	232.81	48.23	11/2019 -	11/2019
262	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 12/2019	11/2019
263	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
264	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	43.14	12/2019 -	12/2019
265	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	29.43	11/2019 -	11/2019
266	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
267	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019
268	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]	11/2017	266.52 -	266.52	95.30	11/2019 -	11/2019
269	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]	6/2017	282.08 -	282.08	66.19	06/2019 -	06/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
270	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	92.42	02/2020 -	02/2020
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
271	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
272	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
	<u>National Highways Authority Of India</u>						
273	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
274	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	230.61	02/2019 -	02/2019
275	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	670.70	09/2019 -	09/2019
276	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	1,066.41	03/2020 -	03/2020
277	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
278	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
279	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
280	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	2/2016	997.15 -	997.15	376.26	03/2019 -	03/2019
281	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	21.72	03/2020 -	03/2020
282	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	9/2016	950.69 -	950.69	549.74	08/2019 -	08/2019
283	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
284	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]	1/2016	1,081.57 -	1,081.57	827.52	06/2019 -	06/2019
285	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
286	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	3/2016	1,587.49 -	1,587.49	201.46	04/2019 -	04/2019
287	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]	7/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019
288	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
289	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]	7/2015	2,128.72 -	2,128.72	963.21	04/2019 -	04/2019
290	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	2,015.00	01/2019 -	01/2019
291	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	462.25	04/2019 -	04/2019
292	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	401.95	04/2020 -	04/2020
293	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	608.89	07/2019 -	07/2019
294	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]	1/2016	701.12 -	701.12	842.34	05/2019 -	05/2019
295	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	460.55	07/2019 -	07/2019
296	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]	8/2016	1,167.42 -	1,167.42	207.31	03/2019 -	03/2019
297	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
298	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	409.11	04/2019 -	04/2019
299	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
300	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
301	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
302	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 -	1,041.10	175.85	04/2019 -	04/2019
	Total		39,750.29 -	40,303.60	12,778.15		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
303	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	121.22	05/2021 -	05/2021
304	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	249.81	05/2020 -	05/2020
	Total		2,769.00 -	2,769.00	371.03		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
305	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	31.88	06/2020 -	06/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		818.00 -	818.00	31.88		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
306	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
307	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	20.59	05/2020 -	05/2020
308	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
309	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107	12/2017	188.00 -	188.00	101.04	06/2019 -	06/2019
310	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089	12/2015	209.00 -	209.00	51.00	10/2019 -	10/2019
311	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118	10/2017	271.90 -	271.90	4.44	11/2019 -	11/2019
312	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098	10/2016	209.84 -	209.84	13.03	03/2020 -	03/2020
313	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108	1/2018	206.58 -	206.58	0.02	03/2019 -	03/2019
	<u>Lucknow Metro Rail Corporation Limited</u>						
314	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
315	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	11,420.00	2,024.91	11/2021 -	11/2021
	<u>National Building Construcion Corporation Ltd</u>						
316	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,746.53	11/2019 -	11/2019
	Total		24,257.89 -	24,433.12	8,500.91		
	Grand Total		5,59,653.61	6,24,319.86	1,36,974.31		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	10/2021	74.69
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
	Total		14,951.00 -	22,680.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	<u>Singareni Colliers Company Limited</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
8	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						
10	JAGANNATHPORA OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						
11	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
12	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
13	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		19,631.17 -	20,970.49			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
14	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
15	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
16	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
17	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
18	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
19	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33
	<u>Gas Authority Of India Limited</u>						
20	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
21	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,751.00	12/2012 -	06/2019	97.29
	<u>Hindustan Petroleum Corporation Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
22	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50
23	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
24	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
25	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	03/2019	36.22
26	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	08/2020	43.82
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
28	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	05/2019	26.44
	<u>Oil & Natural Gas Corporation Limited</u>						
29	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
30	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,577.15	05/2013 -	03/2019	83.01
31	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
32	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
33	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
	<u>Oil India Limited</u>						
34	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	06/2019	24.47
35	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		24,201.74 -	33,407.72			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
36	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
37	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
38	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
39	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
40	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	01/2019	86.27
41	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
42	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
43	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
44	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
45	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65
46	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
47	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
48	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
49	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
50	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>						
51	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51
52	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						
53	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	04/2019	54.59
54	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	06/2019	5.14
55	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65
56	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	06/2019	38.61
57	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	12/2019	5.34
58	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	02/2019	32.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
59	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	03/2019	14.60
60	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	02/2019	26.82
61	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92
62	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	-	39.30
63	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	06/2019	31.17
64	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	02/2019	79.61
65	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	03/2019	22.93
66	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	-	26.86
67	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR- II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
68	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28
69	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15
	<u>Satluj Jal Vidyut Nigam Limited</u>						
70	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT [N18000194]	05/2015	436.68 -	602.44	12/2016 -	03/2019	37.96
	<u>Thdc India Limited</u>						
71	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75
72	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77
73	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65
	Total		1,70,271.18 -	2,32,207.76			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
74	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	298.70	03/2019 -	03/2019	62.28
75	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2021	63.44

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
76	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999 -	-	29.55
77	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
78	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
79	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
80	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
81	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	143.17
82	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>						
83	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,020.94	- -	03/2021	192.42
84	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	- -	03/2023	290.95
85	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73
86	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
87	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
88	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
89	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	-	323.32
90	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
91	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
92	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,474.47	- -	03/2021	296.21
93	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2020	43.41
94	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
95	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
96	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
97	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
98	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48
99	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	528.26	- -	-	192.15
100	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 -	566.41	- -	12/2021	71.96
	<u>East Coast Railway</u>						
101	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
102	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96
103	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43
104	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2020	.07
105	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
106	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	-	542.46
107	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
108	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	-	818.15
109	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	- -	03/2021	124.59
110	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	- -	03/2022	590.61
111	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
112	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2022	36.26
113	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	607.91	02/2013 -	-	.14
114	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.59	02/2012 -	09/2016	105.61
115	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	-	44.46
116	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR- MINAKHAN VIA GHATAKPUR NL [N22000241]	04/2000	297.47 -	299.03	- -	-	.52

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
117	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242	04/2003	337.96 -	355.44	- -	-	5.17
118	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRHAT-KULPI NL - [N22000243	04/2009	499.96 -	665.75	02/2012 -	12/2013	33.16
119	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244	04/2009	257.42 -	258.73	03/2014 -	-	.51
120	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	259.23	- -	-	3.31
121	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	-	6.48
122	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	1,125.89 -	2,021.29	03/2016 -	03/2020	79.53
123	GHUTIASHARIF-CANNING (ER) - [N22000117	04/2009	193.08 -	612.45	12/2011 -	09/2012	217.20
124	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	544.72	03/2006 -	01/2006	33.84
125	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	- -	-	51.19
126	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	332.14	- -	-	27.07
127	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227	04/2010	174.56 -	175.99	- -	-	.82
	<u>Metropolitan Rapid Transport Projects</u>						
128	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
129	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
130	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
131	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
132	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
133	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
134	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
135	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
	<u>North East Frontier Railway</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
136	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
137	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57
138	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56
139	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,040.00	12/2008 -	03/2019	157.59
140	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
142	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
143	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
144	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,407.00	03/2014 -	03/2019	198.34
145	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2020	7.86
146	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
147	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
148	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,733.20	03/2007 -	04/2016	93.65
149	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11
150	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
151	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
152	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
153	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
154	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJBHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
155	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	551.00	03/2019 -	03/2019	75.48
156	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	03/2019 -	03/2019	62.12

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
157	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
	<u>North Eastern Railway</u>						
158	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	413.56	06/2018 -	10/2018	89.54
159	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
160	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08	12/2022 -	05/2019	234.77
161	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
162	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
163	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	- -	-	.33
164	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
165	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	435.00	- -	03/2018	122.35
166	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	01/2019	35.17
167	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
168	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
169	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
170	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16
171	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	03/2019	196.84
172	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
173	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	05/2019	70.85
174	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	12/2019	93.87
175	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
176	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	- -	-	26.25
177	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	10/2020	46.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
178	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	11/2019	41.64
179	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,878.97	- -	-	38.23
180	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	06/2019	24.47
181	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
182	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
183	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	11/2019	14.35
184	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	05/2019	44.16
	<u>Northern Railway</u>						
185	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
186	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
187	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	12/2011 -	-	117.77
188	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
189	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
190	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
191	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96
192	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
193	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56
194	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
195	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
196	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
197	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	02/2019	188.58
198	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,993.00	03/2008 -	03/2020	171.97
199	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
200	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
201	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
202	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70
203	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
204	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
205	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
206	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
207	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
208	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,077.00	03/2019 -	03/2020	16.18
209	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,750.00	03/2020 -	03/2020	145.28
210	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,103.00	03/2020 -	03/2020	16.35
211	BANASGANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						
212	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
213	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
214	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
215	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
216	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
217	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
218	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
219	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
220	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
	<u>South East Central Railway</u>						
221	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	-	186.92
222	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	1,756.00	04/2020 -	04/2020	243.06
223	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
224	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438	04/2010	585.93 -	1,420.39	02/2019 -	02/2019	142.42
225	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	403.00	12/2021 -	12/2021	75.98
226	CHHINDWARA-MANDLA FORT GC - [N22000481	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22
227	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 -	1,279.00	12/2019 -	12/2019	46.67
228	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,919.00	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
229	MM FROM BURAMARA-CHAKULIA - [N22000305	04/2008	466.48 -	1,000.00	- -	12/2024	114.37
230	MM FROM PANSKURA-GHATAL NL - [N22000309	04/2011	276.69 -	426.00	- -	03/2030	53.96
231	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
232	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
233	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	09/2019	153.41
234	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	- -	03/2025	131.89
235	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99
236	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161	04/2011	289.64 -	760.00	- -	-	162.39
237	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	03/2015 -	-	53.44
238	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81	12/2015 -	02/2019	69.92
239	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	365.00	- -	01/2020	41.36
240	ARA-BHABHUA ROAD (NL) - [N22000166	04/2008	633.87 -	2,396.88	- -	-	278.13

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
241	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76
242	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
243	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
244	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
245	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	12/2023	651.97
246	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09
247	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
248	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
249	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
250	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
251	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
252	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
253	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
254	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
255	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2019	185.98
256	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
257	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
258	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
259	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80
260	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	02/2019	627.74

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
261	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
262	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
263	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
264	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
265	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
266	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
267	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
268	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	369.83	- -	-	92.90
269	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	03/2019	1,391.30
270	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
271	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	302.02	03/2005 -	-	12.33
272	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
273	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]	02/2003	199.55 -	330.32	03/2009 -	-	65.53
274	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
<u>West Central Railway</u>							
275	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,713.09	03/2021 -	03/2021	538.98
276	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
277	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,260.61	03/2022 -	03/2022	116.55
<u>Western Railway</u>							
278	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
279	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
280	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		1,72,037.48	3,95,094.22			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
281	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97	268.92	08/2015	-	3.84
282	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18	162.00	07/2015	-	3.07
283	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50	192.00	05/2016	-	.26
284	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640	01/2015	326.63	327.00	04/2018	-	.11
285	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	02/2015	239.91	240.00	10/2017	-	.04
286	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643	12/2013	319.80	320.00	05/2016	-	.06
287	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96	172.00	06/2016	-	.02
288	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647	03/2014	162.51	163.00	05/2016	-	.30
289	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51	284.00	11/2019	11/2019	.17
290	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73	461.00	-	-	.06
291	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80	238.00	11/2019	11/2019	.08
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
292	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93	155.00	01/2017	01/2020	11.57
293	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00	447.37	10/2017	-	15.30
	<u>National Highways Authority Of India</u>						
294	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00	361.00	02/2009	-	28.93

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
295	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [N240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2019	92.75
296	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [N240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
297	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	02/2019	4.99
298	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
299	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
300	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	04/2019	65.82
301	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2019	10.58
302	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
303	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56
304	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
305	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
306	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83
307	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
308	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
309	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
310	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
311	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
312	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
313	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
314	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
315	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
316	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
317	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
318	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
319	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
320	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
321	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
	<u>Public Works Dept Of State</u>						
322	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
323	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
324	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
325	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
326	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24
327	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	31.78
328	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	-	10.82
329	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		29,654.32 -	44,654.88			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
330	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	271.56	12/2017 -	-	11.07
	<u>Mumbai Port Trust</u>						
331	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	-	82.72
	<u>Port Trust</u>						
332	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	02/2019	300.00
	Total		760.89 -	1,541.02			
	<u>STEEL</u>						
	<u>Rastrya Ispat Nigam Limited</u>						
333	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2020	42.39
	Total		343.00 -	488.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
334	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
335	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	486.54	05/2017 -	03/2019	25.40
336	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	04/2014	332.72 -	342.00	09/2016 -	-	2.79
337	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
338	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57
339	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	<u>Chennai Metro Rail Ltd</u>						
340	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Hindustan Steelwork Construction Limited</u>						
341	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
342	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
343	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
344	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>National Building Construcion Corporation Ltd</u>						
345	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		22,711.08 -	28,405.75			
	Grand Total		4,71,202.51	8,09,785.85			

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(January 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	10/2021	74.69	133
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
	Total		14,951.00 -	22,680.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	<u>COAL</u>							
	<u>Singareni Colliers Company Limited</u>							
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
5	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
7	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							
8	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
9	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
	Total		1,549.74 -	2,394.02				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
10	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		197.79	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
11	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11	513.89	11/2013	10/2020	24.10	83
	Total		414.11	513.89				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29	5,245.96	08/2018	11/2019	14.33	15
	<u>Gas Authority Of India Limited</u>							
13	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00	5,751.00	12/2012	06/2019	97.29	78
	<u>Hindustan Petroleum Corporation Limited</u>							
14	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81	723.40	10/2014	02/2019	133.50	52
	<u>Indian Oil Corporation Limited</u>							
15	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06	714.25	10/2017	03/2019	17.66	17
16	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175	03/2014	3,076.00	4,190.00	09/2017	03/2019	36.22	18
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
17	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256	10/2015	135.00	170.70	03/2019	05/2019	26.44	2
	<u>Oil & Natural Gas Corporation Limited</u>							
18	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94	330.35	01/2014	11/2019	62.78	70
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79	1,577.15	05/2013	03/2019	83.01	70
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63	2,665.65	03/2015	12/2019	29.42	57
21	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69	3,247.19	04/2018	05/2019	1.77	13
	<u>Oil India Limited</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
22	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	06/2019	24.47	27
	Total		18,298.77 -	25,054.49				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
23	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69	147
	<u>National Thermal Power Corporation</u>							
24	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14	93
25	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41	60
26	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	01/2019	86.27	88
27	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55	24
28	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55	21
29	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91	28
30	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64	10
31	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65	123
32	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55	20
	<u>North East Electric Power Corporation</u>							
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51	111
	<u>Power Grid Corporation Of India Limited</u>							
34	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	02/2019	32.69	35
35	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	03/2019	14.60	37
36	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92	23
37	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	02/2019	26.82	11
38	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	02/2019	79.61	54

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	550.18	11/2016 -	12/2019	5.34	37
40	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	06/2019	31.17	60
41	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	04/2019	54.59	103
42	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,891.41	04/2016 -	06/2019	38.61	38
43	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	03/2019	22.93	124
44	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061	10/2008	4,824.12 -	5,071.94	10/2012 -	06/2019	5.14	80
45	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15	12
46	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28	12
47	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65	103
	<u>Satluj Jal Vidyut Nigam Limited</u>							
48	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194	05/2015	436.68 -	602.44	12/2016 -	03/2019	37.96	27
	<u>Thdc India Limited</u>							
49	DHUKWAN SMALL HYDRO PROJECT - [N18000189	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75	68
50	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77	102
51	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65	63
	Total		1,27,518.04 -	1,70,513.31				
	<u>RAILWAYS</u>							
	<u>Container Corporation Of India</u>							
52	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							
53	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73	96
54	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
55	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
56	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
57	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48	61
	<u>East Coast Railway</u>							
58	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45	28
59	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43	25
60	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
61	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96	147
	<u>Eastern Railways</u>							
62	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2022	36.26	36
63	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	1,125.89 -	2,021.29	03/2016 -	03/2020	79.53	48
	<u>Metropolitan Rapid Transport Projects</u>							
64	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06	69
65	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
66	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	<u>North East Frontier Railway</u>							
67	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
68	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11	31
69	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
70	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
71	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95	79
72	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,040.00	12/2008 -	03/2019	157.59	123

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,407.00	03/2014 -	03/2019	198.34	60
74	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
75	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56	81
76	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02	108
	<u>North Eastern Railway</u>							
77	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16	46
78	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	01/2019	35.17	5
79	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80	12
80	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	03/2019	196.84	239
	<u>North Western Railway</u>							
81	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	06/2019	24.47	8
82	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	05/2019	44.16	3
83	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33	25
84	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	12/2019	93.87	10
85	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	05/2019	70.85	62
86	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	10/2020	46.55	67
	<u>Northern Railway</u>							
87	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96	220
	<u>Rail Vikas Nigam Ltd.</u>							
88	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	02/2019	188.58	119
89	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70	117
90	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
91	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,077.00	03/2019 -	03/2020	16.18	12
92	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
93	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15	111
94	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57	27
95	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	732.81 -	1,993.00	03/2008 -	03/2020	171.97	144
96	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
	<u>South Central Railway</u>							
98	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85	168
99	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47	12
	<u>South East Central Railway</u>							
100	CHHINDWARA-MANDLA FORT GC - [N22000481	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22	96
	<u>South Eastern Railway</u>							
101	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	09/2019	153.41	33
102	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81	12/2015 -	02/2019	69.92	38
103	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADE FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05	36
104	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99	108
105	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76	3
106	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
107	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96	36
108	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84	24
	<u>Southern Railway</u>							
109	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72	71
	<u>West Central Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
110	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
111	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
112	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
	Total		60,943.39 -	1,41,018.40				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
113	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
114	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	02/2019	4.99	129
115	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2019	10.58	131
116	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	04/2019	65.82	108
117	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2019	92.75	119
118	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
119	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
120	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
121	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
122	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
123	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54	3
124	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
125	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
126	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
127	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
128	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91
	Total		12,281.13 -	15,335.75				
	<u>SHIPPING AND PORTS</u>							
	<u>Port Trust</u>							
129	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	03/2006 -	02/2019	300.00	155
	Total		150.00 -	600.00				
	<u>STEEL</u>							
	<u>Rastrya Ispat Nigam Limited</u>							
130	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2020	42.39	41
	Total		343.00 -	488.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
131	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
132	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
133	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	486.54	05/2017 -	03/2019	25.40	22
134	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
135	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
	Total		2,217.65 -	2,843.53				
	Grand Total		2,52,513.23	4,06,756.56				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(January 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	10/2021	74.69	133
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
	Total		14,951.00 -	22,680.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	<u>COAL</u>							
	<u>Singareni Colliers Company Limited</u>							
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
5	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
7	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							
8	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
9	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
	Total		1,549.74 -	2,394.02				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
10	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		197.79	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
11	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11	513.89	11/2013	10/2020	24.10	83
	Total		414.11	513.89				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29	5,245.96	08/2018	11/2019	14.33	15
	<u>Gas Authority Of India Limited</u>							
13	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00	5,751.00	12/2012	06/2019	97.29	78
	<u>Hindustan Petroleum Corporation Limited</u>							
14	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81	723.40	10/2014	02/2019	133.50	52
	<u>Indian Oil Corporation Limited</u>							
15	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06	714.25	10/2017	03/2019	17.66	17
16	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175	03/2014	3,076.00	4,190.00	09/2017	03/2019	36.22	18
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
17	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256	10/2015	135.00	170.70	03/2019	05/2019	26.44	2
	<u>Oil & Natural Gas Corporation Limited</u>							
18	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94	330.35	01/2014	11/2019	62.78	70
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79	1,577.15	05/2013	03/2019	83.01	70
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63	2,665.65	03/2015	12/2019	29.42	57
21	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69	3,247.19	04/2018	05/2019	1.77	13
	<u>Oil India Limited</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
22	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	06/2019	24.47	27
	Total		18,298.77 -	25,054.49				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
23	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69	147
	<u>National Thermal Power Corporation</u>							
24	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14	93
25	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41	60
26	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	01/2019	86.27	88
27	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55	24
28	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55	21
29	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91	28
30	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64	10
31	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65	123
32	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55	20
	<u>North East Electric Power Corporation</u>							
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51	111
	<u>Power Grid Corporation Of India Limited</u>							
34	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	02/2019	32.69	35
35	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	03/2019	14.60	37
36	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92	23
37	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	02/2019	26.82	11
38	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	02/2019	79.61	54

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	550.18	11/2016 -	12/2019	5.34	37
40	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	06/2019	31.17	60
41	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	04/2019	54.59	103
42	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,891.41	04/2016 -	06/2019	38.61	38
43	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	03/2019	22.93	124
44	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061	10/2008	4,824.12 -	5,071.94	10/2012 -	06/2019	5.14	80
45	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15	12
46	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28	12
47	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65	103
	<u>Satluj Jal Vidyut Nigam Limited</u>							
48	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194	05/2015	436.68 -	602.44	12/2016 -	03/2019	37.96	27
	<u>Thdc India Limited</u>							
49	DHUKWAN SMALL HYDRO PROJECT - [N18000189	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75	68
50	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77	102
51	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65	63
	Total		1,27,518.04 -	1,70,513.31				
	<u>RAILWAYS</u>							
	<u>Container Corporation Of India</u>							
52	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							
53	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73	96
54	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
55	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
56	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
57	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48	61
	<u>East Coast Railway</u>							
58	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45	28
59	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43	25
60	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
61	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96	147
	<u>Eastern Railways</u>							
62	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2022	36.26	36
63	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	1,125.89 -	2,021.29	03/2016 -	03/2020	79.53	48
	<u>Metropolitan Rapid Transport Projects</u>							
64	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06	69
65	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
66	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	<u>North East Frontier Railway</u>							
67	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
68	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11	31
69	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
70	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
71	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95	79
72	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,040.00	12/2008 -	03/2019	157.59	123

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,407.00	03/2014 -	03/2019	198.34	60
74	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
75	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56	81
76	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02	108
	<u>North Eastern Railway</u>							
77	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16	46
78	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	01/2019	35.17	5
79	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80	12
80	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	03/2019	196.84	239
	<u>North Western Railway</u>							
81	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	06/2019	24.47	8
82	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	05/2019	44.16	3
83	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33	25
84	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	12/2019	93.87	10
85	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	05/2019	70.85	62
86	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	10/2020	46.55	67
	<u>Northern Railway</u>							
87	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96	220
	<u>Rail Vikas Nigam Ltd.</u>							
88	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	02/2019	188.58	119
89	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70	117
90	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
91	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,077.00	03/2019 -	03/2020	16.18	12
92	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
93	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15	111
94	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57	27
95	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	732.81 -	1,993.00	03/2008 -	03/2020	171.97	144
96	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
	<u>South Central Railway</u>							
98	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85	168
99	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47	12
	<u>South East Central Railway</u>							
100	CHHINDWARA-MANDLA FORT GC - [N22000481	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22	96
	<u>South Eastern Railway</u>							
101	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	09/2019	153.41	33
102	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81	12/2015 -	02/2019	69.92	38
103	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADE FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05	36
104	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99	108
105	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76	3
106	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
107	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96	36
108	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84	24
	<u>Southern Railway</u>							
109	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72	71
	<u>West Central Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
110	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
111	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
112	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
	Total		60,943.39 -	1,41,018.40				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
113	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
114	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	02/2019	4.99	129
115	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2019	10.58	131
116	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	04/2019	65.82	108
117	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2019	92.75	119
118	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
119	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
120	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
121	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
122	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
123	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54	3
124	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
125	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
126	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
127	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
128	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91
	Total		12,281.13 -	15,335.75				
	<u>SHIPPING AND PORTS</u>							
	<u>Port Trust</u>							
129	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	03/2006 -	02/2019	300.00	155
	Total		150.00 -	600.00				
	<u>STEEL</u>							
	<u>Rastrya Ispat Nigam Limited</u>							
130	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2020	42.39	41
	Total		343.00 -	488.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
131	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
132	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
133	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	486.54	05/2017 -	03/2019	25.40	22
134	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
135	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
	Total		2,217.65 -	2,843.53				
	Grand Total		2,52,513.23	4,06,756.56				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	05/2014 -	04/2018
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2018
3	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	10/2018
4	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Mahanadi Coal Fields Limited</u>				
5	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	03/2010 -	03/2018
	<u>Northern Coal Fields Limited</u>				
6	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	03/2012 -	-
	<u>Singareni Colliers Company Limited</u>				
7	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
8	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 -	-
	<u>South-Eastern Coal Fields Limited</u>				
9	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	03/2018 -	-
	<u>Western Coal Fields Limited</u>				
10	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	03/2018 -	03/2018
	Total		3,688.32 -		
	<u>STEEL</u>				
	<u>Steel Authority Of India Limited (Sail)</u>				
11	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
12	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		4,937.93 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
13	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	<u>Chennai Petroleum Corporation Limited</u>				
14	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
15	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				
16	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 12/2018	12/2018
17	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	12/2016 -	-
18	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 -	-
19	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	-
20	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	- -	-
21	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	- -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
23	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	-
	<u>Oil India Limited</u>				
24	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
25	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		13,431.32 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
27	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	01/2017 -	-
28	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
29	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
30	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
31	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
	<u>North East Electric Power Corporation</u>				
32	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 -	07/2013 -	-
	<u>Power Grid Corporation Of India Limited</u>				
33	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	09/2014 -	-
34	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL, MULTI STATE	03/2013	2,514.88 -	12/2015 -	-
35	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	07/2018 -	-
	Total		44,832.56 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
36	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS, MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 06/2019	-
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
37	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-
38	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	03/2018 -	-
	Total		681.15 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
39	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Container Corporation Of India</u>				
40	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
41	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
42	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
43	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
44	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
45	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
46	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
47	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
48	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
49	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
50	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
51	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
52	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
53	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
54	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
55	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-
<u>East Coast Railway</u>					
56	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
57	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
58	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
<u>Eastern Railways</u>					
59	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	01/2006
60	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 02/2010	02/2010
61	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	05/2010
62	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	193.08 -	12/2011 -	09/2012
63	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHNANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 12/2013	12/2013
64	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	259.51 -	02/2012 -	09/2016
65	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	12/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
66	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	-
67	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
68	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
69	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
70	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
71	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
72	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	-
73	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	-
74	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
75	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
76	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
77	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
78	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	-
79	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
80	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
81	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	-
82	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
83	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
84	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
85	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
86	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
88	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
89	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
90	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
91	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
92	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
93	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>North East Frontier Railway</u>				
94	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 984.97	03/2007 -	04/2016
95	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	792.46 724.31	12/2010 -	-
96	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- -	-
97	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-
	<u>North Eastern Railway</u>				
98	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	03/2018
99	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	06/2018 -	10/2018
100	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71 -	- -	-
101	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
102	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
103	KAPILVASTU-BASTI VIA BANSI SIDHARTH NAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
104	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
105	GONDA - BAHRAICH (60 KMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER, UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-
106	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
107	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH	04/2016	602.50 -	- -	-
	<u>North Western Railway</u>				
108	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
110	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
111	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
112	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
113	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
114	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
115	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-
116	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
117	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
118	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
119	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
120	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
121	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-
122	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
123	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
124	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
125	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
126	JAKHAL-MANSAB DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
127	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
128	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
129	UNCHAHA-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-
130	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
131	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
132	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Rail India Technical And Economic Service</u>				
133	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
134	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
135	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
136	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
137	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
138	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
139	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
140	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
141	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 -	- -	-
142	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
143	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
144	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH	04/2013	3,055.00 -	09/2018 -	-
	<u>South Eastern Railway</u>				
145	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
146	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
147	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
148	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
149	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	633.87 -	- -	-
	<u>Southern Railway</u>				
150	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 -	03/2018 -	03/2018
151	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
152	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
153	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
154	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
155	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
156	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
157	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
158	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
159	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
160	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
161	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
162	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
163	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
164	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
165	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
166	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
167	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
168	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
169	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-
170	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-
171	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
172	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
173	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-
174	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-
175	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-
176	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-
	<u>Western Railway</u>				
177	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
178	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
179	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
180	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
181	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
182	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		87,709.34 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
183	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
184	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
185	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
186	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
187	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
188	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
189	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
190	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-
191	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
192	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
193	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
194	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
195	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
196	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
197	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
198	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
199	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
200	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
201	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
202	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
203	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
204	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
205	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
206	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-
207	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-
208	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
209	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
210	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
214	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-
215	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
216	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
217	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
218	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
219	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
220	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
221	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
222	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
223	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
224	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
225	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
226	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
228	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
229	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
230	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
232	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
233	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
234	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
235	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
236	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
237	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
238	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-
239	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-
240	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
241	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
242	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
243	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-
244	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-
245	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
246	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	-
247	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
248	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	06/2018 -	-
249	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM	03/2015	168.39 -	11/2018 -	-
250	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM	10/2014	588.95 -	11/2018 -	-
251	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL, ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	-
252	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL, ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	-
253	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
254	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA	10/2014	369.00 -	03/2018 -	-
255	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL, TRIPURA	05/2014	497.89 -	04/2017 -	-
256	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL, ARUNACHAL PRADESH	03/2015	235.08 -	05/2018 -	-
257	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL, ASSAM	12/2015	225.02 -	12/2018 -	-
258	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	12/2015	223.30 -	06/2018 -	-
259	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	-
260	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	12/2018 -	-
261	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	01/2016 -	-
262	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	01/2016 -	-
263	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
264	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL, ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	-
265	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
266	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
267	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
268	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
269	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
270	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
271	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
272	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
273	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
274	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
275	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
276	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
277	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
278	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
279	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
280	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
281	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
282	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
283	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
284	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
285	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
286	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
287	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
288	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
289	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-
290	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-
291	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	-
292	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
293	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
294	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
295	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
296	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
297	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
298	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
299	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
300	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-
301	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
302	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
303	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
304	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
305	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
306	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL	03/2017	158.65 -	06/2018 -	-
307	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- -	-
308	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
	<u>National Highways Authority Of India</u>				
309	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	09/2018
310	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2018
311	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	12/2018
312	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	07/2018
313	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	08/2018
314	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018
315	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	10/2018
316	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	11/2018
317	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	11/2018
318	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018
319	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2018
320	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2018
321	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018
322	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2018

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
323	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	12/2018
324	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2018
325	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	12/2018
326	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	12/2018
327	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2018
328	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	12/2018
329	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
330	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
331	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
332	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
333	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
334	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
335	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
336	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
337	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-
338	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
339	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
340	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
341	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
342	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
343	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
344	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
345	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
346	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
347	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
348	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
349	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	-
350	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
351	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
352	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
353	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
354	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
355	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
356	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
357	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	-
358	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	-
359	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
360	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
361	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
362	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	-	-
363	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
364	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	05/2018 -	-
365	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
366	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
367	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
368	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
369	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
370	MEERUT-BULANDSHAHAH - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	-	-
371	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
372	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
373	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
374	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
375	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	-
376	4-LANNING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
377	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
378	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-
379	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-
380	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
381	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
382	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
383	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
384	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-
385	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-
386	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
387	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
388	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
389	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
390	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
391	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-
392	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
393	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
394	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION - [N24000711]NHAI, RAJASTHAN	12/2017	1,308.73 -	- -	-
395	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA	12/2017	404.94 -	- -	-
396	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI, BIHAR	12/2017	2,598.00 -	- -	-
397	REHABILITATION AND UPGRADE OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA	12/2017	686.65 -	- -	-
398	REHABILITATION AND UPGRADE OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA	12/2017	417.51 -	- -	-
399	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-
400	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH	12/2017	328.67 -	- -	-
401	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTING - [N24000719]NHAI, ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
402	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI, ANDHRA PRADESH	12/2017	357.00 -	- -	-
403	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	-
404	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	-
405	REHABILITATION AND UPGRADE OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	- -	-
406	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	- -	-
407	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND	01/2018	273.46 -	- -	-
408	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND	01/2018	1,155.16 -	- -	-
409	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI, MADHYA PRADESH	01/2018	770.73 -	- -	-
410	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA	01/2018	607.00 -	- -	-
411	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA	01/2018	621.00 -	- -	-
412	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI, ODISHA	01/2018	953.09 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
413	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
414	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
415	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-
416	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
417	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
418	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
419	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
420	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
421	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
422	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
423	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
424	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
425	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	-
426	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
427	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	-
428	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
429	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-
430	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	-
431	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
432	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
433	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-
434	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
435	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-
436	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
437	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
438	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	-
439	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
440	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	-
441	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
442	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
443	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
444	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
445	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
446	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	-
447	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	-
448	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
449	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
450	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	-
451	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-
452	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
453	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
454	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
455	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	-
456	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	-
457	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
458	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	-
459	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
460	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
461	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
462	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	-
463	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
464	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	-
465	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
466	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
467	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
468	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-
469	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
470	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-
471	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
472	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-
473	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
474	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	-
475	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
476	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	-
477	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
478	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	-
479	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	-
480	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
481	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-
<u>National Highways Development Project</u>					
482	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	-
483	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
484	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-
485	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
486	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
487	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-
488	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
489	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-
490	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
491	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
492	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-
493	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-
494	SHAHDL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-
495	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
496	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-
497	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-
498	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-
499	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-
500	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-
501	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
502	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-
503	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-
504	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-
Public Works Dept Of State					
505	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
506	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
507	YAN TO NIRMAL SEREABILITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
508	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
509	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
510	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	-
511	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	-
512	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-
513	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
514	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
515	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	-
516	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-
517	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	-
518	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-
519	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
520	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	-
521	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
522	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
523	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
524	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
525	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
526	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
527	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
528	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
529	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
530	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
531	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	-
532	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
533	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
534	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
535	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
536	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
537	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
538	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	-
539	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	-
540	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-
541	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
542	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
543	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
544	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
545	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
546	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
547	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
548	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
549	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
550	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
551	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
552	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
553	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
554	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
555	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
556	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
557	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
558	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
559	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
560	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
561	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
562	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-
563	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
564	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
565	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
566	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-
567	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
568	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
569	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
570	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-
571	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-
572	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-
573	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-
574	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-
575	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
576	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
577	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
578	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
579	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
580	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
581	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-
582	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
583	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
584	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-
585	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
586	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
587	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-
588	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
589	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
	Total		2,36,933.10 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
590	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.33	12/2017 03/2018	-
	<u>Mumbai Port Trust</u>				
591	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	12/2010 -	-
	<u>Port Trust</u>				
592	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		3,038.29 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
593	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
594	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
595	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	09/2018 -	09/2018
596	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	-
597	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
598	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
599	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-
600	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-
601	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- -	-
602	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
	<u>Chennai Metro Rail Ltd</u>				
603	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
604	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
605	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
606	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
607	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
608	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
609	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
610	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
611	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
612	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
613	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
614	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
615	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
616	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-
617	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-
618	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
619	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
<u>National Building Construcion Corporation Ltd</u>					
620	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		28,492.22 -		
<u>DEFENCE PRODUCTION</u>					
<u>Goa Shipyard Limited</u>					
621	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA	12/2016	167.69 168.00	05/2018 01/2019	-
	Total		167.69 -		
	Grand Total		4,28,159.35		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (January 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation</u>								
1	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	601.02	96.75	- -	02/2020	-	0/0
2	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	582.99	61.17	- -	02/2020	-	0/0
3	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99	58.04	- -	02/2020	-	0/0
4	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	268.84	68.33	- -	04/2020	-	0/0
5	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	249.01	46.28	- -	05/2020	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>								
6	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	156.65	54.94	- -	02/2020	-	0/0
	Total		2,510.41 -	2,510.50	385.51				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
7	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 -	3,020.94	-	- -	03/2021	-	0/0
8	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	1,474.47	338.44	- -	03/2021	-	0/0
9	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39 -	566.41	759.20	- -	12/2021	-	0/0
10	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 -	589.15	183.72	- -	03/2022	-	0/0
11	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	2,066.77	330.82	- -	03/2023	-	0/0
12	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	1,605.17 -	1,605.17	.19	- -	03/2023	-	0/0
	<u>East Coast Railway</u>								
13	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 -	729.92	253.10	- -	03/2021	-	0/0
14	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56 -	2,614.36	111.71	- -	03/2022	-	0/0
	<u>North Central Railway</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	10.34	- -	12/2022	-	0/0
	<u>North East Frontier Railway</u>								
16	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	4.98	- -	03/2020	-	0/0
17	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	380.00	101.19	- -	03/2020	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
18	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	2,062.30 2,062.30	2,062.20	758.09	- -	03/2022	-	0/2
	<u>South Eastern Railway</u>								
19	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	365.00	198.49	- 12/2018	01/2020	13(R3)	0/0
20	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	0(R3)	0/0
21	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.77	- 03/2025	03/2025	0(R3)	0/0
22	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	426.00	-	- 03/2030	03/2030	0(R3)	0/0
	<u>South Western Railway</u>								
23	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	1,190.92	207.68	- 03/2021	03/2021	0(R3)	0/0
24	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 1,801.01	1,801.01	14.24	- 12/2023	12/2023	0(R3)	0/0
25	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	1,350.91	927.55	- -	12/2023	-	0/1
26	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	692.43	-	- 12/2023	12/2023	0(R3)	0/0
27	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- 12/2023	12/2023	0(R3)	0/0
28	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 348.85	348.85	.36	- 12/2023	12/2023	0(R3)	0/0
29	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	0(R3)	0/0
30	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	0(R3)	0/0
31	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	2,135.00	144.75	- 12/2024	12/2024	0(R3)	0/0
	<u>Southern Railway</u>								
32	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	83.15	- -	03/2020	-	0/0
	<u>Western Railway</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
33	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	844.10 -	844.10	62.58	-	03/2023	-	0/0
	Total		19,462.59 -	29,726.03	4,532.83				0/3
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways Authority Of India</u>								
34	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	795.76	464.01	-	03/2019	-	0/0
35	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	453.09	-	03/2019	-	0/0
36	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	476.73	-	03/2019	-	0/0
37	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	454.51	-	03/2019	-	0/0
38	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	1,665.00	1,901.17	-	03/2019	-	0/0
39	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	256.10	-	03/2019	-	0/0
40	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	854.80	551.98	-	03/2019	-	0/0
41	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	425.60	-	-	03/2019	-	0/0
42	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	727.93	-	04/2019	-	0/0
43	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	161.79	-	04/2019	-	0/0
44	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	794.30	398.49	-	05/2019	-	0/0
45	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	290.73	101.84	-	05/2019	-	0/0
46	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	-	-	06/2019	-	0/0
47	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	998.18	213.85	-	08/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
48	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	763.08	140.35	- -	08/2019	-	0/0
49	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	723.64	216.75	- -	09/2019	-	0/0
50	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	417.19	100.75	- -	09/2019	-	0/0
51	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	720.00	181.70	- -	10/2019	-	0/0
52	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	834.64	138.71	- -	10/2019	-	0/0
53	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	752.28	-	- -	11/2019	-	0/0
54	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	688.70	490.54	- -	11/2019	-	0/0
55	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	447.75	135.01	- -	11/2019	-	0/0
56	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	1,167.45	38.33	- -	12/2019	-	0/0
57	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	364.56	64.61	- -	12/2019	-	0/0
58	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	458.03	20.00	- -	12/2019	-	0/0
59	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	1,100.19	650.00	- -	12/2019	-	0/0
60	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI, ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	-	- -	12/2019	-	0/0
61	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	47.90	- -	01/2020	-	0/0
62	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	814.04	279.13	- -	01/2020	-	0/0
63	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	829.97	72.69	- -	01/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
64	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	196.05	108.91	- -	01/2020	-	0/0
65	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	1,443.00	147.72	- -	02/2020	-	0/0
66	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	349.13	- -	02/2020	-	0/0
67	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	85.00	- -	02/2020	-	0/0
68	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	-	- -	04/2020	-	0/0
69	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	50.71	- -	04/2020	-	0/0
70	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	1,169.61	301.34	- -	04/2020	-	0/0
71	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	734.18	- -	05/2020	-	0/0
72	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	1,232.21	637.48	- -	05/2020	-	0/0
73	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	5.71	- -	07/2020	-	0/0
74	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	-	- -	07/2020	-	0/0
75	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	32.50	- -	07/2020	-	0/0
76	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASTHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
77	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	960.24	-	- -	08/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
78	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	-	- -	09/2020	-	0/0
79	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	20.12	- -	10/2020	-	0/0
	Total		41,621.10 -	41,621.10	11,577.76				0/0
	Grand Total		63,594.10	73,857.63	16,496.10				0/3

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Eastern Coal Fields Limited</u>					
2	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND	08/2018	513.98 -	03/2024 -	03/2024	0/0
	<u>Mahanadi Coal Fields Limited</u>					
3	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA	05/2018	2,434.75 -	03/2027 -	03/2027	0/0
	<u>Neyveli Lignite Corporation</u>					
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>South-Eastern Coal Fields Limited</u>					
7	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH	05/2018	410.26 -	03/2026 -	03/2026	0/0
8	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH	11/2018	389.97 -	03/2026 -	03/2026	0/0
	<u>Western Coal Fields Limited</u>					
9	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
10	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					
11	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
12	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	06/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
13	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
14	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	03/2021 -	03/2021	0/0
15	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
16	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
<u>Chennai Petroleum Corporation Limited</u>						
17	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
18	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
<u>Gas Authority Of India Limited</u>						
19	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
20	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 -	12/2021 -	12/2021	0/0
21	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 243.53	07/2022 -	07/2022	0/0
22	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	181.20 -	07/2022 -	07/2022	0/0
23	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0
24	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45 -	10/2022 -	10/2022	0/0
<u>Hindustan Petroleum Corporation Limited</u>						
25	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
26	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	06/2020 -	06/2020	0/0
27	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	06/2020 -	06/2020	0/0
28	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	04/2021	0/0
<u>Indian Oil Corporation Limited</u>						
29	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 -	02/2020 -	02/2020	0/0
30	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	02/2020 -	02/2020	0/0
31	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	02/2020 -	02/2020	0/0
32	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
33	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT	09/2016	208.35 -	07/2020 -	07/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
34	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	08/2020 -	08/2020	0/0
35	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	08/2020 -	08/2020	0/0
36	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	10/2020	0/0
37	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	10/2020 -	10/2020	0/0
38	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
39	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
40	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	01/2021 -	01/2021	0/0
41	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
42	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
43	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 -	03/2021	0/0
44	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
45	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2021	0/0
46	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA	04/2018	5,654.00 -	10/2021 -	07/2021	0/0
47	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
48	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
49	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
50	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	10/2021 -	10/2021	0/0
51	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
52	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	04/2022	0/0
53	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	-	0/0
<u>Indian Strategic Petroleum Reserves Ltd</u>						
54	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
<u>Mangalore Refinery And Petrochemicals Limited</u>						
55	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	03/2020 -	03/2020	0/0
<u>Oil India Limited</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
56	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
57	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL, MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
58	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	10/2023	0/0
	<u>National Hydro-Electric Power Corporation</u>					
59	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>National Thermal Power Corporation</u>					
60	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
61	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
62	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 307.18	11/2017 10/2018	02/2019	0/0
63	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH	01/2016	305.04 305.04	03/2017 09/2018	02/2019	0/0
64	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 766.21	11/2018 11/2018	02/2019	0/0
65	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL, GUJARAT	07/2016	300.94 300.94	12/2018 12/2018	02/2019	0/0
66	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 374.63	04/2016 12/2017	03/2019	0/0
67	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 197.40	03/2018 -	03/2019	0/0
68	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38 1,429.38	01/2019 01/2019	03/2019	0/0
69	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHHATISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL, MULTI STATE	07/2016	333.17 333.17	03/2019 03/2019	03/2019	0/0
70	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL, MULTI STATE	08/2016	431.89 431.89	02/2019 02/2019	03/2019	0/0
71	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL, MULTI STATE	09/2016	562.25 562.25	03/2019 03/2019	03/2019	0/0
72	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 322.30	02/2019 02/2019	03/2019	0/0
73	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL, MULTI STATE	03/2017	162.31 162.31	03/2019 03/2019	03/2019	0/0
74	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL, MULTI STATE	02/2017	204.12 204.12	09/2019 09/2019	03/2019	0/0
75	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA	04/2016	844.64 844.64	04/2019 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
76	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 608.24	04/2019 04/2019	04/2019	0/0
77	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
78	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 3,519.59	05/2019 05/2019	05/2019	0/0
79	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL, BIHAR	04/2016	790.13 790.30	06/2019 06/2019	06/2019	0/0
80	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL, MULTI STATE	03/2017	251.60 251.60	06/2019 06/2019	06/2019	0/0
81	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 408.46	01/2019 01/2019	06/2019	0/0
82	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 235.53	06/2019 06/2019	06/2019	0/0
83	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL, MULTI STATE	03/2017	337.75 337.75	06/2019 06/2019	06/2019	0/0
84	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 445.89	02/2019 02/2019	06/2019	0/0
85	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 186.17	07/2019 07/2019	07/2019	0/0
86	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 808.63	01/2018 03/2019	09/2019	0/0
87	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 175.64	09/2018 09/2018	09/2019	0/0
88	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 193.14	06/2019 06/2019	09/2019	0/0
89	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 14,733.37	11/2019 11/2019	11/2019	0/0
90	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL, MULTI STATE	03/2017	283.72 283.72	11/2019 11/2019	11/2019	0/0
91	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 379.95	12/2019 12/2019	12/2019	0/0
92	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL, MULTI STATE	12/2014	4,754.42 4,754.42	12/2018 12/2018	12/2019	0/0
93	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 5,111.33	12/2018 12/2018	12/2019	0/0
94	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 454.11	04/2018 01/2020	01/2020	0/0
95	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL, MULTI STATE	02/2017	195.05 195.05	02/2020 02/2020	02/2020	0/0
96	HVDC BIPOLE LINK BETWEEN WR AND SR-NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 1,931.39	02/2020 02/2020	02/2020	0/0
97	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 198.49	09/2019 02/2020	02/2020	0/0
98	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL, MULTI STATE	02/2017	5,070.13 5,070.13	04/2020 04/2020	04/2020	0/0
99	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 358.83	05/2020 05/2020	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
101	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	-	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Indira Gandhi Centre For Atomic Research</u>					
102	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI	08/2016	1,554.00 -	09/2019 -	09/2019	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
103	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	04/2020	0/0
104	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	06/2020	0/0
105	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	05/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					
106	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2019	0/0
107	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	02/2020	0/0
108	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	02/2020	0/0
109	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	02/2020	0/0
110	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
111	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2020	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
112	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	03/2019	0/0
113	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2019	0/0
114	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2019	0/0
115	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 09/2019	09/2019	0/0
116	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	02/2020	0/0
117	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 10/2020	10/2020	0/0
118	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
119	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 -	03/2019	0/0
120	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 2,271.50	03/2021 -	03/2021	0/0
121	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 792.89	03/2021 -	03/2021	0/0
122	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 540.02	03/2022 -	03/2022	0/0
123	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 1,272.19	03/2022 -	03/2022	0/0
124	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 3,168.29	03/2023 -	03/2023	0/0
125	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 2,449.91	03/2023 -	03/2023	0/0
126	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	03/2023 -	03/2023	0/0
127	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 1,035.16	03/2022 -	03/2023	0/0
128	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 637.95	03/2023 -	03/2023	0/0
129	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
130	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
131	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
132	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.47	03/2024 -	03/2024	0/0
133	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
	<u>Container Corporation Of India</u>					
134	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
135	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
136	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	08/2019	0/0
137	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	12/2019	0/0
138	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
139	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
140	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
141	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
142	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
143	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	<u>East Central Railways</u>					
144	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
145	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 -	03/2012 -	03/2020	0/0
146	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 -	03/2020 -	03/2020	0/0
147	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	477.88 283.95	03/2012 -	03/2020	0/0
148	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	548.00 -	03/2020 -	03/2020	0/0
149	GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
150	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 -	- -	03/2021	0/0
151	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	03/2021	0/0
152	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
153	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR, BIHAR	11/2001	624.47 -	02/2016 -	03/2021	0/0
154	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39 -	- -	12/2021	0/0
155	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 -	- -	03/2022	0/0
156	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR, BIHAR	04/2016	744.04 -	03/2021 -	03/2022	0/0
157	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR, BIHAR	04/2016	731.64 -	03/2021 -	03/2022	0/0
158	HAJIPUR-SAGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	- -	03/2023	0/0
159	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	1,605.17 -	- -	03/2023	0/0
160	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-	0/0
161	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
162	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
163	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
164	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
165	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
166	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
167	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
168	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
169	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
170	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
171	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
172	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-	0/0
	<u>East Coast Railway</u>					
173	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2020	0/0
174	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
175	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
176	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	03/2021	0/0
177	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 -	03/2021	0/0
178	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2021	0/0
179	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2021	0/0
180	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	06/2021	0/0
181	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
182	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2022 -	03/2022	0/0
183	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	03/2022	0/0
184	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2022 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
185	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	03/2023	0/0
186	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
187	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
188	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
	<u>Eastern Railways</u>					
189	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	01/2006	0/0
190	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 02/2010	02/2010	0/0
191	CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	05/2010	0/0
192	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	193.08 -	12/2011 -	09/2012	0/0
193	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 12/2013	12/2013	0/0
194	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 -	02/2012 -	09/2016	0/0
195	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	03/2016 -	03/2020	0/0
196	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2020	0/0
197	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2020	0/0
198	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2022	0/0
199	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2022	0/0
200	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	-	0/0
201	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
202	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
203	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
204	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
205	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
206	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	-	0/0
207	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
209	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
210	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
211	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
212	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	-	0/0
213	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
214	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
215	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	-	0/0
216	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
217	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
218	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
219	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
220	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
221	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
222	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
223	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
224	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
225	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
226	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
227	JHANSI BINA DOUBLING - [N22000496]NCR, UTTAR PRADESH	09/2016	2,001.00 -	03/2021 -	03/2021	0/0
228	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	2,912.96 -	03/2022 -	03/2022	0/0
229	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
230	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
231	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
232	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
233	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
	<u>North East Frontier Railway</u>					
234	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 984.97	03/2007 -	04/2016	0/0
235	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	03/2019	0/0
236	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	1,142.00 3,407.00	03/2014 12/2019	03/2019	0/0
237	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019	0/0
238	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 486.96	03/2019 -	03/2019	0/0
239	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 614.81	03/2019 -	03/2019	0/0
240	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 200.34	03/2019 -	03/2020	0/0
241	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	03/2011 -	03/2020	0/0
242	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	03/2019 -	03/2020	0/0
243	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2020	0/0
244	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	03/2020	0/0
245	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
246	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	03/2020	0/0
247	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
248	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
249	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
250	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
251	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
252	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 2,393.48	03/2014 12/2020	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
253	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	03/2021	0/0
254	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
255	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 2,446.57	03/2015 10/2021	10/2021	0/0
256	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	792.46 724.31	12/2010 -	-	0/0
257	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
258	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
	<u>North Eastern Railway</u>					
259	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
260	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	10/2018	0/0
261	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	01/2019	0/0
262	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	04/1999 -	03/2019	0/0
263	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	05/2019	0/0
264	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019	0/0
265	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2020	0/0
266	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	01/2020	0/0
267	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2020	0/0
268	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	02/2020	0/0
269	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	03/2014 -	04/2021	0/0
270	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
271	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
272	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
273	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
274	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
275	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
276	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
277	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
278	GONDA - BAHRAICH (60 KMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-	0/0
279	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
280	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
	<u>North Western Railway</u>					
281	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 05/2019	05/2019	0/0
282	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	05/2019	0/0
283	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	06/2019	0/0
284	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	11/2019	0/0
285	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	11/2019	0/0
286	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	12/2019	0/0
287	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 295.02	03/2020 -	12/2019	0/0
288	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	10/2020	0/0
289	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
290	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0
291	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
292	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
293	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	03/2021	0/0
294	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
295	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
296	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
297	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
298	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-	0/0
299	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
300	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
301	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
302	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
303	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
304	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-	0/0
305	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
306	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
307	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
308	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
309	JAKHAL-MANSAB DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
310	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
311	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
312	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-	0/0
313	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
314	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
315	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
316	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
317	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
318	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
319	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	03/2008 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
320	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
321	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2020	0/0
322	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	03/2020	0/0
323	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	03/2020	0/0
324	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 03/2017	12/2020	0/0
325	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2020	0/0
326	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
327	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
328	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
329	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 245.00	02/2015 -	12/2021	0/0
330	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
331	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2021	0/0
332	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	631.78 632.00	12/2012 -	03/2022	0/0
333	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
334	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
335	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
336	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
337	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
338	VIZIANAGARAM - SAMBALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 2,335.67	12/2024 -	12/2024	0/0
339	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
340	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 4,200.00	03/2016 -	03/2025	0/0
341	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
342	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
343	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2026	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
344	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2026	0/0
	<u>Railway Electrification</u>					
345	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	<u>South Central Railway</u>					
346	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2019	0/0
347	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2021	0/0
348	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
349	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2023	0/0
350	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2023	0/0
351	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
352	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
353	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
354	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
355	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
	<u>South East Central Railway</u>					
356	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	02/2019 -	02/2019	0/0
357	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	12/2019	0/0
358	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	03/2012 -	03/2020	0/0
359	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	04/2020 -	04/2020	0/0
360	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	03/2021 -	03/2021	0/0
361	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	12/2021 -	12/2021	0/0
362	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 -	12/2021	0/0
363	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH	04/2011	1,471.93 -	03/2022 -	03/2022	0/0
364	GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH	02/2014	2,288.00 -	03/2022 -	03/2022	0/0
365	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 -	03/2023 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
366	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
367	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH	04/2013	3,055.00 -	09/2018 -	-	0/0
	<u>South Eastern Railway</u>					
368	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 12/2018	02/2019	0/0
369	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 08/2018	09/2019	0/0
370	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- 12/2018	01/2020	0/0
371	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 03/2020	06/2020	0/0
372	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	03/2021 03/2021	12/2021	0/0
373	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	1,013.45 1,013.45	12/2021 12/2021	12/2021	0/0
374	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 03/2024	03/2024	0/0
375	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	- 12/2024	12/2024	0/0
376	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 12/2024	12/2024	0/0
377	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- 03/2025	03/2025	0/0
378	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	- 03/2030	03/2030	0/0
379	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 03/2030	03/2030	0/0
380	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
381	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
382	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
383	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
384	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	633.87 -	- -	-	0/0
	<u>South Western Railway</u>					
385	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	03/2020 03/2020	03/2020	0/0
386	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.52	03/2017 -	03/2020	0/0
387	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- 03/2021	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
388	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,870.41	03/2019 03/2021	03/2021	0/0
389	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 1,801.01	- 12/2023	12/2023	0/0
390	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- 12/2023	12/2023	0/0
391	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- 12/2023	12/2023	0/0
392	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 348.85	- 12/2023	12/2023	0/0
393	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	- 12/2023	12/2023	0/0
394	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- 12/2023	12/2023	0/0
395	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	03/2016 12/2023	12/2023	0/0
396	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	03/2002 03/2024	03/2024	0/0
397	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 03/2024	03/2024	0/0
398	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- 12/2024	12/2024	0/0
399	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	12/2018 12/2024	12/2024	0/0
	<u>Southern Railway</u>					
400	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 -	03/2018 -	03/2018	0/0
401	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2019	0/0
402	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	02/2019	0/0
403	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	03/2019	0/0
404	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
405	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
406	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	03/2020	0/0
407	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
408	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
409	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
410	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
411	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
412	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
413	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
414	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
415	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
416	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
417	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
418	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
419	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
420	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
421	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
422	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
423	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
424	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
425	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
426	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-	0/0
427	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-	0/0
428	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
429	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
430	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-	0/0
431	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-	0/0
432	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-	0/0
433	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-	0/0
	<u>West Central Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
434	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	03/2021 -	03/2021	0/0
	<u>Western Railway</u>					
435	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
436	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 -	03/2019 -	03/2019	0/0
437	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 -	03/2020 -	03/2020	0/0
438	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	03/2021 -	03/2020	0/0
439	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 -	03/2020 -	03/2020	0/0
440	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 -	06/2020 -	06/2020	0/0
441	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 -	03/2022 -	03/2022	0/0
442	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	03/2022 -	03/2022	0/0
443	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	03/2022 -	03/2022	0/0
444	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	03/2019 -	03/2022	0/0
445	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	- -	03/2023	0/0
446	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
447	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
448	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
449	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
450	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
451	PALANPUR KHODIAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
452	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	06/2019	0/0
453	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	06/2019	0/0
454	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
455	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
456	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
457	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
458	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS	11/2017	257.34 -	11/2019 12/2019	11/2019	0/0
459	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
460	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
461	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
462	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
463	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
464	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
465	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
466	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
467	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
468	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
469	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
470	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
471	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
472	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
473	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
474	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
475	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
476	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
477	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
478	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
479	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
480	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-	0/0
481	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
482	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
483	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-	0/0
484	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-	0/0
485	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
486	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
487	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
488	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
489	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
490	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
491	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-	0/0
492	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
493	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
494	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
495	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
496	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
497	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
498	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
499	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
500	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
501	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
502	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
503	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
504	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
505	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
506	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
507	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
508	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
509	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
510	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
511	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
512	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
513	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
514	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
515	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-	0/0
516	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-	0/0
517	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
518	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
519	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
520	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-	0/0
521	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
522	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	National Highways And Infrastructure Development Corporation Ltd.					
523	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
524	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
525	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
526	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
527	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-	0/0
528	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
529	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-	0/0
530	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-	0/0
531	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
532	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
533	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
534	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
535	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
536	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
537	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
538	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
539	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
540	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
541	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
542	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
543	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
544	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-	0/0
545	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-	0/0
546	(I) CONSTRUCTION OF FOUR/SIX LANEING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-	0/0
547	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0
548	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-	0/0
549	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	-	0/0
550	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-	0/0
551	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-	0/0
552	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-	0/0
553	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-	0/0
554	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-	0/0
555	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-	0/0
556	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-	0/0
557	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-	0/0
558	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-	0/0
559	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-	0/0
560	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-	0/0
561	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-	0/0
562	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-	0/0
563	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-	0/0
564	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
565	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
566	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-	0/0
	<u>National Highways Authority Of India</u>					
567	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	09/2018	0/0
568	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2018	0/0
569	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	12/2018	0/0
570	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	07/2018	0/0
571	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018	0/0
572	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	10/2018	0/0
573	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	11/2018	0/0
574	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	11/2018	0/0
575	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018	0/0
576	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2018	0/0
577	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2018	0/0
578	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018	0/0
579	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2018	0/0
580	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	12/2018	0/0
581	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2018	0/0
582	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	12/2018	0/0
583	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	12/2018	0/0
584	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2018	0/0
585	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	12/2018	0/0
586	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	01/2019	0/0
587	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	01/2019	0/0
588	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
589	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 174.34	03/2008 -	02/2019	0/0
590	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	02/2019	0/0
591	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	02/2019	0/0
592	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	02/2019	0/0
593	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	02/2019	0/0
594	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	02/2019	0/0
595	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	03/2019	0/0
596	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	03/2019	0/0
597	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2019	0/0
598	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
599	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	03/2019	0/0
600	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019	0/0
601	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2019	0/0
602	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 -	03/2019	0/0
603	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	03/2019	0/0
604	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	03/2019	0/0
605	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	03/2019	0/0
606	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	03/2019	0/0
607	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	03/2019	0/0
608	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 09/2017	03/2019	0/0
609	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2019	0/0
610	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2019	0/0
611	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	03/2019	0/0
612	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
613	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	03/2019	0/0
614	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	03/2019	0/0
615	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	03/2019	0/0
616	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	03/2019	0/0
617	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	03/2019	0/0
618	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	03/2019	0/0
619	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	03/2019	0/0
620	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 -	03/2019	0/0
621	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	03/2019	0/0
622	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	04/2019	0/0
623	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	04/2019	0/0
624	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	04/2019	0/0
625	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	04/2019	0/0
626	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	04/2019	0/0
627	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	04/2019	0/0
628	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	04/2019	0/0
629	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	04/2019	0/0
630	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	04/2019	0/0
631	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	04/2019	0/0
632	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	04/2019	0/0
633	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
634	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	04/2019	0/0
635	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	04/2019	0/0
636	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
637	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	04/2019	0/0
638	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	04/2019	0/0
639	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	04/2019	0/0
640	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	04/2019	0/0
641	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2019	0/0
642	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	05/2019	0/0
643	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	05/2019	0/0
644	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	05/2019	0/0
645	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	05/2019	0/0
646	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	05/2019	0/0
647	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	05/2019	0/0
648	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	-	05/2019	0/0
649	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	05/2019 -	05/2019	0/0
650	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	05/2019	0/0
651	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	-	05/2019	0/0
652	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	06/2019	0/0
653	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	06/2019	0/0
654	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	06/2019	0/0
655	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2019	0/0
656	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	06/2019	0/0
657	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	06/2019	0/0
658	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	06/2019	0/0
659	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	06/2019	0/0
660	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
661	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	06/2019	0/0
662	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	06/2019	0/0
663	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	06/2019	0/0
664	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	06/2019	0/0
665	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	06/2019	0/0
666	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	-	06/2019	0/0
667	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	06/2019	0/0
668	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	06/2019	0/0
669	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	06/2019	0/0
670	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	06/2019	0/0
671	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	06/2019	0/0
672	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	06/2019	0/0
673	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	07/2019	0/0
674	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	07/2019	0/0
675	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	07/2019	0/0
676	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	07/2019	0/0
677	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 -	07/2019	0/0
678	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	07/2019	0/0
679	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	07/2019	0/0
680	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	-	08/2019	0/0
681	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	-	08/2019	0/0
682	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	08/2019	0/0
683	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	08/2019	0/0
684	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
685	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	08/2019	0/0
686	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
687	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
688	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
689	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	09/2019	0/0
690	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	09/2019	0/0
691	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	03/2019 -	09/2019	0/0
692	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
693	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	10/2019	0/0
694	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	10/2019	0/0
695	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	10/2019	0/0
696	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	10/2019	0/0
697	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	- -	11/2019	0/0
698	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	11/2019	0/0
699	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	11/2019	0/0
700	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019	0/0
701	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	11/2019	0/0
702	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	04/2020 -	11/2019	0/0
703	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI, ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	11/2019	0/0
704	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2019	0/0
705	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	12/2019	0/0
706	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA	12/2015	649.50 -	03/2019 -	12/2019	0/0
707	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
708	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
709	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	12/2019	0/0
710	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	12/2019	0/0
711	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	12/2019	0/0
712	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2020	0/0
713	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	01/2020	0/0
714	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
715	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	01/2020	0/0
716	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	01/2020	0/0
717	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
718	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	02/2020	0/0
719	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
720	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
721	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
722	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
723	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
724	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
725	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
726	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
727	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
728	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	04/2020	0/0
729	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
730	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
731	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	04/2020	0/0
732	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
733	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
734	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	05/2020	0/0
735	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	05/2020	0/0
736	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
737	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	05/2020	0/0
738	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
739	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	05/2020	0/0
740	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	06/2020	0/0
741	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2020	0/0
742	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
743	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
744	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
745	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
746	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
747	REHABILITATION AND UPGRADEATION TO FOUR LANING OF BINJABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	07/2020	0/0
748	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	08/2020	0/0
749	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
750	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	08/2020	0/0
751	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
752	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
753	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	08/2020	0/0
754	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	08/2020	0/0
755	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
756	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
757	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
758	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020	0/0
759	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
760	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	11/2020	0/0
761	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
762	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 -	03/2021	0/0
763	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
764	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
765	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
766	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
767	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
768	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
769	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
770	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-	0/0
771	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
772	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
773	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
774	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
775	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
776	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
777	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
778	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
779	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
780	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
781	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
782	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
783	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
784	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
785	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
786	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
787	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
788	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
789	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	-	0/0
790	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
791	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
792	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
793	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
794	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	-	-	0/0
795	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
796	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
797	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
798	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
799	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
800	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
801	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
802	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	-	-	0/0
803	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
804	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
805	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
806	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
807	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	-	0/0
808	4-LANNING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
809	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-	0/0
810	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
811	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
812	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
813	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
814	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
815	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
816	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-	0/0
817	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-	0/0
818	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
819	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
820	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
821	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
822	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
823	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-	0/0
824	BALANCE WORK FOR FOUR LANNING OF ITARSI TO BETUL SECTION OF NH-69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
825	SIX LANNING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-	0/0
826	FOUR LANNING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
827	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-	0/0
828	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
829	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-	0/0
830	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
831	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-	0/0
832	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
833	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
834	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
835	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
836	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
837	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
838	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
839	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
840	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
841	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
842	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-	0/0
843	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-	0/0
844	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-	0/0
845	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
846	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
847	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-	0/0
848	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-	0/0
849	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
850	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
851	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
852	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
853	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
854	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
855	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
856	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
857	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	-	0/0
858	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
859	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	-	0/0
860	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
861	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
862	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	-	0/0
863	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
864	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
865	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-	0/0
866	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
867	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-	0/0
868	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
869	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
870	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	-	0/0
871	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
872	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	-	0/0
873	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
874	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
875	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
876	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
877	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
878	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	-	0/0
879	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	-	0/0
880	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
881	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
882	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	-	0/0
883	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-	0/0
884	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
885	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
886	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
887	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	-	0/0
888	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	-	0/0
889	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
890	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	-	0/0
891	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
892	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
893	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
894	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	-	0/0
895	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
896	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	-	0/0
897	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0
898	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-	0/0
899	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
900	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-	0/0
901	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
902	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-	0/0
903	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
904	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-	0/0
905	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0
906	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	-	0/0
907	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
908	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	-	0/0
909	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-	0/0
910	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	-	0/0
911	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	-	0/0
912	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
913	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-	0/0
National Highways Development Project						
914	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	01/2020	0/0
915	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-	0/0
916	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
917	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-	0/0
918	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
919	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
920	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-	0/0
921	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-	0/0
922	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
923	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
924	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-	0/0
925	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-	0/0
926	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-	0/0
927	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-	0/0
928	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-	0/0
929	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
930	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-	0/0
931	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-	0/0
932	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-	0/0
<u>Public Works Dept Of State</u>						
933	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
934	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
935	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-	0/0
936	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-	0/0
937	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
938	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
939	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
940	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
941	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
942	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
943	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
944	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
945	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
946	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
947	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
948	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-	0/0
949	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-	0/0
950	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
951	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
952	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
953	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
954	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
955	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
956	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
957	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
958	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
959	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
960	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
961	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
962	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
963	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
964	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
965	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
966	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
967	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
968	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
969	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
970	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
971	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
972	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
973	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-	0/0
974	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
975	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
976	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
977	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-	0/0
978	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
979	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-	0/0
980	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0
981	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-	0/0
982	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
983	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
984	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
985	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
986	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
987	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-	0/0
988	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
989	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
990	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
991	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
992	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
993	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
994	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-	0/0
995	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
996	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Cochin Shipyard Ltd</u>					
997	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL,KERALA	05/2016	970.00 -	05/2020 -	05/2020	0/0
998	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL,KERALA	07/2016	1,799.00 -	05/2021 -	05/2021	0/0
	<u>Kamarajar Port Limited</u>					
999	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 257.90	12/2017 05/2020	05/2020	0/0
	<u>Mumbai Port Trust</u>					
1000	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	12/2010 -	-	0/0
	<u>Port Trust</u>					
1001	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 600.00	03/2006 03/2016	02/2019	0/0
1002	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
1003	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 214.10	05/2018 02/2019	02/2019	0/0
1004	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 231.80	10/2018 02/2019	02/2019	0/0
	<u>Department Of Telecommunication</u>					
1005	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
1006	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	Bangalore Metro Rail Corporation Limited					
1007	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14	02/2019	03/2020	0/0
	Central Public Works Department					
1008	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00	06/2019	06/2019	0/0
1009	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013	10/2019	0/0
1010	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90	11/2019	11/2019	0/0
1011	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31	07/2019	11/2019	0/0
1012	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72	03/2020	03/2020	0/0
1013	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56	05/2020	05/2020	0/0
1014	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017	06/2020	0/0
1015	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31	02/2020 09/2020	09/2020	0/0
1016	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72	09/2016	-	0/0
1017	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	12/2015	-	0/0
1018	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77	-	-	0/0
1019	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00	-	-	0/0
1020	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00	-	-	0/0
1021	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20	04/2018	-	0/0
	Chennai Metro Rail Ltd					
1022	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00	03/2018	-	0/0
	Hindustan Steelwork Construction Limited					
1023	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00	03/2015	03/2021	0/0
1024	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015	-	0/0
1025	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016	-	0/0
1026	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016	-	0/0
1027	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1028	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1029	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
1030	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1031	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
1032	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1033	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1034	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1035	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0
1036	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1037	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1038	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1039	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1040	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1041	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 05/2019	05/2019	0/0
1042	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 -	11/2021	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1043	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1044	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 8,680.00	03/2018 12/2019	12/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
1045	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	Total		11,55,738.21 -			0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2019)						
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Grand Total		11,55,738.21			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	106.07	03/2023 -	03/2021
	Total		1,186.64 -	203.82	106.07		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
2	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,112.98	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
3	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
4	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,213.52	12/2020 -	08/2020
5	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	148.35	02/2019 -	01/2019
6	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	579.18	10/2019 -	03/2019
7	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	455.62	12/2020 -	02/2020
8	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	4,807.08	24.09	10/2021 -	07/2021
9	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,712.00	22.47	09/2022 -	06/2021
10	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	112.58	09/2019 -	02/2019
11	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	205.41	05/2019 -	01/2019
	Total		21,075.92 -	20,361.60	4,069.17		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
12	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 204.12	204.12	109.57	09/2019 09/2019	03/2019
	Total		204.12 -	204.12	109.57		

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
13	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	109.68	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
14	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	1,142.00 3,407.00	3,407.00	3,224.14	03/2014 12/2019	03/2019
15	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	288.01	03/2022 -	03/2020
16	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	612.00	33.12	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
17	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	231.72	12/2022 -	05/2019
18	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42	1,295.42	118.03	03/2022 -	12/2019
19	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	366.71	0.46	01/2022 -	01/2020
	<u>North Western Railway</u>						
20	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	144.17	12/2019 -	11/2019
21	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR [N22000152]	4/2013	420.18 295.02	420.18	96.91	03/2020 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
22	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.22	12/2025 -	03/2025
	<u>Western Railway</u>						
23	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39	1,002.39	316.23	03/2021 -	03/2020
	Total		8,842.70 -	11,476.34	4,562.69		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
24	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 12/2019	11/2019
	<u>National Highways Authority Of India</u>						
25	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	202.79	03/2020 -	06/2019
26	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	422.78	03/2020 -	06/2019
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	24.21	03/2020 -	06/2019

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
28	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	63.21	03/2020 -	06/2019
29	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	15.00	04/2020 -	11/2019
	Total		2,492.50 -	2,346.96	769.08		
	Grand Total		33,801.88	34,592.84	9,616.58		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	185.00	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	302.68	03/2022 -	03/2022
4	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	215.56	08/2019 -	08/2019
5	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	45.29	03/2022 -	03/2022
6	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
7	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	-	03/2024 -	03/2024
	<u>Mahanadi Coal Fields Limited</u>						
8	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	690.11	03/2026 -	03/2026
9	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	425.28	03/2021 -	03/2021
10	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	-	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
11	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	400.53	06/2015 09/2019	09/2019
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	4,524.70	11/2021 -	11/2021
13	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	8.71	09/2019 -	09/2019
14	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	173.06	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
15	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	236.49	03/2021 -	03/2021
16	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
17	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	79.96	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019
19	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
20	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.21	03/2023 -	03/2023
21	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	71.55	03/2020 -	03/2020
22	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
23	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
24	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
25	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
26	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.26	03/2021 -	03/2021
27	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,857.01	03/2023 -	03/2023
28	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,957.98	03/2023 -	03/2023
29	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.88	03/2023 -	03/2023
30	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	60.38	03/2020 -	03/2020
31	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
32	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	41.76	03/2021 -	03/2021
33	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.73	03/2021 -	03/2021
34	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	24.21	03/2023 -	03/2023
35	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
36	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	83.39	03/2022 -	03/2022
	<u>Western Coal Fields Limited</u>						
37	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	67.18	03/2020 -	03/2020
38	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	238.47	03/2025 -	03/2025
39	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	258.23	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	91.22	03/2021 -	03/2021
41	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
42	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
43	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	17.67	03/2022 -	03/2022
44	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	129.79	03/2019 -	03/2019
45	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	03/2019
46	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	191.97	03/2020 -	03/2020
47	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	333.43	.07	03/2023 03/2024	03/2024
48	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	116.35	03/2021 -	03/2021
49	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.29	03/2021 -	03/2021
50	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	397.95	03/2020 -	03/2020
51	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	105.38	03/2020 -	03/2020
52	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
	Total		73,425.24 -	72,766.79	14,980.60		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
53	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	61.95	08/2020 -	08/2020
	Total		285.95 -	285.95	61.95		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
54	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	27.83	11/2019 -	11/2019
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	27.56	11/2019 -	11/2019
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	32.53	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
57	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	145.98	11/2016 04/2019	04/2019
58	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	50.89	04/2020 -	04/2020
	Total		1,299.07 -	1,310.72	284.79		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
59	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
60	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
61	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
	<u>Hospital Services Consultancy Corporation</u>						
62	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	111.92	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
63	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	513.89	147.00	11/2013 10/2020	10/2020
64	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	122.43	03/2019 -	03/2019
65	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	125.36	03/2019 -	03/2019
66	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	145.51	05/2018 09/2019	09/2019
	Total		4,042.63 -	4,142.41	1,137.57		
	<u>HEAVY INDUSTRY</u>						
	<u>Indira Gandhi Centre For Atomic Research</u>						
67	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>MINES</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Aluminum Company Limited (Nalco)</u>						
68	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	96.98	04/2021 04/2021	04/2021
69	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	302.60	01/2020 01/2020	01/2020
70	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]	9/2017	166.62 -	166.62	134.00	06/2019 -	06/2019
71	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
72	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
	Total		7,078.62 -	7,078.62	565.50		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
73	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	535.04	10/2018 06/2019	06/2019
74	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	2,627.83	08/2018 11/2019	11/2019
75	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	122.99	12/2019 -	12/2019
76	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	501.94	02/2020 10/2020	10/2020
77	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	172.74	02/2020 -	02/2020
78	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	-	03/2021 -	03/2021
79	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	-	03/2023 -	03/2023
80	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	26.58	12/2020 -	12/2020
81	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
82	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	72.05	08/2020 -	08/2020
	<u>Chennai Petroleum Corporation Limited</u>						
83	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	646.29	12/2019 -	12/2019
84	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	22.22	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Gas Authority Of India Limited</u>						
85	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	803.00	02/2020 -	02/2020
86	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,002.53	12/2020 -	12/2020
87	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	864.97	12/2020 -	12/2020
88	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	38.20	10/2022 -	10/2022
89	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	19.60	12/2021 -	12/2021
90	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	27.11	10/2022 -	10/2022
91	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	27.55	10/2022 -	10/2022
92	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	181.20 -	181.20	17.11	07/2022 -	07/2022
93	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,028.31	12/2020 -	12/2020
94	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	106.74	04/2022 -	04/2022
95	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	34.34	07/2022 -	07/2022
96	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	25.46	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						
97	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	610.73	10/2014 02/2019	02/2019
98	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	2,864.07	07/2020 -	07/2020
99	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	407.00	288.56	09/2019 -	09/2019
100	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB, HARYANA) - [N16000242]	11/2016	230.00 -	230.00	122.05	02/2019 -	02/2019
101	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
102	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
103	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	15.68	11/2020 -	11/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
104	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
105	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	60.42	03/2021 -	03/2021
106	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,048.00	06/2020 -	06/2020
	<u>Indian Oil Corporation Limited</u>						
107	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
108	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	201.34	07/2018 10/2020	10/2020
109	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	579.41	12/2020 -	12/2020
110	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	514.20	08/2021 -	08/2021
111	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	107.15	06/2020 -	06/2020
112	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
113	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
114	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	.02	10/2021 -	10/2021
115	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	2.56	03/2021 -	03/2021
116	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]	4/2018	355.00 -	355.00	-	04/2022 -	04/2022
117	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	128.87	08/2020 -	08/2020
118	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	74.97	02/2020 -	02/2020
119	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	4.04	01/2021 -	01/2021
120	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	889.89	09/2019 -	09/2019
121	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	2.76	02/2020 -	02/2020
122	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	315.44	09/2019 -	09/2019
123	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
124	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,399.13	09/2019 -	09/2019
125	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.90	08/2020 -	08/2020
126	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	3.37	12/2021 -	12/2021
127	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	264.64	09/2019 -	09/2019
128	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	41.38	04/2021 -	04/2021
129	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	7.46	12/2021 -	12/2021
130	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	13.76	02/2020 -	02/2020
131	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	1,068.35	07/2019 -	07/2019
132	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
133	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	.10	08/2020 -	08/2020
134	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	33.79	04/2020 -	04/2020
135	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	1.84	06/2020 -	06/2020
136	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	69.50	07/2020 -	07/2020
137	LPG BP PROJECT KORDHA - [N16000283]	12/2016	161.59 -	161.59	34.31	12/2019 -	12/2019
138	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	28.75	02/2020 -	02/2020
139	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	283.06	01/2019 -	01/2019
140	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	8.74	01/2021 -	01/2021
141	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
142	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,346.72	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
143	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	217.07	08/2019 -	08/2019
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
144	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
145	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	129.95	03/2019 05/2019	05/2019
146	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
147	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
148	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,112.54	03/2013 12/2019	12/2019
149	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,513.89	05/2019 10/2019	10/2019
150	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	89.48	01/2014 11/2019	11/2019
151	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	112.87	12/2019 -	12/2019
152	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	1,671.49	05/2021 05/2021	05/2021
153	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	207.80	32.71	09/2018 02/2019	02/2019
154	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	307.27	03/2026 03/2026	03/2026
155	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	101.71	05/2020 05/2020	05/2020
156	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	1,691.99	06/2020 08/2021	08/2021
157	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	115.49	03/2023 03/2022	03/2022
158	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,123.52	04/2018 05/2019	05/2019
159	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,079.85	12/2017 03/2020	03/2020
160	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,842.42	03/2015 12/2019	12/2019
161	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,577.15	1,195.62	05/2013 03/2019	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
162	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	668.42	11/2019 11/2019	11/2019
163	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	219.96	11/2019 11/2019	11/2019
164	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	249.63	11/2019 11/2019	11/2019
165	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	299.26	05/2019 05/2019	05/2019
166	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	1,888.28	03/2019 05/2020	05/2020
167	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,597.60	04/2019 03/2019	03/2019
	<u>Oil India Limited</u>						
168	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	26.81	10/2020 -	10/2020
169	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	44.43	12/2019 -	12/2019
170	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	2.08	02/2020 -	02/2020
	Total		1,76,796.45 -	1,78,392.48	49,927.15		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
171	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	10,375.32	09/2017 06/2019	06/2019
172	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,775.64	03/2013 12/2020	12/2020
173	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	8,441.41	08/2018 06/2019	06/2019
174	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	384.28	09/2019 02/2022	02/2022
175	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,388.93	11/2019 -	11/2019
176	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	3,272.35	07/2020 10/2020	10/2020
177	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	6,693.90	09/2019 -	09/2019
178	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10,831.46	06/2017 06/2019	06/2019
179	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	9,026.43	11/2016 03/2019	03/2019
180	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	15,441.10	01/2011 04/2021	04/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
181	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	7,916.41	02/2019 10/2020	10/2020
182	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	5,433.65	03/2019 09/2019	09/2019
	<u>North East Electric Power Corporation</u>						
183	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,900.51	12/2009 03/2019	03/2019
	<u>Power Grid Corporation Of India Limited</u>						
184	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,727.30	08/2013 03/2022	03/2022
185	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) [N18000181]	1/2015	871.62 -	871.62	462.92	10/2017 09/2019	09/2019
186	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	260.03	187.46	07/2017 06/2019	06/2019
187	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	2,129.90	05/2019 05/2019	05/2019
188	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS [N18000222]	4/2016	790.13 -	790.30	527.54	06/2019 06/2019	06/2019
189	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	257.53	03/2019 03/2019	03/2019
190	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	152.51	06/2019 06/2019	06/2019
191	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	382.10	04/2019 04/2019	04/2019
192	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	.70	05/2020 05/2020	05/2020
193	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) [N18000267]	9/2017	198.49 -	198.49	22.80	09/2019 02/2020	02/2020
194	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	789.25	07/2020 -	07/2020
195	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI [N18000257]	12/2015	3,654.00 -	3,654.00	2,973.90	04/2019 -	04/2019
196	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	31.80	06/2019 06/2019	06/2019
197	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	1,289.31	04/2020 04/2020	04/2020
198	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII [N18000245]	3/2017	379.95 -	379.95	22.22	12/2019 12/2019	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
199	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244	2/2017	235.53 -	235.53	64.79	06/2019 06/2019	06/2019
200	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243	3/2017	162.31 -	162.31	92.40	03/2019 03/2019	03/2019
201	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241	2/2017	195.05 -	195.05	103.60	02/2020 02/2020	02/2020
202	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238	3/2017	283.72 -	283.72	139.25	11/2019 11/2019	11/2019
203	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	8/2017	1,931.39 -	1,931.39	672.49	02/2020 02/2020	02/2020
204	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262	5/2017	186.17 -	186.17	64.27	07/2019 07/2019	07/2019
205	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233	9/2016	562.25 -	562.25	140.30	03/2019 03/2019	03/2019
206	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223	4/2016	844.64 -	844.64	326.60	04/2019 -	04/2019
207	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	5,633.65	11/2019 11/2019	11/2019
208	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214	4/2016	454.11 -	454.11	255.32	04/2018 01/2020	01/2020
	<u>Satluj Jal Vidyut Nigam Limited</u>						
209	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	648.33	162.41	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
210	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	2,104.21	66.87	09/2020 -	09/2020
	Total		1,61,539.46 -	1,80,587.67	1,19,560.58		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
211	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,011.99	03/2023 -	03/2023
212	KALYAN-KASARA 3RD LINE - [N22000233	4/2011	792.89 -	792.89	277.94	03/2021 -	03/2021
213	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	298.70	245.23	03/2019 -	03/2019
214	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362	2/2016	637.95 -	637.95	30.87	03/2023 -	03/2023
215	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	22.72	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
216	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	3,627.47	357.71	03/2024 -	03/2024
217	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	95.95	03/2023 -	03/2023
218	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	1,272.19 -	1,272.19	172.35	03/2022 -	03/2022
219	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
220	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
221	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	8,857.98	.16	03/2024 -	03/2024
222	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	1,908.80	03/2021 -	03/2021
223	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	540.02 -	540.02	175.86	03/2022 -	03/2022
	<u>Container Corporation Of India</u>						
224	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	253.94	03/2019 -	03/2019
225	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	273.41	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
226	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
227	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020
228	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
229	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	571.51	03/2020 -	03/2020
230	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	183.68	03/2022 -	03/2022
231	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
232	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	81.06	03/2022 -	03/2022
233	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	189.40	03/2022 -	03/2022
234	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
	<u>Eastern Railways</u>						
235	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	542.18	331.05	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
236	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	915.96	319.61	03/2022 -	03/2022
	<u>North Central Railway</u>						
237	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
238	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	-	03/2021 -	03/2021
239	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	-	03/2023 -	03/2023
240	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
	<u>North East Frontier Railway</u>						
241	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	4,968.00	2,541.80	03/2014 12/2020	12/2020
242	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
243	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	4/2006	2,326.52 -	3,000.00	696.02	03/2015 10/2021	10/2021
244	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
245	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	65.88	03/2020 -	03/2020
246	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	551.00	615.94	03/2019 -	03/2019
247	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	257.41	03/2021 -	03/2021
248	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	339.81	03/2019 -	03/2019
249	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.37	03/2020 -	03/2020
250	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	260.10	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
251	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	100.47	12/2021 -	12/2021
252	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>North Western Railway</u>						
253	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) [N22000113]	4/2008	653.19 -	1,116.00	840.30	03/2014 05/2019	05/2019
254	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	225.69	11/2019 -	11/2019
	<u>Northern Railway</u>						
255	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National High Speed Rail Corporation Limited</u>						
256	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	1,425.36	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
257	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
258	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	358.51	12/2026 -	12/2026
259	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	903.15	12/2020 -	12/2020
260	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	958.09	887.59	03/2020 -	03/2020
261	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,103.00	1,009.91	03/2020 -	03/2020
262	VIZIANAGARAM -SAMBALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	355.05	12/2024 -	12/2024
263	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,750.00	1,648.33	03/2020 -	03/2020
264	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	250.05	12/2024 -	12/2024
265	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	378.12	12/2023 -	12/2023
266	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	892.89	12/2021 -	12/2021
267	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	140.65	03/2021 -	03/2021
268	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	691.40	12/2021 -	12/2021
269	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,255.49	03/2023 -	03/2023
	<u>South Central Railway</u>						
270	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	119.69	03/2020 03/2020	03/2020
271	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]	4/2008	2,132.77 -	2,132.77	217.64	03/2014 03/2023	03/2023
272	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	401.52	03/2021 -	03/2021
273	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	<u>South East Central Railway</u>						
274	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
275	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
276	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
277	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
278	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
279	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
280	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	1,471.93 -	543.00	-	03/2022 -	03/2022
281	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
282	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	4/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019
	<u>South Eastern Railway</u>						
283	MM FROM BURAMARA-CHAKULIA - [N22000305]	4/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024
284	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.77	- 03/2025	03/2025
285	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.58	12/2021 12/2021	12/2021
286	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	4/1998	1,027.40 -	2,373.00	484.92	03/2003 03/2030	03/2030
287	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	184.10	12/2021 12/2024	12/2024
288	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	4/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024
289	MM FROM PANSKURA-GHATAL NL - [N22000309]	4/2011	276.69 -	426.00	-	- 03/2030	03/2030
	<u>South Western Railway</u>						
290	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	4/2011	1,801.01 -	1,801.01	14.24	- 12/2023	12/2023
291	SHIMOGA-HARIHAR NL - [N22000278]	4/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024
292	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,870.41	787.72	03/2019 03/2021	03/2021
293	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	465.12	03/2020 03/2020	03/2020
294	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	655.86	03/2020 03/2020	03/2020
295	MIRAJ-LONDA - [N22000327]	3/2015	1,830.00 -	1,190.92	207.68	- 03/2021	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
296	BANGLORE - SATYAMANGALAM (NL)(SWR) - [N20100274	4/1996	1,382.78 -	1,382.78	7.35	03/2002 03/2024	03/2024
297	HUBLI-ANKOLA(NL),SWR - [N20100193	4/1997	2,315.00 -	2,135.00	144.75	- 12/2024	12/2024
298	MARIKUPPAM - KUPPAM - [N22000308	4/2012	279.54 -	279.54	25.88	03/2016 12/2023	12/2023
299	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	4/2013	327.25 -	367.77	.31	- 12/2023	12/2023
300	GADAG-WADI NL - [N22000299	4/2013	2,841.84 -	2,841.84	39.98	12/2018 12/2024	12/2024
301	TORANAGALLU-RANJITPURA DL - [N22000298	4/2011	146.75 -	167.50	.34	- 12/2023	12/2023
302	WHITE FIELD-KOLAR NL - [N22000280	4/2011	348.85 -	348.85	.36	- 12/2023	12/2023
303	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	4/2013	296.00 -	466.65	-	- 12/2023	12/2023
304	BAGALKOT-KUDACHI NL - [N22000258	4/2010	986.30 -	986.30	288.01	03/2016 12/2023	12/2023
305	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	4/2013	558.00 -	692.43	-	- 12/2023	12/2023
	<u>Southern Railway</u>						
306	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI [N22000079	9/2007	724.69 -	2,072.50	1,169.07	02/2019 -	02/2019
307	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	4/2011	120.70 -	1,800.00	112.10	03/2019 -	03/2019
308	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
309	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
310	ATTIPPATTU PUTTUR - [N22000184	4/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019
	<u>West Central Railway</u>						
311	RAMGANJMUHDI-BHOPAL (NL),WCR - [N20100314	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
312	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
313	KATNI-BINA 3RD LINE (263 KM) - [N22000415	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
	<u>Western Railway</u>						
314	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	4/2008	3,503.69 -	1,030.29	1,097.39	03/2022 -	03/2022
315	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	385.60	528.96	03/2020 -	03/2020
316	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	2/1991	551.51 -	551.51	257.05	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
317	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494	4/2017	691.84 -	691.84	43.44	03/2020 -	03/2020
318	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493	4/2016	700.00 -	700.00	1,055.19	06/2020 -	06/2020
319	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	4/2007	1,640.04 -	1,640.04	608.62	03/2022 -	03/2022
320	CHOTTAUDEPUR-DHAR(NL) - [N22000138	4/2007	1,347.26 -	1,347.26	611.28	03/2022 -	03/2022
	Total		2,73,140.30 -	3,43,009.46	58,944.35		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
321	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
322	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	92.42	02/2020 -	02/2020
323	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	29.43	11/2019 -	11/2019
324	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
325	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	95.30	11/2019 -	11/2019
326	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019
327	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	66.19	06/2019 -	06/2019
328	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	284.00	94.50	11/2019 -	11/2019
329	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	48.23	11/2019 -	11/2019
330	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	43.14	12/2019 -	12/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
331	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
332	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
	<u>National Highways Authority Of India</u>						
333	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
334	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	2,015.00	01/2019 -	01/2019
335	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480	12/2015	1,041.10 -	1,041.10	175.85	04/2019 -	04/2019
336	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449	7/2015	2,128.72 -	2,128.72	963.21	04/2019 -	04/2019
337	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439	7/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019
338	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540	1/2016	701.12 -	701.12	842.34	05/2019 -	05/2019
339	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	409.11	04/2019 -	04/2019
340	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
341	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
342	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
343	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	21.72	03/2020 -	03/2020
344	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
345	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	950.69	549.74	08/2019 -	08/2019
346	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
347	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603	8/2016	1,167.42 -	1,167.42	207.31	03/2019 -	03/2019
348	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	401.95	04/2020 -	04/2020
349	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
350	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
351	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	1,066.41	03/2020 -	03/2020
352	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
353	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
354	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
355	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	670.70	09/2019 -	09/2019
356	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	608.89	07/2019 -	07/2019
357	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	460.55	07/2019 -	07/2019
358	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	462.25	04/2019 -	04/2019
359	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	3/2016	1,587.49 -	1,587.49	201.46	04/2019 -	04/2019
360	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	2/2016	997.15 -	997.15	376.26	03/2019 -	03/2019
361	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	230.61	02/2019 -	02/2019
362	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]	1/2016	1,081.57 -	1,081.57	827.52	06/2019 -	06/2019
	Total		39,492.95 -	40,065.60	12,737.06		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
363	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	121.22	05/2021 -	05/2021
364	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	249.81	05/2020 -	05/2020
	<u>Kamarajar Port Limited</u>						
365	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]	3/2016	600.00 258.00	257.90	1.45	12/2017 05/2020	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		3,369.00 -	3,026.90	372.48		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
366	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	14,659.90	05/2015 06/2019	06/2019
367	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	31.88	06/2020 -	06/2020
	Total		16,343.00 -	16,343.00	14,691.78		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
368	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	214.10	33.46	05/2018 02/2019	02/2019
369	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	231.80	117.63	10/2018 02/2019	02/2019
	Total		447.10 -	445.90	151.09		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
370	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33 -	197.33	14.99	04/2019 06/2020	06/2020
371	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	209.00	51.00	10/2019 -	10/2019
372	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	20.59	05/2020 -	05/2020
373	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]	1/2018	206.58 -	206.58	.02	03/2019 -	03/2019
374	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	4.44	11/2019 -	11/2019
375	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
376	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
377	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	101.04	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
378	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	13.03	03/2020 -	03/2020
379	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]	12/2016	246.31 -	246.31	34.90	02/2020 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>						
380	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
381	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	37,044.70	03/2016 05/2019	05/2019
382	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	2,024.91	11/2021 -	11/2021
	<u>Nagpur Metro Rail Corporation Ltd</u>						
383	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	4,898.72	03/2018 12/2019	12/2019
	<u>National Building Construcion Corporation Ltd</u>						
384	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,746.53	11/2019 -	11/2019
	Total		71,966.53 -	72,141.76	50,494.22		
	Grand Total		8,30,780.30	9,21,151.26	3,24,244.15		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,100.00	09/2010 -	10/2021	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
3	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	<u>Singareni Colliers Company Limited</u>						
5	RAMAGUNDAM OC-II EXTENSION - [N06000078	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
7	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						
9	JAGANNATHPORA OCP(3.00MTY) - [N06000075	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	Total		18,876.68 -	19,914.04			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
11	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45
12	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
13	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
14	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
15	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,751.00	12/2012 -	06/2019	97.29
	<u>Hindustan Petroleum Corporation Limited</u>						
16	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
17	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
19	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	<u>Oil & Natural Gas Corporation Limited</u>						
20	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
	<u>Oil India Limited</u>						
21	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	06/2019	24.47

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
22	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		10,212.66 -	14,463.53			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
23	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69
24	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
25	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
26	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
27	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
28	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
29	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
30	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
31	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
32	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
33	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
34	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
35	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>						
36	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						
37	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	-	39.30
38	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	-	26.86

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
39	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28
40	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15
	<u>Satluj Jal Vidyut Nigam Limited</u>						
41	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	03/2019	37.96
	<u>Thdc India Limited</u>						
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77
43	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65
	Total		1,32,013.26 -	1,75,289.01			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
44	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	298.70	03/2019 -	03/2019	62.28
45	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2021	63.44
46	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999 -	-	389.99
47	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
48	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
	<u>Container Corporation Of India</u>						
49	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
50	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,020.94	-	03/2021	192.42
51	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	-	03/2023	290.95
52	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	163.78
53	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
54	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	-	03/2022	261.73
55	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
56	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	-	-	323.32
57	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	-	-	338.91
58	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	-	252.66
59	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,474.47	-	03/2021	296.21
60	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020	03/2020	43.41
61	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	-	-	72.37
62	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014	-	68.57
63	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021	03/2022	63.37
64	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021	03/2022	62.06
65	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016	03/2021	468.48
66	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	528.26	-	-	192.15
67	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	566.41	-	12/2021	71.96
<u>East Coast Railway</u>							
68	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021	03/2023	137.80
69	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009	06/2021	29.96
70	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019	03/2021	38.43
71	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020	03/2020	.07
72	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020	03/2020	52.77
73	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	-	-	542.46
74	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	-	-	32.26
75	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	-	-	818.15
76	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	-	03/2021	124.59

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
77	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	-	03/2022	590.61
78	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
79	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2022	36.26
80	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	607.91	02/2013 -	-	.14
81	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.59	02/2012 -	09/2016	105.61
82	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	-	44.46
83	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	299.03	- -	-	.52
84	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]	04/2003	337.96 -	355.44	- -	-	5.17
85	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	665.75	02/2012 -	12/2013	33.16
86	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	04/2009	257.42 -	258.73	03/2014 -	-	.51
87	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
88	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
89	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	1,125.89 -	2,021.29	03/2016 -	03/2020	79.53
90	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	193.08 -	612.45	12/2011 -	09/2012	217.20
91	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	544.72	03/2006 -	01/2006	33.84
92	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	-	51.19
93	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
94	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]	04/2010	174.56 -	175.99	- -	-	.82
	<u>Metropolitan Rapid Transport Projects</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
95	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
96	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
97	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
98	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [N220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
99	ETAWAH-MAINPURI (NL),NCR - [N220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
100	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [N220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
101	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
	<u>North East Frontier Railway</u>						
102	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [N220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
103	KATIHAR - JOGBANI (GC)(NEFR) - [N220100247	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57
104	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56
105	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266	04/2000	1,180.19 -	3,040.00	12/2008 -	03/2019	157.59
106	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
107	NEW B.G. LINE FROM TETELIA TO BYRNIAHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
108	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
109	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
110	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	- -	03/2020	7.86
111	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
112	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	- -	03/2020	71.62
113	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,733.20	03/2007 -	04/2016	93.65
114	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
115	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
116	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
117	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
118	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
119	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
120	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	551.00	03/2019 -	03/2019	75.48
121	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
	<u>North Eastern Railway</u>						
122	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	413.56	06/2018 -	10/2018	89.54
123	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
124	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08	12/2022 -	05/2019	234.77
125	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
126	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
127	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	- -	-	.33
128	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
129	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	435.00	- -	03/2018	122.35
130	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	01/2019	35.17
131	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
132	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
133	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
134	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16
135	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	03/2019	70.07
136	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>North Western Railway</u>						
137	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00 -	03/2014 -	05/2019	70.85
138	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01 -	02/2019 -	12/2019	93.87
139	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99 -	03/2020 -	04/2022	14.33
140	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04 -	- -	-	26.25
141	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00 -	03/2015 -	10/2020	46.55
142	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55 -	12/2019 -	11/2019	41.64
143	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,878.97 -	- -	-	38.23
144	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90 -	10/2018 -	06/2019	24.47
145	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54 -	- -	-	33.76
146	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22 -	- -	-	33.81
147	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR - [N22000152]	04/2013	420.18 -	420.18 -	03/2020 -	12/2019	.00
148	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02 -	11/2019 -	11/2019	14.35
149	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00 -	02/2019 -	05/2019	44.16
	<u>Northern Railway</u>						
150	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00 -	03/2012 -	-	210.19
151	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17 -	- -	-	25.87
152	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00 -	12/2011 -	-	117.77
153	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63 -	- -	-	57.68
154	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00 -	- -	-	369.31
155	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00 -	07/2012 -	-	366.67
156	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00 -	11/2002 -	03/2021	1,017.96
157	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10 -	06/2007 -	-	114.33

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
158	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56
159	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
160	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
161	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
162	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	1,202.70	02/2015 -	12/2021	.00
163	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	02/2019	85.99
164	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,993.00	03/2008 -	03/2020	171.97
165	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
166	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
167	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
168	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70
169	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
170	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
171	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
172	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
173	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
174	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,077.00	03/2019 -	03/2020	16.18
175	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,750.00	03/2020 -	03/2020	145.28
176	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,103.00	03/2020 -	03/2020	16.35
177	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						
178	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>South Central Railway</u>						
179	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
180	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
181	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
182	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
183	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
184	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
185	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	645.00	03/2000 -	03/2019	64,400.00
186	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
	<u>South East Central Railway</u>						
187	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
188	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.00	04/2020 -	04/2020	243.06
189	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
190	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,420.39	02/2019 -	02/2019	142.42
191	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	403.00	12/2021 -	12/2021	75.98
192	CHHINDWARA-MANDLA FORT GC - [N22000481]	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22
193	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,279.00	12/2019 -	12/2019	46.67
194	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,919.00	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
195	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	1,000.00	- -	12/2024	114.37
196	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	- -	03/2030	53.96
197	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
198	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
199	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	09/2019	153.41
200	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
201	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99
202	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
203	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
204	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	525.81	12/2015 -	02/2019	69.92
205	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	01/2020	41.36
206	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88	- -	-	278.13
207	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76
208	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
209	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
210	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
211	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
	<u>Southern Railway</u>						
212	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
213	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
214	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
215	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2019	185.98
216	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
217	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
218	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
219	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	-	-	79.80
220	ATTIPPATTU PUTTUR - [N22000184	04/2008	151.84 -	1,105.00	02/2019 -	02/2019	627.74
221	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	2,350.00	- -	-	348.88
222	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
223	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
224	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188	04/1998	271.24 -	520.00	- -	-	91.71
225	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	457.08	- -	-	69.20
226	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	- -	-	295.05
227	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	03/2020	173.71
228	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	369.83	- -	-	92.90
229	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	1,800.00	03/2019 -	03/2019	1,391.30
230	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
231	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	302.02	03/2005 -	-	12.33
232	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
233	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450	02/2003	199.55 -	330.32	03/2009 -	-	65.53
234	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
<u>West Central Railway</u>							
235	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,713.09	03/2021 -	03/2021	538.98
236	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
237	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,260.61	03/2022 -	03/2022	116.55
<u>Western Railway</u>							
238	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
239	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
240	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,39,852.10 -	3,04,887.41			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
241	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
	<u>Ministry Of Road Transport And Highways</u>						
242	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
243	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	11/2019 -	11/2019	.17
244	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06
245	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
246	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
247	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
248	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2019	92.75
249	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
250	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	02/2019	4.99
251	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
252	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
253	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	04/2019	65.82
254	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2019	10.58

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
255	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
256	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56
257	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
258	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
259	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83
260	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
261	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
262	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
263	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
264	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
265	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
266	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
267	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
268	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
269	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
270	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
271	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
272	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
273	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
274	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48/O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
	<u>Public Works Dept Of State</u>						
275	REHABILITATION AND UPGRADE OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
276	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
277	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	.12
278	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	.01
279	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		27,118.65 -	41,914.00			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
280	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	271.56	12/2017 -	-	5.26
	Total		244.50 -	271.56			
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
281	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2020	42.39
	Total		343.00 -	488.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
282	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(January 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
283	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	486.54	05/2017 -	03/2019	25.40
284	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	04/2014	332.72 -	342.00	09/2016 -	-	2.79
285	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
286	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.60
	<u>Chennai Metro Rail Ltd</u>						
287	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
288	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
289	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>National Building Construcion Corporation Ltd</u>						
290	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		22,218.72 -	27,706.04			
	Grand Total		3,70,814.43	6,21,160.16			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above						(January 2019)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00	6,100.00	5,738.32	09/2010	10/2021	133	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00	16,580.00	12,987.00	12/2015	06/2020	54	43
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00	12,320.00	10,285.00	12/2016	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00	39,849.00	12,070.00	11/2020	11/2023	36	-
	Total		67,120.00	74,849.00	41,080.32				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61	441.33	85.79	09/2018	06/2020	21	-
	Total		314.61	441.33	85.79				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27	1,230.27	334.71	04/2015	04/2019	48	-
	<u>Central Coal Fields Limited</u>								
7	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87	179.87	175.17	03/2012	03/2019	84	-
8	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68	264.68	178.37	03/2012	03/2019	84	-
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85	510.85	340.33	03/2016	03/2019	36	-
10	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	89.21	03/2014	03/2019	60	-
11	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51	163.51	103.83	03/2011	03/2020	108	-
12	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40	706.40	185.62	07/2012	03/2021	104	-
	<u>Eastern Coal Fields Limited</u>								
13	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05	1,055.05	393.45	03/2018	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
14	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10	490.10	421.62	03/2017	03/2020	36	-

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	584.87	03/2013 -	03/2020	84	-
16	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	267.99	03/2010 -	03/2020	120	-
17	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	397.41	03/2013 -	03/2020	84	-
18	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	30.04	03/2018 -	03/2020	24	-
19	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	235.51	03/2012 -	03/2021	108	-
20	JAGANNATH RE-ORGANISATION OC. (6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	65.58	03/2019 -	03/2021	24	-
21	BASUNDHARA (WEST) OC EXTN (7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	123.19	03/2019 -	03/2024	60	-
	<u>Neyveli Lignite Corporation</u>								
22	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	5,892.64	12/2015 12/2018	03/2019	39	3
	<u>Northern Coal Fields Limited</u>								
23	KHADIA EXPANSION OPENCAST PROJECT (4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	715.00	03/2018 -	03/2019	12	-
	<u>Singareni Colliers Company Limited</u>								
24	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	154.21	03/2015 -	03/2019	48	-
25	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	204.26	06/2015 -	03/2019	45	-
26	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	160.45	03/2016 -	03/2019	36	-
27	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
28	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	384.32	146.45	07/2016 -	03/2020	44	-
29	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	12.69	03/2015 -	03/2021	72	-
30	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2021	72	-
31	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	437.51	353.61	03/2015 -	03/2021	72	-
32	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	-
33	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	186.91	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
34	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.50	03/2016 -	03/2019	36	-
35	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	168.00	03/2016 -	03/2019	36	-
36	JAGANNATHPOR OCP (3.00 MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	459.49	184.45	03/2015 -	03/2020	60	-
37	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
38	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	206.84	03/2014 -	03/2020	72	-
	<u>Western Coal Fields Limited</u>								
39	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 409.68	409.68	97.41	03/2023 02/2017	03/2023	0	73
40	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 313.34	313.34	26.44	03/2021 09/2018	03/2024	36	66
	Total		19,168.66 -	20,054.26	13,089.97				
	<u>FERTILISERS</u>								
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
41	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA	02/2016	482.85 482.85	482.85	430.86	12/2017 01/2019	02/2019	14	1
	Total		482.85 -	482.85	430.86				
	<u>STEEL</u>								
	<u>Raastriya Ispat Nigam Limited</u>								
42	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	972.10	09/2018 -	06/2019	9	-
43	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	150.36	08/2018 -	06/2019	10	-
44	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	316.25	07/2018 -	06/2019	11	-
45	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,133.76	12/2017 -	09/2019	21	-
46	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	247.65	10/2016 -	03/2020	41	-
	<u>Steel Authority Of India Limited (SAIL)</u>								
47	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,638.63	04/2018 -	05/2019	13	-
48	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	878.27	12/2017 -	06/2019	18	-
49	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	384.47	10/2017 -	06/2020	32	-
50	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	78.83	06/2019 -	06/2020	12	-
	Total		11,248.72 -	11,036.12	6,800.32				
	<u>PETROLEUM</u>								
	<u>Gas Authority Of India Limited</u>								
51	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	03/2015	3,957.00 3,561.00	3,397.00	2,382.96	12/2018 -	03/2019	3	-
52	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH	07/2015	1,427.94 -	800.00	618.58	12/2018 -	03/2019	3	-

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
53	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	134.00	04/2018 -	03/2019	11	-
54	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 3,030.00	5,751.00	2,038.08	12/2012 02/2019	06/2019	78	4
	<u>Indian Oil Corporation Limited</u>								
55	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	352.66	10/2017 -	03/2019	17	-
56	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 4,190.00	4,190.00	3,224.62	09/2017 06/2018	03/2019	18	9
57	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	868.92	11/2018 -	03/2019	4	-
58	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	11.66	06/2020 -	10/2020	4	-
59	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	4,497.00	370.09	12/2018 -	12/2020	24	-
60	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	14.11	01/2021 -	04/2021	3	-
61	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	1.53	04/2021 -	07/2021	3	-
62	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	1.18	10/2020 -	08/2021	10	-
63	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	9.20	01/2021 -	10/2021	9	-
64	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	13.93	08/2021 -	11/2021	3	-
	<u>Oil & Natural Gas Corporation Limited</u>								
65	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 567.22	567.22	457.84	11/2019 12/2018	02/2019	-9	2
66	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	174.22	03/2019 -	04/2019	1	-
	<u>Oil India Limited</u>								
67	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	199.43	03/2017 -	06/2019	27	-
68	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
	Total		22,441.97 -	24,165.72	10,875.07				

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
69	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,006.39	04/2020 -	10/2023	42	-
	<u>National Hydro-Electric Power Corporation</u>								
70	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,394.80	7,164.11	09/2009 -	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
71	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	7,220.84	09/2011 06/2018	01/2019	88	7
72	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	7,511.72	05/2014 -	05/2019	60	-
73	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,798.00	12/2016 -	08/2019	32	-
74	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	12,593.00	01/2018 -	05/2020	28	-
	<u>Power Grid Corporation Of India Limited</u>								
75	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 534.02	534.02	441.88	08/2014 09/2018	02/2019	54	5
76	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	145.82	03/2016 09/2018	02/2019	35	5
77	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	244.80	03/2018 09/2018	02/2019	11	5
78	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 3,705.61	3,705.61	2,572.10	04/2018 09/2018	02/2019	10	5
79	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 307.18	307.18	211.31	11/2017 10/2018	02/2019	15	4
80	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 305.04	305.04	237.11	03/2017 09/2018	02/2019	23	5
81	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE	05/2016	766.21 766.21	766.21	456.84	11/2018 11/2018	02/2019	3	3
82	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT	07/2016	300.94 300.94	300.94	226.76	12/2018 12/2018	02/2019	2	2
83	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,106.62	11/2008 09/2018	03/2019	124	6
84	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	187.24	04/2016 12/2017	03/2019	35	15
85	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	151.02	02/2016 09/2018	03/2019	37	6
86	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 197.40	197.40	74.71	03/2018 -	03/2019	12	-

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 1,429.38	1,429.38	880.26	01/2019 01/2019	03/2019	2	2
88	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE	08/2016	431.89 431.89	431.89	231.96	02/2019 02/2019	03/2019	1	1
89	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 322.30	322.30	127.38	02/2019 02/2019	03/2019	1	1
90	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	687.26	09/2010 12/2018	04/2019	103	4
91	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,547.47	10/2012 12/2018	06/2019	80	6
92	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	512.80	06/2014 12/2018	06/2019	60	6
93	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,221.08	04/2016 12/2018	06/2019	38	6
94	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 539.82	539.82	424.53	06/2016 09/2018	06/2019	36	9
95	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 408.46	408.46	204.44	01/2019 01/2019	06/2019	5	5
96	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 445.89	445.89	243.46	02/2019 02/2019	06/2019	4	4
97	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 5,151.37	5,151.37	2,937.30	03/2018 03/2019	08/2019	17	5
98	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 1,394.52	1,394.52	293.99	05/2017 06/2019	09/2019	28	3
99	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 808.63	808.63	416.66	01/2018 03/2019	09/2019	20	6
100	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 175.64	175.64	80.24	09/2018 09/2018	09/2019	12	12
101	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 193.14	193.14	4.80	06/2019 06/2019	09/2019	3	3
102	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 55,018.00	550.18	446.23	11/2016 06/2019	12/2019	37	6
103	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 4,754.42	9,141.97	993.85	12/2018 12/2018	12/2019	12	12

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
104	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE <u>Satluj Jal Vidyut Nigam Limited</u>	12/2014	5,111.33 5,111.33	6,652.57	1,035.32	12/2018 12/2018	12/2019	12	12
105	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	540.02	12/2016 -	03/2019	27	-
106	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT <u>Thdc India Limited</u>	11/2016	330.00 -	330.00	311.17	11/2017 -	03/2019	16	-
107	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	232.92	02/2014 02/2018	10/2019	68	20
108	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,731.61	02/2016 12/2020	05/2021	63	5
109	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND <u>Total</u>	08/2008	2,491.58 -	4,105.30	1,593.51	06/2013 -	12/2021	102	-
			87,083.71 -	1,12,309.29	72,048.53				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
110	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	282.43	05/2017 06/2018	03/2019	22	9
111	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	244.00	247.47	09/2018 -	03/2019	6	-
112	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	95.16	02/2018 02/2018	06/2019	16	16
113	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI <u>Total</u>	12/2013	204.44 -	204.44	176.22	05/2017 06/2018	07/2019	26	13
			895.04 -	895.04	801.28				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
114	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA <u>Container Corporation Of India</u>	02/2016	1,035.16 1,035.16	1,035.16	27.86	03/2022 -	03/2023	12	-
115	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	140.94	03/2019 -	08/2019	5	-
116	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	415.31	03/2018 -	12/2019	21	-
117	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	291.62	03/2019 -	12/2019	9	-
118	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH <u>East Central Railways</u>	08/2016	234.50 -	235.00	4.98	03/2019 -	12/2020	21	-
119	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	28.46	03/2019 -	12/2019	9	-
120	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96	-

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
121	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96	-
122	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 -	678.54	-	03/2019 -	03/2020	12	-
123	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	315.40	03/2020 -	03/2021	12	-
124	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61	-
125	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	-	03/2020 -	10/2021	19	-
126	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	-	03/2020 -	10/2021	19	-
127	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12	-
128	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	-	03/2021 -	03/2022	12	-
	<u>East Coast Railway</u>								
129	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	765.60	02/2019 -	03/2021	25	-
130	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	81.26	10/2020 -	03/2021	5	-
131	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28	-
132	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27	-
133	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147	-
134	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	574.98	06/2021 -	03/2023	21	-
	<u>Eastern Railways</u>								
135	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	2,021.29	2,021.29	03/2016 -	03/2020	48	-
136	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.52	137.93	03/2016 -	03/2020	48	-
137	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,620.01	844.78	03/2019 12/2009	03/2022	36	147
	<u>Metropolitan Rapid Transport Projects</u>								
138	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	445.91	06/2013 -	03/2019	69	-
139	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
140	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	1,348.23	03/2004 -	03/2020	192	-
	<u>North East Frontier Railway</u>								
141	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	3,040.00	3,109.99	12/2008 -	03/2019	123	-

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
142	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	614.00	270.28	03/2019 -	03/2020	12	-
143	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	13,809.00	8,350.11	03/2011 -	03/2020	108	-
144	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	1,532.00	575.61	03/2019 -	03/2020	12	-
145	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	2,145.00	930.20	03/2019 -	03/2020	12	-
146	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
147	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	569.63 -	650.00	-	03/2020 -	10/2022	31	-
	<u>North Eastern Railway</u>								
148	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	270.00	267.76	08/2018 -	01/2019	5	-
149	MANDHANA - BRAHMAWART NEW LINE PROJECT - [N22000458]NER, UTTAR PRADESH	04/1997	609.04 1,063.00	1,807.88	1,808.14	04/1999 -	03/2019	239	-
150	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	192.85	01/2019 -	01/2020	12	-
151	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER, UTTAR PRADESH	04/2017	622.50 427.00	426.74	57.31	04/2017 -	01/2020	33	-
152	INDARA - DOHRIGHAT GAUGE CONVERSION - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	213.35	.59	04/2016 -	02/2020	46	-
153	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	1.58	03/2014 -	04/2021	85	-
154	ETAH - KASGANJ - NEW LINE - [N22000462]NER, UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
155	NANPARA - NEPALGANJ GAUGE CONVERSION - [N22000459]NER, UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
156	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	349.00	303.99	02/2019 -	05/2019	3	-
157	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	294.90	167.81	10/2018 -	06/2019	8	-
158	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 780.98	795.01	467.29	02/2019 -	12/2019	10	-
159	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,216.00	741.81	03/2015 -	10/2020	67	-
160	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	685.99	3.58	03/2020 -	04/2022	25	-
161	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR, RAJASTHAN	08/2018	808.85 -	808.85	.08	08/2022 -	09/2022	1	-
	<u>Northern Railway</u>								
162	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	27,949.00	17,336.24	11/2002 -	03/2021	220	-
	<u>Rail Vikas Nigam Ltd.</u>								

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
163	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	385.00	377.10	03/2009 03/2009	02/2019	119	119
164	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	383.54 -	555.00	588.95	03/2010 -	12/2019	117	-
165	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	1,185.64 -	1,844.47	1,458.49	12/2017 -	03/2020	27	-
166	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	732.81 -	1,993.00	2,017.37	03/2008 -	03/2020	144	-
167	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	1,077.00	1,011.81	03/2019 -	03/2020	12	-
168	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	618.31	03/2016 03/2017	12/2020	57	45
169	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,120.00	910.97	03/2019 -	03/2021	24	-
170	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	923.92	12/2020 -	03/2021	3	-
171	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 245.00	1,202.70	706.84	02/2015 -	12/2021	82	-
172	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	631.78 632.00	1,195.00	675.36	12/2012 -	03/2022	111	-
173	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,005.66	03/2020 -	03/2022	24	-
174	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	943.60	158.12	03/2022 -	12/2024	33	-
175	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	375.62	03/2023 -	12/2024	21	-
176	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,966.91	03/2016 -	03/2025	108	-
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	794.78	03/2016 -	03/2025	108	-
178	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
179	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,235.71	12/2024 -	03/2026	15	-
<u>South Central Railway</u>									
180	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	645.00	734.72	03/2000 -	03/2019	228	-
181	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48 -	1,160.47	130.50	03/2010 -	03/2022	144	-
182	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	393.16	03/2021 -	03/2022	12	-
183	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	289.91	03/2009 -	03/2023	168	-

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
184	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	177.18	03/2022 -	03/2023	12	-
185	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	229.44	03/2023 -	03/2024	12	-
	<u>South East Central Railway</u>								
186	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96	-
	<u>South Eastern Railway</u>								
187	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	525.81	516.38	12/2015 12/2018	02/2019	38	2
188	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	161.29	12/2016 08/2018	09/2019	33	13
189	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	365.00	198.49	- 12/2018	01/2020	-	13
190	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,151.81	403.78	03/2020 03/2020	06/2020	3	3
191	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	1,724.20	198.68	03/2021 03/2021	12/2021	9	9
	<u>South Western Railway</u>								
192	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.52	889.52	433.71	03/2017 -	03/2020	36	-
193	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,140.93	1,140.93	714.14	03/2020 03/2020	03/2021	12	12
	<u>Southern Railway</u>								
194	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71	-
195	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	<u>West Central Railway</u>								
196	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	-	03/2020 -	10/2021	19	-
197	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	<u>Western Railway</u>								
198	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	83.53	03/2012 -	03/2019	84	-
199	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	858.96	550.16	03/2019 -	03/2022	36	-
	Total		1,05,322.70 -	1,75,705.14	69,223.06				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
200	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
201	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
202	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
203	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
204	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	<u>National Highways Authority Of India</u>								
205	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	839.86	01/2014 -	01/2019	60	-
206	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	604.80	10/2017 -	01/2019	15	-
207	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 174.34	174.34	214.88	03/2008 -	02/2019	131	-
208	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	167.98	202.58	05/2008 -	02/2019	129	-
209	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	02/2019	30	-
210	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	1,871.34	3,235.12	01/2018 -	02/2019	13	-
211	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	320.30	193.54	01/2019 -	02/2019	1	-
212	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	209.80	04/2009 -	03/2019	119	-
213	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	297.81	04/2008 -	03/2019	131	-
214	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9	-
215	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	03/2019	79	-
216	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,403.47	07/2015 -	03/2019	44	-
217	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	03/2019	54	-

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
218	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30	-
219	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	567.51	53.70	03/2018 -	03/2019	12	-
220	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	447.91	05/2018 -	03/2019	10	-
221	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	395.53	06/2016 -	03/2019	33	-
222	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	703.00	04/2018 -	03/2019	11	-
223	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	574.28	380.25	07/2018 -	03/2019	8	-
224	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31	-
225	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 09/2017	03/2019	89	18
226	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	934.46	330.04	03/2018 -	03/2019	12	-
227	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	1,042.73	03/2016 -	03/2019	36	-
228	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	470.59	05/2018 -	03/2019	10	-
229	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	78.39	01/2019 -	03/2019	2	-
230	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130	-
231	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	360.84	390.71	04/2010 -	04/2019	108	-
232	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,177.45	05/2013 -	04/2019	71	-
233	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	04/2019	29	-
234	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	45.11	05/2018 -	04/2019	11	-
235	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	331.17	05/2018 -	04/2019	11	-
236	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	950.40	08/2018 -	04/2019	8	-

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
237	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	163.99	12/2017 -	04/2019	16	-
238	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	18.26	11/2018 -	04/2019	5	-
239	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	289.10	07/2018 -	04/2019	9	-
240	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	305.99	06/2018 -	04/2019	10	-
241	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33	-
242	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	05/2019	56	-
243	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	461.13	07/2014 -	05/2019	58	-
244	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	926.73	11/2017 -	05/2019	18	-
245	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12	-
246	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	185.52	06/2018 -	05/2019	11	-
247	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,954.66	11/2011 -	06/2019	91	-
248	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,264.75	03/2013 -	06/2019	75	-
249	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	884.58	02/2013 -	06/2019	76	-
250	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,003.77	05/2014 -	06/2019	61	-
251	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	832.77	07/2013 -	06/2019	71	-
252	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,315.36	08/2013 -	06/2019	70	-
253	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	688.86	06/2014 -	06/2019	60	-
254	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64	-
255	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,411.79	09/2016 -	06/2019	33	-
256	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18	-

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
257	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	662.12	11/2016 -	06/2019	31	-
258	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	284.92	05/2018 -	06/2019	13	-
259	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	1,469.10	01/2019 -	06/2019	5	-
260	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	323.95	04/2018 -	06/2019	14	-
261	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	235.70	08/2018 -	06/2019	10	-
262	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	-
263	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-
264	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	544.89	11/2018 -	07/2019	8	-
265	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	23.70	03/2019 -	07/2019	4	-
266	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.95	03/2019 -	07/2019	4	-
267	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	175.56	05/2019 -	07/2019	2	-
268	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	37.20	08/2018 -	08/2019	12	-
269	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	212.53	05/2019 -	08/2019	3	-
270	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	576.75	06/2019 -	09/2019	3	-
271	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	-
272	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	186.83	08/2018 -	09/2019	13	-
273	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6	-
274	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,065.56	12/2018 -	10/2019	10	-

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
275	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	158.10	04/2019 -	10/2019	6	-
276	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	155.03	06/2019 -	11/2019	5	-
277	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,820.02	04/2019 -	11/2019	7	-
278	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	22.70	06/2017 -	11/2019	29	-
279	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,141.90	03/2014 -	12/2019	69	-
280	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	-
281	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	174.43	03/2019 -	12/2019	9	-
282	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	118.92	10/2017 -	01/2020	27	-
283	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	71.28	04/2018 -	04/2020	24	-
284	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	57.93	03/2020 -	04/2020	1	-
285	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	260.79	02/2020 -	05/2020	3	-
286	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	420.38	03/2020 -	05/2020	2	-
287	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2	-
288	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	43.99	03/2020 -	05/2020	2	-
289	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,829.14	08/2013 -	06/2020	82	-
290	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	121.00	03/2020 -	06/2020	3	-
291	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	460.33	03/2020 -	06/2020	3	-

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
292	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	94.03	09/2017 -	06/2020	33	-
293	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	-
294	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	-	03/2020 -	08/2020	5	-
295	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	503.06	03/2020 -	08/2020	5	-
296	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	469.50	03/2020 -	08/2020	5	-
297	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	549.02	06/2020 -	08/2020	2	-
298	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	11.30	03/2019 -	11/2020	20	-
299	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	-	03/2020 -	11/2020	8	-
300	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	197.98	03/2017 -	11/2020	44	-
301	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	-
302	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	119.87	06/2019 -	12/2020	18	-
<u>National Highways Development Project</u>									
303	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	704.26	5.21	05/2015 -	01/2020	56	-
	Total		90,619.80 -	93,602.74	67,918.87				
<u>SHIPPING AND PORTS</u>									
<u>Port Trust</u>									
304	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 600.00	600.00	550.78	03/2006 03/2016	02/2019	155	35
	Total		150.00 -	600.00	550.78				
<u>TELECOMMUNICATIONS</u>									
<u>Department Of Telecommunication</u>									
305	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				

Costing Rs. 150 Crore and above

(January 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>URBAN DEVELOPMENT</u>								
	<u>Bangalore Metro Rail Corporation Limited</u>								
306	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
307	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	163.97	11/2014 -	02/2019	51	-
308	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	148.80	08/2016 -	03/2019	31	-
309	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77	-
310	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	486.54	394.49	05/2017 02/2019	03/2019	22	1
311	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL	10/2014	162.88 -	162.88	101.71	04/2018 -	07/2019	15	-
312	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	146.37	04/2019 06/2019	09/2019	5	3
313	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
314	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2019	56	-
315	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	540.42	234.59	07/2019 -	11/2019	4	-
316	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	377.51	10/2019 -	03/2020	5	-
317	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	41.28	03/2016 -	04/2020	49	-
318	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	34.09	06/2017 -	06/2020	36	-
319	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	13.00	07/2020 09/2018	09/2020	2	24
	<u>Hindustan Steelwork Construction Limited</u>								
320	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
321	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								

Costing Rs. 150 Crore and above

(January 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
322	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	Total		60,107.32 -	60,724.31	2,917.72				
	Grand Total		4,78,289.38	5,99,529.80	2,94,219.57				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2019	430.45	36
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2019	365.01	45
9	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
10	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2019	209.78	48
11	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
12	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2020	321.5	72
13	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
14	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
15	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
16	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2021	337.66	24
17	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
18	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
19	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	NCL	06/2011	03/2018	03/2019	1131.28	12
20	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2019	510.85	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2020	457.77	84
22	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
23	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
24	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
25	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
26	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
27	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
28	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
29	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2019	198.59	36
30	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
31	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
32	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
35	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
36	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2020	479.53	84
37	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2020	172.08	120
38	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2019	258.56	36
39	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	03/2019	5907.11	39
40	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
41	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
42	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	RCF	02/2016	12/2017	02/2019	482.85	14
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	CNCI KOLKATA WEST BENGAL	HSCC	08/2016	09/2018	03/2019	244	6
45	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	09/2019	363.99	16
46	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	06/2019	152.95	16
47	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	10/2020	414.11	83
48	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	07/2019	204.44	26
49	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	03/2019	293.65	22

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
51	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
52	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
53	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	06/2019	352.56	27
54	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
55	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	03/2019	3076	18
56	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
57	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
58	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
59	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2019	861.79	70
60	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
61	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	52

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
62	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2020	4619.94	27
63	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2019	3190.69	13
64	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	06/2019	2915	78
65	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	12/2019	2465.15	81
66	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	15
67	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	06/2019	694	8
68	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	03/2019	327.78	11
69	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
70	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
71	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	12/2020	4497	24

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
72	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
73	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
74	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	11638.55	21
75	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
76	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	06/2019	1364.52	38
77	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	03/2019	374.63	35
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	06/2019	539.82	36
79	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	10/2023	8112.12	42
80	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	6
81	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	12532.44	10
82	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	14366.58	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
83	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
84	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	PGCIL	01/2015	03/2018	02/2019	268.8	11
85	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
86	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	06/2019	203.28	23
87	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	03/2019	197.4	12
88	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	12/2019	522.29	37
89	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	02/2019	155.57	35
90	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
91	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	01/2019	4375.35	88
92	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	08/2019	5151.37	17
93	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	03/2019	196.58	37
94	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	09/2019	1394.52	28
95	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	10/2019	195.42	68
96	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353	60
97	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	03/2019	436.68	27
98	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	PGCIL	04/2015	04/2018	02/2019	3705.61	10
99	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	02/2019	307.18	15
100	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2021	2491.58	102
101	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	06/2019	487.49	60
102	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	09/2019	175.64	12
103	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	12964.6	28
104	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	08/2019	9750.89	32

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
105	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
106	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	04/2019	477.69	103
107	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	06/2019	4824.12	80
108	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	02/2019	297.33	54
109	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	03/2019	1779.29	124
110	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	123
111	SOLAPUR STPP	NTPC	03/2012	11/2016	03/2019	9395.18	28
112	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	11846	24
113	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	02/2019	305.04	23
114	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	09/2019	808.63	20
115	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	01/2020	454.11	21
116	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2019	2496.9	111
117	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	05/2021	1657	63
118	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	11/2017	03/2019	330	16

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
119	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
120	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	96
121	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	61
122	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
123	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
124	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
125	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
126	BANKURA DAMODAR VALLEY RLY LINE	SER	04/1998	03/2003	03/2030	1027.4	324

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	96 KM GC WITH 6MMS FOR NL						
127	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
128	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
129	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	03/2026	16216	15
130	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
131	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
132	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
133	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	12/2019	493.17	21
134	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
135	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
136	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
137	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2022	1188.91	36
138	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
139	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
140	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	02/2019	133.41	119
141	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	21
142	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	81
143	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
144	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2022	1160.48	144
145	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	732.81	144
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
147	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	05/2019	653.19	62
148	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2020	277.28	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
149	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
150	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
151	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
152	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2022	2288.7	12
153	KADAPA-BANGALORE (NL), KADAPA- PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2023	2132.77	108
154	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
155	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
156	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2020	495.44	192
157	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	03/2016	03/2020	1125.89	48
158	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
159	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	04/1997	03/2012	03/2020	324.73	96
160	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	1180.19	123
161	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	147
162	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	108
163	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTP	04/2006	06/2013	03/2019	495.74	69
164	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
165	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
166	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
167	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	MRTP	04/2008	03/2014	03/2019	5300	60
168	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2019	1142	60
169	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
170	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	12/2019	410.08	10
171	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	03/2021	2500	220

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
172	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	631.78	111
173	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2019	383.54	117
174	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
175	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
176	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2019	1723	228
177	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
178	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
179	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
180	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2021	1111.99	25
181	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	09/2019	148.77	33
182	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	10/2020	829.74	67
183	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
184	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
185	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	06/2019	236.93	8
186	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651	108
187	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	02/2019	309.44	38
188	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	10/2022	569.63	31
189	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
190	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2021	1763.93	19
191	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
192	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
193	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
194	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	03/2020	678.54	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
195	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2023	1035.16	12
196	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
197	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
198	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	28
199	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2021	1172.92	27
200	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
201	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	36
202	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
203	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
204	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	10/2021	1491.47	19
205	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
206	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
207	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
208	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	03/2019	609.04	239
209	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	02/2020	213	46
210	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
211	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
212	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
213	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	04/2019	641.17	33
214	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	11/2020	476.56	40
215	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	11/2019	648.33	29
216	FOUR LANNING BALANCE WORK FOR	NHAI	10/2017	10/2017	01/2020	639.97	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.						
217	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
218	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	MORTH	02/2015	03/2015	06/2019	383.4	51
219	BHOPAL-BIORA (4L) OF NH-12 IN MP	NHDP	11/2011	05/2015	01/2020	704.26	56
220	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	08/2020	604	128
221	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
222	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2019	671.3	76
223	JORBAT - BARAPANI	NHAI	01/2011	01/2014	01/2019	536	60
224	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	06/2019	575	71
225	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	05/2019	702.16	58
226	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108	91
227	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	06/2019	1348.2	64
228	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2019	617	79
229	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	06/2019	1724.55	75
230	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	04/2019	1585	71
231	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	04/2019	1916.79	29
232	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.6	33
233	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
234	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2019	1535	61
235	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	03/2019	1410	54
236	MUZZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
237	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	06/2019	1078.84	70
238	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2020	998.79	82
239	6-LANING OF DHANKUNI-KHARAGPUR	NHAI	04/2012	09/2014	05/2019	1396.18	56

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SECTION						
240	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	02/2019	530.07	30
241	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	03/2019	822.9	11
242	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	06/2019	923.04	31
243	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	03/2019	1655.01	31
244	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	03/2019	1673.7	89
245	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	04/2019	1388	8
246	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	02/2019	1871.34	13
247	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2019	199.81	119
248	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	02/2019	160	129
249	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	07/2019	478.51	69
250	PANVEL-INDAPUR	NHAI	12/2011	06/2014	06/2019	942.69	60
251	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	03/2019	425.19	30
252	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	05/2019	1387.11	18
253	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2019	563.92	18
254	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	NHAI	09/2015	03/2018	03/2019	567.51	12
255	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	01/2019	597	15
256	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	03/2019	414.51	10
257	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	05/2019	531.13	12
258	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	04/2019	593.26	11
259	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	12/2019	649.5	9
260	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	03/2019	602.95	33
261	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	03/2019	574.28	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
262	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	04/2019	505	11
263	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	05/2019	1083	11
264	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
265	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	08/2019	323.72	12
266	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
267	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	NHAI	09/2016	08/2018	09/2019	767.03	13
268	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	09/2019	400.25	6
269	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
270	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
271	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
272	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
273	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	02/2019	245	131
274	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	04/2019	217.61	108
275	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2019	208	131
276	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2019	225	130
277	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	03/2019	946	9
278	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	03/2019	934.46	12
279	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	07/2019	1423.96	8
280	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	10/2019	2136.97	10
281	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	06/2019	596.67	13
282	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
283	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
284	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
285	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	06/2019	726.67	14
286	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	03/2019	479.2	10
287	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6
288	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
289	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	06/2019	707.82	10
290	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	04/2019	641.17	9
291	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	04/2019	804.97	10
292	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ	NHAI	05/2015	05/2017	06/2019	581.84	25

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
293	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29
294	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	02/2019	150	155

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
295	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	RINL	07/2015	07/2018	06/2019	465.85	11
296	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	06/2019	15525	49
297	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2020	343	41
298	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	05/2019	3127.3	13
299	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
300	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	06/2019	1154.18	18
301	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	06/2019	320.66	10
302	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12
303	FORGED WHEEL PLANT	RINL	04/2014	09/2018	06/2019	1682.85	9
304	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	09/2019	2858	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
305	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
306	MADHYA PRADESH ACCESS (LOT1)	BSNL	08/2017	05/2018	02/2019	215.3	9

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
307	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
308	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	36
309	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
310	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
311	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	04/2020	171.86	49
312	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	03/2019	156.57	31
313	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2020	197.33	14
314	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
315	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2019	216.69	56
316	NSG AT KOLKATA	CPWD	10/2014	04/2018	07/2019	162.88	15
317	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
318	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	03/2019	388	22
319	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	02/2019	270.83	51
320	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2019	165.23	77
321	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
322	DELHI MRTS PHASE-III	MMRC	09/2011	03/2016	05/2019	38585	38
323	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6100	2608
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
8	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5751	2836
13	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
14	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
16	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1577.15	715.36
19	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
21	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9394.8	5475.21
23	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
24	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
25	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
26	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	11638.55	12865.92	1227.37
27	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
28	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	15166.19	16934.65	1768.46
29	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
30	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
31	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
32	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	534.02	236.69
33	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
34	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4401.9	2744.9
35	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4105.3	1613.72
38	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
40	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
41	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	14366.58	15164.05	797.47
42	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	12532.44	13740.53	1208.09
43	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8150	3774.65
44	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
45	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6652.57	1541.24
46	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9141.97	4387.55
47	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
48	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	9870.51	11148.86	1278.35
49	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	2514.88	3190.27	675.39
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
51	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	11846	12739.82	893.82
52	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
53	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
54	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	297.32	614	316.68
55	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
56	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	920	764.45
57	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	ECR	03/1999	N.A.	1033.07	3020.94	1987.87
58	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	792.46	1320	527.54
59	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
60	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND	SR	09/2006	N.A.	343.17	1065	721.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	COIMBATORE						
61	MAYLADUTHURAI - THIRUVARUR - KARAISKUDI - THIRU 'PONDII' - AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
62	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
63	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
64	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
65	HATHUA-BHATNI (N L) (NER)	NER	04/2005	12/2022	230.03	770.08	540.05
66	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
67	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	06/2018	218.19	413.56	195.37
68	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	424.6	2713.09	2288.49
69	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	732.81	1993	1260.19
70	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	749	271.12
71	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.77	1538.12
72	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	4968	2574.53
73	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
74	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
75	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
76	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
77	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1156.41	831.68
79	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
80	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	03/2016	1125.89	2021.29	895.4
81	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
82	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	MM FROM PANSKURA-GHATAL NL	SER	04/2011	N.A.	276.69	426	149.31
84	MM FROM BURAMARA-CHAKULIA	SER	04/2008	N.A.	466.48	1000	533.52
85	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
86	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
87	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
88	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	609.04	1807.88	1198.84
89	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
90	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING	SR	02/2003	03/2009	199.55	330.32	130.77
91	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1420.39	834.46
92	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
93	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1260.61	678.48
94	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
95	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1103	154.96
96	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	1750	1036.52
97	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1077	149.99
98	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
99	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
100	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	1013.45	1428	414.55
101	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1151.81	181.98
102	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
103	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
104	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
105	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
107	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
108	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
109	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	544.72	137.73
110	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3
111	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
112	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	246.07	398.93	152.86
113	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	551	237
114	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
115	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
116	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
117	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
118	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
119	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	369.83	178.11
120	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
121	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
122	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1733.2	838.2
123	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
124	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
125	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
126	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
127	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
128	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
130	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
131	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	785.87	237.87
132	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1474.47	1102.33
133	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
134	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
135	CHHAPRA-MUZAFFARPUR (NL)	ECOR	04/2006	N.A.	378.56	2614.36	2235.8
136	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	325	729.92	404.92
137	BIHTA-AURANGABAD (NL)	ECOR	04/2008	N.A.	326.2	2995.01	2668.81
138	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
139	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	ECOR	04/2008	N.A.	445.25	2860.55	2415.3
140	NAWADA-LAXMIPUR (NL)	ECR	04/2008	N.A.	620.57	2626.98	2006.41
141	ARA-BHABHUA ROAD (NL)	SER	04/2008	N.A.	633.87	2396.88	1763.01
142	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
143	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	525.81	216.37
144	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
145	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
146	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
147	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	349	106.91
148	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
149	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
150	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
151	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2878.97	796.22

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
153	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
154	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
155	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
156	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	435	239.36
157	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
158	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
159	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	845.58	220.58
160	GEVRA ROAD PENDRA ROAD	SECR	02/2014	03/2022	2288	4919	2631
161	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
162	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1279	407
163	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	556.54	1342.46	785.92
164	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	403	174
165	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	566.41	237.02
166	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	528.26	347.44
167	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	624.47	3550	2925.53
168	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
169	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
170	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
171	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
172	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650
173	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	795.01	384.93
174	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
176	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	1142	3407	2265
177	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
178	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	3000	673.48
179	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
180	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.96	195.95
181	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1216	386.26
182	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
183	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1103.04	229.33
184	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
185	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
186	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
187	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
188	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756	1244.14
189	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
190	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
192	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	383.54	555	171.46
193	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	631.78	1195	563.22
194	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	369.9	1581.53	1211.63
195	GHUTIASHARIF-CANNING (ER)	ER	04/2009	12/2011	193.08	612.45	419.37
196	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
197	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
199	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	13809	9354.83
200	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3798.8	875.67
201	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	1180.19	3040	1859.81
202	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	589.15	426.28
203	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
204	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
205	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
206	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
207	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
208	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	625	338
209	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
210	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
211	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773
212	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
213	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
214	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	298.7	114.64
215	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	665.75	165.79
216	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
217	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	ER	04/2009	02/2012	259.51	533.59	274.08
218	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	1116	462.81
219	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
220	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1620.01	431.1

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
221	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
222	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
223	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
224	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
225	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
226	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
227	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
228	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
229	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
230	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
231	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
232	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
233	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
234	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
235	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
236	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
237	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
238	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
239	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
240	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
241	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(JANUARY 2019)

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
242	ENMORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
243	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
244	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
245	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
246	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
247	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
248	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
249	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
250	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6100.00	2608	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	5245.96	657.67	15
8	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	723.40	413.59	52
9	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57
10	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	06/2019	2915.00	5751.00	2836	78
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
12	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	03/2019	3076.00	4190.00	1114	18
13	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION	ONGC	03/2011	05/2013	03/2019	861.79	1577.15	715.36	70

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	UNIT(MOPS)								

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	6652.57	1541.24	12
16	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	1,1846.00	1,2739.82	893.82	24
17	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	1,5095.67	6402.7	123
18	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	02/2019	297.33	534.02	236.69	54
19	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	01/2019	4375.35	8150.00	3774.65	88
20	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	1,2532.44	1,3740.53	1208.09	10
21	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	1,4366.58	1,5164.05	797.47	20
22	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353.00	7998.00	2645	60
23	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	03/2019	436.68	602.44	165.76	27
24	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2021	2491.58	4105.30	1613.72	102
25	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2019	2496.90	6179.96	3683.06	111
26	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	05/2021	1657.00	4401.90	2744.9	63
27	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	06/2019	487.49	639.46	151.97	60
28	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	1,2964.60	1,3731.26	766.66	28
29	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9394.80	5475.21	147
30	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	04/2019	477.69	738.48	260.79	103

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	06/2019	4824.12	5071.94	247.82	80
32	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	1,1638.55	1,2865.92	1227.37	21
33	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,3762.80	2632.61	103
34	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	06/2019	1364.52	1891.41	526.89	38
35	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	3846.30	867.82	93
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	03/2019	1779.29	2187.32	408.03	124
37	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9141.97	4387.55	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
38	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
39	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	1342.46	785.92	96
40	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	3550.00	2925.53	61
41	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1077.00	149.99	12
42	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	939.00	414.57	36
43	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
44	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	3798.80	875.67	147
45	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	1,3809.00	9354.83	108
46	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2019	495.74	734.01	238.27	69

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
48	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
49	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	3000.00	673.48	79
50	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
51	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2019	1142.00	3407.00	2265	60
52	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
53	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
54	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
55	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2022	1188.91	1620.01	431.1	36
56	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	02/2019	133.41	385.00	251.59	119
58	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	1928.07	1117.29	21
59	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	4968.00	2574.53	81
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	749.00	271.12	96
61	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	732.81	1993.00	1260.19	144
62	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	05/2019	653.19	1116.00	462.81	62
63	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
65	MANDARHILL -DUMKA -RAMPURHAT (NL), ER	ER	04/1995	03/2016	03/2020	1125.89	2021.29	895.4	48
66	LALITPUR -SATNA -REWA -SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
67	JAYANAGAR -DARBHANGA -NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1156.41	831.68	96
68	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	1180.19	3040.00	1859.81	123
69	DAUSA -GANGAPUR CITY (NL), NWR	NWR	02/1997	02/2019	12/2019	410.08	795.01	384.93	10
70	UDHAMPUR -SRINAGAR -BARAMULLA (NL), NR	NR	03/1995	11/2002	03/2021	2500.00	2,7949.00	25449	220
71	DALLI -RAJHARA - RAOGHAT (PART OF DALLI -RAJHARA - JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	631.78	1195.00	563.22	111
72	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2019	383.54	555.00	171.46	117
73	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
74	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
75	SAMBALPUR -TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2021	1111.99	1539.28	427.29	25
76	RAJKHARSWAN - CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	09/2019	148.77	377.00	228.23	33
77	HOTGI -KUDGI -GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
78	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	10/2020	829.74	1216.00	386.26	67
79	CHHAPRA -BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
80	RAJKOT -VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR -SARADIYA AND SOMNATH -KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
81	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651.00	1009.00	358	108
82	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	02/2019	309.44	525.81	216.37	38
83	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	810.02	108.41	28
84	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
85	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	1120.00	177.05	24
86	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12
87	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
88	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	03/2019	609.04	1807.88	1198.84	239

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
89	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	04/2019	217.61	360.84	143.23	108
90	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108.00	2288.00	1180	91
91	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.60	1544.00	277.4	33
92	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2019	199.81	385.13	185.32	119

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
93	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	02/2019	150.00	600.00	450	155

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
94	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2020	343.00	488.40	145.4	41

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
95	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
96	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above					(January 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	09/2018	.00	56
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2018	.00	67
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2018	.00	64
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	10/2018	.00	101
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2018	.00	61
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	02/2019	.00	30
10	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	01/2019	.00	60
11	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2018	.00	62
12	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	12/2018	.00	57
13	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	06/2019	.00	71
14	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	08/2020	.00	128
15	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	03/2019	.00	79
16	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
17	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(January 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	-	.00	0
19	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	06/2019	.00	76
20	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	05/2019	.00	58
21	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2019	.00	81
22	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
23	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	03/2019	.00	11
24	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	06/2019	.00	31
25	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	12/2018	.00	65
26	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	12/2018	.00	17
27	4-LANING OF BRAHMAPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	06/2020	.00	82
28	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
29	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	-	.00	0
30	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	06/2019	.00	70
31	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	-	.00	0
32	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
33	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65	67
34	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2018	.00	60
35	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	06/2019	.00	64
36	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	04/2019	.00	8
37	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	05/2019	.00	56
38	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	03/2019	.00	54

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (January 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
40	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	06/2019	.00	61
41	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
42	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	-	.00	0
43	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79 -	1,583.79	01/2019 -	06/2019	.00	5
44	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00 -	1,585.00	05/2013 -	04/2019	.00	71
45	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83	37
46	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	03/2019	.00	31
47	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	01/2019 -	01/2019	.00	0
48	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	-	03/2019	.00	0
49	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	03/2019	.00	89
50	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	-	.00	0
51	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	06/2019	.00	75
52	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	-	.00	0
53	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	02/2019	.00	13
54	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	04/2019	.00	29
55	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	03/2019	.00	44
56	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	-	.00	0
57	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	04/2019 -	04/2019	.00	0
58	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	-	.00	0
59	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(January 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
60	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	05/2019	.00	0
61	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
62	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	12/2019	.00	69
63	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73	0
64	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56	71
	Total		76,530.12 -	81,310.94				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
65	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	271.56	12/2017 -	-	11.07	0
	<u>Mumbai Port Trust</u>							
66	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	-	82.72	0
	Total		610.89 -	941.02				
	Grand Total		77,141.01	82,251.96				

Central Sector Projects Detail's

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					31.01.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	0.00 (0.00) [0]
3	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	0.00 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
5	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (12/2019) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	0.00 (0.00) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	0.00 (0.00) [0]
8	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	29.43 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
9	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [2/2020]	601.02 (-) [601.02]	96.75 (0.00) [-]
10	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2019]	272.19 (-) [272.19]	111.92 (0.00) [0]
	<u>Petroleum</u>				
11	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
12	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	1.53 (0.00) [3]
13	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2021]	384.58 (-) [384.58]	41.38 (0.00) [0]
14	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003,	4/2017	9/2018	420.76	32.71

	NAGAYALANKA-KG		(2/2019) [2/2019]	(207.80) [207.80]	(-212.96) [5]
15	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (8/2021) [8/2021]	34,012.00 (-) [34,012.00]	1,691.99 (0.00) [14]
16	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [4/2022]	355.00 (-) [355.00]	0.00 (0.00) [0]
17	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
18	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	2,864.07 (0.00) [0]
19	VVSPCL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	288.56 (0.00) [0]
	<u>Railways</u>				
20	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
21	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.07 (0.00) [0]
22	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
23	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (-) [3,631.00]	177.18 (0.00) [12]
24	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (-) [2,120.16]	289.91 (1,074.96) [168]
25	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (-) [2,499.71]	183.68 (0.00) [0]
26	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	4.98 (0.50) [21]
27	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
28	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2022]	2,288.70 (-) [2,288.70]	393.16 (0.00) [12]
29	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
30	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	7/2006	3/2008 (-) [3/2020]	732.81 (-) [1,993.00]	2,017.37 (1,260.19) [144]
31	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	378.12 (302.41) [0]
32	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	1,005.66 (0.00) [24]
	<u>Road Transport And Highways</u>				
33	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	0.00 (0.00) [0]

34	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
35	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	0.00 (0.00) [0]
36	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
37	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	5/2013 (-) [4/2019]	1,585.00 (-) [1,585.00]	2,177.45 (0.00) [71]
38	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
39	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	0.00 (0.00) [0]
40	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
41	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [3/2021]	1,532.62 (-) [1,532.62]	0.00 (0.00) [0]
42	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [11/2019]	648.33 (-) [648.33]	22.70 (0.00) [29]
43	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	51.81 (0.00) [0]
44	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	10/2015	/ (-) [0/0]	480.21 (-) [480.21]	0.00 (0.00) [0]
45	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR	7/2015	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
46	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A	12/2014	2/2015 (-) [0/0]	201.12 (201.00) [201.12]	0.00 (0.00) [0]
47	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC	1/2014	7/2014 (-) [0/0]	361.30 (-) [207.40]	44.08 (-153.90) [0]
48	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	2/2015	5/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
49	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	2/2014	11/2014 (-) [0/0]	170.21 (-) [170.21]	5.65 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [0/0]	565.09 (-) [565.09]	0.00 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	3/2015	/ (-) [0/0]	175.03 (-) [175.00]	0.00 (-0.03) [0]
53	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION)	2/2015	2/2017 (-) [0/0]	241.61 (-) [241.61]	7.71 (0.00) [0]
54	REHABILITATION AND UPGRADATION OF NH-167 FROM	2/2015	4/2015	224.83	0.00

	KM 70		(-) [0/0]	(-) [224.83]	(0.00) [0]
55	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (-) [0/0]	271.45 (-) [271.45]	0.00 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [3/2020]	648.32 (-) [503.10]	15.10 (-145.22) [0]
57	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	2/2015	/ (-) [0/0]	266.00 (-) [266.00]	0.00 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	3/2015	9/2015 (-) [0/0]	309.01 (-) [309.01]	0.00 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	2/2014	7/2014 (-) [0/0]	258.99 (-) [258.99]	16.54 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	2/2014	6/2014 (-) [0/0]	417.61 (-) [417.61]	0.00 (0.00) [0]
61	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	11/2014	2/2017 (-) [0/0]	297.78 (330.00) [330.00]	0.00 (32.22) [0]
62	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
63	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [0/0]	1,959.00 (-) [1,959.00]	0.00 (0.00) [0]
64	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [0/0]	1,323.15 (-) [1,323.15]	0.00 (0.00) [0]
65	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [12/2019]	1,550.98 (-) [1,550.98]	0.00 (0.00) [-]
66	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [6/2019]	1,535.00 (-) [1,535.00]	3,003.77 (0.00) [61]
67	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	43.99 (145.48) [2]
68	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [12/2018]	571.00 (-) [571.00]	582.52 (0.00) [0]
69	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
70	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	7/2015	7/2018 (-) [6/2019]	465.85 (-) [465.85]	316.25 (0.00) [11]
71	CENTRAL DISPATCH YARD	8/2015	8/2018 (-) [6/2019]	320.66 (-) [320.66]	150.36 (0.00) [10]
72	COKE OVEN BATTERY-5	12/2011	12/2017 (-) [9/2019]	2,858.00 (-) [2,500.00]	1,133.76 (-358.00) [21]
73	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016 (-) [3/2020]	343.00 (-) [488.40]	247.65 (145.40) [41]
	<u>Urban Development</u>				

74	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [3/2019]	206.58 (-) [206.58]	0.02 (0.00) [0]
75	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
76	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [157.84]	154.30 (0.00) [0]
77	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>ARUNACHAL PRADESH</u>				
	<u>Petroleum</u>				
78	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019 (-) [1/2019]	247.52 (-) [247.52]	148.35 (0.00) [-1]
	<u>Power</u>				
79	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (3/2019) [3/2019]	2,496.90 (6,179.96) [6,179.96]	6,900.51 (3,683.06) [111]
80	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,448.57 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
81	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
82	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH- 229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
83	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH- 229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
84	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
85	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
86	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
87	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
88	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
89	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	38.50 (0.00) [0]
90	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
91	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
92	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]

93	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
94	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
95	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [0/0]	334.22 (-) [334.22]	0.00 (0.00) [0]
96	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]
97	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
98	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
99	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
100	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
101	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
102	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]
103	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [0/0]	165.00 (-) [165.00]	0.00 (0.00) [0]
104	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
105	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
106	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
107	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
108	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [0/0]	104.00 (-) [201.00]	0.00 (97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
109	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [5/2021]	875.00 (-) [875.00]	174.00 (0.00) [0]
110	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
111	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,112.54 (-86.29) [81]
112	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	74.97

			(-) [2/2020]	(-) [557.00]	(0.00) [0]
113	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	315.44 (0.00) [0]
114	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
115	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	89.48 (127.41) [70]
116	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	217.07 (0.00) [0]
117	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	2.08 (0.00) [0]
118	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,346.72 (0.00) [0]
119	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	101.71 (-5.15) [0]
120	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Power</u>				
121	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [1/2019]	4,375.35 (8,150.00) [8,150.00]	7,220.84 (3,774.65) [88]
	<u>Railways</u>				
122	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (486.96) [551.00]	615.94 (237.00) [0]
123	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	288.01 (-50.32) [-24]
124	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	257.41 (-49.96) [0]
125	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (614.81) [398.93]	339.81 (152.86) [0]
126	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	575.61 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
127	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
128	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
129	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	0.00 (-65.82) [0]
130	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
131	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-)	520.01 (-)	0.00 (0.00)

			[0/0]	[520.01]	[0]
132	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	80.00 (0.00) [0]
133	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	0.00 (0.00) [0]
134	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
135	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
136	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
137	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [4/2019]	217.61 (-) [360.84]	390.71 (143.23) [108]
138	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [2/2019]	160.00 (-) [167.98]	202.58 (7.98) [129]
139	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
140	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	16.84 (0.00) [0]
141	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
142	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	0.00 (0.00) [0]
143	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
144	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [12/2018]	280.00 (-) [361.00]	410.32 (81.00) [0]
145	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
146	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
147	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [3/2019]	199.81 (-) [385.13]	209.80 (185.32) [119]
148	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [0]
149	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2019]	208.00 (-) [230.00]	297.81 (22.00) [131]
150	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [4/2019]	225.00 (-) [225.00]	312.79 (0.00) [130]
151	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [2/2019]	245.00 (174.34) [174.34]	214.88 (-70.66) [131]

152	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
153	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	BIHAR				
	Petroleum				
154	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	455.62 (0.00) [-10]
155	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	38.20 (0.00) [0]
156	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	2.56 (0.00) [0]
157	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	0.00 (0.00) [0]
158	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [3/2019]	822.66 (-) [822.66]	868.92 (0.00) [4]
159	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	4.04 (0.00) [0]
160	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	0.00 (0.00) [0]
161	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [6/2020]	324.00 (-) [324.00]	107.15 (0.00) [0]
	Power				
162	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS	4/2016	6/2019 (6/2019) [6/2019]	790.13 (790.30) [790.30]	527.54 (0.17) [0]
163	BARH STPP(3X660MW) NTPC	2/2005	1/2011 (4/2021) [4/2021]	8,692.97 (15,095.67) [15,095.67]	15,441.10 (6,402.70) [123]
164	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	5/2014 (-) [5/2019]	5,353.00 (-) [7,998.00]	7,511.72 (2,645.00) [60]
165	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	1/2018 (-) [5/2020]	12,964.60 (-) [13,731.26]	12,593.00 (766.66) [28]
166	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	5/2015	12/2016 (-) [3/2019]	436.68 (-) [602.44]	540.02 (165.76) [27]
	Railways				
167	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [2,396.88]	0.39 (1,763.01) [0]
168	ARARIA-SUPAUL (NL)	4/2008	/ (-) [3/2023]	1,605.17 (-) [1,605.17]	0.19 (0.00) [-]
169	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [0/0]	326.20 (-) [2,995.01]	1.68 (2,668.81) [0]
170	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	378.56 (-) [2,614.36]	111.71 (2,235.80) [-]

171	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/	406.92	200.00
			(-)	(-)	(-67.92)
			[0/0]	[339.00]	[0]
172	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-)	(-)	(0.00)
			[0/0]	[205.00]	[0]
173	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/	329.39	759.20
			(-)	(-)	(237.02)
			[12/2021]	[566.41]	[-]
174	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	0.00
			(-)	(-)	(2,415.30)
			[0/0]	[2,860.55]	[0]
175	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	13.00
			(-)	(-)	(154.16)
			[0/0]	[367.17]	[0]
176	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	330.82
			(-)	(-)	(1,538.12)
			[3/2023]	[2,066.77]	[-]
177	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	876.49
			(-)	(-)	(831.68)
			[3/2020]	[1,156.41]	[96]
178	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	40.00
			(-)	(-)	(237.87)
			[3/2020]	[785.87]	[0]
179	KATIHAR - JOGBANI (GC)(NEFR)	9/2001	12/2010	792.46	929.63
			(-)	(724.31)	(527.54)
			[0/0]	[1,320.00]	[0]
180	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	183.72
			(-)	(-)	(426.28)
			[3/2022]	[589.15]	[-]
181	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	4.98
			(-)	(-)	(26.24)
			[3/2020]	[360.00]	[-]
182	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	0.00
			(-)	(-)	(0.00)
			[10/2021]	[1,200.20]	[19]
183	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	640.78
			(-)	(-)	(16.61)
			[3/2020]	[516.02]	[0]
184	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.38
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
185	MAHARAJGANJ-MASRAKH (NL) - NER	4/2003	6/2018	218.19	370.10
			(-)	(-)	(195.37)
			[10/2018]	[413.56]	[0]
186	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	495.40
			(-)	(283.95)	(271.12)
			[3/2020]	[749.00]	[96]
187	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	4.41
			(-)	(-)	(715.09)
			[0/0]	[926.09]	[0]
188	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	0.00
			(-)	(-)	(454.09)
			[3/2022]	[1,185.73]	[12]
189	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.58
			(-)	(-)	(0.00)
			[0/0]	[281.30]	[0]
190	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.52
			(-)	(-)	(0.00)
			[0/0]	[228.05]	[0]
191	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	538.21

			(-) [0/0]	(-) [559.91]	(227.76) [0]
192	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.00
			(-) [0/0]	(-) [2,626.98]	(2,006.41) [0]
193	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	930.20
			(-) [3/2020]	(2,132.03) [2,145.00]	(1,612.13) [12]
194	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	11/2001	2/2016	624.47	97.63
			(-) [3/2021]	(-) [3,550.00]	(2,925.53) [61]
195	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/	180.82	462.75
			(-) [0/0]	(-) [528.26]	(347.44) [0]
196	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	0.00
			(-) [10/2021]	(-) [1,491.47]	(0.00) [19]
197	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	1.81
			(-) [3/2022]	(-) [1,215.54]	(471.50) [12]
198	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	253.10
			(-) [3/2021]	(-) [729.92]	(404.92) [-]
199	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	338.44
			(-) [3/2021]	(-) [1,474.47]	(1,102.33) [-]
200	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	0.00
			(-) [0/0]	(-) [380.00]	(0.00) [0]
201	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.17
			(-) [0/0]	(-) [2,393.23]	(1,714.61) [0]
	Road Transport And Highways				
202	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013	351.54	351.23
			(-) [0/0]	(-) [351.54]	(0.00) [0]
203	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	564.70
			(-) [12/2018]	(-) [511.54]	(0.00) [0]
204	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33
			(-) [0/0]	(-) [375.09]	(0.00) [0]
205	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	832.77
			(-) [6/2019]	(-) [575.00]	(0.00) [71]
206	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	77.43
			(-) [6/2019]	(-) [581.84]	(0.00) [25]
207	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015	288.24	0.00
			(-) [0/0]	(-) [288.24]	(0.00) [0]
208	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-) [0/0]	(-) [2,598.00]	(0.00) [0]
209	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020	235.48	0.00
			(-) [3/2020]	(-) [227.77]	(-7.71) [0]
210	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20	0.00
			(-) [0/0]	(-) [496.20]	(0.00) [0]
211	ENGINEERING, PROCUREMENT, AND CONSTRUCTION	11/2013	7/2016	683.83	0.00

	OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P		(-) [0/0]	(-) [683.83]	(0.00) [0]
212	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	0.00 (0.00) [0]
213	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [553.30]	0.00 (0.00) [0]
214	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
215	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	38.33 (0.00) [-]
216	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [10/2020]	642.41 (-) [642.41]	20.12 (0.00) [-]
217	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [4/2020]	322.09 (-) [322.09]	71.28 (0.00) [24]
218	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	0.00 (0.00) [0]
219	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [814.04]	279.13 (0.00) [-]
220	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
221	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [4/2019]	1,041.10 (-) [1,041.10]	175.85 (0.00) [0]
222	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [12/2018]	574.00 (-) [574.00]	768.65 (0.00) [0]
223	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [6/2019]	671.30 (-) [671.30]	884.58 (0.00) [76]
224	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	0.00 (0.00) [0]
225	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
226	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2014	3/2014 (-) [0/0]	377.64 (-) [377.64]	0.00 (0.00) [0]
227	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
228	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
229	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [319.68]	0.00 (0.00) [0]
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	8/2016 (-)	282.41 (-)	67.52 (0.00)

	ANISABAD-AURANG		[0/0]	[282.41]	[0]
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/2013	8/2014 (-) [0/0]	322.01 (-) [322.01]	0.00 (0.00) [0]
233	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [358.22]	188.71 (0.00) [0]
234	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	0.00 (0.00) [0]
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
236	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
237	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [0/0]	950.64 (-) [950.64]	0.00 (0.00) [0]
238	STRENGTHENING & WIDENING WORK OF EXISTING 2- LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	0.00 (0.00) [0]
239	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [10/2019]	399.54 (-) [399.54]	158.10 (0.00) [6]
240	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [3/2019]	854.80 (-) [854.80]	551.98 (0.00) [-]
241	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [12/2018]	516.13 (-) [516.13]	404.29 (0.00) [0]
242	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
	<u>Urban Development</u>				
243	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [6/2020]	496.18 (496.00) [498.99]	34.09 (2.81) [36]
244	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
245	AMERA OC RCE	2/2015	3/2018 (-) [0/0]	335.97 (-) [335.97]	51.70 (0.00) [0]
246	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	60.38 (0.00) [0]
247	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016 (-) [3/2019]	198.59 (-) [198.59]	169.50 (0.00) [36]
248	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2019]	258.56 (-) [258.56]	168.00 (0.00) [36]
249	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	71.55 (0.00) [0]
250	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	83.39 (0.00) [0]

251	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	3.88 (0.00) [0]
252	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,857.01 (0.00) [0]
253	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (-) [3/2020]	152.43 (-) [459.49]	184.45 (307.06) [60]
254	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
255	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	5.16 (0.00) [72]
256	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	1,957.98 (0.00) [0]
257	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
258	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
259	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2020]	321.50 (-) [321.50]	206.84 (0.00) [72]
260	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.21 (0.00) [0]
261	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
262	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	0.00 (0.00) [0]
	<u>Power</u>				
263	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	6/2017 (6/2019) [6/2019]	11,846.00 (-) [12,739.82]	10,831.46 (893.82) [24]
264	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,388.93 (0.00) [0]
	<u>Railways</u>				
265	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (-) [12/2019]	872.00 (-) [1,279.00]	0.00 (407.00) [0]
266	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	4/1995	12/2012 (-) [3/2022]	631.78 (632.00) [1,195.00]	675.36 (563.22) [111]
267	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [3/2022]	2,288.00 (-) [4,919.00]	67.00 (2,631.00) [0]
268	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (-) [3/2021]	1,973.00 (-) [1,973.00]	78.00 (0.00) [0]
269	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM	4/2011	3/2022 (-) [3/2022]	1,471.93 (-) [543.00]	0.00 (-928.93) [0]
270	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST	4/2013	9/2018	3,055.00	600.00

	CORRIDOR-PHASE I		(-) [0/0]	(-) [3,055.00]	(0.00) [0]
271	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2020]	1,160.00 (-) [1,160.83]	571.51 (0.83) [0]
272	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
273	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [3/2020]	1,402.02 (-) [958.09]	887.59 (-443.93) [0]
274	SALKA ROAD -ANUPNAGAR LINE DOUBLING	9/2006	3/2010 (-) [12/2019]	383.54 (-) [555.00]	588.95 (171.46) [117]
	<u>Road Transport And Highways</u>				
275	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [0/0]	1,029.96 (-) [1,029.96]	0.00 (0.00) [0]
276	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700- 292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-	12/2010	12/2012 (-) [0/0]	169.26 (-) [169.26]	0.00 (0.00) [0]
277	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [6/2019]	726.67 (-) [726.67]	323.95 (0.00) [14]
278	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	7.21 (0.00) [0]
279	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [6/2019]	596.67 (-) [596.67]	284.92 (0.00) [13]
280	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION.	10/2014	3/2015 (-) [0/0]	213.47 (-) [213.47]	0.00 (0.00) [0]
281	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	0.00 (0.00) [0]
282	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION.	12/2014	/ (-) [0/0]	394.20 (-) [394.20]	0.00 (0.00) [0]
283	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	0.00 (0.00) [0]
284	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV	10/2014	3/2015 (-) [0/0]	298.34 (-) [298.34]	0.00 (0.00) [0]
285	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I	11/2014	3/2015 (-) [0/0]	262.54 (-) [262.54]	0.00 (0.00) [0]
286	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	3/2015	/ (-) [0/0]	422.34 (-) [422.34]	22.25 (0.00) [0]
	<u>Steel</u>				
287	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	6/2020 (-) [6/2020]	818.00 (-) [818.00]	31.88 (0.00) [0]
288	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	4/2015 (-) [0/0]	188.93 (-) [188.93]	128.44 (0.00) [0]
289	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (6/2019) [6/2019]	15,525.00 (-) [15,525.00]	14,659.90 (0.00) [49]

	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
290	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,513.89 (-243.77) [5]
	<u>DELHI</u>				
	<u>Health And Family Welfare</u>				
291	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (6/2018) [7/2019]	204.44 (-) [204.44]	176.22 (0.00) [26]
292	AIIMS - OPD(NEW)	8/2014	5/2017 (6/2018) [3/2019]	293.65 (-) [293.65]	282.43 (0.00) [22]
293	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [2/2020]	156.56 (-) [156.65]	54.94 (0.09) [-]
294	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (10/2020) [10/2020]	414.11 (-) [513.89]	147.00 (99.78) [83]
	<u>Heavy Industry</u>				
295	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [9/2019]	1,554.00 (-) [1,554.00]	335.03 (0.00) [0]
	<u>Power</u>				
296	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (6/2019) [9/2019]	1,394.52 (1,394.52) [1,394.52]	293.99 (0.00) [28]
	<u>Railways</u>				
297	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [0/0]	295.68 (-) [295.68]	1.20 (0.00) [0]
298	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [0/0]	156.65 (-) [197.17]	56.10 (40.52) [0]
	<u>Road Transport And Highways</u>				
299	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/ (-) [0/0]	771.18 (-) [7,558.00]	261.77 (6,786.82) [0]
	<u>Telecommunications</u>				
300	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	367.03 (0.00) [0]
	<u>Urban Development</u>				
301	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2020) [6/2020]	197.33 (-) [197.33]	14.99 (0.00) [14]
302	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	677.49 (0.00) [0]
303	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [11/2019]	271.90 (-) [271.90]	4.44 (0.00) [0]
304	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [6/2019]	188.00 (-) [188.00]	101.04 (0.00) [0]
305	DELHI MRTS PHASE-III	9/2011	3/2016 (5/2019) [5/2019]	38,585.00 (-) [38,585.00]	37,044.70 (0.00) [38]
306	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2020]	1,219.21 (-) [1,592.00]	377.51 (372.79) [5]

307	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (-) [238.56]	20.59 (0.00) [0]
308	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [11/2019]	4,264.00 (-) [4,439.23]	3,746.53 (175.23) [0]
309	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/ (-) [0/0]	392.00 (-) [392.00]	0.00 (0.00) [0]
310	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/ (-) [0/0]	422.00 (-) [422.00]	0.00 (0.00) [0]
311	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [0/0]	2,694.00 (-) [2,694.00]	0.00 (0.00) [0]
312	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018 (-) [0/0]	248.20 (-) [248.20]	1.21 (0.00) [0]
	<u>GOA</u>				
	<u>Defence Production</u>				
313	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020 (-) [8/2020]	285.95 (286.00) [285.95]	61.95 (0.00) [0]
314	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018 (1/2019) [0/0]	167.69 (168.00) [167.69]	105.91 (0.00) [0]
	<u>Health And Family Welfare</u>				
315	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [5/2020]	249.01 (-) [249.01]	46.28 (0.00) [-]
	<u>Road Transport And Highways</u>				
316	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [280.16]	16.06 (0.00) [0]
317	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	10.72 (0.00) [0]
318	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM- MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	0.00 (0.00) [0]
319	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	16.10 (0.00) [0]
320	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	38.33 (0.00) [0]
321	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	0.00 (0.00) [0]
322	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	0.00 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
323	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (11/2016) [6/2020]	11,459.00 (16,580.00) [16,580.00]	12,987.00 (5,121.00) [54]
	<u>Petroleum</u>				
324	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (-) [0/0]	588.20 (-) [588.20]	0.00 (0.00) [0]

325	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [9/2019]	3,380.00 (-) [3,380.00]	1,399.13 (0.00) [0]
326	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [3/2019]	327.78 (-) [200.00]	134.00 (-127.78) [11]
327	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	3.90 (0.00) [0]
328	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [2/2020]	906.00 (-) [906.00]	13.76 (0.00) [0]
329	GAMJI REDEVELOPMENT PROJECT	5/2015	11/2019 (12/2018) [2/2019]	1,671.22 (567.22) [567.22]	457.84 (-1,104.00) [-9]
330	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	69.50 (0.00) [0]
331	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (3/2026) [3/2026]	1,162.56 (1,162.56) [1,162.56]	307.27 (0.00) [0]
332	REPLACEMENT OF KV SECTION OF KSPL	10/2014	8/2018 (-) [0/0]	279.00 (-) [279.00]	200.05 (0.00) [0]
	<u>Power</u>				
333	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (6/2019) [9/2019]	193.14 (193.14) [193.14]	4.80 (0.00) [3]
334	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (9/2018) [9/2019]	175.64 (175.64) [175.64]	80.24 (0.00) [12]
335	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B)	7/2016	12/2018 (12/2018) [2/2019]	300.94 (300.94) [300.94]	226.76 (0.00) [2]
336	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	11/2017 (-) [3/2019]	330.00 (-) [330.00]	311.17 (0.00) [16]
	<u>Railways</u>				
337	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	691.40 (106.70) [0]
338	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (-) [3/2020]	829.74 (-) [385.60]	528.96 (-444.14) [0]
339	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [203.00]	202.29 (85.64) [0]
340	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (-) [3/2019]	551.51 (-) [551.51]	257.05 (0.00) [0]
341	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-) [3/2019]	318.24 (-) [321.62]	83.53 (3.38) [84]
342	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (-) [3/2020]	691.84 (-) [691.84]	43.44 (0.00) [0]
343	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	140.65 (0.00) [0]
344	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON	3/2017	/ (-)	243.60 (-)	0.00 (0.00)

	AIR SPACE OF STATIO		[0/0]	[243.60]	[0]
345	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/	844.10	62.58
			(-)	(-)	(0.00)
			[3/2023]	[844.10]	[-]
346	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019	343.00	291.62
			(-)	(-)	(0.00)
			[12/2019]	[343.00]	[9]
347	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/	153.83	0.00
			(-)	(-)	(0.00)
			[0/0]	[153.83]	[0]
348	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021	1,548.66	892.89
			(-)	(-)	(0.00)
			[12/2021]	[1,548.66]	[0]
349	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019	320.66	550.16
			(-)	(-)	(538.30)
			[3/2022]	[858.96]	[36]
350	SURENDRA NAGAR RAJKOT	4/2015	3/2021	1,002.39	316.23
			(-)	(-)	(0.00)
			[3/2020]	[1,002.39]	[-12]
351	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/	248.26	0.00
			(-)	(-)	(0.00)
			[0/0]	[248.26]	[0]
	<u>Road Transport And Highways</u>				
352	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/	417.19	100.75
			(-)	(-)	(0.00)
			[9/2019]	[417.19]	[-]
353	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/	829.97	72.69
			(-)	(-)	(0.00)
			[1/2020]	[829.97]	[-]
354	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020	1,958.88	549.02
			(-)	(-)	(0.00)
			[8/2020]	[1,958.88]	[2]
355	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015	2,125.24	4,659.71
			(-)	(-)	(0.00)
			[0/0]	[2,125.24]	[0]
356	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/	364.56	64.61
			(-)	(-)	(0.00)
			[12/2019]	[364.56]	[-]
357	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/	1,161.39	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,161.39]	[0]
358	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/	1,437.64	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,437.64]	[0]
359	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/	2,702.05	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,702.05]	[0]
360	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/	998.18	213.85
			(-)	(-)	(0.00)
			[8/2019]	[998.18]	[-]
361	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/	723.64	216.75
			(-)	(-)	(0.00)
			[9/2019]	[723.64]	[-]
362	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/	834.64	138.71
			(-)	(-)	(0.00)
			[10/2019]	[834.64]	[-]
363	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/	763.08	140.35
			(-)	(-)	(0.00)
			[8/2019]	[763.08]	[-]
364	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012	1,509.10	3,187.21
			(-)	(-)	(1,728.77)

			[8/2018]	[3,237.87]	[0]
365	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
366	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [12/2018]	953.88 (-) [953.88]	976.36 (0.00) [0]
367	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [0/0]	1,052.21 (-) [1,052.21]	0.00 (0.00) [0]
368	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,251.11]	0.00 (0.00) [0]
369	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [3/2019]	425.60 (-) [425.60]	0.00 (0.00) [-]
370	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	346.60 (0.00) [0]
	<u>Urban Development</u>				
371	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
372	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	27.83 (0.00) [0]
	<u>Health And Family Welfare</u>				
373	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [0/0]	505.58 (-) [523.00]	508.29 (17.42) [0]
	<u>Petroleum</u>				
374	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [7/2019]	3,529.00 (-) [3,529.00]	1,068.35 (0.00) [0]
375	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	2.76 (0.00) [0]
376	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	15.68 (0.00) [0]
377	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	128.87 (0.00) [0]
	<u>Railways</u>				
378	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	4/2013	/ (-) [0/0]	400.00 (-) [400.00]	0.00 (0.00) [0]
379	JIND-SONEPAT (NL),NR	1/2004	3/2012 (-) [0/0]	238.56 (-) [740.00]	722.65 (501.44) [0]
380	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2019]	346.32 (-) [300.00]	273.41 (-46.32) [0]
381	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [0/0]	287.00 (-) [625.00]	4.38 (338.00) [0]
	<u>Road Transport And Highways</u>				
382	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-)	602.95 (-)	395.53 (0.00)

			[3/2019]	[602.95]	[33]
383	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [3/2019]	574.28 (-) [574.28]	380.25 (0.00) [8]
384	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [6/2019]	639.79 (-) [552.90]	422.78 (-86.89) [-9]
385	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [4/2019]	2,128.72 (-) [2,128.72]	963.21 (0.00) [0]
386	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [8/2019]	248.97 (-) [248.97]	212.53 (0.00) [3]
387	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [0/0]	1,484.30 (-) [1,484.30]	0.00 (0.00) [0]
388	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [5/2019]	1,004.67 (-) [1,004.67]	0.00 (0.00) [0]
389	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [10/2018]	486.00 (-) [486.00]	470.01 (0.00) [0]
390	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
391	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
392	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [6/2019]	1,108.00 (-) [2,288.00]	3,954.66 (1,180.00) [91]
393	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [0/0]	551.58 (-) [551.58]	0.00 (0.00) [0]
394	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [0/0]	275.12 (-) [275.12]	0.00 (0.00) [0]
395	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING	3/2018	/ (-) [0/0]	307.79 (-) [307.79]	0.00 (0.00) [0]
396	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.78 (-) [181.78]	0.00 (0.00) [0]
397	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [0/0]	198.05 (-) [198.05]	0.00 (0.00) [0]
398	ROHTAK-BAWAL	5/2011	11/2013 (-) [0/0]	650.00 (-) [650.00]	832.39 (0.00) [0]
399	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I	3/2018	/ (-) [0/0]	795.50 (-) [795.50]	0.00 (0.00) [0]
400	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [0/0]	634.70 (-) [634.70]	0.00 (0.00) [0]
	<u>HIMACHAL PRADESH</u>				
	<u>Petroleum</u>				
401	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019 (-) [2/2019]	151.00 (-) [151.00]	112.58 (0.00) [-7]
402	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT	2/2016	5/2019	356.00	205.41

	UNA, HP		(-) [1/2019]	(-) [356.00]	(0.00) [-4]
	<u>Power</u>				
403	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2021]	3,919.59 (-) [9,394.80]	7,164.11 (5,475.21) [147]
	<u>Railways</u>				
404	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2026]	2,966.99 (-) [7,000.00]	358.51 (4,033.01) [0]
	<u>Road Transport And Highways</u>				
405	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [2/2019]	273.20 (-) [273.20]	230.61 (0.00) [0]
406	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [6/2020]	2,485.93 (-) [2,485.93]	0.00 (0.00) [0]
407	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016 (-) [4/2019]	1,916.79 (-) [1,916.79]	1,948.92 (0.00) [29]
408	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2019]	934.46 (-) [934.46]	330.04 (0.00) [12]
409	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [0/0]	478.74 (-) [478.74]	0.00 (0.00) [0]
410	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [7/2020]	1,273.71 (-) [1,273.71]	0.00 (0.00) [-]
411	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [11/2019]	447.75 (-) [447.75]	135.01 (0.00) [-]
412	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (-) [1,583.18]	0.00 (0.00) [-]
	<u>Urban Development</u>				
413	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [2/2019]	270.83 (-) [270.83]	163.97 (0.00) [51]
	<u>JAMMU AND KASHMIR</u>				
	<u>Power</u>				
414	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [10/2023]	8,112.12 (-) [8,112.12]	1,006.39 (0.00) [42]
	<u>Railways</u>				
415	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [3/2021]	2,500.00 (-) [27,949.00]	17,336.24 (25,449.00) [220]
	<u>Road Transport And Highways</u>				
416	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [0/0]	1,471.75 (-) [1,471.75]	0.00 (0.00) [0]
417	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	119.87 (0.00) [18]
418	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [10/2019]	2,136.97 (-) [2,136.97]	1,065.56 (0.00) [10]
419	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]

420	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	3,986.82 (0.00) [0]
421	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [3/2019]	1,987.00 (-) [1,987.00]	2,403.47 (0.00) [44]
422	SRINAGAR TO BANIHAI	6/2011	6/2014 (-) [0/0]	1,100.70 (-) [1,100.70]	1,288.68 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
423	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	185.00 (0.00) [0]
424	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	0.00 (0.00) [0]
425	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2020]	163.51 (-) [163.51]	103.83 (0.00) [108]
426	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	45.29 (0.00) [0]
427	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
428	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2019]	162.46 (-) [162.46]	89.21 (0.00) [60]
429	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [4/2018]	289.45 (-) [289.45]	194.20 (0.00) [0]
430	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2021]	706.40 (-) [706.40]	185.62 (0.00) [104]
431	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [4/2019]	1,230.27 (-) [1,230.27]	334.71 (0.00) [48]
432	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2018]	339.88 (-) [339.88]	12.08 (0.00) [0]
433	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.24 (0.00) [0]
434	NORTH URIMARI OCP (3.0 MTY)	12/2007	3/2012 (-) [3/2019]	179.87 (-) [179.87]	175.17 (0.00) [84]
435	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2018]	269.82 (-) [269.82]	179.95 (0.00) [0]
436	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2019]	510.85 (-) [510.85]	340.33 (0.00) [36]
437	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2019]	264.68 (-) [264.68]	178.37 (0.00) [84]
	<u>Petroleum</u>				
438	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	17.78 (0.00) [0]
439	CITY GAS DISTRIBUTION (CGD) NETWORK,	10/2017	10/2022	221.45	27.11

	JAMSHEDPUR		(-) [10/2022]	(-) [221.45]	(0.00) [0]
440	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	27.55 (0.00) [0]
441	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	658.62 (910.23) [910.23]	115.49 (251.61) [-12]
442	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	4/2011	5/2015 (-) [0/0]	191.96 (-) [191.96]	176.28 (0.00) [0]
	<u>Power</u>				
443	NORTH KARANPURA STPP (3X660 MW)	2/2014	2/2019 (10/2020) [10/2020]	14,366.58 (-) [15,164.05]	7,916.41 (797.47) [20]
444	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,038.00 (314.04) [0]
	<u>Railways</u>				
445	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2021]	1,724.20 (1,724.20) [1,724.20]	198.68 (0.00) [9]
446	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	4/2010	12/2015 (12/2018) [2/2019]	309.44 (-) [525.81]	516.38 (216.37) [38]
447	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	109.68 (0.00) [-3]
448	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (-) [3,020.94]	0.00 (1,987.87) [-]
449	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [0/0]	459.91 (-) [459.91]	221.54 (0.00) [0]
450	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	4/1995	3/2016 (-) [3/2020]	1,125.89 (-) [2,021.29]	2,021.29 (895.40) [48]
451	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	/ (12/2018) [1/2020]	258.20 (-) [365.00]	198.49 (106.80) [-]
452	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [9/2019]	148.77 (-) [377.00]	161.29 (228.23) [33]
	<u>Road Transport And Highways</u>				
453	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [6/2019]	239.68 (-) [235.90]	63.21 (-3.78) [-9]
454	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [6/2019]	165.50 (-) [172.16]	24.21 (6.66) [-9]
455	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [0/0]	1,005.08 (-) [1,005.08]	0.00 (0.00) [0]
456	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [3/2019]	997.15 (-) [997.15]	376.26 (0.00) [0]
457	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
458	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-)	323.72 (-)	37.20 (0.00)

			[8/2019]	[323.72]	[12]
459	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
460	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
461	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [12/2019]	458.03 (-) [458.03]	20.00 (0.00) [-]
	<u>Steel</u>				
462	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	2/2014	9/2017 (-) [0/0]	4,749.00 (-) [4,749.00]	108.38 (0.00) [0]
463	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (-) [6/2019]	1,154.18 (-) [1,154.18]	878.27 (0.00) [18]
464	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (-) [6/2020]	1,034.01 (-) [1,034.01]	384.47 (0.00) [32]
465	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (-) [6/2020]	262.87 (-) [262.87]	78.83 (0.00) [12]
	<u>Urban Development</u>				
466	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [4/2020]	171.86 (-) [171.86]	41.28 (0.00) [49]
467	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
468	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
469	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
470	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
471	BSVI UPGRADATION	9/2016	12/2019 (-) [12/2019]	1,810.00 (1,810.00) [1,810.00]	130.79 (0.00) [0]
472	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [4/2019]	224.00 (207.00) [207.25]	99.99 (-16.75) [0]
473	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	803.00 (93.00) [0]
474	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (5/2019) [5/2019]	135.00 (170.70) [170.70]	129.95 (35.70) [2]
475	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	0.00 (0.00) [0]
476	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [3/2020]	581.00 (-) [581.00]	0.00 (0.00) [0]
477	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-)	993.00 (-)	1,549.85 (700.00)

			[0/0]	[1,693.00]	[0]
	<u>Power</u>				
478	KUDGI STPP STAGE 1	1/2012	1/2017 (-) [0/0]	15,166.19 (-) [16,934.65]	15,364.00 (1,768.46) [0]
479	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (2/2019) [6/2019]	445.89 (445.89) [445.89]	243.46 (0.00) [4]
	<u>Railways</u>				
480	ARSIKERE-TUMKUR	3/2015	3/2020 (3/2020) [3/2020]	578.00 (578.00) [578.00]	465.12 (0.00) [0]
481	BAGALKOT-KUDACHI NL	4/2010	3/2016 (12/2023) [12/2023]	986.30 (986.30) [986.30]	288.01 (0.00) [93]
482	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (3/2024) [3/2024]	1,382.78 (1,382.78) [1,382.78]	7.35 (0.00) [264]
483	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (12/2023) [12/2023]	327.25 (367.77) [367.77]	0.31 (40.52) [-]
484	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (12/2023) [12/2023]	558.00 (692.43) [692.43]	0.00 (134.43) [-]
485	GADAG-WADI NL	4/2013	12/2018 (12/2024) [12/2024]	2,841.84 (2,841.84) [2,841.84]	39.98 (0.00) [72]
486	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,900.00]	1,255.49 (773.00) [0]
487	HUBLI- CHIKJAJUR	3/2015	3/2020 (3/2020) [3/2021]	1,156.94 (1,140.93) [1,140.93]	714.14 (-16.01) [12]
488	HUBLI-ANKOLA(NL),SWR	4/1997	/ (12/2024) [12/2024]	2,315.00 (-) [2,135.00]	144.75 (-180.00) [-]
489	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (889.52) [889.52]	433.71 (244.74) [36]
490	MARIKUPPAM - KUPPAM	4/2012	3/2016 (12/2023) [12/2023]	279.54 (279.54) [279.54]	25.88 (0.00) [93]
491	MUNIRABAD (GINGERA) -RAICHUR NL	4/2007	/ (-) [12/2023]	179.65 (1,350.91) [1,350.91]	927.55 (1,171.26) [-]
492	SHIMOGA-HARIHAR NL	4/2011	3/2016 (3/2024) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
493	TORANAGALLU-RANJITPURA DL	4/2011	/ (12/2023) [12/2023]	146.75 (167.50) [167.50]	0.34 (20.75) [-]
494	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (12/2023) [12/2023]	1,801.01 (1,801.01) [1,801.01]	14.24 (0.00) [-]
495	WHITE FIELD-KOLAR NL	4/2011	/ (12/2023) [12/2023]	348.85 (348.85) [348.85]	0.36 (0.00) [-]
	<u>Road Transport And Highways</u>				
496	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (-) [3/2019]	1,167.42 (-) [1,167.42]	207.31 (0.00) [0]

497	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	0.00 (0.00) [0]
498	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [3/2019]	1,655.01 (-) [1,655.01]	1,515.16 (0.00) [31]
499	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/ (-) [0/0]	720.69 (-) [720.69]	99.03 (0.00) [0]
500	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [7/2019]	701.40 (-) [701.40]	23.70 (0.00) [4]
501	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	11.30 (0.00) [20]
502	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [4/2019]	1,388.00 (-) [1,388.00]	950.40 (0.00) [8]
503	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	401.95 (0.00) [0]
504	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [3/2019]	946.00 (-) [946.00]	818.53 (0.00) [9]
505	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
506	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	460.33 (440.84) [3]
507	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [6/2020]	831.58 (-) [1,177.00]	121.00 (345.42) [3]
508	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,177.80]	0.00 (0.00) [0]
509	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [0/0]	1,995.34 (-) [1,995.34]	0.00 (0.00) [0]
510	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
511	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
512	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [12/2018]	709.00 (-) [709.00]	380.95 (0.00) [0]
513	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [8/2019]	950.69 (-) [950.69]	549.74 (0.00) [0]
<u>Urban Development</u>					
514	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
515	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
516	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]

517	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (9/2020) [9/2020]	246.31 (-) [246.31]	34.90 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
518	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [6/2019]	1,112.00 (-) [1,112.00]	108.79 (0.00) [0]
519	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [3/2019]	607.06 (-) [714.25]	352.66 (107.19) [17]
520	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	501.94 (-24.04) [8]
521	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [11/2019]	4,588.29 (5,245.96) [5,245.96]	2,627.83 (657.67) [15]
522	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	0.00 (0.00) [0]
	<u>Railways</u>				
523	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (-) [2,815.62]	254.53 (1,249.62) [0]
524	CHENGANNUR-CHINGAVANAM	4/2006	/ (-) [0/0]	191.72 (-) [369.83]	432.50 (178.11) [0]
525	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (-) [189.24]	6.70 (0.00) [0]
526	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (-) [252.96]	8.50 (0.00) [0]
527	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	2/2005	3/2014 (-) [0/0]	241.00 (-) [241.00]	294.63 (0.00) [0]
528	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
529	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [0/0]	1,431.90 (-) [1,431.90]	23.84 (0.00) [0]
530	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (-) [828.50]	0.08 (-171.50) [0]
	<u>Road Transport And Highways</u>				
531	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [4/2019]	845.24 (-) [845.24]	727.93 (0.00) [-]
532	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [4/2019]	804.97 (-) [804.97]	305.99 (0.00) [10]
533	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,124.11]	94.03 (0.00) [33]
534	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,424.77]	0.00 (0.00) [0]
535	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	1/2014	11/2017 (-) [0/0]	267.16 (352.00) [352.05]	201.35 (84.89) [0]

536	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [0/0]	255.75 (348.00) [348.43]	231.56 (92.68) [0]
537	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [3/2019]	617.00 (-) [617.00]	943.17 (0.00) [79]
	Shipping And Ports				
538	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	5/2016	5/2020 (-) [5/2020]	970.00 (-) [970.00]	249.81 (0.00) [0]
539	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA	7/2016	5/2021 (-) [5/2021]	1,799.00 (-) [1,799.00]	121.22 (0.00) [0]
	Urban Development				
540	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
541	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2019]	165.23 (-) [165.23]	58.85 (0.00) [77]
542	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [12/2019]	5,181.79 (-) [5,181.79]	0.00 (0.00) [29]
	MADHYA PRADESH				
	Coal				
543	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	112.26 (0.00) [0]
544	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
545	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
546	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2021]	1,186.64 (-) [203.82]	106.07 (-982.82) [-24]
547	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	17.67 (0.00) [0]
548	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	94.68 (0.00) [0]
549	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	236.49 (0.00) [0]
550	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	41.76 (0.00) [0]
551	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	24.21 (0.00) [0]
552	NIGAHU OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	3/2012 (-) [0/0]	259.40 (-) [486.57]	266.38 (227.17) [0]
553	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	114.73 (0.00) [0]
	Petroleum				
554	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR	8/2017	6/2020 (-)	236.00 (-)	11.66 (0.00)

	MS,HSD AND		[10/2020]	[236.00]	[4]
	<u>Power</u>				
555	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [2,104.21]	66.87 (0.00) [0]
556	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	9/2017 (6/2019) [6/2019]	11,638.55 (-) [12,865.92]	10,375.32 (1,227.37) [21]
557	KHARGONE STPP STAGE I (1320 MW)	3/2015	9/2019 (-) [9/2019]	9,870.51 (-) [11,148.86]	6,693.90 (1,278.35) [0]
558	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	1/2016	3/2017 (9/2018) [2/2019]	305.04 (305.04) [305.04]	237.11 (0.00) [23]
	<u>Railways</u>				
559	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2021]	1,370.00 (-) [1,370.00]	101.00 (0.00) [0]
560	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.85 (-) [1,485.85]	903.15 (0.00) [0]
561	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,101.16]	194.91 (717.37) [0]
562	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [2/2019]	585.93 (-) [1,420.39]	104.10 (834.46) [0]
563	CHHINDWARA-MANDLA FORT GC	3/2011	3/2012 (-) [3/2020]	556.54 (-) [1,342.46]	396.00 (785.92) [96]
564	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (-) [6/2020]	700.00 (-) [700.00]	1,055.19 (0.00) [0]
565	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [10/2021]	1,763.93 (-) [1,763.93]	0.00 (0.00) [19]
566	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2022]	582.13 (-) [1,260.61]	0.00 (678.48) [0]
567	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2022]	2,478.23 (-) [2,478.23]	112.07 (0.00) [0]
568	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [8/2019]	174.00 (-) [174.00]	140.94 (0.00) [5]
569	RAMGANJMUUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2021]	424.60 (-) [2,713.09]	898.83 (2,288.49) [0]
570	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (-) [3/2022]	3,503.69 (-) [1,030.29]	1,097.39 (-2,473.40) [0]
	<u>Road Transport And Highways</u>				
571	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN)	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	0.00 (0.00) [0]
572	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [3/2019]	227.49 (-) [227.49]	78.39 (0.00) [2]
573	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]

574	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [0/0]	990.61 (-) [990.61]	0.00 (0.00) [0]
575	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
576	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [0/0]	390.51 (-) [390.51]	43.25 (0.00) [0]
577	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	11/2011	2/2015 (-) [0/0]	670.82 (-) [670.82]	590.00 (0.00) [0]
578	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	5/2015 (-) [1/2020]	704.26 (-) [704.26]	5.21 (0.00) [56]
579	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	3/2013	2/2016 (-) [0/0]	257.80 (-) [257.80]	59.30 (0.00) [0]
580	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (-) [6/2019]	1,583.79 (-) [1,583.79]	1,469.10 (0.00) [5]
581	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [8/2020]	960.24 (-) [960.24]	0.00 (0.00) [-]
582	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [3/2019]	1,012.90 (-) [1,012.90]	1,042.73 (0.00) [36]
583	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [12/2018]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
584	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [3/2019]	928.83 (-) [928.83]	476.73 (0.00) [-]
585	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [5/2019]	794.30 (-) [794.30]	398.49 (0.00) [-]
586	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [3/2019]	795.76 (-) [795.76]	464.01 (0.00) [-]
587	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [3/2019]	810.22 (-) [810.22]	454.51 (0.00) [-]
588	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	118.92 (0.00) [27]
589	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	0.00 (0.00) [0]
590	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	6/2018 (-) [0/0]	927.54 (-) [927.54]	29.17 (0.00) [0]
591	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [0/0]	497.05 (-) [497.05]	0.00 (0.00) [0]
592	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
593	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [11/2018]	1,175.00 (-) [1,206.10]	1,342.77 (31.10) [0]
594	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN	11/2015	3/2018	628.45	20.74

	MADHYA PRADESH KM 11/400 TO 66/400		(-) [0/0]	(-) [628.45]	(0.00) [0]
595	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	2/2015	5/2017 (-) [0/0]	327.32 (-) [327.32]	142.73 (0.00) [0]
596	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	2/2015	7/2017 (-) [0/0]	377.83 (-) [377.83]	57.42 (0.00) [0]
597	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	6/2015	12/2017 (-) [0/0]	641.02 (-) [641.02]	89.88 (0.00) [0]
598	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	381.86 (-) [381.86]	252.03 (0.00) [0]
599	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
600	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	6/2015	5/2017 (-) [0/0]	532.49 (-) [532.49]	137.08 (0.00) [0]
601	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [0/0]	871.15 (-) [871.15]	332.25 (0.00) [0]
602	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [0/0]	511.83 (-) [511.83]	40.87 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Coal</u>				
603	ADASA UG TO OC	8/2015	3/2023 (3/2024) [3/2024]	288.90 (333.43) [333.43]	0.07 (44.53) [12]
604	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2019]	198.68 (-) [198.68]	254.72 (0.00) [0]
605	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	116.35 (0.00) [0]
606	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	238.47 (0.00) [0]
607	BHANEGAON OC	2/2015	3/2023 (2/2017) [3/2023]	187.94 (409.68) [409.68]	97.41 (221.74) [0]
608	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2019]	304.52 (-) [304.52]	129.79 (0.00) [0]
609	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	397.95 (0.00) [0]
610	GOKUL	11/2014	3/2018 (-) [3/2018]	267.67 (-) [267.67]	208.09 (0.00) [0]
611	KAMPTEE DEEP OC MINE	11/2015	3/2021 (9/2018) [3/2024]	277.65 (313.34) [313.34]	26.44 (35.69) [36]
612	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	258.23 (0.00) [0]
613	MAKARDHOKRA I OC	9/2014	3/2021 (-) [3/2021]	266.23 (-) [266.23]	143.29 (0.00) [0]

614	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	67.18 (0.00) [0]
615	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2019]	295.56 (-) [295.56]	88.13 (0.00) [0]
616	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	191.97 (0.00) [0]
617	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	105.38 (0.00) [0]
	<u>Fertilisers</u>				
618	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	50.89 (0.00) [0]
619	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	2/2016	12/2017 (1/2019) [2/2019]	482.85 (482.85) [482.85]	430.86 (0.00) [14]
620	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (4/2019) [4/2019]	197.79 (209.44) [209.44]	145.98 (11.65) [29]
	<u>Health And Family Welfare</u>				
621	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [2/2020]	582.99 (-) [582.99]	61.17 (0.00) [-]
622	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [3/2019]	274.19 (-) [274.19]	125.36 (0.00) [0]
	<u>Petroleum</u>				
623	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	58.33 (0.00) [0]
624	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (11/2019) [11/2019]	968.61 (968.61) [968.61]	668.42 (0.00) [0]
625	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	8.74 (0.00) [0]
626	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	14.11 (0.00) [3]
627	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	9.20 (0.00) [9]
628	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (3/2019) [3/2019]	861.79 (1,577.15) [1,577.15]	1,195.62 (715.36) [70]
629	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (11/2019) [11/2019]	546.15 (546.15) [546.15]	249.63 (0.00) [0]
630	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (11/2019) [11/2019]	511.30 (511.30) [511.30]	219.96 (0.00) [0]
631	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,006.83) [4,006.83]	1,671.49 (0.00) [0]
632	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (4,619.94) [4,619.94]	4,079.85 (0.00) [27]
633	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT	2/2016	2/2020	554.00	172.74

	TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY		(-) [2/2020]	(-) [554.00]	(0.00) [0]
634	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,842.42 (606.02) [57]
635	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	514.20 (0.00) [0]
636	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2019) [5/2019]	3,190.69 (-) [3,247.19]	2,123.52 (56.50) [13]
637	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	122.99 (0.00) [0]
638	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (3/2019) [3/2019]	6,068.80 (6,068.80) [5,296.93]	4,597.60 (-771.87) [-1]
639	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [7/2019]	4,199.00 (-) [4,199.00]	194.97 (0.00) [-8]
640	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	1,888.28 (0.00) [14]
641	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY	1/2017	5/2019 (5/2019) [5/2019]	474.15 (474.15) [474.15]	299.26 (0.00) [0]
642	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	112.87 (0.00) [0]
643	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	72.05 (0.00) [0]
	<u>Power</u>				
644	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
645	SOLAPUR STPP	3/2012	11/2016 (3/2019) [3/2019]	9,395.18 (-) [9,395.18]	9,026.43 (0.00) [28]
646	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	9/2010 (12/2018) [4/2019]	477.69 (738.48) [738.48]	687.26 (260.79) [103]
	<u>Railways</u>				
647	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [3/2019]	184.06 (199.12) [298.70]	245.23 (114.64) [0]
648	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2021]	2,271.50 (2,271.50) [3,712.50]	1,908.80 (1,441.00) [0]
649	AMRAVATI-NARKHER NL(CR)	6/1994	6/1999 (-) [0/0]	663.01 (668.34) [858.96]	716.90 (195.95) [0]
650	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2020]	495.44 (1,781.98) [1,781.98]	1,348.23 (1,286.54) [192]
651	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (2,081.27) [2,081.27]	22.72 (205.27) [0]
652	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	713.48 (-) [1,750.00]	1,648.33 (1,036.52) [0]

653	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.22 (0.00) [-9]
654	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [8,857.98]	0.16 (-1,110.02) [0]
655	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (2,449.91) [2,449.91]	95.95 (0.00) [0]
656	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2021]	792.89 (792.89) [792.89]	277.94 (0.00) [0]
657	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2023]	1,035.16 (1,035.16) [1,035.16]	27.86 (0.00) [12]
658	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [3/2019]	305.00 (-) [305.00]	253.94 (0.00) [0]
659	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
660	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2019]	5,300.00 (-) [7,986.04]	2,423.55 (2,686.04) [60]
661	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2024]	3,627.47 (3,627.47) [3,627.47]	357.71 (0.00) [0]
662	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
663	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (-) [3/2023]	1,908.51 (-) [2,686.63]	0.00 (778.12) [0]
664	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
665	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
666	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
667	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2021]	229.00 (-) [403.00]	36.28 (174.00) [0]
668	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2023]	637.95 (637.95) [637.95]	30.87 (0.00) [0]
669	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2022]	1,272.19 (1,272.19) [1,272.19]	172.35 (0.00) [0]
670	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (3,168.29) [3,168.29]	1,011.99 (0.00) [0]
671	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2022]	540.02 (540.02) [540.02]	175.86 (0.00) [0]
<u>Road Transport And Highways</u>					
672	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [5/2019]	2,288.18 (-) [2,288.18]	0.00 (0.00) [0]

673	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [5/2019]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
674	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [12/2018]	972.50 (-) [972.50]	1,485.01 (0.00) [0]
675	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [0/0]	607.00 (-) [607.00]	0.00 (0.00) [0]
676	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	0.00 (0.00) [0]
677	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [6/2019]	923.04 (-) [923.04]	662.12 (0.00) [31]
678	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
679	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [0/0]	1,071.61 (-) [1,071.61]	0.00 (0.00) [0]
680	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [7/2019]	446.17 (-) [446.17]	38.95 (0.00) [4]
681	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [8/2020]	1,098.06 (-) [1,160.64]	469.50 (62.58) [5]
682	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	0.00 (0.00) [0]
683	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	0.00 (0.00) [0]
684	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [9/2019]	400.25 (-) [400.25]	64.89 (0.00) [6]
685	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [0/0]	1,064.88 (-) [1,064.88]	0.00 (0.00) [0]
686	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [11/2020]	1,059.73 (-) [1,071.00]	197.98 (11.27) [44]
687	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [5/2020]	1,030.44 (-) [1,065.51]	420.38 (35.07) [2]
688	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (-) [1,043.28]	503.06 (54.94) [5]
689	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (-) [4/2019]	505.00 (-) [505.00]	331.17 (0.00) [11]
690	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	16.75 (0.00) [0]
691	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60	3/2016	7/2018 (-) [0/0]	244.00 (-) [244.00]	0.00 (0.00) [0]
692	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [0/0]	1,162.92 (-) [1,162.92]	0.00 (0.00) [0]
693	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING	12/2015	3/2019	649.50	174.43

	ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN		(-) [12/2019]	(-) [649.50]	(0.00) [9]
694	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/	291.53	0.00
			(-) [0/0]	(-) [291.53]	(0.00) [0]
695	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019	244.90	175.56
			(-) [7/2019]	(-) [244.90]	(0.00) [2]
696	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/	289.21	0.00
			(-) [0/0]	(-) [289.21]	(0.00) [0]
697	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018	593.26	45.11
			(-) [4/2019]	(-) [593.26]	(0.00) [11]
698	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/	156.26	65.16
			(-) [0/0]	(227.00) [156.26]	(0.00) [0]
699	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	3/2011	/	185.82	205.97
			(-) [0/0]	(292.00) [185.82]	(0.00) [0]
700	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018	531.13	163.10
			(-) [5/2019]	(-) [531.13]	(0.00) [12]
701	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/	168.30	13.43
			(-) [0/0]	(-) [168.30]	(0.00) [0]
702	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	8/2014	7/2016	187.79	57.60
			(-) [0/0]	(-) [187.79]	(0.00) [0]
703	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020	247.02	0.00
			(-) [3/2020]	(-) [157.49]	(-89.53) [0]
704	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018	414.51	447.91
			(-) [3/2019]	(-) [414.00]	(-0.51) [10]
705	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020	296.19	202.79
			(-) [6/2019]	(-) [254.00]	(-42.19) [9]
706	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012	1,170.52	2,047.41
			(-) [12/2018]	(-) [1,170.52]	(0.00) [0]
707	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/	642.13	0.00
			(-) [0/0]	(-) [642.13]	(0.00) [0]
708	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018	1,871.34	3,235.12
			(-) [2/2019]	(-) [1,871.34]	(0.00) [13]
709	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020	904.16	260.79
			(-) [5/2020]	(-) [904.16]	(0.00) [3]
710	NAGPUR - KONDHALI	9/2005	6/2006	168.00	226.24
			(-) [0/0]	(-) [168.00]	(0.00) [0]
711	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019	546.00	460.55
			(-) [7/2019]	(-) [546.00]	(0.00) [0]
712	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019	591.66	608.89
			(-) [7/2019]	(-) [591.66]	(0.00) [0]
713	PANVEL-INDAPUR	12/2011	6/2014	942.69	688.86
			(-)	(-)	(0.00)

			[6/2019]	[942.69]	[60]
714	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [6/2019]	1,724.55 (-) [1,724.55]	2,264.75 (0.00) [75]
715	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00	12/2013	11/2016 (-) [0/0]	220.72 (-) [220.72]	95.02 (0.00) [0]
716	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337	6/2014	11/2016 (-) [0/0]	260.39 (-) [260.39]	87.43 (0.00) [0]
717	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	87.62 (0.00) [0]
718	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	1/2014	11/2014 (-) [0/0]	292.98 (-) [292.98]	95.60 (0.00) [0]
719	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	6.50 (0.00) [0]
720	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [0/0]	404.94 (-) [404.94]	0.00 (0.00) [0]
721	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [5/2019]	290.73 (-) [290.73]	101.84 (0.00) [-]
722	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	0.00 (0.00) [0]
723	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [6/2019]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [64]
	<u>Shipping And Ports</u>				
724	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	1/2007	12/2010 (-) [0/0]	366.39 (669.46) [669.46]	413.91 (303.07) [0]
	<u>Telecommunications</u>				
725	MADHYA PRADESH ACCESS (LOT1)	8/2017	5/2018 (2/2019) [2/2019]	215.30 (214.10) [214.10]	33.46 (-1.20) [9]
726	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (2/2019) [2/2019]	231.80 (231.80) [231.80]	117.63 (0.00) [4]
	<u>Urban Development</u>				
727	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2018) [9/2020]	223.37 (-) [223.37]	13.00 (0.00) [2]
728	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
729	NAGPUR METRO RAIL	8/2014	3/2018 (12/2019) [12/2019]	8,680.00 (8,680.00) [8,680.00]	4,898.72 (0.00) [21]
730	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (-) [11,420.00]	2,024.91 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
731	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	8,350.11 (9,354.83) [108]
	<u>Urban Development</u>				

732	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [11/2019]	216.69 (-) [216.69]	52.00 (0.00) [56]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
733	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (9/2019) [9/2019]	363.99 (-) [363.99]	145.51 (0.00) [16]
	<u>Railways</u>				
734	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [6,000.00]	260.10 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
735	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
736	JORBAT - BARAPANI	1/2011	1/2014 (-) [1/2019]	536.00 (-) [536.00]	839.86 (0.00) [60]
737	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [3/2019]	479.20 (-) [479.20]	470.59 (0.00) [10]
738	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	<u>Urban Development</u>				
739	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
740	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,968.00]	2,541.80 (2,574.53) [81]
	<u>Road Transport And Highways</u>				
741	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
742	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
743	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
744	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	16.00 (0.00) [0]
745	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	91.22 (0.00) [0]
746	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	58.04 (0.00) [0]
	<u>Heavy Industry</u>				
747	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	4/2011	9/2011 (6/2019) [0/0]	1,718.00 (3,727.30) [3,827.30]	2,933.23 (2,109.30) [0]
	<u>Petroleum</u>				
748	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017	500.00	0.00

			(-) [0/0]	(-) [500.00]	(0.00) [0]
749	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (-) [1,823.00]	579.41 (0.00) [0]
750	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	44.43 (0.00) [0]
751	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	19.60 (0.00) [0]
752	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,028.31 (0.00) [0]
753	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	6/2007	9/2011 (-) [0/0]	736.65 (-) [571.47]	543.05 (-165.18) [0]
754	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,002.53 (0.00) [0]
755	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	60.42 (0.00) [0]
756	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [3/2019]	890.00 (-) [887.00]	579.18 (-3.00) [-7]
757	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2019) [6/2019]	2,915.00 (3,030.00) [5,751.00]	2,038.08 (2,836.00) [78]
758	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2019 (12/2020) [12/2019]	2,881.40 (-) [2,000.00]	1,112.98 (-881.40) [0]
759	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,048.00 (0.00) [0]
760	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	1,213.52 (1,017.00) [-4]
761	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (10/2020) [10/2020]	690.00 (-) [690.00]	201.34 (0.00) [27]
762	PARADIP-RAIPUR- RANCHI PIPELINE	8/2009	12/2016 (-) [0/0]	1,793.00 (-) [1,793.00]	1,788.86 (0.00) [0]
763	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	3/2015	12/2018 (-) [3/2019]	3,957.00 (3,561.00) [3,397.00]	2,382.96 (-560.00) [3]
764	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	26.81 (0.00) [0]
765	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)	11/2016	2/2019 (-) [2/2019]	230.00 (-) [230.00]	122.05 (0.00) [0]
766	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [6/2019]	352.56 (-) [438.84]	199.43 (86.28) [27]
767	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (2/2019) [2/2019]	309.81 (723.40) [723.40]	610.73 (413.59) [52]
	<u>Power</u>				
768	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH)	9/2017	9/2019	198.49	22.80

	LINE CKT II (INDIA PORTION)		(2/2020) [2/2020]	(198.49) [198.49]	(0.00) [5]
769	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	3/2014	3/2016 (9/2018) [2/2019]	155.57 (206.42) [206.42]	145.82 (50.85) [35]
770	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	3/2013	12/2015 (-) [0/0]	2,514.88 (-) [3,190.27]	2,281.28 (675.39) [0]
771	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (12/2018) [12/2019]	4,754.42 (4,754.42) [9,141.97]	993.85 (4,387.55) [12]
772	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (5/2020) [5/2020]	358.83 (358.83) [358.83]	0.70 (0.00) [0]
773	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (9/2018) [3/2019]	196.58 (225.28) [225.28]	151.02 (28.70) [37]
774	EASTERN REGION STRENGTHENING SCHEME XI	5/2016	11/2018 (11/2018) [2/2019]	766.21 (766.21) [766.21]	456.84 (0.00) [3]
775	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (12/2018) [6/2019]	1,364.52 (1,891.41) [1,891.41]	1,221.08 (526.89) [38]
776	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2019) [12/2019]	522.29 (55,018.00) [550.18]	446.23 (27.89) [37]
777	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	789.25 (0.00) [0]
778	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (6/2019) [6/2019]	235.53 (235.53) [235.53]	64.79 (0.00) [0]
779	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (2/2019) [3/2019]	322.30 (322.30) [322.30]	127.38 (0.00) [1]
780	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [3/2019]	197.40 (197.40) [197.40]	74.71 (0.00) [12]
781	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (5/2019) [5/2019]	3,519.59 (3,519.59) [3,519.59]	2,129.90 (0.00) [0]
782	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	4/2015	4/2018 (9/2018) [2/2019]	3,705.61 (3,705.61) [3,705.61]	2,572.10 (0.00) [10]
783	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (4/2020) [4/2020]	5,070.13 (5,070.13) [5,070.13]	1,289.31 (0.00) [0]
784	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (11/2019) [11/2019]	14,733.37 (14,733.37) [14,733.37]	5,633.65 (0.00) [0]
785	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (2/2020) [2/2020]	1,931.39 (1,931.39) [1,931.39]	672.49 (0.00) [0]
786	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (6/2019) [6/2019]	251.60 (251.60) [251.60]	152.51 (0.00) [0]
787	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (12/2018) [12/2019]	5,111.33 (5,111.33) [6,652.57]	1,035.32 (1,541.24) [12]
788	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022)	11,130.19 (13,762.80)	12,727.30 (2,632.61)

			[3/2022]	[13,762.80]	[103]
789	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	2/2014	6/2016 (9/2018) [6/2019]	539.82 (539.82) [539.82]	424.53 (0.00) [36]
790	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA	3/2017	3/2019 (3/2019) [3/2019]	162.31 (162.31) [162.31]	92.40 (0.00) [0]
791	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN	7/2016	3/2019 (3/2019) [3/2019]	333.17 (333.17) [333.17]	257.53 (0.00) [0]
792	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION	8/2016	2/2019 (2/2019) [3/2019]	431.89 (431.89) [431.89]	231.96 (0.00) [1]
793	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (11/2019) [11/2019]	283.72 (283.72) [283.72]	139.25 (0.00) [0]
794	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (3/2019) [3/2019]	562.25 (562.25) [562.25]	140.30 (0.00) [0]
795	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [4/2019]	3,654.00 (-) [3,654.00]	2,973.90 (0.00) [0]
796	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (4/2019) [4/2019]	608.24 (608.24) [608.24]	382.10 (0.00) [0]
797	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [6/2019]	203.28 (260.03) [260.03]	187.46 (56.75) [23]
798	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (12/2019) [12/2019]	379.95 (379.95) [379.95]	22.22 (0.00) [0]
799	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (6/2019) [6/2019]	337.75 (337.75) [337.75]	31.80 (0.00) [0]
800	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION	1/2016	7/2018 (-) [0/0]	1,455.47 (-) [1,455.47]	1,028.69 (0.00) [0]
801	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	8/2014 (9/2018) [2/2019]	297.33 (534.02) [534.02]	441.88 (236.69) [54]
802	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (12/2018) [6/2019]	487.49 (639.46) [639.46]	512.80 (151.97) [60]
803	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2018) [6/2019]	4,824.12 (5,071.94) [5,071.94]	4,547.47 (247.82) [80]
804	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP	1/2015	3/2018 (9/2018) [2/2019]	268.80 (340.88) [340.88]	244.80 (72.08) [11]
805	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [9/2019]	871.62 (871.62) [871.62]	462.92 (0.00) [23]
806	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (1/2019) [6/2019]	408.46 (408.46) [408.46]	204.44 (0.00) [5]
807	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (3/2019) [8/2019]	5,151.37 (5,151.37) [5,151.37]	2,937.30 (0.00) [17]
808	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (3/2019) [9/2019]	808.63 (808.63) [808.63]	416.66 (0.00) [20]

809	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [3/2019]	374.63 (374.63) [374.63]	187.24 (0.00) [35]
810	WESTERN REGION STRENGTHENING SCHEME XVII	2/2017	9/2019 (9/2019) [3/2019]	204.12 (204.12) [204.12]	109.57 (0.00) [-6]
811	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (2/2020) [2/2020]	195.05 (195.05) [195.05]	103.60 (0.00) [0]
	<u>Railways</u>				
812	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	1,425.36 (0.00) [0]
813	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH	4/2010	/ (-) [0/0]	338.54 (-) [338.54]	212.64 (0.00) [0]
814	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [0/0]	288.35 (-) [238.36]	291.43 (-49.99) [0]
815	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [0/0]	450.55 (-) [250.55]	19.82 (-200.00) [0]
816	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (704.31) [704.31]	119.69 (0.00) [0]
817	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [1,787.00]	2.46 (863.77) [0]
818	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [0/0]	175.80 (-) [173.91]	153.48 (-1.89) [0]
819	CALICUT-MANGALORE (DL) (SR)	2/1996	/ (-) [0/0]	240.00 (-) [579.37]	537.30 (339.37) [0]
820	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	229.95 (1,211.86) [0]
821	CHANDIGARH-BADDI NL	4/2007	/ (-) [0/0]	328.14 (-) [1,540.00]	45.20 (1,211.86) [0]
822	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [0/0]	337.96 (-) [355.44]	72.84 (17.48) [0]
823	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,350.00]	2.27 (1,826.48) [0]
824	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	192.85 (182.31) [12]
825	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	100.47 (651.22) [0]
826	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [5/2010]	595.51 (-) [538.37]	109.04 (-57.14) [0]
827	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (-) [3/2022]	1,347.26 (-) [1,347.26]	611.28 (0.00) [0]
828	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (-) [3/2022]	1,640.04 (-) [1,640.04]	608.62 (0.00) [0]

829	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [0/0]	365.17 (-) [296.43]	134.36 (-68.74) [0]
830	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR	4/2013	/	1,239.00	0.00
			(-) [0/0]	(-) [1,239.00]	(0.00) [0]
831	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/	336.91	143.18
			(-) [0/0]	(-) [336.91]	(0.00) [0]
832	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013	607.09	634.43
			(-) [0/0]	(-) [607.91]	(0.82) [0]
833	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR	4/2010	/	2,030.50	10.34
			(-) [12/2022]	(-) [2,030.50]	(0.00) [-]
834	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (3/2024) [3/2024]	651.00 (-) [1,009.00]	7.96 (358.00) [108]
835	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/	11,589.00	0.00
			(-) [0/0]	(30,357.00) [28,181.00]	(16,592.00) [0]
836	GAYA-CHATRA (NL)	4/2008	/	415.67	14.62
			(-) [0/0]	(-) [549.75]	(134.08) [0]
837	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020	511.86	967.96
			(-) [4/2020]	(-) [1,756.00]	(1,244.14) [0]
838	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/	636.38	0.00
			(-) [0/0]	(-) [636.38]	(0.00) [0]
839	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	4/1986	3/1994	158.77	629.43
			(-) [0/0]	(274.56) [634.48]	(475.71) [0]
840	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022	2,912.96	1.92
			(-) [3/2022]	(-) [3,845.60]	(932.64) [0]
841	HAJIPUR - BACHAWARA	5/2015	3/2019	678.54	0.00
			(-) [3/2020]	(-) [678.54]	(0.00) [12]
842	HANSDIHA-GODDA NL	4/2011	3/2020	542.18	331.05
			(-) [3/2020]	(-) [542.18]	(0.00) [0]
843	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/	172.03	10.84
			(-) [0/0]	(-) [260.10]	(88.07) [0]
844	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022	230.03	231.72
			(-) [5/2019]	(-) [770.08]	(540.05) [-43]
845	HOTGI-KUDGI-GADAG	3/2015	3/2019 (3/2021) [3/2021]	1,614.59 (1,870.41) [1,870.41]	787.72 (255.82) [24]
846	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018	157.94	50.69
			(-) [0/0]	(-) [157.94]	(0.00) [0]
847	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	246.00
			(-) [0/0]	(-) [166.89]	(0.00) [0]
848	JAKHAL-MANSA DOUBLING ON SPR SECTION	4/2008	/	162.96	153.31
			(-) [0/0]	(-) [162.96]	(0.00) [0]
849	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016	625.00	0.00

			(-) [0/0]	(-) [845.58]	(220.58) [0]
850	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	3/2002	6/2007 (-) [0/0]	625.30 (408.76) [876.10]	841.57 (250.80) [0]
851	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (3/2023) [3/2023]	2,132.77 (-) [2,132.77]	217.64 (0.00) [108]
852	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (2/2010) [2/2010]	923.52 (-) [792.27]	337.16 (-131.25) [0]
853	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [0/0]	174.56 (-) [175.99]	57.52 (1.43) [0]
854	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	4/1999	/ (-) [0/0]	744.71 (-) [1,126.79]	751.05 (382.08) [0]
855	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2021]	2,063.03 (-) [2,063.03]	401.52 (0.00) [0]
856	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [2,200.00]	229.44 (343.05) [12]
857	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (-) [457.08]	317.14 (186.94) [0]
858	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [1/2006]	406.99 (-) [544.72]	147.26 (137.73) [0]
859	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [6,093.31]	972.82 (5,845.65) [178]
860	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [0/0]	257.42 (-) [258.73]	113.58 (1.31) [0]
861	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [3/2019]	120.70 (-) [1,800.00]	112.10 (1,679.30) [0]
862	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRHAT-KULPI NL	4/2009	2/2012 (12/2013) [12/2013]	499.96 (-) [665.75]	149.69 (165.79) [0]
863	MIRAJ-LONDA	3/2015	/ (3/2021) [3/2021]	1,830.00 (1,190.92) [1,190.92]	207.68 (-639.08) [-]
864	MM FROM BURAMARA-CHAKULIA	4/2008	0/0 (12/2024) [12/2024]	466.48 (-) [1,000.00]	0.83 (533.52) [-]
865	MONIGRAM- NIMTITA	4/2012	/ (-) [0/0]	250.93 (-) [259.23]	208.85 (8.30) [0]
866	MUNEERABAD-MAHABOONNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2019]	1,723.00 (1.00) [645.00]	734.72 (-1,078.00) [228]
867	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	121.37 (246.16) [0]
868	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [0/0]	450.00 (-) [2,100.00]	484.14 (1,650.00) [0]
869	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-	4/2010	3/2005 (-)	494.54 (-)	32.00 (-1.86)

	BAHRAHAT NL		[0/0]	[492.68]	[0]
870	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	65.88 (228.78) [0]
871	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [0/0]	241.52 (-) [394.28]	148.33 (152.76) [0]
872	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [3/2019]	1,798.00 (-) [1,798.00]	0.00 (0.00) [0]
873	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
874	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2019]	1,180.19 (2,531.34) [3,040.00]	3,109.99 (1,859.81) [123]
875	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	3.58 (85.99) [25]
876	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [0/0]	261.38 (-) [332.14]	378.90 (70.76) [0]
877	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2022]	915.98 (-) [915.96]	319.61 (-0.02) [0]
878	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [0/0]	299.60 (-) [299.60]	1.12 (0.00) [0]
879	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	3/1998	/ (-) [0/0]	280.00 (-) [1,122.00]	834.87 (842.00) [0]
880	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [2,878.97]	183.61 (796.22) [0]
881	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	2,062.30 (2,062.30) [2,062.20]	758.09 (-0.10) [-]
882	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE	4/2010	/ (-) [0/0]	268.52 (-) [268.52]	78.81 (0.00) [0]
883	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL	4/2000	/ (-) [0/0]	297.47 (-) [299.03]	53.11 (1.56) [0]
884	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2020]	277.28 (-) [266.52]	137.93 (-10.76) [48]
885	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (12/2023) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
886	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [0/0]	450.00 (-) [288.85]	9.31 (-161.15) [0]
887	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [0/0]	365.17 (-) [527.54]	1.73 (162.37) [0]
888	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
889	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	4/2013	/ (-) [0/0]	876.00 (-) [876.00]	0.00 (0.00) [0]

890	YELAHANKA-PENUKONDA	5/2015	3/2020 (3/2020) [3/2020]	860.43 (860.43) [860.43]	655.86 (0.00) [0]
	<u>Road Transport And Highways</u>				
891	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
892	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	3,000.11 (1,016.78) [0]
893	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
894	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,294.47]	0.00 (0.00) [0]
895	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [998.70]	0.00 (0.00) [0]
896	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [8/2020]	604.00 (-) [604.00]	423.83 (0.00) [128]
897	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [12/2019]	754.00 (-) [754.00]	1,363.43 (0.00) [81]
898	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	85.00 (0.00) [-]
899	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,675.28 (0.00) [0]
900	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2019]	2,848.00 (-) [2,848.00]	1,141.90 (0.00) [69]
901	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	3/2015	/ (-) [0/0]	789.83 (-) [789.83]	109.77 (0.00) [0]
	<u>Telecommunications</u>				
902	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	8,397.00 (11,330.00) [58]
903	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
904	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
905	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (10/2021) [10/2021]	2,326.52 (2,446.57) [3,000.00]	696.02 (673.48) [79]
	<u>Road Transport And Highways</u>				
906	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
907	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
908	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM	3/2018	9/2018 (-)	282.98 (-)	0.00 (0.00)

	EXISTING KM 40.090 TO KM65.		[0/0]	[282.98]	[0]
909	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	0.00 (0.00) [0]
910	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
911	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
912	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
913	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	0.00 (0.00) [0]
914	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]
915	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	0.00 (0.00) [0]
916	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
917	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
918	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
919	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	0.00 (0.00) [0]
920	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	0.00 (0.00) [0]
921	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
922	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
923	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
924	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
925	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	235.51 (0.00) [108]
926	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2020]	172.08 (-) [172.08]	267.99 (0.00) [120]
927	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	123.19 (0.00) [60]
928	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017	490.10	421.62

			(-) [3/2020]	(-) [490.10]	(0.00) [36]
929	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	425.28 (0.00) [0]
930	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2020]	479.53 (-) [479.53]	397.41 (0.00) [84]
931	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	0.00 (0.00) [0]
932	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2021]	337.66 (-) [337.66]	65.58 (0.00) [24]
933	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2020]	457.77 (-) [457.77]	584.87 (0.00) [84]
934	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	30.04 (0.00) [24]
935	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2018]	302.96 (-) [302.96]	302.96 (0.00) [0]
936	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	690.11 (0.00) [0]
	Mines				
937	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	96.98 (0.00) [0]
938	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	31.92 (0.00) [0]
939	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.00 (0.00) [0]
940	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	302.60 (0.00) [0]
	Petroleum				
941	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	26.58 (0.00) [0]
942	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	3.37 (0.00) [0]
943	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (243.53) [243.53]	34.34 (0.00) [0]
944	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	181.20 (-) [181.20]	17.11 (0.00) [0]
945	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	864.97 (0.00) [0]
946	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [7/2021]	5,654.00 (-) [4,807.08]	24.09 (-846.92) [-3]
947	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [1/2019]	429.00 (-) [429.00]	283.06 (0.00) [0]

948	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	34.31 (0.00) [0]
949	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	0.02 (0.00) [0]
950	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (12/2018) [12/2018]	3,150.00 (-) [3,150.00]	2,494.51 (0.00) [0]
	<u>Power</u>				
951	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	8/2018 (6/2019) [6/2019]	12,532.44 (-) [13,740.53]	8,441.41 (1,208.09) [10]
952	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (-) [4/2019]	844.64 (844.64) [844.64]	326.60 (0.00) [0]
	<u>Railways</u>				
953	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [1,120.00]	910.97 (177.05) [24]
954	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2021]	843.04 (-) [843.04]	81.26 (0.00) [5]
955	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2021]	1,172.92 (-) [1,172.92]	245.16 (0.00) [27]
956	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
957	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2020]	5,200.00 (-) [5,200.00]	0.00 (0.00) [0]
958	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,458.49 (658.83) [27]
959	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	1,547.38 (-) [1,547.38]	189.40 (0.00) [0]
960	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2021]	701.61 (-) [810.02]	88.04 (108.41) [28]
961	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [2/2019]	133.41 (207.00) [385.00]	377.10 (251.59) [119]
962	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [6/2021]	2,923.13 (-) [3,798.80]	1,123.73 (875.67) [147]
963	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2022]	2,361.74 (-) [2,361.74]	81.06 (0.00) [0]
964	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [6/2020]	969.83 (-) [1,151.81]	403.78 (181.98) [3]
965	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	4/1995	12/2021 (12/2024) [12/2024]	524.43 (-) [939.00]	184.10 (414.57) [36]
966	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2020]	155.81 (-) [238.03]	180.78 (82.22) [0]
967	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-)	948.04 (-)	1,009.91 (154.96)

			[3/2020]	[1,103.00]	[0]
968	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2021]	1,111.99 (-) [1,539.28]	765.60 (427.29) [25]
969	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (245.00) [1,202.70]	706.84 (0.00) [82]
970	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2023]	810.78 (-) [1,928.07]	574.98 (1,117.29) [21]
971	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (2,335.67) [2,335.67]	355.05 (0.00) [0]
	Road Transport And Highways				
972	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [4/2020]	1,282.94 (-) [1,282.94]	0.00 (0.00) [-]
973	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [8/2019]	2,510.04 (-) [2,510.04]	0.00 (0.00) [0]
974	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
975	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016 (-) [0/0]	319.80 (320.00) [320.00]	0.00 (0.20) [0]
976	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016 (-) [0/0]	319.80 (-) [319.80]	0.00 (0.00) [0]
977	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [6/2019]	1,069.65 (-) [1,069.65]	0.00 (0.00) [-]
978	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [3/2019]	1,410.00 (-) [1,410.00]	1,555.96 (0.00) [54]
979	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [7/2020]	1,008.96 (-) [1,008.96]	32.50 (0.00) [-]
980	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [0/0]	564.66 (-) [564.66]	0.00 (0.00) [0]
981	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [11/2020]	476.56 (-) [476.56]	0.00 (0.00) [40]
982	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
983	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [0/0]	953.09 (-) [953.09]	0.00 (0.00) [0]
984	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [0/0]	668.86 (-) [668.86]	0.00 (0.00) [0]
985	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [0/0]	614.48 (-) [614.48]	0.00 (0.00) [0]
986	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	0.00 (0.00) [0]
987	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM.	1/2018	/ (-)	1,522.00 (-)	0.00 (0.00)

	62.000 TO KM		[0/0]	[1,522.00]	[0]
988	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [0/0]	503.88 (-) [503.88]	0.00 (0.00) [0]
989	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2020]	1,288.07 (-) [1,420.00]	0.00 (131.93) [0]
990	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
991	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
992	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [0/0]	417.51 (-) [417.51]	0.00 (0.00) [0]
993	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	0.00 (-0.05) [0]
994	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [0/0]	999.00 (-) [999.00]	0.00 (0.00) [0]
995	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	0.00 (0.04) [0]
996	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
997	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
998	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,613.62 (0.00) [0]
999	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [0/0]	806.11 (-) [806.11]	0.00 (0.00) [0]
1000	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	3/2014	5/2016 (-) [0/0]	162.51 (163.00) [163.00]	0.00 (0.49) [0]
1001	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	0.00 (0.50) [0]
1002	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [240.00]	0.00 (0.09) [0]
1003	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [327.00]	0.00 (0.37) [0]
1004	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.00]	0.00 (-0.30) [0]
1005	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	0.00 (0.00) [0]
1006	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	0.00 (0.00) [0]
1007	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	3/2015	10/2017 (-) [0/0]	226.31 (226.00) [226.00]	0.00 (-0.31) [0]

	<u>Steel</u>				
1008	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (-) [5/2019]	3,127.30 (-) [3,127.30]	2,638.63 (0.00) [13]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1009	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	27.56 (0.00) [0]
1010	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	32.53 (0.00) [0]
	<u>Health And Family Welfare</u>				
1011	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [6/2020]	703.00 (-) [703.00]	272.00 (0.00) [0]
1012	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (2/2018) [6/2019]	152.95 (-) [152.95]	95.16 (0.00) [16]
	<u>Railways</u>				
1013	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	4/2009	/ (-) [0/0]	396.04 (-) [369.00]	186.27 (-27.04) [0]
1014	QADIAN-BEAS	4/2011	/ (-) [0/0]	205.22 (-) [205.22]	3.18 (0.00) [0]
	<u>Road Transport And Highways</u>				
1015	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	/ (-) [0/0]	573.96 (605.00) [605.00]	209.74 (31.04) [0]
1016	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	2/2015	/ (-) [0/0]	486.74 (-) [486.74]	189.39 (0.00) [0]
1017	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (-) [1,169.61]	301.34 (0.00) [-]
1018	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	11/2014	/ (-) [0/0]	463.65 (546.00) [463.65]	280.16 (0.00) [0]
1019	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	2/2015	/ (-) [0/0]	483.38 (-) [483.38]	65.76 (0.00) [0]
1020	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	2/2015	/ (-) [0/0]	616.36 (-) [616.36]	68.58 (0.00) [0]
1021	4-LANING OF LAMBRA-SHAKHOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	299.81 (0.00) [0]
1022	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [889.24]	389.64 (0.00) [0]
1023	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [9/2019]	1,388.34 (-) [1,388.34]	670.70 (0.00) [0]
1024	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	3/2015	/ (-) [0/0]	312.79 (-) [312.79]	17.57 (0.00) [0]
1025	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K	7/2014	/ (-) [0/0]	319.80 (-) [319.80]	102.55 (0.00) [0]
1026	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED	3/2017	3/2020	754.54	57.93

	FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN		(-) [4/2020]	(-) [756.27]	(1.73) [1]
1027	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/	766.36	99.86
			(-) [0/0]	(-) [766.36]	(0.00) [0]
1028	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	12/2015	/	578.38	128.53
			(-) [0/0]	(-) [578.38]	(0.00) [0]
1029	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017	447.29	163.99
			(-) [4/2019]	(-) [447.29]	(0.00) [16]
1030	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/	261.76	0.00
			(-) [0/0]	(-) [261.76]	(0.00) [0]
1031	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	453.09
			(-) [3/2019]	(-) [479.00]	(0.00) [-]
1032	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	9/2015	/	273.06	161.79
			(-) [4/2019]	(-) [273.06]	(0.00) [-]
1033	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/	196.05	108.91
			(-) [1/2020]	(-) [196.05]	(0.00) [-]
1034	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/	199.90	0.00
			(-) [0/0]	(-) [199.90]	(0.00) [0]
1035	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	3/2015	/	435.90	31.02
			(-) [0/0]	(-) [435.90]	(0.00) [0]
1036	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	1/2015	/	279.68	25.28
			(-) [0/0]	(-) [279.68]	(0.00) [0]
1037	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	6/2015	/	899.21	25.08
			(-) [0/0]	(-) [899.21]	(0.00) [0]
1038	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/	892.17	26.92
			(-) [0/0]	(-) [892.17]	(0.00) [0]
	<u>Urban Development</u>				
1039	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017	388.00	394.49
			(2/2019) [3/2019]	(-) [486.54]	(98.54) [22]
1040	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	9/2018	430.00	39.43
			(-) [9/2018]	(-) [430.00]	(0.00) [0]
1041	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019	294.00	146.37
			(6/2019) [9/2019]	(-) [294.00]	(0.00) [5]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1042	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12,320.00	10,285.00
			(3/2017) [12/2020]	(-) [12,320.00]	(0.00) [48]
	<u>Coal</u>				
1043	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019	513.63	173.06
			(-) [12/2019]	(-) [513.63]	(0.00) [0]
1044	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019	522.45	8.71
			(-) [9/2019]	(-) [522.45]	(0.00) [0]
	<u>Petroleum</u>				

1045	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1046	LPG BP PROJECT JODHPUR	3/2018	/	229.80	69.04
			(-) [0/0]	(-) [229.80]	(0.00) [0]
	Power				
1047	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (1/2019) [3/2019]	1,429.38 (1,429.38) [1,429.38]	880.26 (0.00) [2]
1048	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	7/2015	11/2017 (10/2018) [2/2019]	307.18 (307.18) [307.18]	211.31 (0.00) [15]
	Railways				
1049	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/	873.71	2.69
			(-) [0/0]	(-) [1,103.04]	(229.33) [0]
1050	AJMER-BANGURGRAM	4/2011	11/2019 (-) [11/2019]	213.39 (-) [244.02]	225.69 (30.63) [0]
1051	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/	822.00	0.00
			(-) [0/0]	(-) [1,099.54]	(277.54) [0]
1052	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [5/2019]	242.09 (-) [349.00]	303.99 (106.91) [3]
1053	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [11/2019]	246.08 (-) [348.55]	144.17 (102.47) [-1]
1054	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [12/2019]	410.08 (780.98) [795.01]	467.29 (384.93) [10]
1055	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	4/2008	3/2015 (-) [10/2020]	829.74 (-) [1,216.00]	741.81 (386.26) [67]
1056	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	4/2008	3/2014 (5/2019) [5/2019]	653.19 (-) [1,116.00]	840.30 (462.81) [62]
1057	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	0.08 (0.00) [1]
1058	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [12/2019]	420.18 (295.02) [420.18]	96.91 (0.00) [-3]
1059	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [12/2019]	493.17 (-) [493.17]	415.31 (0.00) [21]
1060	PUSHKAR-MERTA	4/2013	/	323.00	0.00
			(-) [0/0]	(-) [432.22]	(109.22) [0]
1061	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [6/2019]	236.93 (-) [294.90]	167.81 (57.97) [8]
	Road Transport And Highways				
1062	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [1/2019]	597.00 (-) [597.00]	604.80 (0.00) [15]
1063	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [2/2019]	320.30 (-) [320.30]	193.54 (0.00) [1]
1064	2-LANE WITH PAVED SHOULDER WITH PROVISION OF	11/2012	8/2016	530.07	556.02

	CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA		(-) [2/2019]	(-) [530.07]	(0.00) [30]
1065	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [11/2019]	688.70 (-) [688.70]	490.54 (0.00) [-]
1066	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [8/2020]	1,031.95 (-) [1,031.95]	367.00 (0.00) [-]
1067	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [3/2019]	822.90 (-) [822.90]	703.00 (0.00) [11]
1068	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	0.00 (0.00) [0]
1069	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	0.00 (0.00) [0]
1070	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1071	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	0.00 (0.00) [0]
1072	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	155.03 (0.00) [5]
1073	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	0.00 (0.00) [3]
1074	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	0.00 (0.00) [0]
1075	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (9/2017) [3/2019]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [89]
1076	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1077	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1078	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	9/2015	3/2018 (-) [3/2019]	567.51 (-) [567.51]	53.70 (0.00) [12]
1079	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1080	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	1/1991	5/2016 (-) [0/0]	208.87 (-) [208.87]	206.78 (0.00) [0]
1081	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	1/1991	10/2016 (-) [0/0]	269.26 (-) [269.26]	212.72 (0.00) [0]
1082	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1083	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [12/2019]	1,100.19 (-) [1,100.19]	650.00 (0.00) [-]
1084	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM.	9/2016	/ (-)	1,239.82 (-)	734.18 (0.00)

	214.870 (		[5/2020]	[1,239.82]	[-]
1085	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [11/2019]	894.00 (-) [894.00]	15.00 (0.00) [-5]
1086	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (-) [3/2019]	425.19 (-) [425.19]	274.20 (0.00) [30]
1087	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [3/2019]	275.90 (-) [275.90]	256.10 (0.00) [-]
1088	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [11/2018]	331.46 (-) [331.46]	259.22 (0.00) [0]
1089	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	576.75 (0.00) [3]
1090	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	0.00 (0.00) [0]
1091	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [0/0]	1,103.88 (-) [1,103.88]	0.00 (0.00) [0]
1092	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.80 (0.00) [0]
1093	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [6/2019]	383.40 (-) [383.40]	224.68 (0.00) [51]
1094	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1095	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	0.00 (0.00) [0]
	<u>Urban Development</u>				
1096	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [0/0]	189.00 (-) [189.00]	0.00 (0.00) [0]
1097	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (-) [11/2019]	549.31 (-) [540.42]	234.59 (-8.89) [4]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1098	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
1099	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
1100	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
1101	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
1102	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	0.00 (0.00) [0]
1103	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM	11/2017	11/2017 (-)	290.05 (-)	18.12 (0.00)

	16.000 TO KM 32.5		[0/0]	[290.05]	[0]
1104	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	7.50 (0.00) [0]
1105	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1106	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1107	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	12,070.00 (0.00) [36]
1108	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2021]	3,492.00 (-) [6,100.00]	5,738.32 (2,608.00) [133]
	<u>Coal</u>				
1109	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (9/2019) [9/2019]	1,458.17 (709.06) [709.06]	400.53 (-749.11) [51]
1110	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (12/2018) [3/2019]	5,907.11 (-) [5,907.11]	5,892.64 (0.00) [39]
	<u>Mines</u>				
1111	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (-) [6/2019]	166.62 (166.62) [166.62]	134.00 (0.00) [0]
	<u>Petroleum</u>				
1112	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	1.84 (0.00) [0]
1113	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	646.29 (0.00) [0]
1114	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	1.18 (0.00) [10]
1115	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [12/2020]	4,497.00 (-) [4,497.00]	370.09 (0.00) [24]
1116	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1117	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (-) [4/2019]	390.52 (390.52) [390.52]	174.22 (0.00) [1]
1118	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [0/0]	678.00 (-) [678.00]	5.12 (0.00) [0]
1119	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	22.22 (0.00) [0]
1120	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.42 (0.00) [0]
	<u>Power</u>				
1121	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	9/2011	9/2014 (-) [0/0]	1,940.13 (-) [2,702.65]	2,529.92 (762.52) [0]

1122	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (9/2018) [3/2019]	1,779.29 (2,187.32) [2,187.32]	2,106.62 (408.03) [124]
1123	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (7/2019) [7/2019]	186.17 (186.17) [186.17]	64.27 (0.00) [0]
	Railways				
1124	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [3/2018]	257.00 (-) [257.00]	0.00 (0.00) [0]
1125	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [2/2019]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1126	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	4/1998	/ (-) [0/0]	271.24 (-) [520.00]	468.18 (248.76) [0]
1127	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	303.72 (357.96) [0]
1128	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	9/2006	/ (-) [0/0]	343.17 (-) [1,065.00]	1,049.68 (721.83) [0]
1129	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1130	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [3/2019]	495.74 (-) [734.01]	445.91 (238.27) [69]
1131	KARUR-SALEM(NL),SR	2/1997	/ (-) [0/0]	155.55 (-) [920.00]	856.94 (764.45) [0]
1132	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [3/2020]	760.00 (-) [1,182.31]	0.00 (422.31) [0]
1133	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION	2/1997	3/2015 (-) [0/0]	458.63 (-) [458.63]	0.92 (0.00) [0]
1134	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	83.15 (285.59) [-]
1135	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING	2/2003	3/2009 (-) [0/0]	199.55 (-) [330.32]	2.12 (130.77) [0]
1136	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION.	2/2006	3/2012 (-) [0/0]	208.00 (-) [208.00]	3.58 (0.00) [0]
1137	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [3/2022]	1,700.00 (-) [1,700.00]	0.00 (0.00) [0]
1138	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2019]	724.69 (-) [2,072.50]	1,169.07 (1,347.81) [0]
1139	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	7.62 (44.41) [71]
1140	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.61 (661.00) [0]
1141	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [302.02]	304.07 (33.15) [0]

1142	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [0/0]	582.83 (-) [2,300.00]	237.73 (1,717.17) [0]
1143	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [900.00]	61.97 (672.60) [0]
1144	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
1145	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	2/2000	3/2014 (-) [0/0]	200.84 (-) [200.84]	394.26 (0.00) [0]
1146	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	2/2005	3/2010 (-) [0/0]	600.00 (600.00) [645.54]	671.00 (45.54) [0]
	Road Transport And Highways				
1147	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [12/2018]	485.00 (-) [485.00]	406.68 (0.00) [0]
1148	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1149	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	0.00 (0.00) [0]
1150	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [0/0]	1,227.87 (-) [1,227.87]	0.00 (0.00) [0]
1151	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1152	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1153	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [0/0]	600.00 (-) [600.00]	325.55 (0.00) [0]
1154	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [0/0]	1,016.92 (-) [1,016.92]	0.00 (0.00) [0]
1155	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [5/2019]	1,387.11 (-) [1,387.11]	926.73 (0.00) [18]
1156	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [0/0]	628.71 (-) [628.71]	0.00 (0.00) [0]
1157	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,065.96]	0.00 (0.00) [0]
1158	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [0/0]	1,166.26 (-) [1,166.26]	0.00 (0.00) [0]
1159	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [4/2019]	641.17 (-) [641.17]	244.33 (0.00) [33]
1160	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [0/0]	505.35 (-) [505.35]	0.00 (0.00) [0]
1161	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [0/0]	1,176.37 (-) [1,176.37]	0.00 (0.00) [0]

1162	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [6/2019]	707.82 (-) [707.82]	235.70 (0.00) [10]
1163	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	21.72 (0.00) [0]
1164	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [4/2019]	641.17 (-) [641.17]	289.10 (0.00) [9]
1165	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1166	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [0/0]	379.90 (-) [379.90]	43.24 (0.00) [0]
1167	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [12/2018]	1,250.00 (-) [1,250.00]	1,329.49 (0.00) [0]
1168	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	11/2014	11/2016 (-) [0/0]	563.92 (-) [563.92]	186.50 (0.00) [0]
1169	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1170	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	627.47 (0.00) [0]
1171	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [12/2018]	374.00 (-) [374.00]	237.00 (0.00) [0]
1172	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [633.55]	0.00 (0.00) [0]
1173	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [6/2019]	563.92 (-) [563.92]	96.48 (0.00) [18]
<u>Shipping And Ports</u>					
1174	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017 (5/2020) [5/2020]	600.00 (257.90) [257.90]	1.45 (-342.10) [29]
1175	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017 (3/2018) [0/0]	244.50 (258.33) [271.56]	271.56 (27.06) [0]
1176	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006 (3/2016) [2/2019]	150.00 (600.00) [600.00]	550.78 (450.00) [155]
1177	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008 (-) [0/0]	2,427.40 (-) [2,427.40]	831.21 (0.00) [0]
<u>Urban Development</u>					
1178	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [10/2019]	209.00 (-) [209.00]	51.00 (0.00) [0]
1179	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1180	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.77 (4,458.00) [0]
1181	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-)	348.77 (-)	11.10 (0.00)

			[0/0]	[348.77]	[0]
1182	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	4/2014	9/2016 (-) [0/0]	332.72 (-) [342.00]	321.13 (9.28) [0]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1183	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	0.00 (0.00) [0]
1184	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2019]	426.79 (-) [426.79]	0.00 (0.00) [12]
1185	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2021]	447.06 (-) [437.51]	353.61 (-9.55) [72]
1186	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1187	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2019]	413.84 (-) [413.84]	0.00 (0.00) [0]
1188	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2019]	397.09 (-) [442.42]	79.96 (45.33) [0]
1189	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [384.32]	146.45 (-33.01) [44]
1190	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	12.69 (-78.25) [72]
1191	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	159.87 (0.00) [0]
1192	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	477.74 (70.65) [132]
1193	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	1.31 (186.52) [72]
1194	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2019]	430.45 (-) [415.37]	160.45 (-15.08) [36]
1195	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [3/2019]	365.01 (-) [365.01]	204.26 (0.00) [45]
1196	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2019]	209.78 (-) [209.78]	154.21 (0.00) [48]
1197	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2024]	249.03 (-) [448.86]	186.91 (199.83) [144]
	<u>Power</u>				
1198	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	7/2020 (10/2020) [10/2020]	10,598.98 (-) [10,598.98]	3,272.35 (0.00) [3]
	<u>Railways</u>				
1199	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (3/2017) [12/2020]	632.68 (-) [816.55]	618.31 (183.87) [57]
1200	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-)	636.38 (-)	169.16 (0.00)

			[3/2021]	[636.38]	[0]
1201	KONDAPALLI-KOTHAGUDEM	4/2013	/	723.00	0.00
			(-)	(-)	(-106.92)
			[0/0]	[616.08]	[0]
1202	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/	458.25	3.69
			(-)	(-)	(0.01)
			[0/0]	[458.26]	[0]
1203	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022	119.73	0.00
			(-)	(185.00)	(65.24)
			[3/2022]	[184.97]	[0]
1204	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010	1,160.48	130.50
			(-)	(-)	(-0.01)
			[3/2022]	[1,160.47]	[144]
1205	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92
			(-)	(-)	(1,799.84)
			[0/0]	[2,911.84]	[0]
1206	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024	773.94	250.05
			(-)	(-)	(0.00)
			[12/2024]	[773.94]	[0]
	<u>Road Transport And Highways</u>				
1207	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	1/2014	3/2016	340.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[340.00]	[0]
1208	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016	1,266.60	1,411.79
			(-)	(-)	(277.40)
			[6/2019]	[1,544.00]	[33]
1209	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	3/2011	12/2015	218.31	208.28
			(-)	(-)	(121.51)
			[0/0]	[339.82]	[0]
1210	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017	153.21	0.00
			(-)	(-)	(0.00)
			[0/0]	[153.21]	[0]
1211	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017	4,429.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[4,429.00]	[0]
1212	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/	857.62	0.00
			(-)	(-)	(0.00)
			[0/0]	[857.62]	[0]
1213	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/	802.65	0.00
			(-)	(-)	(0.00)
			[0/0]	[802.65]	[0]
1214	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/	950.63	0.00
			(-)	(-)	(0.00)
			[0/0]	[950.63]	[0]
1215	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/	828.29	0.00
			(-)	(-)	(0.00)
			[0/0]	[828.29]	[0]
1216	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018	1,423.96	544.89
			(-)	(-)	(0.00)
			[7/2019]	[1,423.96]	[8]
1217	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO	12/2013	3/2016	158.65	103.50
			(-)	(-)	(0.00)
			[0/0]	[158.65]	[0]
1218	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S	12/2013	3/2016	177.18	40.51
			(-)	(-)	(0.00)
			[0/0]	[177.18]	[0]
1219	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016	270.00	19.84
			(-)	(-)	(0.00)
			[0/0]	[270.00]	[0]
1220	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR	10/2014	2/2017	295.47	0.00
			(-)	(-)	(17.80)

	RUDRAMPUR		[0/0]	[313.27]	[0]
1221	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	10/2014	12/2016 (-) [0/0]	244.30 (-) [156.09]	0.00 (-88.21) [0]
1222	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW	12/2013	3/2016 (-) [0/0]	244.08 (-) [244.08]	38.32 (0.00) [0]
	<u>Urban Development</u>				
1223	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [3/2020]	209.84 (-) [209.84]	13.03 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Power</u>				
1224	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
1225	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (3,407.00) [3,407.00]	3,224.14 (2,265.00) [60]
1226	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
1227	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (984.97) [1,733.20]	1,553.74 (838.20) [0]
	<u>Road Transport And Highways</u>				
1228	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	261.24 (0.00) [0]
1229	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Urban Development</u>				
1230	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1231	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1232	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Coal</u>				
1233	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	6/2011	3/2018 (-) [3/2019]	1,131.28 (-) [1,131.28]	715.00 (0.00) [12]
1234	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	4,524.70 (0.80) [0]
	<u>Health And Family Welfare</u>				
1235	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [4/2020]	785.00 (-) [785.00]	39.35 (0.00) [0]
1236	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	68.33 (0.00) [-]
	<u>Petroleum</u>				
1237	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR	3/2018	12/2021 (-)	676.00 (-)	7.46 (0.00)

	PIPELINE A		[12/2021]	[676.00]	[0]
1238	AURAIYA PHULPUR PIPELINE PROJECT	7/2015	12/2018 (-) [3/2019]	1,427.94 (-) [800.00]	618.58 (-627.94) [3]
1239	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	264.64 (0.00) [0]
1240	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	106.74 (0.00) [0]
1241	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	0.10 (0.00) [0]
1242	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	13.93 (0.00) [3]
	<u>Power</u>				
1243	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (2/2018) [10/2019]	195.42 (294.60) [294.60]	232.92 (99.18) [68]
1244	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW)	7/2013	12/2016 (-) [0/0]	3,363.12 (-) [3,363.12]	2,244.00 (0.00) [0]
1245	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	12/2016 (-) [8/2019]	9,750.89 (-) [9,750.89]	8,798.00 (0.00) [32]
1246	TANDA TPP STAGE-II (2X660 MW)	9/2014	3/2019 (9/2019) [9/2019]	9,188.98 (-) [9,188.98]	5,433.65 (0.00) [6]
	<u>Railways</u>				
1247	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	4/1999	12/2009 (-) [0/0]	108.00 (-) [432.72]	446.52 (324.72) [0]
1248	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [308.00]	0.00 (1.00) [0]
1249	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2020]	600.00 (-) [366.71]	0.46 (-233.29) [-24]
1250	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	3/2012	8/2018 (-) [1/2019]	199.75 (-) [270.00]	267.76 (70.25) [5]
1251	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1252	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	923.92 (0.00) [3]
1253	BHOJIPUR TANAKPUR VIA PILIBHIT	3/2008	/ (-) [3/2018]	195.64 (-) [435.00]	457.93 (239.36) [0]
1254	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	0.00 (111.84) [0]
1255	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1256	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1257	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008	120.00	210.67

			(-) [0/0]	(-) [245.39]	(125.39) [0]
1258	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	4/2013	/	654.00	0.00
			(-) [0/0]	(-) [654.00]	(0.00) [0]
1259	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/	182.92	0.00
			(-) [0/0]	(-) [197.73]	(14.81) [0]
1260	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	4/1997	4/1999	233.00	341.38
			(-) [0/0]	(-) [318.42]	(85.42) [0]
1261	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016	213.00	0.59
			(-) [2/2020]	(-) [213.35]	(0.35) [46]
1262	JHANSI BINA DOUBLING	9/2016	3/2021	2,001.00	0.00
			(-) [3/2021]	(-) [2,001.00]	(0.00) [0]
1263	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023	4,329.53	0.00
			(-) [3/2023]	(-) [4,329.53]	(0.00) [0]
1264	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/	643.00	0.00
			(-) [0/0]	(-) [644.00]	(1.00) [0]
1265	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019	528.57	28.46
			(-) [12/2019]	(-) [528.57]	(0.00) [9]
1266	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019	927.01	1,011.81
			(-) [3/2020]	(-) [1,077.00]	(149.99) [12]
1267	MANDHANA - BRAHMAWART NEW LINE PROJECT.	4/1997	4/1999	609.04	1,808.14
			(-) [3/2019]	(1,063.00) [1,807.88]	(1,198.84) [239]
1268	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020	668.70	0.00
			(-) [3/2020]	(668.00) [668.00]	(-0.70) [0]
1269	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023	1,765.92	375.62
			(-) [12/2024]	(-) [1,765.92]	(0.00) [21]
1270	MEERUT-MUZAFARNAGAR PATCH DL	4/2012	/	377.44	182.85
			(-) [0/0]	(-) [377.44]	(0.00) [0]
1271	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017	150.00	0.00
			(-) [10/2022]	(-) [150.00]	(0.00) [66]
1272	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018	1,343.00	0.00
			(-) [0/0]	(-) [1,343.00]	(0.00) [0]
1273	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017	622.50	57.31
			(-) [1/2020]	(427.00) [426.74]	(-195.76) [33]
1274	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020	2,436.21	315.40
			(-) [3/2021]	(-) [2,436.21]	(0.00) [12]
1275	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022	1,295.42	118.03
			(-) [12/2019]	(-) [1,295.42]	(0.00) [27]
1276	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019	1,177.96	1.58
			(-) [4/2021]	(-) [1,028.95]	(-149.01) [16]
1277	UNCHAHAH-AMETHI	4/2012	/	1,229.00	4.12
			(-)	(-)	(-849.00)

			[0/0]	[380.00]	[0]
1278	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	4/2006	3/2010 (-) [0/0]	369.90 (-) [1,581.53]	618.19 (1,211.63) [0]
1279	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [943.60]	158.12 (0.00) [33]
	Road Transport And Highways				
1280	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	235.41 (0.00) [0]
1281	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1282	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	425.99 (0.00) [0]
1283	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	608.73 (0.00) [0]
1284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [9/2018]	291.36 (-) [291.36]	442.51 (0.00) [0]
1285	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	197.72 (0.00) [0]
1286	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [11/2019]	2,016.00 (-) [2,016.00]	1,820.02 (0.00) [7]
1287	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,120.57]	0.00 (0.00) [0]
1288	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [2/2020]	1,668.00 (-) [1,668.00]	349.13 (0.00) [-]
1289	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	701.24 (0.00) [0]
1290	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [7/2020]	1,408.00 (-) [1,408.00]	5.71 (0.00) [-]
1291	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	50.71 (0.00) [-]
1292	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	301.48 (0.00) [0]
1293	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [4/2019]	1,587.49 (-) [1,587.49]	201.46 (0.00) [0]
1294	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	169.51 (0.00) [0]
1295	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [1/2019]	1,657.20 (-) [1,657.20]	2,015.00 (0.00) [0]
1296	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [3/2020]	2,064.99 (-) [2,447.00]	1,066.41 (382.01) [0]
1297	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-	12/2017	/ (-)	207.00 (-)	0.00 (0.00)

	MUZAFFARN		[0/0]	[207.00]	[0]
1298	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [4/2019]	676.73 (-) [676.73]	409.11 (0.00) [0]
1299	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	6/2015	3/2018 (-) [0/0]	774.57 (-) [774.57]	0.00 (0.00) [0]
1300	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150	1/2014	10/2016 (-) [0/0]	397.04 (-) [397.04]	0.00 (0.00) [0]
1301	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43	10/2013	3/2017 (-) [0/0]	317.76 (-) [317.76]	15.47 (0.00) [0]
1302	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [0/0]	1,046.00 (-) [1,046.00]	805.19 (0.00) [0]
1303	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	3/2015	/ (-) [0/0]	629.74 (-) [629.74]	0.00 (0.00) [0]
1304	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	0.00 (0.00) [0]
1305	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [534.55]	304.89 (0.00) [0]
1306	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1307	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [0/0]	1,117.84 (-) [1,117.84]	0.00 (0.00) [0]
1308	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	350.99 (0.00) [0]
1309	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	0.00 (0.00) [0]
1310	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	1/2016	5/2019 (-) [5/2019]	701.12 (-) [701.12]	842.34 (0.00) [0]
1311	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [6/2019]	1,081.57 (-) [1,081.57]	827.52 (0.00) [0]
1312	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [5/2020]	1,232.21 (-) [1,232.21]	637.48 (0.00) [-]
1313	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [5/2020]	1,989.00 (-) [1,989.00]	842.34 (0.00) [2]
1314	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018 (-) [0/0]	785.78 (-) [785.78]	839.63 (0.00) [0]
1315	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	1,998.25 (0.00) [0]
1316	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	0.00 (0.00) [0]
1317	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	0.00 (0.00) [0]

1318	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [925.40]	0.00 (0.00) [0]
1319	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	441.14 (0.00) [0]
1320	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	404.76 (0.00) [0]
1321	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	492.20 (0.00) [0]
1322	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	396.67 (0.00) [0]
1323	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1324	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [11/2020]	1,373.28 (-) [1,373.28]	0.00 (0.00) [8]
1325	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [8/2020]	1,184.71 (-) [1,310.00]	0.00 (125.29) [5]
1326	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [4/2019]	899.00 (-) [899.00]	462.25 (0.00) [0]
1327	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,948.72 (0.00) [0]
1328	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	10/2013	10/2016 (-) [0/0]	283.45 (-) [283.45]	0.00 (0.00) [0]
1329	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [683.24]	538.60 (0.00) [0]
1330	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [1,025.80]	0.00 (0.00) [0]
1331	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [1,115.28]	0.00 (0.00) [0]
1332	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [445.89]	0.00 (0.00) [0]
1333	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1334	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	10/2013	3/2017 (-) [0/0]	493.94 (-) [493.94]	0.00 (0.00) [0]
1335	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	10/2014	10/2016 (-) [0/0]	227.74 (-) [227.74]	0.00 (0.00) [0]
1336	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1337	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1338	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO	12/2014	/	207.88	0.00

	538.00 OF NH-730 (EPC MODE)		(-) [0/0]	(-) [207.88]	(0.00) [0]
1339	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	0.00 (0.00) [0]
	<u>Steel</u>				
1340	FORGED WHEEL PLANT	4/2014	9/2018 (-) [6/2019]	1,682.85 (-) [1,682.85]	972.10 (0.00) [9]
	<u>Urban Development</u>				
1341	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	0.00 (0.00) [0]
1342	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Petroleum</u>				
1343	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [2/2020]	160.10 (-) [160.10]	28.75 (0.00) [0]
	<u>Power</u>				
1344	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	151.99 (274.07) [0]
1345	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	162.41 (0.00) [0]
1346	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (-) [3,846.30]	3,775.64 (867.82) [93]
1347	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (12/2020) [5/2021]	1,657.00 (2,978.86) [4,401.90]	2,731.61 (2,744.90) [63]
1348	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2021]	2,491.58 (-) [4,105.30]	1,593.51 (1,613.72) [102]
	<u>Railways</u>				
1349	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	38.33 (126.80) [0]
1350	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1351	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2026]	16,216.00 (-) [16,216.00]	1,235.71 (0.00) [15]
	<u>Road Transport And Highways</u>				
1352	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	0.00 (0.00) [0]
1353	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	0.00 (0.00) [0]
1354	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [7/2018]	605.84 (-) [605.84]	722.46 (0.00) [0]
1355	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	147.72 (0.00) [-]
1356	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD	3/2018	5/2018	274.31	0.00

	TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399		(-) [0/0]	(-) [274.31]	(0.00) [0]
1357	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1358	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [10/2019]	720.00 (-) [720.00]	181.70 (0.00) [-]
1359	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [7/2019]	478.51 (-) [478.00]	409.17 (-0.51) [69]
1360	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	48.23 (0.00) [0]
1361	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [284.00]	94.50 (0.49) [0]
1362	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	0.00 (0.00) [0]
1363	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [6/2019]	282.08 (-) [282.08]	66.19 (0.00) [0]
1364	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	43.14 (0.00) [0]
1365	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	92.42 (0.00) [0]
1366	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	95.30 (0.00) [0]
1367	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	0.26 (0.00) [0]
1368	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.74 (0.27) [0]
1369	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.01 (0.00) [0]
	<u>Urban Development</u>				
1370	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Coal</u>				
1371	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	302.68 (0.00) [0]
1372	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2019]	2,661.73 (-) [2,661.73]	215.56 (0.00) [0]
1373	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1374	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	393.45 (0.00) [24]
	<u>Health And Family Welfare</u>				
1375	CNCI KOLKATA WEST BENGAL	8/2016	9/2018	244.00	247.47

			(-) [3/2019]	(-) [244.00]	(0.00) [6]
1376	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/	651.99	58.04
			(-) [2/2020]	(-) [651.99]	(0.00) [-]
1377	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019	355.15	122.43
			(-) [3/2019]	(-) [355.15]	(0.00) [0]
	<u>Petroleum</u>				
1378	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022	3,712.00	22.47
			(-) [6/2021]	(-) [3,712.00]	(0.00) [-15]
1379	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019	2,934.40	889.89
			(-) [9/2019]	(-) [2,934.40]	(0.00) [0]
1380	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	3/2014	9/2017	3,076.00	3,224.62
			(6/2018) [3/2019]	(4,190.00) [4,190.00]	(1,114.00) [18]
1381	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020	1,740.00	25.46
			(-) [12/2020]	(-) [1,740.00]	(0.00) [0]
1382	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020	1,021.00	4.45
			(-) [12/2020]	(-) [1,021.00]	(0.00) [0]
1383	HALDIA LPG IMPORT FACILITY	3/2015	10/2018	694.00	535.04
			(6/2019) [6/2019]	(1,097.54) [694.00]	(0.00) [8]
1384	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020	163.02	33.79
			(-) [4/2020]	(-) [163.02]	(0.00) [0]
	<u>Power</u>				
1385	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018	454.11	255.32
			(1/2020) [1/2020]	(454.11) [454.11]	(0.00) [21]
1386	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019	1,381.84	384.28
			(2/2022) [2/2022]	(-) [1,381.84]	(0.00) [29]
	<u>Railways</u>				
1387	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003	1,027.40	484.92
			(3/2030) [3/2030]	(1,966.70) [2,373.00]	(1,345.60) [324]
1388	BARDHAMAN-KATWA (GC)	4/2007	12/2010	1,106.62	634.34
			(-) [12/2017]	(-) [1,092.20]	(-14.42) [0]
1389	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/	255.64	89.78
			(-) [0/0]	(-) [272.20]	(16.56) [0]
1390	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	4/2011	/	289.64	0.13
			(-) [0/0]	(-) [760.00]	(470.36) [0]
1391	BOWAICHANDI-ARAMBAGH	4/2010	/	267.37	40.77
			(3/2025) [3/2025]	(-) [620.00]	(352.63) [-]
1392	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/	573.78	0.67
			(-) [0/0]	(-) [268.52]	(-305.26) [0]
1393	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	4/2009	2/2012	259.51	145.35
			(-) [9/2016]	(-) [533.59]	(274.08) [0]
1394	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016	4,874.58	1,881.65
			(-)	(-)	(0.00)

			[0/0]	[4,874.58]	[0]
1395	GHUTIASHARIF-CANNING (ER)	4/2009	12/2011 (-) [9/2012]	193.08 (-) [612.45]	150.92 (419.37) [0]
1396	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1397	MM FROM PANSKURA-GHATAL NL	4/2011	0/0 (3/2030) [3/2030]	276.69 (-) [426.00]	0.00 (149.31) [-]
1398	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [3/2020]	221.42 (-) [380.00]	101.19 (158.58) [-]
1399	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (200.34) [614.00]	270.28 (316.68) [12]
1400	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	33.12 (9.73) [-21]
1401	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.13 (435.44) [141]
1402	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (4,200.00) [2,913.50]	794.78 (-0.01) [108]
1403	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1404	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	1,966.91 (307.50) [108]
1405	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	1/1991	12/2021 (12/2021) [12/2021]	1,013.45 (1,013.45) [1,428.00]	484.58 (414.55) [0]
1406	TAMLUK DIGHA,LINE DOUBLING (SER)	3/1984	6/2005 (-) [0/0]	293.97 (-) [749.69]	0.00 (455.72) [0]
1407	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2022]	1,188.91 (-) [1,620.01]	844.78 (431.10) [36]
1408	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,544.30 (2,355.23) [0]
	Road Transport And Highways				
1409	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [5/2019]	1,083.00 (-) [1,083.00]	185.52 (0.00) [11]
1410	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2020]	998.79 (-) [998.79]	1,829.14 (0.00) [82]
1411	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [6/2019]	1,078.84 (-) [1,078.84]	2,315.36 (0.00) [70]
1412	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [5/2019]	1,396.18 (-) [1,396.18]	2,614.84 (0.00) [56]
1413	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2020]	361.15 (-) [361.15]	47.90 (0.00) [-]
1414	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND	3/2017	6/2018 (-)	158.65 (-)	0.00 (0.00)

	PANITNAKI I		[0/0]	[158.65]	[0]
1415	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [4/2019]	229.37 (-) [229.37]	18.26 (0.00) [5]
1416	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (-) [767.03]	186.83 (0.00) [13]
1417	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [5/2019]	702.16 (-) [702.16]	461.13 (0.00) [58]
1418	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,261.98]	0.00 (0.00) [0]
1419	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1420	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [3/2019]	1,665.00 (-) [1,665.00]	1,901.17 (0.00) [-]
	<u>Urban Development</u>				
1421	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [3/2019]	156.57 (-) [156.57]	148.80 (0.00) [31]
1422	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1423	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	101.71 (0.00) [15]
	Total			18,25,733.41 (4,52,193.97) [21,44,298.86]	8,24,847.36 (3,18,565.45)

North East Central Sector Project Detail's

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on 31.01.2019)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Petroleum</u>				
1	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019 (-) [1/2019]	247.52 (-) [247.52]	148.35 (0.00) [-1]
	<u>Power</u>				
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (3/2019) [3/2019]	2,496.90 (6,179.96) [6,179.96]	6,900.51 (3,683.06) [111]
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,448.57 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
6	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
7	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
9	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
10	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
12	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	38.50 (0.00) [0]
13	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
14	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
15	CONSTRUCTION OF TWOLANE WITH PAVED	2/2017	4/2017	216.71	0.00

	SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS		(-) [0/0]	(-) [216.71]	(0.00) [0]
16	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
17	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/	264.16	0.00
			(-) [0/0]	(-) [264.16]	(0.00) [0]
18	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016	334.22	0.00
			(-) [0/0]	(-) [334.22]	(0.00) [0]
19	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	0.00
			(-) [0/0]	(-) [434.06]	(0.00) [0]
20	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	0.00
			(-) [0/0]	(-) [284.09]	(0.00) [0]
21	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	0.00
			(-) [0/0]	(-) [195.23]	(0.00) [0]
22	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	0.00
			(-) [0/0]	(-) [203.36]	(0.00) [0]
23	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	0.00
			(-) [0/0]	(-) [194.66]	(0.00) [0]
24	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	0.00
			(-) [0/0]	(-) [198.22]	(0.00) [0]
25	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012	207.03	0.00
			(-) [0/0]	(-) [207.03]	(0.00) [0]
26	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010	165.00	0.00
			(-) [0/0]	(-) [165.00]	(0.00) [0]
27	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017	180.57	0.00
			(-) [0/0]	(-) [180.57]	(0.00) [0]
28	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017	168.32	0.00
			(-) [0/0]	(-) [168.32]	(0.00) [0]
29	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012	156.63	132.21
			(-) [0/0]	(276.00) [276.00]	(119.37) [0]
30	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011	305.49	0.00
			(-) [0/0]	(-) [305.49]	(0.00) [0]
31	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010	104.00	0.00
			(-) [0/0]	(-) [201.00]	(97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
32	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021	875.00	174.00
			(-) [5/2021]	(-) [875.00]	(0.00) [0]
33	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	113.50
			(-) [0/0]	(-) [175.57]	(0.00) [0]
	<u>Petroleum</u>				
34	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019)	2,465.15 (-)	2,112.54 (-86.29)

			[12/2019]	[2,378.86]	[81]
35	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	74.97 (0.00) [0]
36	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	315.44 (0.00) [0]
37	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
38	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	89.48 (127.41) [70]
39	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	217.07 (0.00) [0]
40	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	2.08 (0.00) [0]
41	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,346.72 (0.00) [0]
42	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	101.71 (-5.15) [0]
43	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Power</u>				
44	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [1/2019]	4,375.35 (8,150.00) [8,150.00]	7,220.84 (3,774.65) [88]
	<u>Railways</u>				
45	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (486.96) [551.00]	615.94 (237.00) [0]
46	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	288.01 (-50.32) [-24]
47	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	257.41 (-49.96) [0]
48	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (614.81) [398.93]	339.81 (152.86) [0]
49	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	575.61 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
50	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
51	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
52	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	0.00 (-65.82) [0]
53	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]

54	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
55	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	80.00 (0.00) [0]
56	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	0.00 (0.00) [0]
57	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
58	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
59	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
60	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [4/2019]	217.61 (-) [360.84]	390.71 (143.23) [108]
61	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [2/2019]	160.00 (-) [167.98]	202.58 (7.98) [129]
62	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
63	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	16.84 (0.00) [0]
64	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
65	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	0.00 (0.00) [0]
66	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
67	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [12/2018]	280.00 (-) [361.00]	410.32 (81.00) [0]
68	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
69	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
70	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [3/2019]	199.81 (-) [385.13]	209.80 (185.32) [119]
71	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [0]
72	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2019]	208.00 (-) [230.00]	297.81 (22.00) [131]
73	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [4/2019]	225.00 (-) [225.00]	312.79 (0.00) [130]
74	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008	245.00	214.88

			(-) [2/2019]	(174.34) [174.34]	(-70.66) [131]
75	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
76	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
77	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	8,350.11 (9,354.83) [108]
	<u>Urban Development</u>				
78	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [11/2019]	216.69 (-) [216.69]	52.00 (0.00) [56]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
79	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (9/2019) [9/2019]	363.99 (-) [363.99]	145.51 (0.00) [16]
	<u>Railways</u>				
80	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [6,000.00]	260.10 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
81	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
82	JORBAT - BARAPANI	1/2011	1/2014 (-) [1/2019]	536.00 (-) [536.00]	839.86 (0.00) [60]
83	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [3/2019]	479.20 (-) [479.20]	470.59 (0.00) [10]
84	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	<u>Urban Development</u>				
85	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
86	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,968.00]	2,541.80 (2,574.53) [81]
	<u>Road Transport And Highways</u>				
87	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
88	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
89	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
90	DIMAPUR-TIZIT NL	4/2013	3/2020	4,274.00	0.00

			(-) [3/2020]	(-) [4,274.00]	(0.00) [0]
91	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (10/2021) [10/2021]	2,326.52 (2,446.57) [3,000.00]	696.02 (673.48) [79]
	<u>Road Transport And Highways</u>				
92	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
93	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
94	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	0.00 (0.00) [0]
95	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	0.00 (0.00) [0]
96	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
97	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
98	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
99	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	0.00 (0.00) [0]
100	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]
101	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	0.00 (0.00) [0]
102	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
103	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
104	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
105	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	0.00 (0.00) [0]
106	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	0.00 (0.00) [0]
107	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
108	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
109	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
110	WIDENING OF 2(TWO) LANING OF LONGLENG-	12/2010	2/2011	1,296.00	0.00

	CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA		(-) [0/0]	(-) [1,296.00]	(0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
111	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
112	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
113	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
114	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
115	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	0.00 (0.00) [0]
116	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	18.12 (0.00) [0]
117	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	7.50 (0.00) [0]
118	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
119	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Power</u>				
120	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
121	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (3,407.00) [3,407.00]	3,224.14 (2,265.00) [60]
122	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
123	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (984.97) [1,733.20]	1,553.74 (838.20) [0]
	<u>Road Transport And Highways</u>				
124	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	261.24 (0.00) [0]
125	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Urban Development</u>				
126	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
127	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]

128	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			78,297.80 (27,669.68) [1,25,986.70]	55,901.71 (47,688.90)
